
TECHNICAL PROPOSAL

GLX Constructors is one team with one goal – to design, build, and commission the Green Line Extension. Our team has working relationships from past projects, and also offers the strongest combination of local and national transit-oriented contractors with proven experience in Design Build delivery of transit systems; integration of new and existing rail systems; start-up, testing, and commissioning; and extensive community outreach.

On the following pages, you will find a summary of our technical proposal submission.



MANAGEMENT APPROACH

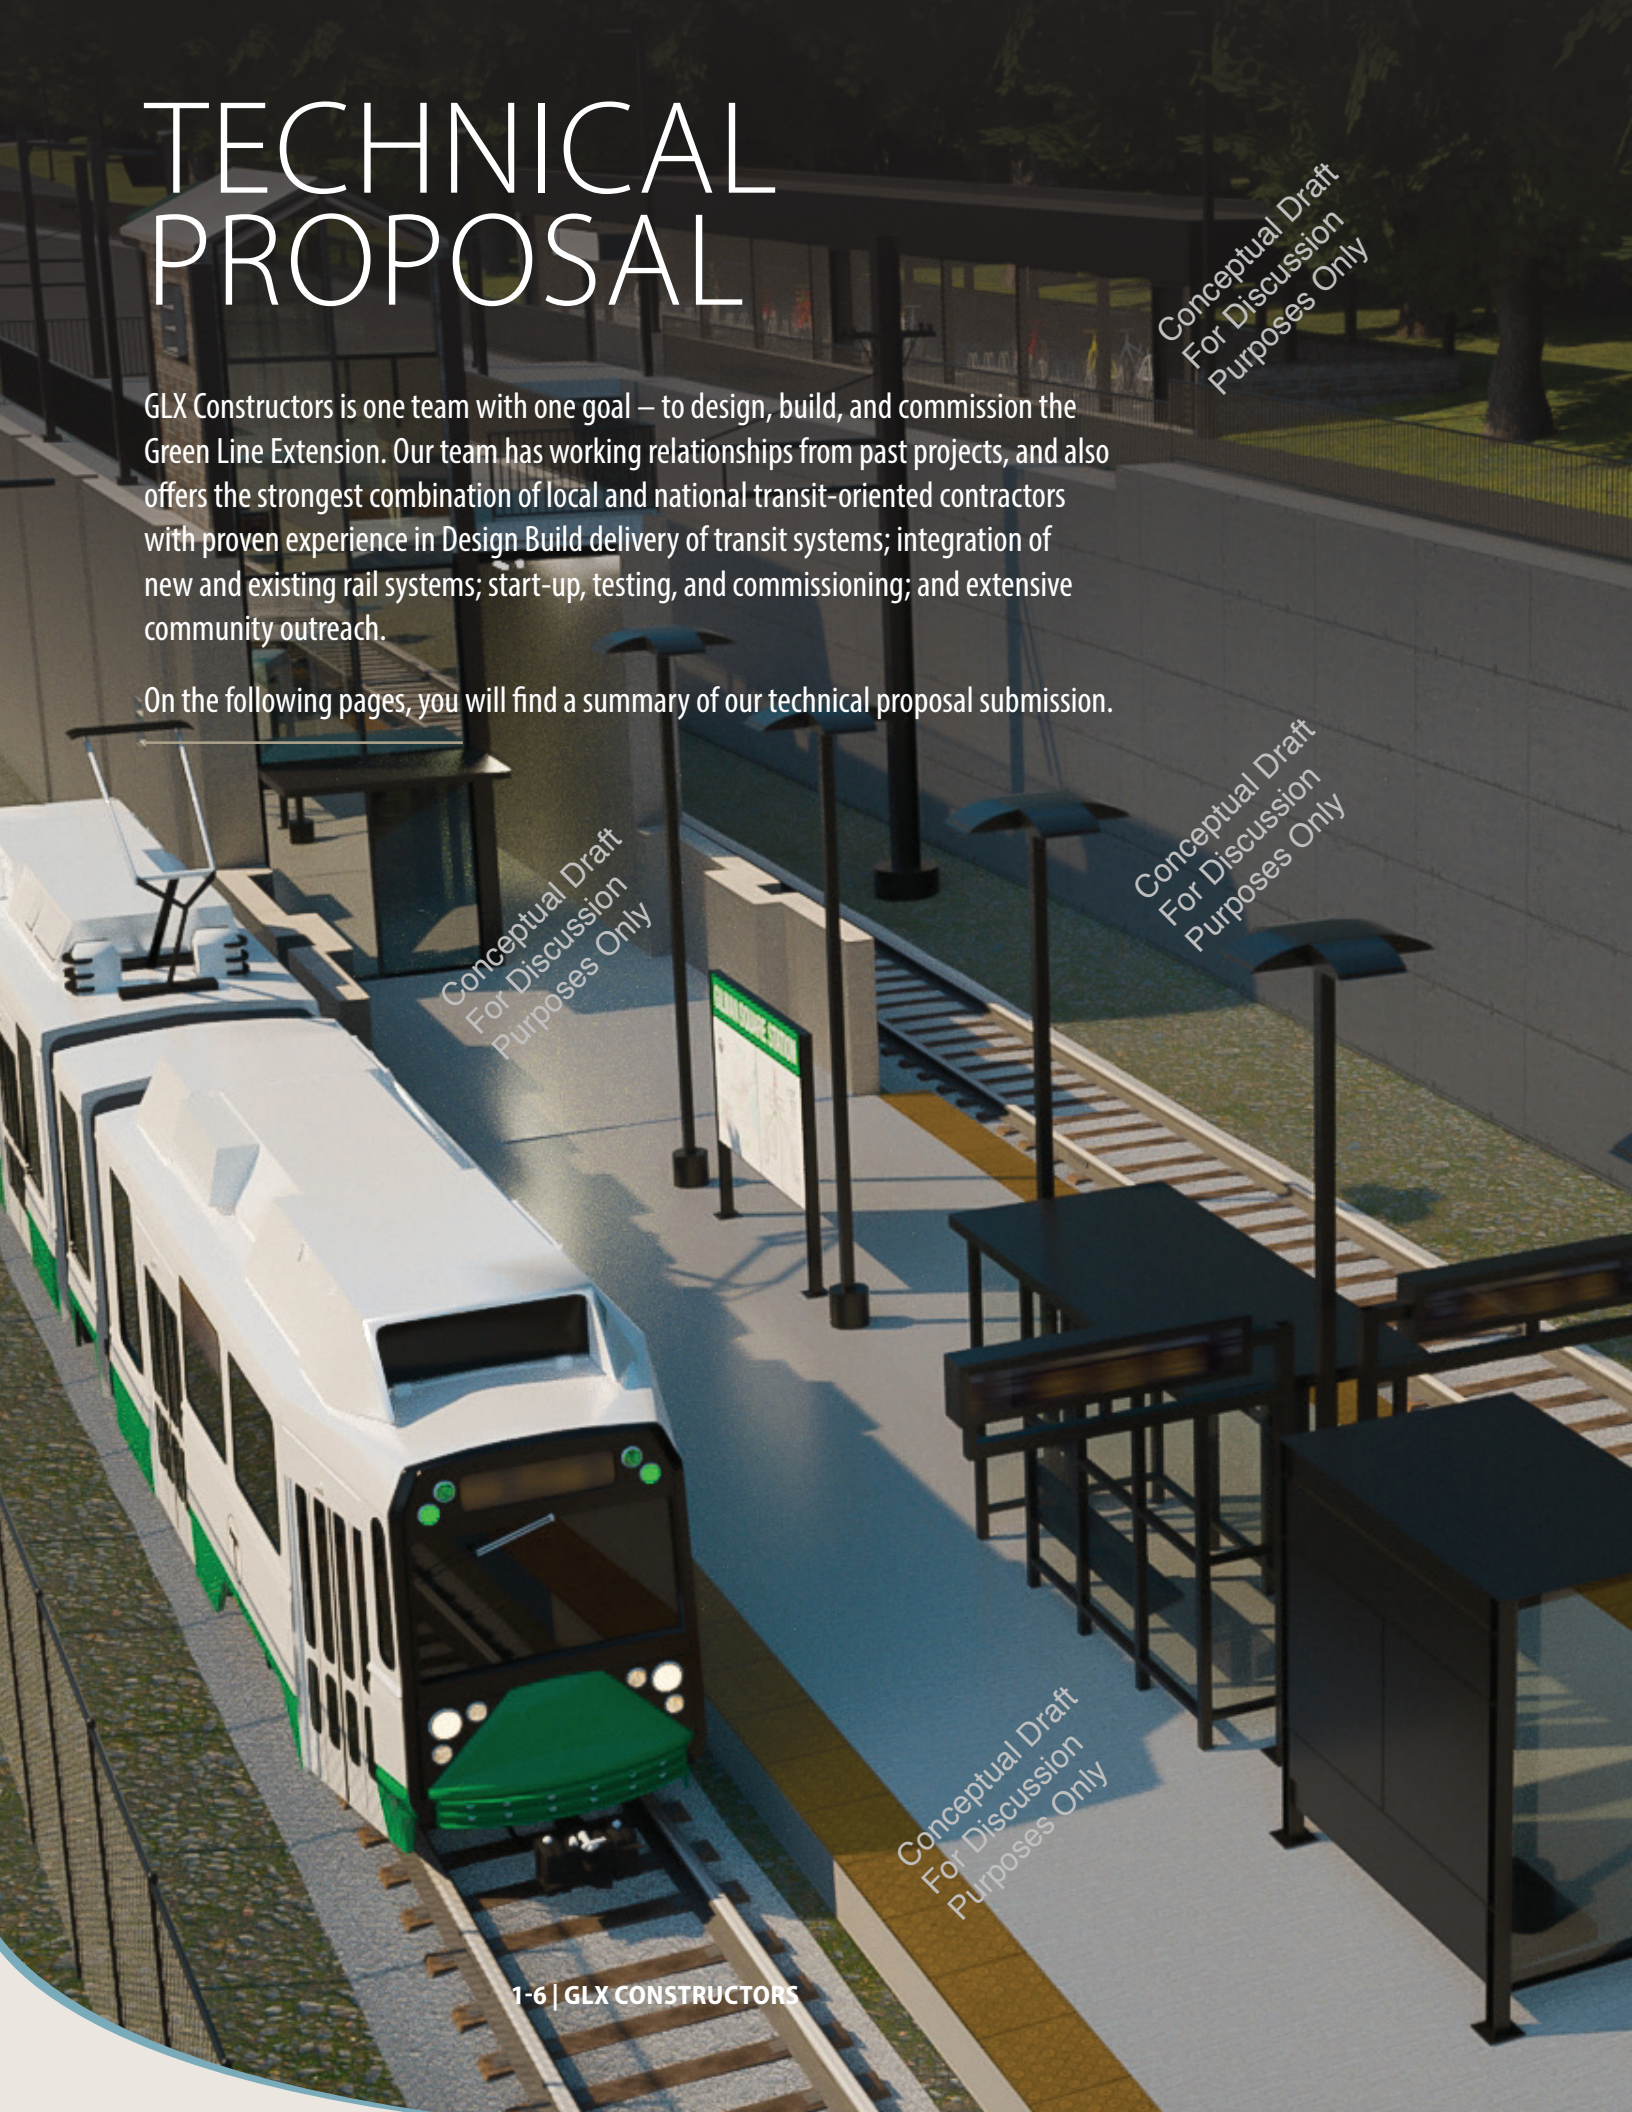

During the preparation of our Statement of Qualifications and as part of our proposal development, GLX Constructors has built an experienced Project Team based on the needs of the Project. Our team was assembled with the expressed goal of developing a Management Approach to incorporate the initial design of the Project with how the Project will be constructed and commissioned. Our construction-driven approach drives our collaborative team integration, providing the MBTA with a fully integrated Project Team to deliver cost and schedule certainty.

Our construction-driven approach to Project Management begins during the Design Phase of the Project and integrates safety, quality, construction, and commissioning into the heart of the Project.

Our Management Approach demonstrates:

- A clear understanding of the Project with a proven approach to managing quality; safety, security, and emergency management; risks; and schedule.
- Our approach to construction while minimizing impacts to the traveling public, the MBTA, and rail operations.
- Our approach to controlling costs and minimizing claims and delays, as well as resolving disputes.

> **A construction-driven approach will minimize interruptions and impact on the community, optimize schedule, maximize quality and efficiency. Schedule and cost certainty are a product of a construction-driven approach.**

DESIGN MANAGEMENT


“Construction-driven approach drives cost and schedule efficiencies in a collaborative environment.

GLX Constructors' Lead Designer, STV, brings local and national expertise in Design Build project delivery, including the successful completion of some of the most complex, large-scale transportation projects in Massachusetts and the United States.

Mark Pelletier, PE, Design Manager, will lead the Design Team. He brings his valuable experience working with the MBTA and other GLX Constructors' team members to the Project. He has designated experienced personnel and design subconsultants to efficiently complete the Project from design through safety certifications, revenue operations, and closeout.

To ensure overall project integration and schedule certainty, GLX Constructors has appointed an additional team member to serve in a critical role to oversee and collaborate with the Design Team. Michael Hoitink, our Design Build Coordinator, brings more than 15 years of experience on similar DB projects. This role provides the team with a designated individual for all activities between the design and construction team.

As part of our construction-driven approach, Mark Pelletier has built a team of Design Discipline Leads that will work alongside the Construction Discipline Project Engineers and Superintendents to develop a comprehensive design solution that will be implemented through construction, testing, and commissioning.

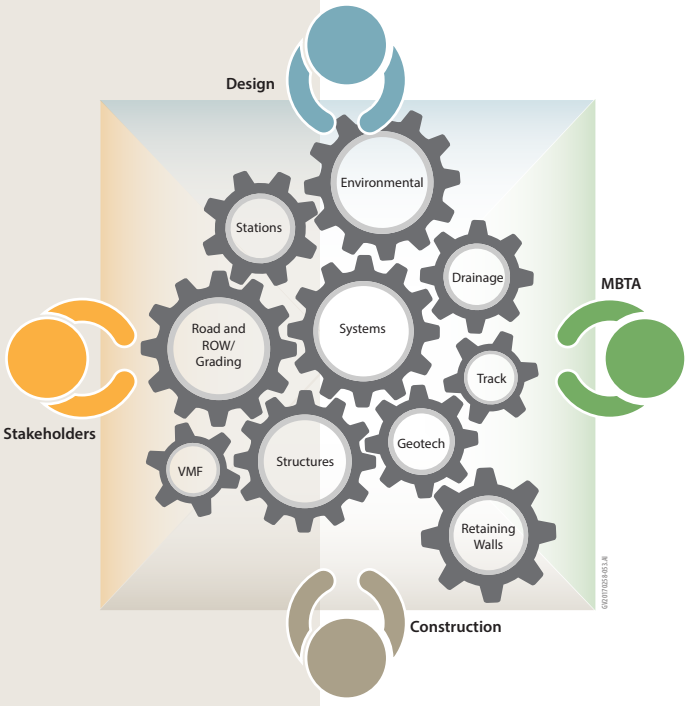

To effectively and efficiently manage the design phase, we have divided the design submission into 10 categories and will dedicate a Discipline Design and Construction lead to each package. Each package will be managed through our Technical Work Groups (TWG). TWGs will be composed of the Design Discipline Leads, Construction Discipline Leads, the MBTA, and the appropriate third-party stakeholders. The 10 TWGs will interact both formally through regularly scheduled meetings, and informally on a daily basis at the co-located office. By embedding the Construction Team, the MBTA, and third-party stakeholders into the TWGs, we advance our design and Technical Solutions in a cohesive manner, and we immediately address any potential issues surrounding constructability and work phasing during design development.

CONSTRUCTION MANAGEMENT

Experience is so important when it comes to construction, but proper teamwork is essential to drive the Project to success and exceed expectations. As such, GLX Constructors' team members have been working together since late 2016 to meet the goals and objectives of the Project. In addition, two members of our team competed for the Project in the initial 2012 CM/GC procurement. We are pleased to have the opportunity to build this project.

The execution of the Green Line Extension DB Project is led by our Project Manager, John West, and Construction Manager, Jamie Doyle. Combined, these gentlemen bring decades of DB experience to the Project.

In addition, we have formed a team that has the added benefit of having prior working relationships, including the successful completion of the Greenbush Line Rail Restoration Design Build Project for the MBTA. This experience of working together on prior projects provides the MBTA and the Project with an already-established communication and coordination system, and eliminates a learning curve that is typically in place at the start of a project.



Design Manager, Mark Pelletier, and Construction Manager, Jamie Doyle bring their past experience working together on the Greenbush Line Rail Restoration to the Green Line Extension.

"GLX Constructors' team members have formed an integrated team that has the added benefit of having a prior working relationship to successfully complete the Greenbush Line Rail Restoration Design Build Project for the MBTA.



GLX Constructors' team members have been actively involved in many transit Safety and Security efforts for successful transit system projects nationwide, including Dallas Area Rapid Transit, Houston Metro Rail, Denver Regional Transport District, LAMTA, UTA, and WMATA (Dulles Phase 2), along with task order work for agencies such as Amtrak, BART, and Hampton Roads Transit.

QUALITY MANAGEMENT

We have specifically developed our Quality Management Plan to complement the MBTA's Quality Management Plan, which is well known and understood by our team members. We have an owner-operator approach to quality management. GLX Constructors has an ISO 9001-compliant Quality Management Plan that is aligned with our Project Management Plan and incorporates our staff members' NETTCP and ASQ quality management certifications.

Our Quality Team is independent from the Construction Team. The Quality Team reports directly to the Project Executive, the Executive Committee, and the MBTA on the same reporting level as the Project Manager. In this manner, the MBTA has immediate confirmation of quality concerns and approvals, providing confidence in the integrity of the Quality Management System and a close oversight of our quality performance.

SAFETY, SECURITY, AND EMERGENCY MANAGEMENT

GLX Constructors will further assess the Project's requirements and develop a Safety, Security, and Emergency Management Plan. We will provide the MBTA with a fully compliant program that comprises safety, security, and emergency elements for protecting both the MBTA's operations, workforce, and the commuting public during day-to-day public use once the Project is successfully completed. Our Team has extensive startup, commissioning, testing, and systems certification experience, and we apply our best practices during the Design and Construction Phases for systems testing and commissioning, facilitating an effective Project start up and reduced costs along the way.

GV20170258-110.INDD

RISK MANAGEMENT

Supporting the MBTA's Project goals surrounding cost and schedule certainty, GLX Constructors offers the MBTA a risk management process that will minimize and manage risks that may threaten the Project's success. Our team will identify, assess, monitor, mitigate, and manage Project-specific risks during each Project phase and activity. As a result, the MBTA can rest assured that we will live up to our goal of "no surprises" for the MBTA; maintaining cost and schedule certainty from Design through the Construction, Testing, Commissioning, and Startup Phases of the Project.

GLX Constructors will engage local agencies and stakeholders through our TWGs and regularly scheduled meetings during the planning stages of both design and construction, so we may address concerns early and proactively.

Through our extensive experience in DB project delivery, GLX Constructors has defined a systematic approach that enables us to effectively identify risks, assign management of those risks, and mitigate any potential risks of impacting the Project. These risks incorporate the MBTA risks as well. We have established a Risk Management Plan to minimize and manage risk. This plan is a project-specific implementation of GLX Constructors' managing partner, Fluor's Business Risk Management Framework (BRMF). This process has been effectively used on previous DB projects performed by GLX Constructors' team members, and will help to ensure the project is delivered on schedule and under budget.

SCHEDULE CERTAINTY

Since our SOQ submittal in early 2017, GLX Constructors has invested tremendous resources in the Green Line Extension DB Project. We have performed an in-depth schedule analysis to fully assess the design and construction challenges of the Project. While performing these activities, we focused on the MBTA's milestones, objectives, and activity restrictions. In establishing our Initial Baseline Schedule, we have coordinated the scope of all Project-related activities to ensure schedule certainty, identify potential risks, and implement appropriate mitigation measures to address any concerns from the MBTA and local municipalities.

COST CERTAINTY

The MBTA has delivered a clear message that the Green Line Extension DB Project will be financially successful. The system has many capital needs and priorities competing for these precious project funds. Cost certainty is a clear Project goal, and one that we embrace as we partner with the MBTA to support and work to bring the best value to the Commonwealth and transit ridership.

TECHNICAL SOLUTIONS



SYSTEMS

GLX Constructors has developed an efficient and innovative design and construction solution which demonstrates our understanding of the overall Project requirements. Details of our approach to each of the Technical Solutions and the benefits of our approach are more fully explained in our Technical Proposal.

- GLX Constructors' Lead Designer has more than 35 years of experience with the MBTA and understands the current systems in place as well as the proposed system to allow for seamless integration.
  - ✦ STV has one of the largest systems groups in the Boston area and in the country with many professionals that have worked for and with the MBTA for 30+ years.
- GLX Constructors has a dedicated group of local systems and integration professionals to bring their lessons learned from prior relevant projects to this Project to ensure cost and schedule certainty.

ELEVATED GUIDEWAY AND STRUCTURES



- To reduce cost and improve aesthetics, we have lowered the elevation of the guideway.
- For a more efficient foundation design, we will use driven piles, which will also limit the impacts associated with excavating contaminated soils.
- In order to increase design optimization, we have avoided the need for concrete counter weighting in curved superstructures supporting single track.
- Through our approved ATC No. 36, the underpass at Walnut Street has been completely eliminated which will bring cost savings to the Project.
- We provide a more reliable and standardized approach by replacing the underpass structures with back spans at Medford Street and School Street Bridges.
- Our approach provides a shorter duration to replace one span.
- We maximized the use of precast concrete elements for retaining walls, which are cost effective and have a 75-year design life.

GV20170258-110.INDD



STATIONS

- GLX Constructors developed a unique approach at Gilman Square Station which provides better connectivity to the Community Path, provides improved access to both School Street and Medford Street to the station, and eliminates the need for an elevated walkway between the tracks.
- ATC No. 36 raises the elevation of the Community Path at Gilman Square Station which will improve public access to the station.

LANDSCAPING AND STATION SIGNAGE

- GLX Constructors' design provides opportunities for branding at each station and will utilize the MBTA's well-established standards for signage.
- Our approach offers clear wayfinding for separating the riders from the Community Path.
- GLX Constructors understands the existing vegetation along the Project alignment and our design incorporates low maintenance and drought-tolerant landscaping components.



VMF

- Our design and construction approach to the VMF maximizes function and productivity.
  - We have removed the longitudinal column line between Tracks 1 and 2, which optimizes the space, provides flexibility for positioning equipment, and increases working envelopes for personnel.
  - Three lateral column lines have been removed to allow us to reposition the remaining column lines to eliminate potential interference with personnel and equipment to move throughout the area, especially between Tracks 3 and 4 and the maintenance and storage areas.
- Our design includes a lowered and simplified roof line, which reduces construction and maintenance costs.
- The floor elevation was raised to eliminate flood plain issues and maximize reuse of the excavated soils from the Project, thereby minimizing costly soil disposal.

GV20170258-110.INDD

CIVIL & GUIDEWAY


- GLX Constructors optimized the track both vertically and horizontally to simplify its construction which minimizes excavation and reduces exposure to risk from hazardous materials and trucking.
- We optimized the Community Path design to maximize its width and provide better accessibility for the public.
- Through the approved ATC No. 36, our approach increases the number of opportunities to access the Community Path at street levels from the surrounding communities.
- The horizontal and vertical track realignments have reduced the degree of curvature, thereby allowing increased train speeds.
- In our design approach, we shifted the tracks at the Washington Street Bridge to eliminate stacking of the Community Path which improves safety and security for the path users.

DRAINAGE

- GLX Constructors has optimized the drainage design to shift the drain lines to minimize impacts to the active commuter rail line.
- Through our past experience with the MBTA, our team has a thorough understanding of the site-wide drainage system and the permitting requirements.

“We have optimized the track both vertically and horizontally, reducing the amount of soil to be removed from the ROW, thus resulting in reduced exposure to risk from hazardous materials and trucking.



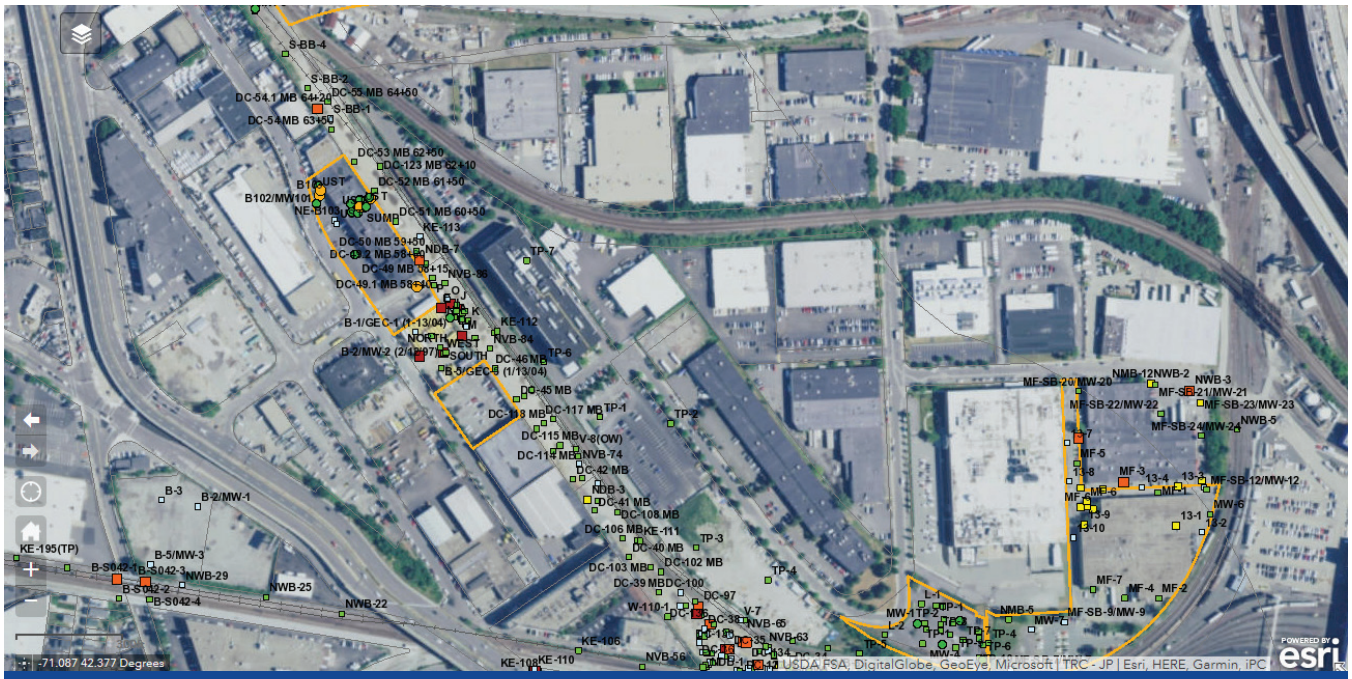

GLX Constructors performed extensive hazardous materials due diligence during the proposal phase to identify all recorded soil and groundwater contamination along the entire project corridor. This information was then incorporated into our design to maximize use of excavated contaminated material on-site versus off-site; thereby, reducing both costs and risks of unnecessary transport of material for off-site disposal.

ENVIRONMENTAL

- Through our optimization of the vertical track alignment, GLX Constructors has minimized the amount of excavation and disposal, thereby reducing the amount of heavy truck traffic on local roads.
- Our team has an understanding of the previously-sampled soil and groundwater along the Project corridor and will maximize reuse of materials to minimize costly disposal.
- By adjusting the VMF site elevation our team has maximized the reuse of excavated soil as fill on site and minimized the amount of excavation and costly disposal.

UTILITIES

- Our team has identified known utilities impacted along the alignment and has developed an approach to relocate, mitigate, and protect affected utilities.
- Our design approach, through ATC No. 36, eliminates the impacts to the MWRA 48" waterline at Walnut Street Bridge, as well as minimizes the impacts to the 24" Algonquin Gas Line at Medford Street.

GV20170258-110.INDD

ALTERNATIVE TECHNICAL CONCEPTS

We expended significant time and effort looking for Project innovations and optimizations to improve cost and schedule certainty while maintaining quality. These efforts resulted in the following formal ATCs that have been incorporated into our proposal, providing additional benefits to the MBTA.

ATC NO. 12

PROJECT AREA
STRUCTURES

DESCRIPTION
Use of OCS Poles on the outside of the tracks on new viaduct structure

VALUE TO THE PROJECT
- Reduction of viaduct deck width
- Decreased deep foundation dead loads
- Improved maintenance access
- Elimination of walkway obstructions

ATC NO. 35

PROJECT AREA
CIVIL

DESCRIPTION
Replacement of three sections of elevated track with MSE walls south of Washington Street

VALUE TO THE PROJECT
- Elimination of deep foundations and associated risks with unforeseen conditions
- Reduction of maintenance for elevated structure and associated bridge deck area
- Increased service life of MSE wall sections

ATC NO. 36

PROJECT AREA
CIVIL

DESCRIPTION
Improved Community Path, accessibility, and public safety

VALUE TO THE PROJECT
- Increased safety and security of Community Path users
- Elimination of Walnut Street pedestrian underpass
- Elimination of underpass Fire and Life Safety features
- Reduction of Medford Street underpass width
- Elimination of underpass lighting at Walnut Street and Medford Street
- Improved accessibility for emergency and maintenance vehicles operating on the Community Path
- Eliminates relocation of 48" MWRA waterline at Walnut Street

ATC NO. 43

PROJECT AREA
TRACK

DESCRIPTION
Reduction of subballast sections through use of a filter fabric and geogrid reinforcement

VALUE TO THE PROJECT
- Limits ballast settlement and lateral creep
- Reduces excavation and export of potentially contaminated soils
- Reduces trucking impacts to local streets; expedite installation
- Increases service life
- Reduces ballast maintenance

KEY PERSONNEL

GLX Constructors has developed a strong project organization that possesses the expertise, leadership, and depth of experience to successfully deliver the Project to the MBTA and stakeholders. Our proposed team is comprised of leaders in the rail industry who have prior successful experience working together.

The majority of this team, including John West, Jamie Doyle, Clyde Joseph, Mark Pelletier, Aaron Neeley, and Lloyd Lovell have been working on the pursuit of this Project since shortly after submission of our Letter of Interest, with several having been dedicated full-time since shortlisting. They have developed the necessary project knowledge, synergy, and inter-personal relationships necessary in all successful teams, and will undoubtedly provide the MBTA with an outstanding combination of dedication, professional knowledge, experience, and the partnering approach needed to make this project a success for all.



Clyde Joseph
Project Executive



John West
Project Manager



Jamie Doyle
Construction Manager



Mark Pelletier, PE
Design Manager



Bob Horn
Project Controls Manager



Sandro Plutino
Quality Manager



Hannah Brockhaus
Title VI Program Lead



Hannah Carmical
EEO Compliance Lead



Lloyd Lovell
DBE Compliance Lead



Michael Hoitink
Design Build Coordinator



Chris Poe
Project Safety and Security Manager



Aaron Neeley
Systems Integration Manager and Testing and Commissioning Manager

GV20170258-110.INDD

CIVIL RIGHTS

While the Project is a large-scale, heavy-civil construction project, it is also a deeply rooted community project, constructed through a densely populated urban environment. GLX Constructors is committed to exceeding the MBTA's expectation by integrating local vendors, subcontractors, and service providers into our team and communicating effectively to the surrounding communities to minimize disruption, inform them of our progress, and contribute to the overall Project's success.

DBE PLAN

GLX Constructors is dedicated to creating meaningful and growth-oriented opportunities for disadvantaged and minority-owned businesses. We commit to staffing the project with a diverse and highly-qualified workforce in order to create a level playing field on which small and disadvantaged businesses will compete fairly. To drive this, we have appointed Lloyd Lovell as the DBE Compliance Lead. Lloyd develops, implements, and manages Small, Minority, Women, and Disadvantaged Business Enterprise Programs.

WORKFORCE/EQUAL EMPLOYMENT OPPORTUNITIES

GLX Constructors shares the MBTA's value of promoting diversity in the workplace and on its projects. Our team is committed to achieving a diverse workforce and providing an environment where all employees are treated fairly and with respect.

TITLE VI PROGRAM COMPLIANCE

GLX Constructors will tailor our outreach to engage the entire community, including minorities and non-English speakers. To strengthen our team's efforts, we have engaged Hannah Brockhaus with Howard Stein Hudson (HSH) as the Title VI Program Lead. HSH routinely provides Title VI Program development, implementation, and management services to the MBTA and MassDOT on a wide variety of construction projects, including the recent Chelsea Viaduct Rehabilitation Project. Using these lessons learned, Hannah will work with community members to go beyond the traditional public information meeting to ensure that all members of the community are equally well informed about the advancing construction and how it will affect their daily lives, and how they can participate and benefit from this Project.

"GLX Constructors will bring lessons learned from managing diverse workforces on many comparable DB and rail projects, including:

- **Eagle P3 Commuter Rail Line, Denver, Colorado, $3 billion**
- **Greenbush Line Rail Restoration Design Build, Massachusetts, $334 million**
- **West Rail Line, Denver, Colorado, $438 million**
- **495 Express Lanes, Northern Virginia, $1.4 billion**

WHY GLX CONSTRUCTORS?

GLX CONSTRUCTORS

GLX Constructors delivers local knowledge, MBTA working relationships, and demonstrated rail and Design Build (DB) expertise. We offer the experience necessary to meet the primary goals for the Project listed in the RFP, including:

LOCAL EXPERIENCE WITH MBTA	GLX Constructors' team members, Middlesex and STV, have an established local presence in Boston, and have partnered with the MBTA for more than 35 years.
DESIGN BUILD EXPERTISE	GLX Constructors has delivered more than $30 billion in complex DB projects, including STV and Balfour Beatty's experience on the Greenbush Line Rail Restoration DB Project, the first large-scale DB project for the MBTA.
EXPERIENCE WORKING TOGETHER	Our team members and proposed key personnel have experience working together on large, complex transportation projects and with the MBTA.
COMPLEX RAIL EXPERIENCE	GLX Constructors' team members have individually and collectively delivered rail projects in dense urban environments including active rail and integration with new and existing systems; and extensive experience with start-up, testing, commissioning, and FTA safety certification.
EXTENSIVE COMMUNITY INVOLVEMENT	GLX Constructors is committed to exceeding the MBTA's expectation. We have experienced and dedicated resources to make a positive long-term impact on the local communities.

GV20170258-110.IINDD



Response to the Request for Proposal for the Green Line Extension Design Build Project

Submitted to

Massachusetts Department of Transportation and The Massachusetts Bay Transportation Authority

Part 2 – Financial Pass/Fail Evaluation Criteria Information

GLX CONSTRUCTORS



Response to the Request for Proposal

for the Green Line Extension Design Build Project

Submitted to

Massachusetts Department of Transportation and The Massachusetts Bay Transportation Authority

Part 3 – Management Approach Qualitative Evaluation Criteria Information

GLX CONSTRUCTORS

TABLE OF CONTENTS

PART 3 →

Section 3.1 Project Management Plan
Section 3.2 Quality Management Plan
Section 3.3 Safety, Security, and Emergency Management
Section 3.4 Risk Management Approach
Section 3.5 Initial Baseline Schedule

3. MANAGEMENT APPROACH QUALITATIVE EVALUATION CRITERIA INFORMATION

Construction-driven execution of Project Management delivers a safe, quality, and economical Design Build Project providing the best investment value for the MBTA.

During the Proposal Phase, Fluor, Middlesex, Herzog, and Balfour Beatty, along with STV, have revisited our past, successful projects that are similar in complexity, scope, and nature to generate efficiency for this Project.

3.1 PROJECT MANAGEMENT PLAN

GLX Constructors is a versatile team that offers the MBTA the essential knowledge, capability, and systems to maintain both cost and schedule certainty on the Green Line Extension Design Build (DB) Project. From managing third parties, integrating our Design and Construction Teams, and implementing critical project controls, GLX Constructors' local experience will give the MBTA an aggressive price and the best value for its investment. In working with GLX Constructors, the MBTA can expect value in the form of a reliable work plan, transparent communication, quick and seasoned problem solving, and a fully resource-loaded critical path schedule that will maintain existing rider capacity throughout construction.

GLX Constructors will deliver a collaborative approach with the MBTA and Project Stakeholders to successfully execute this transformative infrastructure project. Key members of our Project Team have been involved in the delivery of this Project beginning with the SOQ and Proposal Phases, and we remain committed to continue through the Execution Phase. This transition of our integrated Key Personnel from the Proposal Phase into the Execution Phase, along with our project management procedures, processes, systems, and structures will enable our Team from day one to be fully focused on the MBTA's Design Build (DB) objectives, the Green Line's specific challenges, key result areas, and our successful partnership with the MBTA.

GLX Constructors applies a construction-driven approach to project management, beginning with integrating our health, safety, and environmental (HSE), quality, and construction standards into each phase of the Project, including the Design Phase. Safety for our workforce, Management Team, Design Team, the MBTA, and the traveling public is the first and most critical aspect of our project management approach.

> **To enhance time and cost savings for the MBTA, we will include a senior-level DB Coordinator as a liaison on our team. By doing so, we will smooth the interfaces between design and construction activities and seamlessly integrate a construction-driven execution across design disciplines.**

To provide for the most economical design and facilitate efficient construction execution done right the first time, our quality systems, discussed in detail in Section 3.2, are implemented at the onset of project execution in cohesion with our Construction Management Team, project engineers, and superintendents within the Technical Work Groups (TWGs), discussed in further detail in Section 3.1.B. This integrated process allows for an efficient transition from the Design Phase into the Construction Phase, minimizing learning curves for the construction execution personnel. Because our Construction Team Leadership has been heavily involved in developing our Technical Solutions, our Team is ready and capable to construct the proposed and approved plans for the Project. Our commitment of these resources during the front end of the Project (approximately 15 percent) provides invaluable benefit to the primary Construction Phase (approximately 85 percent) and delivers a safe, quality, and economical solution for the MBTA, which allows for greater schedule certainty in completing the Project under the required timeline.

After project award, we will finalize the following site-specific plans that are compliant with the Technical and Contractual Provisions:

- Project Management Plan
- Project Execution Plan
- Quality Management Plan
- Safety, Security, and Emergency Management Plan

The following section details our Initial Project Management Plan.

3.1.A GLX CONSTRUCTORS' ORGANIZATION CHARTS

Proposed Design Organization

GLX Constructors' Design Team, led by STV, is experienced in rail transit design and remains committed to the Project goals. Figure 3.1-1 illustrates the relationships among our Design Team, including their direct interfaces with our Construction Team. For the resumes of the Design personnel to the level of Design Discipline Leads listed in the Proposed Design Organization Chart, we have included summary resumes within this section. For further reference, we have included detailed two page resumes in Appendix 1 - Design Discipline Lead Resumes at the end of Section 3.1.

Members on our Proposed Design Organization Chart will be 100 percent committed to the Green Line Extension DB Project throughout the Design Phase, until we have transitioned out of the Design Phase and into the Construction Phase, during which time the Design Team members will take on a supporting role to the Construction Team. When in their supporting role, the Design Team's commitment to the project will remain, but their time commitments will decrease, reducing the resource costs over the Project life.

GV20171052-001.INDD

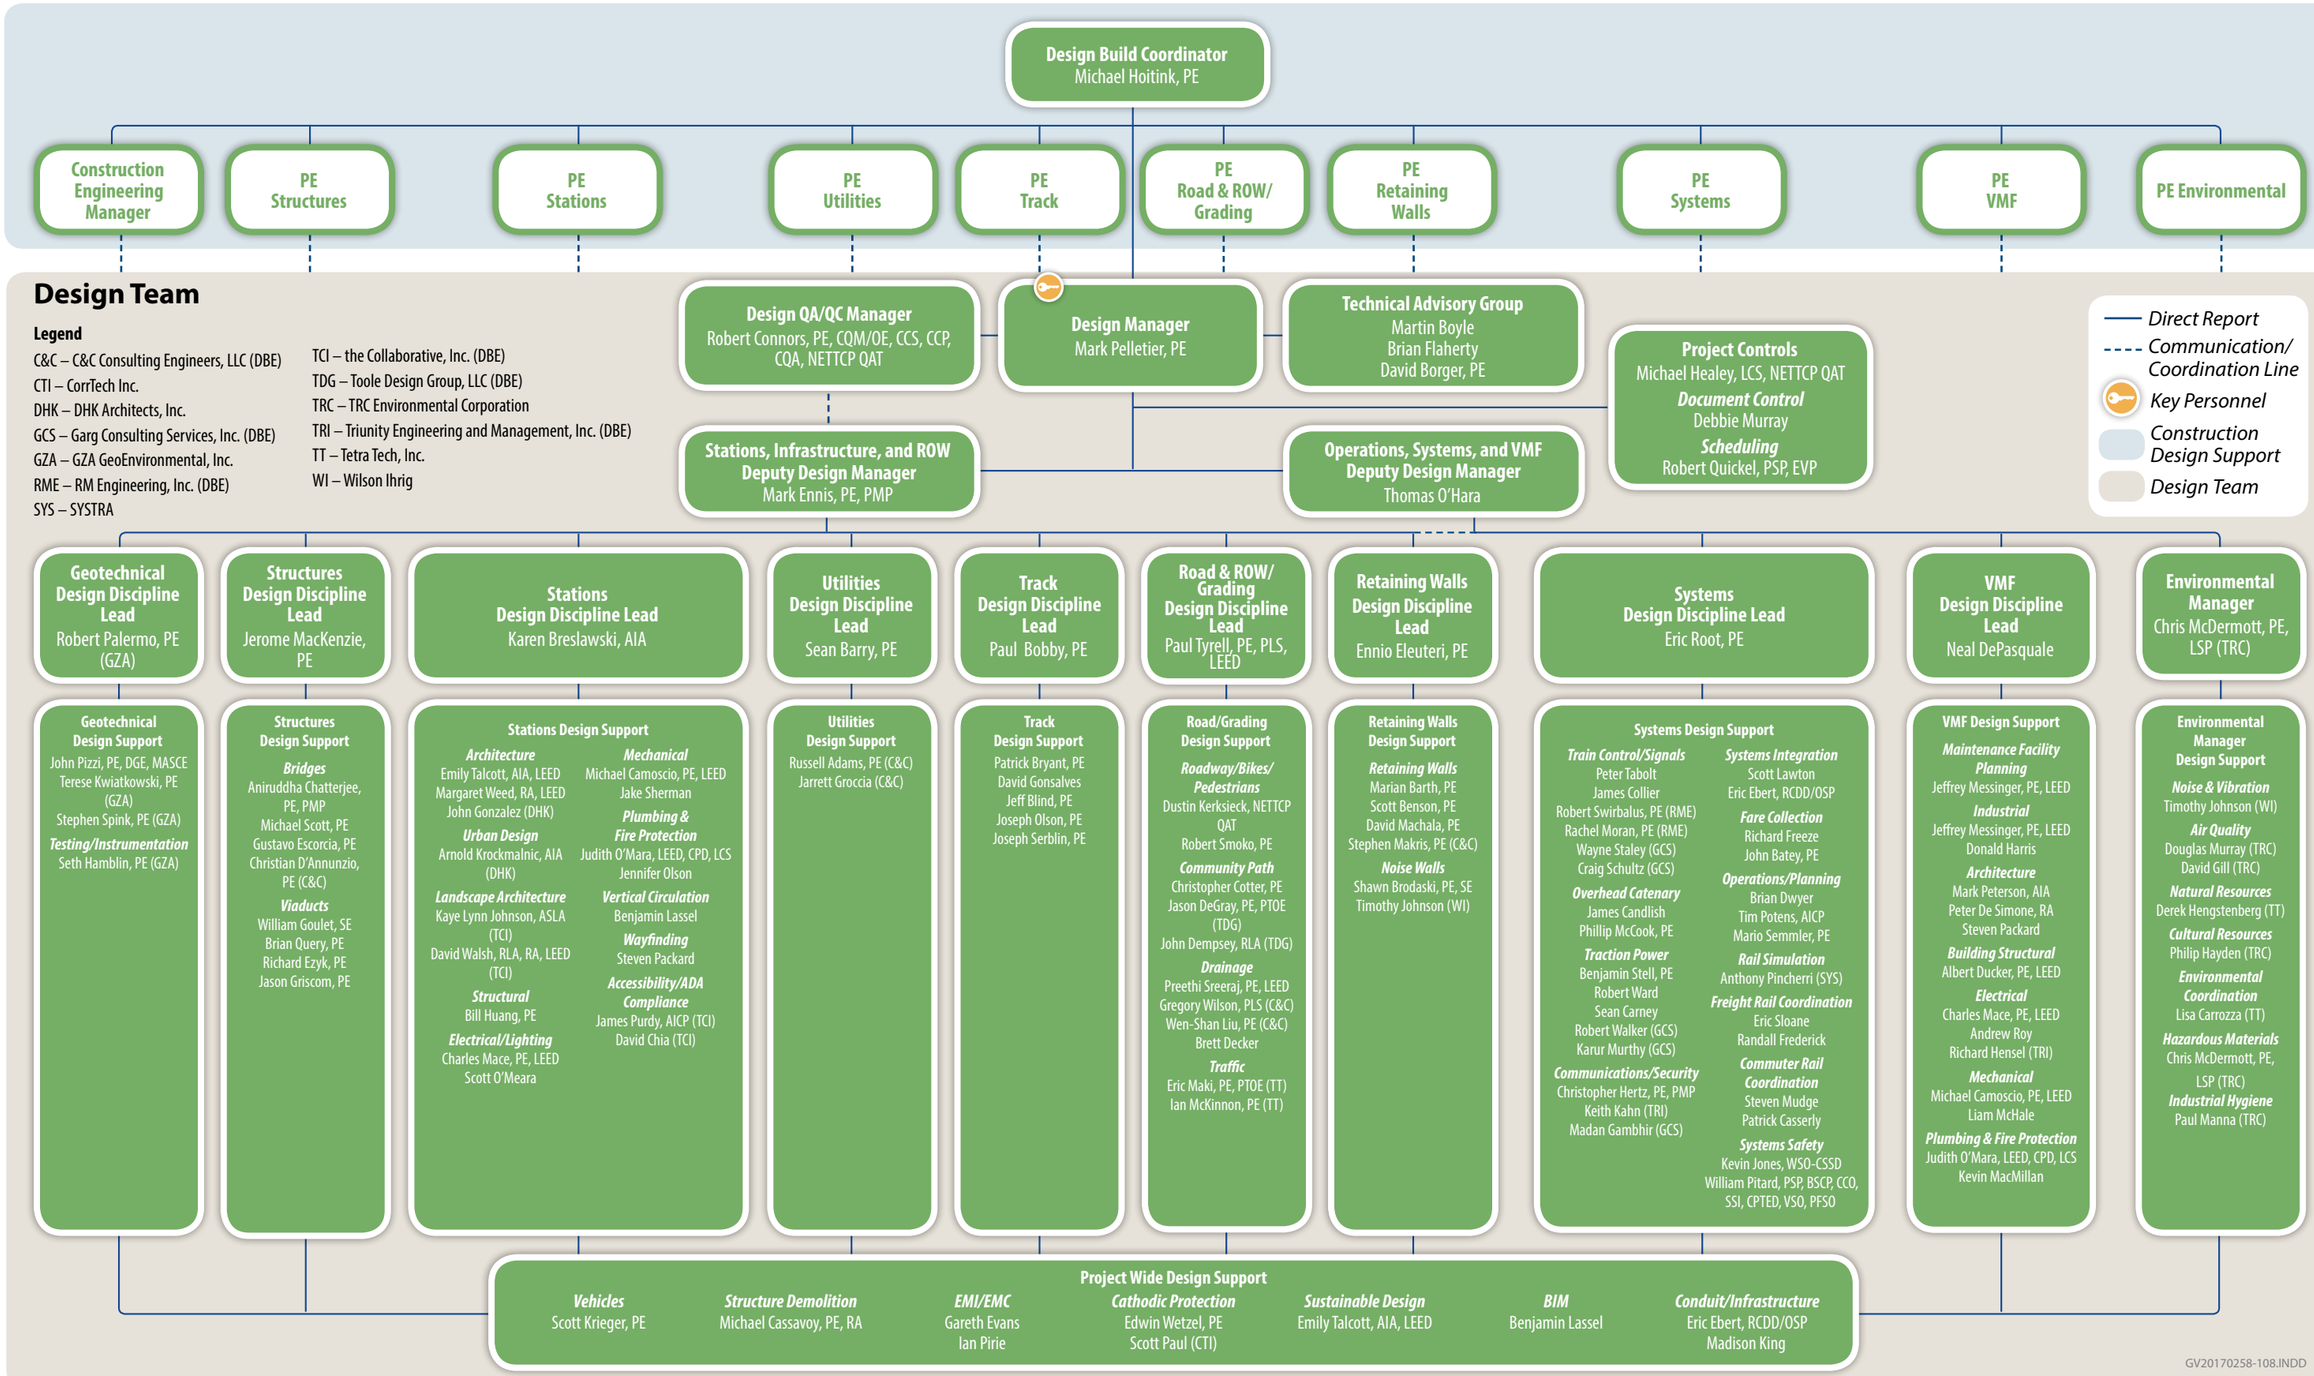


Figure 3.1-1. Proposed Design Organization. *Our Proposed Design Organization chart illustrates our proposed design organization, indicating the responsibilities and structure of the design staff and independent design check staff, down to and including discipline leads and the staff positions proposed in each discipline.*

GV20170258-118.INDD

Integrated Design and Construction Organization

Michael Hoitink, our Design Build (DB) Coordinator, will be a dedicated key lead for GLX Constructors, with the primary responsibility for fully integrating our Design Organization and execution with our Construction Team. Our Design Manager, Mark Pelletier, will report directly to Michael and retain responsibility for STV, our Lead Designer, and their subconsultants. Two Deputy Design Managers will support Mark:

- Mark Ennis, Deputy Design Manager, Stations, Infrastructure, and ROW
- Tom O'Hara, Deputy Design Manager, Operations, Systems, and VMF

Each Deputy Design Manager will lead multiple Design Discipline Leads who will initiate our TWGs. These TWGs are composed of:

- Design Discipline Lead, supporting the discipline designers
- Construction discipline Project Engineers and Superintendents
- The MBTA's discipline Technical Design Reviewers and appropriate third-party representatives

GLX Constructors' Safety, Quality, Environmental, Scheduling, and Cost Control Leads, as well as appropriate interdisciplinary design and construction personnel, will complete our TWG makeup.

This cross-pollination of all parties into the design effort secures the most cost-effective and efficient design solution with a focus on constructability. Early and active engagement – and focused collaboration of the construction, design, and interagency teams – is at the core of our construction-driven approach to design and construction execution.

> **"Communication and integration are crucial for successful execution.**

Summary Resumes for Design Personnel

Sean Barry, PE, Utilities Design Discipline Lead	
Education:	B.S., Civil Engineering, University of Massachusetts, Amherst
Professional License/ Certification:	Professional Engineer, MA #41802

Sean has more than 20 years of experience in the design and construction phases of civil engineering projects. He has provided engineering services for numerous utility and roadway projects that have involved the installation of water, sewer, drainage, gas, power, and telecommunications improvements.

City of Somerville, Central Broadway/Winter Hill Roadway and Streetscape Improvements Study and Design, Somerville, Massachusetts, Project Manager. Sean oversaw the design of roadway and streetscape improvements to a 1-mile corridor. He coordinated efforts with STV traffic engineers and survey, landscaping, and public outreach subconsultants.

MBTA, Greenbush Line Rail Restoration Design Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Project Engineer. Sean prepared site layout grading and drainage designs, as well design packages for various at-grade roadway crossings and seven rail stations, for the restoration of this commuter rail line.

MBTA, Wellington Carhouse Expansion and Improvements, Medford, Massachusetts, Lead Civil Engineer. Sean managed the development of civil plans and specifications for the MBTA's planned expansion and renovation of the Wellington Carhouse. His work involved coordinating with other design disciplines, including track, structural, electrical, traction power, plumbing, fire protection, and architectural professionals.

Town of Barnstable, Lincoln Road Reconstruction, Hyannis, Massachusetts, Project Manager. Sean is managing the development of plans for the $1.5 million reconstruction of 0.75 mile of roadway between Route 28 and West Main Street.

Paul Bobby, PE, Track Design Discipline Lead	
Education:	B.S., Civil Engineering, University of Wisconsin/Platteville
Professional License/ Certification:	Professional Engineer, Georgia # PE034469

Paul is a track designer with more than 15 years of experience in the design and construction of rail improvements.

City of Ottawa, O-Train Expansion, Ottawa, Ontario, Lead Track Engineer. Paul oversaw the design of track and acceptance inspection activities during the service expansion of the O-Train light rail transit system in Ottawa, Ontario.

IDOT, Granite City to St. Louis Corridor Phase I Environmental Studies, Granite City, Illinois and St. Louis, Missouri, Project Manager/Project Engineer. Paul is supervising preliminary engineering efforts for all work associated with the preparation of the Environmental Impact Study for the expansion of rail service between Granite City and St. Louis.

St. Louis Metro, East Riverfront Interlocking, St. Louis, Missouri, Project Engineer. Paul oversaw the track design for a new diamond interlocking located between St. Louis Metro's existing East Riverfront light-rail station and the Eads Bridge spanning the Mississippi River.

David Borger, PE, Technical Advisor	
Education:	M.S., Civil Engineering, New Jersey Institute of Technology B.S., Civil Engineering, Newark College of Engineering
Professional License/ Certification:	Registered Professional Civil Engineer, NJ # 24GE02673700 Professional Planner (PP), NJ# 33LI00402800

David has more than 40 years of experience in the supervision of complex systems and facility design including trackwork, communications, traction power, and signals.

NJ TRANSIT, Hudson-Bergen Light Rail Transit DBOM, Hudson and Bergen Counties, New Jersey, Systems Design Manager. David managed the industrial engineering design for the 10-mile-long initial operating segment of this $1 billion, 20-mile light rail system.

Metro Pasadena, Metro Blue Line (Gold Line) Light Rail, Los Angeles to East Pasadena, California, Principal-in-Charge. David held overall responsibility for the construction management of this light rail system. He was responsible for performing design and constructability reviews, resident engineering and inspection, QA/QC, systemwide and facilities engineering support, and systems integration.

RCTC, Perris Valley Line, Riverside to Perris, California, Principal-in-Charge. David is responsible for executive oversight of planning, design, and construction services for the 24-mile Riverside County Transportation Commission (RCTC) extension of the Metrolink commuter rail system.

GV20170258-118.INDD

SMART, Initial Operating Segment Design-Build, San Rafael to San Rose, California, Principal-in-Charge. David is providing executive oversight of design services for all civil, track, and structural improvements for the initial operating segment of Sonoma-Marin Area Rail Transit District (SMART) implementation of passenger rail service along the Northwestern Pacific Railroad corridor.

Martin Boyle, Technical Advisor

Education:	A.S., Business Administration, Fisher College

Martin, the MBTA's former Superintendent of Transmission and Distribution, has 50 years of experience managing the design, construction, and maintenance of electrified transit systems and vehicles.

City of Ottawa, Confederation Line LRT, Ottawa, Canada, Senior Advisor. Martin is serving as Senior Advisor responsible for providing supervisory support for development of preliminary engineering necessary for the transition of Ottawa's exclusive, fully built-out bus rapid transit system to an LRT network.

CATS, LYNX Blue Line Extension, Charlotte, North Carolina, Principal-in-Charge. As Principal-in-Charge, Martin has overall responsibility for transportation planning, environmental investigations and documentation, and preliminary engineering services to 65% design for a 9.3-mile extension of the Charlotte Area Transit System (CATS) Blue Line.

MBTA, Boston, Massachusetts, Former Superintendent of Transmission and Distribution. Martin directed and coordinated all operating activities for the Transmission and Distribution Division. He was responsible for the maintenance of 100 miles of catenary, 13 miles of trolley bus, 1,300 miles of DC cable, and 300 miles of AC cable.

Karen Breslawski, AIA, Stations Design Discipline Lead

Education:	M.S., Architecture, State University of New York, Buffalo B.A., Professional Studies in Architecture, State University of New York, Buffalo
Professional License/ Certification:	Registered Architect, Massachusetts National Council of Architectural Registration Boards

Karen is a Senior Architect with more than 30 years of experience in the planning, design, and development of transportation facilities for public agencies throughout Massachusetts.

NB Development Group, Boston Landing Station, Brighton, Massachusetts, Senior Architect. Karen oversaw the development of final architectural plans and provided construction administration for the new $26 million commuter rail station located adjacent to the New Balance headquarters in Brighton.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Architect. Karen was responsible for providing technical support for architectural aspects of the rehabilitation of the Longfellow Bridge. Karen led the review of the architectural design drawings and performed QC checking for the architectural portions of the project.

MBTA, Wellington Carhouse Expansion and Improvements, Medford, Massachusetts, Project Manager. Karen was responsible for coordinating a team of architects and engineers that developed final plans for a 12,000-sf single-bay addition to the east side of the 40-year-old building. Karen provided bid-phase support and assisted the MBTA with selecting a general contractor.

MBTA, Hingham Intermodal Center, Hingham, Massachusetts, Technical Advisor. Karen conducted QA/QC reviews for the design of the intermodal transportation facility to determine whether it met applicable codes, including ADA and Massachusetts Architectural Access Board standards.

MassDOT, Central Artery DO11A, Boston, Massachusetts, Project Manager. Karen oversaw the structural, civil, mechanical, and electrical elements along with the architectural pieces of the tunnel finishes for this portion of the Central Artery/Tunnel Project.

Robert Connors, PE, CQM/OE, CQA, CCS, CCP NETTCP QAT, Design Quality Assurance/Quality Control Manager	
Education:	M.S., Finance; Suffolk University M.S., Business Administration, Suffolk University B.S., Civil Engineering; University of Rhode Island
Professional License/ Certification:	Professional Engineer, MA Civil #39185 Professional Engineer, MA Structural #38924 Certified Manager of Quality/Organizational Excellence, ASQ #13209 Certified Quality Auditor, ASQ #41100 Certified Quality Assurance Technologist, NETTCP

Robert is a Senior Quality Manager with more than 30 years of experience in engineering and project oversight for clients including the MBTA and MassDOT.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Quality Administrator. Robert is directing the QC team in the preparation and administration of the design and construction quality plans for the design build rehabilitation of the Longfellow Bridge. Robert prepared quality management plans, trained project personnel on the plans, implemented the plans, audited performance, and implemented quality improvements for design and construction.

City of Ottawa, Confederation Line LRT, Ottawa, Ontario, Canada, Quality Control/Procurement Manager. Robert performed QC and prepared bridging documents as part of the procurement team for this $2.1 billion public-private partnership. Robert reviewed all components of the proposed project, including 13 stations, four of which are in a tunnel under downtown Ottawa between Bronson Avenue and the University of Ottawa.

WRTA, Bus Maintenance, Operations, and Storage Facility, Worcester, Massachusetts, QC Manager. Robert prepared the quality plan, trained to the plan, managed quality audits, and provided QC oversight for the design of a new vehicle maintenance, operations, and storage facility for the Worcester Regional Transit Authority (WRTA).

Metropolitan Washington Airport Authority, Dulles Corridor Metro Rail Phase 2 Project, Fairfax County, Virginia, External Quality Auditor. Robert performed FTA based quality auditing and related quality work for the Dulles Metrorail Project Management Procedures.

LIRR/MTA, East Side Access, New York, New York, External Quality Auditor. Robert performed quality auditing and related quality work for an FTA based audit of the General Engineering Consultant for this $10.8 billion project.

Neal Depasquale, VMF Design Discipline Lead	
Education:	B.S., Architectural Engineering; Wentworth College of Technology
Professional License/ Certification:	Massachusetts Certified Public Purchasing Official (MCPPO)

Neal is a Senior Project Manager with more than 35 years of experience supervising the study, design, and construction of various transportation and industrial projects for clients including the MBTA and MassDOT.

GV20171052-001.INDD

Amtrak, ARRA CM Services Southampton Yard, Boston, Massachusetts, On-Site Quality Control Engineer/Closeout Documentation. Neal provided QC services for $22 million in rail yard and maintenance facility improvements for this design build project at Southampton Yard. Neal's role included daily inspections of the work to ensure that the work adhered to safety requirements and design documents, specifications, and approved shop drawings.

Amtrak, Northeast Corridor Acela High-Speed Rail Maintenance Facilities Design-Build, Boston, Massachusetts and Queens, New York, Assistant Project Manager. Neal was responsible for overseeing the civil/site and utility design at the Southampton Yard in Boston and Sunnyside Yard in Queens.

WRTA, Vehicle Maintenance, Operations, and Storage Facility, Worcester, Massachusetts, Project Manager. Neal oversaw design services for a new, $75 million vehicle maintenance, operations, and storage facility for the Worcester Regional Transit Authority (WRTA).

MBTA, Green Line Copley Station Accessibility Improvements, Boston, Massachusetts, Project Manager. Neal oversaw the design and administrative duties for $20 million accessibility improvements and general renovation of historic underground Copley Station. Neal worked closely with these agencies to develop elaborate construction zones and traffic management plans in coordination with city officials and abutters.

Ennio Eleuteri, PE, Retaining Walls Design Discipline Lead

Education:	M.S., Civil Engineering, Northeastern University B.S., Civil Engineering, Northeastern University
Professional License/ Certification:	Professional Structural Engineer: MA, # EN41284-ST

Ennio is a structural engineer with more than 20 years of experience in design of various structural elements of roadways, bridges, and transit facilities for clients including the MBTA and MassDOT.

MBTA, Greenbush Line Rail Restoration Design-Build, Boston, Massachusetts, Lead Structures Engineer. Ennio performed and reviewed superstructure and substructure design calculations for 10 railroad and 8 highway bridge rehabilitations. He assessed six prestressed concrete box beam bridges, designed or reviewed designs for substructure abutments, and performed construction phase services for the construction of steel and concrete bridges.

NB Development Group, Boston Landing Station, Boston, Massachusetts, QA/QC Reviewer. Ennio conducted a QA/QC review of structural designs for this new MBTA commuter rail station under construction adjacent to the New Balance corporate headquarters.

MassDOT, Belden Bly Bridge, Lynn and Saugus, Massachusetts, Project Manager. Ennio is overseeing the replacement of the Belden Bly Bridge. He has also served as the point of contact for MassDOT's project manager for all technical and contractual issues.

MassDOT, Fore River Bridge Replacement, Quincy and Weymouth, Massachusetts, Lead Structural Engineer. Ennio is providing construction-phase support for a new $245 million vertical lift bridge. Ennio coordinated architectural, mechanical, and electrical disciplines and reviewed the final design developed by the design-build team.

South Shore Tri-Town Development Corporation, East-West Parkway Design-Build, Abington, Weymouth, and Rockland, Massachusetts, Senior Structural Engineer. Ennio performed design

reviews of bridges and retaining walls built along the eastern portion of the East-West Parkway. He also verified that the designs met contract requirements, MassDOT Bridge Manual standards, and AASHTO criteria.

J. Mark Ennis, PE, PMP, Deputy Design Manager Stations, Infrastructure, ROW	
Education:	M.S., Civil Engineering; Old Dominion University B.S., Civil Engineering; University College of Dublin
Professional License/ Certification:	Registered Professional Civil Engineer, Massachusetts

Mark has more than 25 years of varied experience involving new and rehabilitated bridge design, bridge confirmatory inspection and capacity ratings, retaining walls, and building design.

MBTA, Greenbush Line Rail Restoration Design Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Deputy Project Manager/Technical Coordinator. Mark oversaw the layout and design of 7 rail stations, 18 rail and highway bridges, 28 grade crossings, roadway intersections, 18 miles of track, and 2 railroad underpasses for the design-build project.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Design Lead. Mark provided design oversight and obtained design approval from regulatory and public agencies, including MassDOT, FHWA, MBTA, Massachusetts Department of Conservation and Recreation, U.S. Coast Guard, the City of Boston, the City of Cambridge, MassDEP, and the Historic Review Board (Section 106).

MassDOT, Fore River Bridge Replacement, Quincy and Weymouth, Massachusetts, Project Manager. Mark managed the preparation of estimates, type study reports, and sketch plans, as well as environmental permitting. He also oversaw construction support services.

Brian Flaherty, Technical Advisor	
Education:	Coursework, Civil Engineering, Hofstra University

Brian, STV's Design Build National Practice Leader, has more than 40 years of experience in the engineering and construction industry.

MBTA, Greenbush Line Rail Restoration Design Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Constructibility Coordinator. Brian served as Constructibility Coordinator responsible for coordinating all design efforts and developing constructibility reports for the 18-mile railroad rehabilitation project.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Constructibility Coordinator. Brian is serving as Constructibility Coordinator responsible for coordinating all design efforts and developing constructibility reports.

MTA, Capital Construction/LIRR East Side Access, Queens, New York, Constructibility Coordinator. Brian is serving as Constructibility Coordinator responsible for coordinating all design efforts and preparing constructibility reports for this $10 billion project.

NJ TRANSIT, Meadowlands Maintenance Complex, Kearny, New Jersey, Project Director. Brian directed the construction management of this major rail vehicle maintenance facility and yard. He was responsible for establishing the project procedures manuals, a QA/QC program, the project schedule, and a work breakdown structure to administer the budget for the duration of the project.

GV20171052-001.INDD

Michael Healey, LCS, NETTCP QAT, Project Controls Manager

Education:	B.S., Administration, University of Massachusetts at Amherst
Professional License/ Certification:	Licensed Construction Supervisor (LCS), Massachusetts # CS- 063675 Certified Quality Assurance Technologist, NETTCP Massachusetts Certified Public Purchasing Official (MCPPO)

Michael is a project controls expert and licensed construction supervisor with 38 years of experience providing contractor oversight, document control, requests for information responses, change-order management, and QA/QC to the MBTA.

MBTA, Greenbush Line Rail Restoration Design-Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Director of Project Controls and QA/QC. Michael was responsible for all document control functions related to the submittal of more than 100 individual design packages, from preliminary to final design.

MassDOT, Longfellow Bridge Rehabilitation Design-Build, Boston and Cambridge, Massachusetts, Project Controls Manager/Assistant QC Manager. Michael tracked change orders and reviewed civil, structural, and traffic control designs for the project. Michael tracked all project documentation, including cost and schedule records.

MBTA, Green Line Copley Station Accessibility Improvements, Boston, Massachusetts, Deputy Project Manager. Michael oversaw the day-to-day design and administrative duties for this project.

MBTA, Commuter Rail Maintenance Facility, Somerville, Massachusetts, Inspector. Michael conducted construction phase service site visits for coordination of disciplines.

Amtrak, ARRA CM Services Southampton Yard, Boston, Massachusetts, Senior Resident Engineer. Michael reviewed design-build submissions and performed QC inspection of all contractors' work to verify compliance with the approved plans and specifications.

Jerome Mackenzie, PE, Structures Design Discipline Lead

Education:	B.S., Civil Engineering, Northeastern University
Professional License/ Certification:	Professional Structural Engineer: MA #34740-ST

Jerome has more than 30 years of experience as a structural engineer, possessing a strong management background for the design of fixed and movable bridge rehabilitation and replacement projects for clients including the MBTA and MassDOT.

MBTA, Greenbush Line Rail Restoration Design-Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Senior Structural Engineer. Jerome reviewed the structural design for several rail bridges on this project.

MassDOT, Longfellow Bridge Rehabilitation Design-Build, Boston and Cambridge, Massachusetts, Lead Structural Design Engineer. Jerome oversaw teams of designers focused on the superstructure elements.

DART, LRT Extensions Phase I & Phase II, Dallas, Texas, Lead Bridge Engineer. Jerome oversaw preliminary through final design for three light rail and three heavy rail bridges for the project.

Metro-North, PECK Drawbridge and Bridgeport Railroad Viaduct Rehabilitation, Bridgeport, Connecticut, Structural Design Engineer/Inspector. Jerome performed a bridge inspection for the rehabilitation of the PECK Railroad Bridge.

MassDOT, University Avenue Bridge Improvements, Lowell, Massachusetts, Project Manager. Jerome managed the design and construction phases for the replacement of this historic steel deck truss bridge over the Merrimack River.

Christopher R. McDermott, PE, LSP, Environmental Manager

Education:	B.S., Engineering Sciences, Washington University, St. Louis, MO B.S., Applied Math and Physics, Providence College
Professional License/ Certification:	Licensed Site Professional, MA # 1955 Professional Engineer, MA # 48272

Christopher has more than 20 years of experience providing environmental engineering and Licensed Site Professional (LSP) services to large infrastructure and transportation projects in Massachusetts.

MassDOT, Longfellow Bridge Rehabilitation Design-Build, Boston and Cambridge, Massachusetts, LSP. Christopher managed the characterization of contaminated soil and all hazardous materials on the bridge, the MBTA Red Line right-of-way, the piers, towers and abutments, the Storrow Drive pedestrian walkway, and associated subsurface soil in the area.

WRTA, Vehicle Maintenance, Operations, and Storage Facility, Worcester, Massachusetts, LSP. Christopher directed extensive pre-construction characterization, developed plans, specifications, and cost estimates for soil remediation and a vapor barrier for the Worcester Regional Transit Authority (WRTA)'s new vehicle maintenance facility.

Bosfuel Corporation, MCP Compliance and Environmental Management during Pipeline Construction at Logan Airport, Boston, Massachusetts, LSP-of-Record/Project Manager. Christopher provided environmental investigation, remediation design, construction oversight and MCP compliance in support of Bosfuel's replacement of a portion of Logan's Fuel Delivery System (FDS).

MBTA, On-Call Environmental Services Contract, Boston, Massachusetts, Project Manager/LSP. Christopher provided environmental engineering and LSP services on several task orders, including the Durante Wetlands Mitigation remedial cost estimation and evaluation of groundwater remediation at Cabot Yard.

MBTA, Wellington Carhouse Expansion and Improvements, Medford, Massachusetts, LSP/Senior Engineer. Christopher performed the assessment of contaminated soil and hazardous building materials during the carhouse renovation.

MBTA, 12 Bridges Replacement Project, Boston, Massachusetts, Senior Engineer/LSP. Christopher directed the due diligence hazardous materials assessment of multiple bridges, as well as the evaluation of hazardous materials, including asbestos and lead-based paint, in existing bridge structures.

GV20171052-001.INDD

Thomas O'Hara, Deputy Design Manager Operations, Systems, and VMF	
Education:	Coursework, Business Management; Quincy Junior College
Professional License/ Certification:	Journeyman Electrician, Massachusetts Right-of-Way Training, Massachusetts Bay Transportation Authority

Thomas is an expert in transit operations and rail power systems who led the MBTA's Power Division for almost eight years. He has 34 years of experience in commissioning of new traction power substations, installation of OCS for the Silver Line, the AC cable replacement program, SCADA systems, and mobile substations, and is intimately familiar with MBTA operations, having directed and supervised the maintenance of local power systems, equipment, and transmission and distribution areas.

MBTA, Wellington Carhouse Expansion and Improvements, Medford, Massachusetts, Traction Power Specialist. Thomas coordinated with multiple disciplines to design the stinger trolley system for the expansion and renovation of the 120,000-sf Wellington Carhouse maintenance facility.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Systems Lead. Thomas coordinated with all the different disciplines to design the rail systems for MassDOT's rehabilitation of the Project. Thomas has also introduced a vital serial link for the signal system, which the MBTA approved.

MBTA, Orange Line Traction Power Upgrades, Boston, Massachusetts, Project Manager. Thomas has provided design, QA/QC, scheduling, and budget services for the project.

HMLP, Stray Current Testing and Evaluation, Boston, Massachusetts, Project Manager. Thomas oversaw the monitoring and evaluation of stray current within an area of the MBTA's Greenbush Line on behalf of Hingham Municipal Light & Power (HMLP).

MBTA, Operations Support GEC, Massachusetts, Project Manager. Thomas managed an on-call team of professional consultants that assisted with the maintenance of tracks, stations, vehicles, and maintenance facilities.

Robert J. Palermo, PE, Geotechnical Design Discipline Lead	
Education:	B.S., Civil Engineering, Northeastern University M.S. Studies, Massachusetts Institute of Technology
Professional License/ Certification:	Professional Engineer, MA No. 32053

Robert has more than 40 years of experience in all aspects of geotechnical engineering and underground construction on bridge and transit projects in the U.S. and Canada, including: soil and rock mechanics, shallow and deep foundation engineering, seismic design, underpinning, instrumentation and monitoring, ground improvement, construction dewatering, and lateral support systems.

NY State Freeway Authority, Tappan Zee Hudson River Crossing Design-Build, Tarrytown/South Nyack, New York, Lead Geotechnical Engineer. Robert was responsible for the foundation design performed during the Tender Design phase, as well as the subsurface explorations, pile load testing program, and engineering analyses performed during the final design phase.

MassDOT/MBTA, Multiple Bridges, Various Locations, Massachusetts, Lead Geotechnical Engineer/ Senior Technical Reviewer. Robert has served as the Lead Geotechnical Engineer/Senior Technical Reviewer on more than 100 replacement or rehabilitation bridge projects, some of which included use of accelerated bridge construction methods.

Amtrak, Hartford Line, Various locations, Connecticut and Massachusetts, Lead Geotechnical Engineer. Robert was responsible for the redesign of more than 8,000 lf of retaining wall to support Cooper E80 train loads as value engineering for the contractor, Middlesex Corporation. The redesign resulted in significant schedule and cost savings to the owner and the contractor.

MBTA/Delaware North, TD Garden, Boston, Massachusetts, Lead Geotechnical Engineer. Robert designed rock socketed caissons, load bearing elements, and lateral support walls for a new facility with 5 levels of below grade parking.

Mark W. Pelletier, PE, Design Manager

See Proposal Part 5 – Key Personnel and Experience Qualitative Evaluation Criteria for resume.

Eric Root, PE, Systems Design Discipline Lead

Education:	B.S., Electrical Engineering; Virginia Polytechnic Institute and State University
Professional License/ Certification:	Professional Engineer, VT Electrical #018.0107605

Eric is an electrical engineer with more than 27 years of experience involving transportation, utility, and power generation projects. His expertise includes systems project management, electric power systems, system start-up, interfaces for light rail transit and commuter systems, and controller design for clients including MassDOT.

City of Ottawa, Confederation Line LRT, Ottawa, Ontario, Canada, Traction Power Engineer. Eric completed the initial traction power design and analysis for the project to transform an exclusive, fully built-out bus rapid transit system into a light rail transit network – the first such conversion in North America.

Region of Waterloo, Rapid Transit Division ION LRT System, Ontario, Canada, Systems Manager. Eric is providing engineering services for the ION LRT system for the Region of Waterloo Rapid Transit Division. The 11.8-mile (19-km) network will operate 14 light rail vehicles across 22 stations.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Traction Power Engineer. Eric was responsible for both train control and traction power for this design build rehabilitation project

Metro East, San Fernando Valley Transit Corridor, Los Angeles, California, Systems/Traction Power Design Lead. Eric led rail systems and traction power design for proposed improvements to transit service and regional connections through the heart of Los Angeles's San Fernando Valley along Van Nuys Boulevard and San Fernando Road.

CATS, LYNX Blue Line Extension Light Rail Project, Charlotte, North Carolina, Systems Manager/ Traction Power Engineer. Eric was responsible for performing systems management for preliminary and final engineering services for the 9.3-mile Blue Line Extension for the Charlotte Area Transit System (CATS).

GV20171052-001.INDD

He was responsible for the sizing and location of traction power substations, and developed traction power technical reports and design criteria.

MassDOT, Red/Blue Line Connector, Boston, Massachusetts, Lead Systems Engineer. Eric performed load flow simulation for a proposed MassDOT project to extend the MBTA Blue Line 1,500 feet on the Bowdoin end while eliminating the existing Bowdoin Station and adding a new Charles/MGH Station. Eric's simulation also included installation of a new traction power substation and removal of an existing feeder from North Substation. The load flow simulation verified that the design met the operation criteria of 6-car trains running at 4-minute headways at crush load.

Paul Tyrell, PE, PLS, LEED AP BD+C, Road & Right-of-Way/Grading Design Discipline Lead

Education:	B.S., Civil Engineering; Wentworth Institute of Technology
Professional License/ Certification:	Registered Professional Civil Engineer, Massachusetts Professional Land Surveyor, Massachusetts LEED Accredited Professional

Paul is an accomplished professional engineer and land surveyor with 31 years of technical expertise in boundary and subdivision control law, easements and property rights issues, environmental permitting, hydraulics and hydrology, and trenchless technologies.

MBTA, Greenbush Line Rail Restoration Design-Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Senior Civil Engineer. Paul designed all required project utilities and utility relocations for the 18-mile-long reconstruction of the out-of-service railroad ROW. Paul oversaw preparation of more than 130 design packages with multiple submissions. He managed all utility design; was responsible for inventory, evaluation, relocation, and protection of more than 250 different utilities along the proposed alignment; and coordinated with the design-build contractor and numerous public and private agencies.

MassDOT, Longfellow Bridge Rehabilitation Design-Build, Boston and Cambridge, Massachusetts, Deputy Project Manager. Paul is responsible for coordinating design and construction for the design-build rehabilitation of the Longfellow Bridge. During the design phase, Paul coordinated design efforts for the entire design team including numerous subconsultants. He managed document control, design schedule, project submissions, and monitored QA/QC and permit compliance.

MBTA, Wellington Carhouse Expansion and Improvements, Medford, Massachusetts, Civil QA/QC Reviewer. Paul conducted a quality review and endorsed the final design submission for all civil components of the planned expansion and renovation of the Wellington Carhouse. Paul reviewed final designs and specifications for track alignment modifications within the carhouse and yard.

Amtrak, ARRA CM Services Southampton Yard, Boston, Massachusetts, Owner's Representative. Paul provided design review services for improvements to the Southampton Rail Yard. Paul provided construction management (CM) services, including review of all design-build submissions and QC inspections of all contractors' works to verify compliance with the approved plans and specifications.

Proposed Construction Organization

Our well-seasoned construction execution team has worked together extensively on past projects. Communication and integration are crucial for successful execution. In preparing for the Green Line Extension DB Project, we have revisited our previously established coordination plans for projects that are similar in size, complexity, and nature, and we have customized our plans to be Project-specific. Derived from multiple best practice construction management plans from our respective corporations, the MBTA can have full confidence that GLX Constructors has a solid construction approach that is fully tailored to achieve the MBTA's Project goals, cost, and schedule objectives.

Figure 3.1-2 illustrates the required relationships among the Construction Team. Our Construction Organization will be 100 percent dedicated to the Green Line Extension DB Project during the time in which their respective construction phases are ongoing. Our key personnel have been 100 percent dedicated to the Project since the Proposal Phase, and they will continue to be completely dedicated until completion of their scope of work.

Our Construction Team will be fully committed to the efficient execution and collaboration with the MBTA and Project stakeholders to mitigate risks, respond quickly to issues as they arise, and achieve the MBTA's goals to deliver the Project in a cost-effective, timely manner.

John West will lead GLX Constructors' Construction Team. Jamie Doyle, Aaron Neeley, Michael Hoitink, Sam Choy, and Robert Horn will support John and lead individual Construction Project Engineers and Superintendents managing the following disciplines:

- Stations
- Utilities
- Road and ROW/grading
- Systems
- Track
- Vehicle Maintenance Facility (VMF)
- Structures
- Retaining walls
- Environmental
- Geotechnical

We will mobilize these same construction discipline Project Engineers and Superintendents during the Design Phase of the Project to begin developing work plans and providing schedule input, engaging with third parties, performing constructability reviews, and refining the budget as the design progresses.

GV20171052-001.INDD

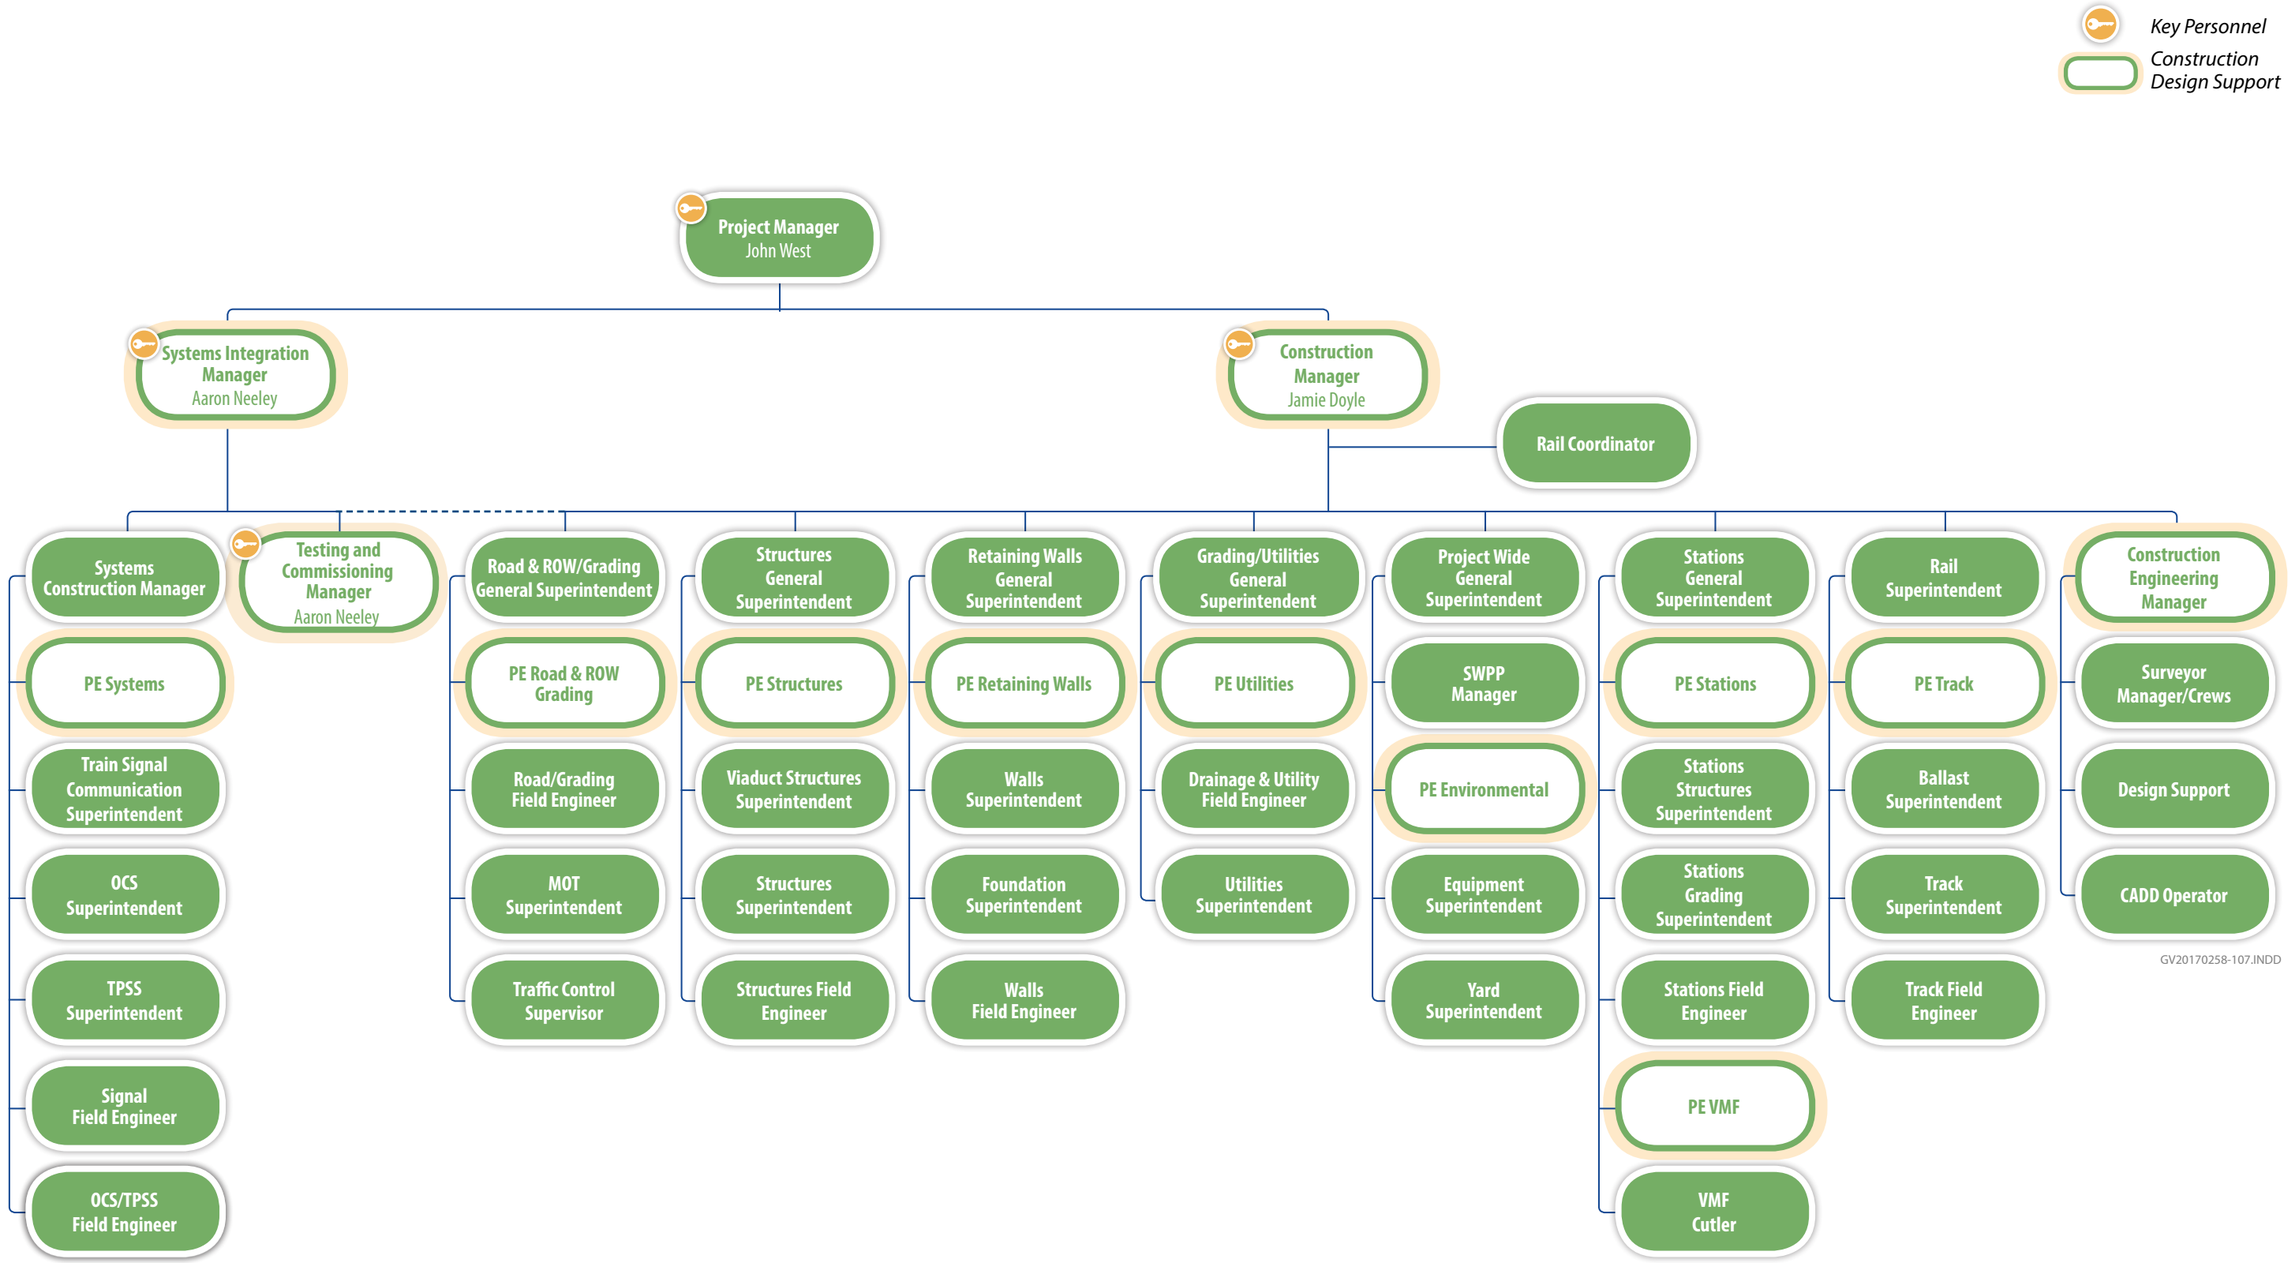


Figure 3.1-2. Proposed Construction Execution Organization. *Our Proposed Construction Execution Organization chart illustrates our proposed construction organization, indicating the responsibilities and structure of the construction staff, down to and including field superintendents and the staff positions proposed under each field superintendent for all shifts, and including systems integration and testing and commissioning functions.*

Proposed Project Organization

The firms that comprise GLX Constructors closely possess the skills and resources necessary to make the Green Line Extension DB Project a success, including extensive DB experience, applicable technical and construction expertise, and long-term working relationships with the MBTA and local major stakeholders. Using a fully integrated joint venture model and a best-person-for-the-job approach, we have carefully selected our project Personnel from our combined pool of resources.

Figure 3.1-3 represents GLX Constructors' integrated Project Organization chart, which illustrates how the Design Team and Construction Team will work together over the duration of the Project. Together they will provide a successful handoff for Testing and Commissioning and Closeout Phases.

Our Project Executive, Clyde Joseph, and Project Manager, John West, will lead the overall Project Management efforts through the Design and Construction Phases of the Project and through full Testing and Commissioning. Clyde and John will be jointly responsible for integrating the Safety, Quality, Design, Construction, and Business Teams to form a single, cohesive DB Management Team and will report directly to the MBTA Program Manager, John Dalton, for Contract Execution and to the JV Executive Committee for internal management decisions.

To provide an efficient and cost-effective DB Management Team organization, we engage Project Directors and their respective primary leaders at the onset of the Proposal Phase and throughout the Project Execution Phase. At the start of the Project Execution Phase, our DB Management Team will publish a refined and compliant Project Management Plan; Quality Management Plan (including a Design Quality Management Plan); Safety, Security, and Emergency Management Plan; and the project HSE Plan.

The DB Coordinator, Design Manager, and multiple Technical Design Discipline Leads manage our Design Team, completing and developing our Technical Solutions, in accordance with the Technical Provisions. Concurrently with the Design Team's efforts, the Construction Manager will mobilize our Construction Team, including the construction discipline Project Engineers and Superintendents. This critical group of Construction Team Lead personnel will directly integrate with the Design Discipline Leads and our TWGs.

Our Business Services Team will manage the construction scheduling, cost, document control, procurement, and finance functions of the Project.

Construction Discipline Project Engineers and Superintendents from our Construction Team will work directly with the Design Discipline Leads in our TWGs to seamlessly integrate the Project's Design and Construction Phases.

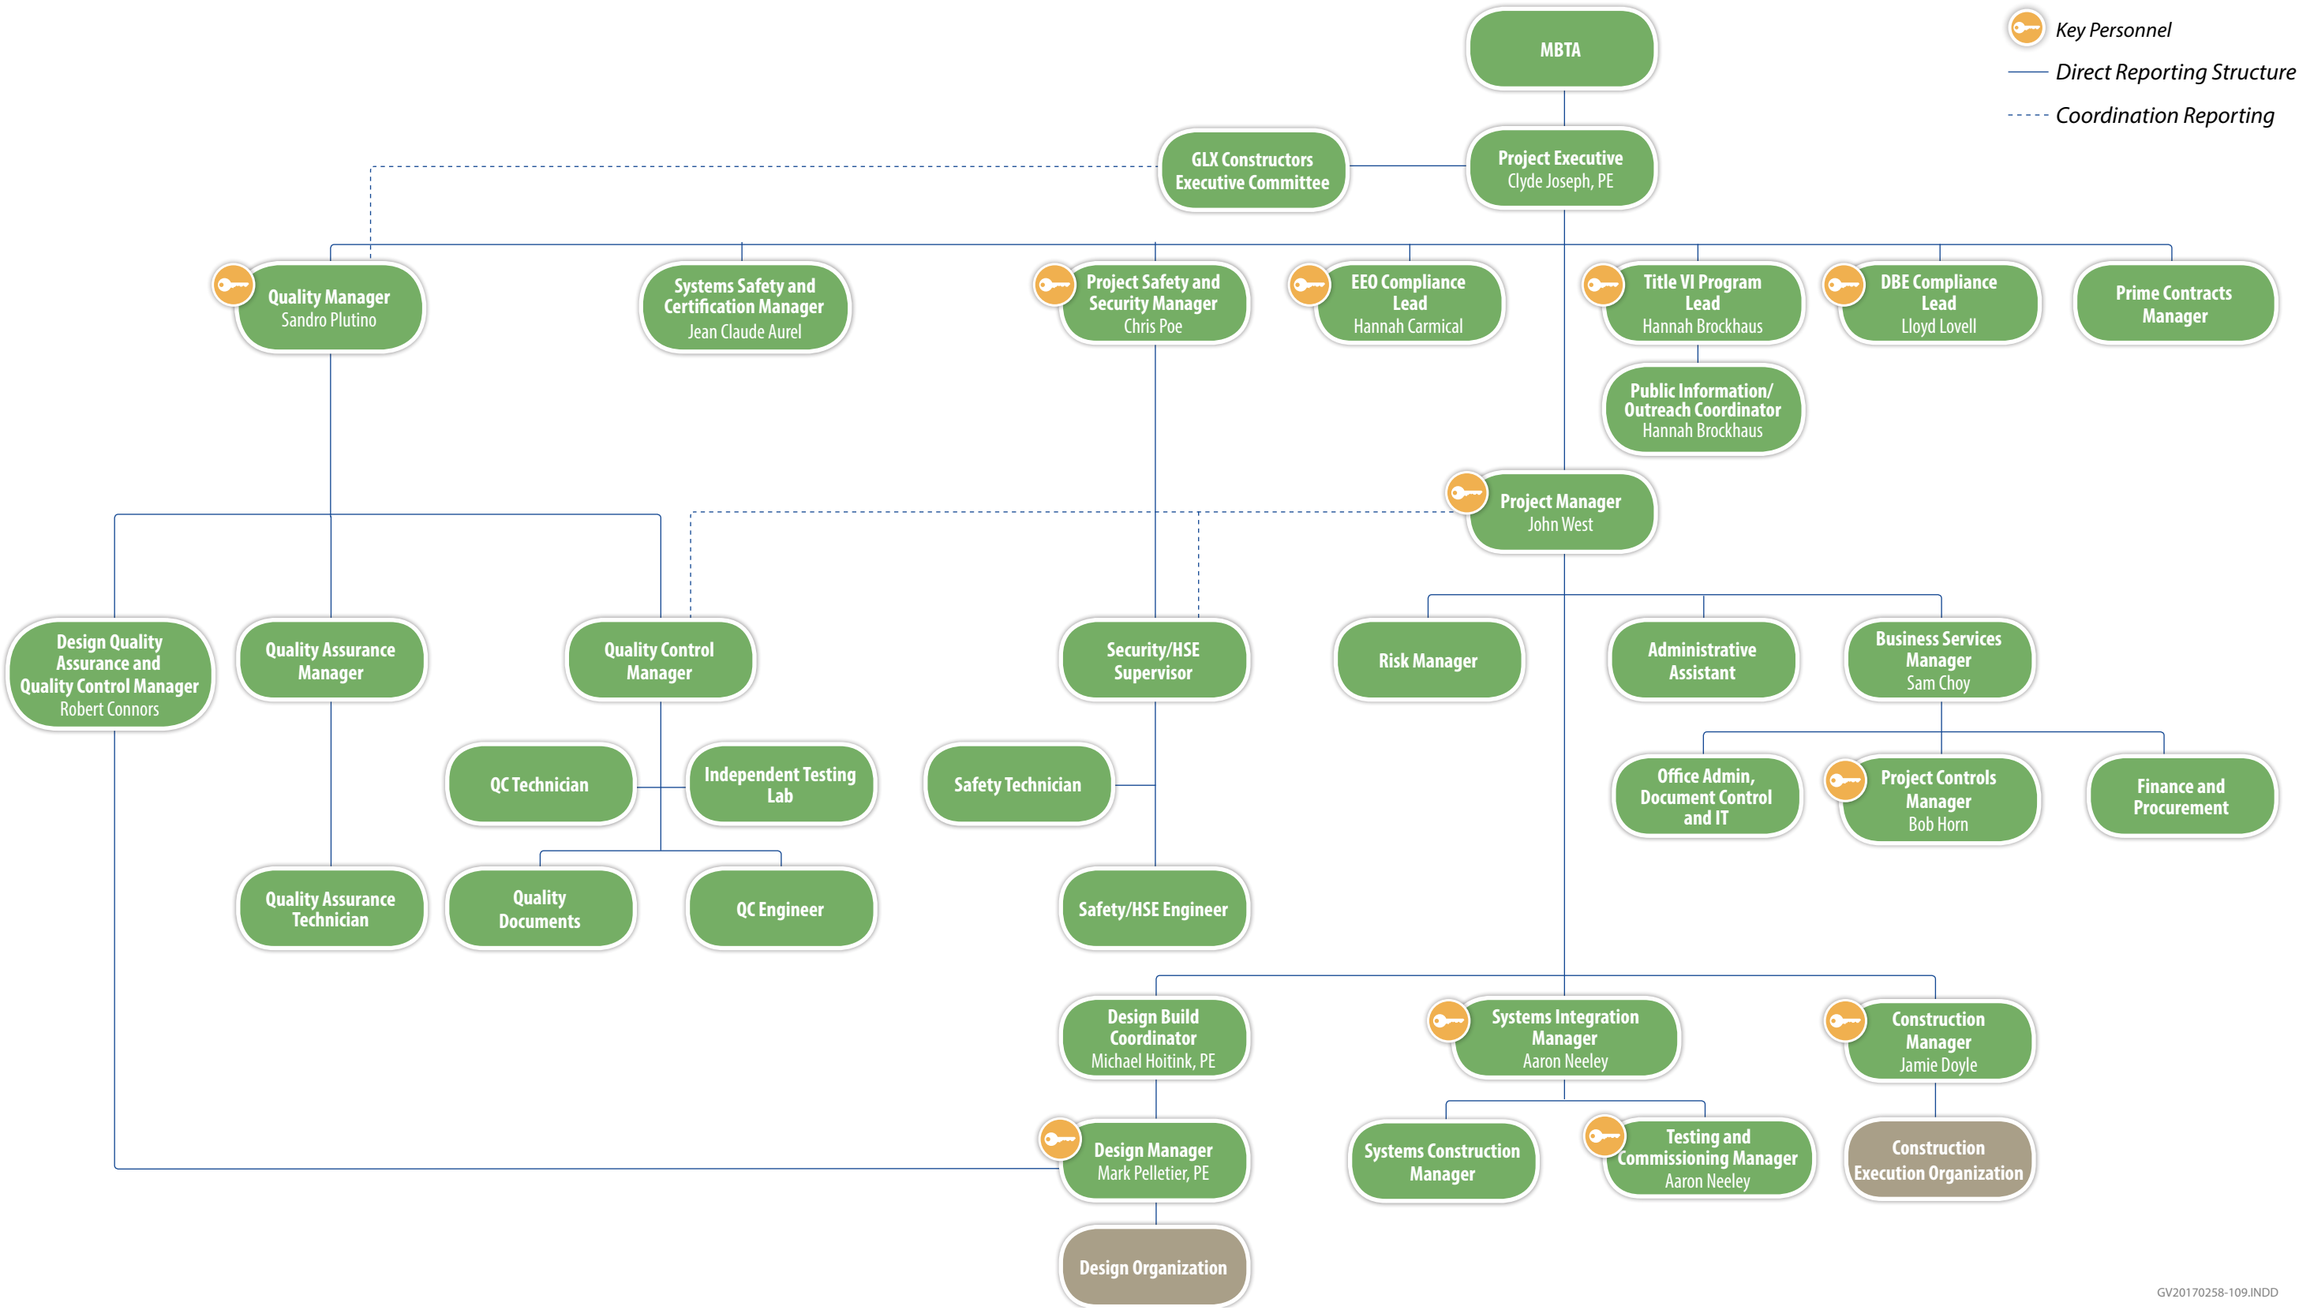


Figure 3.1-3. Proposed Project Management Organization. *Our Proposed Project Management Organization chart illustrates how the Design Organization and Construction Organization will work together over the duration of the Project.*

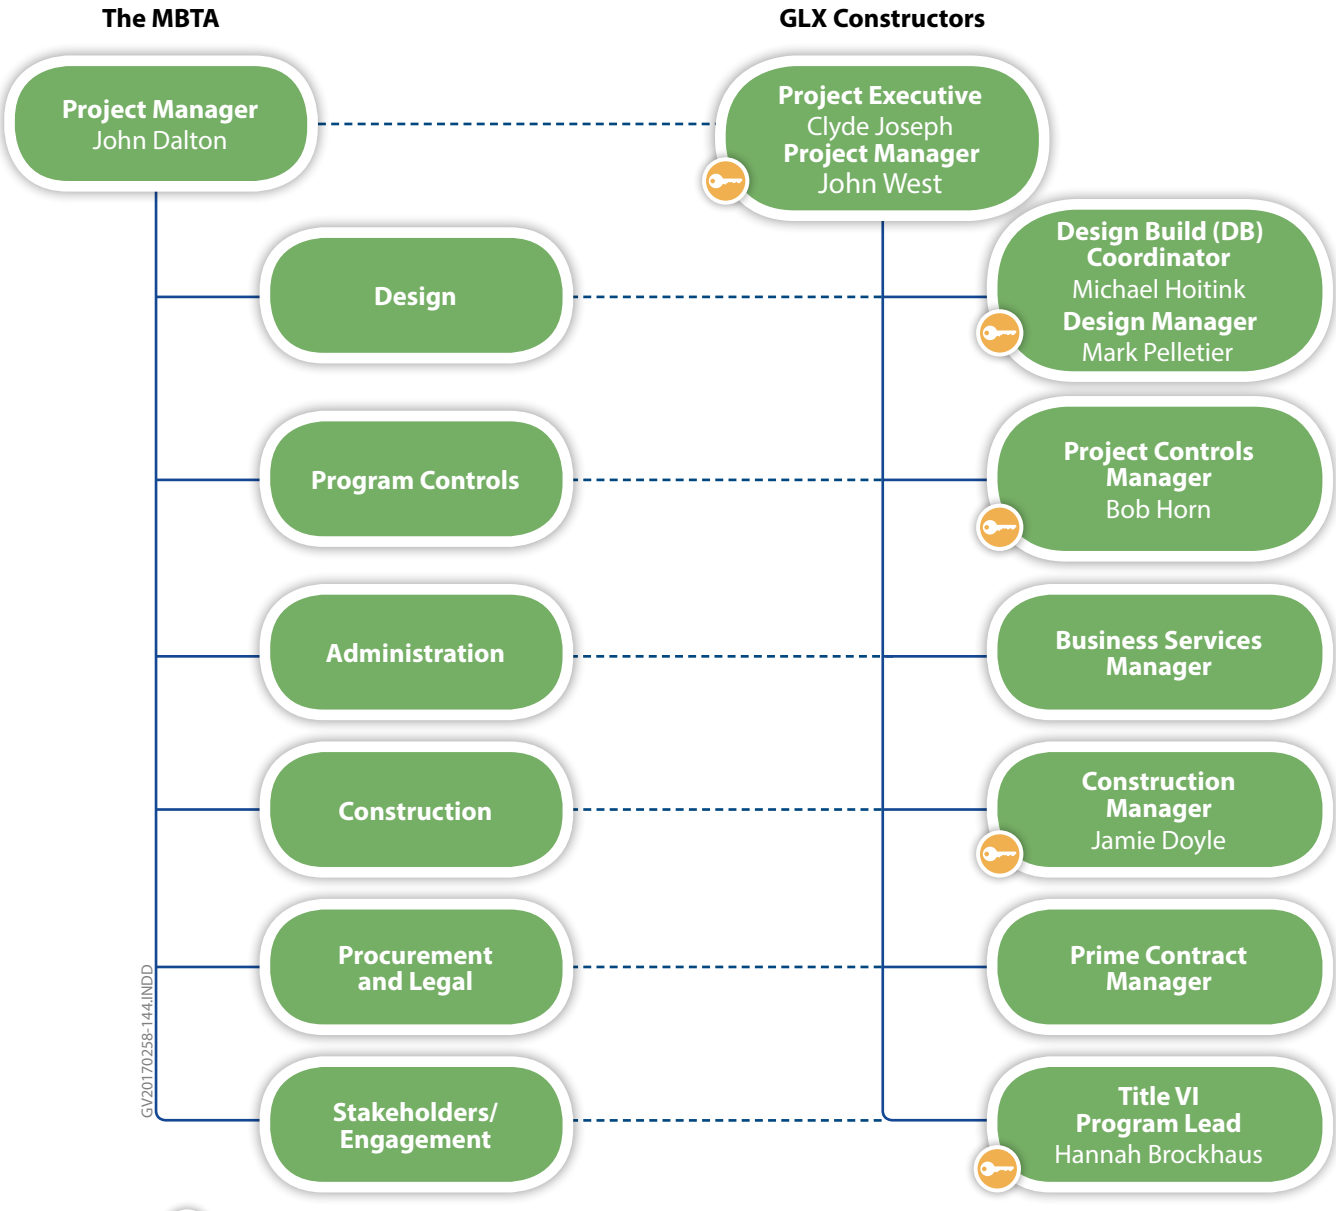


Figure 3.1-4. Interfaces between the MBTA and GLX Constructors. *GLX Constructors' collaborative approach to Project execution with the MBTA will facilitate direct lines of communication and transparency to get the job done right the first time.*

Important direct interfaces between GLX Constructors' team members with the MBTA's key team members are illustrated in Figure 3.1-4.

We have assembled GLX Constructors to provide transparent, effective, and efficient Project Management collaboratively with the MBTA and third-party stakeholders. Our Key Personnel are fully dedicated and committed to executing the Project, providing schedule and cost certainty for the MBTA.

3.1.B DESIGN MANAGEMENT CONCEPT

GLX Constructors' Lead Designer, STV, brings local and national expertise in DB project delivery, including the successful completion of some of the most complex, large-scale transportation projects in Massachusetts and across the United States.

STV has designated experienced and capable personnel to the Project. As residents of Boston, STV understands this Project is one of the most desired and needed transportation projects in the Commonwealth, and the allocation of their most highly qualified personnel to the GLX Constructors team is a direct reflection of this understanding. Through our commitment to providing excellent design staff to the MBTA, STV and GLX Constructors' design concept will provide the MBTA with the resources necessary to efficiently complete the Project from design through safety certifications, revenue operations, and closeout.

Mark Pelletier, PE
Design Manager

Michael Hoitink
Design Build Coordinator

Structure of GLX Constructors' Design Organization

Our DB Coordinator, Michael Hoitink, and Design Manager, Mark Pelletier, PE, will provide overall Design Project leadership during the Design Phase. Michael reports directly to Project Manager, John West, and he has the primary responsibility for fully integrating the design into construction. Our Design Manager, Mark, is responsible for delivering the fully approved design. Mark has an extensive record of successfully completing significant transit DB projects in Massachusetts and a long history of excellent work performed for the MBTA.

Mark Ennis
Deputy Design Manager
Stations, Infrastructure, and ROW

Thomas O'Hara
Deputy Design Manager
Operations, Systems, and Vehicle Maintenance Facility (VMF)

As our Design Manager on the Green Line Extension DB Project, Mark will:

- Provide direction to the Design Team and its subconsultants
- Interface with the MBTA and MassDOT through our DB Coordinator
- Collaborate with regulatory agencies that hold jurisdiction over the Project

GV20171052-001.INDD

Because of the magnitude and influence of the Green Line Extension DB Project, STV has assigned two Deputy Design Managers, Mark Ennis, PE, PMP, and Thomas O'Hara to our team to support the Project.

In our organization, the Deputy Design Managers will report directly to Mark Pelletier, our Design Manager leading the advancement of the Project. To this end, all deliverables will be consistently prepared with the program requirements, focused on meeting schedule, cost, and Contract requirements.

Design Discipline Leads

The next level of the design organization comprises the Design Discipline Leads. These leads facilitate the Project's overall technical design coordination effort. We have divided the Project into 10 major categories with their identified Design Discipline Leads.

Category	Design Discipline Lead
Stations	Karen Breslawski, AIA
Utilities	Sean Barry, PE
Road and ROW/grading	Paul Tyrell, PE, PLS, LEED
Systems	Eric Root, PE
Track	Paul Bobby, PE
VMF	Neal DePasquale
Structures	Jerome MacKenzie, PE
Retaining walls	Ennio Eleuteri, PE
Environmental	Chris McDermott, PE, LSP
Geotechnical	Robert Palermo, PE

Technical Working Groups (TWGs)

The TWGs will be composed of the Design Discipline Lead, Construction Discipline Project Engineers and Superintendents, the MBTA's discipline Technical Reviewers, and the appropriate third-party stakeholders as shown in Figure 3.1-5. The 10 TWGs will interact both formally through regularly scheduled meetings, and informally on a daily basis at the co-located office. For more information about the benefits of our co-located office, see Section 3.1.B.3.

By embedding the Construction Team, the MBTA, and third-party stakeholders into the TWGs, we advance our design and Technical Solutions in a cohesive manner, and we immediately address any potential issues surrounding constructability and work phasing during design development.

The Construction discipline's Project Engineers and Superintendents will oversee the Design Packages' transition from design into construction through the development of Construction Work Plans. To maintain

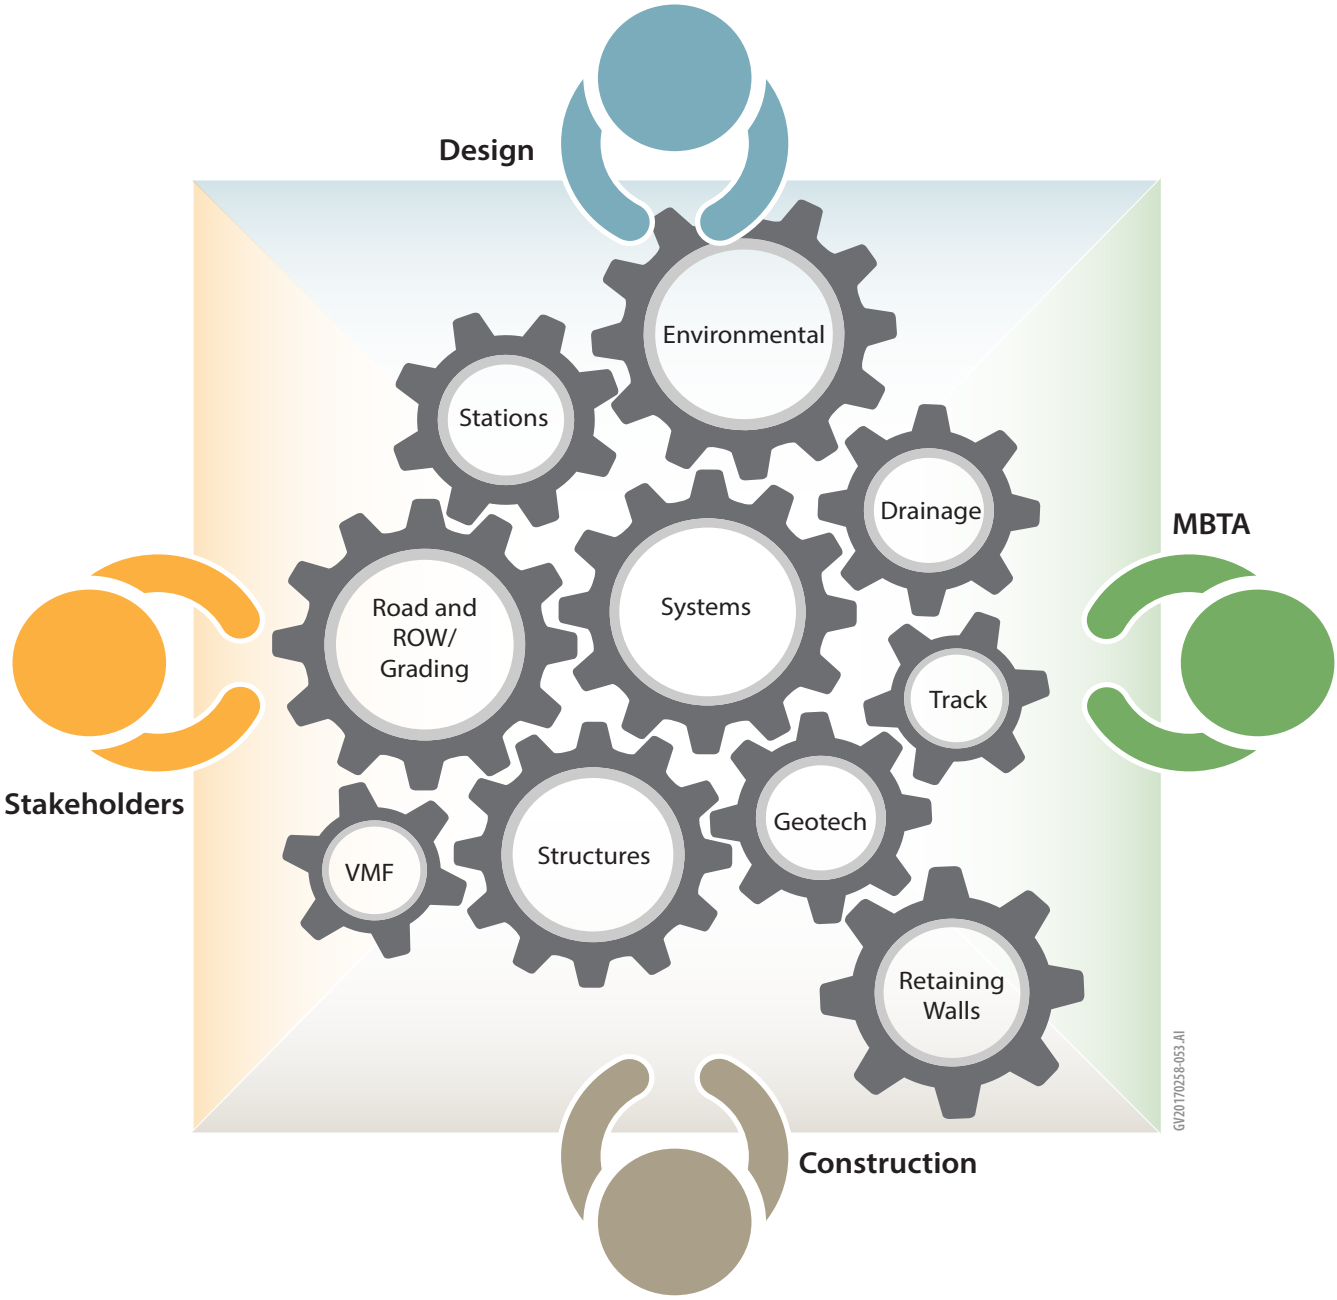


Figure 3.1-5. TWGs – a Seat at the Table. *By including the MBTA and third-party stakeholders in each of our TWGs, all design elements will function together as a piece of the whole design, which will be executed to meet or exceed the MBTA's requirements.*

collaboration and unity throughout the entirety of Project execution, the TWG structure will remain in effect during the Construction Phase, but with the design team transitioning to a supporting role.

These TWGs will fulfill the MBTA's requirements listed in Section 2.2.3.

To the Project's benefit, GLX Constructors has consistently held TWGs since the beginning of Proposal development. During the Proposal Phase, we have established a TWG Communications Plan, which supports holistic

integration by defining how we record and distribute design decisions made within each TWG. Further, the TWG Communication Plan identifies the protocol for interactions and information sharing with other groups, which expedites the design process and improves its quality.

The Design Discipline Leads are responsible for implementing and overseeing the TWG Communications Plan, for organizing Over-the-Shoulder Reviews, Progress Reviews, and other interactions with the MBTA's Design Review Team. We will include the MBTA's discipline Lead Reviewers and appropriate third-party stakeholders in each Technical Working Group for the duration of the Design Phase and Construction Phase. During these informal reviews, we will partner with MBTA to address any potential issues or conflicts. By doing so, we will have issues resolved prior to the formal Design Package submittal.

We will conduct internal weekly Progress Meetings, scheduled ahead of the MBTA's weekly Progress Meetings. The Design Discipline Leads will meet with the Design Manager, the Deputy Design Managers, and the DB Coordinator to address the design status, coordinate the efforts between TWGs, identify any significant concerns or potential issues raised by each TWG, and provide an update for the formal Progress Meeting.

GLX Constructors will interface with the MBTA on a daily basis and with third parties as required for approvals and design completion. The Design Management Team will participate in relevant meetings identified in Volume 2, Section 2.2 of the Contract. A summary of the recurring meetings identified in Volume 2, Section 2.2 is presented in Figure 3.1-6.

Construction supports Design, which supports Construction.

Construction-driven execution embeds Construction Project Engineers within the Design Phase, then reverses and embeds Design Discipline Leads within the Construction Phase.

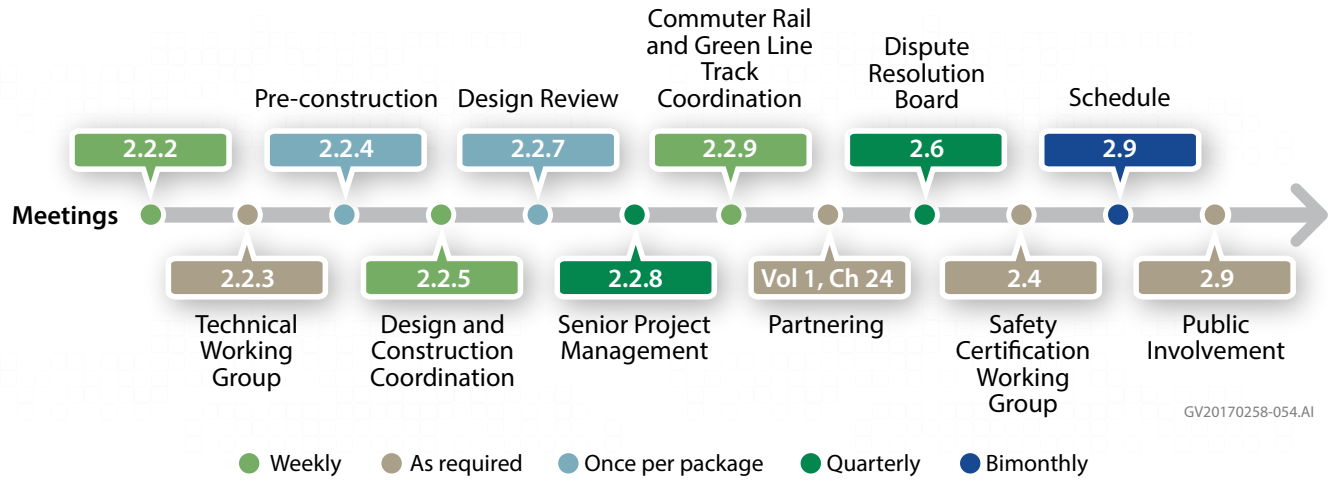


Figure 3.1-6. Minimum Mandatory Project Meetings with the MBTA and Other Parties. *Regularly scheduled meetings will mitigate or eliminate issues before they arise and smooth the seam between the Design and Construction Phases of the Project.*

Design Packages

Figure 3.1-7 details our Design Package structure. As indicated, each Design Package will be assigned to one of the Design Discipline Leads who have the daily responsibility for design execution. It is the Design Discipline Leads' responsibility to confirm that the work is performed in accordance with both the Contract, and the Safety and Quality Management Plans.

Design Package	Technical Working Group	Discipline Design Leads (All Co-Located)	Package Manager	30% Basis of Design	60% Preliminary Design	90% Final Design	RFC Submission
Medford Street Bridge	Structures	Jerome MacKenzie	Gustavo Escoria	■		■	■
Broadway Bridge	Structures	Jerome MacKenzie	Ani Chatterjee	■		■	■
Cedar Street Bridge	Structures	Jerome MacKenzie	Michael Scott	■		■	■
College Avenue Roadway and Ped Bridges	Structures	Jerome MacKenzie	Christian D'Annunzio	■		■	■
School Street Bridge	Structures	Jerome MacKenzie	Christian D'Annunzio	■		■	■
Walnut Street Bridge	Structures	Jerome MacKenzie	Michael Scott	■		■	■
Lowell Street Bridge	Structures	Jerome MacKenzie	Gustavo Escoria	■		■	■
Magoun Square Station	Stations	Karen Breslawski	Benjamin Lassel	■	■	■	■
Gilman Square Station	Stations	Karen Breslawski	Benjamin Lassel	■	■	■	■
College Avenue Station	Stations	Karen Breslawski	Margret Weed	■	■	■	■
East Somerville Station	Stations	Karen Breslawski	Emily Talcott	■	■	■	■
Ball Square Station	Stations	Karen Breslawski	Margret Weed	■	■	■	■
Lechmere Station	Stations	Karen Breslawski	John Gonzalez	■	■	■	■
Union Square Station	Stations	Karen Breslawski	Emily Talcott	■	■	■	■
Viaduct – Pier 1 thru Pier 7 (Lechmere)	Structures	Jerome MacKenzie	William Goulet	■		■	■
Viaduct – Pier 7 thru Pier 21 (Lechmere/Medford Branch)	Structures	Jerome MacKenzie	Brian Query	■		■	■
Viaduct – Pier 21 thru Abut 37 (Medford Branch)	Structures	Jerome MacKenzie	William Goulet	■		■	■
Viaduct – Union Square Eastbound	Structures	Jerome MacKenzie	Jason Griscom	■		■	■
Viaduct – Union Square Westbound	Structures	Jerome MacKenzie	Richard Ezyk	■		■	■
Walls (1)	Retaining Walls	Ennio Eleuteri	Marian Barth	■		■	■
Walls (2)	Retaining Walls	Ennio Eleuteri	Scott Benson	■	■	■	■
Walls (3)	Retaining Walls	Ennio Eleuteri	David Machalla	■	■	■	■
Walls (4)	Retaining Walls	Ennio Eleuteri	Stephen Makris	■	■	■	■
Track Medford and Union Branches, Commuter Rail	Track	Paul Bobby	Patrick Bryant	■	■	■	■

Design Package	Technical Working Group	Discipline Design Leads (All Co-Located)	Package Manager	30% Basis of Design	60% Preliminary Design	90% Final Design	RFC Submission
Rail Yard Track	Track	Paul Bobby	David Gonsalves	■	■	■	■
Drainage (Watershed 1)	Roadway/Grading	Paul Tyrell	Preethi Sreeraj	■		■	■
Drainage (Watershed 2)	Roadway/Grading	Paul Tyrell	Preethi Sreeraj	■		■	■
Drainage (Watershed 3)	Roadway/Grading	Paul Tyrell	Gregory Wilson	■		■	■
Drainage (Watershed 4)	Roadway/Grading	Paul Tyrell	Gregory Wilson	■		■	■
Pump Stations	Roadway/Grading	Paul Tyrell	Judith O'Mara	■		■	■
Washington Street Rail Bridge	Structures	Jerome MacKenzie	Ani Chatterjee	■		■	■
Medford St and Harvard St Rail Bridges	Structures	Jerome MacKenzie	Michael Scott	■		■	■
Signals	Systems	Eric Root	James Collier	■	■	■	■
Power and OCS	Systems	Eric Root	James Candlish	■	■	■	■
Red Bridge Traction Power Sub-Station	Systems	Eric Root	Robert Ward	■	■	■	■
Ball Square Traction Power Sub-Station	Systems	Eric Root	Robert Ward	■	■	■	■
Pearl Street Traction Power Sub-Station	Systems	Eric Root	Robert Ward	■	■	■	■
Communications	Systems	Eric Root	Chris Hertz	■	■	■	■
VMF and Rail Yard – Site Preparation	VMF/Buildings	Neal DePasquale	David Gonsalves	■		■	■
Vehicle Maintenance Facility	VMF/Buildings	Neal DePasquale	Steve Packard	■	■	■	■
Transportation Building	VMF/Buildings	Neal DePasquale	Peter Di Simone	■	■	■	■
Community Path – Civil/Lighting/ Communications	Roadway/Grading	Paul Tyrell	Christopher Cotter	■	■	■	■
Community Path – Structural	Structures	Jerome MacKenzie	Scott Benson	■	■	■	■
Off Site Intersections	Roadway/Grading	Paul Tyrell	Erik Maki	■	■	■	■
VMF Site Building Demolition	VMF/Buildings	Neal DePasquale	Chris McDermott	■		■	■
Gilman Square Station Site Building Demolition	VMF/Buildings	Neal DePasquale	Chris McDermott	■		■	■
Ball Square Site Building Demolition	VMF/Buildings	Neal DePasquale	Chris McDermott	■		■	■
Utility Bridges	Structures	Jerome MacKenzie	Michael Scott	■	■	■	■
Fences and Landscaping	Roadway/Grading	Paul Tyrell	Sean Barry	■	■	■	■

Figure 3.1-7. Design Package Structure. *Each Design Package will be assigned to one of the Design Discipline Leads who have the daily responsibility for design execution.*

Our Design Management Plan requires an inter-disciplinary review where the Design Discipline Lead presents the proposed technical solution to other design discipline Leads for review and coordination, ensuring a "holistic" design that is complementary among and across all disciplines. This inter-disciplinary review occurs prior to submission for review and approval by the MBTA. Most recently, STV successfully implemented this strategy on the Longfellow Bridge Rehabilitation Project, a project in which extensive interdependency between 40 separate Design Packages was required. GLX Constructors has included this same coordination review procedure in our Quality Management Plan.

Resources and Personnel Needed to Effectively and Efficiently Manage the Project During the Design Phase

Our Design Team utilizes resource-loaded scheduling methods to identify the number of personnel required completing each Design Package, the schedule for each, and consequently, the total number of designers needed on a weekly basis for the duration of design activities. As evidenced by our Key Personnel throughout Project Execution, illustrated in Figure 3.1-7, GLX Constructors will maintain a versatile and experienced DB Management Team that is closely familiar with the MBTA's and the FTA's procedures and practices to support the Design Team. In similar fashion, GLX Constructors will be responsible for proper document control, scope conformance, schedule adherence, and for implementing the Quality Management Plan.

Our Design Management Team – Michael Hoitink, Mark Pelletier, Mark Ennis, and Tom O'Hara – will support the Design Discipline Leads in preparing each Design Package submittal. Prior to submission, our DB Coordinator, Michael Hoitink, will be responsible for confirming that each package conforms to the Quality Management Plan and to the requirements of the Contract Volume 2, Section 2.7.4. For each Design Package, we will complete the corresponding checklist, and our final Design Package submission will conform to the Contract.

GLX Constructors and our Design Team understand that 17 items are required to be submitted for each Preliminary Design Submission (30%), 16 items are required for each Intermediate Design Submission (60%), and 14 items are required for each Pre-release for Construction Submission (90%) for the MBTA's review.

Management and Integration of Subcontractors and Suppliers

We will manage our design subconsultants as an extension of our own Design Team. This means they will be fully integrated into our Design Team, attend our TWG meetings, and work from our co-located Project Office with the MBTA. Co-location is critical to the success of this Project, as discussed in further detail below. Where utilized, suppliers will provide detailed

GV20171052-001.INDD

Personnel Resources					
Key Personnel	**Name**	**Design Phase**	**Construction Phase**	**Testing and Commissioning Phase**	**Closeout Phase**
Project Manager	John West	→	→	→	→
Project Safety and Security Manager	Chris Poe	→	→	→	→
Construction Manager	Janie Doyle	→	→	→	
Design Manager	Mark Pelletier	→	→		
Project Controls Manager	Robert Horn	→	→	→	→
Systems Integration Manager	Aaron Neeley	→	→	→	→
Quality Manager	Sandro Plution	→	→	→	→
Title VI Program Lead	Hannah Brockhaus	→	→	→	→
EEO Compliance Lead	Hannah Carmical	→	→	→	→
DBE Compliance Lead	Lloyd Lovell	→	→	→	→
Testing and Commissioning Manager	Aaron Neeley	→	→	→	

GV20170258-160.INDD

Figure 3.1-7. GLX Constructors' Key Staffing on the Project from Design to Closeout. *As it is with our Key Personnel, our staffing durations are critical to managing the Project from the Design Phase until Project Closeout.*

documentation about their products so we can properly evaluate the product for compliance and inclusion within the Design Specifications and Drawings.

Our Design Team has extensive working experience with our selected subconsultants – often on alternative delivery projects with accelerated schedules. For example, during the design of the Longfellow Bridge Rehabilitation DB Project, STV worked with Chris McDermott of TRC, our GLX Environmental Design Consultant, to mitigate the unexpected discovery of contaminated soils located in the Longfellow towers. To avoid a schedule delay, it was necessary to take immediate and proactive action. In coordination with the DB Contractor, Chris worked closely with several STV staff members through the Civil and Environmental Technical Working Groups to prevent schedule slippage. To provide an added layer of benefit to the MBTA, GLX Constructors has implemented our TWG processes in the same manner they were coordinated on the Longfellow Bridge Rehabilitation DB Project.



On the MBTA's Greenbush Commuter Rail Project, the alignment included many hazardous conditions. As part of the project execution team, GLX Constructors' team member, Balfour Beatty, was part of the Joint Venture that achieved a superior safety record throughout the project, including worker safety and the potential impacts to the public. For example, Balfour Beatty was responsible for all testing and commissioning of the system working in partnership with the MBTA's Operator and FTA inspectors. This involved staged testing of each crossing, following which testing was performed on a live track using operator-provided locomotives on the four-quad crossing gate systems, which the MBTA had not previously used. The work under live track was successfully completed in accordance with Balfour Beatty's site-specific safety plan.

Where Different Elements of the Design will be Performed

GLX Constructors' Design Management Team, Design Discipline Leads, subconsultants, and necessary support staff will be co-located with GLX Constructors at the Green Line Extension DB Project Office site, designated by the MBTA, at 200 Innerbelt Road, Somerville, Massachusetts. By co-locating at the MBTA's Project Office site, we will be able to simply walk down the hallway to resolve issues or receive answers to pertinent questions. Co-location flattens the organization and produces quick results in real-time.

Our Design Team will perform the majority of the design work at the co-located Project Office, and we will supplement any remaining design work from satellite STV offices in Boston, Chicago, and Charlotte, utilizing our regional and national resources. The Design Team will manage these supplemental design resources from the co-located Project Office.

3.1.C CONSTRUCTION MANAGEMENT CONCEPT

> **We plan on moving excavated materials by rail to a designated point for processing. This will take trucks off the streets along the alignment.**

GLX Constructors has defined our Project Management approach as "construction-driven execution." Our process involves five key actions for execution. These five actions will provide for a more efficient construction project, elevated schedule and cost certainty, and in the successful end, a satisfied Client, stakeholders, and community members. The five actions are:

1. **Engage Early and Often.** To get timely "buy in" from the Construction Team, the Design Team engages early and often with the Construction Team and the MBTA personnel that are involved in the early Design and Project Implementation Phases.

2. **Construction Advice.** Early and often through constructability reviews, interdisciplinary reviews, and recommendations for construction efficiency.

3. **Ask which Cost-Effective Construction Solutions are Best for the Construction Team.** Because the majority of Project costs are associated with the physical construction and materials, our process emphasizes this phase to develop cost-effective solutions.

4. **Long-Term Solutions.** We focus on long-term goals rather than short-term deadlines.

5. **Construction Efficiency and Productivity.** We prioritize field efficiency and productivity over the needs of any one discipline or area. This is likewise driven by interdisciplinary reviews to make certain one discipline does not design in a vacuum; rather, each discipline produces a holistic design that can be constructed in accordance with the Contract.

Our construction-driven execution approach begins with incorporating safety into the start of any process or procedure. Our commitment to safety is paramount, and it will not be sacrificed for cost or productivity. It is appropriate to present our commitment to Safety as the first and primary step in our Project Management Plan.

GLX Constructors' first priority is safe and secure Project execution. The following highlights our HSE Program, which is drawn from Fluor Enterprise's global, company-wide safety program and adopted to promote HSE processes in executing the Green Line Extension DB Project.

We have based our HSE Management System on a Continuous Improvement Model as contained in international standards such as ANSI Z 10, OHSAS 18002:2008, and ISO 14001:20015. This model is shown in Figure 3.1-9.

This establishes our commitment to the HSE process by providing a documented company HSE Policy. The HSE Policy is appropriate to our business strategy and culture, and it sets the direction of the HSE Management System. Additionally, we will include the MBTA and third-party stakeholders into our HSE Plan to provide a safe work place across the Project.

All GLX Constructors personnel are held responsible, empowered, and accountable to work together as a team to execute all HSE-related systems and processes. GLX Constructors is committed to providing a healthy and safe workplace for all personnel at each of its offices and project sites; for stakeholders, the MBTA's personnel, and riders; and to protecting the environment in accordance with applicable laws and our HSE Policy.

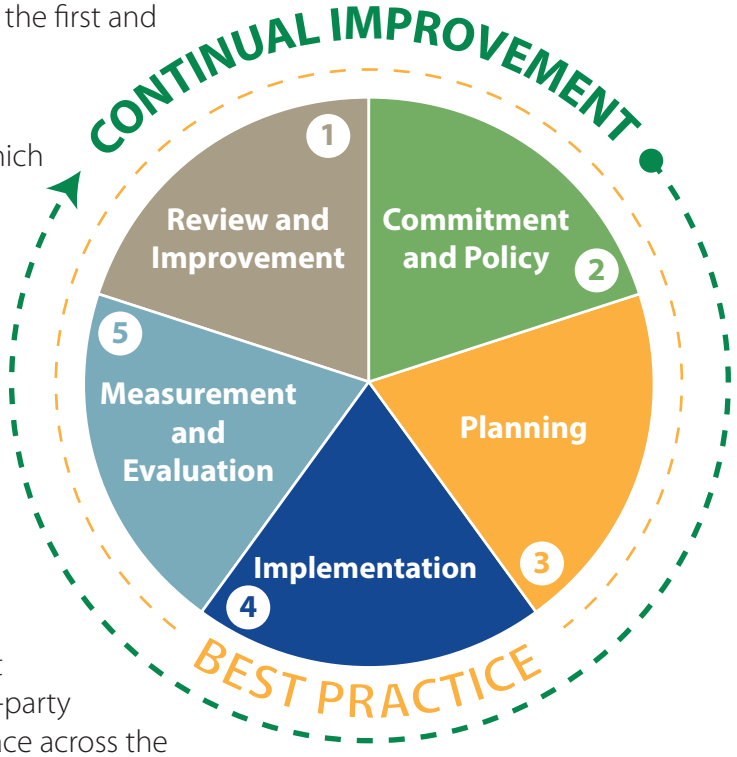


Figure 3.1-9. HSE Management System Continuous Improvement Model. *Our commitment to safety is the first step in establishing our Construction Management concept. We constantly improve our processes through our Continuous Improvement Model.*

GLX Constructors' commitment is based on the principle that accidents are preventable and risks will be controlled to a level that is as low as reasonably practicable.

GLX Constructors Management's unequivocal commitment to HSE is at the foundation of our values and culture.

"Safety will not be sacrificed for the sake of cost savings or increased productivity.

We will execute our HSE Policy by:

- Adopting recognized standards, applicable codes of practice, and relevant statutory provisions.
- Incorporating recognized HSE standards into engineering, design and, construction processes.
- Providing effective training, communication, and continual performance review.
- Establishing realistic and challenging tasks and performance targets for employees.
- Setting GLX Constructors team objectives and targets on an annual basis and assigning accountability for meeting these objectives and targets.
- Preparing and implementing HSE documentation in accordance with HSE, JV partner, and client requirements.
- Regularly auditing implementation of the HSE Management System.
- Working with the MBTA and our subcontractors to continually improve HSE performance.
- Developing communication and control networks.
- Monitoring, measuring, and reporting HSE performance.
- Conducting training to help all personnel understand their responsibilities, and empower them for continual improvement.

As illustrated in Figure 3.1-10, Our HSE Management System provides an integrated tool – a set of practices – to implement the HSE program and execute GLX Constructors' commitment to continually improving HSE performance.

Our HSE Management System and complements our Management Plan by considering the following six key metrics:

- Sustainable development
- Risk management
- Accountability to community

GV20171052-001.INDD

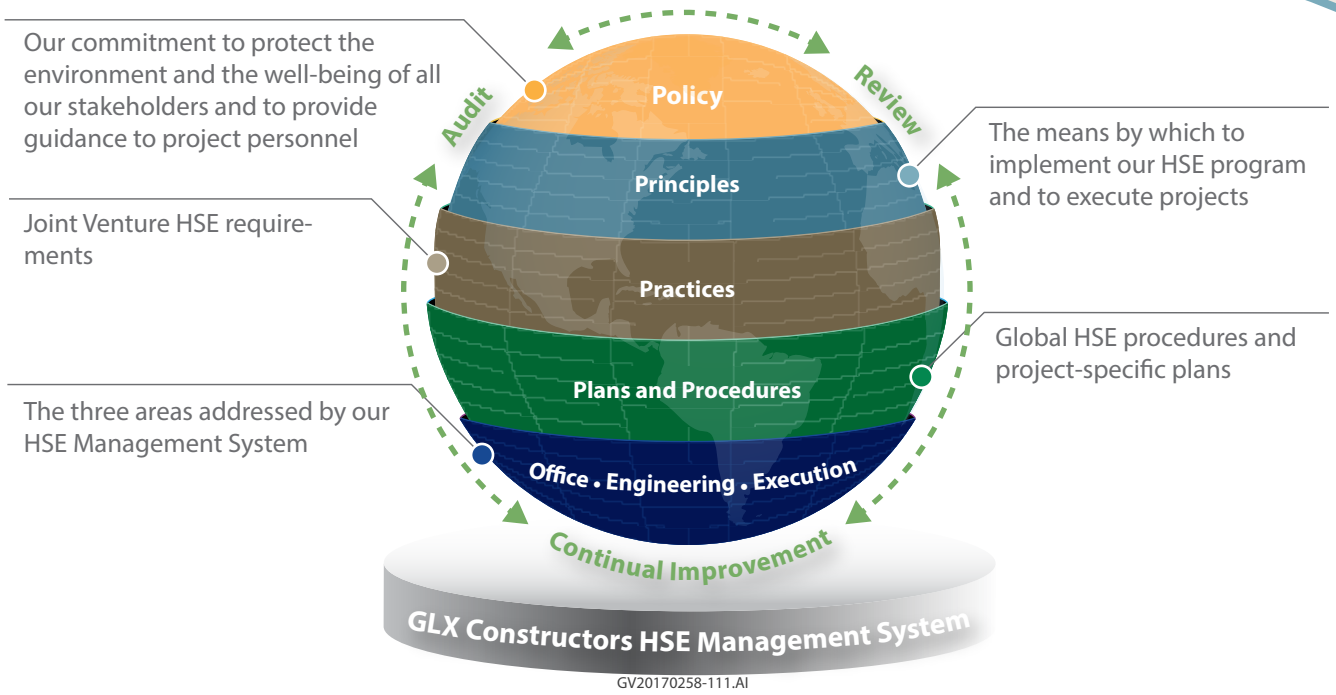


Figure 3.1-10. GLX Constructors' Health, Safety, and Environment Management System. *Our HSE Management System allows GLX Constructors to consistently deliver distinctive solutions to improve the life cycle of our projects and promote the wellbeing of our employees, clients, and the communities in which we work and live.*

- Cross-discipline cooperation
- Best practices
- Requirements applicable to the scope of work (e.g., regulatory, JV partner, and Contract requirements)



Construction zones present safety hazards due to a variety of reasons, from working in close proximity to traffic, to the dangers of working around heavy equipment, to working in an active rail corridor. GLX Constructors understands working in urban environments and confined areas, and we will coordinate with the active rail lines, adjacent property owners, and local jurisdictions to safeguard optimum construction operations. We have identified public roads along the corridor for our construction crews to safely access specific work areas, which will provide adequate access with minimal community impacts. Our approach is to promote safe and efficient movement – for motorists, bicyclists, and pedestrians – through and around work zones while protecting workers and equipment.

As transit contractors, our firms operate and maintain large fleets of hy-rail equipment and work trains. We understand the dangers and risks of rail equipment, and we fully appreciate the safety implications of operating in an active rail corridor. We have the safety procedures and resources in place to protect a safe working environment with this equipment.

Project Manager, John West, leads a morning safety meeting before the crews begin their daily work to meet or exceed their project's schedule needs.

HSE incident prevention is a primary responsibility of all levels of the organization. Each manager is directed to use maximum initiative in communication, training, motivation, and monitoring techniques to apply every reasonable precaution to prevent incidents. Each employee and individual entering the Project is expected to take appropriate steps to eliminate incidents in the workplace.

The HSE professional staff at the project site, will directly assist management as well as the work force in the execution of the HSE Management System. HSE Representatives will be responsible for consulting with management in matters affecting the environment and the health and safety of employees, contractor personnel, clients, and the community. Incident prevention responsibilities of managers cannot be delegated.

This site-specific HSE Plan will be developed in conjunction with the Legal and Other Requirements Register and the HSE Management system Compliance and equivalency process. Together, the HSE Procedures and HSE Plan comprise the site-specific HSE Manual, which will be the foundation for the Project's program implementation.

GLX Constructors not only monitors the standard lagging indicators for HSE performance but focuses on key HSE Leading Indicators. Leading indicators are the results of positive behaviors, a measurement of what is going right, are aimed at the future, and can be directly and quickly influenced. Leading indicators produce proactive data. If we solely focus on lagging indicators, we are working reactively; when we also focus on leading indicators, we are working pro-actively.

Tracking and trending of leading indicators allows GLX Constructors to analyze and drive the required behaviors and provides for continual improvement of the culture. Leading indicators enable us to identify and correct process deficiencies before they produce undesirable results and include.

- **Tracking severity rates** for all incidents including near misses, to allow improved tracking of key areas which increase likelihood of incidents so that action can be taken to tackle the risk prior to a serious incident.
- **HSE Weekly Assessments.** Required to ensure all areas of the work are regularly inspected.
- **Management Participation in Assessments.** Senior project management is involved in HSE assessments on a weekly basis. This not only allows management to observe what is happening in the field but also drives safety excellence and demonstrates its importance to all on site by being involved; this is management in action relative to HSE.

Measurement tools are used to confirm that the HSE Management System is being executed and implemented correctly. They also measure performance, monitor effectiveness, and evaluate changes to the system. Evaluation and feedback loops are an integral part of the HSE Management System.

GV20171052-001.INDD

Measurement and evaluation tools include:

- **Audit.** Auditing is the primary tool for measuring performance. The following audit protocols will be developed and executed:
  - Systems audit. To measure implementation and effectiveness of the HSE Management System.
  - Compliance audit. To measure compliance with the HSE practices and project-specific procedures.
  - Performance audit. To measure whether the expected performance level is being met.
- **Measurement Process.** Performance measurement processes will be implemented to assess the overall effectiveness of the HSE Management System.
- **Client Review.** An evaluation process will be developed at the project to gain feedback from MBTA.
- **GLX Constructors' Project Offices.** The Project office will evaluate the effectiveness of the HSE Management System and provide suggestions on continued improvements.
- **HSE Alignment Process.** HSE professionals involved in the alignment process before and during project startup will identify key areas of the project/site that require particular attention, and adopt or create procedures that are tailored to the project/site.

Responsibilities of the Named Individuals Shown in the Construction Organization

Our proposed Construction Organization chart is illustrated in Figure 3.1-11. The responsibilities of the named individuals shown on the Construction Organization Chart are as listed below.

Project Manager John West will lead our Construction Team. John has over 40 years of experience in heavy/civil and track construction, and he will be dedicated to the Green Line Extension DB Project full time. As a Project Manager, John has overseen all aspects of nearly $3 billion in construction and transit projects, including the $876 million Silicon Valley Berryessa Light Rail Extension DB Project in Milpitas, California, and the $438 million RTD West Rail Line Project in Denver, Colorado, in which he delivered the project eight weeks ahead of schedule. John will be responsible for overall project design and construction operations, and he will have an informal line of communication to the Quality Manager and Project Safety and Security Manager. The Quality Manager and Project Safety and Security Manager will remain independent from the Construction operations, but will maintain a direct line of communication with and will report to our Project Executive, Clyde Joseph.

Name	Role	Responsibilities	Dedication to the Project
John West	Project Manager	Responsible for overall project design and construction operations.	Full time and will begin their assignment upon Project onset.
Jamie Doyle	Construction Manager	Responsible for all operations of infrastructure construction, including right-of-way (ROW); grading and alignment; drainage; utilities; structures, including bridge and wall construction; track; station; and VMF construction.	Full time and will begin their assignment upon Project onset.
Michael Hoitink	Design Build Coordinator	Responsible for managing the Design Team through the design phase and will transition into the role of Construction Engineering Manager during the Construction Phase of the Project.	Full time and will begin their assignment upon Project onset.
Aaron Neeley	Systems Integration Manager and Testing and Commissioning Manager	Responsible for the Systems Integration Design and Construction, including the Overhead Contact System (OCS), communications systems, and Traction Power Systems.	Full time and will begin their assignment upon Project onset.
Sam Choy	Business Services Manager	Manages the Business Services Team, including finance, administration, and procurement.	Full time and will begin their assignment upon Project onset.
Bob Horn	Project Controls Manager	Manages project Controls and scheduling.	Full time and will begin their assignment upon Project onset.

Figure 3.1-11. Individuals on the Construction Organization Chart. *Successfully performing these roles are critical to the success of a DB project of the size and complexity of the Green Line Extension DB Project. GLX Constructors' personnel have the skills and experience to get the job done right the first time.*

Jamie, Michael, Aaron, Sam, and Bob will assist John West in his role as Project Manager. They will lead the constructability reviews of the Project design as it progresses from TWGs through final design.

Management and Integration of Subcontractors and Suppliers

We will fully integrate our subcontractors and suppliers into the Project through on-site orientations and HSE training, which will serve to familiarize them with our policies and procedures. Training also implements the subcontractor or supplier's individual QA/QC Program into our overall Project QA/QC Plan and establishes contractual communication lines.

We will incorporate the subcontractor or supplier's schedule information into our overall Construction Schedule, providing additional detail as necessary, to properly manage timely execution of the work. GLX Constructors will commit a direct, dedicated supervisor to each subcontractor and supplier to maintain immediate communication.

GLX Constructors will manage subcontractors and suppliers to comply with all regulatory requirements. Our process begins with issuing proposal packages and Contract documents through our Contracts and Procurements Department. This department will be under the leadership of Sam Choy, our Business Services Manager.

Upon Project Award and negotiation of a detailed scope of work or supply, we will issue the Contract for signature. Following, we will delegate subcontractor

GV20171052-001.INDD

and supplier field management to the construction discipline's Project Engineer and Superintendent under the leadership of John West, our Project Manager, and Jamie Doyle, our Construction Manager.

We maintain subcontractor and supplier coordination on a daily basis with the Project Engineer, Superintendent, and subcontractor, including safety orientations, daily and weekly safety toolbox meetings, QA/QC meetings, and weekly scheduling meetings. In addition, our Project Safety and Security Manager, Chris Poe, and Quality Manager, Sandro Plutino, will have a direct line of contact and communication with the subcontractor or supplier to effectively integrate and manage all requirements of their contract.

3.1.D INTERNAL COORDINATION

The initial Project Management Plan shall describe the interrelationships and interfaces between each discipline within the Proposer's organization (e.g., design, design check, construction, Project controls, and quality management).

Interrelationships and Interfaces between Each Discipline

Our construction-driven execution approach fully integrates the Design, Design and Construction Review, Quality (design and construction), Safety, Construction, and Project Controls Teams into the design, approval, and construction process.

After Project Award, we will reconvene each of the design disciplines' TWG Meetings. As discussed in earlier in this section, these TWGs began during the Proposal Phase with the intention to produce updated design solutions to allow Pricing Proposals to be completed. Each TWG is co-led by the Discipline Design Lead and the Construction Discipline's Project Engineer and Superintendent.

As the Project's design progresses through each TWGs Illustrated in Figure 3.1-12, the Technical Design Reviewers, Project Engineers, the MBTA, and appropriate third-party stakeholders will review and comment on the design. The Project Safety and Security Manager reviews the design for development of potential hazards and analysis for mitigation, the Quality Manager develops inspection and testing plans, and the scheduling lead reviews the design for incorporation of additional detail into the Project Schedule and Cost controls.

We embed the MBTA and appropriate third-party stakeholders in this process to provide immediate feedback to the designer, and streamlines the review, comment, and reconciliation process at each TWG checkpoint, which will expedite the overall Project Schedule.

> **"GLX Constructors is fully committed to working together as a team. We have intentionally formed this Joint Venture partnership based on our shared corporate values and mutual commitments to the MBTA's Green Line Extension DB Project goals. We will achieve the requisite cost and schedule certainty through the internal and external relationships necessary to drive successful Project execution.**

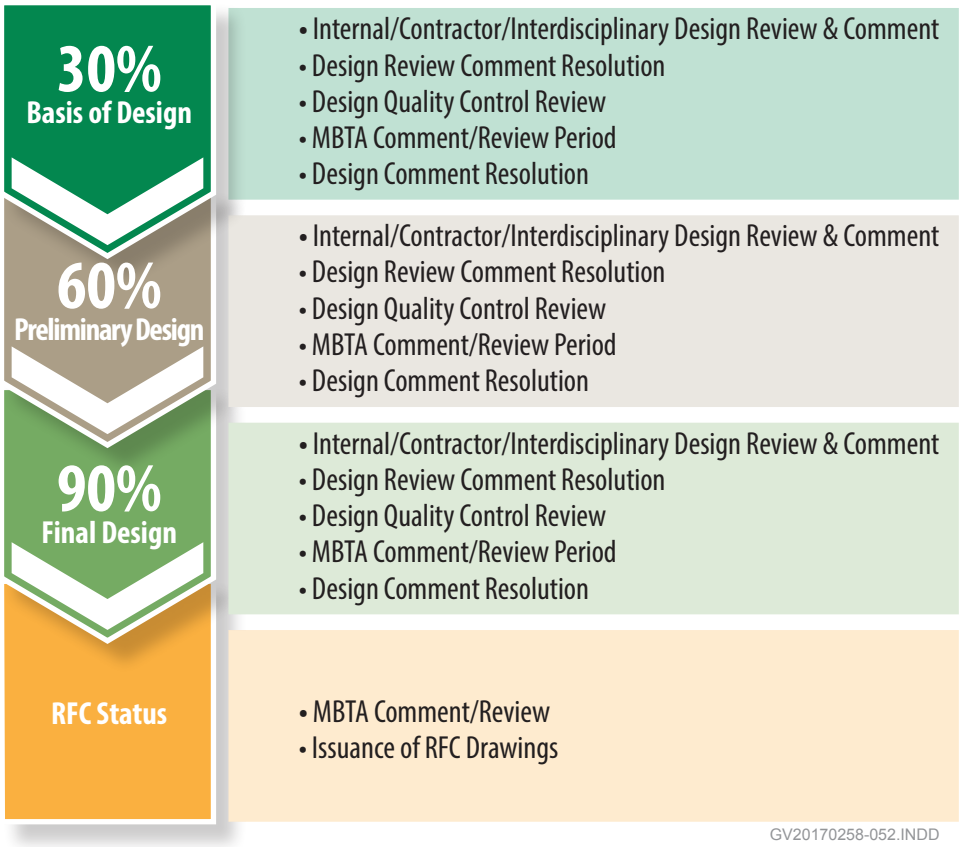


Figure 3.1-12. Design Package Progression. *The progression of the Design Package demonstrates the collaboration that is required between the Design Team, the Construction Team, and the MBTA.*

As the design progresses to the final design stage (90%), the Construction Discipline Project Engineer and Superintendent will prepare Construction Work Plans (CWP) to define and control the design element's construction. Figure 3.1-13 illustrates a CWP checklist. These CWPs include the design plans and specifications, any detailed work sequence drawings required for construction, associated submittals for review, and approval by the Engineer of Record (EOR) and bills of material.



Figure 3.1-13. Construction Work Plan Checklist. *Before beginning construction activities, it is critical to have all construction elements in one, easily accessible place.*

Mirroring the design phase, the Project Safety and Security Manager reviews the CWP to identify potential hazards and, if necessary, develops procedures for eliminating or mitigating the hazards. The Quality Manager develops Inspection and Testing Plans and specific checkpoints. The Environmental Manager reviews the CWP for compliance with our Project's Environmental Plan. The Project Controls Team reviews the CWP to provide the required schedule completion dates and the associated cost control metrics.

The finalized CWP is submitted to the DB Management Team and the MBTA for review; after its approval, it is able to move forward with construction.

Incorporating Construction, Safety, Quality, Environmental, and Project Controls Teams; DB Management Team; the MBTA; and appropriate third-party stakeholders into the design and construction process provides the most efficient and economical construction solution. All parties "buy in" to our proposed solution, and any potential changes or "surprises" during construction are either minimized or eliminated.

3.1.E EXTERNAL COORDINATION

As members of the community, we understand the reach of the Green Line's influence in the greater Boston area. Coupled with our large-scale project experience, GLX Constructors' homegrown relationships and nuanced understanding of the local community will lay the foundation for our public outreach communication program, third party management, and stakeholder relationships. Our experience with these interfaces will offer the MBTA a safer Project execution, more satisfied community members, and fewer complaints from the public arena.

Interrelationships and Interfaces between GLX Constructors and Others

As detailed above, we include the MBTA and appropriate third-party stakeholders into the development, review, approval, and construction of each design element. During this process, we identify key interface points with the local communities, and we engage the Public Information Office to develop proactive approaches to communicating with the third-party stakeholders.

Our experience has proven this proactive process will facilitate timely review and construction approval. Additionally, it provides the local communities with a transparent and simple approach to relevant construction notifications.

Reviews of Plans and Permits

The Construction Project Engineers are responsible for permits in each of their respective disciplines.

> **"Paired with our familiarity with the MBTA's policies and procedures, GLX Constructors has managed design internally and externally on a national stage. This will give the MBTA confidence about our ability to effectively manage our design processes through to the end of Project completion.**

During TWGs, the Construction, DB Management, Quality, Safety, and Environmental Teams; the MBTA; and associated third-party agencies simultaneously review the design. As each Design Phase completes, the our Construction Team reviews the Design Package at the same time as the Design Quality Manager, who signs off on the design for Contract compliance. The Design Package is then transmitted to the MBTA and necessary third-party agencies for review and comment. By incorporating the MBTA and third-party agencies into the ongoing design process, this streamlines their review and comment period, which minimizes comments for resolution.

After the MBTA and third-party agencies review and comment on the Design Package, it is returned to the Design Discipline Lead to resolve review comments, and continue the design to the next completion point where the process is repeated.

After the final design is completed and comments are resolved, the Design Package is stamped, signed, and released for construction (RFC) to the Construction Team for execution.

Progress, Workshop, Partnering, and Utility Coordination Meetings

The Kickoff Meeting with the MBTA is critical and will set the foundation for our partnership moving forward. This is an essential step for integration with the MBTA, and move forward together with executing the Green Line Extension DB Project in an effective, trustworthy partnership.

We will propose initial partnering sessions with follow-up reviews on a quarterly basis, or more frequently if necessary. We also hold Project team alignment meetings to make certain our team performs to the highest degree, and will extend the courtesy to the MBTA and third-party stakeholders.

TWG meetings are scheduled on a weekly basis, during which design decisions are documented from the previous week and new concepts are brought forward for resolution. Additional workshop meetings and Over-the-Shoulder Reviews are scheduled as needed to facilitate the design review, comment, and approval process. These meetings include necessary Utility Coordination meetings, which are part of the Utilities and Drainage TWG. We hold weekly Schedule Progress Meetings to review and update the design and construction schedule and prepare the progress reports.

Our organization includes in-depth risk management meetings on a quarterly basis, and risk register reviews on a monthly basis.

Construction, Engineering, and Inspection Activities

As the Construction Work Plans (CWPs) are developed from our final design solutions, the QA/QC Inspection and Testing Plan for each work plan is

> **“Coupled with our large-scale project experience, GLX Constructors’ homegrown relationships and nuanced understanding of the local community will lay the foundation for our public outreach communication program, third party management, and stakeholder relationships.**

GV20171052-001.INDD



GREENBUSH LINE RAIL RESTORATION DESIGN BUILD

South Shore, Massachusetts

The first ever Design Build project executed by the MBTA – was awarded the 2006 American Road and Transportation Builders Association (ARBTA) "PRIDE" First Place Private Sector Award for its most successful community outreach effort. The project team instituted a thorough and effective public outreach program, including a 24-hour dedicated "hot line" and a culture of continuous outreach to neighborhoods affected by the construction. Regular meetings were held to inform the affected communities of progress to date and upcoming milestones, particularly in terms of road closures and utility relocations. Community outreach and public information was managed by a full-time public information officer responsible for all coordination of community involvement and community feedback.



developed, reviewed, and approved by the Quality Manager to be included in the CWP. Additionally, safety check points and Job Hazard Analyses are prepared to allow for safe work construction. Any environmental concerns are addressed in accordance with industry Best Management Practices and the Project-specific Environmental Management plan.

Community Outreach

Where specific design or construction directly impacts the community, GLX Constructors' Title VI Program Lead, Hannah Brockhaus, will provide input and schedule community outreach meetings when appropriate. This will allow the MBTA, with support from GLX Constructors, to clearly and accurately present the community with Project updates.

The development of the design and our Project management sets up the Title VI Program Lead to easily identify specific interface points between construction and third-party stakeholders. Specifically, we are prepared that the communities of Medford, Somerville, and Cambridge, as well as the area surrounding Tufts University, will require in-depth analysis to produce the most effective program for public involvement, comment, and input. This will also set the groundwork to create a process of continuous feedback that will lead to communications improvements.

A similar process was used by GLX Constructors' team member, Fluor Enterprises, Inc., on the Tappan Zee Bridge Hudson River Crossing DB Project for the New York State Thruway Authority, and on the Purple Line Transit DB Project for the Maryland Department of Transportation and Maryland Transit Administration. On the Tappan Zee Bridge Project, multiple construction zones were located immediately adjacent to local communities. As such, the Project required extensive pre-planning for a noise control plan that sufficiently notified third-party stakeholders. We carried our approach over to the Purple Line Transit DB Project, which required extensive collaboration and planning for the section of the rail line that traversed directly through

> **"To support the MBTA's third-party stakeholder goals, we have a local, proficient Title VI Program Lead who will disseminate information on upcoming construction activities and provide status updates to the community at regular intervals about our construction progress as we move toward the Project's successful completion.**

the University of Maryland's campus. In both instances, our Public Outreach Programs were collaborative, engaging, and successful.

GLX Constructors' construction-driven approach to design and construction produces a collaborative, economical, efficient, and inclusive process for safe and quality construction. Our approach allows for schedule and cost certainty, both for the MBTA and GLX Constructors. Our partnering approach fosters collaboration and timely problem solving and solutions to eliminate rework, mitigate impacts to the MBTA and the local communities and transit ridership. Our approach will ensure the MBTA is represented in a positive light with the public and media outlets.

"

In partnership with the UDOT Public Information Team, a Fluor-led Joint Venture won the 2013 ARTBA Pride Award for outstanding Public Outreach associated with the I-15 CORE Project.

GV20171052-001.INDD

APPENDIX 1

Design Discipline Lead Résumés

SEAN BARRY, PE

Utilities Design Discipline Lead

Valuable Experience:

- ✓ MBTA
- ✓ Extensive rail transit
- ✓ Power systems
- ✓ Power facility operations
- ✓ Infrastructure improvements
- ✓ Design disciplines
- ✓ Construction teams

Years of Experience: 21

Education: B.S., Civil Engineering, University of Massachusetts, Amherst

Professional License/ Certification: Professional Engineer, MA #41802

Sean has more than 20 years of experience in the design and construction phases of civil engineering projects. He has provided engineering services for numerous utility and roadway projects that have involved the installation of water, sewer, drainage, gas, power, and telecommunications improvements. His responsibilities have included the inventory, inspection, evaluation, relocation, and protection of utilities, as well as contract administration, budget and schedule oversight, reporting, recording, and staff supervision. As a lead project engineer on the seven station designs for the MBTA Greenbush Line Rail Restoration Design-Build, he designed various site stormwater systems that implement the Massachusetts Department of Environmental Protection's stormwater management standards, particularly the sizing of innovative/alternative stormwater control and underground detention and infiltration systems following best management practices. Sean has also been a project engineer on several Massachusetts Water Resources Authority and local municipality projects, as well as bridge, infrastructure, and roadway projects. Additionally, he is experienced in addressing delicate project issues, including ROW and abutter concerns, during the public hearing phase of the project permitting process.

DESCRIPTION OF COMPARABLE PROJECTS

City of Somerville, Central Broadway/Winter Hill Roadway and Streetscape Improvements Study and Design, Somerville, Massachusetts, Project Manager. Sean oversaw the design of roadway and streetscape improvements to a 1-mile corridor. He coordinated efforts with STV traffic engineers and survey, landscaping, and public outreach subconsultants. Phase I included a traffic study of existing conditions and the development of preliminary layouts of proposed roadway and streetscaping improvements, including bicycle lanes and additional green space. The firm developed three alternatives and led public meetings and presentations. Sean oversaw the development of final plans and bid documents for the preferred option, which is a "complete street" concept that calls for cycle tracks on both sides of Broadway separated from traffic by a parking lane.

MBTA, Greenbush Line Rail Restoration Design Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Project Engineer. Sean prepared site layout grading and drainage designs, as well design packages for various at-grade roadway crossings and seven rail stations, for the $320 million restoration of this commuter rail line. Sean was responsible for designing packages for 15%, 30%, 60%, 90%, and 100% submittals to the MBTA, the engineer/contractor, and the various towns for approval. His other tasks included coordination with other design disciplines (track drainage, structural, electrical, architectural, and traffic professionals) and the preparation of and response to RFI documents during the design and construction process. Sean responded to QA/QC requests from the towns, MassDOT, and the MBTA. He was actively involved in the public outreach process and provided engineering design support during the question and answer phases of those meetings. He also oversaw the revision to and implementation of sensitive ROW and mitigation agreements into the designs and assisted in local, state, and federal permitting tasks. Additionally, Sean prepared and coordinated design changes to contract documents, issued field memos, and provided civil construction phase services to the engineer/contractor to resolve any construction issues.

MBTA, Wellington Carhouse Expansion and Improvements, Medford, Massachusetts, Lead Civil Engineer. Sean managed the development of civil plans and specifications for the MBTA's planned expansion and renovation of the Wellington Carhouse. The project will expand the facility's east side by 12,000 sf and renovate the existing 120,000-sf space. The improvements will allow the MBTA to maintain 152 new, state-of-the-art Orange Line cars that are to replace the agency's current fleet of 120 cars. Sean was responsible for overseeing civil design submittals at the 60%, 90%, and 100% levels of completion. His work involved coordinating with other design disciplines, including track, structural, electrical, traction power, plumbing, fire protection, and architectural professionals. Sean also prepared documents depicting design constraints and requests for a variance from the MBTA's track clearance envelope for work adjacent to active service operations at the Wellington Station.

Town of Barnstable, Lincoln Road Reconstruction, Hyannis, Massachusetts, Project Manager. Sean is managing the development of plans for the $1.5 million reconstruction of 0.75 mile of roadway between Route 28 and West Main Street. His team has developed roadway geometry, cross section, traffic calming elements, pedestrian crossings, handicapped accessibility, pavement markings and signage, and alignment of a shared use bicycle and pedestrian path. The team has also identified impacts to abutters, utilities, and the existing drainage system while minimizing utility relocations and reusing as much of the existing drainage system as possible to minimize costs. The pavement design calls for recycling the existing asphalt and using it for the base course under the new roadway.

PAUL BOBBY, PE

Track Design Discipline Lead

Valuable Experience:

- ✓ Track design of light rail expansions
- ✓ Design of track alignment
- ✓ Geometry
- ✓ ROW and utility conflict identification
- ✓ Construction staging plans

Years of Experience:	18
Education:	B.S., Civil Engineering, University of Wisconsin/ Platteville
Professional Licenses/ Certifications:	Professional Engineer, Georgia # PE034469, Illinois #058268, Indiana #PE10708276, North Carolina #043621, Wisconsin #38452-6

Paul is a track designer with more than 15 years of experience in the design and construction of rail improvements. He began his career as a track laborer for the Wisconsin Central Ltd. (now Canadian National Railway Company), and has since earned a solid reputation within the rail industry for his knowledge of light rail, passenger, and freight rail design programs. He served as Lead Rail Engineer for the $120 million Chicago Transit Authority (CTA) Block 37 Station and Tunnel Connector, for which he provided design of a 2-track connection between the Blue and Red transit lines. He has also served as lead rail engineer for several capacity improvement projects, including work for CSXT, Norfolk Southern Railway, and Kansas City Southern. In addition, Paul has provided project management for blanket civil/structural and project administration contracts with Metra, including more than 20 assigned tasks, all completed within budget and on schedule.

DESCRIPTION OF COMPARABLE PROJECTS

City of Ottawa, O-Train Expansion, Ottawa, Ontario, Lead Track Engineer. Paul oversaw the design of track and acceptance inspection activities during the service expansion of the O-Train light rail transit system in Ottawa, Ontario. To accommodate increased ridership on the 5-mile (8-km), single-track, diesel multiple unit (DMU) rail system, the city initiated efforts to install two new passing sidings on the single-track system. As part of this design-build effort, activities also included the replacement of the Ellwood Diamond (a crossing of the O-Train and the Canadian Northern Railway), signal system upgrades, civil grading and drainage, utility relocations, additional storage tracks at Walkley Yard, improvements to the Walkley Maintenance Facility, passenger station enhancements, and the acquisition of six new DMU train sets. As part of this effort, Paul's responsibilities included developing the preliminary configurations for the two passing sidings, as well as performing acceptance inspection of the track work. In addition, he contributed to the preparation of an advanced material package and prepared bid documents.

IDOT, Granite City to St. Louis Corridor Phase I Environmental Studies, Granite City, Illinois and St. Louis, Missouri, Project Manager/Project Engineer. Paul is supervising preliminary engineering efforts during Phase I services for all work associated with the preparation of the Environmental Impact Study for the expansion of high-speed rail (HSR) service between Granite City and St. Louis for the Illinois Department of Transportation (IDOT). The 284-mile-long Chicago to St. Louis Corridor transportation network consists of highway, air, and rail (Amtrak) service. The purpose of the IDOT Chicago to St. Louis HSR Program is to improve rail service and to establish a more balanced use of the multimodal transportation network. As with the rest of the corridor, the 20-mile section of rail through Madison and St. Clair counties currently operates on one set of tracks. The design team is working to identify a preferred alternative to allow speeds up to 79 mph through the study section and increase on-time reliability for Amtrak service. The firm's scope of work includes data collection, preparation of base maps and mosaics, geometric studies, capacity analysis, railroad coordination, environmental field studies and reviews, cost estimates, and public involvement. Paul is providing overall project coordination of all engineering tasks, managing the firm's financial reporting, and reviewing all railroad alignments and feasibility analyses.

St. Louis Metro, East Riverfront Interlocking, St. Louis, Missouri, Project Engineer. Paul oversaw the track design for a new diamond interlocking located between St. Louis Metro's existing East Riverfront light-rail station and the Eads Bridge spanning the Mississippi River. The Eads Bridge is a 2-level structure carrying two sets of tracks for the MetroRail transit system on its lower level and a 4-lane highway on the upper level. The new interlocking is located in an area east of the bridge known as the East Arcade. Paul and his team designed the new interlocking on a tight schedule and within a restricted area, which made design work challenging. The project required the installation of an asymmetrical double crossover using a combination of No. 6 and No. 8 turnouts on concrete ties to allow single-track operation over the Eads Bridge with minimal disruption to the passenger rail service while the bridge is rehabilitated. This project had an aggressive completion schedule, which required the firm to develop an independent material procurement package in advance of the construction contract. Paul directed the track design for the new interlocking and reviewed the final plans, successfully meeting the aggressive schedule.

DAVID BORGER, PE

Technical Advisor

Valuable Experience:
- ✓ Design build
- ✓ Light rail projects
- ✓ Complex systems
- ✓ Facility designs

Years of Experience: 43

Education: M.S., Civil Engineering, New Jersey Institute of Technology
B.S., Civil Engineering, Newark College of Engineering

Professional Licenses/ Certifications: Registered Professional Civil Engineer, NJ # 24GE02673700
Professional Planner (PP), NJ# 33LI00402800

An industrial engineer with more than 40 years of diverse management and design experience, David has been responsible for supervision of complex systems and facility design including trackwork; communications; traction power; signals; equipment selection and layout; and yard planning, layout, and design, including several projects delivered to the Los Angeles County Metropolitan Transportation Authority (Metro) and other transit operators throughout the country. Notable projects completed under David's direction include NJ TRANSIT's Hudson-Bergen Light Rail Transit DBOM and and construction management for Metro's Gold Line (Blue Line) light rail system to Pasadena.

DESCRIPTION OF COMPARABLE PROJECTS

NJ TRANSIT, Hudson-Bergen Light Rail Transit DBOM, Hudson and Bergen Counties, New Jersey, Systems Design Manager. David managed the industrial engineering design for the 10-mile-long initial operating segment of this $1 billion, 20-mile light rail system. In an effort to alleviate bus and automobile congestion in Hudson County and improve access to Bergen County, as well as to meet projected ridership forecasts, the project involved civil/right-of-way, structural, and industrial engineering design services. David supervised a multidisciplinary design team for the track and systems design of the alignment, which consisted of at-grade and elevated sections employing ballasted, direct fixation, and embedded track. He also made sure that the track and systems design were integrated with the system's 16 stations, maintenance facility, and yard. The system was subsequently expanded to run more than 20 miles between Bayonne in Hudson County and the Vince Lombardi Park/Ride Facility in Bergen County, and include 33 stations.

Metro Pasadena, Metro Blue Line (Gold Line) Light Rail, Los Angeles to East Pasadena, California, Principal-in-Charge. David held overall responsibility for the construction management (CM) of this 13.6-mile,

$865 million light rail system — completed by the Los Angeles Pasadena Blue Line Construction Authority as part of the Gold Line. He oversaw a 12-member CM staff and 20 subconsultants responsible for performing design and constructability reviews, resident engineering and inspection, QA/QC, systemwide and facilities engineering support, and systems integration. He was responsible for the design and constructability review of each construction package to reduce costs and to avoid claims. David managed the QA/QC program, including supervision of the area manager and all resident engineering and inspection activities, to see that all quality objectives were met and documented. He supervised extensive coordination with the cities of Los Angeles, South Pasadena, and Pasadena, as well as with the California Department of Transportation, to continue the maintenance and protection of traffic on the many busy freeways and roads impacted by the project. David also oversaw coordination with these cities, as well as local businesses and communities, to keep them informed about construction activities and to incorporate their concerns into the construction program. He also made certain that the project's safety program objectives were met or exceeded.

RCTC, Perris Valley Line, Riverside to Perris, California, Principal-in-Charge. David is responsible for maintaining executive oversight of planning, design, and construction services for the 24-mile Riverside County Transportation Commission (RCTC) extension of the Metrolink commuter rail system. The scope of the $247.2 million project includes rehabilitation of more than 20 miles of existing track, upgrade, or closure of multiple grade crossings, installation of a signal system, replacement of two railroad bridges, and design for four new stations and a new layover facility with locomotive service and inspection areas. Under David's oversight, the firm kept the design on schedule and within budget despite scope changes by the client. The firm is currently providing design support during construction, including response to requests for information; change order review and resulting design revisions; submittal and shop drawing review; nonconformance reports, as needed; and oversight of systems inspection, testing, and startup by the systems subconsultant.

SMART, Initial Operating Segment Design-Build, San Rafael to San Rose, California, Principal-in-Charge. David is providing executive oversight of design services for all civil, track, and structural improvements for the initial operating segment of Sonoma-Marin Area Rail Transit District (SMART) implementation of passenger rail service along the Northwestern Pacific Railroad corridor. STV's scope of work for the $360 million design-build project includes the rehabilitation or replacement of 37 miles of track, 16 bridges, and numerous grade crossings along the alignment between San Rafael and Santa Rosa, CA. The firm is also designing the boarding platforms for the segment's seven stations.

MARTIN BOYLE

Technical Advisor

Valuable Experience:

- ✓ Design build
- ✓ LRT
- ✓ MBTA
- ✓ Multi-billion dollar projects
- ✓ Systems integration
- ✓ Start-up, and testing

Years of Experience: 50

Education: A.S., Business Administration, Fisher College

Martin, the MBTA's former Superintendent of Transmission and Distribution, has unparalleled experience managing the design, construction, and maintenance of electrified transit systems and vehicles. He joined STV to manage the Houston Metropolitan Transit Authority (METRO) light rail transit (LRT) starter line as the vehicle/systems manager. This project was successfully delivered to the community in less than four years from the start of design to revenue service. Martin has since served as the construction manager of rail systems for the Charlotte Area Transit System (CATS) LYNX Blue Line LRT, the first of five routes in a $3.9 billion transit program.

DESCRIPTION OF COMPARABLE PROJECTS

City of Ottawa, Confederation Line LRT, Ottawa, Canada, Senior Advisor. Martin is serving as Senior Advisor responsible for providing supervisory support for development of preliminary engineering necessary for the transition of Ottawa's exclusive, fully built-out bus rapid transit system to an LRT network. The approximately 7.8-mile electric line will feature 13 stations, four inside of a nearly 2-mile-long tunnel under downtown Ottawa. This bored tunnel presents another major challenge, as it will burrow beneath federal lands and buildings in the Canadian capital. To mitigate any potential impacts, the firm is coordinating with applicable stakeholders and complying with all requisite federal rules and regulations. The project also involves the construction of a new maintenance and storage facility to service the LRT fleet, and the firm is providing preliminary engineering services for this structure as well. The firm is currently coordinating with a joint venture partner on project management and project controls. In addition to preliminary design and final design and construction specifications, the firm is responsible for scheduling services, including construction staging.

CATS, LYNX Blue Line Extension, Charlotte, North Carolina, Principal-in-Charge. As Principal-in-Charge, Martin has overall responsibility for transportation planning, environmental investigations and documentation, and preliminary engineering services to 65% design for a 9.3-mile extension of the Charlotte Area Transit System (CATS) Blue Line. The estimated $1.16 billion extension from the city's central business district to the University of North Carolina at Charlotte includes 11 stations, three parking garages, one surface parking lot, and a storage yard with an operations building. The firm worked

with CATS to identify more than $200 million in value engineering and project scope reductions, and accelerated the corresponding redesign and supplemental environmental investigations to incorporate the project changes into the Final Environmental Impact Statement that was submitted to FTA in 2011. The firm is also working with CATS to successfully integrate transit and land use on the extension and to solve challenges associated with crossing and running along existing freight railroad ROW. Because the BLE runs through developed areas, extensive utility coordination is required. In addition, the firm is designing the 3-car center, side, and elevated platforms. Station amenities include canopies, benches, ticket vending machines, variable message signs, public address speakers, closed circuit television cameras, lighting, and tree wells. The firm is also responsible for designing the park-and-ride lots, a 1,500-car garage, and a 650-car garage, as well as planning and design for traction power, overhead contact, train control, and communications systems.

MBTA, Boston, Massachusetts, Former Superintendent of Transmission and Distribution. Martin directed and coordinated all operating activities for the Transmission and Distribution Division. He was responsible for the maintenance of 100 miles of catenary, 13 miles of trolley bus, 1,300 miles of DC cable, and 300 miles of AC cable. Martin directed the performance, training, and discipline of 130 professional and trade personnel, including supervisors, engineers, linespeople, cable splicers, cable layers, equipment operators, and driver groundspeople. He also prepared the multimillion-dollar division budget and monitored expenditures. He administered contracts for asbestos abatement, Dig Safe Utility Marking, and high-voltage cable splicing. Martin served as project manager for two major catenary construction projects performed with MBTA personnel under force account — projects that both came in under budget and without any disruption to service. He monitored all work performed by contracts on catenary construction projects, including review and final decision of designs by consultants. In addition, Martin managed an engineering support group responsible for system wide design and maintenance of all catenary trolley bus transmission and distribution lines. He also served as a member of the Board of Directors of Dig Safe.

KAREN BRESLAWSKI, AIA

Stations Design Discipline Lead

Valuable Experience:

- ✓ Managed design teams for rail stations and facilities
- ✓ Experience working with the MBTA
- ✓ Coordination with design build teams
- ✓ Public involvement

Years of Experience	35
Education:	M.S., Architecture, State University of New York, Buffalo B.A., Professional Studies in Architecture, State University of New York, Buffalo
Professional License/ Certification:	Registered Architect, Massachusetts National Council of Architectural Registration Boards

Karen is a Senior Architect with more than 30 years of experience in the planning, design, and development of transportation facilities for public agencies throughout Massachusetts. She has a successful record of accomplishments in the transit market with projects that include feasibility studies, task orders, and large-scale endeavors for clients including the MBTA and MassDOT. She has successfully managed designs for new rail stations, station renovations, and bus stations and intermodal transportation centers, overseeing station elements including platforms and canopies; pedestrian circulation around stairs, elevators, and enclosed bridges; signage and lighting; and track rearrangement. She has proven skill in coordinating with multidisciplinary teams to maintain quality from the study phase through construction administration. Karen also has experience making presentations at town meetings and committees.

DESCRIPTION OF COMPARABLE PROJECTS

NB Development Group, Boston Landing Station, Brighton, Massachusetts, Senior Architect. Karen oversaw the development of final architectural plans and provided construction administration for the new $26 million commuter rail station located adjacent to the New Balance headquarters in Brighton. The project elements include track rearrangement; platforms and canopies; pedestrian circulation around stairs, elevators, and enclosed bridges; and signage and lighting. The project was built through a construction manager-at-risk delivery method and was the first in Massachusetts to be built through a public-private partnership with the MBTA.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Architect. Karen was responsible for providing technical support for architectural aspects of this $255 million design build rehabilitation of the Longfellow Bridge, a 2,135-foot structure that carries Route 3 and the MBTA's Red Line over the Charles River between Boston and

Cambridge. Karen led the review of the architectural design drawings and performed QC checking for the architectural portions of the project, which include railings, decorative elements, and the bridge's signature granite towers that are to be dismantled and restored.

MBTA, Wellington Carhouse Expansion and Improvements, Medford, Massachusetts, Project Manager. Karen was responsible for providing construction-phase services for the MBTA's $75 million expansion of the Wellington Carhouse. The agency is expanding the facility to accommodate 152 new Orange Line cars that will eventually replace the current fleet of 120 cars. As Project Manager, Karen was responsible for coordinating a team of architects and engineers that developed final plans for a 12,000-sf single-bay addition to the east side of the 40-year-old building. Her design role entailed analyses of the facility's as-built conditions to determine programming based on staff and equipment space needs, as well as cost effectiveness. Karen provided bid-phase support and assisted the MBTA with selecting a general contractor. During construction, she is responding to RFIs, reviewing shops drawings, and conducting site inspections, as needed.

MBTA, Hingham Intermodal Center, Hingham, Massachusetts, Technical Advisor. Karen conducted QA/QC reviews for the design of a $6.4 million intermodal transportation facility. The 8,400-sf facility is a terminal building for both bus and commuter boat operations, and it provides office space for the Hingham Harbormaster, the Massachusetts Department of Conservation and Recreation's Harbor Islands staff, MBTA Operations staff and ticket sales, and the Massachusetts Environmental Police. The facility was designed to LEED® Gold standards and incorporates a green roof, geothermal heat exchange system, passive ventilation, rapidly renewable materials, regional materials, low emitting materials, daylighting, sun shading devices, and stormwater recharging. Karen reviewed the final design to verify that it met STV's standards and specifications. She also reviewed the proposed layout to determine whether it met applicable codes, including ADA and Massachusetts Architectural Access Board standards.

MassDOT, Central Artery DO11A, Boston, Massachusetts, Project Manager. Karen oversaw the architectural pieces of the tunnel finishes for this portion of the Central Artery/Tunnel Project in Boston. Karen coordinated wall tile layout and patterns, signage, railings, doors, exits, ceiling panels, and entries and exits with structural, civil, and mechanical/electrical elements for the $450 million design-build project section, which is located between Kneeland Street and Congress Street in the heart of Boston.

ROBERT CONNORS, PE, CQM/OE, CQA, CCS, CCP NETTCP QAT

Design Quality Assurance/Quality Control Manager

Valuable Experience:

- ✓ MBTA
- ✓ Quality management plans
- ✓ Communication
- ✓ QA/QC

Years of Experience: 30

Education:
M.S., Finance; Suffolk University
M.S., Business Administration, Suffolk University
B.S., Civil Engineering; University of Rhode Island

Professional Licenses/ Certifications:
Professional Engineer, MA Civil #39185
Professional Engineer, MA Structural #38924
Certified Cost Professional, AACE #2966
Certified Construction Specifier, CSI
MasterFormat Accredited Instructor, CSI
Certified Management Accountant, IMA #962879
Certified Manager of Quality/Organizational Excellence, ASQ #13209
Certified Quality Auditor, ASQ #41100Certified Quality Assurance Technologist, NETTCP

Robert is a Senior Quality Manager with more than 30 years of experience in engineering and project oversight for clients including the MBTA and MassDOT. With a varied project portfolio that includes rail, bridge, maintenance facilities, and stations, he has the credentials needed to tackle high-profile quality challenges involving large teams. Robert has extensive experience with design-build, including the MBTA Greenbush Line Rail Restoration Design Build, and public-private partnerships. A Certified Quality Manager and Certified Quality Auditor through the American Society of Quality, he provides quality management and oversight for national projects and serves as the quality manager in the Boston office. His experience with inspection, design, specifications, construction materials testing, project management, construction cost estimating, cost accounting, scheduling, claims analysis, finance, and contract administration allows him to find optimum solutions to quality issues on large complex projects.

DESCRIPTION OF COMPARABLE PROJECTS

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Quality Administrator. Robert is directing the QC team in the preparation and administration of the design and construction quality plans for the $255 million design build rehabilitation of the Longfellow Bridge. The 2,135-foot structure, constructed in 1908, carries Route 3 and MBTA Red Line tracks over the Charles River between Boston and Cambridge. Robert prepared quality management plans, trained project personnel on

the plans, implemented the plans, audited performance, and implemented quality improvements for design and construction. The design phase is complete and the firm is providing construction support services for the contractor.

City of Ottawa, Confederation Line LRT, Ottawa, Ontario, Canada, Quality Control/Procurement Manager. Robert performed QC and prepared bridging documents as part of the procurement team for this $2.1 billion public-private partnership. Project is constructing a 7.8-mile electric line from Tunney's Pasture Station in the west to Blair Station in the east via a downtown transit tunnel. Robert reviewed all components of the proposed project, including 13 stations, four of which are in a tunnel under downtown Ottawa between Bronson Avenue and the University of Ottawa. The remaining nine stations are located at-grade within the existing transitway corridor. A new 26.3-acre vehicle maintenance and storage facility supports the new line. The owner is the City of Ottawa and the system will be operated by OC Transpo.

WRTA, Bus Maintenance, Operations, and Storage Facility, Worcester, Massachusetts, QC Manager. Robert prepared the quality plan, trained to the plan, managed quality audits, and provided QC oversight for the design of a new vehicle maintenance, operations, and storage facility for the Worcester Regional Transit Authority (WRTA). The $75 million, 2-story, 150,000-sf facility will have a capacity to store and maintain 80 vehicles and space for 155 employees.

Metropolitan Washington Airport Authority, Dulles Corridor Metro Rail Phase 2 Project, Fairfax County, Virginia, External Quality Auditor. Robert performed FTA based quality auditing and related quality work for the Dulles Metrorail Project Management Procedures. This $2 billion, design-build, metro extension includes six stations along 11.4 miles from the Wiehle-Reston East Station to Ashburn.

LIRR/MTA, East Side Access, New York, New York, External Quality Auditor. Robert performed quality auditing and related quality work for an FTA based audit of the General Engineering Consultant for this $10.8 billion project. Extending between Sunnyside, Queens, and Grand Central, the project will route the LIRR from its Main Line through new track connections in Sunnyside Yard and through the lower level of the existing 63rd Street Tunnel under the East River. In Manhattan, a new tunnel will begin at the western end of the 63rd Street Tunnel at Second Avenue, curving south under Park Avenue and entering a new LIRR terminal beneath Grand Central Station.

NEAL DEPASQUALE

VMF Design Discipline Lead

Valuable Experience:
- ✓ Design teams
- ✓ Construction teams
- ✓ MBTA
- ✓ Start-up, testing, and commissioning

Years of Experience: 38

Education: B.S., Architectural Engineering; Wentworth College of Technology

Professional License/ Certification: Massachusetts Certified Public Purchasing Official (MCPPO), Certification for School Project Designers and Owner's Project Managers

Neal is a Senior Project Manager with more than 35 years of experience supervising the study, design, and construction of various transportation and industrial projects for clients including the MBTA and MassDOT. He has overseen projects from conceptual stages through construction management that encompass all architectural and engineering disciplines. Neal's responsibilities during construction have included shop drawing documentation control and review, response to contractors' requests for information, evaluation of change order requests, periodic site inspections, revision of designs to accommodate for unforeseen site conditions encountered during construction, and interpretation of contract documents. He has also performed reviews at substantial completion, developed punch list items, participated in the startup and testing of equipment, and conducted final inspections.

DESCRIPTION OF COMPARABLE PROJECTS

Amtrak, ARRA CM Services Southampton Yard, Boston, Massachusetts, On-Site Quality Control Engineer/Closeout Documentation. Neal provided QC services for $22 million in rail yard and maintenance facility improvements for this design build project at Southampton Yard. Subsequent to the firm's completion of a feasibility study at Southampton Yard, Amtrak retained the firm as a subconsultant to a major consulting firm to prepare design build bridging documents and oversee construction. The project, which was funded through the American Reinvestment and Recovery Act of 2009, involved several separate design and contract packages, including the addition of a drop-table building and equipment to the existing high-speed rail building; complete rehabilitation of the existing train washer, including installation of spray arches, brushes, strippers, integrated train sensor systems, electrical power and controls, and interconnecting plumbing and pump systems; and a new building addition to house reclamation and filtering tanks and controls. Neal's role included daily inspections of the work during day, night, and weekend work shifts to ensure that the work adhered to safety requirements and design documents, specifications, and approved shop drawings.

Amtrak, Northeast Corridor Acela High-Speed Rail Maintenance Facilities Design-Build, Boston, Massachusetts and Queens, New York, Assistant Project Manager. Neal was responsible for overseeing the civil/site and utility design at the Southampton Yard in Boston and Sunnyside Yard in Queens, as part of this $112 million design build contract. His tasks included coordination with public and private utility agencies and companies; identifying building and environmental permit requirements, including their priority and approval duration; pedestrian and vehicular site circulation issues; and interfacing with surrounding rail traffic and operations. His responsibilities also included design support during construction.

WRTA, Vehicle Maintenance, Operations, and Storage Facility, Worcester, Massachusetts, Project Manager. Neal oversaw design services for a new, $75 million vehicle maintenance, operations, and storage facility for the Worcester Regional Transit Authority (WRTA). The 2-story, 150,000-sf facility has a capacity for 52 buses, 28 vans, and various nonrevenue vehicles, as well as space for 155 employees. Under his direction, the firm completed the Phase I – Program and Conceptual Design (15%), Phase II – Site Investigation and Analysis to advise the WRTA on the environmental impacts and costs of constructing the facility on the selected NStar site, and Phase III – 30% design to construct the new vehicle facility at the subject site. The firm then completed Phase IV – 100% final design, assisted WRTA and its project manager in the selection of a construction manager-at-risk in accordance with Massachusetts General Law Chapter 149A, and provided construction-phase services for the facility.

MBTA, Green Line Copley Station Accessibility Improvements, Boston, Massachusetts, Project Manager. Neal oversaw the design and administrative duties for $20 million accessibility improvements and general renovation of historic underground Copley Station. Improvements included rehabilitation of historic head houses, raising station platforms by 8 inches to accommodate the MBTA's new low-floor vehicles, adding ADA-compliant elevators at station platforms, and installing CCTV systems. Emergency egress stairs, tactile warning strips along station platforms, pedestrian ramps and crosswalks, new unisex toilets, new fare collection system and booths, new electric rooms, and offices were also included in this project. Neal worked closely with these agencies to develop elaborate construction zones and traffic management plans in coordination with city officials and abutters. He provided day-to-day construction phase services, attended weekly meetings, responded to requests for information and change-order requests, reviewed shop drawings, and visited the site as needed to ensure that completed work matched the design.

ENNIO ELEUTERI, PE

Retaining Walls Design Discipline Lead

Valuable Experience:

- ✓ MBTA
- ✓ Structural design
- ✓ Coordinates engineering and construction

Years of Experience: 23

Education: M.S., Civil Engineering, Northeastern University
B.S., Civil Engineering, Northeastern University

Professional License/ Certification: Professional Structural Engineer: MA, # EN41284-ST

Ennio is a structural engineer with more than 20 years of experience in design of various structural elements of roadways, bridges, and transit facilities for clients including the MBTA and MassDOT. He is a subject matter expert with regard to MassDOT standards and procedures, having worked on numerous contracts in cities and towns throughout Massachusetts. He has performed various types of structural analyses, including finite element analyses, time dependent analyses, and pre-stress/post-tension concrete analyses. Ennio is skilled in managing teams in the preparation of sketch plans and development of designs.

DESCRIPTION OF COMPARABLE PROJECTS

MBTA, Greenbush Line Rail Restoration Design-Build, Boston, Massachusetts, Lead Structures Engineer. Ennio performed and reviewed superstructure and substructure design calculations for 10 railroad and 8highway bridge rehabilitations located along 18 miles in five communities during the $320 million restoration of the Greenbush Line. Ennio coordinated multiple bridge designs with staff in multiple office locations. He assessed six prestressed concrete box beam bridges, designed or reviewed designs for substructure abutments, and performed construction phase services for the construction of steel and concrete bridges. Ennio also reviewed shop drawings and responded to requests for information for the MBTA project.

NB Development Group, Boston Landing Station, Boston, Massachusetts, QA/QC Reviewer. Ennio conducted a QA/QC review of structural designs for this new MBTA commuter rail station under construction adjacent to the New Balance corporate headquarters. Twhe design includes a glass elevator, pedestrian bridge, stairs, a center island platform, and canopy.

MassDOT, Belden Bly Bridge, Lynn and Saugus, Massachusetts, Project Manager. Ennio is overseeing the replacement of the Belden Bly Bridge. The proposed replacement bridge, a heel-trunnion bascule bridge with a 70-foot span, will carry four lanes of roadway traffic and two pedestrian sidewalks over the Saugus River between Lynn and Saugus, MA. The project scope includes

two approach spans, 300 feet of new retaining wall, and approach roadway work. Ennio has coordinated all engineering disciplines, including civil, utility, mechanical, electrical, and structural. He has also served as the point of contact for MassDOT's project manager for all technical and contractual issues. Traffic is currently carried by a temporary movable bridge.

MassDOT, Fore River Bridge Replacement, Quincy and Weymouth, Massachusetts, Lead Structural Engineer. Ennio is providing construction-phase support for a new $245 million vertical lift bridge. The 2,640-foot bridge will carry Route 3A over the Fore River. This project is part of MassDOT's Accelerated Bridge Program. The main span consists of a 324-foot vertical lift movable span over the Fore River that will provide a 250-foot navigation channel. Ennio prepared a sketch plan and 60% design development documents for the bridge. He managed multiple structural engineers in the design and detailing of the steel towers, steel truss lift span, foundation pier, cap, drilled shafts, and fender system. Additionally, Ennio coordinated architectural, mechanical, and electrical disciplines who contributed to the lift span design. He also reviewed the final design developed by the design-build team. During ongoing construction, he is involved with responding to RFIs, nonconformance reports, and other construction-related issues.

South Shore Tri-Town Development Corporation, East-West Parkway Design-Build, Abington, Weymouth, and Rockland, Massachusetts, Senior Structural Engineer. Ennio performed design reviews of bridges and retaining walls built along the eastern portion of the $41 million East-West Parkway, which serves as the main artery for SouthField, a $1.5 billion mixed-use village-style community at the former South Weymouth Naval Air Station. Ennio reviewed the design of bridges that cross two wetlands and the Old Swamp River, as well as the design of a mechanically stabilized earth retaining wall. He also verified that the designs met contract requirements, MassDOT Bridge Manual standards, and AASHTO criteria.

CATS, South Corridor Infrastructure Project, Charlotte, North Carolina, Structural Engineer. Ennio performed a structural review of contract documents for the proposed extension of the light rail for the Charlotte Area Transit System (CATS). The project entailed improvements to eight stations along 5 miles of the corridor to promote vehicular, pedestrian, and bike access to the future light rail stations. Ennio reviewed designs with the goal of reducing the overall construction cost of the project.

J. MARK ENNIS, PE, PMP

Deputy Design Manager

Stations, Infrastructure, ROW

Valuable Experience:

- ✓ MBTA
- ✓ Manage design team
- ✓ Rail transit
- ✓ Community issues
- ✓ State and local agencies
- ✓ Construction impacts

Years of Experience: 29

Education: M.S., Civil Engineering; Old Dominion University
B.S., Civil Engineering; University College of Dublin

Professional License/ Certification: Registered Professional Civil Engineer, Massachusetts

Mark has more than 25 years of varied experience involving new and rehabilitated bridge design, bridge confirmatory inspection and capacity ratings, retaining walls, and building design. He has overseen the design of numerous bridge types, including cable-stayed, vertical lift, bascule, truss, and arch bridges for highways and railroads. He is also experienced in stations, elevated structures and viaducts, tunnel structures, and tracks and signals; ADA compliance; regulatory agency permitting; and the coordination of community issues such as accessibility, safety, noise, and the mitigation of construction impacts. In addition, Mark is a project leader with a record of completing complex, multidisciplinary projects in accordance with quality, schedule, and budget objectives. His managerial responsibilities have included the overall administrative, contractual, financial, and technical leadership of transit and transportation projects, as well as interaction with public and private clients, supervision of subconsultants, and coordination with state and local agencies.

DESCRIPTION OF COMPARABLE PROJECTS

MBTA, Greenbush Line Rail Restoration Design Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Deputy Project Manager/Technical Coordinator. Mark oversaw the layout and design of 7 rail stations, 18 rail and highway bridges, 28 grade crossings, roadway intersections, 18 miles of track, and 2 railroad underpasses for this $320 million design-build project to restore service on the Greenbush Commuter Rail Line. Mark designed and coordinated partial and full demolition of abandoned bridges along the 18-mile rail ROW. Other work included permitting, landscaping, noise mitigation, and signal and communications systems. His coordination responsibilities also included resolving comments and issues with the contractor, the MBTA, the Historic Conservator, the five towns through which the railroad passes, and several other reviewing and permitting agencies. Mark was also responsible for managing construction phase services.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Design Lead. Mark was responsible for the design of the $255 million design-build project to restore what is considered to be the most historically significant bridge in Massachusetts. The 2,135-foot structure, constructed in 1908, carries Route 3 and MBTA Red Line tracks over the Charles River between Boston and Cambridge. It features ornate metal casting and masonry features, including four neoclassically inspired granite towers. Mark provided design oversight and obtained design approval from regulatory and public agencies, including MassDOT, FHWA, MBTA, Massachusetts Department of Conservation and Recreation, U.S. Coast Guard, the City of Boston, the City of Cambridge, the Massachusetts Department of Environmental Protection, and the Historic Review Board (Section 106). He provided ongoing support of public outreach efforts for his highly visible project, and was responsible for all aspects of the design, including the steel arch superstructure rehabilitation, deck system replacement to support both rail and roadway traffic, the masonry substructure strengthening, the masonry tower reconstruction, and the proposed signature pedestrian bridge that is to be located immediately adjacent to the bridge. The design phase is complete and the firm is providing construction support services for the contractor.

MassDOT, Fore River Bridge Replacement, Quincy and Weymouth, Massachusetts, Project Manager. Mark managed the design and permitting of the $245 million replacement of the 2,640-foot crossing of Route 3A over the Fore River. This project is part of MassDOT's Accelerated Bridge Program. The main span consists of a vertical lift movable span over the Fore River navigation channel. The original bascule bridge was constructed in 1933 and was a significant feature along Massachusetts Bay. It was recorded for the Historic American Engineering Record in 1969 but deteriorated and was replaced by a temporary structure in 2002. Mark managed the preparation of estimates, type study reports, and sketch plans, as well as environmental permitting coordinated with MassDOT, the U.S. Coast Guard, and the Massachusetts Office of Coastal Zone Management. During the investigation of different structure types, he participated in 19 public presentations of the project over the course of 18 months to various stakeholders, including elected officials, state and federal agencies, mariners, and the public. Mark generated a set of design-build procurement documents on behalf of MassDOT. He also oversaw construction support services.

BRIAN FLAHERTY

Technical Advisor

Valuable Experience:

- ✓ Design build
- ✓ MBTA
- ✓ Design and construction efforts
- ✓ Light rail

Years of Experience: 46

Education: Coursework, Civil Engineering, Hofstra University

Brian, STV's Design Build National Practice Leader, has more than 40 years of experience in the engineering and construction industry. He has held positions ranging from field engineer and project manager to principal-in-charge. With industry-recognized experience and capabilities, Brian is known for creating a climate in which construction activities progress smoothly and for his excellent direction of all aspects of construction management and design build activities. An experienced project executive, he has considerable experience successfully directing projects for transportation and government agencies, maintaining control over all schedules, costs, and expenditures. Projects under his direction have encompassed the coordination of, and interface with, architectural and engineering designers, contractors, trade unions, transit operators, and rail vehicle manufacturers. Brian's innovative and award-winning assignments have included projects with varying construction costs up to $10 billion.

DESCRIPTION OF COMPARABLE PROJECTS

MBTA, Greenbush Line Rail Restoration Design Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Constructability Coordinator. Brian served as Constructability Coordinator responsible for coordinating all design efforts and developing constructability reports for the 18-mile railroad rehabilitation project. The project scope consisted of the restoration and reconstruction of the largely out-of-service railroad right-of-way and included the implementation of seven new stations (each with an 800-foot-long high-level platform), a new signal and communication system, and a layover facility. The $320 million MBTA project also included a modified shallow cut tunnel, which involved a complicated vertical alignment; an 800-foot cut-and-cover tunnel with 900-foot boat section approaches on each side; and off-line freight facilities.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Constructability Coordinator. Brian is serving as Constructability Coordinator responsible for coordinating all design efforts and developing constructability reports for this $255 million design build rehabilitation of the Longfellow Bridge, a 2,135-foot structure that carries Route 3 and the MBTA's Red Line over the Charles River. As the lead designer, STV provided multidisciplinary design services for the bridge, as well as plans

for trackwork, traction power, communications, and signals for the Red Line. When complete, the bridge will be AASHTO compliant and ADA compliant. The design phase is complete and the firm is providing construction support services for the contractor.

MTA, Capital Construction/LIRR East Side Access, Queens, New York, Constructability Coordinator. Brian is serving as Constructability Coordinator responsible for coordinating all design efforts and preparing constructability reports for this $10 billion project to provide tunnel engineering services, including planning, preliminary and final design engineering, and construction phase services to extend Long Island Rail Road (LIRR) service to Manhattan's East Side, terminating in Grand Central Terminal. Design elements include a new station in Sunnyside; rail maintenance facilities and yard; and new intermodal station and platform facilities within Grand Central Terminal.

NJ TRANSIT, Meadowlands Maintenance Complex, Kearny, New Jersey, Project Director. As Project Director for the construction phase, Brian directed the construction management of this major rail vehicle maintenance facility and yard. He was directly responsible for establishing the project procedures manuals, a QA/QC program, the project schedule, and a work breakdown structure to administer the budget for the duration of the project. He was also responsible for all resource allocations and for the review of project status reports, covering project progress, budget adherence, and schedule compliance. He served as the main point of contact between the client and the construction management team. The $106.7 million complex incorporates state-of-the-art service equipment and machinery; industrial, mechanical and electrical systems for maintenance and operations functions; administrative/employee and storage facilities; traction power systems; and utility systems, covering drainage, water, supply, lighting, communications, ancillary power, and waste disposal. The facility is NJ TRANSIT's primary facility for rolling stock maintenance.

MICHAEL HEALEY, LCS, NETTCP QAT

Project Controls Manager

Valuable Experience:
- ✓ MBTA
- ✓ Project controls
- ✓ Design and construction

Years of Experience:	38
Education:	B.S., Administration, University of Massachusetts at Amherst
Professional Licenses/ Certifications:	Licensed Construction Supervisor (LCS), Massachusetts # CS- 063675 Certified Quality Assurance Technologist, NETTCP Massachusetts Certified Public Purchasing Official (MCPPO), Certification for School Project Designers and Owner's Project Managers

Michael is a project controls expert and licensed construction supervisor (LCS) with considerable experience providing contractor oversight, document control, requests for information responses, change-order management, and QA/QC to the MBTA. He has served in various roles, including deputy project manager, director of project controls, and QA/QC manager for MBTA initiatives, such as the MBTA Greenbush Line Rail Restoration Design-Build. Michael is valued for his ability to coordinate all disciplines, including civil, structural, HVAC, plumbing, electrical, mechanical, and architectural. A well-rounded professional, Michael is also skilled in surveying, design, and resident inspection.

DESCRIPTION OF COMPARABLE PROJECTS

MBTA, Greenbush Line Rail Restoration Design-Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Director of Project Controls and QA/QC. Michael was responsible for all document control functions related to the submittal of more than 100 individual design packages, from preliminary to final design, for the $320 million restoration of this 18-mile-long commuter rail line. This MBTA project encompassed 18 bridges (both railroad and highway), 7 new stations, 1 tunnel, 1 underpass, 7 at-grade parking facilities (200 to 1,000 spaces), access roads, retaining wall structures, and wetland delineation and permitting. Michael assumed the responsibilities of the outgoing Director of Project Controls. He directed project controls for shop drawings, subconsultant coordination, transmittal, and tracking and recovery of all documents via an Expedition database.

MassDOT, Longfellow Bridge Rehabilitation Design-Build, Boston and Cambridge, Massachusetts, Project Controls Manager/Assistant QC Manager. Michael tracked change orders and reviewed civil, structural, and traffic control designs for the $255 million rehabilitation of this bridge over the

Charles River that carries Route 3 and the MBTA's Red Line between Boston and Cambridge. Michael tracked all project documentation, including cost and schedule records, and provided general maintenance of the firm's SharePoint database. His role involved evaluating contractor-initiated changes to the final design, identifying any changes that conflicted with engineering plans, and marking potential change orders that presented the risk of cost increases and schedule overruns. Michael compiled the information in a spreadsheet that was used to negotiate and resolve approximately 100 items with the design team, contractor, and client. Additionally, he provided QC reviews of various elements of design, such as the bridge structure, track, sidewalks, roadway, and traffic control plans. Michael's oversight involved peer reviews of design drawings to identify potential errors, such as miscalculations or cosmetic inadequacies.

MBTA, Green Line Copley Station Accessibility Improvements, Boston, Massachusetts, Deputy Project Manager. Michael oversaw the day-to-day design and administrative duties for this project to make the historic MBTA Copley Station, constructed in 1912, compliant with ADA guidelines. Michael ran meetings, wrote minutes, responded to RFIs and change-order requests, reviewed shop drawings, coordinated with subcontractors and the client, and visited the site to make sure work was completed according to design plans and specifications.

MBTA, Commuter Rail Maintenance Facility, Somerville, Massachusetts, Inspector. Michael conducted construction phase service site visits for coordination of disciplines, including HVAC, plumbing, industrial, structural, civil, trackwork, and survey of a series of buildings constructed to house locomotive and coach repair.

Amtrak, ARRA CM Services Southampton Yard, Boston, Massachusetts, Senior Resident Engineer. Michael provided on-site construction management for $22 million in rail yard improvements at Southampton Yard in Boston. Subsequent to STV's completion of a feasibility study at Southampton, Amtrak retained the firm as a subconsultant to a major consulting firm to prepare design-build bridging documents and oversee construction. The project, which was funded through the American Reinvestment and Recovery Act of 2009, involved restoration of the existing rail facility, including train washer replacement, track improvements, roadway reconstruction, security upgrades, and utility improvements. Michael oversaw four other resident engineers/inspectors staffing this fast-track project and sometimes operated 7 days a week and 24 hours a day. He reviewed design-build submissions and performed QC inspection of all contractors' work to verify compliance with the approved plans and specifications.

JEROME MACKENZIE, PE

Structures Design Discipline Lead

Valuable Experience:

- ✓ Managing design teams
- ✓ Design build teams
- ✓ Construction techniques and staging
- ✓ MBTA

Years of Experience: 34

Education: B.S., Civil Engineering, Northeastern University

Professional License/ Certification: Professional Structural Engineer: MA #34740-ST

Jerome has more than 30 years of experience as a structural engineer, possessing a strong management background for the design of fixed and movable bridge rehabilitation and replacement projects for clients including the MBTA and MassDOT. His areas of expertise include condition assessments; nondestructive inspection techniques; structural analysis; design and review of design calculations; construction inspection; prestressed concrete analysis; and preparation of contract drawings, specifications, and construction cost estimates. A National Bridge Inspection Standards (NBIS)-certified inspector, Jerome is highly knowledgeable of inspection standards for highway and railroad bridges. His projects have ranged from simple footprint replacements to complex structures, often involving elaborate construction techniques and staging. Jerome is a skilled project manager with a thorough understanding of how to complete projects that meet client quality objectives, schedules, and budgets. He is skilled at coordinating tasks among clients, subconsultants, and in-house engineers to bring together engineering documents from planning/ permitting stages to final design/contract award.

DESCRIPTION OF COMPARABLE PROJECTS

MBTA, Greenbush Line Rail Restoration Design-Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts. Senior Structural Engineer. Jerome provided structural engineering services for the MBTA's restoration and reconstruction of this 18-mile-long railroad line on the South Shore of Massachusetts. The project involved reconstruction of the right-of-way, rehabilitation or replacement of 18 bridges (10 rail and 8 highway), and construction of 7 new stations (each with an 800-foot-long high-level platform), a new signal and communication system, and a layover facility at the end of the line in the Greenbush area of Scituate. Jerome reviewed the structural design for several rail bridges on this project.

MassDOT, Longfellow Bridge Rehabilitation Design-Build, Boston and Cambridge, Massachusetts, Lead Structural Design Engineer. Jerome oversaw teams of designers focused on the superstructure elements of the $255 million rehabilitation of the Longfellow Bridge between Boston and

Cambridge. Constructed in 1908, the 2,135-foot bridge carries Route 3 and the Red Line over the Charles River. It has structural deficiencies and widespread deterioration of its ornate masonry and metal casting features. In managing the structural team, Jerome coordinated design efforts with a variety of disciplines such as electrical lighting engineers. During the ongoing construction, he is managing the shop drawing and change order review processes and providing general construction advice, especially as it relates to the fit-up of new bridge elements. Because of the bridge's historic value, Jerome is also working closely with consultants specializing in Section 106 of the National Historic Preservation Act of 1966 to verify that the bridge's original appearance is preserved.

DART, LRT Extensions Phase I & Phase II, Dallas, Texas, Lead Bridge Engineer. Jerome oversaw preliminary through final design for three light rail and three heavy rail bridges in the Northwest Corridor from Houston Street to Turtle Creek in Line Section NW-1A as part of this $2.3 billion project to expand the Dallas Area Rapid Transit (DART) light rail transit system, extending it to points farther from Dallas and making it more comprehensive within the city.

Metro-North, PECK Drawbridge and Bridgeport Railroad Viaduct Rehabilitation, Bridgeport, Connecticut, Structural Design Engineer/ Inspector. Jerome performed a bridge inspection for the $45 million rehabilitation of the PECK Railroad Bridge. Originally constructed in 1903, the PECK Drawbridge is a vital connection on the New Haven Line and the larger Northeast Corridor between Boston and Washington, D.C. The project involved a comprehensive study; in-depth inspection; total design, including civil, structural, and track engineering; and construction support services for the award-winning replacement of the PECK Drawbridge and the 3,000-foot Bridgeport Railroad Viaduct. The viaduct runs through downtown Bridgeport, crossing four main streets and the Pequonnock River.

MassDOT, University Avenue Bridge Improvements, Lowell, Massachusetts, Project Manager. Jerome managed the design and construction phases for the replacement of this historic steel deck truss bridge over the Merrimack River. The $36 million MassDOT project included the demolition and removal of the existing 3-span structure and the construction of a new 520-foot bridge. The superstructure is composed of two continuous spans of deck trusses that are supported by new abutments and a new pier constructed in the middle of the Merrimack River. The project also involved upgrading traffic signal equipment and revising intersection geometry at the Pawtucket Street and University Avenue and V.F.W. Parkway and University Avenue intersections.

CHRISTOPHER R. MCDERMOTT, PE, LSP

Environmental Manager

Valuable Experience:

- ✓ Licensed Site Professional Services
- ✓ Soil Characterization for Disposal
- ✓ Groundwater Characterization & NPDES RGP Permitting & Treatment
- ✓ Soil and Groundwater Remediation Design
- ✓ Contaminated Soil and Groundwater Management

Years of Experience: 22

Education: B.S., Engineering Sciences, Washington University, St. Louis, MO Christopher
B.S., Applied Math and Physics, Providence College

Professional Licenses/ Certifications: Licensed Site Professional, MA # 1955
Professional Engineer, MA # 48272

Christopher has more than 20 years of experience providing environmental engineering and Licensed Site Professional (LSP) services to large infrastructure and transportation projects in Massachusetts. Over the course of his career, he has worked on virtually all of the major stations, facilities, and yards within the MBTA system. He has excellent working relationships with the MBTA Environmental Department, as well as other departments at the MBTA, including Design and Construction, Operations, Budget, Safety, and Contract Administration. Christopher is experienced in collecting data, evaluating current and future risk, and designing a creative and cost-effective strategy for compliance and site closure under the Massachusetts Contingency Plan (MCP). He takes full advantage of MCP exemptions and policy to bring sites to closure.

DESCRIPTION OF COMPARABLE PROJECTS

MassDOT, Longfellow Bridge Rehabilitation Design-Build, Boston and Cambridge, Massachusetts, LSP. Christopher managed the characterization of contaminated soil and all hazardous materials on the bridge, the MBTA Red Line right-of-way, the piers, towers and abutments, the Storrow Drive pedestrian walkway, and associated subsurface soil in the area. The 2,135-foot structure, constructed in 1908, carries Route 3 and MBTA Red Line tracks over the Charles River between Boston and Cambridge. Christopher directed development of soil and hazardous materials management plans to enable cost-effective and timely construction.

WRTA, Vehicle Maintenance, Operations, and Storage Facility, Worcester, Massachusetts, LSP. Christopher directed extensive pre-construction characterization, developed plans, specifications, and cost estimates for soil remediation and a vapor barrier for the Worcester Regional Transit Authority (WRTA)'s new vehicle maintenance facility, prepared Construction Release Action Measure (RAM) and multiple MCP deliverables, and directed the oversight of contaminated materials management, on-site soil remediation,

environmental permitting, and monitoring of work zone and perimeter air quality for contaminated dust and asbestos fibers. He coordinated directly with MassDEP regarding soil remediation efforts and discovery of asbestos in fill. Christopher obtained quotes and coordinating off-site disposal of 70,000 tons of contaminated soil and petroleum/coal tar liquids.

Bosfuel Corporation, MCP Compliance and Environmental Management during Pipeline Construction at Logan Airport, Boston, Massachusetts, LSP-of-Record/Project Manager. Christopher provided environmental investigation, remediation design, construction oversight and MCP compliance in support of Bosfuel's $50 million replacement of a portion of Logan's Fuel Delivery System (FDS). TRC collected subsurface data on soil, groundwater, and light non-aqueous phase liquid (LNAPL) and prepared an Immediate Response Action (IRA) Plan, Phase I – Initial Site Investigation & Tier Classification and multiple IRA Status Reports for a new reportable condition. TRC prepared a RAM Plan and NPDES Remediation General Permit and managed over 20,000 cubic yards of impacted soil as well as contaminated groundwater and LNAPL during construction. Christopher coordinated MCP compliance issues with other airport stakeholders, including Massport.

MBTA, On-Call Environmental Services Contract, Boston, Massachusetts, Project Manager/LSP. Christopher provided environmental engineering and LSP services on several task orders, including the Durante Wetlands Mitigation remedial cost estimation, evaluation of groundwater remediation at Cabot Yard and a wide variety of environmental staff training.

MBTA, Wellington Carhouse Expansion and Improvements, Medford, Massachusetts, LSP/Senior Engineer. Christopher performed the assessment of contaminated soil and hazardous building materials during the carhouse renovation. He provided plans and specifications for environmental design portion of 30%, 60%, 90%, and 100% Final Design contract documents, as well as input to cost estimation and construction scheduling. He recently directed the disposal pre-characterization efforts for roughly 20,000 cubic yards of soil to be excavated during construction.

MBTA, 12 Bridges Replacement Project, Boston, Massachusetts, Senior Engineer/LSP. Christopher directed the due diligence hazardous materials assessment of multiple bridges, as well as the evaluation of hazardous materials, including asbestos and lead-based paint, in existing bridge structures.

THOMAS O'HARA

Deputy Design Manager
Operations, Systems, and VMF

Valuable Experience:

- ✓ MBTA
- ✓ Rail transit
- ✓ Power systems
- ✓ Power facility operations
- ✓ Infrastructure improvements
- ✓ Design disciplines and construction teams

Years of Experience: 34

Education: Coursework, Business Management; Quincy Junior College

Professional Licenses/ Certifications: Journeyman Electrician, Massachusetts Right-of-Way Training, Massachusetts Bay Transportation Authority

Thomas is an expert in transit operations and rail power systems who led the MBTA's Power Division for almost eight years. He has overseen the commissioning of new traction power substations, installation of OCS for the Silver Line, the AC cable replacement program, SCADA systems, and mobile substations, and is intimately familiar with MBTA operations, having directed and supervised the maintenance of local power systems, equipment, and transmission and distribution areas. In his former MBTA role, Thomas managed multiple capital improvement projects and participated in the negotiations of a 5-year, all-requirements power contract to purchase electricity for the agency. He and his Power Department were integral to previous Green Line projects including North Station and Riverside Station. He also successfully terminated rail services on the Mattapan High-Speed Line for complete restoration of the power systems.

DESCRIPTION OF COMPARABLE PROJECTS

MBTA, Wellington Carhouse Expansion and Improvements, Medford, Massachusetts, Traction Power Specialist. Thomas coordinated with multiple disciplines to design the stinger trolley system for the expansion and renovation of the 120,000-sf Wellington Carhouse maintenance facility. The renovation will allow the MBTA to accommodate 152 new Orange Line cars scheduled to replace the current fleet of 120. The stinger system is needed to facilitate the installation of new traction power equipment while the existing feeds power to the stinger trolley bugs. The existing carhouse power receptacles are not functioning and new equipment will be installed in the pit areas.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Systems Lead. Thomas coordinated with all the different disciplines to design the rail systems for MassDOT's rehabilitation of the Longfellow Bridge Project, which carries Route 3 and the MBTA's Red Line between Boston and Cambridge. The design, which incorporates the

communication, signal, track, and traction power systems into one package, has been staged so service can be maintained during construction. Thomas has also introduced a vital serial link for the signal system, which the MBTA approved. The design phase is complete and the firm is providing construction support services for the contractor.

MBTA, Orange Line Traction Power Upgrades, Boston, Massachusetts, Project Manager. Providing construction-phase support during the ongoing upgrade of the traction power substations located at the Sullivan, Wellington, Malden, and Oak Grove stations north of Boston. Thomas has provided design, QA/QC, scheduling, and budget services for the project, which involves the comprehensive replacement of outdated AC and DC equipment originally installed in the 1970s that have reached the end of their life cycles. The $31 million project involves installation of 13.8-kV switchgear, station service auxiliary transformers, traction power transformers, DC switchgear, a cathode buss duct, the negative drainage board, SCADA and 1-on-1 supervisory control cabinets; and STB cabinets.

HMLP, Stray Current Testing and Evaluation, Boston, Massachusetts, Project Manager. Thomas oversaw the monitoring and evaluation of stray current within an area of the MBTA's Greenbush Line on behalf of Hingham Municipal Light & Power (HMLP). HMLP maintains seven utility poles within a 3,100-foot easement owned by the authority that have the potential to produce stray current and damage signal and communications equipment.

MBTA, Operations Support GEC, Various Locations, Massachusetts, Project Manager. Thomas managed an on-call team of professional consultants that assisted with the maintenance of tracks, stations, vehicles, and maintenance facilities. The contract included a Control Center Power Load Study and Electrical Distribution Equipment Condition Assessment and Elevator and Escalator Specifications for Maintenance and Repair, among other tasks.

ROBERT J. PALERMO, PE

Geotechnical Design Discipline Lead

Valuable Experience:

- ✓ Deep Foundations for Bridges/Viaducts
- ✓ Retaining Wall Design
- ✓ Instrumentation and Monitoring
- ✓ Subsurface Explorations
- ✓ Seismic Design
- ✓ LRFD
- ✓ Lateral Earth Support
- ✓ Ground Improvement
- ✓ Extensive design build experience

Years of Experience: 44

Education: B.S., Civil Engineering, Northeastern University
M.S. Studies, Massachusetts Institute of Technology

Professional License/ Certification: Professional Engineer, MA No. 32053

Robert is a Senior Principal at GZA and has more than 40 years of experience in all aspects of geotechnical engineering and underground construction on bridge and transit projects in the U.S. and Canada, including: soil and rock mechanics, shallow and deep foundation engineering, seismic design, underpinning, instrumentation and monitoring, ground improvement, construction dewatering, and lateral support systems.

He has worked on over 150 bridges throughout the country ranging in size from $5 million to the recently completed $3.9 billion Tappan Zee Bridge Replacement Design-Build, which received several industry awards for its foundation design. Having worked on more than 100 bridge projects for MassDOT and the MBTA, he is knowledgeable of the GLX project design requirements and the local ground conditions.

Robert also served as the lead geotechnical engineer on transit projects such as the Bowdoin-Charles Connector, North Station Transportation Improvement Project, TD Garden, Green/Blue and Orange Line Tunnel Rehabilitation for the MBTA, and the recently completed 1st phase of the Second Avenue Subway project, and as the contractors engineer on the New Haven-Hartford-Springfield Amtrak project.

He has worked on several large design-build and P3 projects throughout the U.S. Robert has presented on foundation design at Transportation Research Board, The MOLES, Deep Foundations Institute, and the American Society of Civil Engineers.

DESCRIPTION OF COMPARABLE PROJECTS

NY State Freeway Authority, Tappan Zee Hudson River Crossing Design-Build, Tarrytown/South Nyack, New York, Lead Geotechnical Engineer. This Design-Build project consisted of the design and construction of two new 3-mile-long multiple span structures that carry I-87/287 across the Hudson River between Rockland and Westchester Counties. Robert was

responsible for the foundation design performed during the Tender Design phase, as well as the subsurface explorations, pile load testing program, and engineering analyses performed during the final design phase. Other services included quality control for pile and drilled shaft installation and environmental consulting. GZA's foundation design resulted in significant cost savings to the owner and the Fluor-led team.

MassDOT/MBTA, Multiple Bridges, Various Locations, Massachusetts, Lead Geotechnical Engineer/Senior Technical Reviewer. Robert has served as the Lead Geotechnical Engineer/Senior Technical Reviewer on more than 100 replacement or rehabilitation bridge projects, some of which included use of accelerated bridge construction methods. Projects include: Webster Street over Middle River, Worcester; Revere Beach Parkway over B&M Railroad, Revere; I-495 Bridges (Taylor Street, Route 2, and B&M Railroad), Littleton; I-95 (Rt 128) Add-A-Lane, Needham to Wellesley; Lagoon Pond Bridge, Martha's Vineyard; River Street and Western Avenue Bridges over Charles River, North Washington Street Bridge, Boston, Water Street, Danvers, and the Gloucester Drawbridge and Savin Hill Underpass for the MBTA.

Amtrak, Hartford Line, Various locations, Connecticut and Massachusetts, Lead Geotechnical Engineer. The project consisted of the widening of the existing railroad alignment to accommodate an additional track for high speed service between Springfield and New Haven. GZA redesigned more than 8,000 lf of retaining wall to support Cooper E80 train loads as value engineering for the contractor, Middlesex Corporation. The redesign resulted in significant schedule and cost savings to the owner and the contractor.

MBTA/Delaware North, TD Garden, Boston, Massachusetts, Lead Geotechnical Engineer. Robert designed rock socketed caissons, load bearing elements, and lateral support walls for a new facility with 5 levels of below grade parking. He was responsible for oversight of field engineers present on site during construction of over 200, 2.5- to 8-foot diameter, polymer slurry stabilized caissons and over 1,100 lf of reinforced concrete bentonite stabilized slurry walls. Robert reviewed instrumentation monitoring data during top-down construction activities for the 60-foot-deep excavation into clay/till/rock. He also performed environmental site investigation programs to evaluate the quality of soil and groundwater with regard to any impact on soil and groundwater handling and disposal techniques during construction.

MARK W. PELLETIER, PE

Design Manager



Valuable Experience:

- ✓ Experience working with the MBTA
- ✓ Local knowledge
- ✓ Experience managing large design teams
- ✓ Extensive rail transit experience
- ✓ Systems integration
- ✓ Start-up, testing, and commissioning experience
- ✓ Coordination with design build teams

Years of Experience:	34
Education:	B.S., Civil Engineering; University of Massachusetts
Professional Licenses/ Certifications:	Professional Civil Engineer: MA #34750 Professional Structural Engineer: MA #37343

Mark has spent the better part of his 34-year career at STV helping improve service for MBTA customers, particularly along the Green Line. He has overseen the North Station Transportation Improvement, Green Line Light Rail Accessibility Program, and Copley Station Accessibility Improvements, all of which were complex, multidisciplinary efforts that helped make the nation's busiest light rail system better. Mark is well-versed in all facets of engineering, including feasibility studies, design, permitting, and construction staging, but his greatest skill is his ability to communicate client goals to stakeholders and design teams. This quality made him well-suited to serve as design manager for the Greenbush Line Rail Restoration Design-Build, a challenging, 5-year assignment requiring day-to-day oversight of 100 design professionals and 15 subconsultant firms. Mark's on-site leadership was integral to Greenbush's 2007 launch and helped win STV the 2010 Gold Award for professional design excellence from the American Council of Engineering Companies of Massachusetts. He will commit to the same level of dedication for the duration of the Project.

DESCRIPTION OF COMPARABLE PROJECTS

MBTA, Greenbush Line Rail Restoration Design Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Design Manager. Mark oversaw the $320 million complete design, including engineering services and management of all design consultants, for the reconstruction of the out-of-service railroad ROW. He led the design for the 18-mile ROW construction and oversaw the design for a five-legged roundabout, the rehabilitation of 10 railroad bridges, and eight highway bridges, including substructure and superstructure replacement, as well as seven stations and 28 grade crossings.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Principal-in-charge. Mark is overseeing the $255 million design build effort to rehabilitate the Longfellow Bridge, a 2,135-foot structure that carries Route 3 and the MBTA's Red Line over the Charles River. As the lead designer, STV provided multidisciplinary design

services for the bridge, as well as plans for trackwork, traction power, communications, and signals for the Red Line. When complete, the bridge will be AASHTO compliant and ADA compliant. The design phase is complete and the firm is providing construction support services for the contractor.

MassDOT, Fore River Bridge Replacement Design-Build, Quincy and Weymouth, Massachusetts, Project Manager/Principal-in-Charge. Mark was responsible for the alternatives analysis, permitting, achievement of 60% design, and preparation of bridging documents for design-build procurement for the $245-million vertical-lift bridge of Route 3A over the Fore River. He is currently overseeing construction-phase services and design peer reviews on behalf of MassDOT.

MBTA, Wellington Carhouse Expansion and Improvements, Medford, Massachusetts, Principal-in-Charge. Mark oversaw the design development and final design services for the MBTA's $80 million expansion of the Wellington Carhouse. The firm designed a 12,000-sf single-bay addition to the east side of the building, as well as upgrades to safety and security, and the MEP/fire protection systems.

WRTA, Bus Maintenance, Operations, and Storage Facility, Worcester, Massachusetts, Principal-in-Charge. Mark oversaw the design and construction of a two-story, 150,000 sf operations and maintenance facility for the Worcester Regional Transit Authority (WRTA). The firm provided architectural, structural, MEP, fire protection, industrial, traffic, and civil design services for the $75-million facility. STV also assisted WRTA and their owner's project manager with the RFQ preparation and selection process to secure a CMR for this project, in accordance with Massachusetts General Law Chapter 149A.

MBTA, Green Line Copley Station Accessibility Improvements, Boston, Massachusetts, Project Manager/Project Director. Mark directed the $20 million accessibility improvements and general renovation of historic underground Copley Station. The improvements included rehabilitation of historic head houses, raising station platforms by 8 inches to accommodate the MBTA's new low-floor vehicles, adding ADA-compliant elevators at station platforms, and installing CCTV systems.

ERIC ROOT, PE

Systems Design Discipline Lead

Valuable Experience:

- ✓ Traction power designs and analyses for LRT
- ✓ MassDOT
- ✓ Systems integration
- ✓ Start-up and testing

Years of Experience: 27

Education: B.S., Electrical Engineering; Virginia Polytechnic Institute and State University

Professional License/ Certification: Professional Engineer, VT Electrical #018.0107605

Eric is an electrical engineer with more than 25 years of experience involving transportation, utility, and power generation projects. His expertise includes systems project management, electric power systems, system start-up, interfaces for light rail transit and commuter systems, and controller design for clients including MassDOT. Eric also has experience with voltage analysis and simulations, value engineering, and construction inspection and management. Additionally, he has frequently served as systems manager and traction power engineer for new transit systems in major metropolitan areas throughout the United States and Canada.

DESCRIPTION OF COMPARABLE

City of Ottawa, Confederation Line LRT, Ottawa, Ontario, Canada, Traction Power Engineer. Eric completed the initial traction power design and analysis for the $2.1 billion project to transform an exclusive, fully built-out bus rapid transit system into a light rail transit network – the first such conversion in North America. Eric provided preliminary design for a 1,500-VDC system, instead of a 750-VDC system, to accommodate the required vehicle consists and headways. The line will extend 7.8 miles, linking the neighborhoods of Tunney's Pasture and Blair Station.

Region of Waterloo, Rapid Transit Division ION LRT System, Ontario, Canada, Systems Manager. Eric is providing engineering services for the $818 million ION LRT system for the Region of Waterloo Rapid Transit Division. The 11.8-mile (19-km) network will operate 14 light rail vehicles across 22 stations. Eric is responsible for managing the systems design for the design-build light rail project, including train control, traction power, OCS, and communications. He is coordinating the interfaces between the systems element with the civil, track, and station design leads and working with vendors to achieve a project agreement that is compliant and functionally correct.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Traction Power Engineer. Eric was responsible for both train control and traction power for this $255 million design build

rehabilitation of the Longfellow Bridge, a 2,135-foot structure that carries Route 3 and the MBTA's Red Line over the Charles River. As the lead designer, STV provided multidisciplinary services for the bridge, as well as plans for trackwork, traction power, communications, and signals for the Red Line. When complete, the bridge will be AASHTO compliant and ADA compliant. The design phase is complete and the firm is providing construction support services for the contractor.

Metro East, San Fernando Valley Transit Corridor, Los Angeles, California, Systems/Traction Power Design Lead. Eric led rail systems and traction power design for proposed improvements to transit service and regional connections through the heart of Los Angeles's San Fernando Valley along Van Nuys Boulevard and San Fernando Road. Key alternatives being studied for the Los Angeles County Metropolitan Transportation Authority (Metro) include LRT, bus rapid transit, and streetcar modes. Eric's responsibilities included helping to locate traction power substations for the purposes of environmental clearance.

CATS, LYNX Blue Line Extension Light Rail Project, Charlotte, North Carolina, Systems Manager/Traction Power Engineer. Eric was responsible for performing systems management for preliminary and final engineering services for the 9.3-mile Blue Line Extension for the Charlotte Area Transit System (CATS). The extension will run from Center City Charlotte northeast to the University of North Carolina at Charlotte. Eric managed various systems, including train control, communications, traction power, and the overhead contact system. He was responsible for the sizing and location of traction power substations, and developed traction power technical reports and design criteria. Eric also performed computer-based load flow simulations to determine voltage drop and verification of substation locations. In addition, he led the integration of the systems design package with the civil and station finish design packages.

MassDOT, Red/Blue Line Connector, Boston, Massachusetts, Lead Systems Engineer. Eric performed load flow simulation for a proposed MassDOT project to extend the MBTA Blue Line 1,500 feet on the Bowdoin end while eliminating the existing Bowdoin Station and adding a new Charles/MGH Station. Eric's simulation also included installation of a new traction power substation and removal of an existing feeder from North Substation. The load flow simulation verified that the design met the operation criteria of 6-car trains running at 4-minute headways at crush load.

PAUL TYRELL, PE, PLS, LEED AP BD+C

Road & Right-of-Way/Grading Design Discipline Lead

Valuable Experience:

- ✓ MBTA
- ✓ Civil design elements
- ✓ Design/construction teams
- ✓ Rail transit

Years of Experience:	31
Education:	B.S., Civil Engineering; Wentworth Institute of Technology
Professional Licenses/ Certifications:	Registered Professional Civil Engineer, Massachusetts Professional Land Surveyor, Massachusetts LEED Accredited Professional

Paul is an accomplished professional engineer and land surveyor with technical expertise in boundary and subdivision control law, easements and property rights issues, environmental permitting, hydraulics and hydrology, and trenchless technologies. Paul has worked in both the field and the office preparing designs and overseeing construction of a wide variety of projects, including bridge, highway, and railroad designs; synthetic and natural turf field installations; and commercial and residential developments. He has prepared construction documents for a variety of project delivery methods, including design-build, bid-build, and private solicitation. As a senior civil engineer, he contributed greatly to the success of the Greenbush Line by assuming responsibility for 130 design packages requiring inventory, evaluation, relocation, and protection of more than 250 different utilities along the 18-mile alignment.

DESCRIPTION OF COMPARABLE PROJECTS

MBTA, Greenbush Line Rail Restoration Design-Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Senior Civil Engineer. Paul designed all required project utilities and utility relocations for the $320 million, 18-mile long reconstruction of the out-of-service railroad ROW. Paul oversaw preparation of more than 130 design packages with multiple submissions. He managed all utility design; was responsible for inventory, evaluation, relocation, and protection of more than 250 different utilities along the proposed alignment; and coordinated with the design-build contractor and numerous public and private agencies.

MassDOT, Longfellow Bridge Rehabilitation Design-Build, Boston and Cambridge, Massachusetts, Deputy Project Manager. Paul is responsible for coordinating design and construction for the $255 million design-build rehabilitation of the Longfellow Bridge, a 2,135-foot structure that carries Route 3 and the MBTA's Red Line over the Charles River between Boston and Cambridge. The firm provided multidisciplinary design services for the

bridge and an adjacent pedestrian bridge, as well as plans for trackwork, traction power, communications, and signals for the Red Line. During the design phase, Paul coordinated design efforts for the entire design team including numerous subconsultants. He managed document control, design schedule, project submissions, and monitored QA/QC and permit compliance. The design phase is complete and the firm is providing construction support services for the contractor.

MBTA, Wellington Carhouse Expansion and Improvements, Medford, Massachusetts, Civil QA/QC Reviewer. Paul conducted a quality review and endorsed the final design submission for all civil components of the planned expansion and renovation of the Wellington Carhouse. The firm designed a 12,000-sf single-bay addition to the east side of the building and upgrades to safety, security, and the MEP/fire protection systems. Paul reviewed final designs and specifications for track alignment modifications within the carhouse and yard. He also reviewed final plans for relocating and installing site utilities and the dimensions of an adjacent access road the firm designed between the carhouse addition and the Wellington Station passenger station. After verifying the consistency, clarity, safety, and constructability of the plans, and their adherence with the project's official Quality Management Plan and MBTA standards, Paul authorized the design packages for bidding and construction.

Amtrak, ARRA CM Services Southampton Yard, Boston, Massachusetts, Owner's Representative. Paul provided design review services for $22 million in improvements to the Southampton Rail Yard. Subsequent to STV's completion of a feasibility study at Southampton Yard, Amtrak retained the firm to prepare design-build bridging documents and oversee construction. The project involved complete restoration of the existing rail facility to include a new train washer, track improvements, roadway reconstruction, security upgrades, and utility improvements. Paul provided construction management (CM) services, including review of all design-build submissions and QC inspections of all contractors' works to verify compliance with the approved plans and specifications.

3.2 QUALITY MANAGEMENT PLAN

We have specifically developed our Quality Management Plan to complement the MBTA's Quality Management Plan, which is well known and understood by our team members. By taking an owner-operator perspective to quality management, GLX Constructors has an ISO 9001-compliant Quality Management Plan that is aligned with our Project Management Plan and incorporates our staff members' NETTCP and ASQ quality management certifications.

Our core belief in quality Project execution begins with the maxim: "Quality starts and stops with the individual."

Design Build (DB) construction is a highly integrated and fast-paced environment involving the activities of distinctly different disciplines, working separately and together, to complete a project in the fastest and most cost-effective manner. Therefore, an effective Quality Management Plan (QMP) is essential to involve the MBTA in our Quality Management System (QMS). Our QMP will empower the MBTA to oversee GLX Constructors' performance in design, construction, and commissioning of the Project. It will allow for seamless data handover at the end of the Project, enabling the MBTA to perform cost-effective asset management of the Green Line Extension DB Project.

Quality is of the highest importance and second only to safety. Similar to our approach to safety, we believe that every member of our team, from the top down, is responsible for confirming and delivering quality. Our prior experience developing, implementing, and administering comprehensive and successful quality programs will provide the basis for constructing a quality Project. Our presented data and daily information will prove our compliance with the MBTA's requirements, as well as the design specifications and drawings.

Our QMP will be ISO-9001 compliant, and it will meet the requirements of the U.S. Department of Transportation Quality Assurance (QA)/Quality Control (QC) Guidelines FTA-IT-90-5001-02.1. We will incorporate best practices and lessons learned from our extensive experience, which is derived from some of the United States' most complex infrastructure and rail projects.

GLX Constructors has primary responsibility for the overall QA and QC for the design and construction elements of the Project, including those performed by subcontractors, fabricators, suppliers, vendors, or agents. We will collaborate with the MBTA in developing our final QMP to incorporate the MBTA's quality requirements. This will lead to an optimized, Project-specific QMS that we can all support as a team.

> **"GLX Constructors, including our Design Team and construction subcontractors, entrusts its DB Management Team and personnel to properly implement and document the QMP. We prioritize our responsibility for a quality Project, and we commit that we will document and fully comply with our QMP.**

GLX Constructors' Quality Team is independent from the Construction Team. The Quality Team reports directly to the Project Executive, the Executive Committee, and the MBTA on the same reporting level as the Construction Manager. In this manner, the MBTA has immediate confirmation of quality concerns and approvals, providing confidence in the QMS and a close oversight of our quality performance.

Quality Assurance (QA), part of our QMP, incorporates management capabilities within the QMS that provide confidence our Project will meet or exceed requirements for the final, approved design plans and specifications. Our QMP will also identify the QC operational techniques and activities used to fulfill quality requirements.

We will develop our final QMP in concert with our final Project Management Plan (PMP). The QMP will be compliant with Federal Transit Administration's (FTA) QMS guidelines, and the MBTA's QMS. The QMP is the main document for developing and implementing our QMS. We will organize our QMP around the FTA's 15 essential elements of a QMS:

▸ Management Responsibility	▸ Product Identification and Traceability	▸ Non-conformance
▸ Documented Quality Management System	▸ Process Control	▸ Corrective Action
▸ Design Control	▸ Inspection and Testing	▸ Quality Records
▸ Document Control	▸ Inspection, Measuring, and Test Equipment	▸ Quality Audits
▸ Purchasing	▸ Inspection and Test Status	▸ Training

GV20170258-118.INDD

A matrix of our QMP's document precedence is shown in Figure 3.2-1.

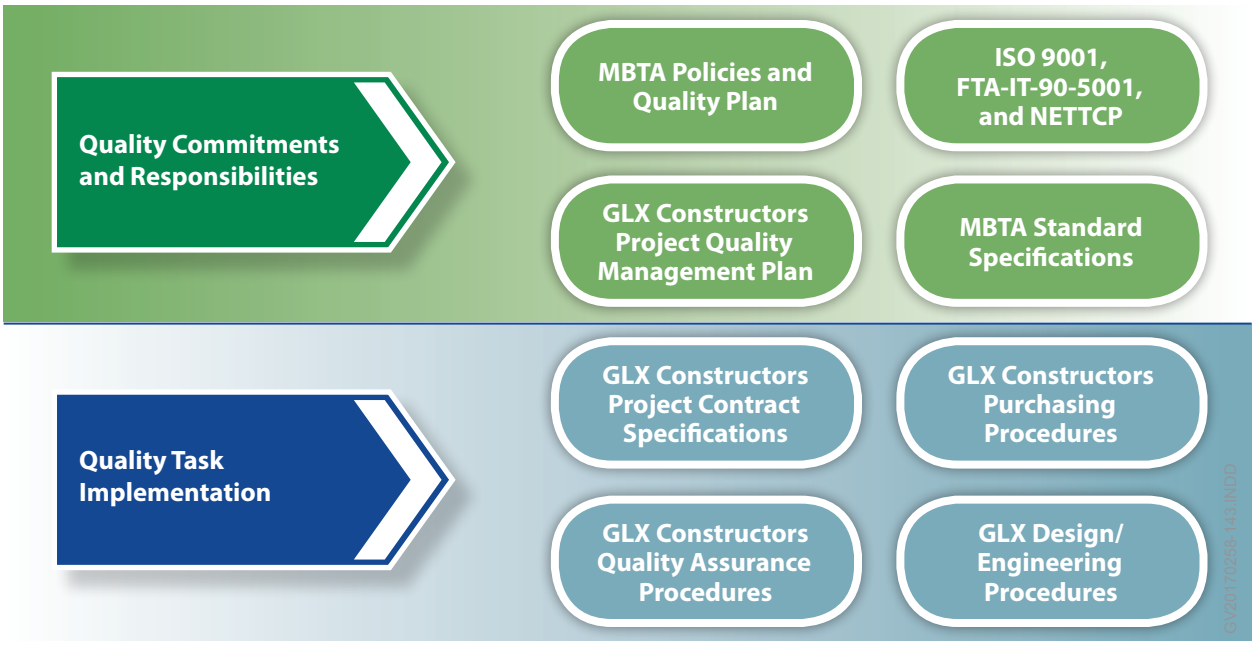


Figure 3.2-1. Our Quality Management Plan Document Precedence. *Establishing documentation precedence organizes the multiple, applicable quality documents.*

3.2.A APPROACH TO QUALITY MANAGEMENT SYSTEM

GLX Constructors will satisfy the requirements of the DB Contract. In doing so, we believe it is important for staff to hold sufficient authority to confront any potential quality complication. As such, our staff will have the autonomy and authority to implement immediate "stop work authority" for recognized, non-compliant issues, and to use simplified solutions to solve any quality-related issue before it is encountered. Our Management Team recognizes that, to be successful, personnel require sufficient authority and organizational freedom to identify a problem and initiate appropriate solutions. GLX Constructors' QC personnel will verify that we have properly designed and installed the compliant solution, and that it meets or exceeds the MBTA's quality requirements.

The Project Executive retains the overall authority for administering the QC system laid out in the QMP. Our Project Manager, John West, is responsible for all aspects of design, construction, and installation. John reports directly to our Project Executive, Clyde Joseph. Concurrently, our Quality Manager, Sandro Plutino, is responsible for implementing the QMP, and he likewise reports to Clyde. An illustration of our Quality Organization is presented in Figure 3.2-2.

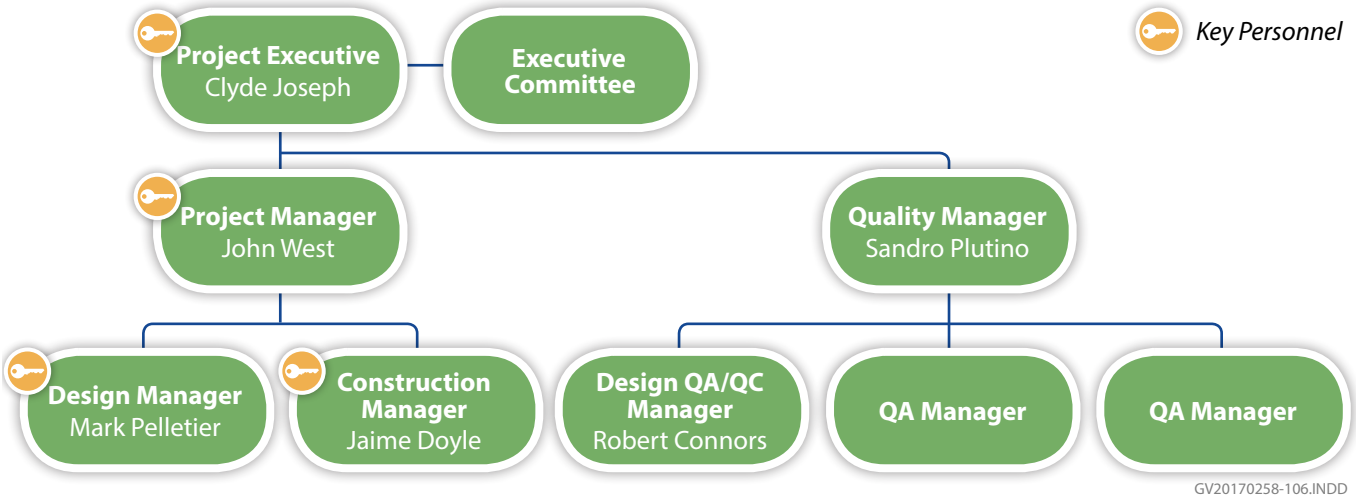


Figure 3.2-2. GLX Constructors' Quality Organization. *GLX Constructors' Quality Team will remain independent from the Design and Construction Teams.*

Figure 3.2-3 indicates the percentage of time dedicated to the Project by the Quality Organization Personnel.

Position	Percentage of Time Dedicated
Quality Manager	100%
Construction Quality Control Manager	100%
Construction Quality Assurance Manager	100%
Construction Quality Control Engineers	100%
Design Quality Manager	100%
Design Quality Control Engineers	100%
Construction Quality Assurance Technicians	50%
Independent Design Quality Control Reviewers	20%
Independent Quality Auditor	20%

Figure 3.2-3. Quality Organization Dedication. *The percentage of time that each personnel listed in the Quality Management Plan will be dedicated to the Green Line Extension DB Project.*

GLX Constructors believes quality, like safety, begins and ends with each individual member of the entire Project Team. Each person is charged with the requirement to produce their work to the highest standard of quality, and to speak up when observing actions that go against our beliefs about quality. When the total quality approach is adhered to, the responsibilities of the Design Quality Control Manager (DQCM) and the Construction Quality Control Manager (CQCM) are simplified to documentation of compliance with the QMP requirements. This allows the Quality Team to be independent from the Operations Team while supporting our common objective – quality across the entire Project.

GV20170258-118.INDD

In the event that quality-related issues cannot be resolved within a typical, organizational manner, the Quality Control Manager will be required to present these issues to the attention of the Project Executive and the MBTA for final resolution.

GLX Constructors' Management Team has established its commitment to quality on the Green Line Extension DB Project through a comprehensive Quality Management Program, including the following guiding principles:

- Communicate the importance of meeting customer, statutory, and regulatory requirements
- Conduct quarterly management reviews
- Provide resources necessary to meet Project requirements including training to the system
- Continually improve our work processes and deliverables through feedback, audits, and checks

The tasks and processes required to meet these commitments will be defined throughout the QMP.

Robert (Bob) Connors will serve as GLX Constructors' Design Quality Assurance and Quality Control Manager. Bob is a Certified Manager of Quality/Organizational Excellence and a Certified Quality Auditor from American Society of Quality. He is also a Certified Quality Assurance Technologist from Northeast Transportation Training and Certification Program. A registered Civil and Structural Engineer in Massachusetts, Bob has served on numerous successful projects for MassDOT and the MBTA, including the Longfellow Bridge Rehabilitation Design Build, Hingham Intermodal Center, Fore River Bridge Replacement Design Build, and the Greenbush Line Rail Restoration Design Build.



Robert (Bob) Connors
Design QA/QC Manager

3.2.B QUALITY POLICIES AND OBJECTIVES

Our Quality Policy is based on the fundamental concept that quality control is a team-obligation to build quality into every aspect of the Project. Our team will provide quality products and services that meet or exceed the MBTA's and FTA's requirements and standards, delivered safely, on time, and within budget. Quality will be the responsibility of every individual performing the work.

"After the first phase of the Longfellow Bridge Rehabilitation DB Project, Bob Connors and his team formed a dedicated team of quality and management personnel to monitor quality trends, perform quality audits, and take action to improve quality. As a result, the number of Non-Conformance Reports was reduced from over 31 significant NCRs with in-place construction in the first phase, to 10 minor NCRs in the final phase, all of which were resolved offsite in fabrication shops prior to on-site arrival.

GLX Constructors' Quality Management System is permeated with the MBTA's vision for the Green Line Extension DB Project, our innovative approach to the work, and the integrity of our Key Personnel to get the job done right the first time.

Quality will be obtained through appropriate planning and control of work operations, as well as specific quality control activities, such as reviewing, checking, inspecting, testing, surveillance, and auditing.

Our QMP will be developed under the following guiding Quality Objectives:

- Implement well-designed quality programs that meet or exceed the MBTA's and the FTA's quality standards, and continually improve our process as the Project progresses.
- Partner with the MBTA to make design, construction, and management processes open to inspection and oversight.
- Effectively communicate our quality program to all relevant Project team members and provide sufficient training for proper implementation.
- Collaborate to incorporate best practices and seek out the MBTA's opinion for quality feedback.
- Base decisions on factual, auditable information, and bring on subcontractors and suppliers who are committed to providing a superior end product.

The above guiding Quality Objectives of our QMP comprise and address the following dimensions[1], which make certain our QMS complies with the Project requirements:

- **Performance.** The Project's main operating or functional characteristics.
- **Conformance.** How the Project will be measured as meeting the contract specification.
- **Reliability.** The mean time or distance between failures.
- **Maintainability.** The mean time to repair.
- **Availability.** The percent of time the system is available for service.
- **Aesthetics.** Appearance, color.
- **Features.** Functionality, beyond the main operating or functional characteristics.
- **Durability.** Ability to adapt to ambient conditions.
- **Safety.** Freedom from hazards.
- **Warranty.** Freedom from defects for a specified period of time.
- **Service Life.** Expected time prior to major overhaul of the system.

A final QMP, including Quality Policies and Quality Objectives, will be developed and detailed based on these objectives at Project Award.

3.2.C GLX CONSTRUCTORS' RECORDS MANAGEMENT PROCEDURES

GLX Constructors' Quality Manager, Sandro Plutino, will review, update, and maintain the QMP based on our discussions during Quality Management

[1] FTA Quality Management System Guidelines, 2012

GV20170258-118.INDD

Meetings. The QMP is a living document, and it is subject to revision as necessary to facilitate and improve the quality process for the Project. We will maintain quality records to provide evidence of conformity with the objectives and requirements of the Document Management Plan and the QMP. Completed forms, including audit forms, and documents will be write protected.

It is a major benefit to the MBTA that our Quality Management Team will utilize a web-based database program, Engineering and Laboratory Vital Information System (ELVIS), provided by Raba Kistner, for the Green Line Extension DB Project. Used on over $14 billion of GLX Constructors' team members' construction projects across the country over the last 13 years, ELVIS efficiently stores and interprets a comprehensive range of documentation. ELVIS is easily customized to fit the needs of individual projects, providing key features for construction engineering and inspection, including, but not limited to:

- Web access grants users anywhere access to project records
- Security controls for the Project
- Contract requirements tracking and verification
- Design submittal tracking and review
- Constructability submittal tracking and review
- Email notifications for critical processes
- RFC Plans entry and viewer by section and/or sheet
- Engineering decision documentation and tracking
- Data input through electronic tablet devices
- Failing tests disposition and tracking
- Approval and tracking of material submittals
- Non-conforming work tracking and resolution
- Integrated quantity tracking of all materials delivered and installed
- Material Management Tools
- Analytical tools for material quality evaluation (control charts/statistical validation)
- Punchlist module for Project closeout
- Numerous search functions for quick retrieval of records
- Transmittal generation
- Logs for incoming and outgoing correspondence

The ability to access ELVIS in the field via a tablet device allows us and the MBTA to access Project plans that incorporate new field design



Inspector entering the Inspection Record into ELVIS on one of our Past Projects, the Dallas Horseshoe DB Project. ELVIS provides web-based access, which improves data collection and access in real time.

changes as they are approved, reducing potential errors caused by using outdated plans.

ELVIS's high functionality and user-friendly interfaces allow for real-time access to Project data, providing unprecedented levels of transparency to construction projects. This facilitates open, quick communication that leads to successful partnering. We will provide the MBTA with access to this system, which will allow the MBTA staff to collaborate in real-time on all aspects of the construction process.

This system will serve as the Electronic Quality Document Management System (EQDMS) for the Project during design and construction, and GLX Constructors will use ELVIS to transmit official correspondence to the MBTA.

ELVIS will maintain current versions of project documents and all controlled Release for Construction (RFC) plans, quality reports, and testing documentation to serve as justifiable evidence confirming established processes are followed and Project requirements met.

GLX Constructors' team members have used ELVIS on the following projects shown in Figure 3.2-4, including, but not limited to:

Project	Agency	Year Complete	Size	Role of ELVIS
SH 130 DB, 1-4, Austin,TX	TxDOT	2007	$1.2 B	Independent Quality Firm (IQF)– Construction
I-15 CORE DB, UT	UDOT	2013	$1.1 B	IQF–Design and Construction
SH 130 DB, 5-6, Austin, TX	TxDOT	2013	$1.2 B	Independent Engineer
Horseshoe DB, Dallas, TX	TxDOT	Ongoing	$800 M	IQF - Construction
Tappan Zee Bridge DB, NY	NYSTA	Ongoing	$3.1 B	Quality Documentation
Bergstrom Expressway DB, TX	CTRMA	Ongoing	$650 M	Developer Quality Control
South Mountain Freeway DB, AZ	ADOT	Ongoing	$900 M	IQF-Construction

Figure 3.2-4. Our Past Experience with ELVIS. *GLX Constructors' team members have experience using ELVIS as their Electronic Quality Document Management System on DB projects of similar size and complexity as the Green Line Extension DB Project.*

In addition to the above, ELVIS is capable of the following:

Design Documents. ELVIS tracks and logs design submittals, design review comment documentation, and RFC drawings. At each stage of design review, ELVIS automatically generates emails to notify identified users when plans or comments are ready for review or response, and tracks response deadlines. Changes to approved RFC designs – notices of design change (NDC) and field design changes (FDC) – are tracked and retained for inclusion in the as-built plan sheets to document the actual improvements

GV20170258-118.INDD

constructed. In addition, the RFC Module grants users in the field access to RFC sets, which incorporate new NDCs or FDCs as they are approved. This module allows the user to view plans as entire sets, specific design sections, or individual sheets in an effort to provide the information needed as quickly as possible.

Project Submittals and Documentation. ELVIS provides platforms to store, track, and easily retrieve project submittals and documentation such as Contract changes and deviations, management plans, certifications, material submittals, meeting minutes, quality reports, audit reports, close-out reports, photos, acceptance testing, utility data, and other official documentation/correspondence as required by the Contract Documents.

Inspection Documentation. Inspectors will log their work in Daily Inspection Reports. These reports track Inspectors' observations, communications with other Project staff, materials placed, samples/tests taken, photos, and any deficiencies identified. Daily Inspection Reports will also track Project Hold Points to properly identify the acceptable completion of work elements that must be completed for subsequent work to proceed.

Non-Conforming Work. ELVIS will track and log the details of non-conforming work through identification, resolution, and closure.

Material Testing and Management. ELVIS maintains comprehensive material testing records, with each test being assigned an individual Lot Identification Number. The testing modules in ELVIS also provide tracking for failing test disposition and resolution, and Engineering Decision documentation, as well as material quantities and Minimum Sampling and Testing Requirements.

Analytical Tools. The Dashboard can be customized to individual users to display data charts specific to their areas of oversight. This allows Project Management to quickly identify trends in work that may adversely affect Project quality, schedule and/or cost.

Punchlist. The punchlist module identifies specific items of work to be completed prior to Project Closeout and tracks each issue through resolution and acceptance.

Project Closeout. The ease with which a user can search for, retrieve, and review project documentation within ELVIS makes Project Closeout a quick and accurate task. The Project Materials held within ELVIS will be delivered in their entirety upon Project Completion. In addition, the data from ELVIS is easily exported to other systems, such as ProjectWise, at any time throughout the duration of the Project.

> **"Analytical Quality Evaluation: We track the number of nonconforming work tests as a percentage of total inspections and tests which provide a trend analysis and will help our team drive improvement.**

Documents Control Plan

GLX Constructors will maintain a standardized system to control, file, and archive all project documents supplemented by the ELVIS system. Procedures will make certain that relevant documents are current and readily available to the MBTA and the users who require them.

A master set of the latest project documents will be managed in a controlled fashion so documents can be stored, retrieved, obsolete documents removed, and document changes controlled. The types of controlled documents include:

- Drawings
- Specifications
- Calculations
- Inspection Procedures and Reports
- Test Procedures and Reports
- Calibration Records
- Work Plans
- Operational Procedures
- Risk and Contingency Plans
- Project Management and Quality Plans
- Safety and Security Management Plans
- Non Conformance Reports
- Corrective Actions
- Quality Audits
- Quality Training Records
- Résumés

We will work collaboratively with the MBTA in developing a document management system. We recommend using ELVIS for Quality document control for the following reasons:

- **Essential and Practical Management Tools for Accelerated Project Delivery.** Accommodates DB and other accelerated project delivery methods' requirements for fast input and quick turn around on changes and quality determinations.
- **Shortens Project Closeout.** Stakeholders can find outstanding items easily throughout the Project without waiting for paperwork to catch up at the end of a project. Results in a significantly shorter punch list at close out as most problems have already been resolved.
- **Transparency and Integrity.** Owners and developer team members have complete, real time access to design, submittals, testing and inspection records thereby building trust in partnering and working together.
- **Risk Management.** Creates a comprehensive, situational picture of the Project that helps decision-makers determine the right choice more quickly against risk metrics.
- **Lessons Learned.** Our experience and continually improved ELVIS presents valuable lessons learned from successful execution of QC/QA/OV/IA roles on infrastructure projects.

GV20170258-118.INDD

- **ISO Compliant.** Compliant with five core ISO procedures and integration with the Quality Management System.
- **Modular Components and Flexibility.** User write protected QC, QA, Independent Assurance, and Owner access of the secured EDMS with a design suite, construction suite, and a whole suite of ASTM, AASTHTO and DOT test methods.
- **Statistical Analysis.** Continuous analysis of t- and F-tests with p-values as shown in Figure 3.2-5.
- **Paperless Reporting and Records Delivery upon Completion.** Searchable database for source and produced documents for quality compliance.
- **Automated Trend Lines.** Trending can help our team identify preventative actions as shown in Figure 3.2-6.
- **Automated Quantity Tracking and Testing Frequency Compliance Extensive Management and Search Tools.** Search engine with comprehensive filters by controlled vocabulary list for individual and summary reports.
- **Automated Monitoring and Tracking of Non- conformances.** Automated initiation and tracking of construction deficiencies and nonconformances with documentation of corrective actions, dispositions, and resolutions of the deficiencies and non-conformances.
- **Email Notifications.** Timely delivery of critical information and required decision request requirements.
- **Ready and On-Line Access.** Released for Construction Plans and Specifications, approved materials and personnel, Construction Quality Management Plan and associated work instructions, procedures, and checklists.

3.2.D QUALITY MANAGER REPORTING AND AUTHORITY

Our Quality Organization will be independent from our Construction Organization. Our Quality Manager, Sandro Plutino, will report directly to Project Executive, Clyde Joseph, and the Executive Committee on the same level as the Project Manager. The Quality Manager will have a simple, informational communication line to the Project Manager. In this manner, Sandro and Quality Organization will provide true verification and confirmation of the constructed system's compliance with the requirements. Sandro will be under the direct authority of the Project Executive, Executive Committee, and – by definition – the MBTA for "stop work authority" as it applies to complying with the project requirements. Our Quality Organization supports, but verifies, the Construction Organization.

Material Category:	Embankment, Borrow and Backfill	Material Property:	In-Place Density
Query Condition 1:	All Grades	Maximum QO Test Number:	14
Query Condition 2:		Query Condition 3:	
Statistical Validation Period:	6/6/2014 - 1/23/2015	Alpha Level:	0.01
QO Test Sample Type(s):	Random-Independent	QA Test Sample Type(s):	Random-Independent and Random-Split

QO Data Point #	14	QO Mean	97.06	QO St. Deviation	2.472
QA Data Point #	1216	QA Mean	95.95	QA St. Deviation	2.071
F Value	1.425	Critical F Value	2.312	Equal Variance?	Yes
T Value	1.991	Critical T Value	2.580	Equal Mean?	Yes

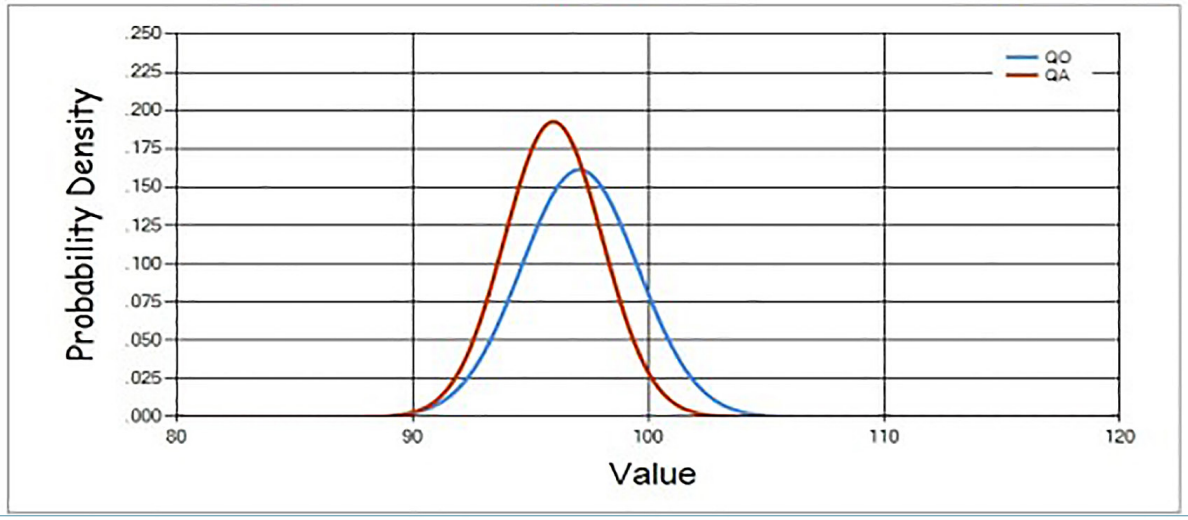


Figure 3.2-5. Statistical Analysis Example. *Using Statistical Analysis will help GLX Constructors identify root cause.*

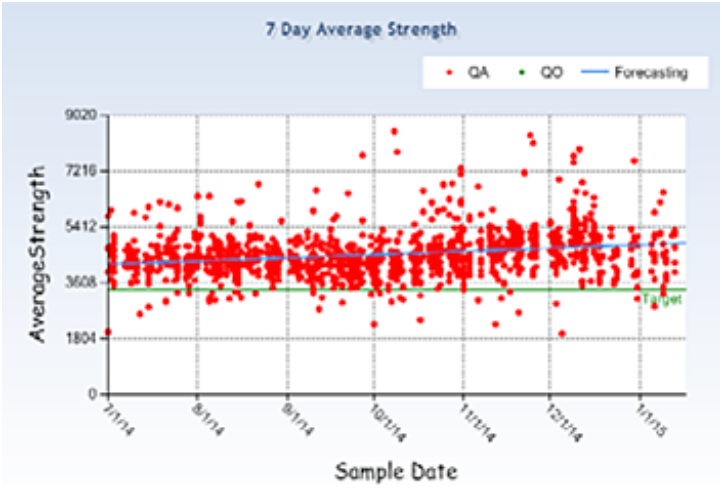


Figure 3.2-6. Automated Trend Lines Example. *Trending can help GLX Constructors identify preventative actions.*

GV20170258-118.INDD

Subcontractors, Suppliers, and Fabricators

Subcontractors, suppliers, and fabricators will be evaluated on their commitment to quality. We believe those performing the work are experts and, therefore, the most appropriate to control quality. Subcontractors, suppliers, and fabricators will provide their quality plans to GLX Constructors for review and approval.

If the subcontractor, supplier, or fabricator plans meet or exceed our QMP, their quality plan will be accepted. If the subcontractors, suppliers, and fabricators quality plans do not meet or exceed our QMP, they will be required to modify for compliance. They may adopt our quality plan as their own. If the subcontractor, supplier, or fabricator elects to adopt our QMP, we will train them accordingly.

While we trust our subcontractors, suppliers, and fabricators, our Quality Manager will verify their compliance with the required quality standards through verification testing and quality auditing.

Interfacing with the MBTA and Third Parties

The Quality Manager will interface with the MBTA and third parties transparently in our reports, decision making, and operations. We follow this approach to foster effective communication and continual improvement, which makes certain the MBTA is provided with a project of the highest quality.

The Quality Manager will provide guidance to the Project Management Team based on the following quality management principles:

- Customer focus
- Leadership
- Involvement of people
- Process approach
- System approach to management
- Continual improvement
- Factual approach to decision making

The Quality Manager will establish and chair weekly meetings to review quality reports, decisions, NCR status, and acceptance status. Additionally, a quarterly meeting will be held to review specific improvements, necessary revisions, or additions to the QMP.

3.2.E NON-CONFORMANCE REVIEW AND DISPOSITION PROCESS

A key component of our QMS and documentation process is the non-conformance module. When non-conformance issues are identified,

they are registered in the ELVIS system, which introduces an intermediate checkpoint that requires resolution prior to continuing the work. This develops the ultimate checks-and-balances for the Construction Phase, and it gives the MBTA authority in accepting the final construction product.

Non-Conformance Tracking System and its Required Components

The Quality Management Plan will identify design documents, materials, products, and construction that do not conform to Project's requirements. Each instance will be documented, evaluated, resolved, and corrective action taken to prevent a recurrence. The non-conforming material, product, or construction will be marked or tagged to prevent its unintended use. The material product or construction will not be used until the non-conformance is resolved. When the non-conformance is corrected, we will perform additional tests or inspections to verify the material, product, or construction is able to be properly used. Staff will be empowered, encouraged, and educated to report non-conformities as soon as they are discovered.

Non-conformities may be identified or discovered in multiple ways. Requests for Information (RFI) are typically questions from the Project site to the Design Team regarding changes to design plans or beneficial changes as a result of the site condition, and NDCs are the Design Team's changes to design documents. Both RFIs and NDCs are carefully implemented through procedures that document the discovery and resolution of non-conformity. In completing the resolution process, all non-conformities are tracked until they are resolved. By properly reviewing the forms, we can assess the reasons for the non-conformities, such as identifying whether the non-conformity is supplier or discipline related.

Quality staff will review data gathered through formal and informal audits, or any of the monitoring procedures discussed above, to assess performance against plans, objectives, and other defined Project Program goals. Through this and other forms of analysis, the Quality Manager, CQAM, and DQAM will seek to determine the root cause of the non-conformity.

The following flow chart, Figure 3.2-7, depicts the steps in identifying, resolving, confirming, and verifying the NCR process. Our process will provide the MBTA with a thorough, transparent procedure with sufficient notifications and check points for resolution.

Corrective and Preventative Response Strategies

When the quality of an item, material, workmanship, or service is unacceptable or indeterminable, we will use the non-conformance review and disposition process to document and resolve the issue. We will use written procedures and isolate non-conforming work so it is not inadvertently used or installed.

GV20170258-118.INDD

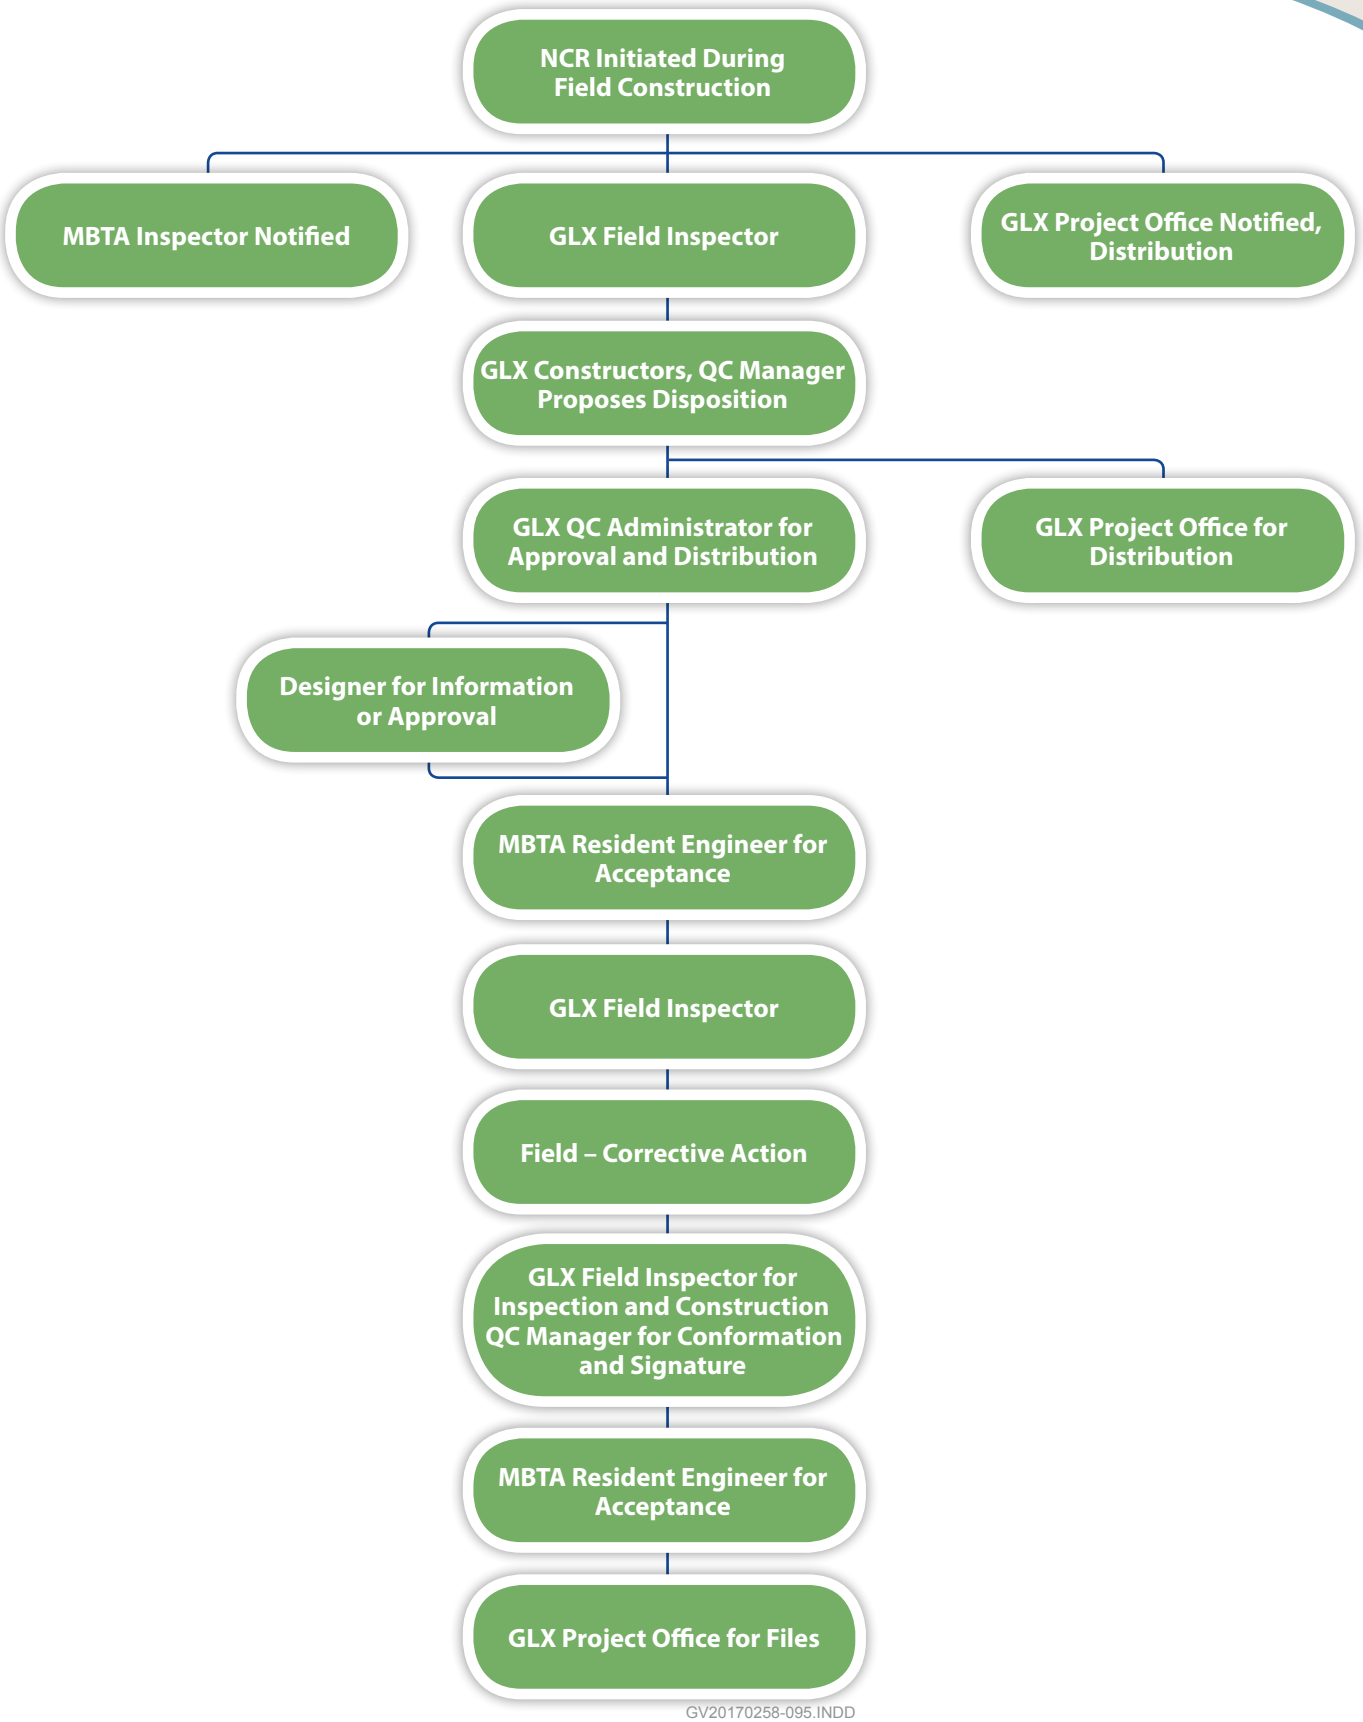


Figure 3.2-7. Non-Conformance Report Process. *Processing through non-conformance reports is a prudent, collaborative process that is carefully documented and approved on multiple organizational levels.*

For design documents, we rely on checking. For construction, we rely on inspection and testing. During checking, inspection, or testing, we gather data for strategic quality planning to find potential non-conformances, or identify trends or issues that may result in a non-conformance. If we identify a trend or issue that may result in a future non-conformance, we will analyze and implement preventative actions to eliminate root causes of possible non-conformities before they arise. The root cause analysis and implementation process is:

1. Identify the problem
2. List possible causes
3. Search out the most likely cause
4. Identify potential solutions
5. Select and implement a solution
6. Follow-up to evaluate the effect
7. Standardize the process to avoid recurrence

Any member of our Quality Team or the MBTA may initiate non-conformances. We will timely notify an MBTA representative if a defect is identified. Once we identify a potential issue, we will determine the cause of that problem. If the cause is not obvious, we will utilize techniques, such as a root cause analysis discussed above, to determine the reason for the non-conformance. We will follow the corrective action procedure.

Appropriate Quality Team members and the MBTA personnel will review and concur with the disposition of the NCR prior to implementing of corrective action. Once the approved corrective action is complete and verified, the NCR will be closed.

3.2.F INTERFACE WITH THE QUALITY MANAGEMENT SYSTEM

The QMS is the common denominator between our key management activities – including project controls, design, construction, rehabilitation, traffic management, environmental management, and project schedule management. The Quality Organization not only confirms our design and construction elements comply with the Project requirements, but they also review and confirm compliance on Project control reporting, Project schedule methodology and reporting, environmental management procedures and reporting, cost and invoicing compilation, traffic management plans and reports, and the rehabilitation of existing structures as required. Specific reports generated for compliance to the contract requirements will include signature approval by the Quality Manager or designee, as well as the Project Manager, prior to transmittal to the MBTA.

Another key feature of our QMS will be the internal and independent auditing of reporting, records, results, and procedures. This is part of our ISO

GV20170258-118.INDD

compliance and corporate commitment to continuous improvement – we define our process, execute our process, then check to confirm that our process and execution yields the expected positive results. Auditors will challenge these results on a random, unscheduled basis. These report results are used to identify potential weak areas of the QMS and prompt revisions as necessary to improve potential gaps.

Our QMS operates on creating an environment of checks, confirming results, identifying and correcting potential weaknesses, thereby continuously improving our quality processes.

We establish the QMS, train our personnel in the procedure and execution of the QMS and audit the results to confirm compliance. In addressing quality, every team member contributes to the Project Execution and each team member is involved in managing and improving the quality of the process for which they are responsible.

3.2.G COMPLYING WITH RELEVANT MANAGEMENT PLANS

The QMP is the primary document for developing and implementing our QMS. We train our workforce accordingly and make the plan available to all Project personnel. Because it is considered a living document, we will revise the QMP as the Project progresses. We will regularly maintain the QMP, at least annually, to make certain relevant processes, products, and services meet the established technical requirements. The QMP will comply with the requisite contract documents, codes, the MBTA's engineering requirements, the FTA's guidelines, and applicable standards. The plan will include processes to make certain the work is documented and verified.

As the Project progresses, training, education, and other resources will be necessary to meet or exceed the MBTA's quality requirements. To continuously improve products and services delivered to MBTA, we will focus on the following to ensure all personnel comply with our QMS:

- Training and Education
- Continual Improvement
- Teamwork and Employee Participation
- Focus on MBTA Satisfaction

Training and Education

We will assign responsibilities to our team members based on their qualifications, including education, skills, abilities, experience, and training. Their qualifications must be evidenced in their resumes. We will maintain resumes, and they will be available for the MBTA's review.

As we proceed through the Project cycle, our team members will need to continually re-educate, develop new skills, and sharpen proven skill sets. To meet this need for continual education and training, we will develop a Quality Training Plan. A training matrix will be developed to determine which team members require training in which procedures. We will maintain a training matrix that summarizes which Project team members attended specific trainings, and it will be available for the MBTA's review.

Our Quality Training Plan process will start with a "needs analysis" to determine the optimum solution to quality training and development. Our Design Quality Manager, Robert Connors, will provide quality training to the design staff, while the Construction Quality Managers will provide quality training to the construction staff. Training will be relevant, and it will focus on the quality plan for design or construction procedures, depending on the staff trained. Training will require sign-in. Project staff will be required to attend quality training, and we will maintain records to document participation.

Quality staff will receive quality training. NETTCP and ASQ will also be utilized to obtain and maintain quality certifications.

Continual Improvement

GLX Constructors will continually improve the effectiveness and efficiency of our activities and processes to provide added benefits to the MBTA, the Project, and the adjacent communities.

The initial procedure for continual improvement will be corrective and preventative actions. Corrective and preventative actions will establish procedures for identifying, documenting, determining cause, correcting, and preventing recurrence of non-conforming work. Corrective and preventative actions include implementing and recording changes in procedures resulting from preventive action, corrective action, and continual improvement initiatives.

A steering committee of senior Project personnel will oversee our continuous improvement. We will target processes that provide strategic Project advantages. Process changes will be based on the MBTA's feedback, needs, and potential impacts. Personnel involved in the process will be able to implement change. Processes will transform inputs to outputs, and decisions will be based on empirical data to the extent possible. Process changes will be evaluated to determine whether the desired impact was achieved.

Teamwork and Employee Participation

A successful QMP must be pervasive throughout any project. Therefore, everyone must participate to the extent that his or her job responsibilities

GV20170258-118.INDD

On UDOT's I-15 CORE Project, a Fluor-led joint venture team developed a comprehensive quality system utilizing two principle quality structures (quality assurance and quality control) with two complementary components for each structure. The program was based on requiring production elements to build quality into their work and providing a quality assurance (QA) function that is 100% independent of production and has the obligation to stop work if it is non-conforming. The production function was responsible for the quality of its work for both design and construction.

At the start of the project, UDOT intended to use a consultant-supplied system. However, after reviewing our QA system, decided to use our system instead. At present, over 6 million quality records are maintained in the system. As evidence of the client's satisfaction, Robert Stewart, PE, I-15 CORE Deputy Project Director for UDOT stated:

". . . [this Fluor-led] team has brought a level of materials expertise to this project that rivals or perhaps exceeds our own. They have a level of sophistication regarding principles of quality that exceeds State highway industry standards. They couple this understanding with deployment hardware and software that has raised the level of quality in both the contractor's organization as well as ours. Their systems have helped us provide more evidence of conformity than any other project with which I've been associated."

allow. This includes members of senior management, functional management, and project management; functional and office staff; and shop and field personnel. In addition, consultants, contractors, and suppliers must adhere to our QMP.

Quality team leaders or quality management will select team members first by determining the needed competence. For us, competence comprises factors such as knowledge, experience, skills, aptitude, and attitude. We will use team-building processes for team members within our quality organization, and where possible, with the MBTA and other stakeholders to facilitate teamwork and participation. While people are our greatest resource, we realize they can also be the Project's greatest risk if not operating as a cohesive team. Quality team leaders and Quality Management will continuously evaluate personnel to confirm that team members are working in support of the overall quality objectives.

Focus on MBTA Satisfaction

Along with day-to-day, open communications with the MBTA and regular meeting discussions surround quality, GLX Constructors proposes to have weekly quality meetings with the MBTA to solicit quality performance feedback.

We will document the MBTA's feedback and respond to it in a timely manner. Areas requiring improvement will require corrective actions to be approved by the MBTA. Performance changes after implementing corrective actions will be tracked and discussed at the next quality performance feedback meeting, or more frequently as required.

We will constantly communicate with the MBTA to understand the issues that are most critical. We will not surprise the MBTA.

GLX Constructors will strongly impress upon our workforce that quality is the responsibility of every person involved with the Green Line Extension DB Project. As such, our QMS will comply with the MBTA's required standards, and it will comprehensively provide for the control and documentation of the Project's design and construction.

Our personnel will be effectively trained on the QMP's requirements, and design and construction works will be constantly monitored, documented, tested, and confirmed in "real time" to safeguard an acceptable and approvable final product.

We are confident in our QMS, which has been used extensively on other major Design Build Projects – on these projects, our QMS has proven to be an excellent tool for providing the Project's Owner with the most quality project achievable.

As stated, we are prepared to use ELVIS as a value differentiator to the benefit of both GLX Constructors and the MBTA.

GV20170258-118.INDD

3.3 SAFETY, SECURITY, AND EMERGENCY MANAGEMENT PLAN

GLX Constructors will assess the Project's requirements and develop a Safety, Security, and Emergency Management Plan. We will provide the MBTA with a fully compliant program that comprises safety, security and emergency elements for protecting both the MBTA's operations workforce and the commuting public during day-to-day public use once the Project is successfully completed. Our Team has the requisite startup, commissioning, testing, and systems certification experience, and we apply our best practices during the Design and Construction Phases for Systems testing and commissioning, facilitating a seamless Project start up and reduced costs along the way.

GLX Constructors believes in safety first. Similar to our workforce Health, Safety, and Environmental (HSE) Plan, detailed in Section 3.2, we will approach the Safety, Security, and Emergency Management Plan requirements with the same goal: to design, build, and commission a transit system that operates with the safety of the MBTA's workforce and the traveling public as the most critical aspect of this Project.

Operational safety begins with developing the Safety, Security, and Emergency Performance Specification at the onset of the Project. This performance specification is the guideline for the formal system design, infrastructure construction, system testing and commissioning, and ultimately, system operations by the MBTA's Operations workforce.

As a team of industry leaders specializing in the self-performance of designing and constructing transit systems, signaling systems, and railroad operations and maintenance, GLX Constructors has a unique ability to draw on people within our organizations who have specialized expertise that is relevant to the Green Line Extension DB Project. To the benefit of the MBTA and the local community in which we work and live, GLX Constructors will make use of the variety of talent from our national

"As a 100 percent dedicated rail contractor, Herzog brings the depth and experience of operating 13 passenger rail systems. Current Operations and Maintenance (O&M) and/or Maintenance of Way contracts include:

- **Altamont Commuter Express**
- **Caltrain**
- **CTRail**
- **Kansas City Streetcar**
- **MetroRail**
- **New Jersey Transit**
- **Oklahoma City Streetcar**
- **New Mexico Rail Runner Express**
- **SunRail**
- **TEXRail**
- **Tren Urbano**
- **Trinity Railway Express**
- **Tri-Rail**



Figure 3.3-1. Rail Line Testing. *GLX Constructors' team members support dynamic envelope testing in Denver, Colorado.*

“A valuable member of GLX Constructors’ joint venture team, Herzog specializes in the operation and maintenance of light rail and commuter rail services. By reviewing the design drawings during Technical Work Groups, Herzog benefits the MBTA by identifying key elements that could be improved, including safe operations, security of the system, emergency ingress and egress, life cycle analysis, and the latest information on new product technology.

and global corporate resources to optimize each significant element of this Project to meet or exceed the MBTA’s needs.

We have extensive experience in integrating systems and providing proper documentation to demonstrate that each Project component has been designed and constructed as required to obtain the necessary safety certification.

In addition, GLX Constructors is able to provide assistance and training to the MBTA’s staff for long-term maintenance and operations, if requested. Our team members routinely provide these services to transit agencies across the country.

Our commitment to the MBTA is to bring our industry-leading expertise, coupled with our design, construction, and safety personnel, to provide the best solution for the Green Line Extension DB Project. Our expertise will provide a safe and secure solution and with our construction-driven execution approach to design and construction. This will produce the most efficient and economical solution.

Rail Activation

After completing the safety and security certification process, described in detail below, rail activation becomes a primary Project objective.

All stakeholders, including the MBTA’s personnel, address rail activation steps – including testing and commissioning – that are required to make the system operational. A Rail Activation Committee, composed of staff from GLX Constructors and the MBTA, will be designated at the Project’s onset. As we successfully move through the Project schedule, Rail Activation Committee meetings will become more frequent. When it is time to test and commission the Project, we will hold daily meetings and discussions amongst key members of the Rail Activation Committee.

In the field, GLX Constructors will take on all necessary testing and commissioning steps to make certain the system is operating as designed for all project elements, including track, traction power/OCS, signals, communications, structures, and facilities. The Rail Activation Committee’s subject matter experts (SME) will be held responsible for verifying that each system element is working as designed. These SMEs will work with appropriate MBTA personnel to incorporate specific, required information elements into critical MBTA documentation, such as standard operating procedures, rulebooks, special orders, maintenance manuals, dispatchers’ manuals, and asset management databases. The Rail Activation Committee must coordinate effectively with the MBTA’s Light Rail Operations and Operations Control Center staff. It is critical that the Project operates safely during diversions in service, simulated operations, drills, and construction coordination.

GV20170258-118.INDD

GLX Constructors' team members, Fluor, Balfour Beatty, and Herzog have prior experience in activating rail on design-build-operate projects throughout the United States. In addition, our Lead Designer, STV, comprises key personnel who have directly overseen light rail operations and safety for the MBTA. These GLX Constructors personnel have actively engaged in past MBTA light rail projects, such as the Riverside Line Reconstruction, the Lechmere Viaduct and Science Park Renovations, and the North Station Turnback Resting, Commissioning, and Revenue Service start-up.

Our team members have experience in complying with the Federal Transit Administration's Oversight Procedure 54 – Readiness for Service. This document details the FTA's process for evaluating the Project Owner's readiness for revenue service. It provides the detail and documentation necessary to verify that, among other critical elements, the system integration, equipment, systems, safety and security certifications, and pre-revenue operations are in accordance with FTA and owner requirements, and that the Project Owner has the management capacity and capability to safely operate the service.

"Our Project Manager, John West, oversaw transit systems safety and security certifications on both the West Rail Line and the Silicon Valley Berryessa Light Rail Extension DB Project.

3.3.A MANAGING SAFETY AND SYSTEMS ASSURANCE

GLX Constructors will implement a robust Safety, Security, and Emergency Management Plan early on in the Project. Our strategy will be to develop a plan that is in accordance with the MBTA's System Safety Program Plan (SSPP) and the FTA's guidance, rules, and regulations, such as the State Safety Oversight of Rail Fixed Guideway System. Outlined in Figure 3.3-2, GLX Constructors will develop our own Safety, Security, and Emergency Management Plan that is specific to the scope of the Green Line Extension DB Project.

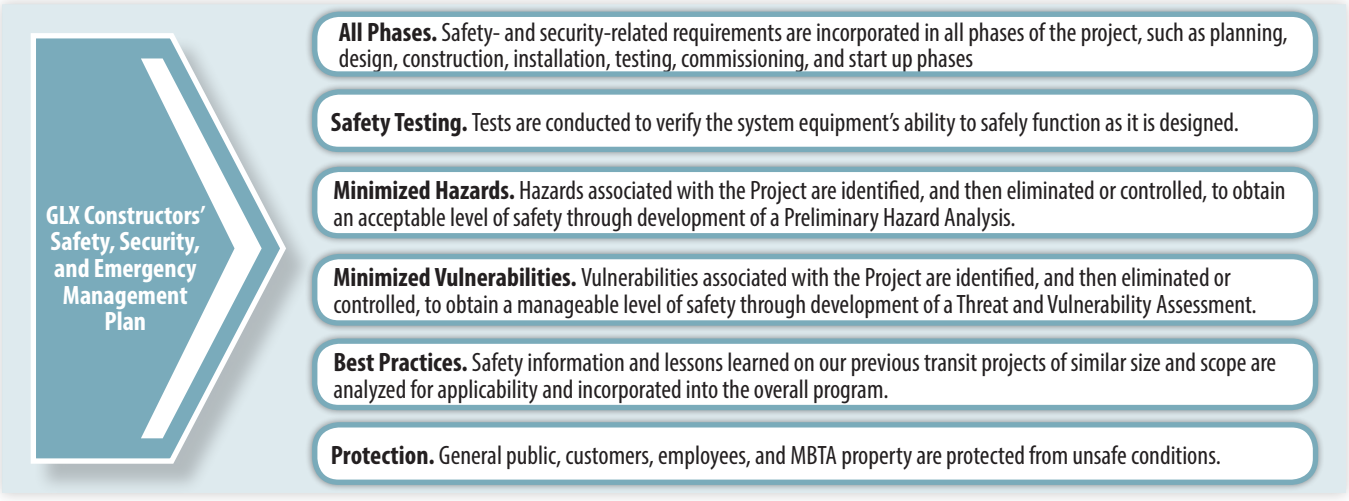


Figure 3.3-2. GLX Constructors' Safety, Security, and Emergency Management Plan. *Our Safety, Security, and Emergency Management Plan will comply with the MBTA's contractual requirements and comprise elements that are critical for operational safety.*

The system safety and security disciplines manage hazards and vulnerabilities throughout the Project's life cycle through a committed approach to risk management. In this context:

- Hazard is a condition or circumstance that could lead to an unplanned or undesired event.
- Vulnerability is a characteristic of the system that increases the probability of occurrence of a security incident.
- Risk is an expression of the impact of an undesired event or security incident in terms of severity and likelihood.

Safety and System Security Certifications is a process to verify the proper application of system safety and security on the project. Through this process, hazards and vulnerabilities are translated into risks, which are then analyzed, assessed, prioritized, and resolved, accepted, or tracked. This process considers safety and security objectives during all phases of the Project Management process.

"GLX Constructors will design, construct, and certify the Green Line Extension DB Project in compliance with both the MBTA's requirements, as well as those of the applicable federal regulatory entities.

GLX Constructors will have a formal kickoff meeting and Project Management Meetings to establish the Project's requirements and review expectations. Our Team will work together to establish relationships and deliver the MBTA with skilled Project Staff that has experience with Safety and Systems Assurance Management on transit projects, both complex and simple. GLX Constructors has the experience to administer the Project's requirements and the FTA's requirements. We have successfully managed the systems and safety certification programs for many freight, commuter, and Light Rail Transit projects throughout the United States and Canada.

We have appointed Jean Claude Aurel as our System Safety and Certification Manager (SSCM) for the Project. Jean will have overall responsibility for leading the Safety, Security, and Emergency Management process to include Systems Assurance and Safety Certification activities. The SSCM will work with other Project personnel, including the Design



Our System Safety and Certification Manager, Jean Claude Aurel, is a Certified Safety Professional and system security expert with 20 years of diverse engineering and safety/security management experience, including threat and vulnerability assessments, gap analyses, hazard analyses, workforce training, and System Safety and Security Certification implementation. He has provided design review and project management on several streetcar, light rail, commuter rail, heavy rail and high-speed rail projects, as well as bus and ferry projects. His experience includes numerous design-build, design-bid-build, and design-build-operate-maintain mass transit projects. Jean is an experienced accident investigator, auditor, and manager of safety and security operations for bus and rail systems. He is proficient in Federal Transit Administration (FTA) SMS approaches, NIOSH standards, ADA regulations, NFPA codes, OSHA 29 CFR 1910/1926 standards, and ANSI standards. Jean will manage a team of experienced interdisciplinary project engineers to administer the MBTA's Green Line Extension DB Project's Safety and Security Certification Plan.

GV20170258-118.INDD

and Construction Teams, to develop the Technical Safety Report, the Technical Security Report, and the overall Safety, Security, and Emergency Management System. These items will ensure our compliance with the Project requirements, and they will confirm the availability of the required information and documentation that verifies the safety and security elements have been properly incorporated into the Project.

As an extension of our Technical Work Groups program, GLX Constructors will work with the MBTA to coordinate a Project System Safety and Security Certification Working Group (SCWG). The SCWG be established at the beginning of the Project, and it will:

- Comprise the MBTA's Safety officials, GLX Constructors' SSCM, GLX Constructors' Systems Leads, and other Subject Matter Experts (SME) as needed.
- Be tasked with reviewing and overseeing any plans and processes related to system safety certification, including hazard and vulnerability management.
- Meet on a regular basis to review the Project's progress to date.
- Ultimately be responsible for reviewing and approving the conformance checklists that validate the safety and system security certification effort.
- Develop meeting minutes to document the SCWG's efforts and become part of the project document control system.

The Safety and Security Certification (SSC) process, illustrated in Figure 3.3-3 will verify conformance to the Project design criteria, specifications, and test plans, as well as document operational readiness. It demonstrates the flow of information for each project phase. This process includes procedures for developing checklists that verify the Project is designed, constructed, and tested and cutover in compliance with the approved project documents.

GLX Constructors will assist with, or develop, the charter to establish a Fire Life Safety Committee (FLSC), and we will actively participate in the FLSC throughout the Project. The intent of the FLSC is to review standards and safety- and security-related designs and tests to verify fire life safety code and regulation compliance. Past experience on large transit projects have proven that the early formation of the FLSC is critical to minimize adverse schedule impacts resulting from differences of opinion on code interpretations late in the project delivery life cycle. Meeting minutes will be kept and become part of the Project Document Control System.

At Project completion, GLX Constructors will prepare and issue a Safety and Security Certification Verification Report (SSCVR) for the Project. The SSCVR will include a summary of all system safety and security activities

> **"A system Safety and Security Certification (SSC) addresses conditions that could result in harm – whether unintentional (safety) or intentional (security). Our SSC process collectively verifies the Green Line's safety and security readiness for public use.**

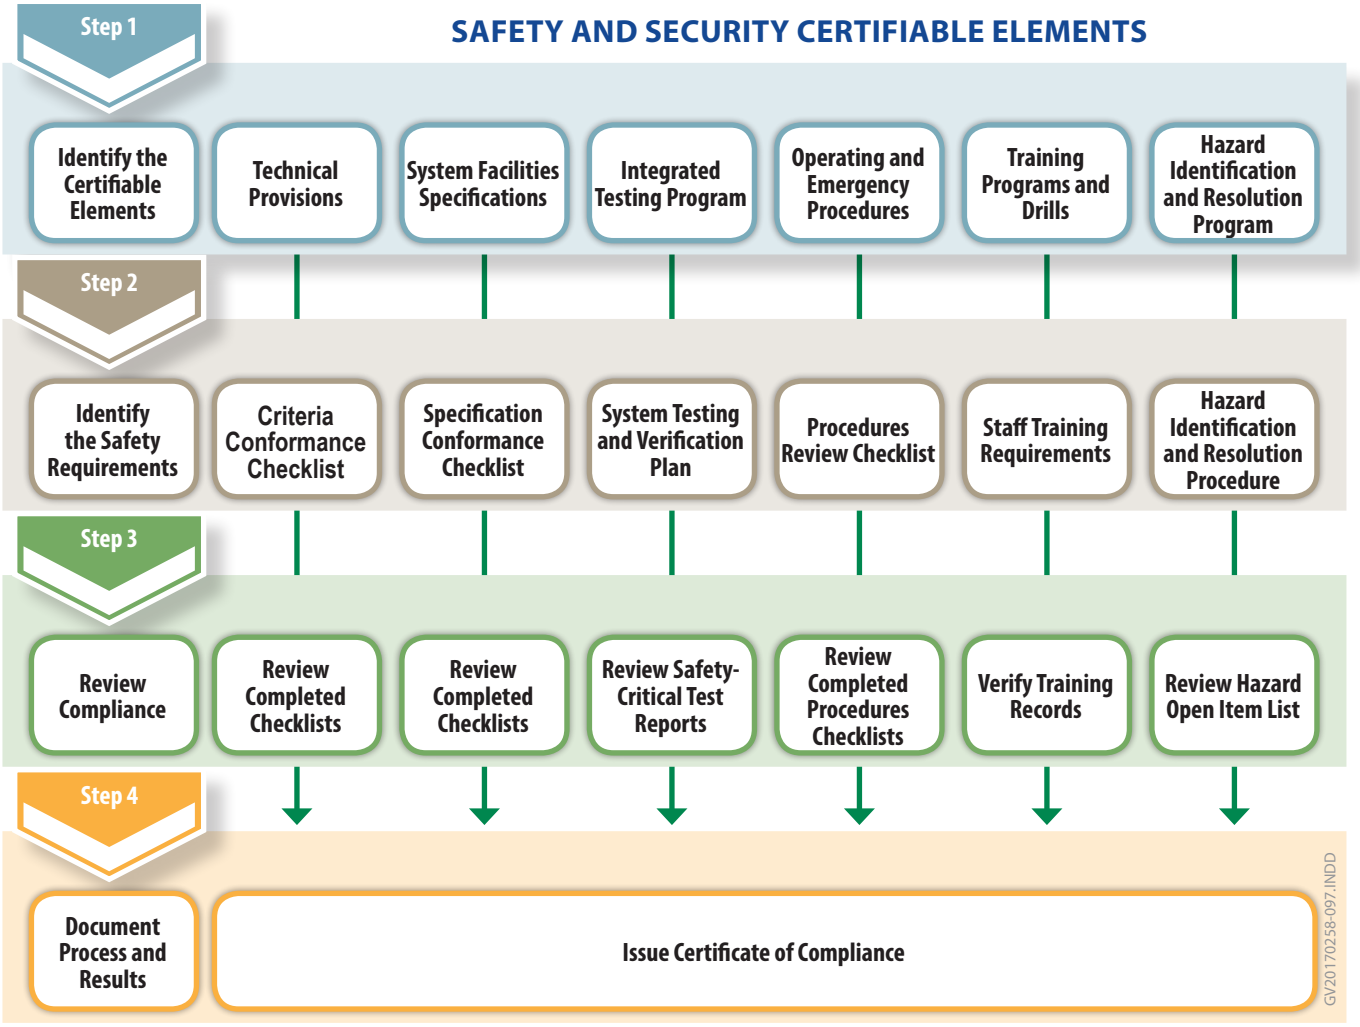


Figure 3.3-3. Safety and Security Certification Process. *This process provides checks-and-balances for conformance to important Project requirements as stipulated by the MBTA, resulting in a Certificate of Compliance.*

that occurred during the Project life cycle to include hazard analysis, conformance verification, and copies of the various project safety and security certificates that have been issued. The SSCVR will also include reference numbers to the various safety and security certificate submittals for the Project. The SSCVR will be the final safety and security certificate deliverable from GLX Constructors.

3.3.B METHODOLOGY TO EVALUATE AND DEVELOP SYSTEM ASSURANCE REQUIREMENTS

System assurance is a vital part of the design effort. The purpose for developing an effective system assurance program is to provide an explicit and direct influence on system design, construction, installation, and testing. GLX Constructors will develop a Systems Assurance Program Plan to provide a system that incorporates a high level of reliability, maintainability, and safety to meet or exceed Project requirements.

GV20170258-118.INDD

Our methodology to evaluate and develop system assurance requirements will include:

- Analyzing relevant operations data from the MBTA and other systems to interpret system availability goals into subsystem requirements while identifying areas of concern.
- Analyzing relevant maintenance data from the MBTA and other systems to establish subsystem maintainability goals and coordinate scheduled maintenance.
- Developing system models to allocate service reliability and restoration time requirements, and to establish subsystem requirements for high system availability.
- Establishing reliability and maintainability subsystem targets.
- Placing system assurance reliability and maintainability (RAM) requirements into subsystem specifications, including program, numerical, submittal, and demonstration requirements.
- Deriving subsystem RAM requirements from the RAM models and the specific RAM requirements contained in the Project baseline specifications.
- Requiring major suppliers, such as signaling, to provide a formal acknowledgment of the GLX Constructors System Assurance Program Plan.
- Analyzing system redundancy and fault recovery.
- Reviewing and compiling system assurance data received from suppliers to maximize high probability of each subsystem passing both the reliability demonstration and the maintainability demonstration.
- Developing a preventive maintenance plan based on subsystem supplier data and operating company requirements.
- Developing subsystem reliability and maintainability demonstration plans in accordance with the Technical Provisions.
- Issuing availability, reliability, and maintainability reports, as required by the Project baseline specifications coordination, and support for the system level reliability and availability demonstrations.

Hazards, Threats, and Vulnerabilities Management

GLX Constructors will develop a Preliminary Hazard Analysis (PHA) during the early phases of design development that may provide input to be used in the refinement of the Certified Elements List (CEL) and Certified Items List (CIL), safety and security design criteria, and overall project design. The items identified during the PHA will be included in the hazard resolution process during final design.

As the Project progresses through design and construction to startup, GLX Constructors will perform reviews to confirm that any potential change orders or MBTA approved deviations from the design criteria will not degrade the safety and security of the System.

GLX Constructors will maintain and update a hazards, threats, and vulnerabilities tracking log, complete with potential mitigation and resolution strategies. As threats and hazards are identified throughout the Design and Construction Phases of the Project, such as during analysis, design reviews, testing, and inspections, all potent threats and hazards will be recorded in the log.

All identified hazards or vulnerabilities will be tracked to resolution by the SSCM and the SCWG. As each threat and hazard is eliminated or mitigated to an acceptable level, the hazard tracking log will be updated with a description of the measures taken to resolve or mitigate the threat or hazard. This log will also be passed on to the Construction Team for use throughout the Construction Phase. The effectiveness of the mitigation will be reviewed by the SCWG to determine that no new threats or hazards have been introduced.

If necessary, GLX Constructors will schedule and chair PHA review meetings to allow for open discussions regarding agency reviews and to approve proposed resolutions or mitigations for any major security or safety issues and physical conditions resulting from a hazard analysis. Once the Project is under construction, all PHAs that have not been fully addressed or resolved through the design process will be converted to an Operating Hazard Analysis (OHA). In most cases, OHA resolutions are addressed through established operating rules and procedures.

We will also conduct or update an existing Threat and Vulnerability Assessment (TVA) to consider the likelihood of criminal or terrorism-related threats that could endanger the transit system. The ultimate objective of the TVA is to influence and provide support documentation to develop the Project security design criteria. We will use the process recommended by the FTA as outlined in ***The Public Transportation System Security and Emergency Preparedness Planning Guide***, final report, dated January 2003.

Knowing the critical nature of any potential security issue related to the operational components of the Project, we will adhere to the MBTA's Sensitive Security Information policy, and we will include the appropriate verbiage on any document that contains such information.

Safety and security threats and hazards will be mitigated to an acceptable level by agreed-upon changes in the proposed design solution, in coordination with the MBTA and other jurisdictional entities, before the SSC process is complete.

When addressing a problem of non-conformance with a given requirement, GLX Constructors will employ reliability, maintainability, and safety principles to determine appropriate corrective action. For instance, we understand that while separate reliability and maintainability actions could each solve a problem, the preferred action might impact safety. In such situations, we will make certain that the problem cannot be considered "solved" if only reliability or maintainability, but not safety, is addressed.

3.3.C SAFETY, SECURITY, AND EMERGENCY MANAGEMENT ANALYSIS

Safety and Security Certification Plan

We will develop a Project-specific Safety and Security Certification Plan (SSCP) that aligns with the MBTA's SSCP, as well as the process identified in FTA requirements under Code of Federal Regulations (CFR) 49 CFR Part 633 "Project Management Oversight"; Part 659 "Rail Fixed Guideway Systems and State Safety Oversight"; and "FTA Project and Construction Management Guidelines," which identifies FTA Circular 5800.1 "Safety and Security Management Guidance for Major Capital Projects."

At a minimum, our SSCP will include these seven sections:

- Section 1: Introduction
- Section 2: Program Management, Organization & Responsibilities
- Section 3: Safety and Security Verification Process
- Section 4: Hazard and Vulnerability Management
- Section 5: Certificates of Conformance
- Section 6: Documentation
- Section 7: Reporting Requirements

In developing the SSCP, our SSCM, Jean Claude Aurel, will identify processes to make certain the following safety and security requirements have been addressed:

- Systems and equipment are designed, constructed, installed, inspected, and tested in accordance with applicable codes, standards, criteria, and specifications with respect to safety and security.
- Identified hazards, threats, and vulnerabilities are eliminated or controlled to acceptable levels.
- Appropriate safety and security verification documentation is provided.

Safety and Security Certification Tasks	Development	Preliminary Design	Final Design	Construction	Integrated Testing	Pre-Revenue	Operations
Develop safety and security policy							
Assign SSC responsibilities							
Establish safety and security committees							
Identify existing safety and security requirements for acquisition process							
Develop SSCP							
Identify safety and security certifiable elements and items							
Initiate SSC project documentation system							
Perform preliminary hazard and vulnerability analysis							
Prepare and update safety and security design criteria							
Integrate O&M requirements into design							
Perform safety and security design reviews							
Develop design criteria conformance checklists							
Perform additional hazard and vulnerability resolution and tracking							
Verify design criteria conformance checklists							
Identify safety and security requirements for test program plans, integrated testing, and operational readiness							
Develop specification conformance checklists (construction)							
Verify specification conformance checklists							
Issue permits and certificate (if applicable)							
Verify completion of integrated testing							
Safety and security review of engineering change orders and waivers							
Complete O&M plans, procedures, and training							
Complete operational readiness review							
Issue final safety and security certification							
Issue final safety and security certification verification report							

GV20170258-098.INDD

Figure 3.3-4. Safety and Security Certification Tasks. *GLX Constructors will implement our best practices to eliminate, minimize, or control potential hazards or vulnerabilities to passengers, staff, property, and the general public.*

As shown in Figure 3.3-4, we will implement best practices based on our past engineering, construction, and operations experience. Each of these requirements will eliminate, minimize, or control potential hazards or vulnerabilities to passengers, staff, property, and the general public. Mitigation techniques will utilize available design, engineering, and procedural measures throughout the term.

GV20170258-118.INDD

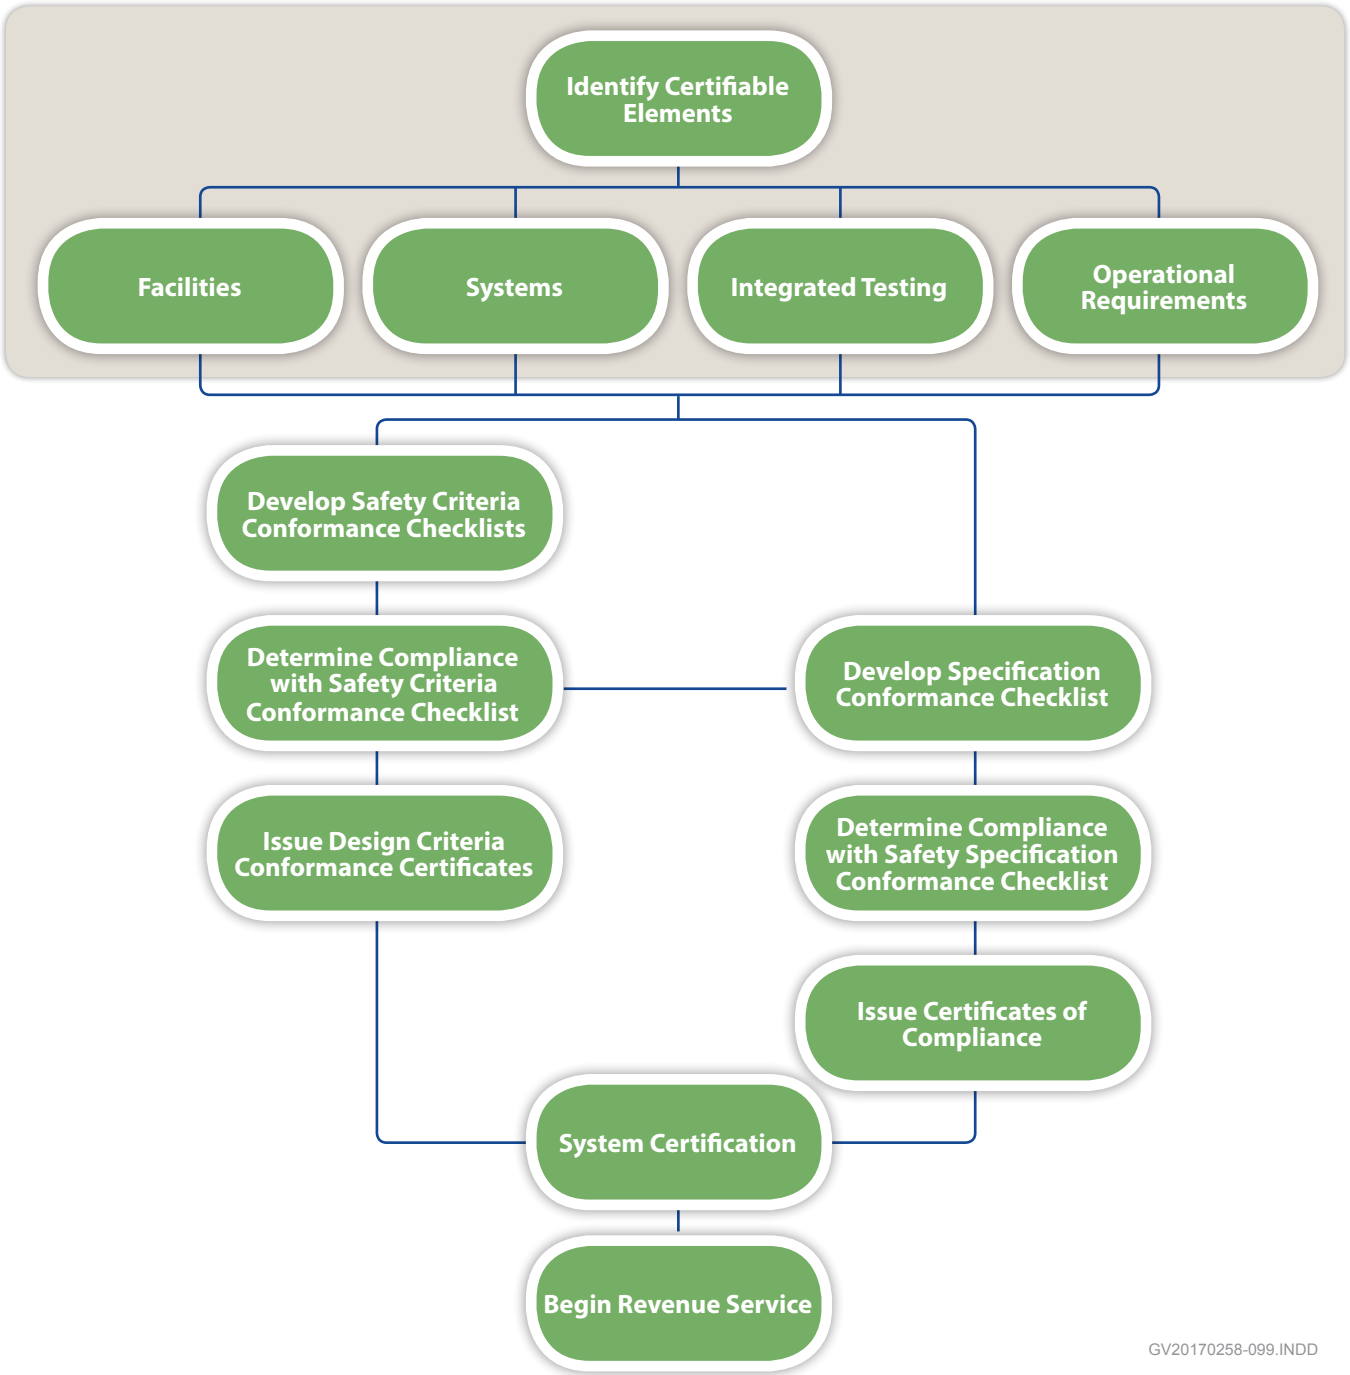


Figure 3.3-5. Safety Certification Verification Overview. *Our safety-driven process for Safety Certification approval, which is necessary to begin revenue service.*

GLX Constructors' first step in the Safety and Security Certification process is to develop the Certifiable Elements List (CEL). As shown in Figure 3.3-5, the CEL will identify the elemental-level components that should be certified. From the CEL, the Certifiable Items List (CIL) will be developed, and it will identify all components and systems to be certified within the scope of the proposed deliverables of each of the items for the Project. The CIL may be reviewed and updated throughout the Project's life cycle as needs are identified.

To validate the CIL, the SSCM will develop conformance checklists for design, construction, and testing. These checklists will be based on the approved Project design criteria, specifications, and test plans. Checklist completion for Design and Construction will be performed in conjunction with the Design and Construction Managers to make certain all identified safety or security requirements have been addressed. All checklist requirements will be tracked in an electronic database that will be provided to the MBTA at agreed-upon intervals for review and additional verification. The database will allow for all references to be maintained in one secure location, and it will provide for the easy viewing of items.

GLX Constructors will store safety verification documents within our Electronic Quality Document Management System (EQDMS), ELVIS, for the Project's life cycle. All of the items identified as part of the checklist requirements and hazard analysis will be tracked in a searchable spreadsheet. Updates to these documents will be submitted as outlined in the contract documents.

Any temporary non-conformances or deviations identified that are related to a certifiable element's safety or security requirements will be subject to a restriction report. GLX Constructors will track restrictions and approved remediation or correction measures until the non-conformance is resolved.

As mentioned in Section 3.3.A, a Safety and Security Certification Verification Report (SSCVR) will be completed at the end of the project. The SSCVR will be the final safety and security document, and it will include the status of safety and security certifiable elements lists; system testing activities; operation, maintenance, and training activities; and hazard identification and resolution.

Integration

The objectives of Integration Testing are:

- To demonstrate that traction power, communications, train control, civil design, and rail vehicles, when operating as a whole, satisfy the functional and performance requirements of the design, scope, services, and contractual obligations.
- Provide for documentation of successful integration testing to the MBTA for their final review and acceptance or work and initiation into revenue service operations.
- To provide documentation of integration testing as evidence for completion of the Project Safety & Security Certification process.

GV20170258-118.INDD

GLX Constructors' SSCM, Jean Claude Aurel, will actively work with our Systems Integration Manager, Aaron Neeley, to make certain all critical safety and security components of testing are fully integrated into this process and all test reports and documents conform to the Technical Provisions. We will capture conformance by using a checklist, which will be developed by GLX Constructors' SSCM and reviewed by the SCWG. The basis of this conformance checklist will come from the Project-approved Systems Integration Plan. Full details on the overall conformance process will be included in our SSCP.

Post-Construction Pre-Revenue Certification

As shown in Figure 3.3-6, the certification process will be an ongoing, ever-evolving process that culminates during the post-Construction Phase of the Project. The proposed process will follow the FTA guidelines and involve conformance verification to design, construction, testing, and operational readiness.

Our SSCP will progressively move through the Project life cycle and close items from the CIL as the documentation is formalized. This rolling process reduces the need for last-minute review or documentation issues post-construction, and it allows for the SCWG to review items throughout the Project life cycle. This proposed process flows with the Project Schedule, and it also creates fewer issues at the end of the Project with a seamless transition from the DB Phases into the final Testing, Commissioning, and Operating Phases.

At the completion of each phase, we will issue a Certificate of Conformance (COC) shown in Figure 3.3-7, which documents that the safety and security requirements have been satisfied for a particular element. Multiple COCs will be issued throughout the project life cycle and they will roll into the overall Project Safety and Security Certificate.

3.3.D TRAINING, EDUCATION, AND OTHER MEASURES

Our safety program will be inspired by, and similar to, the plans employed on our other successful safety projects throughout the United States. Our safety program for this project will be updated, tailored, and it will meet the full requirements of this Project.

Our SSCM and members of his staff will provide GLX Constructors' personnel and the MBTA's staff with in-depth safety training on work practices and compliance with the Safety, Security, and Emergency Management Plan. Training will consist of classroom and field sessions, which will holistically make certain the Safety, Security, and Emergency Management Plan is clearly communicated and well-understood by all personnel.


Massachusetts Bay Transportation Authority (MBTA)

Safety Certification Program

Project Safety and Security Certificate

Completion of this Certificate indicates that the safety and security requirements for all identified Certifiable Elements noted below have been successfully completed or temporarily mitigated (based on noted exceptions)

Certifiable Element: ☐ Stations ☐ Guideway ☐ Track ☐ Communications ☐ Traction Power ☐ Train Control

Exceptions:

Prepared by:	Approved by:	Reviewed and Accepted:
GLX Constructors SSM	GLX Constructors Project Manager	SCWG Chair

Figure 3.3-6. Example Project Safety and Security Certificate. *The Project Safety and Security Certification verifies the proper application of system safety and security disciplines on the Project.*


Massachusetts Bay Transportation Authority (MBTA)

Safety Certification Program

Certificate of Conformance

Completion of this Certificate indicates that the safety and security requirements for the Certifiable Element noted below have been successfully completed or temporarily mitigated (based on noted exceptions)

Certifiable Element: ☐ Stations ☐ Guideway ☐ Track ☐ Communications ☐ Traction Power ☐ Train Control

Phase: ☐ Design ☐ Construction

Exceptions:

Prepared by:	Approved by:	Reviewed and Accepted:
GLX Constructors SSM	GLX Constructors Design Manager	SCWG Chair

Figure 3.3-7. Example Certificate of Conformance. *The Certificate of Conformance documents our compliance to the Project's safety and security requirements.*

On the Eagle P3 Commuter Rail Line Project in Colorado – delivered by Fluor and Balfour Beatty, and with PMO services provided by STV – the Safety Team implemented track allocation and rail alignment safety training programs prior to system energization to protect our workers. Any work performed on or adjacent to the tracks required safety certification and permission. More than 2,000 construction personnel were trained.

Our Project personnel will be up-to-date with the applicable requirements as well as those of the FTA.

Safety, Security, and Emergency Management are paramount to reducing risk to the MBTA, its systems, and the riders it will serve. The goal of Safety, Security and Emergency Management is to address conditions that could result in harm, and it promotes informed management decision-making processes into Project design, construction, testing, and into revenue service. GLX Constructors' Safety, Security, and Emergency Management Plan plays a critical role into our culture of safety, quality, and teamwork that positions GLX Constructors for a successful Project execution and a long-term partnership with the MBTA.

GV20170258-118.INDD

3.4 RISK MANAGEMENT APPROACH

Supporting the MBTA's Project goals surrounding cost and schedule certainty, GLX Constructors offers the MBTA a team that will minimize and manage any risk that may threaten Project success. Our experienced team will identify, assess, monitor, mitigate, and allocate Project-specific risks during each Project phase and activity. As a result, the MBTA can rest assured that we will live up to our goal of "no surprises" for the MBTA, maintaining cost and schedule certainty from Design through the Construction and Commissioning Phases of the Green Line Extension DB Project.

"GLX Constructors' due diligence provides the MBTA with a high-level of confidence that potential risks and corresponding impacts have been mitigated in our Project design and construction. Our goal to identify and mitigate shared Project risks will be met – and the Project will be constructed on time and under budget.

Since the beginning of the Proposal Phase, our DB Management Team and critical risk personnel have focused on identifying, analyzing, and developing mitigation strategies for potential Project risks. For the past year, many individuals who will collaborate on a day-to-day basis with the MBTA – including Project Executive, Clyde Joseph; Project Manager, John West; Construction Manager, Jamie Doyle; and Design Manager, Mark Pelletier – have been fully dedicated to this project while preparing our design, schedule, estimate, and proposal. These four critical team members have collaborated with appropriate third parties and our Design Team to lead our Project Team's effort to fully understand the Green Line Extension DB Project risks. We have already begun the process to mitigate these risks.

Identifying, appropriately managing, and mitigating potential risk is essential to the on-time completion of the Green Line Extension DB Project. Through our extensive experience in DB project delivery, GLX Constructors has defined a systematic approach to implementing policies and procedures that enable us to effectively identify risks, appropriately manage those risks, and put the necessary controls in place to mitigate any potential risks from impacting the Project.

Utilizing the MBTA's knowledge, our team members have the collective and specific expertise necessary to develop a robust Risk Management Team, and we are prepared to evaluate and manage unknown risks before cost- or schedule-related issues manifest. We will convene our Risk Management Team at Project startup, and this team will develop regularly-scheduled evaluation and management meetings to be held until Project Closeout.

GLX Constructors' approach to risk management is a transparent process that minimizes and eliminates unanticipated surprises for all stakeholders. Our monthly Risk Review Meetings – attended by GLX Constructors and MBTA senior management – will make certain the MBTA is actively involved in the risk management process throughout the Project's life cycle, provide a forum for jointly discussing risks and potential mitigations, and raise awareness of potential risks to the appropriate management staff in a timely manner.

GLX Constructors partners with our clients to identify ways to manage unexpected events and Project risks to achieve cost and schedule certainty.

In asking the simple question, "What can go wrong?" and thinking through the likelihood, impact, and ways to reduce the risk, through up-front and contingency planning, the power of risk management becomes readily apparent.

We will minimize and manage risks that may threaten Project success, through identification assessment, monitoring, mitigation, and allocation of Project-specific risks during each project activity. Figure 3.4-1 illustrates our Risk Management Process.

GLX Constructors has established a Risk Management Plan (RMP) designed to minimize and manage risk. This plan is a Project-specific implementation of Fluor's proprietary Business Risk Management Framework℠ (BRMF), tailored specifically to the Green Line Extension DB Project's needs.

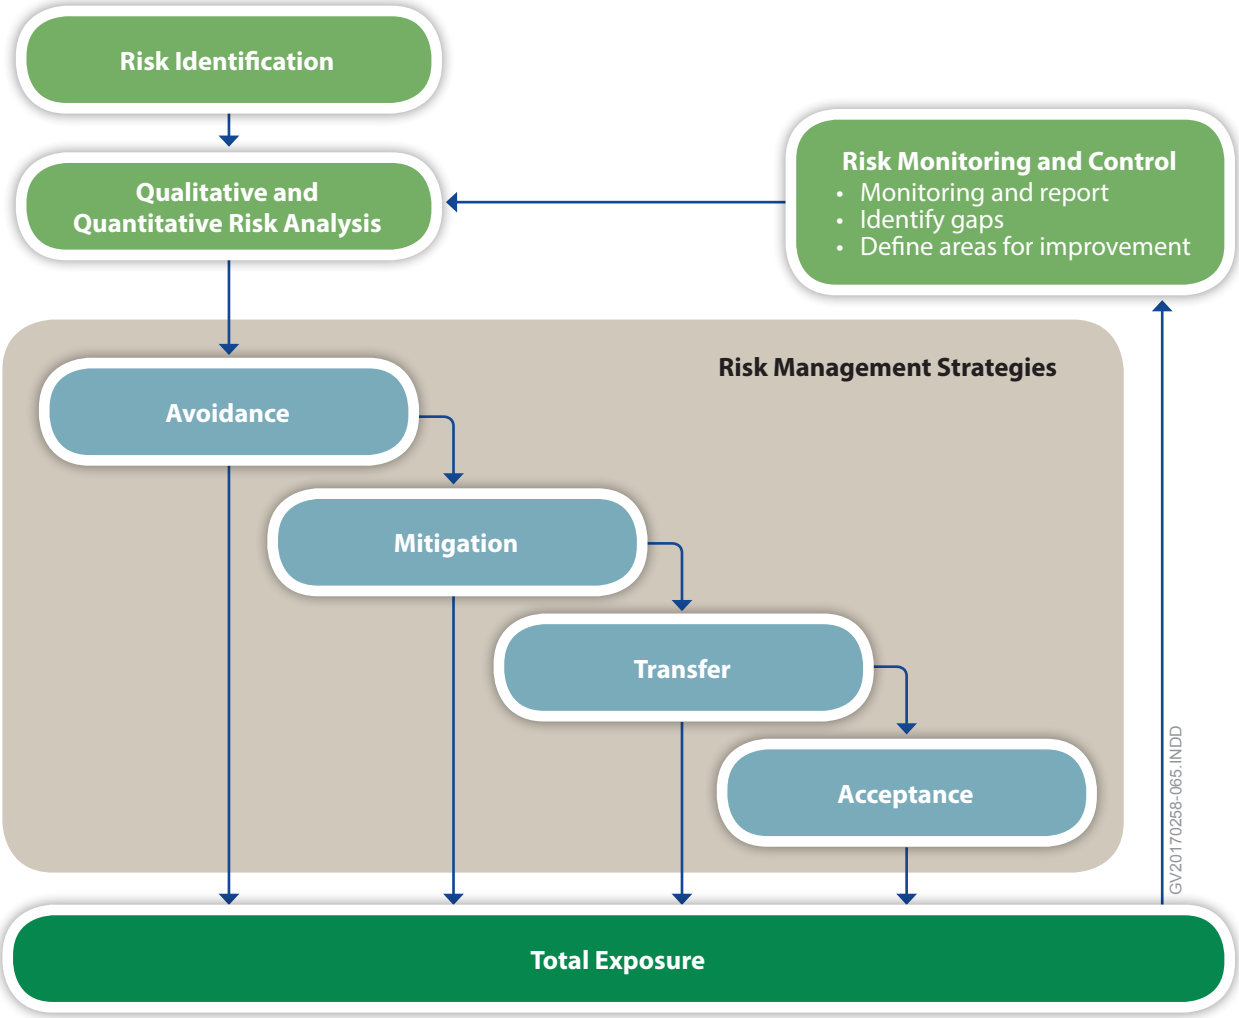


Figure 3.4-1. Risk Management Process. *GLX Constructors' robust process will facilitate cost control and prevent schedule delay.*

GV20171052-001.INDD

By identifying potential risks that may implicate GLX Constructors, or jointly-held Project risks, GLX Constructors began executing our RMP during the Proposal Phase. These identified risks include, but are not limited to:

CONTRACTOR RISKS	THE MBTA/CONTRACTOR RISKS
Constructability	Schedule Certainty – Start Revenue Service
Contract Allocation	Utilities
Design and Construction Performance	Public/Media Exposure
Supply Chain Management	Public Safety
Environmental Conditions	Working near an Active Track
Permits	Adjacent Properties/Abutters
Geotechnical Conditions	Railroad Flagging
Inflation	Subsurface Risks
Material Supply	Environmental Management
Natural Disasters	
ROW Acquisition	
Utility Coordination	
Third-Party Expectations	
Coordination with Ongoing Railroad Operations	

As stated above, GLX Constructors has adopted Fluor's proven BRMF as its primary risk management tool. The BRMF is a formalized, systematic process to identify, manage, mitigate, allocate, and monitor Project risks. Our BRMF will include MBTA risks that we will be able to impact or help mitigate. The steps of the BRMF process are detailed below and are illustrated in Figure 3.4-2.

- **Perform Risk Assessment.** Identify sources of risk, assign responsible party, establish unmitigated exposure value, assign severity, assign likelihood of occurrence, and define priority to rank significant risks. During this step, we prioritize identified risks as a function of likelihood and consequence severity. Consequences are ranked by estimated cost implication into categories: Minor, Moderate, Serious, Major, and Critical.
- **Select Preferred Risk Management Strategies.** Identify mitigation strategies/action plans to be implemented. We have researched each risk and its effective mitigations.
- **Develop and Execute Risk Management Plan.** Assess and revise mitigation strategies as necessary, obtain approval, and execute risk action plans.
- **Monitor and Report Risk Management Performance.** Periodically update the Risk Register throughout the Project's life cycle.

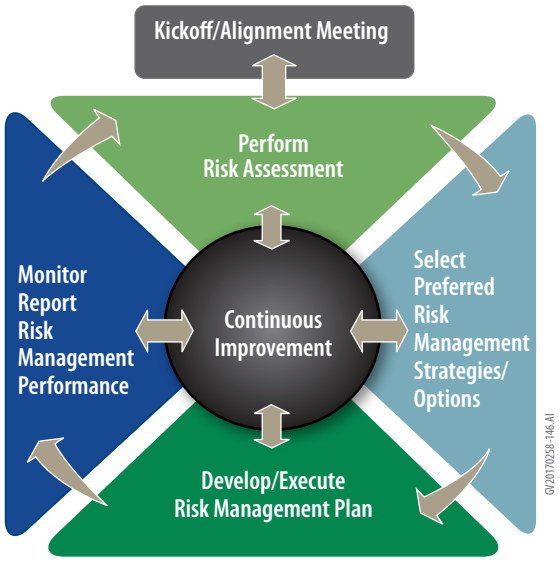


Figure 3.4-2. GLX Constructors' Kickoff/ Alignment Meeting BRMF Model. *Our operational steps for successful risk mitigation.*

As part of our analysis, we assign each risk an unmitigated and mitigated exposure value. Risks with remaining exposure are assigned a value range, assigned a probability of occurrence, and run through a Monte Carlo simulation. This computerized analysis has assessed the schedule, progress, and budgetary impact of risks associated with each Project component. This stochastic sensitivity analysis provides output that prioritizes Project risks, which allows our DB Management Team to focus on those with higher priority.

Within this section, we have included an extraction of our comprehensive Risk Register, shown in Figure 3.4-3, which identifies several key risks related to subsurface conditions, working near an active track, impacts to adjacent properties/travelling public, and other concerns. At the Project's commencement, we will further refine the baseline Risk Register. Throughout the Project, we will use our Risk Register to monitor risks and initiate mitigation activities. Follow-up in-depth reviews will occur quarterly on change events in relation to and at significant Project milestones. We will utilize formal Risk Workshops to track risks identified during the risk management process, and we will continue to identify, assess, mitigate, and manage new risks throughout the Project.

If a potential risk becomes an actuality, our Risk Manager, in conjunction with the DB Management Team, will implement the mitigation strategy that provides the greatest tactical advantage. This proactive risk management process will focus on cost control and preventing schedule impacts. This process has been effective on previous infrastructure projects performed by GLX Constructors' team members and provides schedule certainty.

Updating and addressing risks in the BRMF is an ongoing, iterative process that continues throughout the Project's life cycle, and it includes periodic reviews by both the DB Management Team and the MBTA's Management Team. Our Project Executive, Clyde Joseph, and Project Manager, John West, have been intimately involved in the risk management process during the Proposal Phase, and they will continue to lead this effort throughout the Design and Construction Phases. As part of the transition from construction and integration testing to operations and maintenance, GLX Constructors will work with the MBTA to transfer the Risk Register for continued monitoring and updating.

"For this Project, GZA has drawn on their relevant 53 years of design and construction experience in the local Boston area, which we have incorporated in our preliminary Project design.

3.4.A SUBSURFACE CONDITIONS

See attached Risk Register, Section 3.4.A.

3.4.B WORKING NEAR AN ACTIVE TRACK

See attached Risk Register, Section 3.4.B.

3.4.C IMPACTS TO ADJACENT PROPERTIES AND THE TRAVELING PUBLIC

See attached Risk Register, Section 3.4.C.

3.4.D OTHER MAJOR RISKS

See attached Risk Register, Section 3.4.D.

Figure 3.4-3. Risk Register

#	Risk	Description of Risk	Additional Risk Details	Mitigation Plan/Strategies
3.4.A. Subsurface Conditions				
1	Subsurface Conditions	Differing site conditions	Differing site conditions are considered one of the most significant risks on any project. On this Project, differing site conditions have the potential to adversely impact schedule and costs on work associated with excavations for bridges, retaining walls, noise walls, station and catenary structure foundations, drainage lines, and bridge approach embankments.	▸ To mitigate the effects of potential differing site conditions, GLX Constructors and our geotechnical design consultant, GZA GeoEnvironmental, Inc. (GZA), reviewed the available subsurface information provided on the boring logs and in the reference information documents, and we developed subsurface profiles that depict anticipated geotechnical conditions along the entire alignment. ▸ Additionally, GZA analyzed information from their adjacent projects, including the Commuter Rail Maintenance Facility, to provide a basis for the foundation design and selection for the adjacent proposed VMF. ▸ GLX Constructors performed extensive due diligence during the Proposal Phase to identify potential deviations in soil conditions. ▸ We have leveraged our Team's Project research and vast local design and construction experience to lower the likelihood of design issues related to differing site conditions, and to mitigate any impacts to the Project schedule. ▸ Immediately after Project Award, we will implement a supplemental geotechnical investigation program, detailed in Section 4.2, and sequence our final design with this geotechnical data collection and analysis. ▸ Included in our final design, this supplemental investigation program will include the results of the supplemental explorations and GZA's recommendations, which will be based on the assessed data. Such recommendations may include evaluating the profile to optimize wall heights, incorporating various ground improvements (e.g., surcharging wick drains, removing and replacing areas with poor soil), and considering alternative foundation types. ▸ GLX Constructors will allot specific time for geotechnical investigation and analysis into our Project schedule. ▸ To mitigate potential delays and costs derived from differing site conditions, we will analyze the Project schedule and then implement alternative construction strategies that allow for flexibility and minimize prospective lost time events. ▸ Alternative strategies may include redesign, accelerating the work, or resequencing the work. ▸ Possible differing site conditions and specific mitigations are included below.
2	Differing Site Conditions	Unknown obstructions in the historic fill at the south end of the alignment and in the area of the VMF, which could impact installing deep foundations	These obstructions include the unknown foundations for the two existing buildings to be demolished in the VMF Footprint, the details of which are not available from the City of Somerville's Building Department.	▸ Our preliminary foundation design provides flexibility based on the expectation that obstructions may be encountered. ▸ We will also have appropriate tools and equipment available, at the site. ▸ In addition, GLX Constructors will pre-clear areas, in particular the VMF, in preparation for pile driving operations to expose potential areas of concern early and mitigate any potential issues prior to becoming an impact.
3	Differing Site Conditions	The variability of the bedrock elevation and quality of the bedrock	In addition to the naturally occurring variability, there are several instances where the borings in close proximity to one another were prepared by different geotechnical engineers, and indicate very different ground conditions, potentially impacting deep foundation element installation.	▸ We have already analyzed boring information to identify trends at the top of bedrock elevation and the quality of the bedrock. ▸ We have included provisions for performing supplemental borings in critical areas where drilled shafts are required. ▸ We have adopted driven pile foundations for Piers 8 through 24 of the viaduct to mitigate rock quality issues (piles will take up in soils above the bedrock in many cases). ▸ Additionally, driven pile avoids uncertainty of weathered rock due to pile testing. We will have appropriate tooling and equipment available at the site to deal with obstructions.
4	Differing Site Conditions	Limited subsurface information along some of the proposed retaining walls	Due to access limitations, borings were not performed along the alignment of several retaining walls. Therefore, we expect ground conditions to vary from those inferred for adjacent borings.	▸ We have used conservative preliminary design sections at these wall locations. ▸ We will perform additional borings prior to final design to accommodate for prevailing conditions early. ▸ This approach will facilitate an accurate design that can be completed early or on time to avoid schedule impacts.
5	Differing Site Conditions	Reliable Information regarding levels of soil contamination at the ROW		▸ GLX Constructors has performed extensive hazardous materials due diligence during the proposal phase. ▸ We first identified all recorded soil and groundwater contamination along the entire Project corridor. ▸ We then developed an interactive web mapping tool of all data points to show probable soil conditions linked to associated disposal categories. ▸ Using this information, we have been able to pre-characterize the ROW soils that will be excavated and have incorporated it into our design to maximize the reuse of contaminated soils as backfill material on site. ▸ Additionally, we raised the VMF site elevation and included ATC 35 (changes to portions of the Viaduct Structure to an earth-filled MSE Wall Structure) to provide an opportunity for reuse of appropriate soil. ▸ These approaches maximize reuse of excavated contaminated material on-site versus off-site; thereby, reducing both costs and risks of unnecessary transport of material for off-site disposal.

"The MBTA's Greenbush Commuter Rail Project included many sensitive environmental elements, including the clearance, site preparation, the handling and removal of contaminated materials, installation of trackside drainage, retaining walls, and fill throughout the corridor. The 18-mile-long corridor was constructed through areas of wetland and intense environmental sensitivity that required significant mitigation. It also passed through many urban communities often behind private residences and across major surface streets, requiring a constant awareness and vigilance to the needs of these communities and traffic patterns.

With the support of STV, Balfour Beatty provided support to the prime contractor to ensure environmental compliance throughout the project duration.

Our success in working near an active track within an urban environment with a limited ROW can be attributed to building healthy partnering relationships throughout design and construction on each project.
Fluor and Balfour Beatty's work on portions of the Eagle P3 Commuter Rail Project in Denver, Colorado occurred adjacent to BNSF and UPRR freight rail corridors.

Design and construction considered requirements associated with freight railroads, such as clearances between OCS poles and freight railroad tracks, electromagnetic compatibility with freight railroad communications and signal system, and protection screens and bonding of existing railroad bridges. Portions of construction and installation work were adjacent to Class I ROW. In addition, this team coordinated the design and construction of the shared at-grade crossings with UPRR. This involved joint applications to the PUC, establishing interconnectivity between UPRR and the Fluor- and Balfour Beatty-led team signal houses and city traffic systems, and joint testing and commissioning of the crossings in the field.

#	Risk	Description of Risk	Additional Risk Details	Mitigation Plan/Strategies
6	Working Near An Active Track	Working near an active track	Mitigate and minimize risks of working near an active track through a depth of experience and current working relationships.	▸ GLX Constructors will draw upon our team's personnel expertise and vast experience on past projects working near an active track. ✦We have a depth of experience with railroad owners – in particular, Keolis, Pan Am, CSX, Amtrak, and the MBTA. ▸ We will leverage our established relationships, experience, and knowledge to facilitate communication, coordination, and approvals with the railroad operations. ✦It is a significant benefit to the MBTA that all GLX Constructors' team members have worked on multiple, major infrastructure projects involving work adjacent to, or in, passenger and Class I freight railroad right-of-way (ROW). ✦By successfully executing these projects, we have demonstrated our understanding of the requirements for safe and efficient construction projects of this size and complexity. ✦To the extent we are able; we are committed to maintaining service for the MBTA's passenger and freight rail lines. ✦Our past projects have all required diligent coordination with multiple third parties, interface with the project Owner's active rail lines, and work around other operating, active rail lines. In discussions pertaining to ROW used for freight service, it is critical to properly coordinate and thoroughly understand shared use agreement rights between the MBTA and freight railroads. ▸ Success requires regular, clear, and persistent communication between the freight railroads, the DB Management Team, and the MBTA.
7	Working Near An Active Track	Working near an active track – coordination and permitting	Adjacent railroad stakeholders will be critical to providing information necessary to achieving Substantial Completion. For this reason, these companies will have the priority when we begin early coordination and permitting.	▸ To handle all aspects of railroad coordination, we have appointed Jack Rahmes as our Railroad Coordinator. ▸ Jack will serve as the single point of contact to the railroads, and he will make certain that GLX Constructors clearly communicates with railroad stakeholders throughout the permitting and approval process. ▸ Holding daily and weekly coordination meetings, Jack will remain dedicated through the Construction Phase to keep the MBTA, Keolis, Pan Am, CSX, and Amtrak closely informed about our construction activities and any work that may affect their facilities or operations. ▸ To facilitate working near an active track, our work plans will detail the completion of the day or night shift work activities, which will include sufficient time to inspect the adjacent track to confirm it can be placed back in service. ▸ This inspection will occur with the MBTA's EIC, the MBTA Flagger, and our Superintendent in charge of the associated work. **For the last 5 years, GLX Constructors' team member, Balfour Beatty, has coordinated closely with UPRR on the active Alameda Corridor Transportation Authority (ACTA) Track Maintenance Contract, which involves moving an existing freight corridor between the Ports of Los Angeles and Long Beach and the UPRR and BNSF hubs in Los Angeles into a 30-foot-wide trench.** **With experience working in a dense, urban corridor, Balfour Beatty has a clear understanding of the coordination challenges and freight railroad requirements necessary for successful execution of safe work within a limited ROW envelope.** **GLX Constructors team members, Balfour Beatty and STV, worked on the Charlotte Area Transit Systems (CATS) LYNX LRT Blue Line Extension, which included combined right-of-way with the State of North Carolina, CSX, and North Carolina Railroad.**
8	Working Near An Active Track	Flagger	Working safely and efficiently around the existing commuter rail, freight rail, and active Green Line tracks requires extensive pre-planning, coordination, effective communication, and great attention to detail.	▸ Our Railroad Coordinator, Jack Rahmes will be actively engaged with planning, notifications, and requests for railroad flagging services. ▸ We will coordinate and establish comprehensive work plans that allow for long-term planning for sufficient flagging resources. ▸ This pre-planning detail will help mitigate schedule disruptions that may occur from any potential shortage of flagging resources. ▸ GLX Constructors' work plans will maximize barriers and barrier fences to minimize the need for flaggers while working in the active ROW. ▸ Our Railroad Coordinator will arrange for flagging at the Track Coordination Meetings and in accordance with the Technical Provisions. ▸ Per the contract requirements, GLX Constructors will develop the construction schedule based on a maximum of 18 flagging resource available on any particular day.
9	Working Near An Active Track	Signal work	Interfacing with adjacent developers and projects is critical to the success of the Green Line Extension DB Project; perhaps no item is more critical than effectively coordinating with adjacent freight and commuter railroads.	▸ Beyond co-locating with the MBTA for daily coordination, we will also employ an aggressive coordination schedule to meet frequently with the MBTA, Keolis, Pan Am, CSX, and Amtrak. ▸ In addition to coordinating construction activities and phasing with ongoing railroad operations, our Railroad Coordinator, Jack, will coordinate track and signal work performed by the Railroad Operator (e.g., Keolis for commuter rail). ▸ Work performed by the Railroad Operator will be over-laid on both long- and short-term Project schedules. ▸ During regular construction coordination meetings, we will review our planned work and its associated timing.

GV20171052-001.INDD

#	Risk	Description of Risk	Additional Risk Details	Mitigation Plan/Strategies
10	Working Near An Active Track	Safety	The safety of the traveling public, community members, and our employees is the most critical aspect of the Green Line Extension DB Project. As discussed in Section 3.1, safety is our Number 1 priority – no priority is higher.	▸ GLX Constructors' safety culture is based on the highest corporate standards of Fluor Enterprises, Inc., The Middlesex Corporation, Herzog Contracting Corporation, and Balfour Beatty Infrastructure, Inc., whose concepts and practices have been used and tested with successful results on projects throughout the world. ▸ Working near an active track presents unique safety hazards that require customized procedures to mitigate effectively. ✦ Communicating safety hazards and procedures is critical to the success of our safety and health training programs. ▸ We will adopt a detailed safety program and culture on the Project from inception. ✦ Roadway Worker Protection (RWP) training is required for all workers, which will clearly lay out responsibilities and protocols. ✦ Employee orientation at the Project's onset includes communication work force prior to construction. ✦ This training will emphasize work areas that are adjacent to live rail and vehicular traffic, with measures that include positive barriers, increased visibility, controlled/designated points of ingress and egress, and flaggers. ▸ We will develop a Project-specific Roadway Worker Safety Protection manual (RWSP), which implements stringent standards that are consistent with federal regulations and aligns with Keolis' RWSP. ✦ Our RWSP will afford on-track safety for all roadway workers whose duties occur on the Project's property, and it will provide specific levels of protection required by federal law. ✦ Our policy will include procedures to monitor both the effectiveness and compliance with the program. ▸ Rules and operating procedures governing track occupancy and protection are included together in one manual, which will be readily available to all roadway workers. ✦ GLX Constructors understands that it is responsible for its employees' understanding of and compliance with the rules and the requirements of the on-track safety program. ✦ Each roadway worker will be responsible for following the on-track safety program when working on Project property. ✦ A roadway worker will not foul a track except when necessary for the performance of the work. ✦ Each roadway worker is responsible to ascertain on-track safety before fouling a track. ▸ We will implement a Track Access Program, in which work near active railroads must be coordinated between GLX Constructors' Railroad Coordinator and the Track Access Committee. ✦ This coordination will take place during our daily Track Access Committee Meetings. ✦ Preparation will include developing detailed work schedules, plans, procedures, and other information as required by the railroads. ✦ All planned work is subject to approval by the Track Access Committee. ▸ We will strengthen corridor safety by optimizing our design and carefully phasing construction in a way that reduces or eliminates work over active rail and traffic lanes. ✦ GLX Constructors will develop detailed Management Plans (e.g., PEP, DQMP, CQMP, SWP3) that include work activity planning and processes, and management structures that achieve quality and compliance to improve safety. ✦ To further increase our safety measures, GLX Constructors will implement and enforce detailed lifting/rigging safety procedures, where no pedestrians or vehicles will be allowed under loads during critical lifts or major construction events that may create a potential hazard to nonconstruction personnel. ✦ We will pre-plan all lifts and develop critical lift erection plans for qualifying lifts, complete with critical lift Constructability Reviews performed by GLX Constructors Operations & Safety. ▸ A structural engineer will design support of excavation systems, with Constructability Reviews performed by GLX Constructors Operations & Safety. ✦ As detailed in Section 3.1, GLX Constructors will implement the and training of our Health, Safety, and Environmental (HSE) Plan and philosophy to the Safety Task Assignment (STA) process and incorporate utility location information into the STAs. ✦ We will provide high visibility warning signage and use a utility spotter at all times when working in high-risk areas. ▸ To prevent injury to both the traveling public and Project employees, we will establish and implement a comprehensive Testing and Commissioning Plan. ✦ Third parties will be included as part of the development of these procedures. ✦ We will institute a comprehensive public information campaign prior to live testing, which will require outreach and close coordination with places such as nearby residences, businesses, universities, and places of worship. ✦ We will also add additional security and safety personnel during the Testing and Commissioning Phase to enforce HSE protocols, including the Project Security Plan, which is a component of the HSE plan.

In 2016, the National Railroad Construction and Maintenance Association recognized Balfour Beatty and Herzog with its Platinum Award for excellence in railroad safety after subjecting their safety program and safety practices to a rigorous review.

This award recognizes Balfour Beatty and Herzog's extensive efforts to promote and improve safety in rail construction.




#	Risk	Description of Risk	Additional Risk Details	Mitigation Plan/Strategies
11	Working Near An Active Track	Maintaining convenience to the public	Maintaining adequate access in and around the Project site is important to minimize inconveniences to the traveling public and to fostering a positive community relationship.	▸ GLX Constructors will perform pre-construction video of all surrounding roads to thoroughly document existing conditions, and to seek agreement on pre-existing condition with local entities and the MBTA. ▸ To reduce congestion, improve safety, and limit wear on local roads, GLX Constructors will use off-road hauls when possible. ▸ Our design and construction approach has minimized heavy hauling on local roads. ▸ We will carefully plan our major construction access activities that might interact with local event days, such as the Boston Marathon on Patriot's Day, Evacuation Day, Bunker Hill Day, other sporting events, or local municipality event days. ▸ Our Title VI Program Lead will communicate with the MBTA and appropriate third-party stakeholders to provide this input to our planning and scheduling team
3.4.C. Impacts to Adjacent Properties and the Traveling Public				
12	Impacts to Adjacent Properties and the Traveling Public	Minimize impacts through proactivity, public engagement and awareness	It is critical to the Project's success to maintain an excellent reputation for the MBTA, GLX Constructors, and affiliated companies and maintains positive impressions from the community.	▸ In our partnership with the MBTA, GLX Constructors will involve the local community through sponsored information sessions throughout the Project's life to solicit feedback and identify improvement opportunities for stakeholder involvement. ▸ We will engage local agencies and stakeholders through our TWGs and ad hoc meetings during the planning stages of both design and construction, so we may address concerns early and adequately. ✦ To establish and maintain positive community impressions, we will emphasize the importance of minimizing impacts to adjacent properties and the traveling public. ▸ Understanding the right-of-way limits, the surrounding neighborhoods, and nearby businesses is critical to minimizing impacts to properties that are adjacent to the Project. ✦ Our workers will walk construction work zones prior to construction to familiarize project staff with the Project's right-of-way. ✦ We will define access points during post-award planning. ✦ To encourage their use, enhance safety, and minimize confusion, points of ingress/egress will be clearly marked with orange construction entrance signage. ▸ As part of our planning process, we will know the working hours in each jurisdiction and engage in an active community outreach program. ✦ We will meet with local businesses in particular work zones to provide updates and familiarize ourselves with their concerns and issues. ✦ Additionally, GLX Constructors will execute our work per the approved work plans and permits (e.g., environmental compliance and night work) and closely monitor noise and vibration attributable to on-site construction activities. ✦ Further, our design minimizes driven pile foundations in favor of noise- and vibration-friendly drilled shaft and micro-pile foundation types. ✦ To document existing conditions prior to the start of construction (e.g., nearby building foundations), GLX Constructors will hire a specialized firm to perform pre-construction surveys, which will include video as necessary. ▸ To prevent potential damage during construction to adjacent historic properties and cultural resources found in the Pre-Construction Survey, we will develop a Comprehensive Environmental Protection Program (CEPP) for the project, per the contract, to include protocols for protecting known historic properties and cultural resources. ✦ GLX Constructors will implement a detailed CEPP on the Project from its inception, with training that includes clear responsibilities and protocols. ✦ We will identify known historic and cultural sites/non-disturbance limits in the plans, and fence/protect-in-place known sites prior to the start of construction activities. ✦ Our Environmental Manager, Chris McDermott, will also monitor known historic/cultural sites, and in the event a historic/cultural site is damaged, crews will stop work in the immediate area, create a safe buffer, and notify the Environmental Manager. ▸ To minimize impacts to the traveling public, we will develop comprehensive Track Access and Maintenance of Traffic (MOT) plans, and schedule work to minimize rail/lane impacts (e.g., by using allowable track windows, night, and weekend work). ▸ We will also develop comprehensive work plans to eliminate the need for unplanned rail/lane closures. ✦ By coordinating with and obtaining approval from the MBTA on the proposed schedule for all full closures, we will develop hour-by-hour schedules, including an additional 30-minute buffer to provide maximum planning for all such events. ✦ As an extra measure of insurance, we will develop contingency plans for all partial and full rail/lane closures. ✦ In our experience, effectively communicating lane closure requirements to all subcontractors and inspectors enhances their performance.

GV20171052-001.INDD

#	Risk	Description of Risk	Additional Risk Details	Mitigation Plan/Strategies
3.4.D. Other Major Risks				
13	Schedule	Schedule certainty	Delivering schedule certainty begins very early in the process through a robust understanding of the Project, and continuous engagement of interdisciplinary teams of subject matter experts and key stakeholders in a formal, collaborative structure, i.e., Technical Working Groups, to collectively mitigate and minimize potential and actual schedule impacts.	▸ GLX Constructors have developed a detailed construction schedule based on our initial design. ▸ We have included input from our Design Team, Construction Team, Environmental Team, local subcontractors, and our DB Management Team. ▸ We have reviewed safety concerns and modified design and construction procedures where necessary. ▸ By properly including our Construction Team into our Design Team's Technical Work Groups, we have streamlined our design's review and approval process. ✦ This approach to construction-driven execution adds certainty that we will achieve faster startup of construction activities, taking advantage of as much of the 2018 construction season as possible. ▸ Utility relocations and their associated designs have been identified and scheduled for early works design and construction to mitigate potential impacts to the Project's DB Schedule. ▸ We will develop detailed early work design schedules for execution and construction, allowing the MBTA and appropriate third-party stakeholders' adequate time to react and plan. ▸ After Project Award, we will begin coordinating and proactively partner with local cities and stakeholders for optimal night work windows, which will help mitigate schedule impacts and lessen the burden to local communities. ✦ We will train all workers in accordance with the requirements of each jurisdiction impacted by night work operations and their associated noise control plans. ▸ The original baseline schedule is produced on the Primavera P6 platform, and we have also evaluated our construction resources using Time Location Diagram software, TILOS, to highlight areas of heightened concern for resource allocation, including flagging resources. ▸ GLX Constructors performed a Primavera Schedule Risk Analysis to assesses the schedule, progress, and budgetary impact of risks associated with each Project component, and the output shows the probabilistic likelihood of achieving particular major milestones ✦ A schedule risk analysis calculation has been performed generating a P85 confidence level of achieving the required milestone dates, as shown in the graph below.

Initial Baseline Schedule Analysis

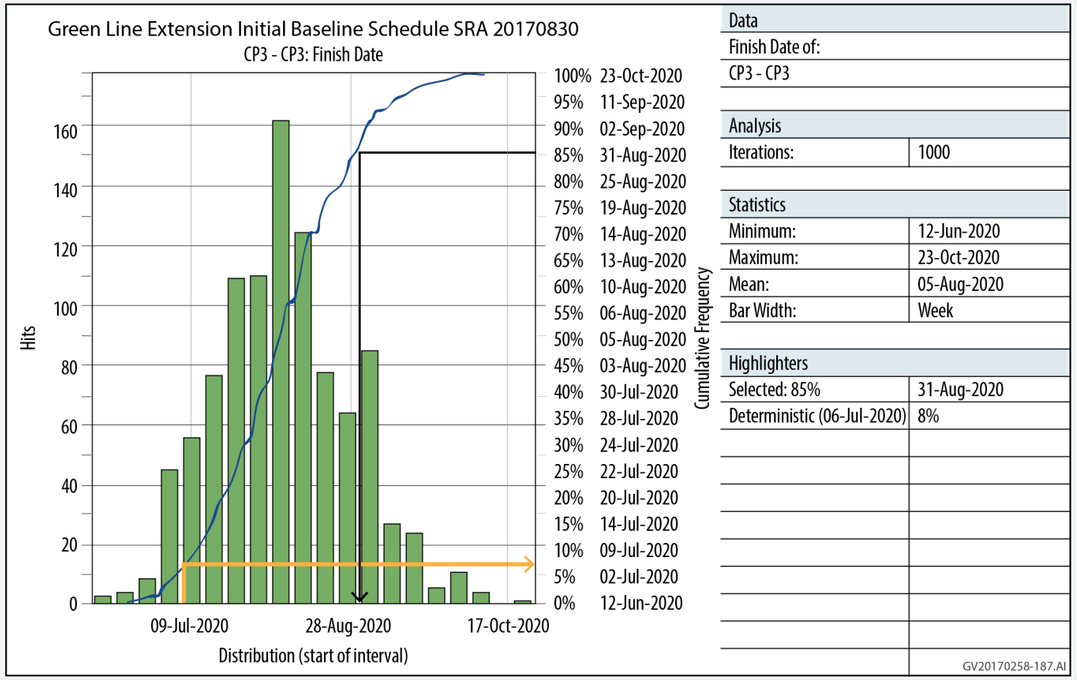

Data	
Finish Date of:	
CP3 - CP3	
Analysis	
Iterations:	1000
Statistics	
Minimum:	12-Jun-2020
Maximum:	23-Oct-2020
Mean:	05-Aug-2020
Bar Width:	Week
Highlighters	
Selected: 85%	31-Aug-2020
Deterministic (06-Jul-2020)	8%

GV20170258-187.AI

"Our construction team is well-versed in accelerating construction to avoid rail closures.

For example, on the Utah I-15 CORE Highway Design Build Project, GLX Constructors' team members used Accelerated Bridge Construction (ABC) to expedite the schedule. Under this ABC method, four bridges were constructed on the side of I-15. With the use of a remote-controlled, self-propelled modular transporter, the bridges were swiftly moved into place overnight, allowing for only a single-night full freeway closure – without affecting the safety or travel times of motorists using the interstate.



#	Risk	Description of Risk	Additional Risk Details	Mitigation Plan/Strategies
14	Utility Risks	Effectively managing several high-risk utilities that lie within the Project corridor	Spectra Energy Algonquin's (now Enbridge) gas line at STA 266+50; the MWRA 12" waterline and Verizon ductbank at Medford Street; the at-grade ductbank, waterlines, and sanitary sewer lines at School Street; and the water, electrical, and communication lines at Broadway. Relocating these utilities will have long durations and coordination will involve long lead times, as discussed in Section 4.9.	▸ GLX Constructor's design approach includes adjustments that minimize the impacts to utilities, leaving them, in-place where possible. ▸ Our Utility Coordinator will be the main point of contact between GLX Constructors, the MBTA, and Utility Owners, and we will leverage our previous experience and relationships with MWRA, Enbridge, Verizon, AT&T, and others throughout the Project limits to help expedite reviews and approvals. ▸ GLX Constructors will maintain a good working relationship with all Utility Owners and will comply with each Utility Agreement and its Project Execution Plan (PEP). ▸ The Utility Coordinator will develop, manage, and update the Utility Coordination Plan (UCP), and will organize coordination meetings to identify, clarify, and resolve issues. ▸ Utility coordination will take place immediately after Project Award to minimize schedule impacts. ▸ Early coordination will include identifying and confirming utility locations, potential conflicts, and required relocations. ▸ As part of this process, we will develop a utility relocation and new service matrix to identify relocations, required easements, new service delivery points and routings, utility test pits, and costs associated with relocations. ▸ Sharing information with Utility Owners early on will reduce problems arising from an inadequate available Subsurface Utility Engineering (SUE) level, including risk of an accidental utility strike by crews working in close proximity to existing lines and infrastructure. ▸ The UC will prepare Utility Agreements, PEP documents, and maintain a Project utility composite map, showing existing and proposed utility alignments, and an issues status log. ▸ The UC will also develop action plans and schedules to control and monitor execution and compliance with the respective PEP. ▸ We will maintain ongoing communication with utility companies so that design and construction of relocations is performed in an efficient, cost-effective, and constructible manner to the Utility and MBTA Standards. ▸ To accelerate utility relocations, we will use special utility designers approved by the Utility Owners. ▸ If required, we will update and reissue the UCP to address changes in site conditions and Project scope. ▸ GLX Constructors will execute any necessary agreements with Utility Owners, and we will perform the design and construction of the utility relocation to minimize risk. ▸ In the event that we encounter an unidentified utility, we will perform a Utility Adjustment Amendment to accelerate the relocation process if a Utility Agreement is already in place with the owner of the unidentified utility.
15	Public/Media Exposure	Maintaining rider satisfaction	Maintaining rider satisfaction, as well as convenience to the public, during the construction of the Green Line Extension DB Project is essential to us.	▸ GLX Constructors understands the importance of not disrupting train schedules, particularly in a congested, urban area. ▸ We will reduce public inconveniences through design optimization and careful construction planning that streamlines cutover/tie-in activities and accelerates the work. ▸ We will coordinate with and obtain approval from the MBTA on the proposed schedule for all full closures to support cutover/tie-in operations. ✦ We will develop detailed cutover/tie-in plans that are realistic and achievable within the allowable outage windows and provided time constraints. ▸ Detailed planning will include developing hour-by-hour schedules for all cutover/tie in events, including an additional 30 minute buffer for demobilization. ▸ As an extra measure of insurance, GLX Constructors will also develop contingency plans for all cutover/tie-in events.
16	Public/Media Exposure	Public awareness and outreach	Maintaining public awareness with extensive outreach to communicate project status and mitigate public concerns/issues during construction.	▸ GLX Constructors' Title VI Program Lead, Hannah Brockhaus, and her team will support the MBTA on public and media exposure events, whether planned or unplanned. ▸ Our approach is to identify potential exposure during the initial design evaluation and assemble an event specific plan or approach for dissemination to the public and media.

The Green Line Extension DB Project has unique technical, public relations, and logistical challenges. It presents potential Projects risks that must be actively managed for the Project to be successfully delivered on time and within budget. These include, but are not limited to:

Mobility and Safety. *The Green Line is a highly congested, active commuter, passenger and freight rail corridor, and a gateway to visitors who enter the city for special events. Therefore, the Project demands advanced track allocation/access management, maintenance of traffic, construction planning, sequencing, scheduling, and communications/SCADA, signals, systems, and ITS management to protect the safety and mobility of the public before, during, and after construction.*

Third-party interfaces. *The biggest risk to on-time completion lies within third-party interfaces and utilities such as MWRA, Enbridge, Verizon, and AT&T. These stakeholders and their requirements must be well understood and built into our plans and schedule in advance.*

Environmental. *Cambridge, Somerville, and Medford are Environmental Justice communities that pride themselves in environmental stewardship. The Green Line Extension DB Project will result in significant air quality improvements in the region's most densely populated community.*

We are committed to completing the Green Line Extension DB Project on time and within budget. We sincerely understand the critical nature of these requirements – many of us live here, and we have successfully completed other infrastructure Projects in the area.

To make certain these challenges were known, properly addressed, and built into our plans, price, and schedule, we have assigned a group of highly experienced staff to develop a detailed list of potential Project risks and their associated mitigation measures. We have invested an extensive amount of time into due diligence, including detailed meetings with key stakeholders to make certain we fully understand the Project's implications, challenges, and requirements. As a result, GLX Constructors is prepared for a rapid, efficient, and successful start to the Project, focused from the first day on the MBTA's Project goals.

3.5 INITIAL BASELINE SCHEDULE

Since our SOQ submittal in early 2017, GLX Constructors has invested tremendous resources in the pursuit of the Green Line Extension DB Project. In developing our proposal, we have performed schedule analyses to fully assess the design and construction challenges of the Project. While performing these activities, we focused on the MBTA's milestones, objectives, and activity restrictions. In establishing our Initial Baseline Schedule, we have coordinated the scope of all Project-related activities to safeguard schedule certainty, identify potential risks, and implement appropriate mitigation measures to address concerns from the MBTA and local municipalities.

The Project's schedule is at the core of Project execution, and it must be continuously monitored to make certain that work is performed within the established time allotted. As it is with all schedule preparations, the Project Team's input and active participation is essential. GLX Constructors will make certain that the Project Team – comprising the Superintendents, Project Controls Team, and DB Management Team – is the principal driver for developing and maintaining the Project Schedule from Notice to Proceed 1 (NTP 1) through Final Acceptance.

GLX Constructors' Scheduling Team works closely with our engineers, managers, and designers to create and maintain the most achievable, aggressive schedule for the Green Line Extension DB Project. We have evaluated and included considerations for potential needs and impacts of local residents, the traveling public, the environment, weather, and other anticipated events to produce an achievable Initial Baseline Schedule. We have accurately determined the baseline construction period, and we commit to the completion of each required milestone while maintaining minimal inconvenience to the public.

3.5.A GLX CONSTRUCTORS' UNDERSTANDING OF DESIGN PHASE AND CONSTRUCTION PHASE PLANNING

Our Initial Baseline Schedule is a construction-driven Critical Path Method (CPM) schedule developed as a collaborative effort by all Project disciplines, including our Lead Designer, STV, and relevant subconsultants. During the Proposal Phase, GLX Constructors collaborated in our Technical Work Groups (TWG) to develop the Initial Baseline Schedule and include initial design concepts. These TWGs will continue during the DB phase of the Project, during which the schedule will remain a critical, primary topic of discussion. We will regularly review and update the schedule to meet the MBTA's goal to achieve schedule certainty.

Included in our Initial Baseline Schedule is our Design Team's input for the Design Phase of the Project. The Design Team is committed to completing the design activities in a timely manner to support the overall Project

Schedule. Each step of the Design Package (30/60/90/RFC, as illustrated in Figure 3.1-12 in Section 3.1, Project Management Plan) has been included in the Initial Baseline Schedule, as well as appropriate QA/QC, constructability, the MBTA, and third-party review timelines.

Receiving the Ready for Construction (RFC) drawings initiates construction activities. We have evaluated the construction activities with our principal estimators, construction superintendents, and DB Management Team to make certain the construction activities' depictions are accurate. We have allotted time in each construction activity for QA/QC inspection and approval, which allows for proper work documentation.

After construction activities are complete, the Testing and Commissioning Phase of the Project commences; we have included aggressive, achievable timelines for the completion of this work in the Initial Baseline Schedule. Our Systems Team, composed of design and construction personnel, has collaborated to confirm the proper amount of time needed for testing, commissioning, certification, and rail activation before revenue service begins.

3.5.B GLX CONSTRUCTORS' UNDERSTANDING OF HOW THE CRITICAL PATH METHOD WILL BE UTILIZED

Our Initial Baseline Schedule, which comprises the integrated design, procurement, construction, and testing/commissioning schedules, includes a fully integrated CPM schedule that identifies critical design packages and long-lead procurement items that support our initial construction activities. By integrating design, procurement, construction, testing, and commissioning activities into a single CPM schedule, the critical path schedule incorporates all necessary elements and displays the float to the specific activity, rather than design, procurement, or construction as a whole.

Our critical path determines the duration of the longest path from Project Award through Contract Final Acceptance, and it does not contain arbitrary resource ties. The activity and logic ties show all required work sequentially; the logic ties define all tasks related to the MBTA or third parties. We have determined our critical path by pure construction logic.

All activities, with the exception of the Project Start and Completion milestones, are logically tied without using Start-to-Finish relationships. No unrelated or interim dates are used to influence any float values. The total float value is initially determined by NTP to Milestone 4A, then from Milestone 4A to Milestone 4B, then to the Contract Final Acceptance. The longest path with the least float value (0 days) defines the critical path from Design to Construction to Contract Final Acceptance.

GV20170258-118.INDD

We will use the critical path schedule during contract execution to highlight the activities where potential delays may occur without mitigation efforts. In addition, we will highlight any schedule paths that are near critical, five days or less of float, to identify other schedule areas that may require mitigation.

The critical path activities that determine our baseline Construction Phase are shown in Appendix 2 – Initial Baseline Schedule Critical Path.

3.5.C GLX CONSTRUCTORS' UNDERSTANDING OF THE MBTA'S REQUIREMENTS

During the Proposal Phase, GLX Constructors carefully reviewed the RFP and associated documentation. Our thorough understanding of the MBTA's requirements is clearly demonstrated by our schedule submittal, which includes:

- A complete CPM.
- A resource-loaded schedule to include a sample figure of $100 million.
- Effective logic showing all responsibility designations and durations.
- Sample cash flow report.
- Complete outline of the schedule coding.
- A complete production rate basis table.
- A work breakdown structure (WBS) depicting the MBTA's mandatory codes, with additional codes added to enable GLX Constructors to further filter through and analyze the data.

3.5.D GLX CONSTRUCTORS' INNOVATIVE APPROACH TO THE WORK

Our Initial Baseline Schedule incorporates all approved ATCs. In addition, our schedule has been integrated with a time-location diagram using the program TILOS®. This innovative diagram linearly depicts the entire construction of this Project segment in a cohesive, one-page format, as exemplified in Appendix 3 – TILOS Schedule for Union Square Line and Appendix 4 – TILOS Schedule for Medford Line.

As illustrated in Figure 3.5-1, a snapshot of the TILOS schedule for Medford Line, the left side of the diagram depicts the time scale of the Project, and the top section shows the linear segmentation of the Project. As a benefit, the time-location diagram conveniently shows the location of all construction activities, as well as their time frames in a linear fashion.

Through carefully analyzing the TILOS diagram, crew density, and productivity rates, the simultaneous construction activities demonstrate potential constructability and conflict issues long before construction

> **"The innovative use of Herzog's Multi-Purpose Machine (MPM), gondola cars, flatcars, and low-railers will allow GLX Constructors to avoid congestion in the corridor by shuttling materials and equipment into and out of the work areas during off peak hours. Because of the low profile of the cars, equipment can be easily transported to and from the corridor, and work operations can be performed from low-rail mounted equipment.**

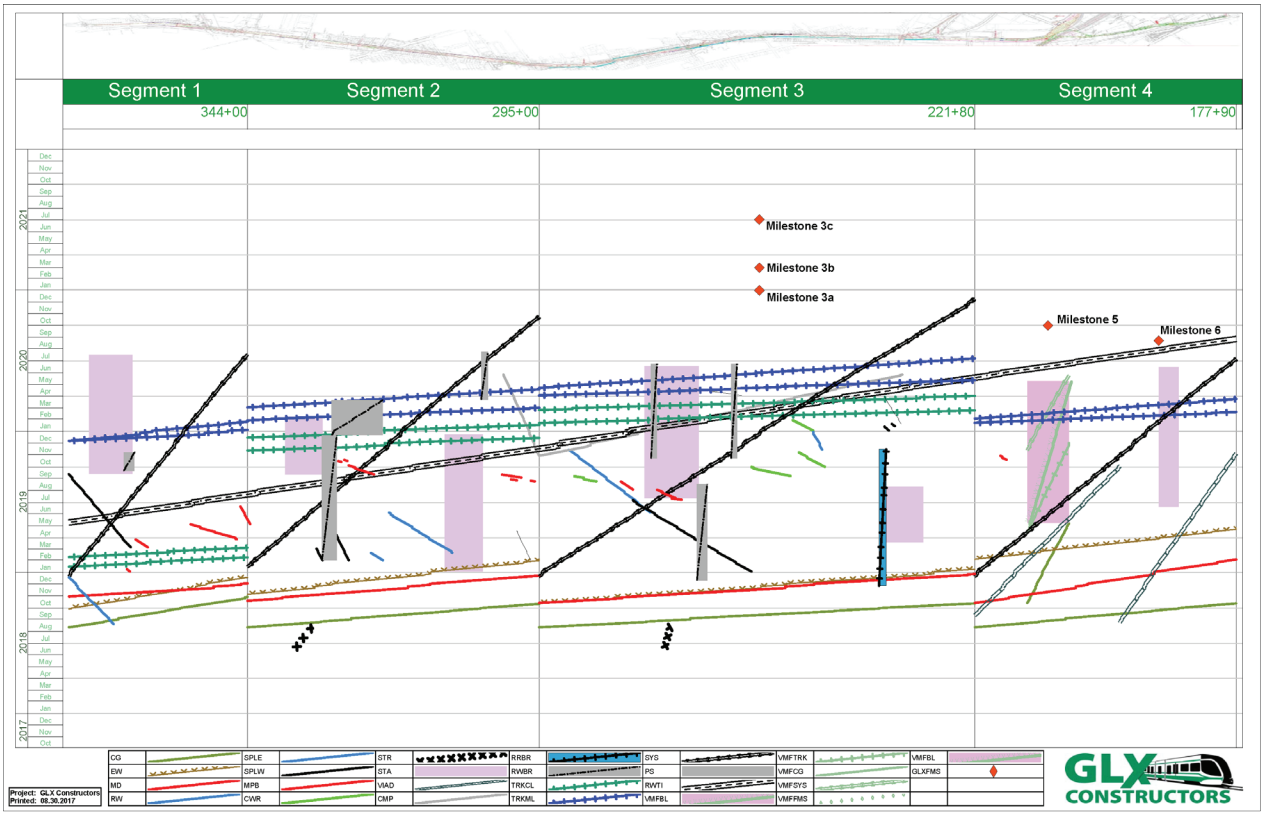


Figure 3.5-1. TILOS Example. *GLX Constructors will use TILOS to demonstrate the entire construction of the Project in a cohesive, one-page format.*

begins. This information is seamlessly integrated with our Primavera schedule for simple import and export functionality.

This integration allows us to perform constant, real-time analysis of our Project schedule and adjust, as necessary, to protect an on-time Project completion.

Innovative Rail Techniques

Our team will eliminate, or overcome, many of the risks associated with the constricted work zones by using Herzog's proprietary rail equipment. We believe our capabilities and experience in using this equipment will vastly reduce risk to GLX Constructors and the MBTA to successfully complete the Project on or ahead of schedule. During preconstruction, we will use hy-rail light detecting and ranging (LiDAR) trucks to create a 3D model of the corridor features to confirm elevations, clearances, and spatial relationships.

LiDAR Imaging

Herzog's specialized LiDAR trucks can produce in-depth laser scans for horizontal and vertical geometry of the ROW in an electronic file format, which is able to be directly uploaded into our design software programs as needed. The LiDAR information allows us to provide information to the

GV20170258-118.INDD



On the DCTA A-Train Project, ballast was brought in and was stored in several locations along the alignment. Once sufficient track was constructed, our team used Herzog's 300-ton capacity ballast train to dump ballast down the track, making the placement process more efficient. For areas with subgrade, the ballast trucks placed ballast directly onto grade, followed with a blade to smooth and level out the ballast. Bottom ballast was trucked directly to the jobsite.

Design Team in real-time, and it allows more efficient and effective design and construction work planning.

Multi-Purpose Machines (MPMs)

MPMs, designed and built by Herzog, enable us to perform work activities including excavation, utility installation, wall construction, pile installation, signal installation, and other track construction needs directly from the existing track, during available work windows, using the MPM as a mobile work platform. Other equipment, including flatcars powered by Track Mobiles for delivering bridge materials and station components, ballast cars for placing ballast, low-railers, and hy-rail trucks for delivering materials and personnel, will be used to minimize the need for at-grade access from local streets.

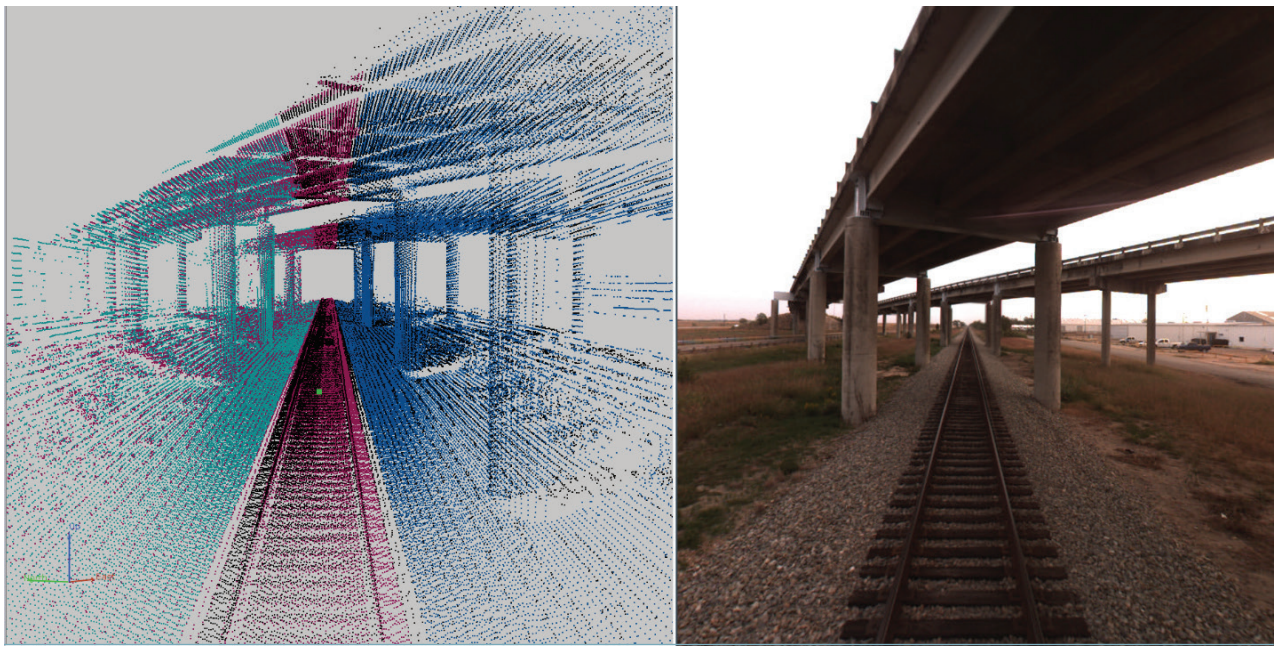


Figure 3.5-2. LiDAR Imaging Example. *GLX Constructors will use Herzog's LiDAR Imaging technology to meet or exceed our schedule's critical path activities by allowing for quick information processing and more proficient construction work planning.*

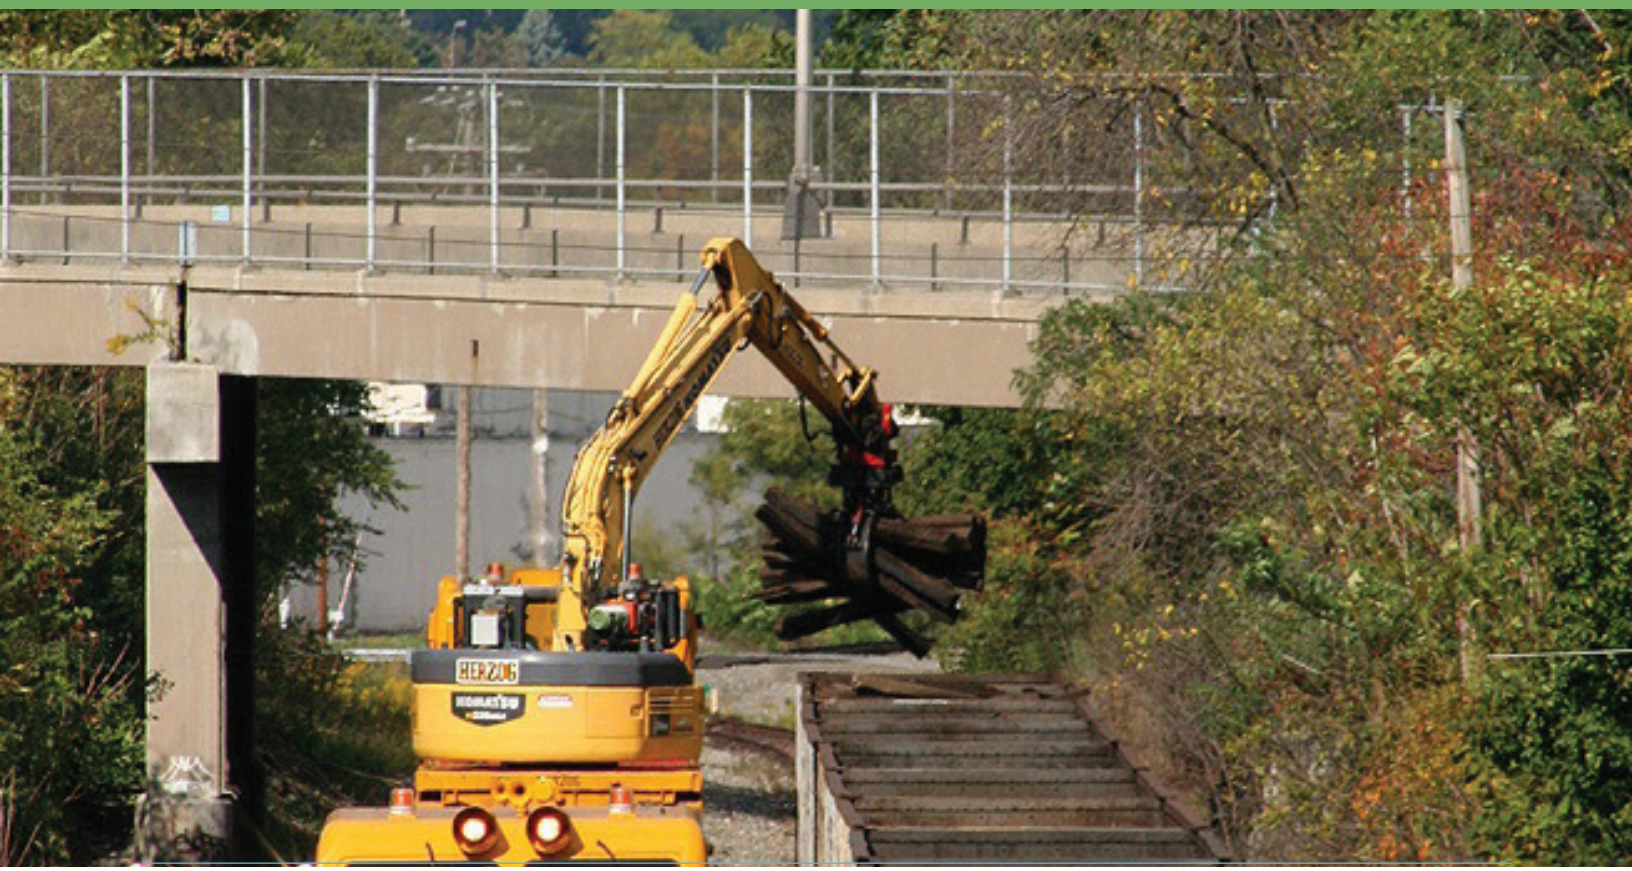


Figure 3.5-3. An Example of a Multi-Purpose Machine. *Using Herzog's MPMs will allow GLX Constructors to remain on schedule, even in the case of potential, unexpected delays. This poses a sincere benefit to the MBTA and the public realm.*

3.5.E GLX CONSTRUCTORS' APPROACH TO MANAGING INTERFACES

To successfully deliver a Project of the scope, size, and complexity as the Green Line Extension DB Project, managing interfaces is critical to have a seamless transition from the Design Phase to the Construction Phase of the Project. We have kept this critical transition in mind during the Proposal Phase, and we intend to mirror the same focus during the Execution Phase of the Project.

For example, we have developed the Project's Design Schedule to accommodate for the field's needs, such as procurement or testing and commissioning, interfaces demonstrated in Figure 3.5-4. We will schedule our earliest submittals to provide adequate procurement and construction times for the work items that define our critical path



The benefits of the MPMs were demonstrated on the Southwest Rail Line Project in Denver in 2008. Herzog was asked to assist in the cleanup and reconstruction after the derailment of freight cars in a shared freight/light rail corridor damaged several hundred feet of LRT track, walls, catenary poles, and associated improvements. To avoid the need to reconstruct the undamaged outbound LRT line, a track-based repair solution was required. Mounted on one of three Consolidated Mainline freight tracks and working under a Form B Order, MPMs worked in support of our construction crews to remove and rebuild the MSE wall, track, and other improvements in just 11 days. Our ability to work from existing commuter/freight tracks is a distinct advantage GLX Constructors offers the MBTA.

GV20170258-118.INDD

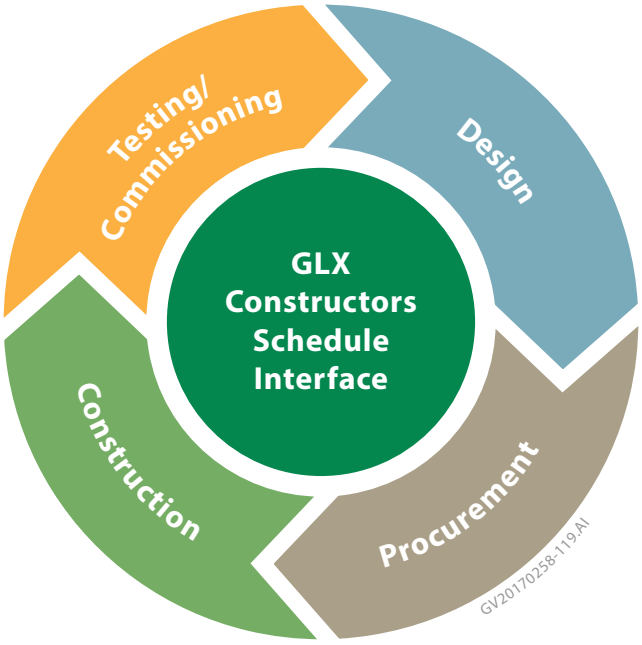


Figure 3.5-4. GLX Constructors' Schedule Interfaces. *To smooth the transitions between each critical Project Phase, our schedule takes into account information from design, procurement, construction, and testing and commissioning, which facilitates an efficient DB execution.*

Our construction project engineers interface with the Design and Scheduling Teams during the Design Phase to provide constructability, schedule reviews, and mitigation efforts. During the Project's Construction Phase, our project and field engineers will work with the Design Team to mitigate and resolve construction issues as they arise.

Similarly, our Scheduling Team interfaces with Construction and Procurement Teams when the design solution requires procuring materials and resources. These requirements are identified during the Design Phase and quantified by our project and field engineers to determine the procurement activities necessary to properly supply the materials. In turn, the procurement information is provided to the Scheduling Team to update the schedule accordingly.

3.5.F OTHER KEY ASPECTS OF SCHEDULE PROGRESSION AND CONTROL

Effective resource management is urgent to the success of a DB project. Our Project Manager, John West, and Construction Manager, Jamie Doyle, will lead GLX Constructors' resource management on a day-to-day basis. Our Project Controls Manager and Lead Scheduler will assist John and Jamie and maintain progress to look for early symptoms of schedule slippage.

For cost certainty and timely Project execution, GLX Constructors will determine the resources required and plan accordingly. We will develop

> **"On multiple DB projects, our team members have repeatedly proven that we are capable of managing interfaces, working together as designers and builders to execute projects that meet or exceed our clients' needs and expectations.**

action plans for directing and controlling resources of workers, equipment, and materials in a coordinated and timely manner.

When managing our Project resources, we will consider all scheduling activities, ranging from the daily adjustments necessary to keep a project running efficiently, to formally submitting a recovery schedule if required. By planning the Project with the foresight to schedule work on multiple fronts concurrently by various Project disciplines, we create the schedule flexibility to offset delay in one area by moving crews to other locations with minimal lost time. We can then focus on resolving the issue that is delaying one phase and, when it is resolved, recover the schedule by adding resources to complete the delayed activities.

Because schedule slippages can cause the critical path to shift, we will conduct weekly reviews of the critical path to help the Lead Scheduler and DB Management Team understand how priorities need to be modified. Action items developed during the schedule review meetings can include steps such as securing additional resources and material, shifting resources to other areas, initiating night shifts, or meeting with suppliers to update fabrication or delivery schedules.

Enforcing resource objectives is driven by close supervision, monitoring of progress against an updated plan, and escalating issues as necessary. See Section (w.) below for more information.

Overcoming Schedule Execution Challenges

On the Denver Eagle P3 Project, executed by Fluor, Balfour Beatty, and STV, there were numerous Schedule Execution Challenges that our team members overcame.

- **IDC Retrofits.** Designs for the bulk of already constructed bridge structures were determined to be noncompliant with AREMA per the Concession Agreement less than two years prior to the project's Revenue Service date. Resolutions varied from complete bridge demolition and replacement to field retrofits of various degrees, impacting a total of 15 bridge structures at a total cost of $25 million. All bridge structure remedial work was completed and the ensuing OCS and Train Control systems installation was compressed into 50 percent of the original schedule timeframe without delay to Revenue Service.
- **Third-Party Coordination.** Coordination and schedule challenges with a significant number of various third parties that maintained design acceptance authority within their jurisdiction, including DIA, FRA, multiple Denver area cities and counties, BNSF and UPRR railroads, Colorado PUC, and multiple utility companies involving approximately 1,000 conflicts.

GV20170258-118.INDD

- **Client Changes.** Over 180 client changes that modified the project scope by a value of 25 percent. Late client changes to the alignment less than two years prior to the project's Revenue Service date included the addition of a station and significant lengths of railway corridor protection barrier.
- **Rolling Stock Procurement.** Major rolling stock procurement of an original 50 vehicles with a client change for an additional 16 vehicles within two to three years of the project's Revenue Service date. All 66 rolling stock vehicles were scheduled and managed to on-time delivery in support of the Revenue Service date and ensuing operations period.

3.5.G MEASURE OF HOW MUCH WORK REMAINS TO COMPLETE AN ACCEPTABLE BASELINE SCHEDULE SUBMISSION AFTER NOTICE TO PROCEED

After Project Award and the Initial Baseline Schedule submission, GLX Constructors will conduct a schedule planning session with the MBTA to begin creating a more detailed design and construction schedule. We estimate our current schedule is approximately 30 percent complete in the level of detail that will ultimately be developed.

We will continue to develop the remaining detail as the permanent design progresses and completes, allowing for more clearly refined and updated construction activities. The Project schedule will be a living document as it progresses through the discipline interfaces in an update – progress – refine – update cycle, as illustrated in Figure 3.5-5. From this planning session and by expanding the current Initial Baseline Schedule, GLX Constructors will work with the MBTA to further develop the Baseline Schedule rev. 0.

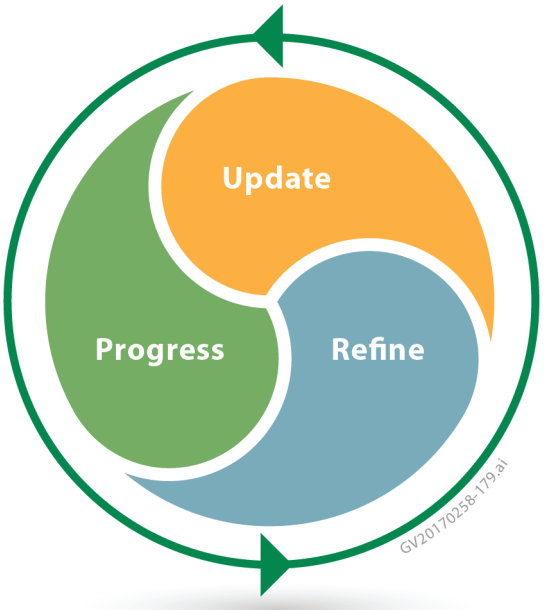


Figure 3.5-5. Cycle to Refine the Project Schedule. *Our Project Schedule is a versatile, living document that will adjust well to the needs and circumstances of the Project.*

Electronic Schedule Submission

The electronic schedule submission is included in our Proposal submission.

Sample Figure Requirements

Our electronic submission is cost-loaded with a sample figure of $100 million and included in our Proposal submission.

Roll Plan Hardcopy

The 36-inch roll plan hardcopy showing logic ties is included in our Proposal submission.

Sample Reports

The sample reports are included in our Proposal submission.

GLX Constructors' Detailed Narrative Description of our Proposed Project Approach

To properly estimate and develop a proposal for this Project, GLX Constructors has created an Initial Baseline Schedule that comprises design, procurement, construction, start-up testing, commissioning, and safety certification plus third-party activities. We have developed the Initial Baseline Schedule to meet or exceed contract requirements proposed by the MBTA, with a commitment to the timely completion of the Project Milestones outlined in Volume 1, Section 2.3, while maintaining minimal impacts to the public. Our schedule is aggressive; yet, because it is supported by our experience on similar, relevant rail and DB projects, our schedule is reliable, reasonable, and achievable.

Our schedule strategy is based on our familiarity with and understanding of the Green Line Extension DB Project; our relationship with the MBTA; and knowing how to best allocate the personnel, equipment, and materials necessary to complete the Project within the required timeframe. Our schedule is a direct result of developing an efficient rail construction sequencing approach to maximize work areas and minimize construction impacts to stakeholders, communities, and the traveling public. The Initial Baseline Schedule was developed by:

- Identifying activities required to support the optimized sequencing plan within each segment
- Identifying early design packages to support aggressive early construction
- Using our extensive design experience under the DB umbrella to create a detailed design schedule, including submittals and associated review times, to forecast a more accurate start of construction
- Applying quantities and proven execution history on production to identify durations associated with the installation

The key elements of the Project Schedule are design work, bridges (both roadway and railroad), drainage, utilities, MOT, subcontracts, rail schedules, geotechnical conditions, retaining and noise walls, and earthwork phasing requirements.

Effective Schedule/Cost Control

With the Baseline Schedule in place, GLX Constructors will use a system of long-range planning and short-term scheduling. The Baseline Schedule will be used for long-range planning and will be organized by a Work Breakdown Structure (WBS), which allows the schedule activities to be separated into schedules for design, pre-construction, and construction. The appropriate managers will develop detailed, short-range schedules for the performance of work within their responsibility areas.

Short-term scheduling will be the basis for the four-week look-ahead schedules. These short-range schedules will be integrated with our subcontractors' work scopes and individual activities. All activity progress will be reported to our Lead Scheduler, who will update the Project Baseline Schedule and analyze the schedule for performance against the Project's milestones.

The Baseline Schedule will be the basis for planning and monitoring the work progress and generating monthly invoices. A cost- and resource-loaded P6 schedule will be fully integrated with GLX Constructors' cost systems.

a. Critical Schedule Management Reporting

Our critical Schedule Management Reporting will include the following reports:

- Activity Reports with logic ties
- Bid Item Reports
- An Example of Craft Performance Curves Reports
- Look-Back and Look-Ahead Schedules
- Time-Location Diagrams

We have included example reports from each of these as Appendix 5 – Critical Schedule Management Report Examples.

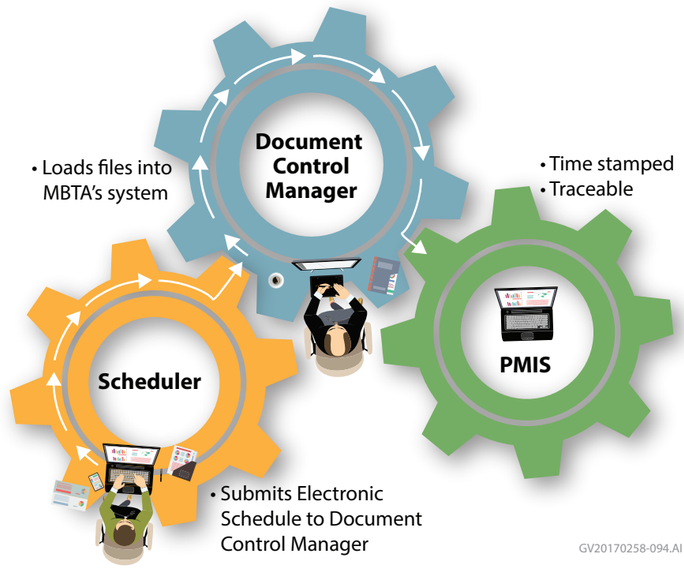


Figure 3.5-6. Document Control System. *Our document control process provides accountability and reliability from our Project Controls Team to the MBTA.*

b. Integration of Schedule Activities with Document Control

As part of our Document Management Plan, indicated in Figure 3.5-6, we intend to upload all native files into the MBTA's PMIS as required. These native Primavera files can then be uploaded into the MBTA's master schedule.

c. Description of the Schedule Updating Process that will be Implemented and detailed Daily, Weekly, and Monthly

On a daily basis, field engineers will provide information to our Lead Scheduler, who, in turn, will update the schedule based on these daily reports.

On a weekly basis, GLX Constructors will update the cumulative craft-hour performance curves, including self-perform and subcontractor hours within the schedule.

Our Project Controls Team will collect data from the field and analyze the findings. Any schedule impact that identified prior to data collection will be promptly communicated to the Lead Scheduler to be reflected in the schedule. A craft-hour analysis, requirements, and forecast will be updated on a monthly basis.

As required by the Technical Provisions, before the monthly progress meeting with the MBTA, our Project Controls team will submit a draft progress schedule to the MBTA for validation.

In addition to the Monthly Primavera Baseline Scheduling, we will submit a time-location diagram using TILOS, at a minimum of once every two months, as required in Volume 2, Section 2.4.6(h).

GLX Constructors will conduct a weekly meeting that provides a two-week look-back schedule and a four-week look-ahead schedule. Design discipline leads and construction discipline project engineers will lead their superintendents to develop these schedules weekly in conjunction with the Project Controls Leads. The four-week look-ahead schedules will be based on the Project Baseline Schedule, and provide day-to-day details. These details will include activities planned at both the end of the week and at the month-end closing.

Two weeks before our monthly submittal date, GLX Constructors will a conduct a meeting with the MBTA to discuss our monthly progress.

d. Description of How GLX Constructors' Project Manager, Design Manager, and Site Supervisors will use the Schedule Information

The Project Manager, Design Manager, and site supervisors will use the Baseline Schedule daily in the field to monitor all scheduled Project activities. The actual work progress will be documented, resource requirements will be evaluated, and critical work areas and tasks will be identified.

Updated critical paths and resource curves will be generated for review with the balance of the Project Team. Analyzing to-date performance compared to the Baseline Schedule provides the basis for decision making and correcting negative trends as required. The Project Team will analyze actual start and completion dates, cost value of work reported in place, activity physical percent completion, revised logic, remaining durations, craft-hour analysis and forecasting, the influence of change orders (if applicable), and other revisions.

In addition, GLX Constructors and the MBTA will review the look-back and look-ahead schedules; the time-location drawing schedule, or TILOS diagrams; craft-hour performance curves; craft-hour analysis curves showing craft-days of effort for each month; cash flow projection broken out by major cost centers (as determined by the MBTA); identified schedule delays; recovery plans; and detailed schedule narratives.

e. Description of How this Information will be Used in Project Management Meetings

During Project Management Meetings, GLX Constructors and the MBTA will review the progress, forecasted finish for in-progress activities, and re-forecasted early dates for activities planned during the next update period. We will review logic revisions or potential changes in the work, pre-existing activities, revisions due to unauthorized modifications, and recovery schedules. In addition, we will review any schedule delays – with an associated description of their extent and the cause for delay – that occurred since the previous progress schedule submittal. In addition, we will discuss the MBTA's responses to previous update review comments, recap progress, days gained or lost versus the previous progress schedule submittal, changes in resources, and identify delays, their extent, and causes.

From our schedule analysis, a monthly report consisting of the following elements will be developed and discussed at the monthly progress review meetings:

- **Bar Chart Schedules.** These will include the Level 1 summary schedule (total project and for construction only); near-term Level 3 detailed schedule (two months history and six months into the future); and comparison bar chart schedules with current early and late dates compared to the target date sets – again for the near-term as described herein.
- **Management Schedule Report.** This is a summary report presenting high-level Project information in a narrative, tabular format. At a minimum, it will include milestone statuses, highlights from the previous update, and any major issues or risks of which the Project Team needs to be aware.
- **Schedule Progress Narrative Report.** This is a narrative description of the Project's design and construction progress, schedule conformance to the specifications, any deviations from previous progress schedule and/or baseline schedule, and potential schedule issues.

> **"The Project Manager, Design Manager, and site supervisors will use the Baseline Schedule daily in the field to monitor all scheduled Project activities.**

> **We will build all fabricator and subcontractor construction activities into the Project Schedule, and their activities will be appropriately tracked like any other construction activity.**

- **Critical and Near-Critical Path Reports.** This report will call attention to the planned activities currently on the critical and near-critical paths, their progress to-date, as well as the variance from the planned schedule.

f. Description of How the Proposer Plans to Capture Work from Fabricators and Subcontractors

Effectively managing our fabricators and subcontractors is critical to maintaining our proposed Schedule. Our subcontractors' work scopes encompass track and guideway, Systems, traction power, rolling stock provisions, and operations and maintenance facilities. During the Proposal Phase, we relied on input from our dedicated subcontractors and fabricators, and we have incorporated the applicable information into our Initial Baseline Schedule.

GLX Constructors will be responsible for managing the progress and successful work completion performed by our fabricators and subcontractors. We will make certain their execution is properly coordinated with our design effort and self-performed construction activities. To properly integrate their activities into the Baseline Schedule, our subcontractors will be co-located and participate in the Project's early Design Phases.

We will build all fabricator and subcontractor construction activities into the Project Schedule, and their activities will be appropriately tracked like any other construction activity. We will hold pre-activity meetings prior to the start of a subcontractor's operation to make certain everyone involved understands the schedule and Project concerns. These meetings will include discussions about safety, environmental, quality, and local neighborhood constraints to make certain that all subcontractors comprehend the expectations and importance of the Project requirements. Subcontractors are to participate in the scheduling, planning on the job, and decisions affecting their work. Ongoing contact and weekly meetings with our fabricators will confirm timely updates to their respective activities are incorporated into our schedule.

The methodology of capturing work from our fabricators and subcontractors will be communicated to the MBTA during the Schedule Planning session with the MBTA within ten days after issuance of NTP.

g. Schedule Coding

GLX Constructors will use a combination of WBS and Activity Codes to organize the schedule and allow for a multifaceted approach to filtering and analyzing the data. We have incorporated the mandatory coding (Stand Cost Category) file as listed in Volume 2, Section 2.4.5(e). We have added additional coding to provide further granularity of activity groups. Our Project Activity Codes are depicted in Appendix 6 – GLX Activity Codes.

h. Work Breakdown Structure/Schedule Organization

The Project's WBS segments were developed as a collaborative effort between the Design Team and the Construction Team.

The WBS is a multi-level, hierarchical arrangement of the work to be performed on the Project. GLX Constructors has laid out the WBS to enable a straightforward identification of areas, segments, responsibilities, and work types within each segment, as shown in Appendix 7 – Work Breakdown Schedule. Our design has been further broken down into specific Design Packages to include clearing and grubbing, drainage, bridges, track, stations, utility bridges, viaducts, retaining walls, systems, roadway bridges, underpasses, community path, roadways, and fencing. Likewise, construction has been divided into smaller work types to include utilities, drainage, bridges, track, stations, systems, drainage, testing, and commissioning, to name a few.

i. Schedule Detail

Following Project Award, we will expand the Initial Baseline Schedule to encompass the full detailed scope of all design and construction activities. It will be used to actively progress the Project and manage our resources. During the Initial Baseline Schedule development, we convened our weekly TWGs to collaborate on the primary disciplinary aspects of the Project, such as utilities, track, drainage, structures, roadway, Systems, testing and commissioning, environmental, maintenance of traffic, and safety. TWGs integrated the participation of all disciplines, including O&M and Light Rail Vehicle (LRV) representatives, to vet issues on specific work elements. The TWGs' primary focus is to meet or exceed the overall Project goals by sharing best practices, determining priorities, identifying concerns, and resolving potential conflicts.

Information gathered during the TWGs formed the basis of our Initial Baseline Schedule and identified the complexities of the scope. The schedule is organized around logical, understandable, buildable units that enable both the MBTA and GLX Constructors to track and monitor design, procurement, and construction activities. This comprehensive schedule identifies critical path design activities to commence with DB Contract Execution and NTP, prioritizes long-lead items, takes advantage of innovations, and illustrates the plan to complete by the defined milestones dates. The schedule has a clear and concise level of detail demonstrating our complete scope understanding. Activity durations are based on consistent calculation methods. The level of detail demonstrating steps, with logic ties, required to complete the work while avoiding lags, is sufficient to control day-to-day activities.

j. Schedule Logic Competency

Our Initial Baseline Schedule represents the complete, logical time-phased representation of the Project plan. It covers the full scope and our understanding of the work execution. There are activity date constraints for the Project's start and finish milestones. The schedule logic is based on a determined sequence of work without resource constraints.

k. Organization and Management of the Critical Path and All of the Other Paths

The schedule's critical path identifies activities with the 0 float path from design, procurement, construction, startup, testing, commissioning, and safety certification. It will clearly identify critical submittals for the MBTA, third parties, and GLX Constructors. Daily monitoring of all schedule activities will alert GLX Constructors of any potential delay in critical path activities. If any critical path work is delayed more than 30 calendar days, we will submit written notice to the MBTA along with a recovery schedule for review and approval.

Managing All Other Paths. As with the critical path activities, we will continuously monitor the near-critical path activities, which have total float values between 1 and 20 days, to make certain that work is performed within the established time allotted. The Project Team's input and active participation is essential. Through daily monitoring, input, feedback, and activities review, we will make certain these near-critical activities do not become critical.

l. Cost Loading Example

Our $100 million cost loading example includes design, procurement, pre-construction, and construction activities. These activities include labor, equipment, materials, and subcontracts, and they are consistent with bid items. These activities have reasonable and proportional cost allocations to their respective activity and duration. With this cost loading spread, we will extract basic schedule information, categorize it in an Excel spreadsheet, and apply the summarized cost and revenue information of up to 20-30 summary categories each with revenue and cost information. Please see Appendix 8 – $100 Million Cost Loading Example.

m. Cash Flow Projections

We will perform cash flow projections monthly for the entire life of Project. Projections will include key input from Design Discipline Leads, Material Management, Contract Management, Scheduling, Construction, and Project Business Services. We will measure cash flow projections against early and late baseline revenue curves. These projections will be derived from the schedule data export into tabular format broken out by MBTA-determined major cost centers. Please see Appendix 9 – Cash Flow Projections.

n. Responsibility Coding

The schedule responsibility coding indicates the party responsible for executing a specific activity. We use responsibility coding to break down the work for our designers, subcontractors, suppliers, the MBTA, and other third parties. For the Project's responsibility codes, see Section (g.) above.

o. Design and Construction Submittal management, including, completeness of the list, preparation, review, approval, coding, prioritization, and relation to the start of work

We manage our design and construction submittals to the MBTA and third parties with a database that includes information as it pertains to coding, prioritization, and the relation to the start of the work. Using logical sequences, each submittal to either the MBTA or to third parties shows the subsequent, required review cycles and final submittals. Figures 3.5-7 and 3.5-8 illustrate the completeness of our submittal list, including preparation activities, subsequent reviews and approvals, and appropriate coding.

The prioritization of design activities has been determined by the critical path construction activities. Likewise, design packages have been prioritized accordingly as depicted in Figure 3.5-9. As shown in these three graphics, the Release for Construction (RFC) finish date designates the start of its related construction activity.

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility
Design		335	19-Apr-17	31-Jul-18	
DSUM	Design - SUMMARY	335	19-Apr-17	31-Jul-18	
Project Wide		335	19-Apr-17	31-Jul-18	
Pedestrian Bridge		148	19-Apr-17	10-Nov-17	
Pump Stations		148	19-Apr-17	10-Nov-17	
Railroad Bridge		148	19-Apr-17	10-Nov-17	
Roadway Bridges		160	19-Apr-17	28-Nov-17	
Stations		152	19-Apr-17	17-Nov-17	
Ball Square		152	19-Apr-17	17-Nov-17	
DSTASUM	Ball Square Station - Design SUMMARY	152	19-Apr-17	17-Nov-17	
DSTA110	Ball Square Station - Preliminary Design - Submit to MBTA for Review	40	19-Apr-17	14-Jun-17	DBF
DSTA120	Ball Square Station - Preliminary Design - MBTA Review & Comment	20	15-Jun-17	12-Jul-17	MBTA
DSTA130	Ball Square Station - Intermediate Design - Submit to MBTA for Review	20	13-Jul-17	10-Aug-17	DBF
DSTA140	Ball Square Station - Intermediate Design - MBTA Review & Comment	20	11-Aug-17	07-Sep-17	MBTA
DSTA150	Ball Square Station - RFC Design - Submit to MBTA for Review	20	08-Sep-17	05-Oct-17	DBF
DSTA160	Ball Square Station - RFC Design - MBTA Review & Comment	20	06-Oct-17	02-Nov-17	MBTA
DSTA170	Ball Square Station - RFC Design - Incorporate Comments, Release for Construction	5	03-Nov-17	09-Nov-17	DBF
DSTA180	Ball Square Station - Final Design Docs - Submit to MBTA for Review	5	03-Nov-17	10-Nov-17	DBF
DSTA190	Ball Square Station - Final Design Docs - MBTA Review & Approve	5	10-Nov-17	17-Nov-17	MBTA

Figure 3.5-7. Design and Construction Submittal Management to the MBTA.
Demonstrates responsibility coding submissions to the MBTA.

"We manage our design and construction submittals to the MBTA and third parties with a database that includes information as it pertains to coding, prioritization, and the relation to the start of the work.

Community Path		240	13-Dec-17	13-Nov-18	
DCMP100	Community Path - Design SUMMARY	224	13-Dec-17	13-Nov-18	DBF
DCMP110	Community Path - Preliminary Design - Submit to MBTA/3rd Party/Govt for Review	20	13-Dec-17	24-Jan-18	DBF
DCMP120	Community Path - Preliminary Design - MBTA/3rd Party/Govt Review & Comment	40	25-Jan-18	21-Mar-18	MBTA3rd
DCMP130	Community Path - Intermediate Design - Submit to MBTA/3rd Party/Govt for Review	10	22-Mar-18	04-Apr-18	DBF
DCMP140	Community Path - Intermediate Design - MBTA/3rd Party/Govt Review & Comment	40	05-Apr-18	01-Jun-18	MBTA3rd
DCMP200	Community Path - Pre-RFC Design - Submit to MBTA/3rd Party/Govt for Review	10	04-Jun-18	15-Jun-18	DBF
DCMP210	Community Path - Pre-RFC Design - MBTA/3rd Party/Govt Review & Comment	40	18-Jun-18	13-Aug-18	MBTA3rd
DCMP150	Community Path - RFC Design - Submit to MBTA/3rd Party/Govt for Review	10	14-Aug-18	27-Aug-18	DBF
DCMP160	Community Path - RFC Design - MBTA/3rd Party/Govt Review & Comment	40	27-Aug-18	23-Oct-18	MBTA3rd
DCMP170	Community Path - RFC Design - Incorporate Comments, Release for Construction	5	23-Oct-18	30-Oct-18	DBF
DCMP180	Community Path - Final Design Docs - Submit to MBTA for Review	5	30-Oct-18	06-Nov-18	DBF
DCMP190	Community Path - Final Design Docs - MBTA Review & Approve	5	06-Nov-18	13-Nov-18	MBTA3rd

Figure 3.5-8. Design and Construction Submittal Management to the MBTA and Third Parties. *Demonstrates responsibility coding submissions to the MBTA and third parties.*

p. Design Schedule Management and Activity Detail

For detail about our Lead Designer's schedule management and activities, such as responsibilities, logic, and resources, see Section (o.) above.

In each of our Design Packages, the specific activities are logically linked and coded to the responsible party. Resources are assigned as shown in our $100 million cost-loaded schedule sample in order to carefully track cost and schedule adherence.

q. Resource Loading (Labor/Crews and Equipment Detail/Activities)

All scheduled activities will be resource-loaded at a sufficient level to support generating progress curves. The resources will be based on our approved, logic-driven schedule, and quantities from our estimate. We will organize crews according to the resources available, scheduled time of work activities, and work restrictions, such as track access, weather, work hours/day, and the like. This will enable resource leveling that will optimize our resources while meeting or exceeding the schedule requirements.

Additionally, as discussed in Section 3.5.D., the resource-loaded Primavera schedule will be demonstrated in a TILOS time-location diagram that depicts the planned progression of each of the major crews, over-laid with the Project stationing graphic.

r. Production Rate Basis and Relationship to Estimate Details/ Subcontractor Pricing

Our detailed production rate basis is derived from the experience of the four contracting partners' experience working in an active rail corridor. We have linked our crew-based estimate, which also incorporates our subcontractor pricing, to our Primavera P6 schedule. It will be refined upon contract award and will form the basis of the productivities used in our schedule.

Activity ID	Activity Name	Original Duration	Start	Finish
Design		332	11-Dec-17	19-Mar-19
DESFMS	Design Complete	0		11-Dec-17
Project Wide		316	11-Dec-17	19-Mar-19
Documentation / Pre-Design Plan		316	11-Dec-17	19-Mar-19
Earthwork	Clearing & Grubbing	178	11-Dec-17	15-Aug-18
Community Path		241	11-Dec-17	12-Nov-18
Track Drainage		158	11-Dec-17	18-Jul-18
Main Drainage		222	11-Dec-17	16-Oct-18
Retaining Walls		225	11-Dec-17	19-Oct-18
Noise Walls		158	11-Dec-17	18-Jul-18
Fencing		158	11-Dec-17	18-Jul-18
Viaducts		332	11-Dec-17	19-Mar-19
Lechmere (LEV)		244	11-Dec-17	15-Nov-18
Medford (MBV)		316	11-Dec-17	25-Feb-19
Union Square EB (UEV)		332	11-Dec-17	19-Mar-19
Union Square WB (UWV)		316	11-Dec-17	25-Feb-19
Railroad Bridge		180	11-Dec-17	17-Aug-18
Washington St Bridge		180	11-Dec-17	17-Aug-18
Roadway Bridges		286	11-Dec-17	14-Jan-19
Broadway (Bridge No. S-17-013)		286	11-Dec-17	14-Jan-19
Medford St (Somerville) (Bridge No. S-17-007)		213	11-Dec-17	03-Oct-18
Cedar St (Somerville) (Bridge No. S-17-012)		158	11-Dec-17	18-Jul-18
College Ave (Medford) (Bridge No. M-12-012)		158	11-Dec-17	18-Jul-18
Lowell St (Somerville) (Bridge No. S-17-011)		211	11-Dec-17	01-Oct-18
School St (Somerville) (Bridge No. S-17-008)		211	11-Dec-17	01-Oct-18
Walnut St (Somerville) (Bridge No. S-17-006)		211	11-Dec-17	01-Oct-18
Stations		281	11-Dec-17	07-Jan-19
Magoun Square		281	11-Dec-17	07-Jan-19
East Somerville		281	11-Dec-17	07-Jan-19
Ball Square		206	11-Dec-17	25-Sep-18
College Ave		206	11-Dec-17	25-Sep-18
Gilman Square		206	11-Dec-17	25-Sep-18
Lechmere Relocation		206	11-Dec-17	25-Sep-18
Union Square		206	11-Dec-17	25-Sep-18
Track		280	11-Dec-17	04-Jan-19
Commuter Lines		280	11-Dec-17	04-Jan-19
Medford, VMF, Union Square, and Yard Lines		280	11-Dec-17	04-Jan-19
Utility Bridges		206	11-Dec-17	25-Sep-18
Underpasses		206	11-Dec-17	25-Sep-18
Walnut St		206	11-Dec-17	25-Sep-18
Medford St		206	11-Dec-17	25-Sep-18
School St		206	11-Dec-17	25-Sep-18
Lowell St Modification		206	11-Dec-17	25-Sep-18
Systems		206	11-Dec-17	25-Sep-18
Overhead Contact Systems		206	11-Dec-17	25-Sep-18
Communications		206	11-Dec-17	25-Sep-18
Traction Power Systems		206	11-Dec-17	25-Sep-18
Signaling		206	11-Dec-17	25-Sep-18
Utilities		281	11-Dec-17	07-Jan-19
Utility Bridges (Broadway & Medford)		242	11-Dec-17	13-Nov-18
VMF		206	11-Dec-17	25-Sep-18
Transportation Office Building		206	11-Dec-17	25-Sep-18
Vehicle Maintenance Building		206	11-Dec-17	25-Sep-18
Pump Stations		161	11-Dec-17	23-Jul-18
Washington St (B)		158	11-Dec-17	18-Jul-18
Red Bridge		161	11-Dec-17	23-Jul-18
Washington St (A)		158	11-Dec-17	18-Jul-18
Pedestrian Bridge		158	11-Dec-17	18-Jul-18
College Ave		158	11-Dec-17	18-Jul-18
Roadways & Traffic Improvements		158	11-Dec-17	18-Jul-18

Figure 3.5-9. Design Package Priorities. *We have prioritized our design packages according to critical path construction activities.*

s. Considerations for Necessary Steps Needed, Prior to the Start the Physical Work Such as Special Permits and Approvals

GLX Constructors has carefully considered the necessary steps needed prior to breaking ground, including permits, plans, studies, and approvals. Every required permit (obtained by GLX Constructors, the MBTA, and any other third party), approvals, studies, meetings, plans, protocols, SOPs, and statements of qualifications are listed in the Initial Baseline Schedule within the Contract Deliverables/Submittals and Pre-Construction sections.

t. Construction Phasing and Traffic Management Planning

An essential element of all roadway and bridge construction is providing for the safe passage of vehicles, pedestrians, cyclists, and transit operators through the work zone. This includes persons with disabilities in accordance with the Americans with Disabilities Act (ADA) of 1990. Equally as important to the mobility of road users is the safety and protection of the construction workers performing tasks within the work space.

Consistent with MBTA/MassDOT policy, the reconstruction of the Project's roadways and bridges will include a variety of Temporary Traffic Control (TTC) measures depending on the particular work element being performed, the expected duration, and the time of day. When the normal function of the roadway, bridge, sidewalk, bike path, or transit way are suspended for reconstruction, TTC planning provides for the appropriate notification to the public, and for the safety and continuity of movement along roadways while maintaining access to private property and commercial businesses.

GLX Constructors will be responsible for managing the progress and successfully completing Traffic Management Plans. Design activities for traffic management plans will be included in the roadway bridge and railroad bridge design activities to make certain traffic management plans will properly accompany the RFC plans.

Design activities will be included for the submission of traffic management plans for the closures of the Medford Street Bridge, School Street Bridge, Broadway Bridge, and the closure of Washington Street between Joy Street and Tufts Street for the reconstruction of Washington Street and the Railroad Bridge crossing Washington Street to the City of Somerville traffic engineer for prior review and approval. Design activities will be included for the submission of the Traffic Management Plan for the staged construction across the exiting College Avenue Bridge and the intersection of College Avenue and Boston Street.

TTC plans and the variety of devices used for the Project will be consistent with local and industry-wide standards. Public outreach and coordination with the cities of Medford, Somerville, and Cambridge will be important for the approval of the TTC plans and also for coordination of adjacent construction projects, such as the city of Boston's interim work at Sullivan Square by the Wynn casino; MassDOT's planned rehabilitation to the Maffa Way and Mystic Avenue bridges; and the ongoing work on the Longfellow Bridge, for example.

The FHWA's Manual on Uniform Traffic Control Devices (MUTCD), includes the following guidance:

The MUTCD and MassDOT's Standard Details and Drawings for the Development of TTC Plans will offer the primary guidance on the TTC. Unknown at this time are the means and methods for the work element, road conditions, duration of operations, and physical constraints to the work area. However, the MUTCD and MassDOT standard drawings cover the majority of situations likely to be encountered, such as lane closures, merges, detours, sidewalk and bike lane construction, and will be engineered to fit the specific situation. Special attention will be paid to non-motorized users and persons with disabilities, as all temporary routes must meet ADA guidelines and allow for bicycle travel.

The Project will closely coordinate with transit service providers for the temporary relocation of transit stops and/or bus shelters as needed for construction. A project of this magnitude will also include a robust public outreach component to inform residents and road users of the reconstruction work and planned traffic mitigation including notification via email/text, navigations services (Waze, etc.), and other social media platforms.

GLX Constructors will build MOT activities into the Project Schedule and the activities will be tracked as any other construction activity.

GLX Constructors has carefully considered the necessary construction phasing and traffic management planning to include the appropriate activities for weekly planning and proper execution. Our plan minimizes disruption to the traveling public (rail, pedestrian, vehicular), as shown below.

"A project of this magnitude will also include a robust public outreach component to inform residents and road users of the reconstruction work and planned traffic mitigation including notification via email/text, navigations services (Waze, etc.), and other social media platforms.

> Consideration for road user safety, worker and responder safety, and the efficiency of road user flow is an integral element of every TTC zone, from planning through completion. A concurrent objective of the TTC is the efficient construction and maintenance of the highway and efficient resolution of traffic incidents.

WASHINGTON ST – TRAFFIC DETOURS – Pending city approval. Check MBTA Bus Routes

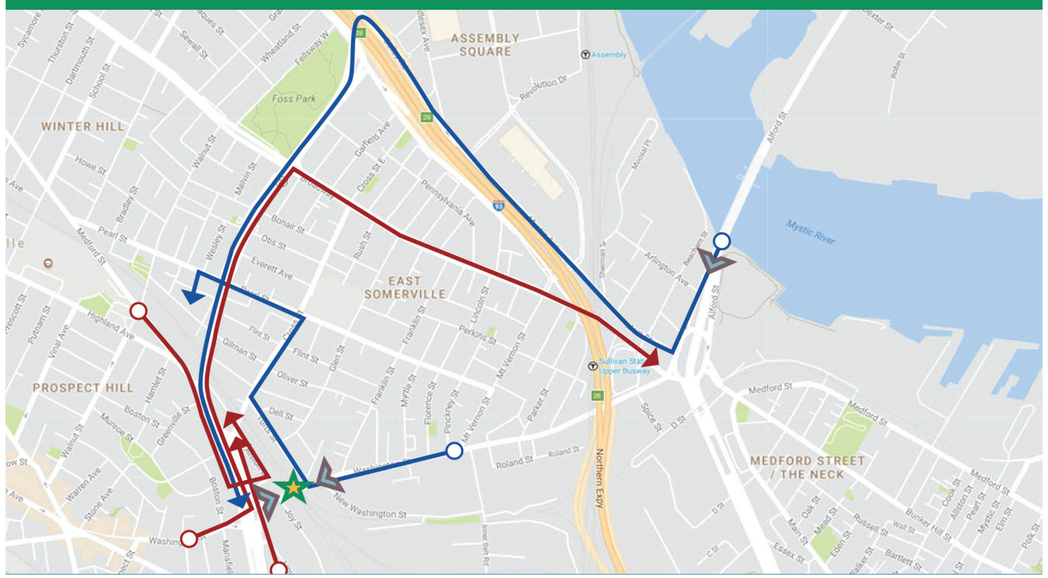


Figure 3.5-10. Washington Street Bridge. *The railroad bridge over Washington Street shall be demolished and replaced with a structure which accommodates two proposed System tracks, two existing Railroad tracks, one proposed maintenance track, the Community Path, and new approach slabs. The vertical clearance between Washington Street and the proposed structure shall be increased from 13'-10" to 14'-6" at the minimum. Demolition and removal of the existing bridge and its approach slabs is included in this scope.*

WASHINGTON ST – Local traffic access – Joy Street businesses- detour at road barricade

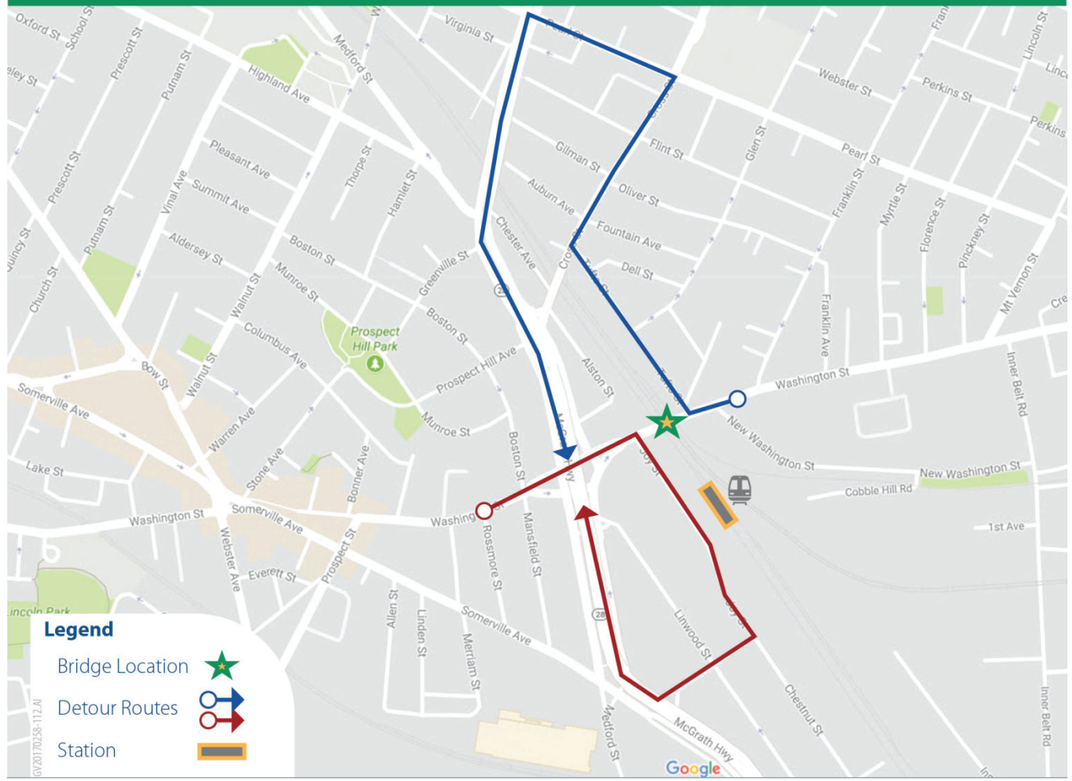


Figure 3.5-11. Washington Street Bridge. *The railroad bridge over Washington Street shall be demolished and replaced with a structure which accommodates two proposed System tracks, two existing Railroad tracks, one proposed maintenance track, the Community Path, and new approach slabs. The vertical clearance between Washington Street and the proposed structure shall be increased from 13'-10" to 14'-6" at the minimum. Demolition and removal of the existing bridge and its approach slabs is included in this scope.*

u. Payment/Invoicing (relationship to the schedule and bid values)

The cost-loaded schedule determines the monthly activities that must be completed to achieve the Project milestones that maintain the tempo of our schedule. We will base our invoices on the percentage of earned work activities completed within the allotted time frame.

v. Demonstration of the Chosen Scheduling Software Capabilities

GLX Constructors will employ the Primavera P6 Software, an industry standard that is compatible with the MBTA's Primavera Software. The functionality of the Primavera Software includes full import and export capabilities to and from multiple versions of Primavera and with TILOS, our time-location diagram software. Our staff is highly experienced with the functionality of this software.

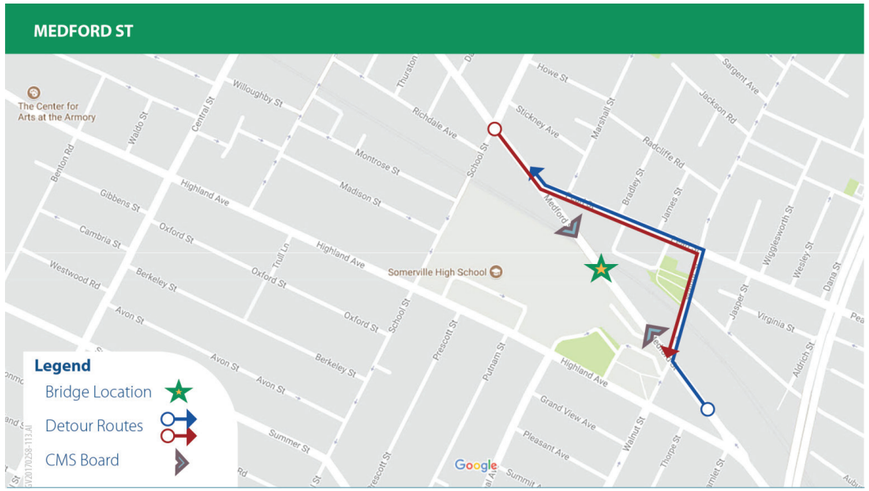


Figure 3.5-12. Medford Street (Somerville) (Bridge No. S-17-007). *An underpass shall be provided at the Medford Street Bridge behind the south abutment. The underpass shall be wide enough to accommodate one System track and associated dynamic clearance envelope (See Section 10), a separation wall with fence, and a minimum 8'-0" clear width for the Community Path.*



Figure 3.5-13. School Street (Somerville) (Bridge No. S-17-008). *The School Street Bridge shall be supported in place and the south abutment replaced. Behind the new abutment, an underpass structure shall be constructed to accommodate a new System track.*

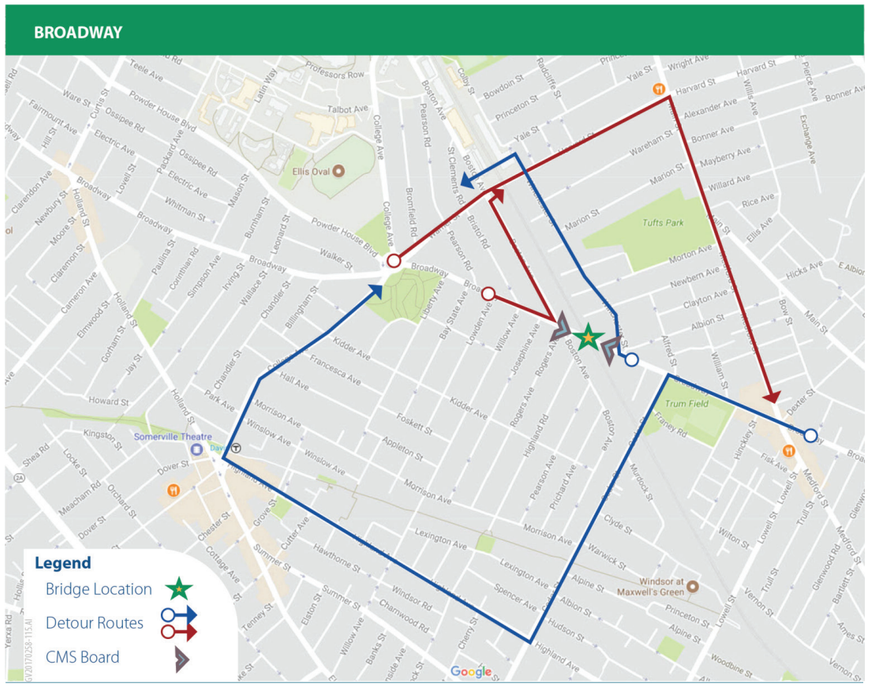


Figure 3.5-14 Broadway Bridge (Bridge No. S-17-013). *The existing Broadway Bridge shall be demolished and a new bridge shall be constructed whose clear span is long enough to accommodate the two proposed System tracks and two Railroad tracks in accordance with Section 10.*

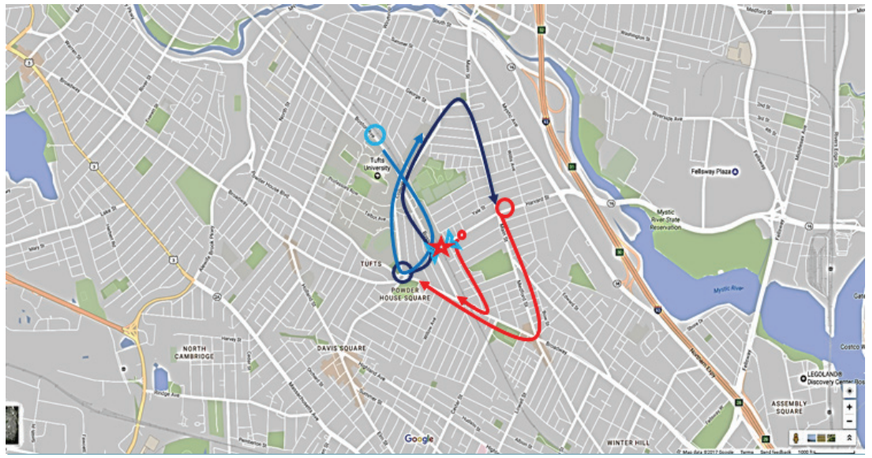


Figure 3.5-15. Harvard Street Rail Bridge. *New approach slabs shall be provided to accommodate the existing bridge deck previously complete. The new approach slabs shall run the full width of the new structures and accommodate all drainage and utility requirements as outlined in Section 7.3 and Section 7.4.*

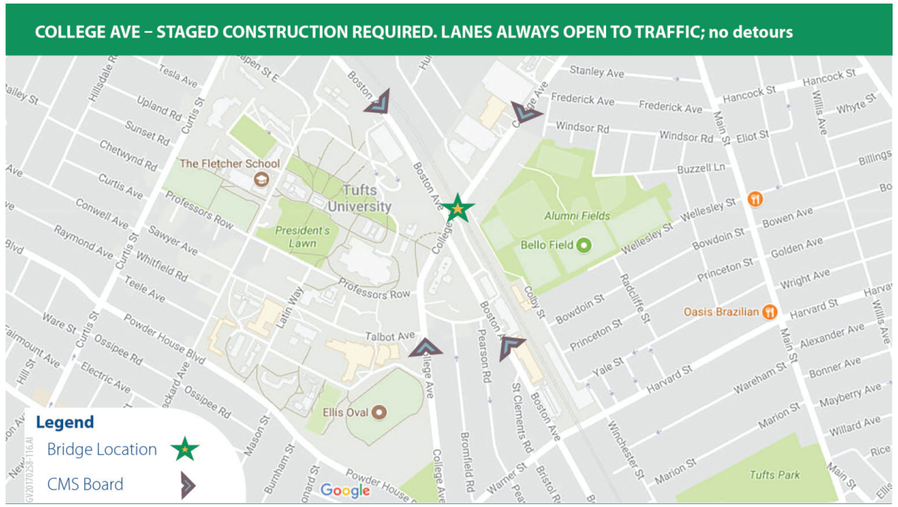


Figure 3.5-16. College Avenue (Medford) (Bridge No. M-12-012). *The sidewalk on the north side of the existing bridge shall be removed and this space shall be replaced with 10'-6" right turn lane. The existing College Avenue Bridge shall be modified as necessary to accommodate (from South to North) a 6'-6" sidewalk, 1'-0" shoulder, 12'-2" lane, an 11' lane, a 10'-6" right turn lane, and a 1' shoulder and the two existing bridge rails on both sides. The total width of the existing structure shall be maintained. A separate pedestrian bridge with a minimum clear path width of 12'-0" shall be constructed north of the MWRA utility support structure that is adjacent to the College Avenue Bridge to accommodate both pedestrian and bicycle traffic over the tracks. See Section 8.6 for further information.*

w. How Activities will be Rescheduled to Achieve Schedule Recovery Objectives and How Objectives will be Enforced

Rescheduling critical and near-critical activities will be an iterative process with the MBTA and our DB Management Team based on progress reporting from field supervision. The process to reschedule these activities is:

1. Compare to the Baseline Schedule to the previous periodic updated schedule to determine variances .
2. Review variances with our DB Management Team to establish workarounds or a recovery schedule for approval.
3. In Schedule Review Meetings with the MBTA, describe any resource changes and identify delays, their extent, and causes.
4. Itemize and explain changes in activities, calendar, and logic ties, schedule recovery plans, and GLX Constructors-initiated revisions.
5. Incorporate approval from the MBTA.

To recover the schedule, we will add additional equipment and labor resources as needed. Specifically, field managers will be held accountable for the schedule recovery. Please see Section 3.5.F for more information.

x. Innovative Approaches That Have Been Used and Will Be Used For Schedule Controls


For schedule controls, GLX Constructors will utilize TILOS, the industry-leading time-location diagram software, which highlights the number of crews required, concurrent work activities, resource utilization, flagger requirements for safety control, and risk management.

GLX Constructors has created an Initial Baseline Schedule that has been jointly prepared and agreed to by all discipline managers. It expresses realistic expectations of the schedule of work to be completed by all team members and third parties during the course of concurrent Project activities. We are confident that our Schedule, which meets all of the MBTA's milestone requirements, will provide the MBTA and GLX Constructors with the detailed information necessary to effectively manage the Green Line Extension DB Project.

APPENDIX 2

Initial Baseline Schedule Critical Path

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
Green Line Extension Initial Baseline Schedule 20170908		1052	28-Sep-17	08-Oct-21	0
Milestones		1052	28-Sep-17	08-Oct-21	0
PWMS011	Financial Proposal Submittal	0		28-Sep-17	0
PWMS010	Technical Proposal Submittal	0		28-Sep-17	0
PWMS020	MassDOT Announce Preferred Proponent	0		17-Nov-17*	0
PWMSAWD	Project Award	0		27-Nov-17	0
PWMSNTP	DB Contract Execution and NTP	0		12-Dec-17*	0
PWMS006	Plaza Work Complete in Plaza Easement Areas	0		21-Aug-20*	0
PWMS005	VMF - Functionally Complete & Ready for MBTA Operational Testing	0		30-Sep-20*	0
PWMS004a	New Green Line (1st Branch) Functionally Complete, Ready for Integrated Testing	0		22-Oct-20*	0
PWMS004b	New Green Line (1st Branch) Ready for MBTA Demonstration Testing	0		24-Dec-20*	0
PWMS003a	New Green Line (2nd Branch) Functionally Complete, Ready for Integrated Testing	0		30-Dec-20*	0
PWMS003b	New Green Line (2nd Branch) Ready for MBTA Demonstration Testing	0		26-Feb-21*	0
PWMS004c	New Green Line (1st Branch) Open to Revenue Service	0		20-Apr-21*	0
PWMS003c	New Green Line (2nd Branch) Open to Revenue Service	0		08-Jun-21*	0
PWMS002	Contract Substantial Completion	0		11-Aug-21*	0
PWMS150	Notice of Final Completion - MBTA Review & Approve	15	20-Sep-21	08-Oct-21	0
PWMS001	MBTA Issue Certificate of Final Completion - Contract Final Acceptance	0		08-Oct-21*	0
Design		317	12-Dec-17	27-Feb-19	0
Viaducts		287	12-Dec-17	16-Jan-19	0
Lechmere (LEV) Pkg 2		287	12-Dec-17	16-Jan-19	0
DLEV765	Lechmere Viaduct (LEV) Pkg 2 - Preliminary Design - Submit to MBTA for Review	60	12-Dec-17	20-Mar-18	0
DLEV760	Lechmere Viaduct (LEV) Pkg 2 - Preliminary Design - MBTA Review & Comment	20	21-Mar-18	18-Apr-18	0
DLEV745	Lechmere Viaduct (LEV) Pkg 2 - Pre-RFC Design - Submit to MBTA for Review	60	19-Apr-18	13-Jul-18	0
DLEV740	Lechmere Viaduct (LEV) Pkg 2 - Pre-RFC Design - MBTA Review & Comment	20	16-Jul-18	10-Aug-18	0
DLEV755	Lechmere Viaduct (LEV) Pkg 2 - RFC Design - Submit to MBTA for Review	55	13-Aug-18	26-Oct-18	0
DLEV750	Lechmere Viaduct (LEV) Pkg 2 - RFC Design - MBTA Review & Comment	20	29-Oct-18	28-Nov-18	0
DLEV770	Lechmere Viaduct (LEV) Pkg 2 - RFC Design - Incorporate Comments, Release for Construc	35	29-Nov-18	16-Jan-19	0
Retaining & Noise Walls		192	12-Dec-17	05-Sep-18	0
Retaining Walls (Early)		192	12-Dec-17	05-Sep-18	0
DRTW240	Retaining Walls (Early) - Preliminary Design - Submit to MBTA for Review	40	12-Dec-17	20-Feb-18	0
DRTW250	Retaining Walls (Early) - Preliminary Design - MBTA Review & Comment	20	21-Feb-18	20-Mar-18	0
DRTW280	Retaining Walls (Early) - Pre-RFC Design - Submit to MBTA for Review	40	22-Mar-18	22-May-18	0
DRTW290	Retaining Walls (Early) - Pre-RFC Design - MBTA Review & Comment	20	23-May-18	20-Jun-18	0
DRTW320	Retaining Walls (Early) - RFC Design - Submit to MBTA for Review	25	21-Jun-18	25-Jul-18	0
DRTW330	Retaining Walls (Early) - RFC Design - MBTA Review & Comment	20	26-Jul-18	22-Aug-18	0
DRTW230	Retaining Walls (Early) - RFC Design - Incorporate Comments, Release for Construction	10	23-Aug-18	05-Sep-18	0
Track		150	12-Dec-17	09-Jul-18	0
Medford, Commuter, Union Square		150	12-Dec-17	09-Jul-18	0
DRWB2490	Medford & Union Line Track - Preliminary Design - Submit to MBTA for Review	65	12-Dec-17	28-Mar-18	0
DRWB2500	Medford & Union Line Track - Preliminary Design - MBTA Review & Comment	20	29-Mar-18	26-Apr-18	0
DRWB2510	Medford & Union Line Track - Intermediate Design - Submit to MBTA for Review	50	30-Apr-18	09-Jul-18	0
Drainage		226	12-Dec-17	23-Oct-18	0
Drainage - Watershed 2		201	12-Dec-17	18-Sep-18	0
DDRA430	Drainage W2 - Preliminary Design - Submit to MBTA for Review	50	12-Dec-17	06-Mar-18	0
DDRA425	Drainage W2 - Preliminary Design - MBTA Review & Comment	20	07-Mar-18	03-Apr-18	0
DDRA400	Drainage W2 - Pre-RFC Design - Submit to MBTA for Review	30	04-Apr-18	21-May-18	0
DDRA395	Drainage W2 - Pre-RFC Design - MBTA Review & Comment	20	21-May-18	19-Jun-18	0
DDRA420	Drainage W2 - RFC Design - Submit to MBTA for Review	25	19-Jun-18	24-Jul-18	0
DDRA415	Drainage W2 - RFC Design - MBTA Review & Comment	20	24-Jul-18	21-Aug-18	0
DDRA435	Drainage W2 - RFC Design - Incorporate Comments, Release for Construction	20	21-Aug-18	18-Sep-18	0
Drainage - Watershed 3		226	12-Dec-17	23-Oct-18	0
DDRA480	Drainage W3 - Preliminary Design - Submit to MBTA for Review	60	12-Dec-17	20-Mar-18	0
DDRA475	Drainage W3 - Preliminary Design - MBTA Review & Comment	20	21-Mar-18	18-Apr-18	0
DDRA450	Drainage W3 - Pre-RFC Design - Submit to MBTA for Review	40	19-Apr-18	15-Jun-18	0
DDRA445	Drainage W3 - Pre-RFC Design - MBTA Review & Comment	20	18-Jun-18	16-Jul-18	0

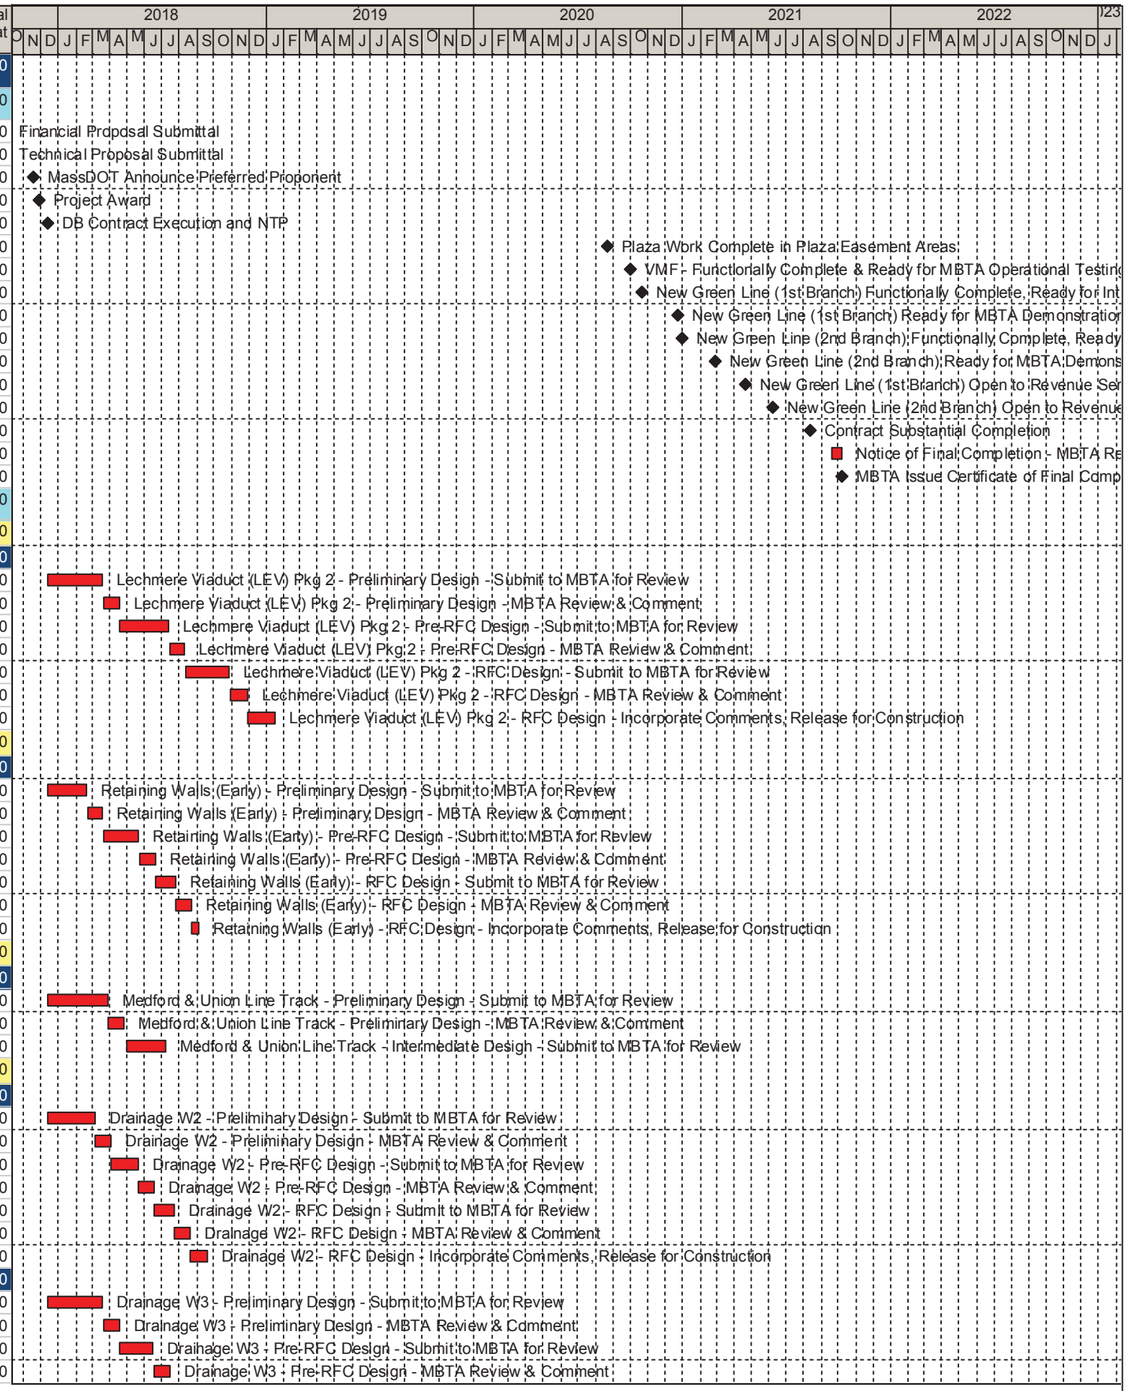

Actual Work | Critical Remaining Work | Remaining Work | Milestone


GLX CONSTRUCTORS

Green Line Extension Detail CPM Schedule

Page: 1 of 5 Data Date: 28-Sep-17 Print: 19-Sep-17

GV20170258-283.pdf

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
DDRA470	Drainage W3 - RFC Design - Submit to MBTA for Review	30	17-Jul-18	27-Aug-18	0
DDRA465	Drainage W3 - RFC Design - MBTA Review & Comment	20	27-Aug-18	25-Sep-18	0
DDRA485	Drainage W3 - RFC Design - Incorporate Comments, Release for Construction	20	25-Sep-18	23-Oct-18	0
Railroad Bridges		218	30-Apr-18	27-Feb-19	0
Washington St Bridge		218	30-Apr-18	27-Feb-19	0
DRRBB3125	Washington St RR BR - Pre-RFC Design - Submit to MBTA for Review	55	30-Apr-18	16-Jul-18	0
DRRBB3130	Washington St RR BR - Pre-RFC Design - MBTA Review & Comment	40	16-Jul-18	11-Sep-18	0
DRRBB3135	Washington St RR BR - RFC Design - Submit to MBTA for Review	55	11-Sep-18	27-Nov-18	0
DRRBB3140	Washington St RR BR - RFC Design - MBTA Review & Comment	20	27-Nov-18	26-Dec-18	0
DRRBB3145	Washington St RR BR - RFC Design - Incorporate Comments, Release for Construction	45	26-Dec-18	27-Feb-19	0
VMF		166	12-Dec-17	31-Jul-18	0
Vehicle Maintenance Building		166	12-Dec-17	31-Jul-18	0
DVMB105	Vehicle Maintenance Bldg - Preliminary Design - Submit to MBTA for Review	85	12-Dec-17	30-Apr-18	0
DVMB110	Vehicle Maintenance Bldg - Preliminary Design - MBTA Review & Comment	20	30-Apr-18	29-May-18	0
DVMB115	Vehicle Maintenance Bldg - Intermediate Design - Submit to MBTA for Review	45	29-May-18	31-Jul-18	0
Procurement		455	12-Jul-18	08-Apr-20	0
Special Trackwork		365	12-Jul-18	04-Dec-19	0
PRSTRK130	Special Trackwork - Prepare & Submit	30	12-Jul-18	23-Aug-18	0
PRSTRK110	Special Trackwork - MBTA Review & Approve	30	24-Aug-18	05-Oct-18	0
PRSTRK120	Special Trackwork - Place Order	2	08-Oct-18	09-Oct-18	0
PRSTRK100	Special Trackwork - Fabricate & Deliver	260	10-Oct-18	04-Dec-19	0
Maintenance Facility Equipment		441	31-Jul-18	08-Apr-20	0
PRMFE130	Maintenance Facility Equipment - Prepare & Submit	30	31-Jul-18	14-Sep-18	0
PRMFE110	Maintenance Facility Equipment - MBTA Review & Approve	30	14-Sep-18	26-Oct-18	0
PRMFE120	Maintenance Facility Equipment - Place Order	2	29-Oct-18	30-Oct-18	0
PRMFE100	Maintenance Facility Equipment - Fabricate & Deliver	325	31-Oct-18	08-Apr-20	0
Pre-Construction		120	30-Jan-18	25-Jul-18	0
Studies		120	30-Jan-18	25-Jul-18	0
PSTU170	Pre-Construction - Geotechnical Drilling	120	30-Jan-18	25-Jul-18	0
Construction		583	03-Aug-18	27-Oct-20	0
Project Wide		516	03-Aug-18	27-Oct-20	0
CMOTS110	Project Wide Construction - MOT Support	516	03-Aug-18	27-Oct-20	0
CSURV110	Project Wide Construction - Construction Surveying	516	03-Aug-18	27-Oct-20	0
CLDNS110	Project Wide Construction - Landscaping throughout Transit Corridor	516	03-Aug-18	27-Oct-20	0
Segment 1		70	06-Sep-18	26-Dec-18	0
Retaining & Noise Walls		70	06-Sep-18	26-Dec-18	0
C1RNW110	Retaining Wall ME-3 (366+50 - 374+00) - Install Soldier Pile Wall	70	06-Sep-18	26-Dec-18	0
Segment 2		150	18-Sep-18	17-May-19	0
Earthwork, Clearing & Grubbing		51	04-Oct-18	26-Dec-18	0
C2CGE110	Earthwork / Access Road - Segment 2	51	04-Oct-18	26-Dec-18	0
Drainage		40	18-Sep-18	19-Nov-18	0
C2DRA125	Main Drainage - Excavate & Install	40	18-Sep-18	19-Nov-18	0
Retaining & Noise Walls		89	02-Jan-19	17-May-19	0
C2RNW165	Retaining Wall ME-2.1 (321+25 - 323+25) - Install Soldier Pile Wall	14	02-Jan-19	21-Jan-19	0
C2RNW120	Retaining Wall ME-2 (309+63 - 320+50) - Install Soldier Pile Wall	75	22-Jan-19	17-May-19	0
Segment 3		525	23-Oct-18	27-Oct-20	0
C3SG200	Segment 3 Complete	0		27-Oct-20	0
Earthwork, Clearing & Grubbing		94	23-Oct-18	26-Mar-19	0
C3CGE110	Earthwork - Segment 3	94	23-Oct-18	26-Mar-19	0
Railroad Bridge		239	27-Feb-19	16-Mar-20	0
Washington St Bridge		239	27-Feb-19	16-Mar-20	0
C3RRBR105	Washington St RR Bridge - P1 North Abutments - Demo & Remove Existing	24	27-Feb-19	04-Apr-19	0
C3RRBR110	Washington St RR Bridge - P1 North Drilled Shafts	20	04-Apr-19	07-May-19	0
C3RRBR170	Washington St RR Bridge - P1 North Pile Caps	20	07-May-19	07-Jun-19	0
C3RRBR155	Washington St RR Bridge - P1 North Superstructure (Place Girders)	28	07-Jun-19	22-Jul-19	0
C3RRBR165	Washington St RR Bridge - P1 North Waterproofing	15	22-Jul-19	14-Aug-19	0

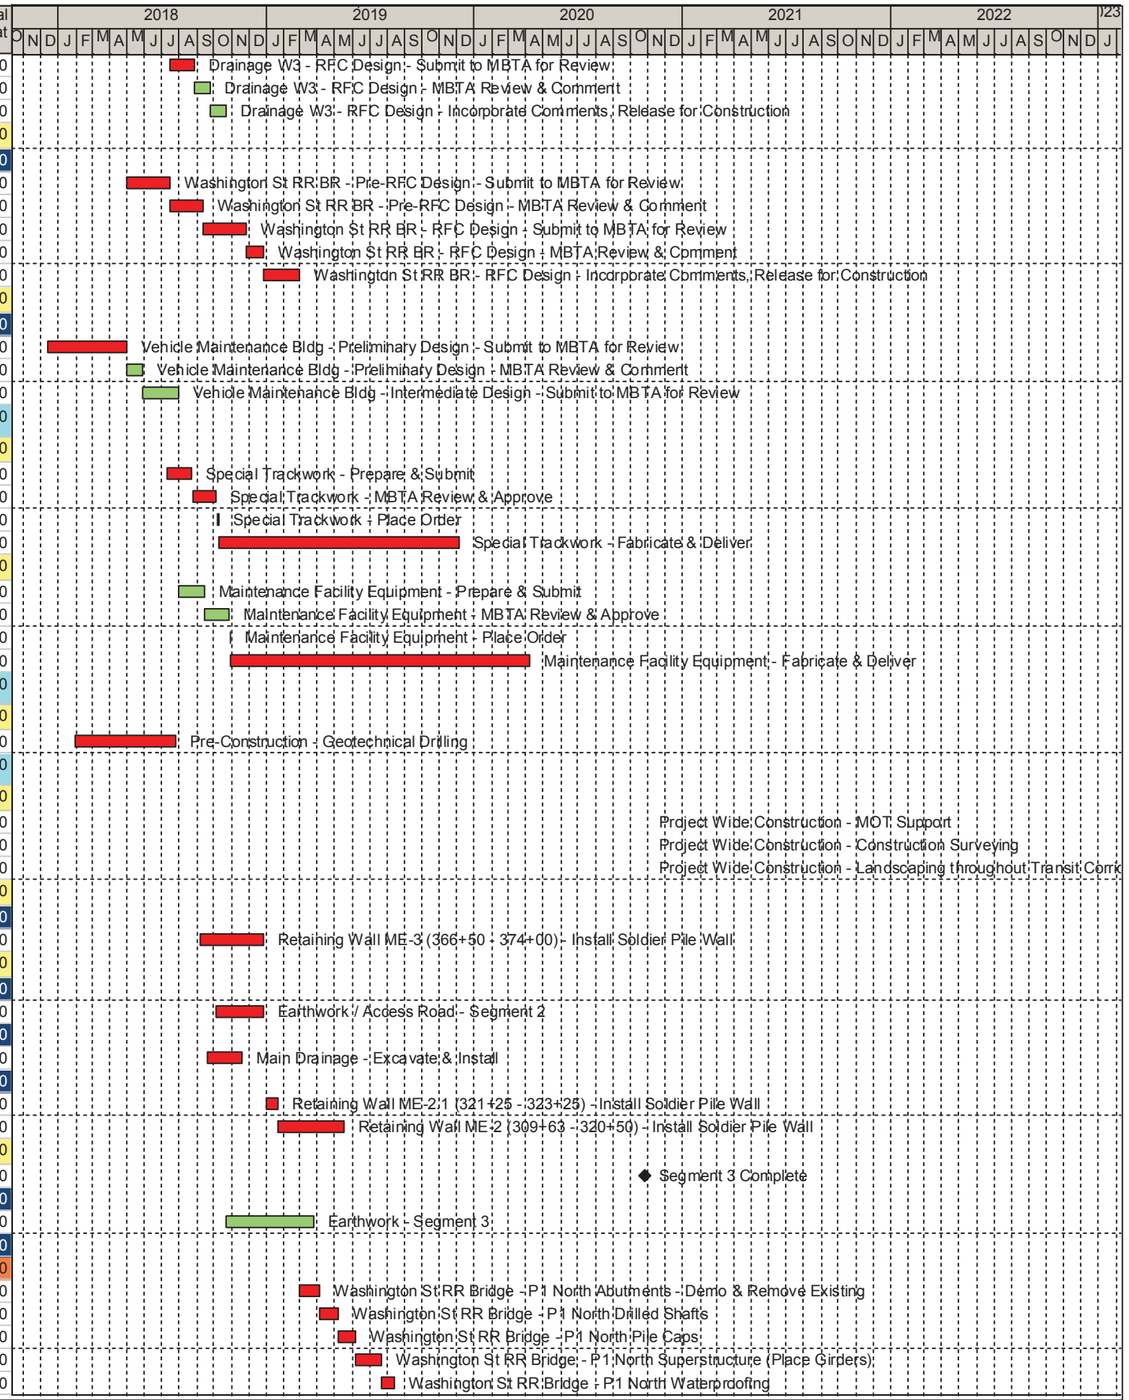

Actual Work | Critical Remaining Work | Remaining Work | Milestone


GLX CONSTRUCTORS

Green Line Extension Detail CPM Schedule

Page: 2 of 5 Data Date: 28-Sep-17 Print: 19-Sep-17

GV20170258-283.pdf

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
C3RRBR145	Washington St RR Bridge - P1 North Approach Slabs	15	22-Jul-19	14-Aug-19	0
C3RRBR125	Washington St RR Bridge - P1 North Finishes	15	14-Aug-19	09-Sep-19	0
C3RRBR180	Washington St RR Bridge - P2 South Abutments - Demo & Remove Existing	22	23-Sep-19	29-Oct-19	0
C3RRBR185	Washington St RR Bridge - P2 South Drilled Shafts	20	29-Oct-19	03-Dec-19	0
C3RRBR190	Washington St RR Bridge - P2 South Pile Caps & Wing Walls	17	03-Dec-19	02-Jan-20	0
C3RRBR200	Washington St RR Bridge - P2 South Superstructure (Place Girders)	28	02-Jan-20	13-Feb-20	0
C3RRBR210	Washington St RR Bridge - P2 South Waterproofing	10	13-Feb-20	02-Mar-20	0
C3RRBR205	Washington St RR Bridge - P2 South Approach Slabs	10	13-Feb-20	02-Mar-20	0
C3RRBR215	Washington St RR Bridge - P2 South Finishes	10	02-Mar-20	16-Mar-20	0
Drainage		286	23-Oct-18	03-Feb-20	0
C3DRA105	Main Drainage - Excavate & Install	46	23-Oct-18	11-Jan-19	0
C3DRA110	Commuter Line 1 EB Track Drainage - Excavate & Install	10	17-Jan-20	03-Feb-20	0
Retaining & Noise Walls		149	20-May-19	16-Jan-20	0
C3NRW230	Retaining Wall N7+Sycamore to Central (276+29 - 289+40) - Install Soldier Pile Wall	104	20-May-19	31-Oct-19	0
C3NRW145	Retaining Wall ME-1 (247+47 - 248+98) - Install Soldier Pile Wall	25	01-Nov-19	12-Dec-19	0
C3NRW180	Crib Wall MCE-1 (248+98 - 252+42) - Rehabilitate Crib Wall	20	13-Dec-19	16-Jan-20	0
Track		96	09-Jan-20	21-May-20	0
Commuter Track 1 (EB) (Sta. 151+20 - 87+70)		22	09-Jan-20	11-Feb-20	0
C3CTRK150	Commuter Track 1 EB - Install Bottom Ballast	16	09-Jan-20	03-Feb-20	0
C3CTRK110	Commuter Track 1 EB - Install Ties & Rail	16	13-Jan-20	05-Feb-20	0
C3CTRK115	Commuter Track 1 EB - Install Top Ballast, Surface & Line	16	15-Jan-20	07-Feb-20	0
C3CTRK120	Commuter Track 1 EB - Destress & Weld Track	16	17-Jan-20	11-Feb-20	0
Commuter Track 2 (WB) (Sta. 151+20 - 87+70)		22	12-Feb-20	16-Mar-20	0
C3CTRK155	Commuter Track 2 WB - Install Bottom Ballast	16	12-Feb-20	06-Mar-20	0
C3CTRK130	Commuter Track 2 WB - Install Ties & Rail	16	14-Feb-20	10-Mar-20	0
C3CTRK135	Commuter Track 2 WB - Install Top Ballast, Surface & Line	16	18-Feb-20	12-Mar-20	0
C3CTRK140	Commuter Track 2 WB - Destress & Weld Track	16	20-Feb-20	16-Mar-20	0
Medford Branch EB (Sta. 295+00 - 221.80)		23	18-Mar-20	21-Apr-20	0
C3MTRK110	Medford Line EB - Install Sub Ballast	19	18-Mar-20	14-Apr-20	0
C3MTRK190	Medford Line EB - Install Bottom Ballast	19	20-Mar-20	16-Apr-20	0
C3MTRK120	Medford Line EB - Install Ties & Rail	19	24-Mar-20	21-Apr-20	0
Medford Branch WB (Sta. 295+00 - 221.80)		21	22-Apr-20	21-May-20	0
C3MTRK150	Medford Line WB - Install Ties & Rail	19	22-Apr-20	19-May-20	0
C3MTRK155	Medford Line WB - Install Top Ballast, Surface & Line	19	27-Apr-20	21-May-20	0
Systems		106	22-May-20	27-Oct-20	0
Signaling		106	22-May-20	27-Oct-20	0
C3SIG170	Washington Sattelite CIH - Install Cable Trough	13	22-May-20	11-Jun-20	0
C3SIG145	Washington CIH - Install Cable Trough	13	22-May-20	11-Jun-20	0
C3SIG120	Gilman CIH - Install Cable Trough	13	22-May-20	11-Jun-20	0
C3SIG175	Washington Sattelite CIH - Install CIH, Wayside Equipment	24	12-Jun-20	16-Jul-20	0
C3SIG150	Washington CIH - Install CIH, Wayside Equipment	24	12-Jun-20	16-Jul-20	0
C3SIG125	Gilman CIH - Install CIH, Wayside Equipment	24	12-Jun-20	16-Jul-20	0
C3SIG180	Washington Sattelite CIH - Pull & Terminate Cables	44	17-Jul-20	21-Sep-20	0
C3SIG155	Washington CIH - Pull & Terminate Cables	44	17-Jul-20	21-Sep-20	0
C3SIG130	Gilman CIH - Pull & Terminate Cables	44	17-Jul-20	21-Sep-20	0
C3SIG185	Washington Sattelite CIH - Local Testing	25	22-Sep-20	27-Oct-20	0
C3SIG160	Washington CIH - Local Testing	25	22-Sep-20	27-Oct-20	0
C3SIG135	Gilman CIH - Local Testing	25	22-Sep-20	27-Oct-20	0
Segment 4		285	17-Jan-19	16-Apr-20	0
Station		175	11-Jul-19	16-Apr-20	0
Lechmere Relocation		175	11-Jul-19	16-Apr-20	0
C4STA6185	Lechmere Station Platform - Platform Slabs	40	11-Jul-19	11-Sep-19	0
C4STA6145	Lechmere Station - Elevators (2)	75	12-Sep-19	14-Jan-20	0
C4STA6150	Lechmere Station - Lighting, Finishes, Signage	25	15-Jan-20	20-Feb-20	0
C4STA6200	Lechmere Station Plaza - Lighting, Finishes, Signage	30	03-Mar-20	16-Apr-20	0
Viaducts		150	17-Jan-19	11-Sep-19	0
Lechmere (LEV)		130	18-Feb-19	11-Sep-19	0
C4LEV330	Lecheme Viaduct (LEV) (Pier 16) - Column Caps	15	18-Feb-19	12-Mar-19	0

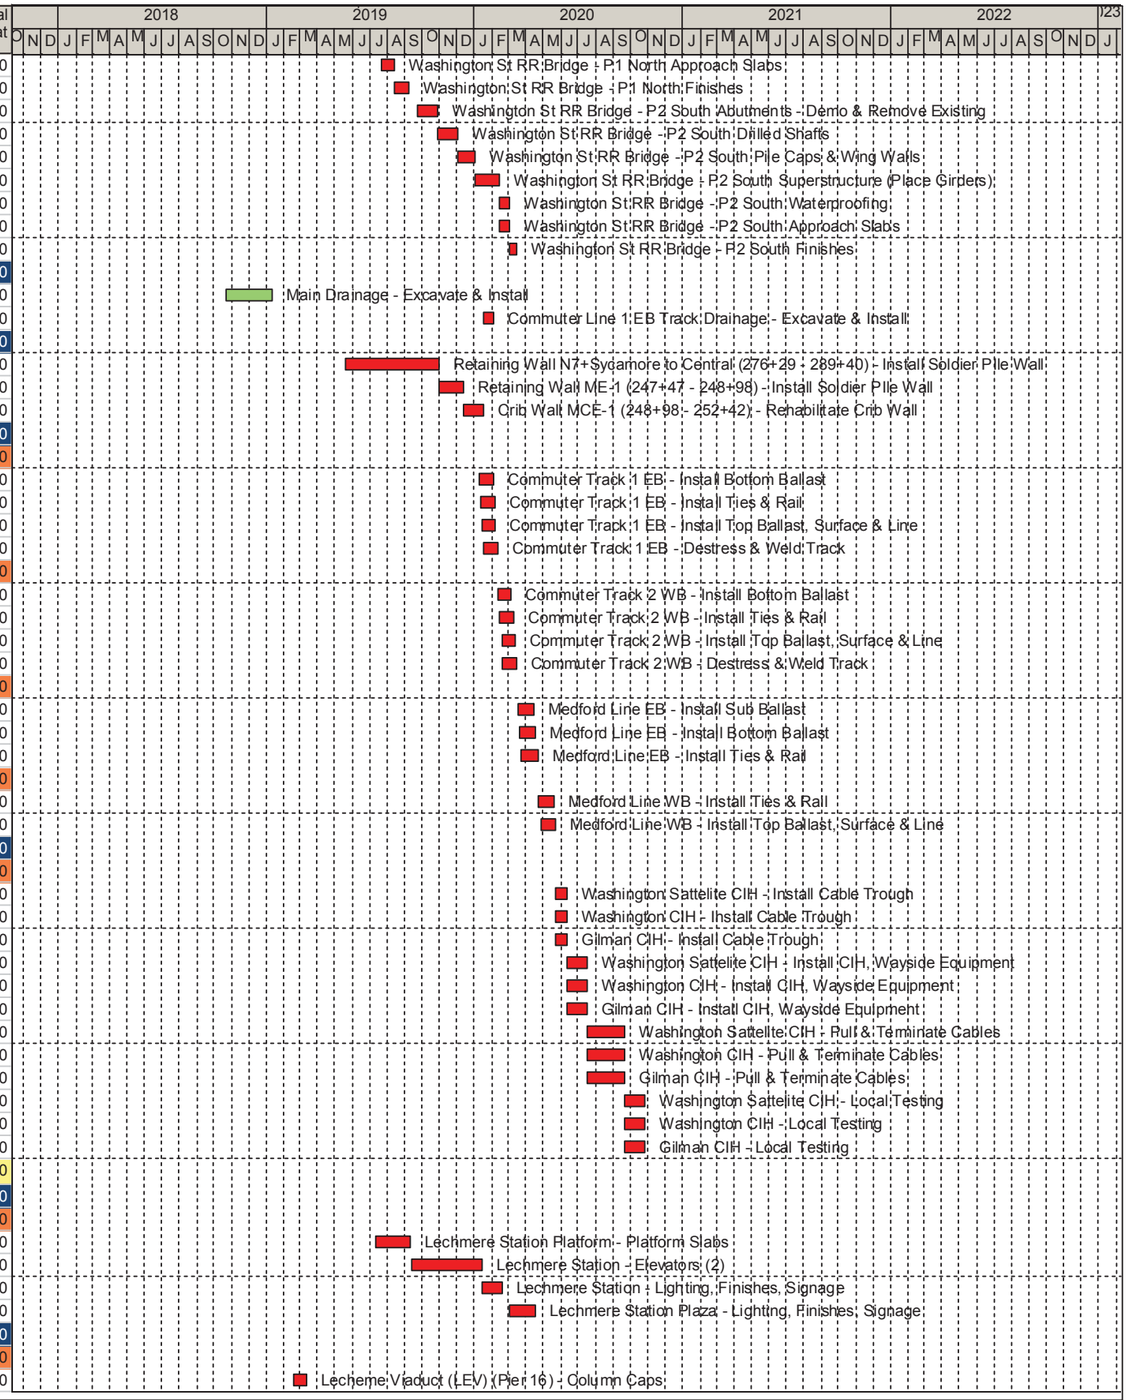

Actual Work | Critical Remaining Work | Remaining Work | Milestone


GLX CONSTRUCTORS

Green Line Extension Detail CPM Schedule

Page: 3 of 5 Data Date: 28-Sep-17 Print: 19-Sep-17

GV20170258-283.pdf

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
C4LEV320	Lecheme Viaduct (LEV) (Piers 8 - 15) - Column Caps	56	18-Feb-19	15-May-19	0
C4LEV170	Lecheme Viaduct (LEV) (Spans 8 - 15) - Set Structural Steel	45	12-Apr-19	21-Jun-19	0
C4LEV200	Lecheme Viaduct (LEV) (Spans 8 - 15) - Deck	35	18-Jul-19	11-Sep-19	0
Medford (MBV)		118	17-Jan-19	22-Jul-19	0
Medford Branch South		118	17-Jan-19	22-Jul-19	0
C4MBV215	Medford Viaduct (MBV) (Piers 17 - 29, 32) - Columns	42	17-Jan-19	21-Mar-19	0
C4MBV350	Medford Viaduct (MBV) (Piers 17 - 29, 32) - Column Caps	98	18-Feb-19	22-Jul-19	0
Medford Branch North		55	17-Jan-19	11-Apr-19	0
C4MBV370	Medford Viaduct (MBV) (Piers 33 - 37) - Columns	20	17-Jan-19	15-Feb-19	0
C4MBV415	Medford Viaduct (MBV) (Piers 33 - 37) - Column Caps	35	18-Feb-19	11-Apr-19	0
Segment 5 - VMF		401	23-Oct-18	27-Jul-20	0
Clearing & Grubbing		102	23-Oct-18	09-Apr-19	0
C5STR140	VMF - Vehicle Maint Building - Complete Site Clearing & Grading	102	23-Oct-18	09-Apr-19	0
Drainage		10	09-Apr-19	24-Apr-19	0
C5DRA105	VMF and Track Drainage - Excavate & Install	10	09-Apr-19	24-Apr-19	0
Retaining & Noise Walls		25	24-Apr-19	05-Jun-19	0
C1RNW155	Retaining Wall W-3 - Install MSE Wall	25	24-Apr-19	05-Jun-19	0
Vehicle Maintenance Facility		264	05-Jun-19	27-Jul-20	0
Vehicle Maintenance Building		264	05-Jun-19	27-Jul-20	0
C5VMB115	Vehicle Maintenance Bldg - Foundations	55	05-Jun-19	28-Aug-19	0
C5VMB120	Vehicle Maintenance Bldg - Walls	65	28-Aug-19	13-Dec-19	0
C5VMB135	Vehicle Maintenance Bldg - Girders, Roof	51	13-Dec-19	06-Mar-20	0
C5VMB140	Vehicle Maintenance Bldg - Cranes, Equipment	48	09-Apr-20	19-Jun-20	0
C5VMB145	Vehicle Maintenance Bldg - Finishes	25	22-Jun-20	27-Jul-20	0
Segment 6 - Union Square		141	05-Nov-19	19-May-20	0
Track		20	05-Nov-19	09-Dec-19	0
Union Square WB (Sta. 39+33 - 1+15)		20	05-Nov-19	09-Dec-19	0
C6TRK145	Union Sq Line WB - Install Ties & Rail	18	05-Nov-19	05-Dec-19	0
C6TRK150	Union Sq Line WB - Install Top Ballast, Surface & Line	18	07-Nov-19	09-Dec-19	0
Systems		102	10-Dec-19	19-May-20	0
Signaling		102	10-Dec-19	19-May-20	0
C6SIG125	Union Sq CIH - Install Cable Trough	20	10-Dec-19	13-Jan-20	0
C6SIG120	Red Bridge Satellite CIH - Install Cable Trough	20	10-Dec-19	13-Jan-20	0
C6SIG145	Union Sq CIH - Install CIH, Wayside Equipment	26	14-Jan-20	20-Feb-20	0
C6SIG140	Red Bridge Satellite CIH - Install CIH, Wayside Equipment	26	14-Jan-20	20-Feb-20	0
C6SIG135	Union Sq CIH - Pull & Terminate Cables	34	21-Feb-20	15-Apr-20	0
C6SIG130	Red Bridge Satellite CIH - Pull & Terminate Cables	34	21-Feb-20	15-Apr-20	0
C6SIG155	Union Sq CIH - Local Testing	22	16-Apr-20	19-May-20	0
C6SIG150	Red Bridge Satellite CIH - Local Testing	22	16-Apr-20	19-May-20	0
Start-up / Testing / Commissioning		360	17-Apr-20	02-Sep-21	0
TPW6105	Plaza Work (6) Notice of Milestone 6 - Submit to MBTA for Review	15	17-Apr-20	11-May-20	0
TUS4A115	(4a) - LFAT and Systems Integration Testing	85	20-May-20	23-Sep-20	0
TPW6110	Plaza Work (6) Notice of Milestone 6 - MBTA Review & Approve, Issue Certificate	20	17-Jun-20	14-Jul-20	0
TVMF5120	VMF (5) - Final Project Safety & Security Certificate - Submit to MBTA for Review	5	28-Jul-20	04-Aug-20	0
TVMF5115	VMF (5) - Certificate of Occupancy - Submit to MBTA	15	28-Jul-20	18-Aug-20	0
TVMF5125	VMF (5) - Final Project Safety & Security Certificate - MBTA Review & Approve	15	05-Aug-20	25-Aug-20	0
TVMF5130	VMF (5) - Notice of Milestone 5 - Submit to MBTA for Review	5	19-Aug-20	25-Aug-20	0
TVMF5135	VMF (5) - Notice of Milestone 5 - MBTA Review & Approve, Issue Certificate	15	26-Aug-20	16-Sep-20	0
TUS4A125	(4a) - Pre-Revenue Demonstration Testing Meeting with MBTA	1	23-Sep-20	23-Sep-20	0
TUS4A135	(4a) - Notice of Milestone 4a - Submit to MBTA for Review	1	24-Sep-20	24-Sep-20	0
TUS4A140	(4a) - Notice of Milestone 4a - MBTA Review & Approve, Issue Certificate	15	25-Sep-20	15-Oct-20	0
TUS4A145	(4b) - Approval to Start Pre-Revenue Demonstration Testing	1	16-Oct-20	16-Oct-20	0
TUS4A150	(4b) - Notice of Milestone 4b - Submit to MBTA for Review	5	19-Oct-20	23-Oct-20	0
TUS4A155	(4b) - Notice of Milestone 4b - MBTA Review & Approve, Issue Certificate	15	26-Oct-20	13-Nov-20	0
TMB3A115	(3a) - Certificate of Occupancy - Submit to MBTA	15	28-Oct-20	18-Nov-20	0
TUS4A160	(4c) - Pre-Revenue Demonstration Testing	60	16-Nov-20	18-Feb-21	0
TMB3A135	(3a) - Notice of Milestone 3a - Submit to MBTA for Review	1	19-Nov-20	19-Nov-20	0

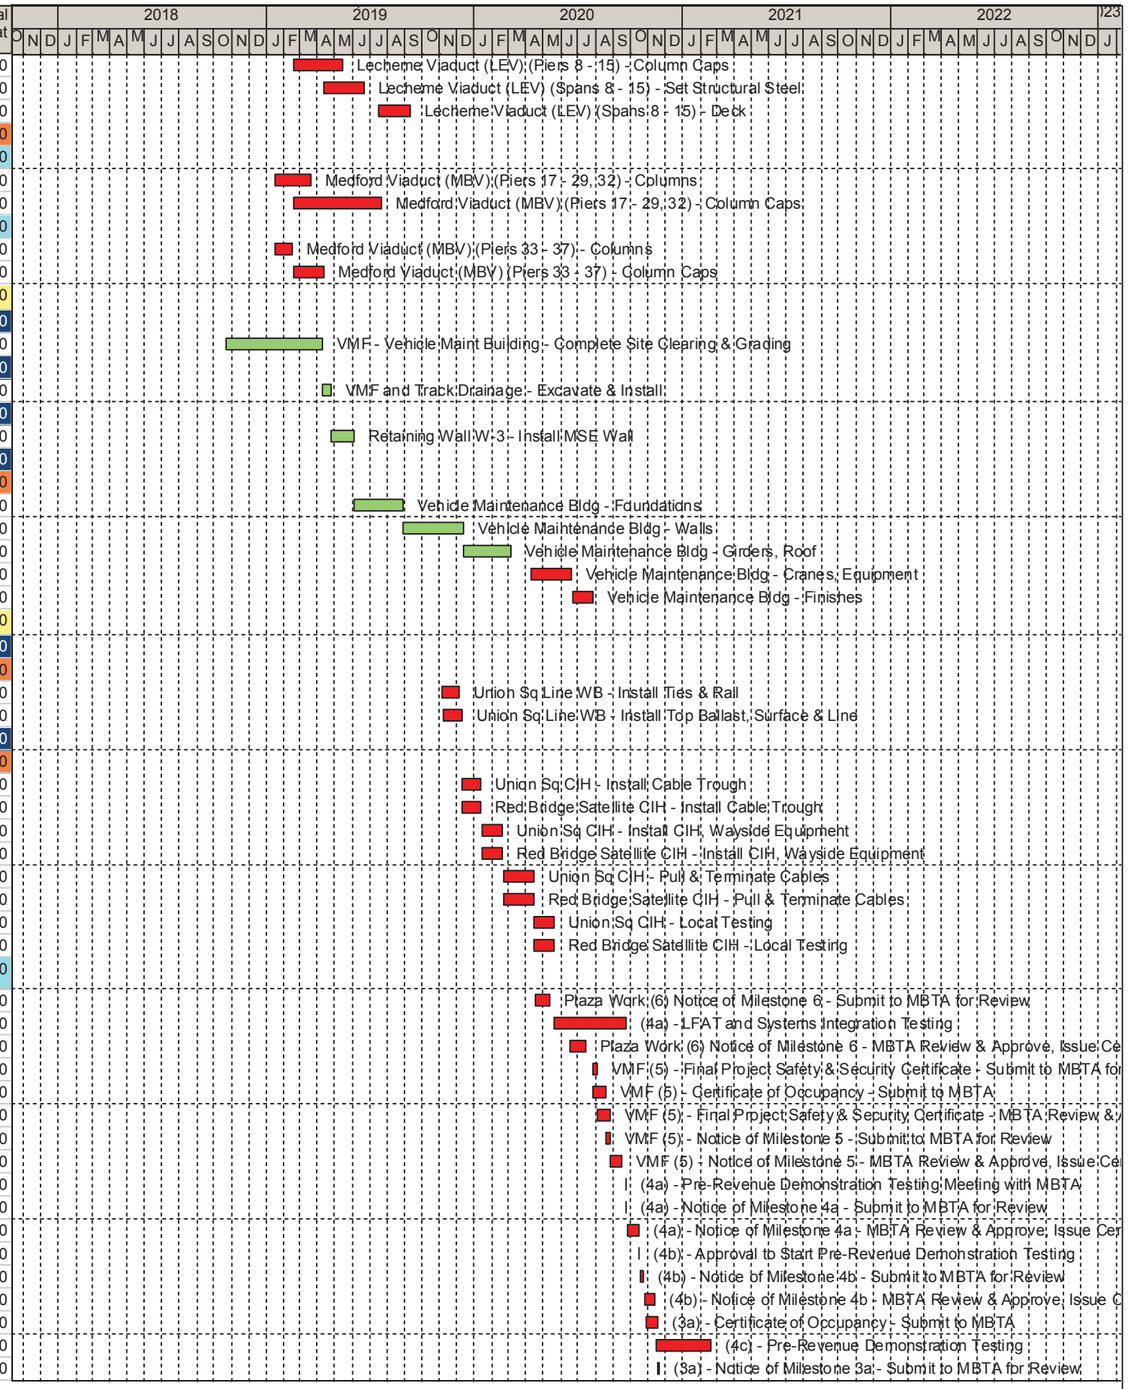

Actual Work Critical Remaining Work
Remaining Work Milestone


GLX CONSTRUCTORS

Green Line Extension Detail CPM Schedule

Page: 4 of 5 Data Date: 28-Sep-17 Print: 19-Sep-17

GV20170258-283.pdf

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
TMB3A140	(3a) - Notice of Milestone 3a - MBTA Review & Approve, Issue Certificate	15	20-Nov-20	15-Dec-20	0
TMB3A150	(3b) - Approval to Start Pre-Revenue Demonstration Testing	1	16-Dec-20	16-Dec-20	0
TMB3B115	(3b) - Notice of Milestone 3b - Submit to MBTA for Review	15	17-Dec-20	12-Jan-21	0
TMB3B120	(3b) - Notice of Milestone 3b - MBTA Review & Approve, Issue Certificate	15	13-Jan-21	02-Feb-21	0
TMB3C105	(3c) - Pre-Revenue Demonstration Testing	60	03-Feb-21	04-May-21	0
TUS4A170	(4c) - Final Change-Over, Keys Transmitted to MBTA	1	22-Feb-21	22-Feb-21	0
TUS4A165	(4c) - All Systems, Comms, Stations, Etc. Completed & Tested	1	22-Feb-21	22-Feb-21	0
TUS4A185	(4c) - Notice of Milestone 4c - Submit to MBTA for Review	15	23-Feb-21	15-Mar-21	0
TUS4A190	(4c) - Notice of Milestone 4c - MBTA Review & Approve, Issue Certificate	15	15-Mar-21	06-Apr-21	0
TMB3C115	(3c) - Final Change-Over, Keys Transmitted to MBTA	1	05-May-21	05-May-21	0
TMB3C110	(3c) - All Systems, Comms, Stations, Etc. Completed & Tested	1	05-May-21	05-May-21	0
TMB3C130	(3c) - Notice of Milestone 3c - Submit to MBTA for Review	5	06-May-21	12-May-21	0
TMB3C135	(3c) - Notice of Milestone 3c - MBTA Review & Approve, Issue Certificate	15	13-May-21	03-Jun-21	0
COMSUM10	Start-up, Testing, Commissioning Complete	0		08-Jun-21	0
COMSUM20	Notice of Contract Substantial Completion	20	16-Jun-21	14-Jul-21	0
COMSUM30	MBTA Issue Contract Substantial Completion Certificate	0		14-Jul-21	0
PWMS0120	GLX Provide Notice of Final Completion	15	13-Aug-21	02-Sep-21	0

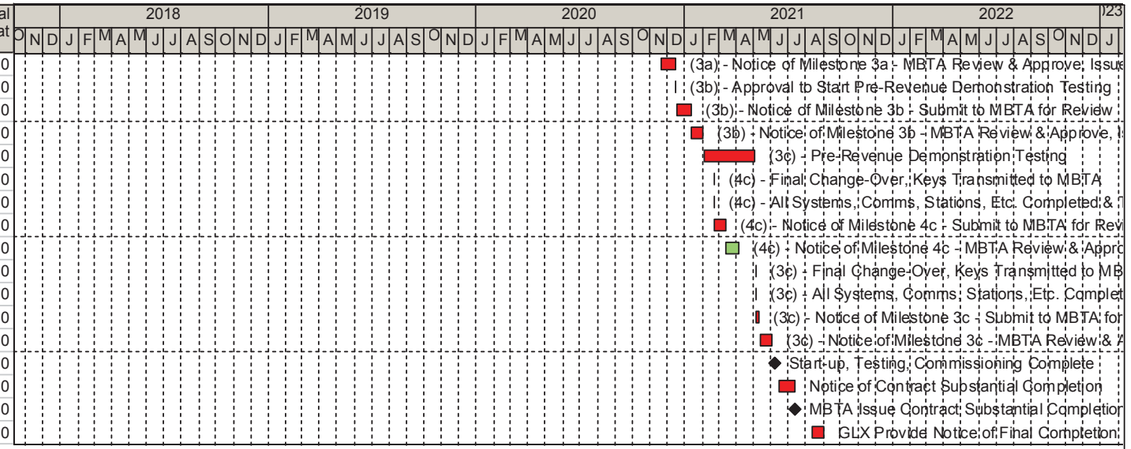

Actual Work
Remaining Work
Critical Remaining Work
Milestone

GLX CONSTRUCTORS

Green Line Extension Detail CPM Schedule

APPENDIX 3

TILOS Schedule for Union Square Line



Segment 6 - Union Square

0+00

2022: Mar, Feb, Jan


2021: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May, Apr, Mar, Feb, Jan

2020: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May, Apr, Mar, Feb, Jan

2019: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May, Apr, Mar, Feb, Jan

2018: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May, Apr, Mar, Feb, Jan

2017: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May

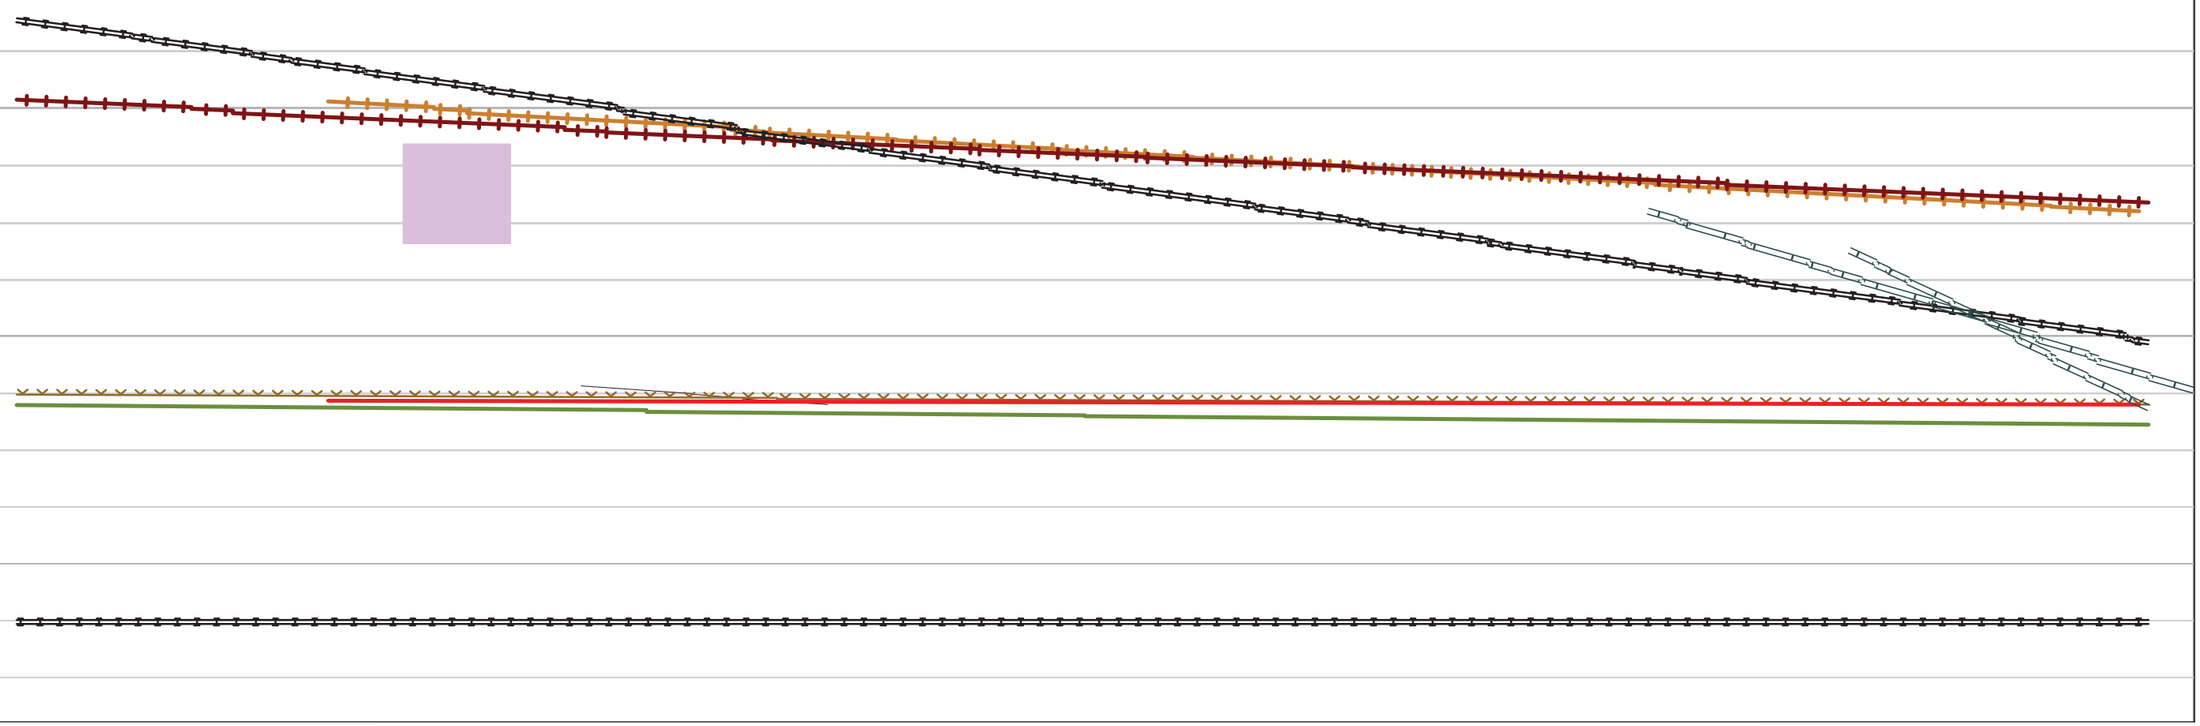

Clearing & Grubbing		Viaducts		Systems	
Earthwork		Union Square Station		GLXFMS	
Main Drainage		Track - Un Sq EB			
Retaining Wall		Track - Un Sq WB			


Project: GLX Constructors
Printed: 08.30.2017

GLX CONSTRUCTORS

GV20170258-283.pdf

APPENDIX 4

TILOS Schedule for Medford Line



Segment 1	Segment 2	Segment 3	Segment 4
344+00	295+00	221+80	177+90

2021: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May, Apr, Mar, Feb, Jan

2020: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May, Apr, Mar, Feb, Jan

2019: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May, Apr, Mar, Feb, Jan

2018: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May, Apr, Mar, Feb, Jan

2017: Dec, Nov, Oct

Milestone 3c

Milestone 3b

Milestone 3a

Milestone 5

Milestone 6

CG		SPLE		STR		RRBR		SYS		VMFTRK		VMFBL							
EW		SPLW		STA		RWBR		PS		VMFCG		GLXFMS							
MD		MPB		VIAD		TRKCL		RWTI		VMFSYS									
RW		CWR		CMP		TRKML		VMFBL		VMFFMS									

Project: GLX Constructors
Printed: 08.30.2017

GLX CONSTRUCTORS

APPENDIX 5

Critical Schedule Management Report Examples

GLX Activities with Pred/Succ

Activity ID	Activity Name	Predecessors	Successors
A6020	Track - Design SUMMARY		
A6030	Track S2 - SUMMARY		
A6050	Track S3 - SUMMARY		
A6070	Systems S3 - SUMMARY		
A6080	Track S4 - SUMMARY		
A6090	Systems S4 - SUMMARY		
A6110	Systems S5 (VMF) - SUMMARY		
A6120	Track S6 (Union Square Branch) - SUMMARY		
A6130	Ball Sq TPSS - Install, Field Test	C2TPS170, C2STA2105, PRTPS100, DUDP950	TMB3A145

Activity ID	Activity Name	Relationship Type	Lag	Driving
C2TPS170	Ball Sq TPSS - Field Test	FF	0	No
C2STA2105	Ball Square Station - Excavate, CIP Frost Wall & Backfill	SS	0	Yes
PRTPS100	Traction Power Substation - Fabricate & Deliver	SS	40	No
DUDP950	Traction Power Systems - RFC Design - Incorporate Comments, Release for Construction	FS	0	No

Activity ID	Activity Name	Relationship Type	Lag	Driving
TMB3A145	(3a) - LFAT and Systems Integration Testing	FF	0	No

A6140	Segment 1 - SUMMARY		
A6150	Segment 2 - SUMMARY		
A6160	Segment 3 - SUMMARY		
A6170	Segment 4 - SUMMARY		

GLX Activities with Pred/Succ

Activity ID	Activity Name	Predecessors	Successors
A6180	**Segment 5 VMF - SUMMARY**		
A6190	**Segment 6 - Union Square - SUMMARY**		
A6200	**Final Testing - SUMMARY**		
A6210	**Roadway & Traffic Improvements - SUMMARY**		
C1CGE105	**Clearing & Grubbing - Segment 1**	**PSTU105, DDRA340**	**C1UT135, C1UT130, C1UT125, C1UT115, C1UT110, C1UT105, C1DRA135, C1CGE110**

Activity ID	Activity Name	Relationship Type	Lag	Driving
PSTU105	Pre-Construction Studies - Design Confirmation	FS	0	No
DDRA340	Earthwork, Clearing & Grubbing - RFC Design - Incorporate Comments, Release for Construction	FS	0	Yes

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1UT135	Utilities - Relocate Overhead ELEC STA 357+25 MB-WB to STA 375+00 MB-WB (MBTA)	FS	0	No
C1UT130	Utilities - Relocate FIBER OPTICS Overhead STA 357+25 MB-WB to STA 375+00 MB-WB (MBTA)	FS	0	No
C1UT125	Utilities - Relocate 4" FIBER OPTIC Overhead STA 335+00 MB-WB to STA 357+00 MB-WB	FS	0	No
C1UT115	Utilities - Relocate Overhead ELEC on College Ave Bridge STA	FS	0	No

GLX Activities with Pred/Succ

Activity ID	Activity Name		Predecessors	Successors
	363+50 MB-WB			
C1UT110	Utilities - 30" MDC C/W Water ABANDONED Demolish & Cap STA 358+50 MB-WB	FS	0	No
C1UT105	Utilities - 24" MDC C/W Water ABANDONED Demolish & Cap STA 358+50 MB-WB	FS	0	No
C1DRA135	Main Drainage - Excavate & Install	FS	0	Yes
C1CGE110	Earthwork - Segment 1	SS	30	Yes

C1CGE110	**Earthwork - Segment 1**		**DDRA340, C1CGE105**	**C1SG200, C1DRA135, C1RWB110, C1OCS110, C1OCS105, C1RNW170, C1RNW165, C1RNW105, C1RNW115, C1RNW110, C1RNW125**

Activity ID	Activity Name	Relationship Type	Lag	Driving
DDRA340	Earthwork, Clearing & Grubbing - RFC Design - Incorporate Comments, Release for Construction	FS	0	No
C1CGE105	Clearing & Grubbing - Segment 1	SS	30	Yes

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1SG200	Segment 1 Complete	FS	0	No
C1DRA135	Main Drainage - Excavate & Install	SS	0	No
C1RWB110	College Ave Bridge (M-12-012) - Demo Existing Sidewalk (on north side) and Railing	FS	0	No

GLX Activities with Pred/Succ

Activity ID	Activity Name		Predecessors	Successors
C1OCS110	Medford Line EB - Drill & Place OCS Foundations & Poles	FF	10	No
C1OCS105	Medford Line WB - Drill & Place OCS Foundations & Poles	FF	10	No
C1RNW170	Retaining Wall MW-9.5 (360+75 - 362+80) - Install Modular Pre-Cast Block Wall	FS	0	No
C1RNW165	Retaining Wall ME-2.5 (363+75 - 364+25) - Install Modular Pre-Cast Block Wall	FS	0	No
C1RNW105	Retaining Wall MW-10 (363+63 - 374+02) - Install Soil Nail Wall	FS	0	No
C1RNW115	Retaining Wall MW-8.2 (343+56 - 345+20) - Install MSE Wall	FS	1	No
C1RNW110	Retaining Wall ME-3 (366+50 - 374+00) - Install Soldier PIle Wall	FF	0	Yes
C1RNW125	Retaining Wall MW-9 (345+80 - 353+54) - Install MSE Wall	FS	1	No

C1COM105 **College Ave Station - Mechanical, Electrical, Communications Eqp** **C1STA1135, PRCME100, DUDP850** **C1COM115**

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1STA1135	College Ave Station - Shelter, Roof	FF	10	Yes
PRCME100	Communications Equipment - Fabricate & Deliver	FS	0	No
DUDP850	Communications - RFC Design - Incorporate Comments, Release for Construction	FS	0	No

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1COM115	College Ave Station - Pull & Terminate Wire,	FS	0	No

GLX Activities with Pred/Succ

Activity ID	Activity Name	Predecessors	Successors
	Local Test		
C1COM110	**College Ave Station - Install FDP & Patch Cables**	**C1STA1135, DUDP850**	**C1COM115**

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1STA1135	College Ave Station - Shelter, Roof	FF	10	Yes
DUDP850	Communications - RFC Design - Incorporate Comments, Release for Construction	FS	0	No

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1COM115	College Ave Station - Pull & Terminate Wire, Local Test	FS	0	No

C1COM115	**College Ave Station - Pull & Terminate Wire, Local Test**	**C1COM110, C1STA1150, C1COM105**	**TMB3A145**

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1COM110	College Ave Station - Install FDP & Patch Cables	FS	0	No
C1STA1150	College Ave Station - Lighting, Signage, Finishes	FF	0	Yes
C1COM105	College Ave Station - Mechanical, Electrical, Communications Eqp	FS	0	No

Activity ID	Activity Name	Relationship Type	Lag	Driving
TMB3A145	(3a) - LFAT and Systems Integration Testing	FF	0	No

C1CTRK100	**Commuter Track 1 EB - SUMMARY**		

C1CTRK115	**Commuter Track 1 EB - Install Ties & Rail**	**C1CTRK150, PRTRK100**	**C1CTRK120**

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CTRK150	Commuter Track 1 EB - Install Bottom Ballast	SS	2	Yes

GLX Activities with Pred/Succ

Activity ID	Activity Name		Predecessors	Successors
PRTRK100	Trackwork - Fabricate &	FS	0	No
Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CTRK120	Commuter Track 1 EB - Install Top Ballast, Surface & Line	SS	2	Yes
C1CTRK120	**Commuter Track 1 EB - Install Top Ballast, Surface & Line**		**C1CTRK115**	**C1CTRK125**
Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CTRK115	Commuter Track 1 EB - Install Ties & Rail	SS	2	Yes
Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CTRK125	Commuter Track 1 EB - Destress & Weld Track	SS	2	Yes
C1CTRK125	**Commuter Track 1 EB - Destress & Weld Track**		**C1CTRK120**	**C1CTRK155, C1SG200**
Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CTRK120	Commuter Track 1 EB - Install Top Ballast, Surface & Line	SS	2	Yes
Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CTRK155	Commuter Track 2 WB - Install Bottom Ballast	FS	0	Yes
C1SG200	Segment 1 Complete	FS	0	No
C1CTRK135	**Commuter Track 2 WB - Install Ties & Rail**		**C1CTRK155, PRTRK100**	**C1CTRK140**
Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CTRK155	Commuter Track 2 WB - Install Bottom Ballast	SS	2	Yes
PRTRK100	Trackwork - Fabricate &	FS	0	No
Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CTRK140	Commuter Track 2 WB - Install Top Ballast, Surface & Line	SS	2	Yes
C1CTRK140	**Commuter Track 2 WB - Install Top Ballast, Surface & Line**		**C1CTRK135**	**C1CTRK145**
Activity ID	Activity Name	Relationship Type	Lag	Driving

GLX Activities with Pred/Succ

Activity ID	Activity Name		Predecessors	Successors
C1CTRK135	Commuter Track 2 WB - Install Ties & Rail	SS	2	Yes
Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CTRK145	Commuter Track 2 WB - Destress & Weld Track	SS	2	Yes
C1CTRK145	**Commuter Track 2 WB - Destress & Weld Track**		**C1CTRK140**	**C1RNW170, C1RNW105, C1MTRK160, C1DRA150, C1SG200**
Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CTRK140	Commuter Track 2 WB - Install Top Ballast, Surface & Line	SS	2	Yes
Activity ID	Activity Name	Relationship Type	Lag	Driving
C1RNW170	Retaining Wall MW-9.5 (360+75 - 362+80) - Install Modular Pre-Cast Block Wall	FS	0	Yes
C1RNW105	Retaining Wall MW-10 (363+63 - 374+02) - Install Soil Nail Wall	FS	0	Yes
C1MTRK160	Medford Line EB - Install Sub Ballast	FS	0	No
C1DRA150	Commuter Line 2 WB Track Drainage - Excavate & Install Drainage	FS	0	No
C1SG200	Segment 1 Complete	FS	0	No
C1CTRK150	**Commuter Track 1 EB - Install Bottom Ballast**		**C1DRA110, C1RNW165, C1DRA135, DRWB2460, C1RNW110**	**C1CTRK115**
Activity ID	Activity Name	Relationship Type	Lag	Driving
C1DRA110	Commuter Line 1 EB Track Drainage - Excavate & Install	FS	0	Yes
C1RNW165	Retaining Wall ME-2.5 (363+75 - 364+25) - Install Modular Pre-Cast Block Wall	FS	0	No

GLX Activities with Pred/Succ

Activity ID	Activity Name	Predecessors	Successors
C1DRA135	Main Drainage - Excavate & Install	FS 0	No
DRWB2460	Commuter Line Track - RFC Design - Incorporate Comments, Release for Construction	FS 0	No
C1RNW110	Retaining Wall ME-3 (366+50 - 374+00) - Install Soldier PIle Wall	FS 0	No
Activity ID	Activity Name	Relationship Type	Lag Driving
C1CTRK115	Commuter Track 1 EB - Install Ties & Rail	SS	2 Yes
C1CTRK155	**Commuter Track 2 WB - Install Bottom Ballast**	**C1CTRK125, DRWB2460**	**C1CTRK135**
Activity ID	Activity Name	Relationship Type	Lag Driving
C1CTRK125	Commuter Track 1 EB - Destress & Weld Track	FS	0 Yes
DRWB2460	Commuter Line Track - RFC Design - Incorporate Comments, Release for Construction	FS	0 No
Activity ID	Activity Name	Relationship Type	Lag Driving
C1CTRK135	Commuter Track 2 WB - Install Ties & Rail	SS	2 Yes
C1CTRK165	**Commuter Track 2 WB - SUMMARY**		
C1DRA100	**Drainage S1 - SUMMARY**		
C1DRA110	**Commuter Line 1 EB Track Drainage - Excavate & Install**	**C1RNW165, C1RNW110, C1DRA135, DDRA170**	**C1CTRK150**
Activity ID	Activity Name	Relationship Type	Lag Driving
C1RNW165	Retaining Wall ME-2.5 (363+75 - 364+25) - Install Modular Pre-Cast Block Wall	FS	0 Yes
C1RNW110	Retaining Wall ME-3 (366+50 -	FS	0 No

GLX Activities with Pred/Succ

Activity ID	Activity Name	Predecessors	Successors
	Soldier PIle Wall		
C1DRA135	Main Drainage - Excavate & Install	FS 0	No
DDRA170	Track Drainage - RFC Design - Incorporate Comments, Release for Construction	FS 0	No

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CTRK150	Commuter Track 1 EB - Install Bottom Ballast	FS	0	Yes

C1DRA125 **Medford Line WB Track Drainage - Excavate & Install** — Predecessors: **C1MTRK155, C1RNW115, C1RNW125, C1RNW105, DDRA170** — Successors: **C1SG200**

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1MTRK155	Medford Line WB - Destress & Weld Track	FS	0	Yes
C1RNW115	Retaining Wall MW-8.2 (343+56 - 345+20) - Install MSE Wall	FS	0	No
C1RNW125	Retaining Wall MW-9 (345+80 - 353+54) - Install MSE Wall	FS	0	No
C1RNW105	Retaining Wall MW-10 (363+63 - 374+02) - Install Soil Nail Wall	FS	0	No
DDRA170	Track Drainage - RFC Design - Incorporate Comments, Release for Construction	FS	0	No

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1SG200	Segment 1 Complete	FS	0	No

C1DRA135 **Main Drainage - Excavate & Install** — Predecessors: **C1CGE110, C1CGE105, DDRA230** — Successors: **C1SG200, C1DRA110, C1CTRK150**

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CGE110	Earthwork - Segment 1	SS	0	No
C1CGE105	Clearing & Grubbing -	FS	0	Yes

GLX Activities with Pred/Succ

Activity ID	Activity Name		Predecessors	Successors
	Segment 1			
DDRA230	Main Drainage - RFC Design - Incorporate Comments, Release for Construction	FS	0	No

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1SG200	Segment 1 Complete	FS	0	No
C1DRA110	Commuter Line 1 EB Track Drainage - Excavate & Install	FS	0	No
C1CTRK150	Commuter Track 1 EB - Install Bottom Ballast	FS	0	No

C1DRA150	Commuter Line 2 WB Track Drainage - Excavate & Install Drainage	C1CTRK145, C3DRA110	C1SG200

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1CTRK145	Commuter Track 2 WB - Destress & Weld Track	FS	0	No
C3DRA110	Commuter Line 1 EB Track Drainage - Excavate & Install	FS	0	Yes

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1SG200	Segment 1 Complete	FS	0	No

C1MTRK120	Medford Line EB - Install Ties & Rail	C1MTRK190, PRTRK100	C1MTRK145, C1MTRK125

Activity ID	Activity Name	Relationship Type	Lag	Driving
C1MTRK190	Medford Line EB - Install Bottom Ballast	SS	2	Yes
PRTRK100	Trackwork - Fabricate &	FS	0	No


Activity ID	Activity Name	Relationship Type	Lag	Driving
C1MTRK145	Medford Line WB - Install Ties &	FS	0	Yes
C1MTRK125	Medford Line EB - Install Top Ballast, Surface & Line	SS	2	Yes

C1MTRK125	Medford Line EB - Install Top Ballast, Surface & Line	C1MTRK120	C1OCS115, C1MTRK130


Activity ID	Activity Name	Relationship Type	Lag	Driving

Example - Bid Item Report

Bid	Client No.	Type	Description	Bid Quan	Takeoff Quan	Unit	Total Labor	Total Labor UC	Burden	Burden UC	PM	CM	Sub	Equipment	Unit Cost	Total	D-Group
1		D	DIRECT COST ITEMS	1.000	1.000	LS											P
10000		D	### MOBILIZATION ###	1.000	1.000	LS											0
20001		D	AREA 1### REMOVALS & DEMOLITION ###	1.000	1.000	LS											1
20002		D	AREA 2### REMOVALS & DEMOLITION ###	1.000	1.000	LS											2
20003		D	AREA 3### REMOVALS & DEMOLITION ###	1.000	1.000	LS											3
20101		D	REMOVAL OF EXSTG. OBSTRUCTIONS (REMOVE FENCE)	4,628.000	4,628.000	LF											1
20201		D	REM.&DISP. EXSTG. WALLS	96.000	96.000	CY											1
20301		D	REM. & DISP.OF EXIST. CONC.PAVEMENT	6,794.000	6,794.000	SY											1
20303		D	REM. & DISP.OF EXIST. CONC.PAVEMENT	1,807.000	1,807.000	SY											3
20403		D	REM. & DISP. OF EXISTING CURB	6,991.000	6,991.000	LF											3
20501		D	REM.&DISP.OF EXIST ASPH. PVMT.	1,850.000	1,850.000	SY											1
20503		D	REM.&DISP.OF EXIST ASPH. PVMT.	21,270.000	21,270.000	SY											3
20601		D	REM.& DISP. OF EXIST.SHOULDERS	22,828.000	22,828.000	SY											1
20703		D	REM.& DISP.OF EXISTING CONC.SDWLK	3,153.000	3,153.000	CY											3
20801		D	REM.& DISP.OF CONC.MED.BARR.	400.000	400.000	LF											1
20901		D	REMOVAL OF EXIST. GUARDRAIL	11,304.000	11,304.000	LF											1
21001		D	DEMO EXIST. BRIDGE&RAMPS-CMPLTE	96,224.000	96,224.000	SF											1
21103		D	REMOVAL OF PAVEMENT MARKINGS	12,240.000	12,240.000	LF											3
21201		D	DEMO EXIST. BUILDINGS-CMPLTE	210,322.000	210,322.000	SF											1
30001		D	AREA 1###CLEARG, ERTHWK,GRADING&GRND IMPRVMNTS ###	1.000	1.000	LS											1
30002		D	AREA 2###CLEARG, ERTHWK,GRADING&GRND IMPRVMNTS ###	1.000	1.000	LS											2
30003		D	AREA 3###CLEARG, ERTHWK,GRADING&GRND IMPRVMNTS ###	1.000	1.000	LS											3
30101		D	CLEAR. & GRUB. WITHIN ROW	29.000	29.000	ACRE											1
30102		D	CLEAR. & GRUB. WITHIN ROW	10.000	10.000	ACRE					***Pricing Details Removed***						2
30103		D	CLEAR. & GRUB. WITHIN ROW	8.000	8.000	ACRE											3
30201		D	UNCLASSIFIED EXCAVATION	61,467.000	61,467.000	CY											1
30202		D	UNCLASSIFIED EXCAVATION	1,315.000	1,315.000	CY											2
30203		D	UNCLASSIFIED EXCAVATION	17,817.000	17,817.000	CY											3
30252		D	OVEREXCAVATION	19,320.000	19,320.000	CY											2
30253		D	OVEREXCAVATION	9,680.000	9,680.000	CY											3
30301		D	FINE GRADE	252,540.000	252,540.000	SY											1
30302		D	FINE GRADE	20,700.000	20,700.000	SY											2
30303		D	FINE GRADE	140,760.000	140,760.000	SY											3
30401		D	F&I SETTLEMENT DEVICES&MONITORING	9.000	9.000	EA											1
30501		D	GRASS LINED SWALES	13,464.000	13,464.000	LF											1
30503		D	GRASS LINED SWALES	1,000.000	1,000.000	LF											3
30601		D	RETENTION / DETENTION PONDS	2,900.000	2,900.000	CY											1
30701		D	EARTHQUAKE DRAINS	254,741.000	254,741.000	LF											1
30702		D	EARTHQUAKE DRAINS	26,462.000	26,462.000	LF											2
30703		D	EARTHQUAKE DRAINS	49,629.000	49,629.000	LF											3
30803		D	TIMBER PILE STABILIZATION	37,602.000	37,602.000	LF											3
30901		D	STONE COLUMN STABILIZATION	480.000	480.000	EA											1
30903		D	STONE COLUMN STABILIZATION	752.000	752.000	EA											3
31001		D	GEOTEXTILE / GEOGRID REINF.	4,680.000	4,680.000	SY											1
31003		D	GEOTEXTILE / GEOGRID REINF.	29,683.000	29,683.000	SY											3
31101		D	EMBANKMENT IN PLACE-INCL SURCHARGE	145,093.000	145,093.000	CY											1
31102		D	EMBANKMENT IN PLACE-INCL SURCHARGE	8,963.000	8,963.000	CY											2
31103		D	EMBANKMENT IN PLACE-INCL SURCHARGE	32,630.000	32,630.000	CY											3
31111		D	EMBANKMENT	155,245.000	155,245.000	CY											1
31112		D	EMBANKMENT	10,031.000	10,031.000	CY											2
31113		D	EMBANKMENT	33,756.000	33,756.000	CY											3
31131		D	BACKFILL CURBS, SIDWLK,SHLDRS,MUP	2,449.000	2,449.000	CY											1
31133		D	BACKFILL CURBS, SIDWLK,SHLDRS,MUP	1,565.000	1,565.000	CY											3
31143		D	F & I 18" TOPSOIL & PLANTED MEDIAN	1,199.000	1,199.000	CY											3
31201		D	PLACE&REMOVE SURCHARGE MATERIAL-RAMP A	2,278.000	2,278.000	CY											1
31301		D	PLACE&REMOVE SURCHARGE MATERIAL-RAMP B	1,194.000	1,194.000	CY											1
31501		D	PLACE&REMOVE SURCHARGE MATERIAL-RAMP D	1,222.000	1,222.000	CY											1
40001		D	AREA 1### PAVEMENT & BASE ###	1.000	1.000	LS											1
40002		D	AREA 2### PAVEMENT & BASE ###	1.000	1.000	LS											2
40003		D	AREA 3### PAVEMENT & BASE ###	1.000	1.000	LS											3
40103		D	GRADED AGGREGATE BASE COURSE	1,652.000	1,652.000	TON											3

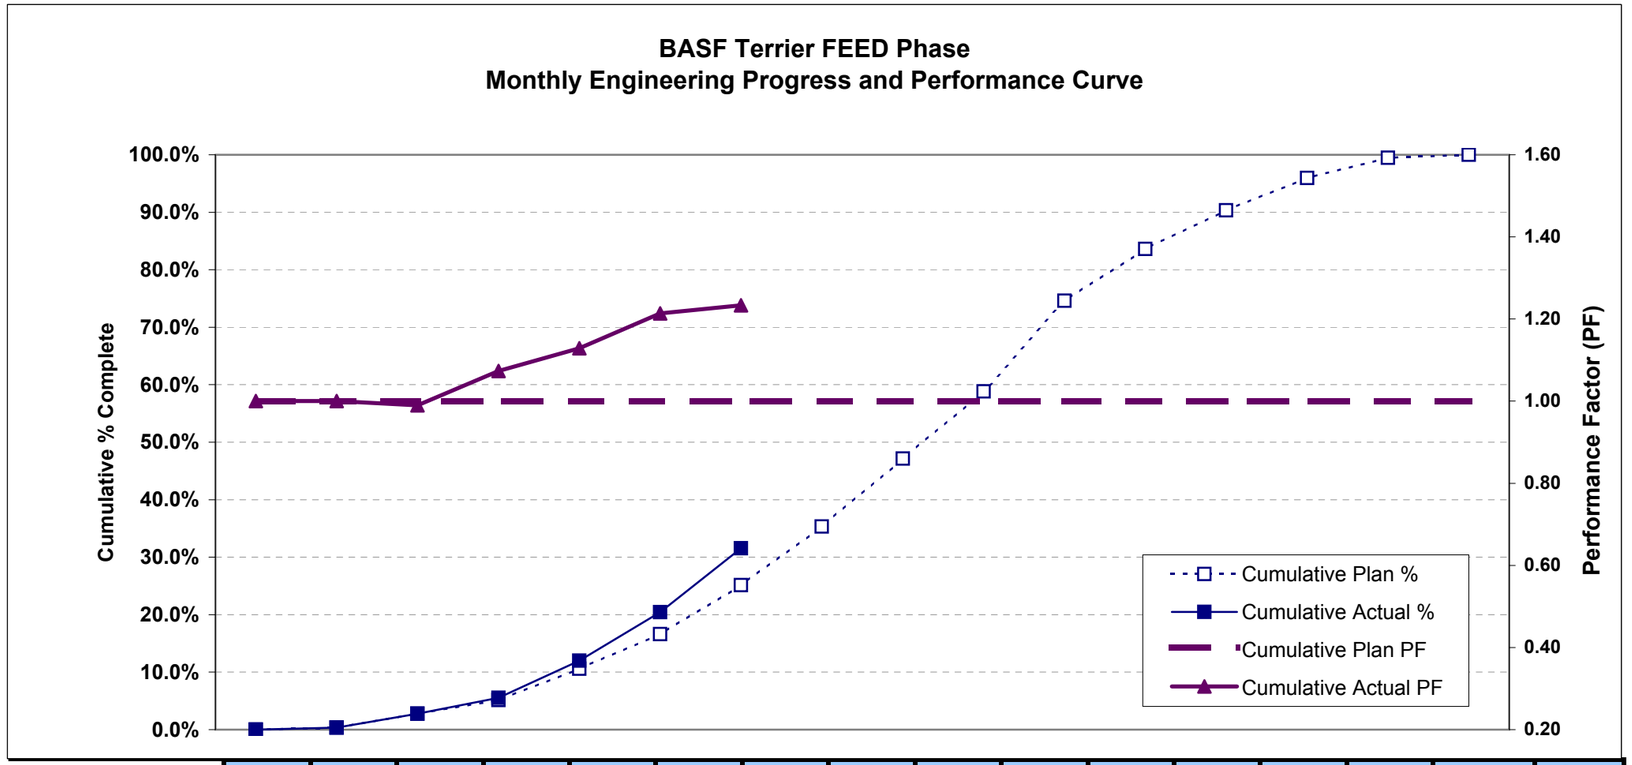


	1-Feb	8-Feb	22-Feb	8-Mar	29-Mar	12-Apr	26-Apr	10-May	24-May	7-Jun	28-Jun	12-Jul	26-Jul-13	9-Aug-13	23-Aug-13	6-Sep-13
Cumulative Plan PF	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00
Cumulative Actual PF	1.00	1.00	0.99	1.07	1.13	1.21	1.23									
Cumulative Plan %	0.0%	0.4%	2.8%	5.2%	10.6%	16.6%	25.1%	35.3%	47.2%	58.8%	74.6%	83.6%	90.3%	96.0%	99.5%	100.0%
Cumulative Actual %	0.0%	0.4%	2.8%	5.5%	12.0%	20.4%	31.6%									

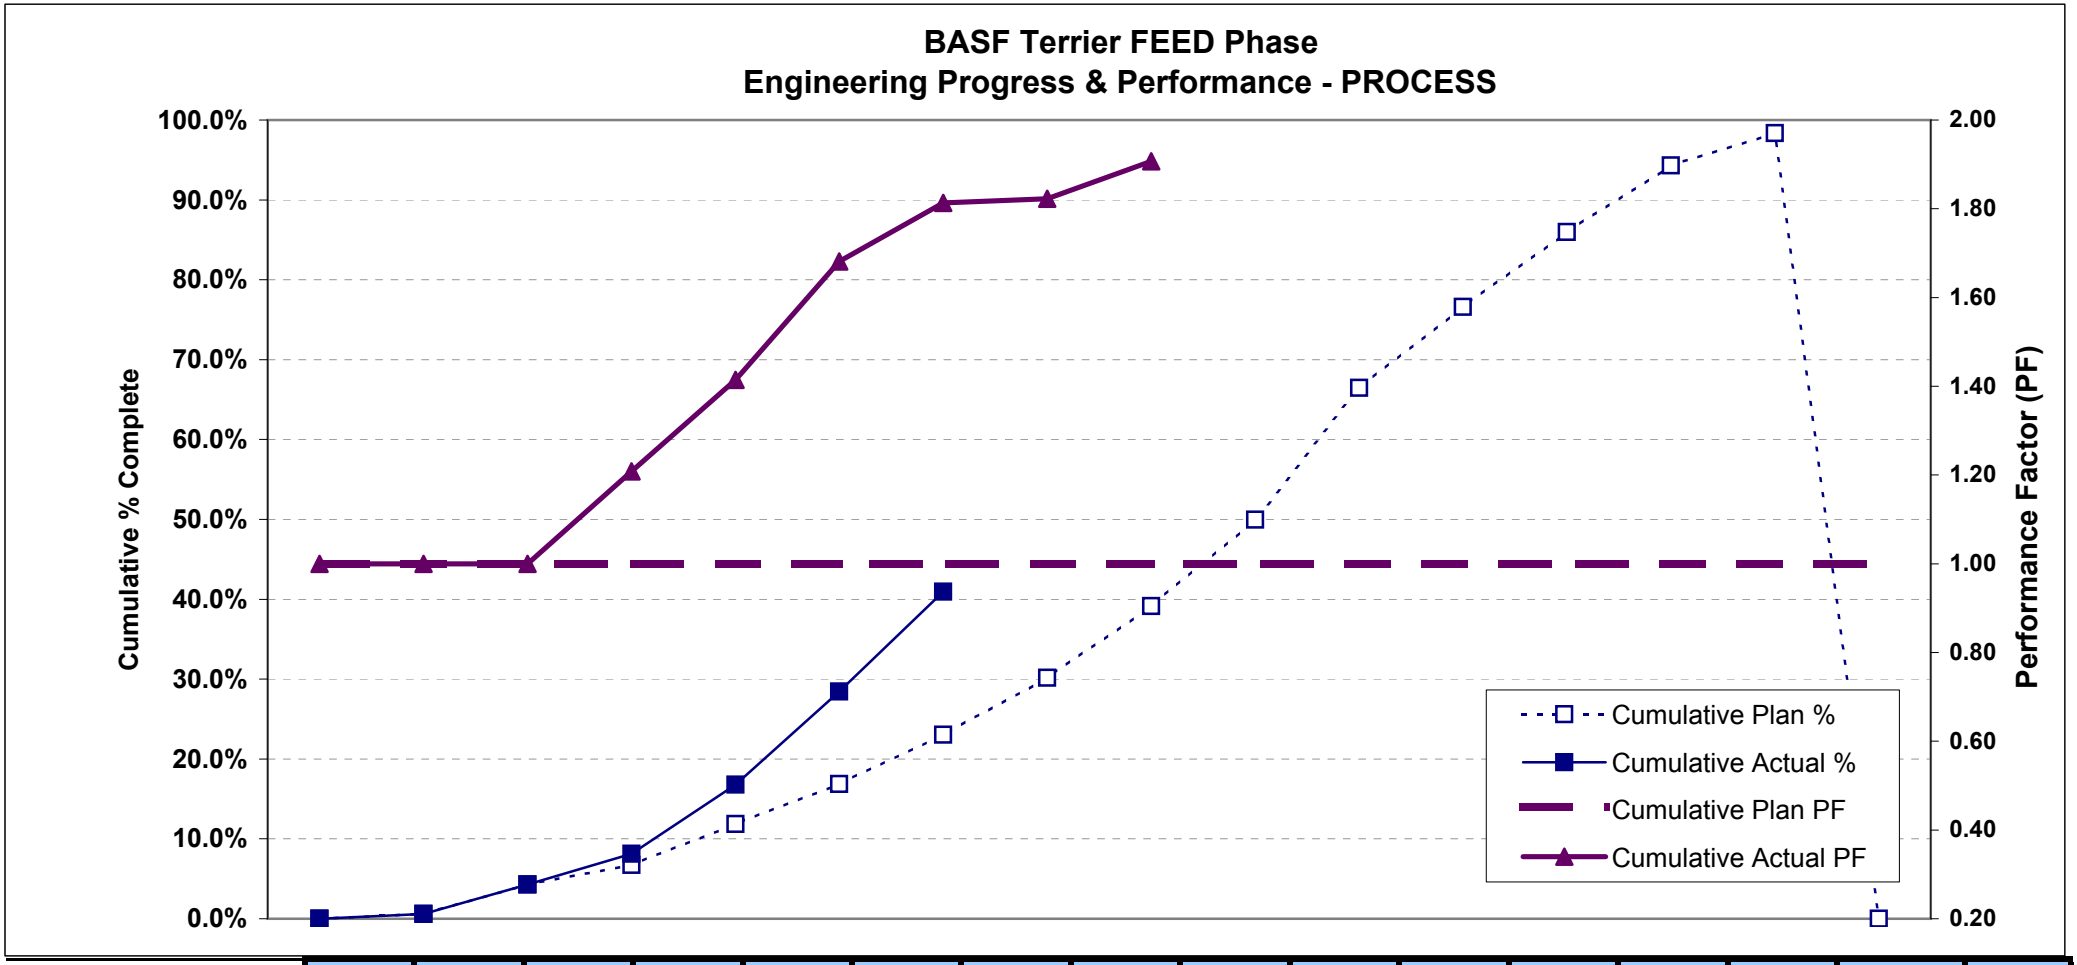


	1-Feb	8-Feb	22-Feb	8-Mar	29-Mar	12-Apr	26-Apr	10-May	24-May	7-Jun	28-Jun	12-Jul	26-Jul-13	9-Aug-13	23-Aug-13	6-Sep-13
Cumulative Plan PF	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00
Cumulative Actual PF	1.00	1.00	1.00	1.21	1.41	1.68	1.81	1.82	1.91							
Cumulative Plan %	0.0%	0.6%	4.3%	6.7%	11.9%	16.9%	23.0%	30.2%	39.2%	50.0%	66.5%	76.6%	86.0%	94.3%	98.4%	0.0%
Cumulative Actual %	0.0%	0.6%	4.3%	8.1%	16.8%	28.4%	40.9%									

FLUOR
Project #: B1SF
Status: 29-Mar-13

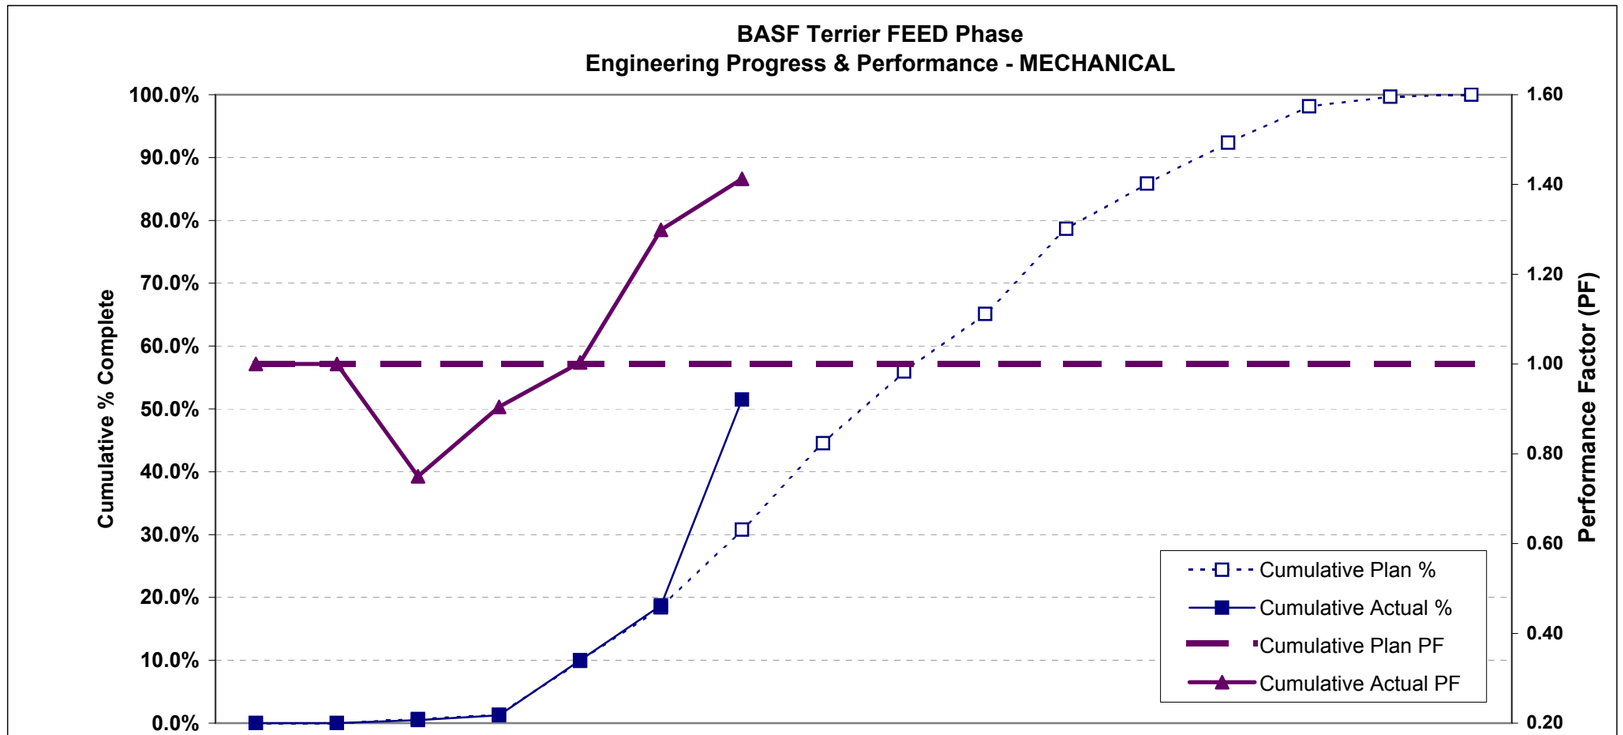


	1-Feb	8-Feb	22-Feb	8-Mar	29-Mar	12-Apr	26-Apr	10-May	24-May	7-Jun	28-Jun	12-Jul	26-Jul-13	9-Aug-13	23-Aug-13	6-Sep-13
Cumulative Plan PF	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00
Cumulative Actual PF	1.00	1.00	0.75	0.90	1.00	1.30	1.41									
Cumulative Plan %	0.0%	0.0%	0.6%	1.3%	9.9%	18.4%	30.8%	44.5%	56.0%	65.1%	78.7%	85.8%	92.4%	98.1%	99.7%	100.0%
Cumulative Actual %	0.0%	0.0%	0.5%	1.2%	10.0%	18.7%	51.5%									


FLUOR
Project #: B1SF
Status: 29-Mar-13

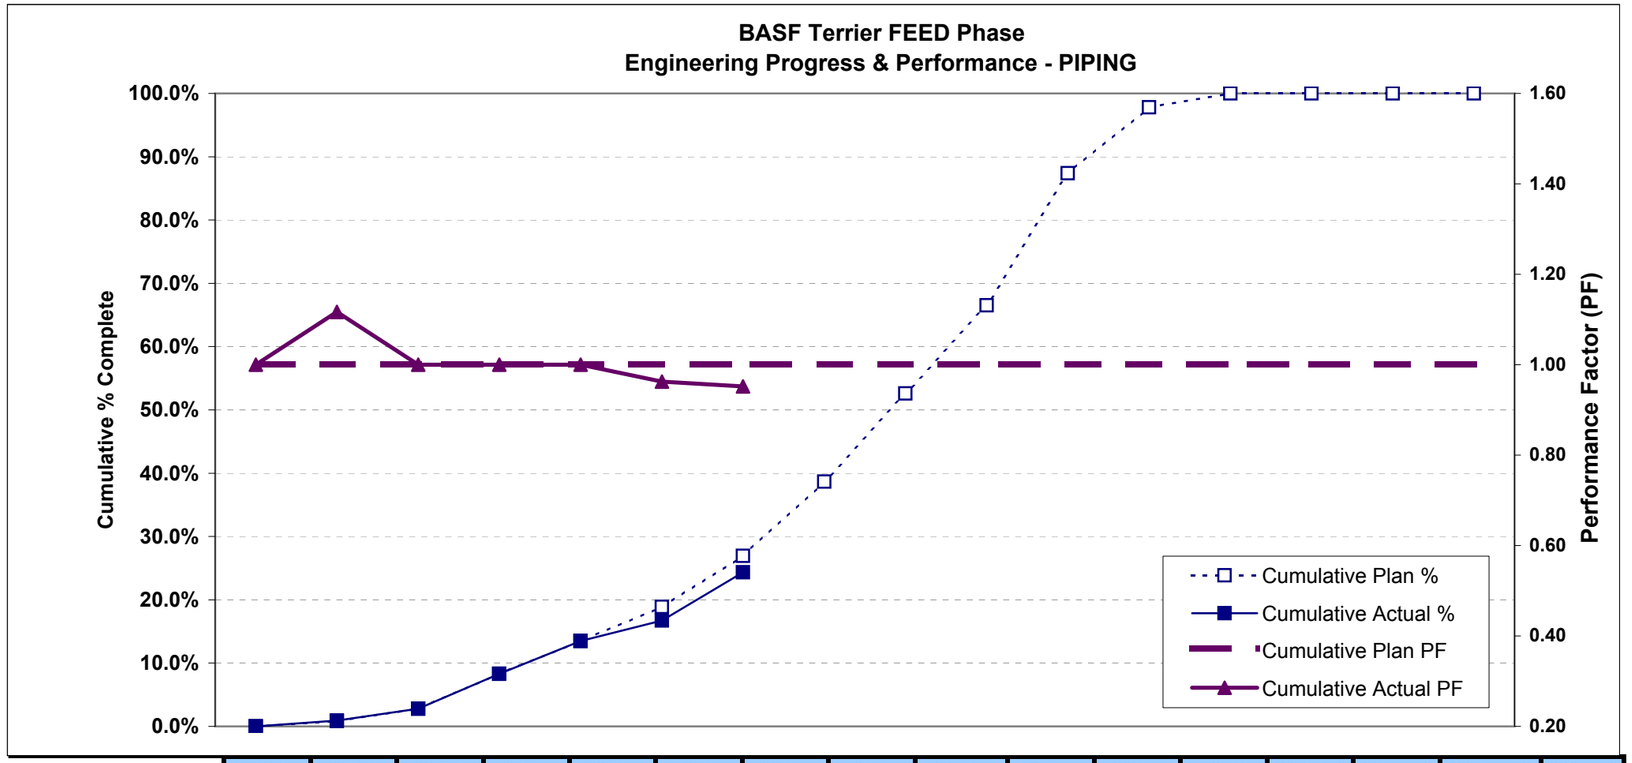


	1-Feb	8-Feb	22-Feb	8-Mar	29-Mar	12-Apr	26-Apr	10-May	24-May	7-Jun	28-Jun	12-Jul	26-Jul-13	9-Aug-13	23-Aug-13	6-Sep-13
Cumulative Plan PF	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00
Cumulative Actual PF	1.00	1.12	1.00	1.00	1.00	0.96	0.95									
Cumulative Plan %	0.0%	0.8%	2.8%	8.3%	13.5%	18.9%	26.9%	38.6%	52.6%	66.5%	87.4%	97.8%	100.0%	100.0%	100.0%	100.0%
Cumulative Actual %	0.0%	0.9%	2.8%	8.3%	13.5%	16.7%	24.3%									

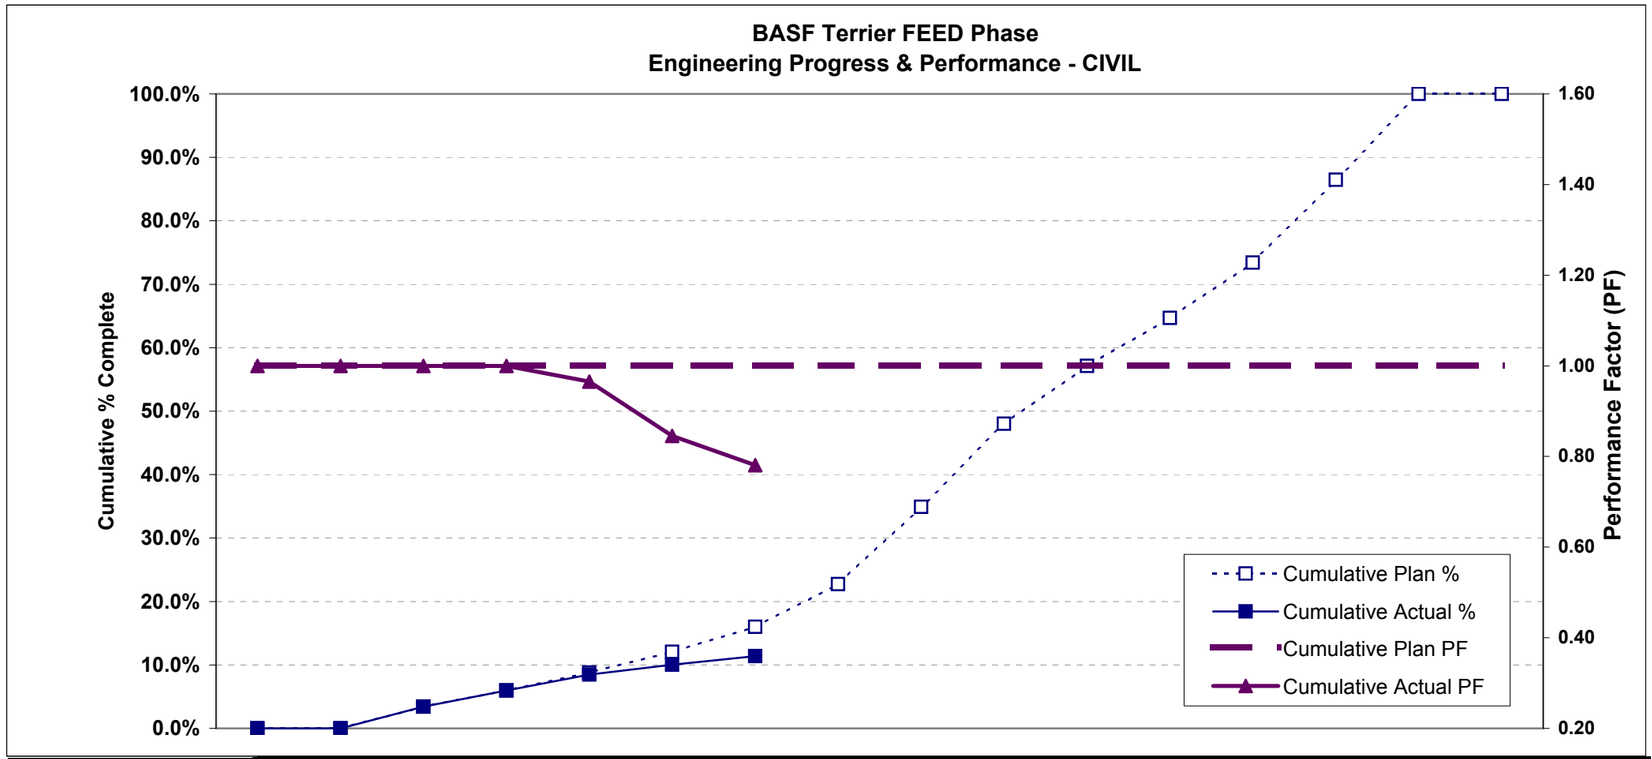


	1-Feb	8-Feb	22-Feb	8-Mar	29-Mar	12-Apr	26-Apr	10-May	24-May	7-Jun	28-Jun	12-Jul	26-Jul-13	9-Aug-13	23-Aug-13	6-Sep-13
Cumulative Plan PF	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00
Cumulative Actual PF	1.00	1.00	1.00	1.00	0.97	0.85	0.78									
Cumulative Plan %	0.0%	0.0%	3.4%	6.0%	8.8%	12.1%	16.0%	22.7%	34.9%	48.0%	57.1%	64.7%	73.4%	86.5%	100.0%	100.0%
Cumulative Actual %	0.0%	0.0%	3.4%	6.0%	8.5%	10.0%	11.4%									

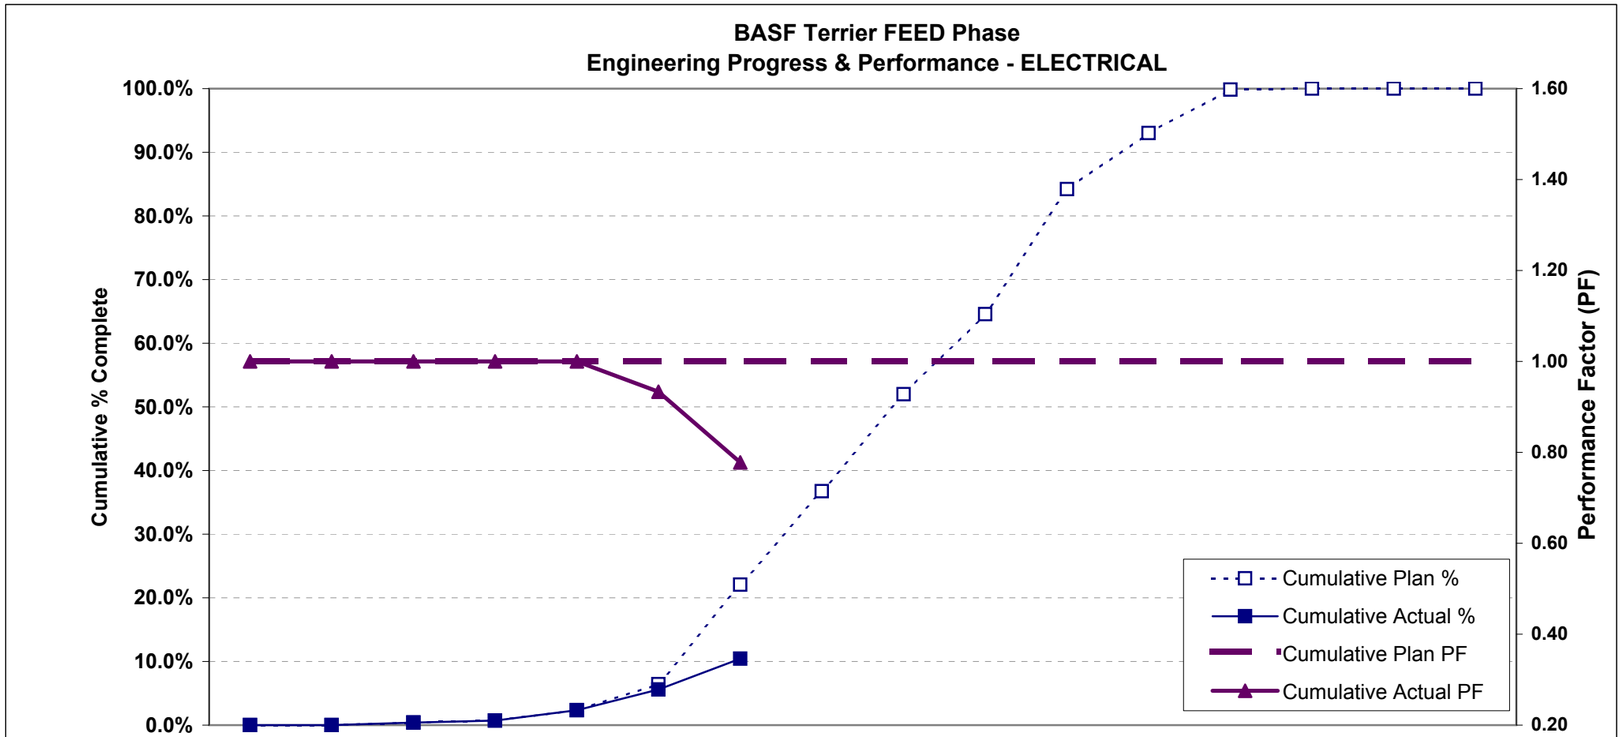

	1-Feb	8-Feb	22-Feb	8-Mar	29-Mar	12-Apr	26-Apr	10-May	24-May	7-Jun	28-Jun	12-Jul	26-Jul-13	9-Aug-13	23-Aug-13	6-Sep-13
Cumulative Plan PF	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00
Cumulative Actual PF	1.00	1.00	1.00	1.00	1.00	0.93	0.78									
Cumulative Plan %	0.0%	0.0%	0.4%	0.7%	2.3%	6.4%	22.1%	36.7%	52.0%	64.6%	84.2%	93.0%	99.8%	100.0%	100.0%	100.0%
Cumulative Actual %	0.0%	0.0%	0.4%	0.7%	2.3%	5.6%	10.4%									

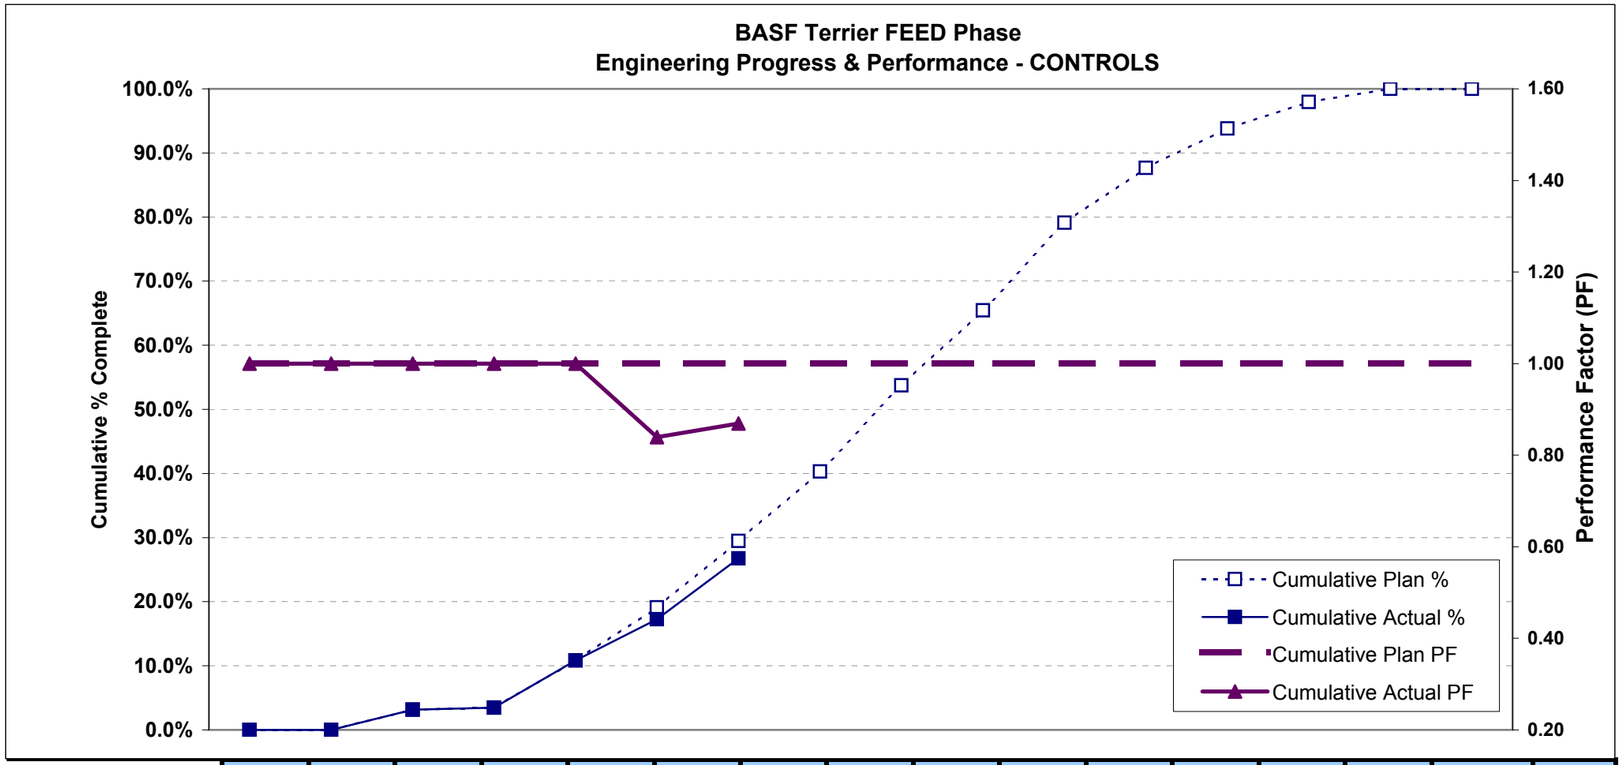


	1-Feb	8-Feb	22-Feb	8-Mar	29-Mar	12-Apr	26-Apr	10-May	24-May	7-Jun	28-Jun	12-Jul	26-Jul-13	9-Aug-13	23-Aug-13	6-Sep-13
Cumulative Plan PF	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00
Cumulative Actual PF	1.00	1.00	1.00	1.00	1.00	0.84	0.87									
Cumulative Plan %	0.0%	0.0%	3.2%	3.5%	10.9%	19.1%	29.5%	40.3%	53.7%	65.4%	79.1%	87.6%	93.8%	97.9%	100.0%	100.0%
Cumulative Actual %	0.0%	0.0%	3.2%	3.5%	10.9%	17.3%	26.8%									

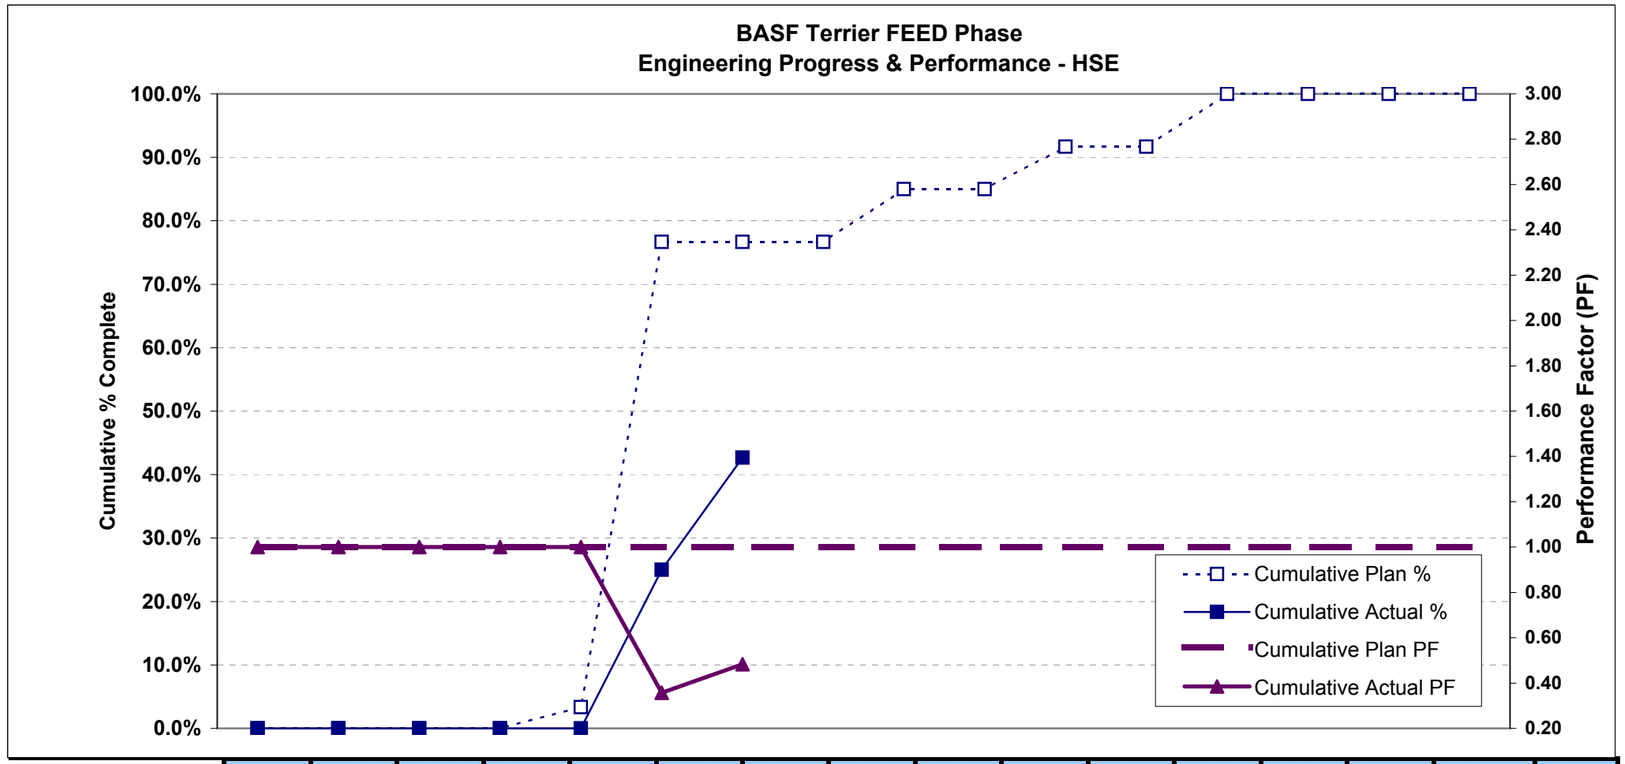

	1-Feb	8-Feb	22-Feb	8-Mar	29-Mar	12-Apr	26-Apr	10-May	24-May	7-Jun	28-Jun	12-Jul	26-Jul-13	9-Aug-13	23-Aug-13	6-Sep-13
Cumulative Plan PF	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00	1.00
Cumulative Actual PF	1.00	1.00	1.00	1.00	1.00	0.36	0.48									
Cumulative Plan %	0.0%	0.0%	0.0%	0.0%	3.3%	76.7%	76.7%	76.7%	85.0%	85.0%	91.7%	91.7%	100.0%	100.0%	100.0%	100.0%
Cumulative Actual %	0.0%	0.0%	0.0%	0.0%	0.0%	25.0%	42.7%									

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
Green Line Extension Initial Baseline Schedule 20170908		457	01-Oct-18	30-Jun-20	226
Design		57	01-Oct-18	18-Dec-18	626
Roadway Bridges		40	11-Oct-18	10-Dec-18	74
Broadway (Bridge No. S-17-013)		40	11-Oct-18	10-Dec-18	74
DBWBR140	Broadway Bridge - RFC Design - MBTA Review & Comment	40	11-Oct-18	10-Dec-18	74
Stations		50	09-Oct-18	18-Dec-18	245
Magoun Square		30	09-Oct-18	20-Nov-18	229
DSTA350	Magoun Square Station - RFC Design - Submit to MBTA for Review	30	09-Oct-18	20-Nov-18	229
Gilman Square		30	09-Oct-18	20-Nov-18	220
DSTA450	Gilman Square Station - RFC Design - Submit to MBTA for Review	30	09-Oct-18	20-Nov-18	220
College Ave		30	09-Oct-18	20-Nov-18	265
DSTA250	College Ave Station - RFC Design - Submit to MBTA for Review	30	09-Oct-18	20-Nov-18	265
East Somerville		20	09-Oct-18	06-Nov-18	218
DSTA540	E Somerville Station - Intermediate Design - MBTA Review & Comment	20	09-Oct-18	06-Nov-18	218
Ball Square		45	16-Oct-18	18-Dec-18	52
DSTA130	Ball Square Station - Intermediate Design - Submit to MBTA for Review	45	16-Oct-18	18-Dec-18	52
Lechmere Station		40	23-Oct-18	17-Dec-18	41
DSTA650	Lechmere Station - RFC Design - Submit to MBTA for Review	40	23-Oct-18	17-Dec-18	41
Retaining & Noise Walls		20	23-Oct-18	19-Nov-18	83
DRTW385	Retaining & Noise Walls - RFC Design - Submit to MBTA for Review	20	23-Oct-18	19-Nov-18	83
Track		31	01-Oct-18	12-Nov-18	223
Medford & Union Square		25	09-Oct-18	12-Nov-18	135
DRWB2550	Medford & Union Line Track - RFC Design - Submit to MBTA for Review	25	09-Oct-18	12-Nov-18	135
Rail Yard		20	01-Oct-18	26-Oct-18	225
DRWB2450	Rail Yard Track - RFC Design - MBTA Review & Comment	20	01-Oct-18	26-Oct-18	225
Drainage - Segment 1		5	23-Oct-18	30-Oct-18	656
DDRA300	Drainage S1 - Final Design Docs - Submit to MBTA for Review	5	23-Oct-18	30-Oct-18	656
Drainage - Segment 3		5	23-Oct-18	30-Oct-18	656
DDRA460	Drainage S3 - Final Design Docs - Submit to MBTA for Review	5	23-Oct-18	30-Oct-18	656
Drainage - Segment 4		5	23-Oct-18	30-Oct-18	656
DDRA510	Drainage S4 - Final Design Docs - Submit to MBTA for Review	5	23-Oct-18	30-Oct-18	656
Drainage - Segment 5		5	23-Oct-18	30-Oct-18	656
DDRA610	Drainage S5 - Final Design Docs - Submit to MBTA for Review	5	23-Oct-18	30-Oct-18	656
Drainage - Segment 6		5	23-Oct-18	30-Oct-18	656
DDRA560	Drainage S6 - Final Design Docs - Submit to MBTA for Review	5	23-Oct-18	30-Oct-18	656
Systems		34	09-Oct-18	23-Nov-18	268
Signaling		25	09-Oct-18	12-Nov-18	53
DUDP1030	Signaling - RFC Design - Submit to MBTA for Review	25	09-Oct-18	12-Nov-18	53
Power & OCS		25	09-Oct-18	12-Nov-18	110
DOCS125	Power & OCS - RFC Design - Submit to MBTA for Review	25	09-Oct-18	12-Nov-18	110
Communications		25	22-Oct-18	23-Nov-18	268
DUDP830	Communications - RFC Design - Submit to MBTA for Review	25	22-Oct-18	23-Nov-18	268
Community Path		40	08-Oct-18	05-Dec-18	268
DCMP210	Community Path - Pre-RFC Design - MBTA, 3rd Party, Govt Review & Comment	40	08-Oct-18	05-Dec-18	268
Roadways & Traffic Improvements		10	10-Oct-18	24-Oct-18	638
DRDW185	Roadways - Final Design Docs - Submit to MBTA for Review	5	10-Oct-18	17-Oct-18	638
DRDW190	Roadways - Final Design Docs - MBTA Review & Approve	5	17-Oct-18	24-Oct-18	638
Procurement		232	02-Oct-18	09-Oct-19	56
Communications Equipment		232	02-Oct-18	09-Oct-19	56
PRCME120	Communications Equipment - Place Order	2	02-Oct-18	04-Oct-18	56
PRCME100	Communications Equipment - Fabricate & Deliver	230	04-Oct-18	09-Oct-19	56
Fare Collection System Equipment		202	02-Oct-18	21-Aug-19	60
PRFCS120	Fare Collection System Equipment - Place Order	2	02-Oct-18	04-Oct-18	60
PRFCS100	Fare Collection System Equipment - Fabricate & Deliver	200	04-Oct-18	21-Aug-19	60
Feeder Cabling		142	02-Oct-18	17-May-19	94

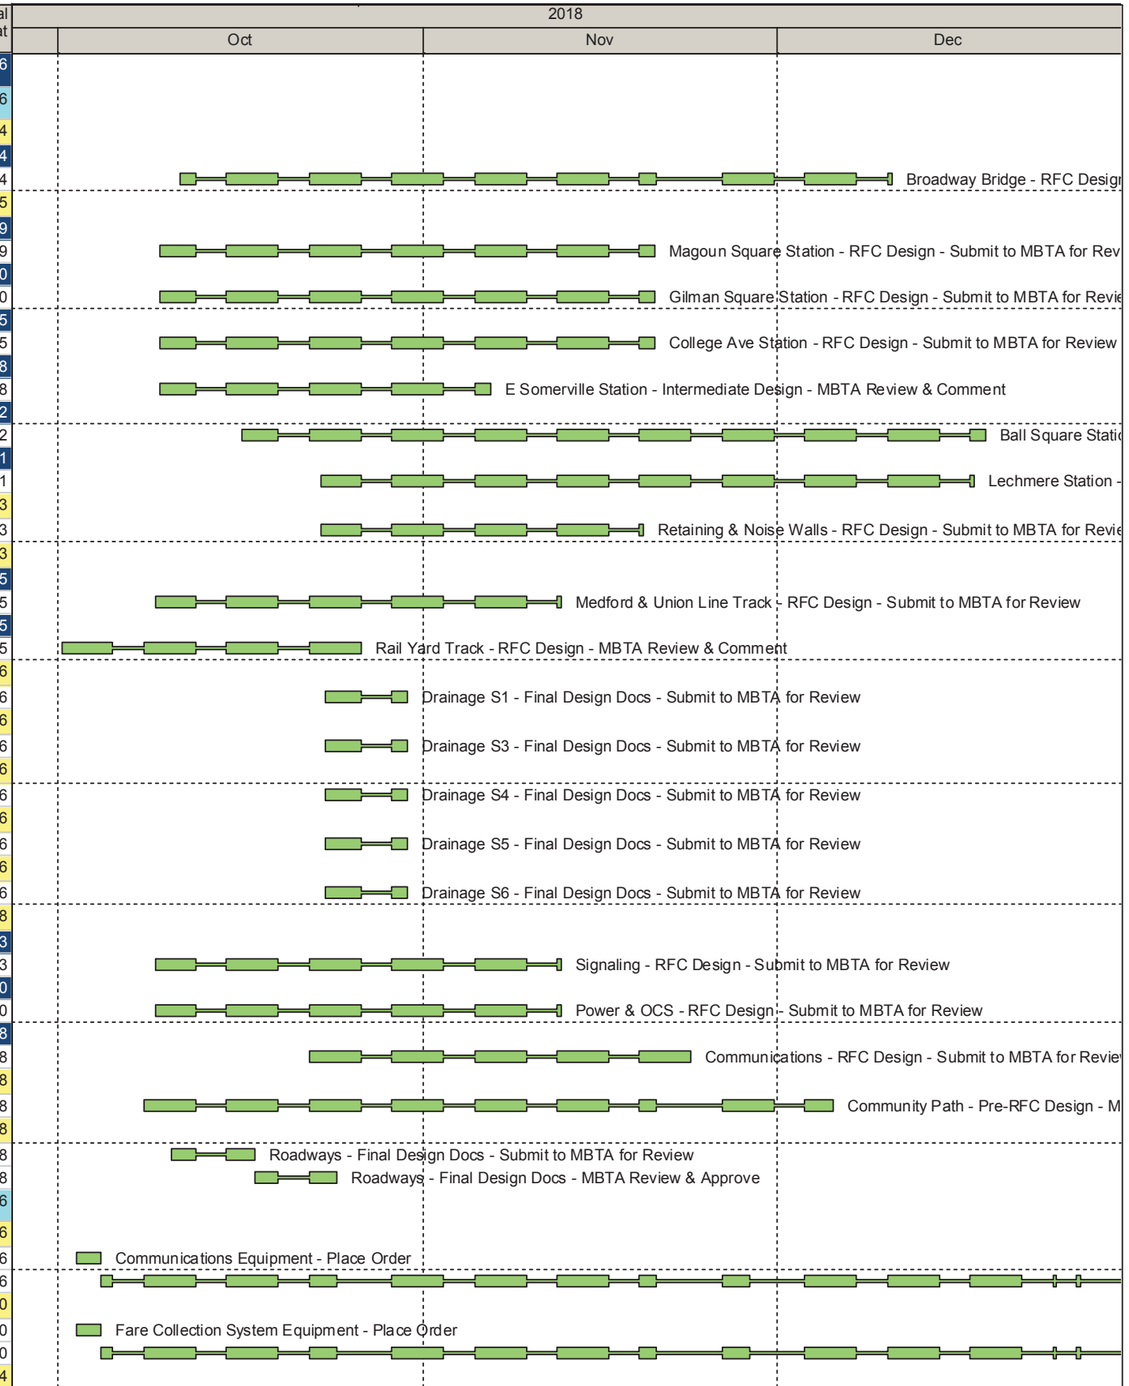

Actual Work | Critical Remaining Work | Remaining Work | Milestone


GLX CONSTRUCTORS

Green Line Extension Proposal Development Schedule

Page: 1 of 2 Data Date: 28-Sep-17 Print: 09-Sep-17

GV20170258-283.pdf

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRCBL120	Feeder Cabling - Place Order	2	02-Oct-18	04-Oct-18	94
PRCBL100	Feeder Cabling - Fabricate & Deliver	140	04-Oct-18	17-May-19	94
Trackwork		122	11-Oct-18	29-Apr-19	40
PRTRK120	Trackwork - Place Order	2	11-Oct-18	12-Oct-18	40
PRTRK100	Trackwork - Fabricate & Deliver	120	15-Oct-18	29-Apr-19	40
Construction		397	02-Oct-18	30-Jun-20	81
Segment 1		320	23-Oct-18	25-Mar-20	143
Drainage		320	23-Oct-18	25-Mar-20	143
C1DRA100	Drainage S1 - SUMMARY	320	23-Oct-18	25-Mar-20	143
C1DRA135	Main Drainage - Excavate & Install	20	23-Oct-18	27-Nov-18	127
Segment 2		51	04-Oct-18	26-Dec-18	0
Earthwork, Clearing & Grubbing		51	04-Oct-18	26-Dec-18	0
C2CGE110	Earthwork / Access Road - Segment 2	51	04-Oct-18	26-Dec-18	0
Segment 3		382	23-Oct-18	30-Jun-20	81
Earthwork, Clearing & Grubbing		94	23-Oct-18	26-Mar-19	33
C3CGE110	Earthwork - Segment 3	94	23-Oct-18	26-Mar-19	33
Drainage		382	23-Oct-18	30-Jun-20	81
C3DRA100	Drainage S3 - SUMMARY	382	23-Oct-18	30-Jun-20	81
C3DRA105	Main Drainage - Excavate & Install	46	23-Oct-18	11-Jan-19	33
Segment 4		82	02-Oct-18	13-Feb-19	396
Utilities		15	23-Oct-18	15-Nov-18	448
C4UT115	Utilities - Relocate Overhead ELEC STA 208+25 MB-WB	10	23-Oct-18	08-Nov-18	453
C4UT120	Utilities - Relocate Overhead ELEC STA 208+50 MB-WB	10	23-Oct-18	08-Nov-18	453
C4UT125	Utilities - Relocate Underground ELEC STA 210+50 MB-WB	15	23-Oct-18	15-Nov-18	448
Drainage		67	23-Oct-18	13-Feb-19	275
C4DRA100	Drainage S4 - SUMMARY	67	23-Oct-18	13-Feb-19	275
C4DRA115	Main Drainage - Excavate & Install	67	23-Oct-18	13-Feb-19	275
Viaducts		37	02-Oct-18	03-Dec-18	285
Medford (MBV)		37	02-Oct-18	03-Dec-18	285
Medford Branch South		37	02-Oct-18	03-Dec-18	285
C4MBV340	Medford Viaduct (MBV) (Piers 22 - 24) - Steep Pipe Pile Caps	13	02-Oct-18	19-Oct-18	69
C4MBV295	Medford Viaduct (MBV) (Piers 25 - 29, 32) - Drilled Shafts	24	19-Oct-18	03-Dec-18	285
C4MBV360	Medford Viaduct (MBV) (Piers 17 - 19) - Drilled Shaft Caps	15	23-Oct-18	15-Nov-18	40
Medford Branch North		10	19-Oct-18	06-Nov-18	285
C4MBV395	Medford Viaduct (MBV) (Piers 33 - 37) - Drilled Shaft Piers	10	19-Oct-18	06-Nov-18	285
Segment 5 - VMF		127	23-Oct-18	17-May-19	111
Clearing & Grubbing		127	23-Oct-18	17-May-19	111
C5STR140	VMF - Vehicle Maint Building - Complete Site Clearing & Grading	102	23-Oct-18	09-Apr-19	35
C5STR150	VMF - Clearing, Excavation, Site Prep - SUMMARY	127	23-Oct-18	17-May-19	111
Segment 6 - Union Square		244	02-Oct-18	29-Oct-19	50
Drainage		229	23-Oct-18	29-Oct-19	50
C6DRA100	Drainage S6 (Union Sq Branch) - SUMMARY	229	23-Oct-18	29-Oct-19	50
C6DRA115	Union Sq Line Main Drainage - Excavate & Install	5	23-Oct-18	01-Nov-18	224
Viaducts		178	02-Oct-18	16-Jul-19	66
Union Square EB (UEV)		178	02-Oct-18	16-Jul-19	66
C6UEV100	Union Square EB Viaduct (UEV) - SUMMARY	178	02-Oct-18	16-Jul-19	66
C6UEV105	Union Square EB Viaduct (UEV) - Steel Pipe Piles	24	02-Oct-18	07-Nov-18	66

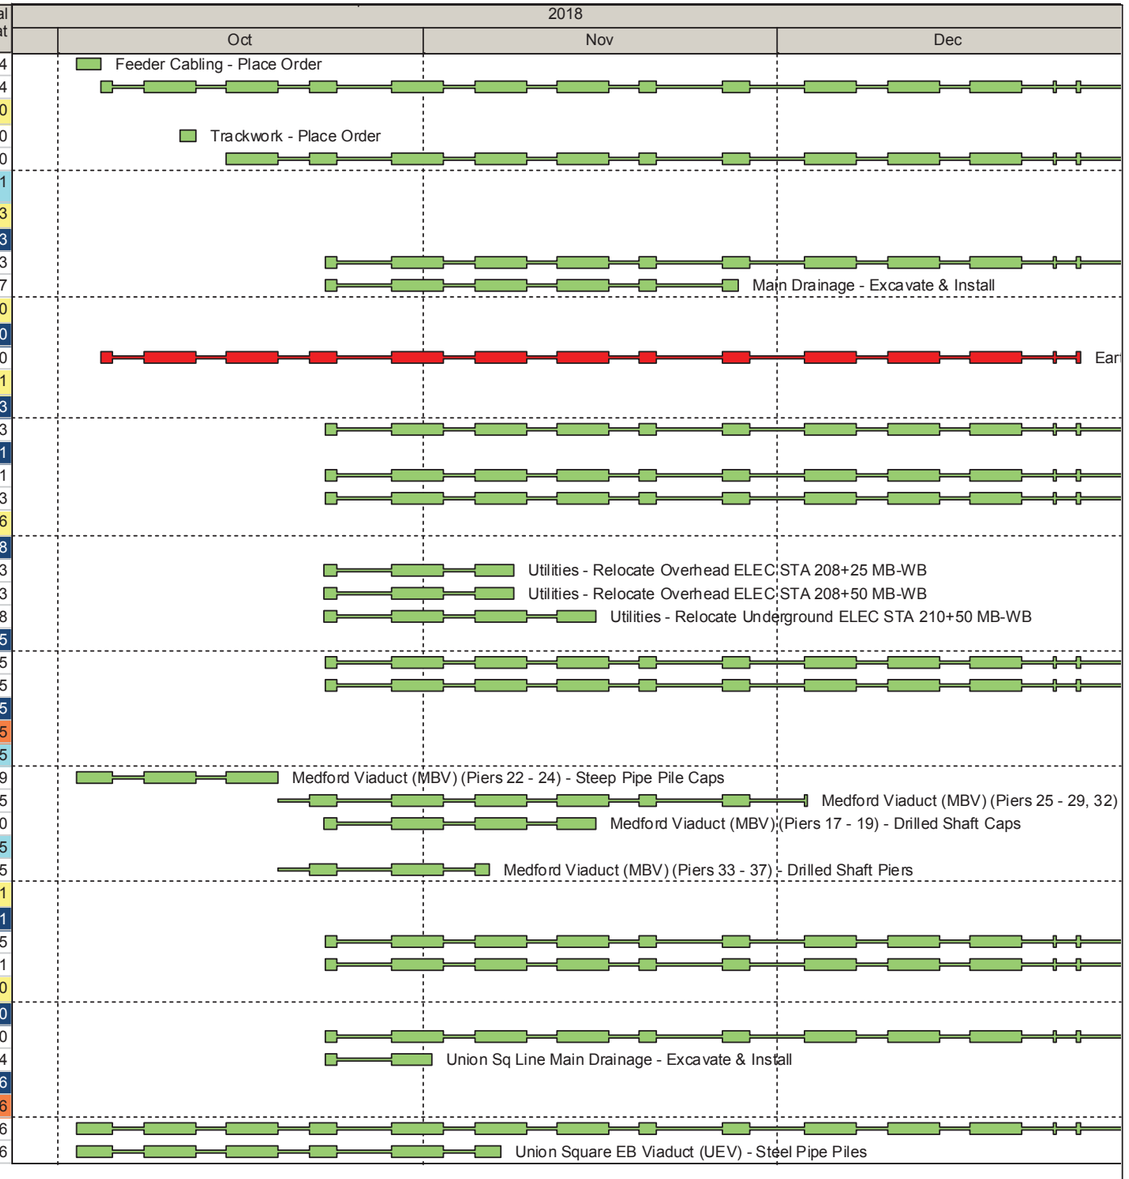

Actual Work | Critical Remaining Work | Remaining Work | Milestone

GLX CONSTRUCTORS

Green Line Extension Proposal Development Schedule

Page: 2 of 2 Data Date: 28-Sep-17 Print: 09-Sep-17

GV20170258-283.pdf



Segment 6 - Union Square


0+00

2022: Mar, Feb, Jan
2021: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May, Apr, Mar, Feb, Jan
2020: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May, Apr, Mar, Feb, Jan
2019: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May, Apr, Mar, Feb, Jan
2018: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May, Apr, Mar, Feb, Jan
2017: Dec, Nov, Oct, Sep, Aug, Jul, Jun, May

Milestone 4c

Milestone 4b

Milestone 4a

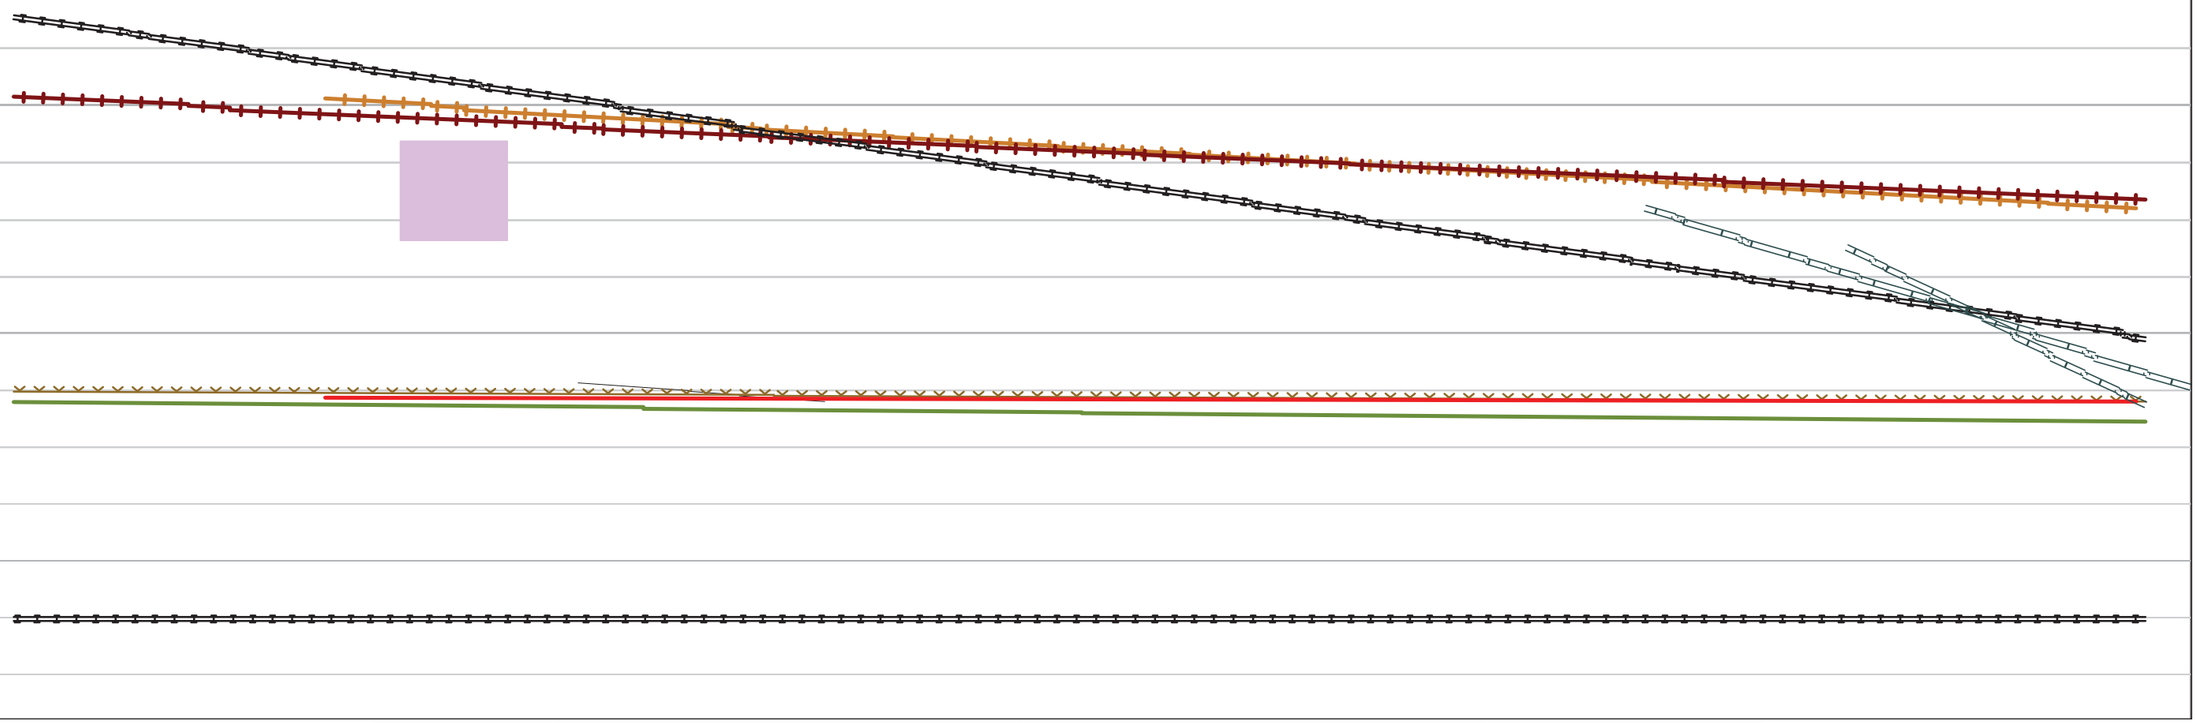

Clearing & Grubbing		Viaducts		Systems	
Earthwork		Union Square Station		GLXFMS	
Main Drainage		Track - Un Sq EB			
Retaining Wall		Track - Un Sq WB			

Project: GLX Constructors
Printed: 08.30.2017

GLX CONSTRUCTORS

GV20170258-283.pdf

APPENDIX 6

GLX Activity Codes

GLX - Activity Codes

EPS/Project

Activity Code

GLX DB-21 Green Line Extension Initial Baseline Schedule 20170908

GLX Area / Segment

Code Value	Description
S1	Segment 1
S2	Segment 2
S3	Segment 3
S4	Segment 4
S5	Segment 5 VMF
S6	Segment 6 Union Square Branch
PW	Project Wide

GLC Critical Path

Code Value	Description
CP1	CP1
CP2	CP2
CP3	CP3

GLX Change Order

GLX Construction / Installation Category

Code Value	Description
CLGR	Clearing & Grubbing
CPTH	Community Paths
DR	Drainage
FN	Fencing
PB	Pedestrian Bridges
PMPS	Pump Stations
RRBR	Railroad Bridge
RWNB	Retaining Walls / Noise Barriers
RWTI	Roadway & Trafic Improvements
RWBRs	Roadway Bridges - Specific
RWBRs.BW	Broadway (Bridge No. S-17-013)
RWBRs.CD	Cedar St (Somerville) (Bridge No. S-17-012)
RWBRs.CA	College Ave (Medford) (Bridge No. M-12-012)
RWBRs.LW	Lowell St (Somerville) (Bridge No. S-17-011)
RWBRs.MD	Medford St (Somerville) (Bridge No. S-17-007)
RWBRs.SS	School St (Somerville) (Bridge No. S-17-008)
RWBRs.WS	Walnut St (Somerville) (Bridge No. S-17-006)
RWB	Roadway Bridges - General
STA	Stations
STA.Ball	Ball Square

GLX - Activity Codes

EPS/Project

Activity Code

STA.Coll	College Ave
STA.Mago	Magoun Square
STA.Gilm	Gilman Square
STA.ESom	E Somerville
STA.Lech	Lechmere
STA.Unio	Union Square
STRU	Structures
SYS	Systems
TRK	Track
UND	Underpasses
UTIL	Utilities
UTBR	Utility Bridge
VMF	Vehicle Maintenance Facility
VMF.TOB	Transportation Office Building
VMF.VMB	Vehicle Maintenance Building
VIAD	Viaducts
VIAD.LEV	Lechmere Viaduct
VIAD.MBV	Medford Viaduct
VIAD.UWV	Union Sq WB Viaduct
VIAD.UEV	Union Sq EB Viaduct
(New)	(New Code Value)

GLX Delivery

Code Value	Description
MAT	Material
EQP	Equipment

GLX Design

Code Value	Description
PW	Project Wide
PW.CLGR	Clearing & Grubbing
PW.PP	Community Paths
PW.DR	Drainage
PW.FN	Fencing
PW.NB	Noise Barriers
PW.RW	Retaining Walls
PW.RDW	Roadways
PW.TRK	Track
PB	Pedestrian Bridges
RRB	Railroad Bridge
RRB.WS	Washington St

GLX - Activity Codes

EPS/Project

Activity Code

RWB	Roadway Bridges
RWB.BW	Broadway (Bridge No. S-17-013)
RWB.CD	Cedar St (Somerville) (Bridge No. S-17-012)
RWB.CA	College Ave (Medford) (Bridge No. M-12-012)
RWB.LW	Lowell St (Somerville) (Bridge No. S-17-011)
RWB.MD	Medford St (Somerville) (Bridge No. S-17-007)
RWB.SS	School St (Somerville) (Bridge No. S-17-008)
RWB.WS	Walnut St (Somerville) (Bridge No. S-17-006)
STA	Stations
STA.Ball	Ball Square
STA.Coll	College Ave
STA.Mago	Magoun Square
STA.Gilm	Gilman Square
STA.ESom	E Somerville
STA.Lech	Lechmere
STA.Unio	Union Square
STRU	Structures
VIA	Viaducts
UTBR	Utility Bridges
UTIL	Utilities
UND	Underpasses
SYS	Systems
VMF	Vehicle Maintenance Facility
VMF.TOB	Transportation Office Building
VMF.VMB	Vehicle Maintenance Building

GLX Drilling Subs

Code Value	Description
DRLSBS	Drilling Subs

GLX Estimating Code

Code Value	Description
100000	MOT
110000	Demo & Removals
120000	Erosion Control & Earthwork
130000	Drainage
140000	Pavement & Base
150000	Bridges
160000	Walls
170000	Railroad Work
180000	VMF

GLX - Activity Codes

EPS/Project

Activity Code

190000	Stations
200000	Systems
210000	Misc Roadway
220000	Community Path
230000	Landscaping
240000	Roadway Electrical
250000	Utility Relocations
300000	Haz Material Remediation
800000	Holding Accounts
995000	Supplemental Direct Cost Items
997000	Indirect Costs

GLX Milestone

Code Value	Description
MS	Major Milestones
L1	Level 1 Executive Management
L2	Level 2 Project Management
L3	Level 3 Field Management

GLX Phase

Code Value	Description
DSN	Design
CDRL	Contract Deliverables
PRC	Procurement
PreC	Pre-Construction
CON	Construction
TST	Testing / Commissioning
CLS	Closeout

GLX Price Item

GLX Procurement/Fabrication

Code Value	Description
MAT	Material
EQP	Equipment

GLX Responsibility

Code Value	Description
GLX	Greenline Constructors
3rd	3rd Party
MBTA	Mass Bay Transit Authority
MassDOT	Mass Dept of Transportation
MBTA3rd	Both MBTA & 3rd Party

GLX - Activity Codes

EPS/Project

Activity Code

GLX Review / Acceptance

Code Value	Description
MBTA	by MBTA
3rd	by 3rd Party, Govt, etc.
MB3rd	by MBTA & 3rd Party

GLX Risk Analysis

Code Value	Description
MDCP1	Medford Branch CP1
MDCP2	Medford Branch CP2
MDCP3	Medford Branch CP3
USCP1	Union Square CP1
USCP2	Union Square CP2
USCP3	Union Square CP3

GLX Standard Cost Category

Code Value	Description
10	Guideway & Track Elements
20	Stations, Stops, Terminals, Intermodal
30	Support Facilities: Yards, Shops, Admin Bldgs
40	Sitework & Special Conditions
50	Systems
60	ROW, Land, Existing Improvements
70	Vehicles
80	Professional Services
90	Unallocated Contingency
100	Finance Charges

GLX Submittal

GLX Summary Level

Code Value	Description
LVL1	Summary Level 1
LVL2	Summary Level 2
LVL3	Summary Level 3
LVL4	Summary Level 4
LVL5	Summary Level 5
LVL6	Summary Level 6

GLX TILOS

Code Value	Description
T	Show TILOS for MD and VMF

GLX - Activity Codes

EPS/Project

Activity Code

TUS	Show TILOS for Union Square

GLX WBS Summary

Code Value	Description
WBS	WBS Summary
LVL1	Summary Level 1
LVL2	Summary Level 2
LVL3	Summary Level 3
LVL4	Summary Level 4
LVL5	Summary Level 5
LVL6	Summary Level 6

GLX Work Type

Code Value	Description
ENG	Engineering
SYS	Systems
MBTA	MBTA ReviApv
CDRL	CDRL
TRKW	Trackwork
PROC	Procurement
COMS	Communications
OCS	CAT System
TPS	Traction Power
TC	Train Control
TST	Testing
STA	Stations
MD	Main Drainage
MSs	Milestones
UTIL	Utility Reloc
CG	Clearing & Grubbing
STR	Structures
RWBR	Roadway Bridge
EW	Earthwork
RW	Roadway
DEMO	Demolition
ROW	ROW
RWs	Retaining & Noise Walls
DB	Ductbank
NW	Noise Walls
CONS	Construction
CPTH	Community Path

GLX - Activity Codes

EPS/Project

Activity Code	
PRMS	Permits
RRBR	Railroad Bridge
PBR	Pedestrian Bridge
VIAD	Viaduct
TD	Track Drainage

APPENDIX 7

Work Breakdown Schedule

WBS Code	WBS Name	Project ID	Project Status
GLX DB-21	Green Line Extension Initial Baseline Schedule 20170	GLX DB-21	Active
GLX DB-21.1	Milestones	GLX DB-21	Active
GLX DB-21.2	Design	GLX DB-21	Active
GLX DB-21.2.1	Project Wide	GLX DB-21	Active
GLX DB-21.2.1.6	Documentation / Pre-Design Plan	GLX DB-21	Active
GLX DB-21.2.2	Roadway Bridges	GLX DB-21	Active
GLX DB-21.2.2.10	Medford St (Somerville) (Bridge No. S-17-007)	GLX DB-21	Active
GLX DB-21.2.2.1	Broadway (Bridge No. S-17-013)	GLX DB-21	Active
GLX DB-21.2.2.5	Cedar St (Somerville) (Bridge No. S-17-012)	GLX DB-21	Active
GLX DB-21.2.2.7	College Ave (Medford) (Bridge No. M-12-012)	GLX DB-21	Active
GLX DB-21.2.2.3	School St (Somerville) (Bridge No. S-17-008)	GLX DB-21	Active
GLX DB-21.2.2.4	Walnut St (Somerville) (Bridge No. S-17-006)	GLX DB-21	Active
GLX DB-21.2.2.6	Lowell St (Somerville) (Bridge No. S-17-011)	GLX DB-21	Active
GLX DB-21.2.9	Stations	GLX DB-21	Active
GLX DB-21.2.9.10	Magoun Square	GLX DB-21	Active
GLX DB-21.2.9.5	Gilman Square	GLX DB-21	Active
GLX DB-21.2.9.2	College Ave	GLX DB-21	Active
GLX DB-21.2.9.1	East Somerville	GLX DB-21	Active
GLX DB-21.2.9.3	Ball Square	GLX DB-21	Active
GLX DB-21.2.9.7	Lechmere Station	GLX DB-21	Active
GLX DB-21.2.9.8	Union Square	GLX DB-21	Active
GLX DB-21.2.6	Viaducts	GLX DB-21	Active
GLX DB-21.2.6.1	Lechmere (LEV) Pkg 2	GLX DB-21	Active
GLX DB-21.2.6.2	Lechmere (LEV) Pkg 1	GLX DB-21	Active
GLX DB-21.2.6.10	Medford (MBV)	GLX DB-21	Active
GLX DB-21.2.6.6	Union Square EB (UEV)	GLX DB-21	Active
GLX DB-21.2.6.3	Union Square WB (UWV)	GLX DB-21	Active
GLX DB-21.2.15	Retaining Walls (Early)	GLX DB-21	Active
GLX DB-21.2.8	Retaining & Noise Walls	GLX DB-21	Active
GLX DB-21.2.18	Track	GLX DB-21	Active
GLX DB-21.2.18.2	Medford & Union Square	GLX DB-21	Active
GLX DB-21.2.18.1	Rail Yard	GLX DB-21	Active
GLX DB-21.2.12	Drainage - Segment 1	GLX DB-21	Active
GLX DB-21.2.11	Drainage - Segment 2	GLX DB-21	Active
GLX DB-21.2.17	Drainage - Segment 3	GLX DB-21	Active
GLX DB-21.2.19	Drainage - Segment 4	GLX DB-21	Active
GLX DB-21.2.23	Drainage - Segment 5	GLX DB-21	Active
GLX DB-21.2.22	Drainage - Segment 6	GLX DB-21	Active
GLX DB-21.2.14	Railroad Bridge	GLX DB-21	Active
GLX DB-21.2.14.3	Washington St Bridge	GLX DB-21	Active
GLX DB-21.2.5	Systems	GLX DB-21	Active
GLX DB-21.2.5.4	Signaling	GLX DB-21	Active
GLX DB-21.2.5.3	Power & OCS	GLX DB-21	Active
GLX DB-21.2.5.9	Communications	GLX DB-21	Active
GLX DB-21.2.4	VMF	GLX DB-21	Active
GLX DB-21.2.4.10	Vehicle Maintenance Building	GLX DB-21	Active
GLX DB-21.2.4.6	Transportation Office Building	GLX DB-21	Active
GLX DB-21.2.13	Community Path	GLX DB-21	Active
GLX DB-21.2.21	Roadways & Traffic Improvements	GLX DB-21	Active
GLX DB-21.3	Contract Deliverables / Submittals	GLX DB-21	Active
GLX DB-21.3.1	Plans	GLX DB-21	Active
GLX DB-21.3.1.1	Project Management Plan	GLX DB-21	Active
GLX DB-21.3.1.2	Comprehensive Environmental Protection Program	GLX DB-21	Active
GLX DB-21.4	Procurement	GLX DB-21	Active
GLX DB-21.4.14	Steel Girders	GLX DB-21	Active
GLX DB-21.4.9	Special Trackwork	GLX DB-21	Active
GLX DB-21.4.1	Traction Power Substation	GLX DB-21	Active
GLX DB-21.4.7	Train Control Signaling Cabinets & Equipment	GLX DB-21	Active
GLX DB-21.4.6	Catenary Components	GLX DB-21	Active
GLX DB-21.4.11	Communications Equipment	GLX DB-21	Active
GLX DB-21.4.8	Fare Collection System Equipment	GLX DB-21	Active
GLX DB-21.4.12	Feeder Cabling	GLX DB-21	Active
GLX DB-21.4.3	Pre-Cast Noise Wall Panels	GLX DB-21	Active
GLX DB-21.4.13	Trackwork	GLX DB-21	Active
GLX DB-21.4.10	Maintenance Facility Equipment	GLX DB-21	Active
GLX DB-21.4.4	Concrete Beams	GLX DB-21	Active
GLX DB-21.7	Pre-Construction	GLX DB-21	Active
GLX DB-21.7.2	Permits	GLX DB-21	Active
GLX DB-21.7.2.1	Obtained by MBTA	GLX DB-21	Active
GLX DB-21.7.2.3	To Be Obtained by GLXC	GLX DB-21	Active
GLX DB-21.7.4	Studies	GLX DB-21	Active
GLX DB-21.5	Construction	GLX DB-21	Active
GLX DB-21.5.1	Project Wide	GLX DB-21	Active
GLX DB-21.5.8	Segment 1	GLX DB-21	Active
GLX DB-21.5.8.9	Earthwork, Clearing & Grubbing	GLX DB-21	Active
GLX DB-21.5.8.10	Utilities	GLX DB-21	Active
GLX DB-21.5.8.2	Retaining & Noise Walls	GLX DB-21	Active
GLX DB-21.5.8.5	Drainage	GLX DB-21	Active
GLX DB-21.5.8.3	Roadway Bridge	GLX DB-21	Active

© Oracle Corporation

WBS Code	WBS Name	Project ID	Project Status
GLX DB-21.5.8.3.22	College Ave (Medford) (Bridge No. M-12-012)	GLX DB-21	Active
GLX DB-21.5.8.16	Pedestrian Bridge - College Ave	GLX DB-21	Active
GLX DB-21.5.8.1	Station	GLX DB-21	Active
GLX DB-21.5.8.1.22	College Ave	GLX DB-21	Active
GLX DB-21.5.8.4	Track	GLX DB-21	Active
GLX DB-21.5.8.4.1	Commuter Track 1 (EB) (Sta. 238+00 - 200+00)	GLX DB-21	Active
GLX DB-21.5.8.4.2	Commuter Track 2 (WB) (Sta. 238+00 - 200+00)	GLX DB-21	Active
GLX DB-21.5.8.4.3	Medford Branch EB(Sta. 374+00 - 344+00)	GLX DB-21	Active
GLX DB-21.5.8.4.4	Medford Branch WB (Sta. 374+00 - 344+00)	GLX DB-21	Active
GLX DB-21.5.8.6	Systems	GLX DB-21	Active
GLX DB-21.5.8.6.1	OCS	GLX DB-21	Active
GLX DB-21.5.8.6.9	TPSS	GLX DB-21	Active
GLX DB-21.5.8.6.3	Signaling	GLX DB-21	Active
GLX DB-21.5.8.6.4	Communications	GLX DB-21	Active
GLX DB-21.5.11	Segment 2	GLX DB-21	Active
GLX DB-21.5.11.12	Utilities	GLX DB-21	Active
GLX DB-21.5.11.11	Earthwork, Clearing & Grubbing	GLX DB-21	Active
GLX DB-21.5.11.8	Structures	GLX DB-21	Active
GLX DB-21.5.11.8.1	Demolitions	GLX DB-21	Active
GLX DB-21.5.11.1	Roadway Bridges	GLX DB-21	Active
GLX DB-21.5.11.1.22	Broadway (Bridge No. S-17-013)	GLX DB-21	Active
GLX DB-21.5.11.1.1	Cedar St (Somerville) (Bridge No. S-17-012)	GLX DB-21	Active
GLX DB-21.5.11.1.3	Lowell St (Somerville) (Bridge No. S-17-011)	GLX DB-21	Active
GLX DB-21.5.11.9	Drainage	GLX DB-21	Active
GLX DB-21.5.11.5	Retaining & Noise Walls	GLX DB-21	Active
GLX DB-21.5.11.6	Stations	GLX DB-21	Active
GLX DB-21.5.11.6.1	Magoun Square	GLX DB-21	Active
GLX DB-21.5.11.6.16	Ball Square	GLX DB-21	Active
GLX DB-21.5.11.4	Track	GLX DB-21	Active
GLX DB-21.5.11.4.1	Commuter Track 1 (EB) (Sta. 200+00 - 151+20)	GLX DB-21	Active
GLX DB-21.5.11.4.2	Commuter Track 2 (WB) (Sta. 200+00 - 151+20)	GLX DB-21	Active
GLX DB-21.5.11.4.3	Medford Branch EB (Sta. 344+00 - 295+00)	GLX DB-21	Active
GLX DB-21.5.11.4.10	Medford Branch WB (Sta. 344+00 - 295+00)	GLX DB-21	Active
GLX DB-21.5.11.10	Community Path	GLX DB-21	Active
GLX DB-21.5.11.3	Systems	GLX DB-21	Active
GLX DB-21.5.11.3.2	OCS	GLX DB-21	Active
GLX DB-21.5.11.3.8	TPSS	GLX DB-21	Active
GLX DB-21.5.11.3.7	Communications	GLX DB-21	Active
GLX DB-21.5.11.3.6	Signaling	GLX DB-21	Active
GLX DB-21.5.18	Segment 3	GLX DB-21	Active
GLX DB-21.5.18.11	Utilities	GLX DB-21	Active
GLX DB-21.5.18.5	Earthwork, Clearing & Grubbing	GLX DB-21	Active
GLX DB-21.5.18.8	Structures	GLX DB-21	Active
GLX DB-21.5.18.8.1	Demolition	GLX DB-21	Active
GLX DB-21.5.18.14	Railroad Bridge	GLX DB-21	Active
GLX DB-21.5.18.14.1	Washington St Bridge	GLX DB-21	Active
GLX DB-21.5.18.9	Drainage	GLX DB-21	Active
GLX DB-21.5.18.7	Retaining & Noise Walls	GLX DB-21	Active
GLX DB-21.5.18.6	Track	GLX DB-21	Active
GLX DB-21.5.18.6.1	Commuter Track 1 (EB) (Sta. 151+20 - 87+70)	GLX DB-21	Active
GLX DB-21.5.18.6.2	Commuter Track 2 (WB) (Sta. 151+20 - 87+70)	GLX DB-21	Active
GLX DB-21.5.18.6.3	Medford Branch EB (Sta. 295+00 - 221.80)	GLX DB-21	Active
GLX DB-21.5.18.6.6	Medford Branch WB (Sta. 295+00 - 221.80)	GLX DB-21	Active
GLX DB-21.5.18.1	Stations	GLX DB-21	Active
GLX DB-21.5.18.1.2	Gilman Square	GLX DB-21	Active
GLX DB-21.5.18.1.1	East Somerville	GLX DB-21	Active
GLX DB-21.5.18.2	Roadway Bridges and Underpasses	GLX DB-21	Active
GLX DB-21.5.18.2.2	Medford St (Somerville) (Bridge No. S-17-007)	GLX DB-21	Active
GLX DB-21.5.18.2.3	School St (Somerville) (Bridge No. S-17-008)	GLX DB-21	Active
GLX DB-21.5.18.2.1	Walnut St (Somerville) (Bridge No. S-17-006)	GLX DB-21	Active
GLX DB-21.5.18.3	Community Path	GLX DB-21	Active
GLX DB-21.5.18.4	Pump Stations	GLX DB-21	Active
GLX DB-21.5.18.4.1	Washington St (B)	GLX DB-21	Active
GLX DB-21.5.18.4.5	Washington St (A)	GLX DB-21	Active
GLX DB-21.5.18.10	Systems	GLX DB-21	Active
GLX DB-21.5.18.10.3	OCS	GLX DB-21	Active
GLX DB-21.5.18.10.8	TPSS	GLX DB-21	Active
GLX DB-21.5.18.10.7	Communications	GLX DB-21	Active
GLX DB-21.5.18.10.6	Signaling	GLX DB-21	Active
GLX DB-21.5.19	Segment 4	GLX DB-21	Active
GLX DB-21.5.19.10	Utilities	GLX DB-21	Active
GLX DB-21.5.19.9	Earthwork, Clearing & Grubbing	GLX DB-21	Active
GLX DB-21.5.19.5	Drainage	GLX DB-21	Active
GLX DB-21.5.19.1	Station	GLX DB-21	Active
GLX DB-21.5.19.1.16	Lechmere Relocation	GLX DB-21	Active
GLX DB-21.5.19.7	Viaducts	GLX DB-21	Active
GLX DB-21.5.19.7.3	Lechmere (LEV)	GLX DB-21	Active
GLX DB-21.5.19.7.1	Medford (MBV)	GLX DB-21	Active
GLX DB-21.5.19.7.1.2	Medford Branch South	GLX DB-21	Active

© Oracle Corporation

WBS Code	WBS Name	Project ID	Project Status
GLX DB-21.5.19.7.1.3	Medford Branch North	GLX DB-21	Active
GLX DB-21.5.19.7.1.4	Medford Branch North-1	GLX DB-21	Active
GLX DB-21.5.19.2	Retaining & Noise Walls	GLX DB-21	Active
GLX DB-21.5.19.8	Pump Station	GLX DB-21	Active
GLX DB-21.5.19.8.9	Red Bridge	GLX DB-21	Active
GLX DB-21.5.19.4	Track	GLX DB-21	Active
GLX DB-21.5.19.4.3	Medford Branch EB (Sta. 221.80 - 177+90)	GLX DB-21	Active
GLX DB-21.5.19.4.1	Medford Branch WB (Sta. 221.80 - 177+90)	GLX DB-21	Active
GLX DB-21.5.19.3	Systems	GLX DB-21	Active
GLX DB-21.5.19.3.1	TPSS	GLX DB-21	Active
GLX DB-21.5.19.3.1.3	Traction Power Substation	GLX DB-21	Active
GLX DB-21.5.19.3.4	Communications	GLX DB-21	Active
GLX DB-21.5.19.3.3	Signaling	GLX DB-21	Active
GLX DB-21.5.19.3.5	OCS	GLX DB-21	Active
GLX DB-21.5.20	Segment 5 - VMF	GLX DB-21	Active
GLX DB-21.5.20.10	Utilities	GLX DB-21	Active
GLX DB-21.5.20.1	Structures & Yard Demolitions	GLX DB-21	Active
GLX DB-21.5.20.6	Clearing & Grubbing	GLX DB-21	Active
GLX DB-21.5.20.5	Drainage	GLX DB-21	Active
GLX DB-21.5.20.4	Retaining & Noise Walls	GLX DB-21	Active
GLX DB-21.5.20.2	Track	GLX DB-21	Active
GLX DB-21.5.20.2.3	Outside	GLX DB-21	Active
GLX DB-21.5.20.2.1	Inside	GLX DB-21	Active
GLX DB-21.5.20.9	Vehicle Maintenance Facility	GLX DB-21	Active
GLX DB-21.5.20.9.6	Transportation Office Building	GLX DB-21	Active
GLX DB-21.5.20.9.10	Vehicle Maintenance Building	GLX DB-21	Active
GLX DB-21.5.20.9.1	VMF Yard	GLX DB-21	Active
GLX DB-21.5.20.3	Systems	GLX DB-21	Active
GLX DB-21.5.20.3.6	Signaling	GLX DB-21	Active
GLX DB-21.5.20.3.2	OCS	GLX DB-21	Active
GLX DB-21.5.20.3.8	TPSS	GLX DB-21	Active
GLX DB-21.5.20.3.7	Communications	GLX DB-21	Active
GLX DB-21.5.20.3.4	Local Testing & Commissioning	GLX DB-21	Active
GLX DB-21.5.21	Segment 6 - Union Square	GLX DB-21	Active
GLX DB-21.5.21.9	Earthwork, Clearing & Grubbing	GLX DB-21	Active
GLX DB-21.5.21.5	Drainage	GLX DB-21	Active
GLX DB-21.5.21.10	Utilities	GLX DB-21	Active
GLX DB-21.5.21.4	Viaducts	GLX DB-21	Active
GLX DB-21.5.21.4.7	Union Square EB (UEV)	GLX DB-21	Active
GLX DB-21.5.21.4.1	Union Square WB (UWV)	GLX DB-21	Active
GLX DB-21.5.21.1	Station	GLX DB-21	Active
GLX DB-21.5.21.1.16	Union Square	GLX DB-21	Active
GLX DB-21.5.21.3	Retaining & Noise Walls	GLX DB-21	Active
GLX DB-21.5.21.2	Track	GLX DB-21	Active
GLX DB-21.5.21.2.1	Union Square WB (Sta. 39+33 - 1+15)	GLX DB-21	Active
GLX DB-21.5.21.2.3	Union Square EB (Sta. 45+90 - 0+95)	GLX DB-21	Active
GLX DB-21.5.21.6	Systems	GLX DB-21	Active
GLX DB-21.5.21.6.1	OCS	GLX DB-21	Active
GLX DB-21.5.21.6.3	Signaling	GLX DB-21	Active
GLX DB-21.5.21.6.6	TPSS	GLX DB-21	Active
GLX DB-21.5.21.6.4	Communications	GLX DB-21	Active
GLX DB-21.5.10	Roadway & Traffic Improvements	GLX DB-21	Active
GLX DB-21.5.10.1	Reconstruction	GLX DB-21	Active
GLX DB-21.5.10.2	Intersections	GLX DB-21	Active
GLX DB-21.8	Start-up / Testing / Commissioning	GLX DB-21	Active

© Oracle Corporation

APPENDIX 8


$100 Million Cost Loading Example

Green Line Extension Initial Baseline Schedule 20170908		12-Dec-17	30-Jun-20		$99,120,347.74		
DRTW345	Retaining & Noise Walls - Preliminary Design - Submit to MBTA for Review	12-Dec-17	28-Mar-18	02	$1,319,024.93		
DDRA240	Drainage S1 - Preliminary Design - Submit to MBTA for Review	12-Dec-17	20-Mar-18	02	$272,037.61		
DDRA430	Drainage S2 - Preliminary Design - Submit to MBTA for Review	12-Dec-17	06-Mar-18	02	$272,037.61		
DDRA480	Drainage S3 - Preliminary Design - Submit to MBTA for Review	12-Dec-17	20-Mar-18	02	$272,037.61		
DDRA530	Drainage S4 - Preliminary Design - Submit to MBTA for Review	12-Dec-17	20-Mar-18	02	$272,037.61		
DDRA580	Drainage S6 - Preliminary Design - Submit to MBTA for Review	12-Dec-17	20-Mar-18	02	$272,037.61		
DDRA630	Drainage S5 - Preliminary Design - Submit to MBTA for Review	12-Dec-17	20-Mar-18	02	$272,037.61		
DRTW280	Retaining Walls (Early) - Pre-RFC Design - Submit to MBTA for Review	22-Mar-18	22-May-18	02	$811,707.65		
DDRA400	Drainage S2 - Pre-RFC Design - Submit to MBTA for Review	04-Apr-18	21-May-18	02	$181,358.41		
DDRA320	Drainage S1 - Pre-RFC Design - Submit to MBTA for Review	19-Apr-18	15-Jun-18	02	$181,358.41		
DDRA450	Drainage S3 - Pre-RFC Design - Submit to MBTA for Review	19-Apr-18	15-Jun-18	02	$181,358.41		
DDRA500	Drainage S4 - Pre-RFC Design - Submit to MBTA for Review	19-Apr-18	15-Jun-18	02	$181,358.41		
DDRA550	Drainage S6 - Pre-RFC Design - Submit to MBTA for Review	19-Apr-18	15-Jun-18	02	$181,358.41		
DDRA600	Drainage S5 - Pre-RFC Design - Submit to MBTA for Review	19-Apr-18	15-Jun-18	02	$181,358.41		
DRTW355	Retaining & Noise Walls - Intermediate Design - Submit to MBTA for Revi	30-Apr-18	09-Jul-18	02	$1,014,634.56		
C6RNW130	Retaining Wall UN-2 (28+80 - 34+00) - Install Sheet Pile Wall	22-May-18	20-Jun-18	05	$855,518.74		
DDRA420	Drainage S2 - RFC Design - Submit to MBTA for Review	19-Jun-18	24-Jul-18	02	$136,018.81		
DRTW320	Retaining Walls (Early) - RFC Design - Submit to MBTA for Review	21-Jun-18	25-Jul-18	02	$507,317.28		
DDRA280	Drainage S1 - RFC Design - Submit to MBTA for Review	17-Jul-18	27-Aug-18	02	$136,018.81		
DDRA470	Drainage S3 - RFC Design - Submit to MBTA for Review	17-Jul-18	27-Aug-18	02	$136,018.81		
DDRA520	Drainage S4 - RFC Design - Submit to MBTA for Review	17-Jul-18	27-Aug-18	02	$136,018.81		
DDRA570	Drainage S6 - RFC Design - Submit to MBTA for Review	17-Jul-18	27-Aug-18	02	$136,018.81		
DDRA620	Drainage S5 - RFC Design - Submit to MBTA for Review	17-Jul-18	27-Aug-18	02	$136,018.81		
DRTW365	Retaining & Noise Walls - Pre-RFC Design - Submit to MBTA for Review	07-Aug-18	24-Sep-18	02	$710,244.19		
DDRA435	Drainage S2 - RFC Design - Incorporate Comments, Release for Constru	21-Aug-18	18-Sep-18	02	$90,679.20		
C1RNW110	Retaining Wall ME-3 (366+50 - 374+00) - Install Soldier Pile Wall	06-Sep-18	26-Dec-18	05	$4,426,228.35		
DRTW300	Retaining Walls (Early) - Final Design Docs - Submit to MBTA for Review	06-Sep-18	12-Sep-18	02	$101,463.46		
C2DRA125	Main Drainage - Excavate & Install	18-Sep-18	19-Nov-18	02	$8,422,269.94		
DDRA410	Drainage S2 - Final Design Docs - Submit to MBTA for Review	18-Sep-18	25-Sep-18	02	$22,669.80		
DDRA230	Drainage S1 - RFC Design - Incorporate Comments, Release for Constru	25-Sep-18	23-Oct-18	02	$90,679.20		
DDRA485	Drainage S3 - RFC Design - Incorporate Comments, Release for Constru	25-Sep-18	23-Oct-18	02	$90,679.20		
DDRA535	Drainage S4 - RFC Design - Incorporate Comments, Release for Constru	25-Sep-18	23-Oct-18	02	$90,679.20		
DDRA585	Drainage S6 - RFC Design - Incorporate Comments, Release for Constru	25-Sep-18	23-Oct-18	02	$90,679.20		
DDRA635	Drainage S5 - RFC Design - Incorporate Comments, Release for Constru	25-Sep-18	23-Oct-18	02	$90,679.20		
DRTW385	Retaining & Noise Walls - RFC Design - Submit to MBTA for Review	23-Oct-18	19-Nov-18	02	$405,853.82		
C6DRA115	Union Sq Line Main Drainage - Excavate & Install	23-Oct-18	01-Nov-18	11	$568,777.00		
C4DRA115	Main Drainage - Excavate & Install	23-Oct-18	13-Feb-19	02	$5,120,411.58		
C3DRA105	Main Drainage - Excavate & Install	23-Oct-18	11-Jan-19	02	$11,436,983.52		
C1DRA135	Main Drainage - Excavate & Install	23-Oct-18	27-Nov-18	02	$2,591,855.38		
DDRA300	Drainage S1 - Final Design Docs - Submit to MBTA for Review	23-Oct-18	30-Oct-18	02	$22,669.80		
DDRA460	Drainage S3 - Final Design Docs - Submit to MBTA for Review	23-Oct-18	30-Oct-18	02	$22,669.80		
DDRA510	Drainage S4 - Final Design Docs - Submit to MBTA for Review	23-Oct-18	30-Oct-18	02	$22,669.80		
DDRA560	Drainage S6 - Final Design Docs - Submit to MBTA for Review	23-Oct-18	30-Oct-18	02	$22,669.80		
DDRA610	Drainage S5 - Final Design Docs - Submit to MBTA for Review	23-Oct-18	30-Oct-18	02	$22,669.80		
DRTW340	Retaining & Noise Walls - RFC Design - Incorporate Comments, Release	20-Dec-18	27-Dec-18	02	$101,463.46		
DRTW375	Retaining & Noise Walls - Final Design Docs - Submit to MBTA for Review	27-Dec-18	03-Jan-19	02	$101,463.46		
C2RNW185	Retaining Wall MW-8.15 (331+39 - 332+39- Install Soldier Pile Wall	02-Jan-19	31-Jan-19	05	$777,441.72		
C2RNW180	Retaining Wall MW-8.1 (327+00 - 329+75) - Install Soldier Pile Wall	02-Jan-19	27-Mar-19	05	$935,359.56		
C2RNW165	Retaining Wall ME-2.1 (321+25 - 323+25) - Install Soldier Pile Wall	02-Jan-19	21-Jan-19	05	$583,081.29		
C3NRW115	Retaining Wall - Medford Bridge Walls (259+31 - 279+25) - Install Soldier	02-Jan-19	05-Jul-19	05	$12,749,558.23		
C2RNW115	Retaining Wall MW-7 (296+40 - 298+75) - Install Soldier Pile Wall	02-Jan-19	18-Mar-19	05	$1,712,801.28		
C1RNW165	Retaining Wall ME-2.5 (363+75 - 364+25) - Install Modular Pre-Cast Blocl	02-Jan-19	08-Jan-19	05	$55,811.76		
C1DRA110	Commuter Line 1 EB Track Drainage - Excavate & Install	09-Jan-19	14-Jan-19	11	$305,665.75		
C2RNW120	Retaining Wall ME-2 (309+63 - 320+50) - Install Soldier Pile Wall	22-Jan-19	17-May-19	05	$528,174.47		
C5DRA105	VMF and Track Drainage - Excavate & Install	09-Apr-19	24-Apr-19	11	$4,124,688.00		
C1RNW155	Retaining Wall W-3 - Install MSE Wall	24-Apr-19	05-Jun-19	05	$2,313,268.02		
C1RNW140	Retaining Wall W-1 - Install MSE Wall	24-Apr-19	06-May-19	05	$596,227.36		
C1RNW150	Retaining Wall W-2 - Install MSE Wall	06-May-19	13-May-19	05	$183,590.36		
C1RNW160	Retaining Wall W-4 (Fence) - Install Fence	13-May-19	17-May-19	05	$182,354.66		
C3NRW230	Retaining Wall N7+Sycamore to Central (276+29 - 289+40) - Install Soldi	20-May-19	31-Oct-19	05	$955,657.12		
C2RNW125	Noise Wall N-11 - Install	20-May-19	28-May-19	05	$99,762.62		
C2RNW145	Noise Wall N-14B - Install	29-May-19	12-Jun-19	05	$489,868.88		
C1RNW170	Retaining Wall MW-9.5 (360+75 - 362+80) - Install Modular Pre-Cast Bloc	14-Jun-19	09-Jul-19	05	$386,147.59		
C1RNW105	Retaining Wall MW-10 (363+63 - 374+02) - Install Soil Nail Wall	14-Jun-19	28-Oct-19	05	$3,214,479.24		
C3NRW105	Retaining Wall MW-3B (271+07 - 272+75) - Install Modular Pre-Cast Bloc	08-Jul-19	10-Jul-19	05	$187,527.50		
C1RNW125	Retaining Wall MW-9 (345+80 - 353+54) - Install MSE Wall	10-Jul-19	13-Aug-19	05	$797,029.32		
C3NRW120	Retaining Wall MW-4A (272+05 - 275+18) - Install Modular Pre-Cast Bloc	11-Jul-19	01-Aug-19	05	$305,708.89		
C6DRA105	Union Sq Line EB Side Track Drainage - Excavate & Install	16-Jul-19	29-Jul-19	11	$568,133.00		
C4RNW105	Noise Wall N-1A - Install	31-Jul-19	06-Aug-19	05	$108,706.86		
C4RNW110	Noise Wall N-1B - Install	31-Jul-19	07-Aug-19	05	$1,006,226.45		
C4RNW115	Noise Wall N-2A - Install	31-Jul-19	09-Aug-19	05	$677,009.80		

© Oracle Corporation

| | April 2019 | | | | May 2019 | | | | | June 2019 | | | | July 2019 | | | | | August 2019 | | | | September 2019 | | | | | October 2019 | | | | November 2019 | | | | December 2019 | | | | | January 2020 | | | | February 2020 | | | | March 2020 | | | | | April 2020 | | | | May 2020 | | | | | June 2020 | | | | |
|---|---|---

Activity ID	Activity Name	Start	Finish	Cost Account	Budgeted Cost	Remaining Units
C4RNW120	Noise Wall N-2B - Install	31-Jul-19	09-Aug-19	05	$684,119.32	
C3NRW220	Retaining Wall MW-5.5 (279+25 - 281+25) - Install Modular Pre-Cast Bloc	02-Aug-19	22-Aug-19	05	$251,152.90	
C3NRW130	Noise Wall N-6 - Install	02-Aug-19	17-Sep-19	05	$1,463,643.81	
C1RNW115	Retaining Wall MW-8.2 (343+56 - 345+20) - Install MSE Wall	14-Aug-19	01-Oct-19	05	$313,633.54	
C2RNW200	Retaining Wall MW-6.5 (295+75 - 296+40) - Install Modular Pre-Cast Bloc	23-Aug-19	26-Aug-19	05	$54,416.46	
C3NRW185	Crib Wall MCW-3 (285+40 - 289+08) - Rehabilitate Crib (MPB) Wall	23-Aug-19	05-Sep-19	05	$820,236.67	
C2RNW190	Retaining Wall MW-7.5 (298+75 - 299+75) - Install Modular Pre-Cast Bloc	27-Aug-19	28-Aug-19	05	$139,529.39	
C2RNW195	Retaining Wall MW-7.6 (298+00 - 301+25) - Install Modular Pre-Cast Bloc	03-Sep-19	10-Sep-19	05	$362,776.42	
C3NRW175	Crib Wall MCW-2 (252+79 - 259+31) - Rehabilitate Crib Wall	06-Sep-19	30-Sep-19	05	$1,089,934.06	
C2RNW105	Retaining Wall MW-8 (322+75 - 327+00) - Install Modular Pre-Cast Block	11-Sep-19	03-Oct-19	05	$474,399.93	
C2RNW175	Retaining Wall ME-2.3 (328+25 - 328+75) - Install Modular Pre-Cast Blocl	13-Sep-19	16-Sep-19	05	$48,835.29	
C2RNW170	Retaining Wall ME-2.2 (327+25 - 327+75) - Install Modular Pre-Cast Blocl	17-Sep-19	18-Sep-19	05	$34,882.35	
C4RNW145	Retaining Wall ME-0.5 (216+49 - 217+53) - Install Modular Pre-Cast Blocl	19-Sep-19	30-Sep-19	05	$85,381.96	
C2DRA105	Commuter Line 1 EB Track Drainage - Excavate & Install	19-Sep-19	11-Oct-19	11	$399,403.25	
C6DRA110	Union Sq Line WB Side Track Drainage - Excavate & Install	23-Sep-19	08-Oct-19	11	$568,000.00	
C3NRW170	Crib Wall MCW-1 (247+03 - 251+36) - Rehabilitate Crib Wall	01-Oct-19	06-Nov-19	05	$724,994.71	
C2RNW135	Noise Wall N-12 - Install	04-Oct-19	16-Oct-19	05	$454,091.94	
C2RNW160	Noise Wall N-9B - Install	17-Oct-19	11-Nov-19	05	$840,987.44	
C2RNW155	Noise Wall N-9A - Install	17-Oct-19	05-Nov-19	05	$629,536.55	
C2RNW140	Noise Wall N-14A - Install	17-Oct-19	01-Nov-19	05	$333,918.11	
C3RNW122	Noise Wall N-15 - Install	17-Oct-19	19-Nov-19	05	$1,173,758.86	
C3NRW145	Retaining Wall ME-1 (247+47 - 248+98) - Install Soldier Plle Wall	01-Nov-19	12-Dec-19	05	$1,027,194.87	
C2RNW130	Noise Wall N-10 - Install	04-Nov-19	03-Dec-19	05	$1,070,212.13	
C6RNW110	Noise Wall N-3A - Install	12-Nov-19	10-Dec-19	05	$875,159.01	
C6RNW115	Noise Wall N-3B - Install	12-Nov-19	09-Dec-19	05	$776,084.40	
C6RNW120	Noise Wall N-17 - Install	12-Nov-19	10-Dec-19	05	$864,150.72	
C3NRW205	Retaining Wall MW-0.8 (236+25 - 236+99) - Install Soldier Plle Wall	13-Dec-19	24-Dec-19	05	$327,983.22	
C3NRW180	Crib Wall MCE-1 (248+98 - 252+42) - Rehabilitate Crib Wall	13-Dec-19	16-Jan-20	05	$527,979.21	
C2CTRK145	Commuter Line 2 WB Track Drainage - Excavate & Install	16-Dec-19	16-Dec-19	11	$427,272.12	
C2DRA115	Commuter Line 2 WB Track Drainage - Flowfill Old Drainage Pipe	17-Dec-19	23-Dec-19	11	$427,272.12	
C3NRW200	Retaining Wall MW-0.7 (235+25 - 235+75) - Install Soldier Plle Wall	30-Dec-19	07-Jan-20	05	$297,733.50	
C3NRW155	Retaining Wall MW-0.5 (234+20 - 237+03) - Install Cast-in-Place Wall	08-Jan-20	16-Mar-20	05	$1,469,909.14	
C3DRA110	Commuter Line 1 EB Track Drainage - Excavate & Install	17-Jan-20	03-Feb-20	11	$588,508.50	
C1DRA150	Commuter Line 2 WB Track Drainage - Excavate & Install Drainage	04-Feb-20	12-Feb-20	11	$152,832.88	
C3CTRK145	Commuter Line 2 WB Track Drainage - Excavate & Install	11-Mar-20	16-Mar-20	11	$567,315.60	
C1DRA125	Medford Line WB Track Drainage - Excavate & Install	12-Mar-20	25-Mar-20	11	$305,665.75	
C3NRW225	Retaining Wall BR-1 (261+00 - 269+00) - Install Ballasted Wall	18-Mar-20	07-Apr-20	05	$706,576.83	
C3DRA120	Commuter Line 2 WB Track Drainage - Flowfill Old Drainage Pipe	18-Mar-20	24-Mar-20	11	$216,873.00	
C2DRA120	Medford Line WB Track Drainage - Excavate & Install	24-Mar-20	17-Apr-20	11	$399,403.25	
C3DRA125	Medford Line WB Track Drainage - Excavate & Install	20-May-20	30-Jun-20	11	$588,508.50	

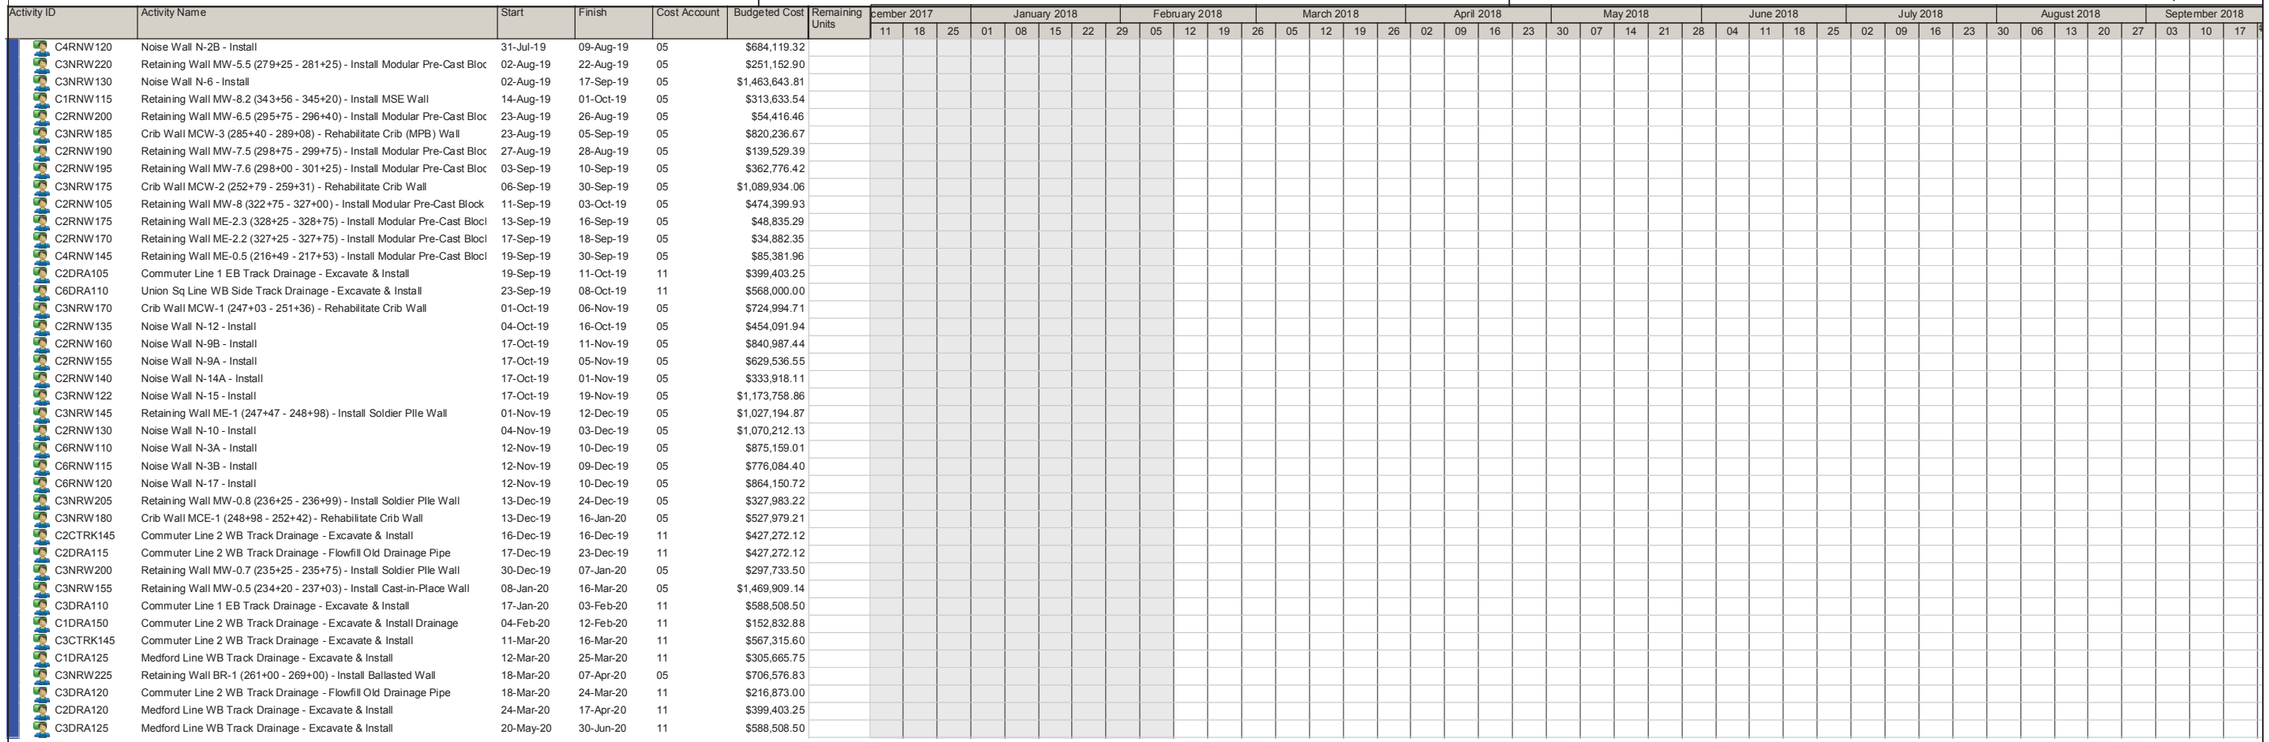

© Oracle Corporation


| | October 2018 | | | | | November 2018 | | | | | December 2018 | | | | | January 2019 | | | | | February 2019 | | | | | March 2019 | | | | | April 2019 | | | | | May 2019 | | | | | June 2019 | | | | | July 2019 | | | | | August 2019 | | | | | September 2019 | | | | | October 2019 | | | | | November 2019 | | | | | December 2019 | | | | | 020 |
|---|---|---

January 2020				February 2020				March 2020				April 2020				May 2020				June 2020				July 2020				August 2020				September 2020				October 2020				November 2020				December 2020				January 2021				February 2021				March 2021				April 2021	
06	13	20	27	03	10	17	24	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05	12
10	8																																																											
16																																																										
24	40	40	24	40	40	40	24	40	40	8																																																	
	17	84	50	17																																																						
				32	24																																																					
									24	8																																																	
									16	32	24																																																
										26	26	43	17																																														
										24	16																																															
											24	40	40	40																																													
																			24	24	40	40	32	32	16																																			

© Oracle Corporation

APPENDIX 9

Cash Flow Projections

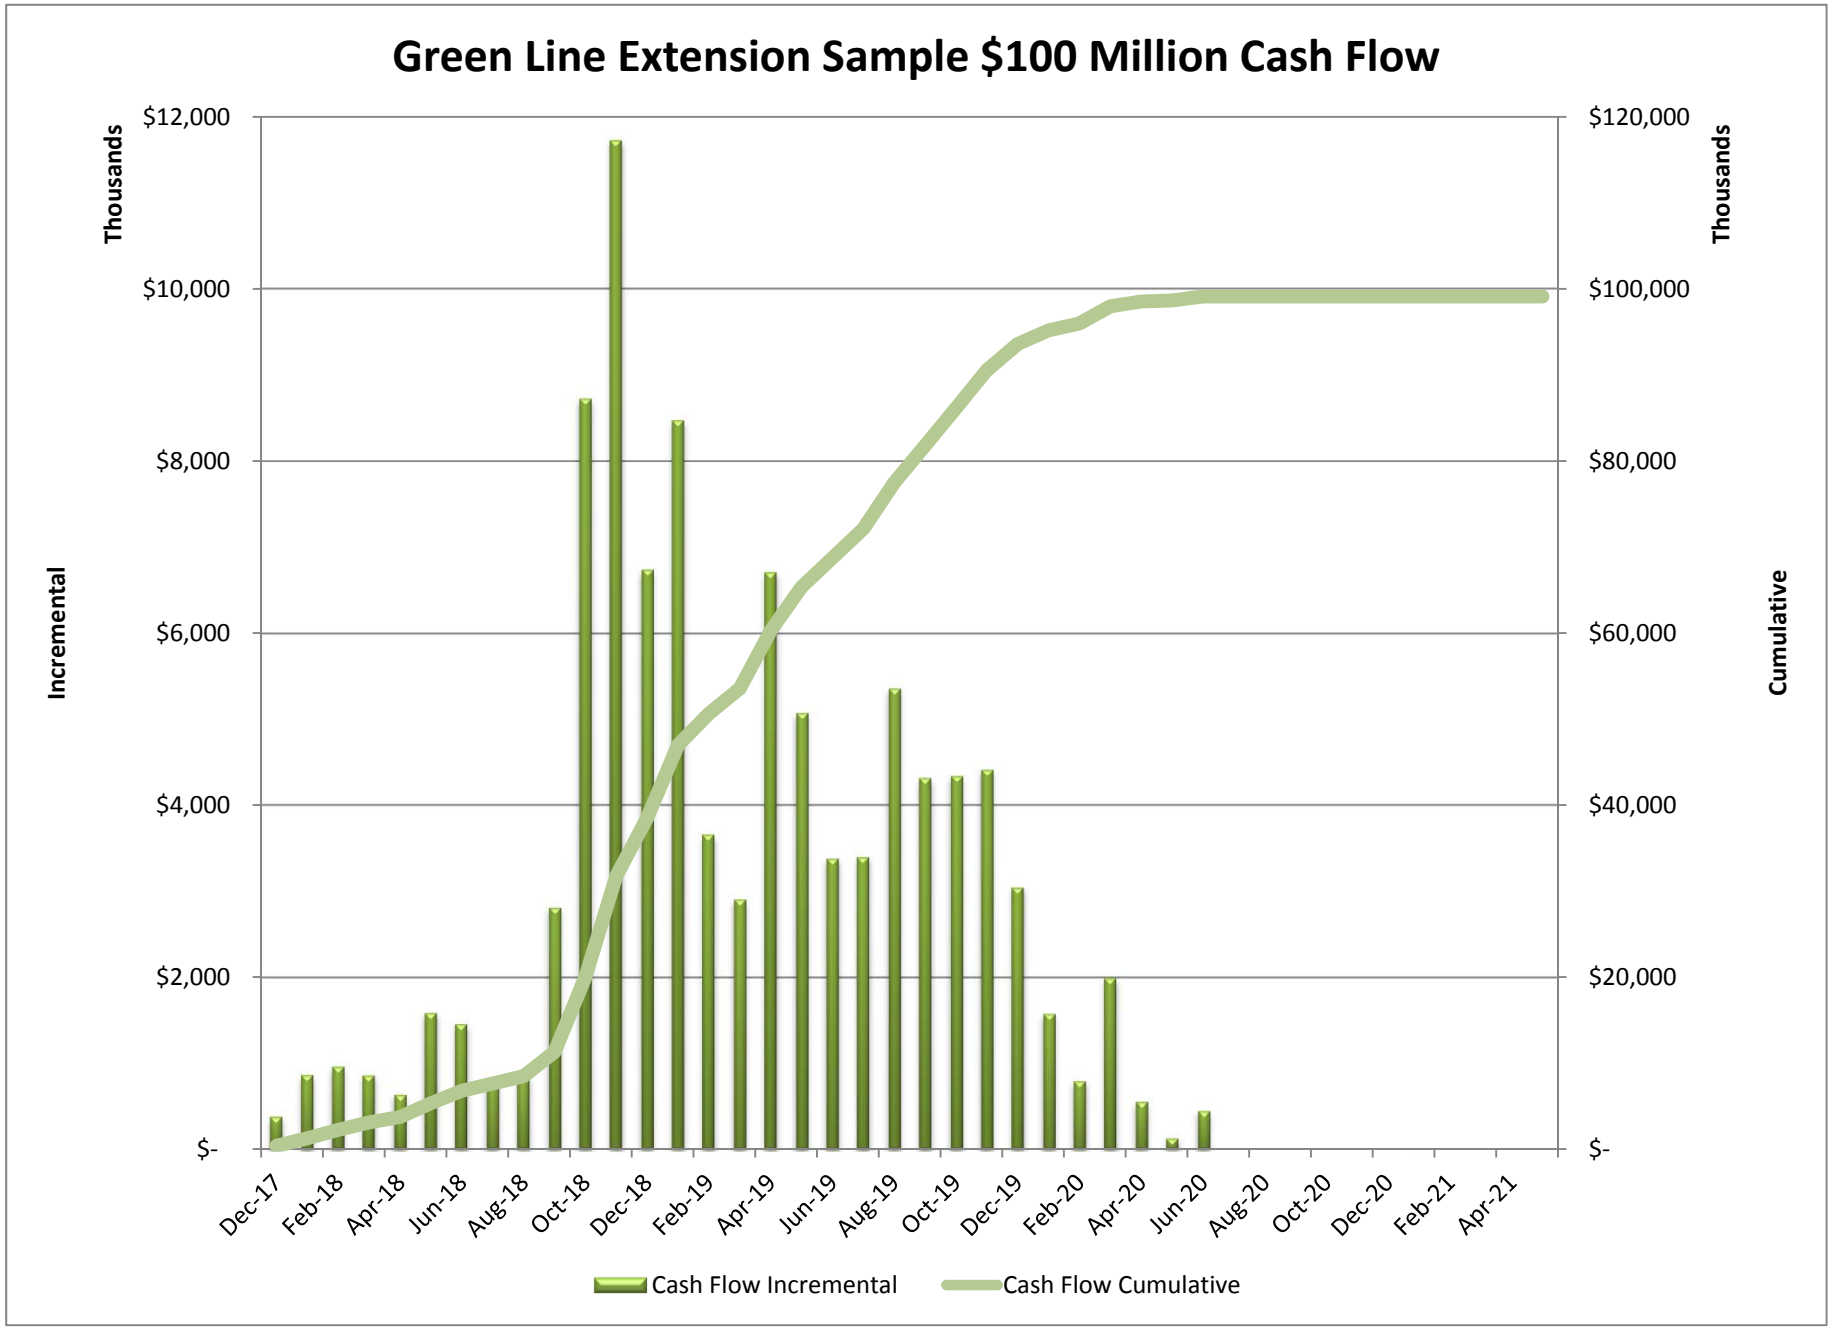
Green Line Extension Sample $100 Million Cash Flow
Incremental
Thousands
$12,000
$10,000
$8,000
$6,000
$4,000
$2,000
$-
$120,000
$100,000
$80,000
$60,000
$40,000
$20,000
$-
Thousands
Cumulative
Dec-17
Feb-18
Apr-18
Jun-18
Aug-18
Oct-18
Dec-18
Feb-19
Apr-19
Jun-19
Aug-19
Oct-19
Dec-19
Feb-20
Apr-20
Jun-20
Aug-20
Oct-20
Dec-20
Feb-21
Apr-21
Cash Flow Incremental
Cash Flow Cumulative



Response to the Request for Proposal

for the Green Line Extension Design Build Project

Submitted to

Massachusetts Department of Transportation and
The Massachusetts Bay Transportation Authority

Part 4 – Technical Solutions Qualitative Evaluation Criteria Information

GLX CONSTRUCTORS

TABLE OF CONTENTS

PART 4

Section 4.1 Systems and System Integration
Section 4.2 Elevated Guideway and Structures along the Guideway
Section 4.3 Stations
Section 4.4 Landscaping and Station Signage
Section 4.5 Vehicle Maintenance Facility
Section 4.6 Civil and Guideway
Section 4.7 Drainage and Stormwater Management
Section 4.8 Environmental Management Strategy
Section 4.9 Utilities

4. TECHNICAL SOLUTIONS QUALITATIVE EVALUATION CRITERIA INFORMATION

4.1 SYSTEMS AND SYSTEMS INTEGRATION

GLX Constructors' approach to the Green Line's systems and systems integration is to customize and implement proven, reliable systems that are successful on other projects and compatible with the MBTA's existing infrastructure.

GLX Constructors' team members have delivered rail projects in dense urban environments, including active rail and integration with new and existing systems including the design of the MBTA's projects for more than 35 years. In addition to our Key Personnel, our team is strengthened by:

- **Tom O'Hara, Deputy Design Manager – Operations, Systems, and VMF.** Tom has worked with the MBTA for 24 years in the Engineering and Maintenance directorate giving him extensive knowledge of operational policies and procedures.
- **Benjamin Stell, Traction Power Lead.** Benjamin has more than 30 years of experience and is familiar with the MBTA's systems.

GLX Constructors' Systems Integration Team will have a central role through all phases of design, construction, commissioning, and rail activation to provide the MBTA with higher schedule and cost certainty.

4.1.A LIGHT RAIL TRANSIT SYSTEMS

Description of GLX Constructors' Design Methodology and Approach

Throughout the design process, GLX Constructors will use system engineering principles to make sure each of the systems' elements are incorporated into a single contiguous, compliant, and functional system. We will use the INCOSE (International Council on Systems Engineering) V-Model, demonstrated in Figure 4.1-1, as the basis for our system design.

System Engineering Management Plan. A System Engineering Management Plan (SEMP) is a management approach that makes sure our systems are designed, integrated, installed, tested and properly operational across design disciplines and throughout the life of the Project. The SEMP focuses on defining customer needs and constraints, lay out the activities, resources, budget, timeline, and required functionality early in the development cycle.

The SEMP documents requirements, and proceeds with design synthesis and system validation while considering the complete issues a hand, including:

- Operations
- Performance
- Testing
- Manufacturing
- Cost & Schedule
- Training and Support
- Disposal

The scope of our SEMP describes the main systems engineering tasks and activities required during the program development stage to make certain the electrical, mechanical, and functional aspects, systems design, and interfaces are in accordance with the Contract Specifications.

Requirements Management Plan. GLX Constructors will institute the Design Requirements Management Plan (DRMP) at the beginning of the Project execution and will serve to identify the key requirements of the Technical Provisions. The DRMP accomplishes the following:

- Confirms which documents were reviewed
- Flags the requirements
- Properly assigns the requirements
- Confirms that the requirements were sufficiently satisfied

The Systems Integration Manager will manage the DRMP and complete the requirement while independent compliance personnel will validate the requirement. Figure 4.1-3 demonstrates GLX Constructors' review of these requirements during the proposal development phase.

> **"Our design team is intimately familiar with the MBTA's transit, commuter, and system operations; Key Personnel and processes; overall function and operation; and how the MBTA services the local community and abroad. This knowledge will allow our team to mitigate issues before they arise.**

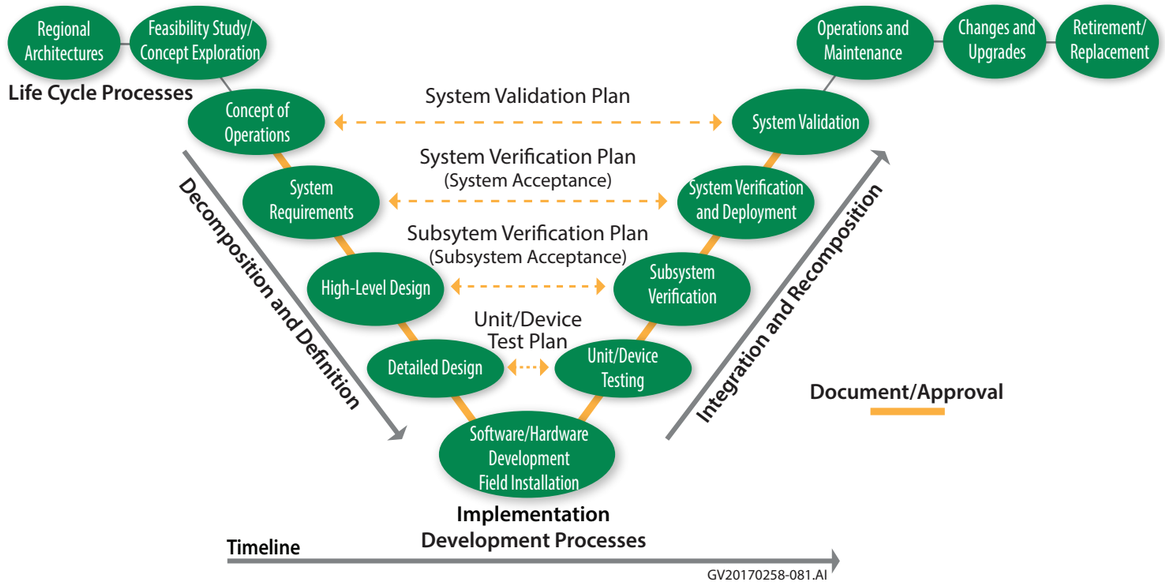


Figure 4.1-1. Systems Engineering Life-Cycle V-Model. *GLX Constructors' Method to review, test, and commission the Project.*

System Integration Management Plan. Our Systems Integration Management Plan (SIMP) will contribute to the Project's successful systems integration through the following approach:

- Implement a "team approach" to the systems integration process and manage the interfaces between parties, disciplines, consultants, and subconsultants.
- Assign Project-wide responsibility for interface management.
- Identify and document interfaces between components by developing, maintaining, and monitoring the interfaces through Interface Control Documents (ICDs) and a Systems Interface Matrix.
- Resolve interface requirement conflicts.
- Confirm that the components function as a whole and meet MBTA's design criteria and guidelines, and local Codes and Guidelines.
- Review interfaces at each design stage and change process.

Testing and Commissioning. Interface management involves controlling the various complex interfaces and requires the following steps shown in Figure 4.1-2 throughout the design and development of the Project.

Project processes are used to manage implement and test interfaces. We will generate an ICD to address and document each individual interfaces. The




Figure 4.1-2. System Interface Management Process. *Project processes are used to manage implement and test interfaces.*

Interface Matrix, Figure 4.1-4, documents the interdependencies and ICDs, which govern interfaces between various Green Line sub-systems.

We have the following systems in place, per the MBTA's standard testing requirements:

- **Train Control/Signaling.** The train control and signaling system will be designed, installed, and locally tested from the control center. The testing and verification from the control center will utilize the SCADA system and will work in conjunction with the other systems.
- **Communications.** This includes all stations communication elements, such as the CCTV, PA, TEL, FA, and Intrusion.
- **Traction Power.** This includes the verification, position, and operation of the traction power disconnect switches, DC circuit breakers, transformers/rectifiers, and all other internals within the substations.

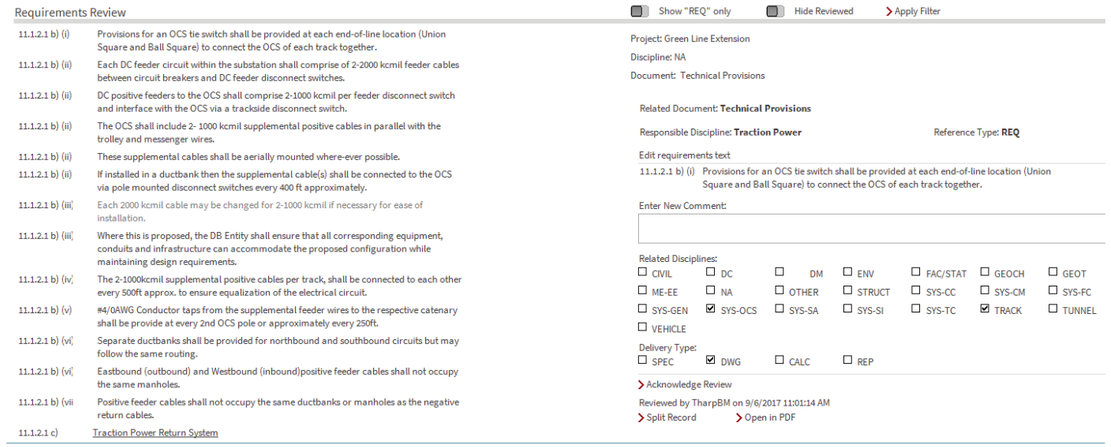


Figure 4.1-3. Requirements Traceability Matrix. *During proposal development, GLX Constructors has thoroughly reviewed the design requirements and will manage the requirements using the Requirements Traceability Matrix.*

- **Overhead Catenary.** The overhead catenary system will be tested, including the verification of all tensions, height and staggers at support and mid-span locations, smooth pantograph travel under the new overhead catenary systems, dynamic outline of the transit cars in conjunction with the overhead catenary system elements, hardware connection and torque, and sectionalizing (in conjunction with the traction power supply system).

Verification and Validation. Fixed facilities, systems, and equipment undergo tests throughout the construction and start-up phases of the Project. As the tests progress and portions of the system become operational, certain start-up tests are performed confirming completeness, operational readiness, and the reliability and safety of the system. Such tests required throughout the construction and start-up phases are:

- First Article Inspection
- Factory Acceptance Testing
- Inspection and Installation Verification Testing
- Site Acceptance Testing
- System Integration Testing
- Pre-Revenue Operations

Interface Control Forms	Interface B	Guideway	Trackwork	Stations	O&M Facility	MEP & Fire Protection	Roadway	Utilities	Light Rail Vehicle	Train Control	Traction Pwr Supply	Overhead Contact	Communications	Control and Monitor	Fire and Security	Traffic Signals/ITS	Fare Collection	Corrosion Ctrl & Grd	Other
Interface A		GDW	TRK	STN	OMF	FRP	TRF	UTL	LRV	TCS	TPS	OCS	COM	CMS	FSS	TRF	FAC	CCG	OTH
Guideway	GDW		▲	▲	▲	▲	▲	▲	▲	▲	n/a	▲	▲	▲	▲	▲	n/a	▲	▲
Trackwork	TRK			▲	▲	n/a	▲	n/a	▲	▲	▲	▲	n/a	n/a	n/a	▲	n/a	▲	▲
Stations	STN				n/a	▲	▲	▲	▲	▲	▲	▲	▲	▲	▲	▲	▲	▲	▲
O&M Facility	OMF					▲	n/a	▲	▲	▲	▲	▲	▲	▲	▲	▲	n/a	▲	▲
MEP & Fire Protection	FRP						n/a	▲	n/a	▲	n/a	n/a	▲	▲	▲	n/a	n/a	n/a	▲
Roadway	RDW							▲	n/a	n/a	n/a	▲	▲	▲	▲	▲	n/a	n/a	▲
Utilities	UTL								n/a	▲	▲	▲	▲	▲	▲	▲	▲	▲	▲
Light Rail Vehicle	LRV									▲	▲	▲	▲	▲	▲	n/a	n/a	n/a	n/a
Train Control	TCS										▲	n/a	▲	▲	▲	▲	n/a	▲	▲
Traction Power Supply	TPS											▲	▲	▲	▲	n/a	n/a	▲	▲
Overhead Contact	OCS												n/a	▲	n/a	▲	n/a	▲	▲
Communications	COM													▲	▲	▲	▲	▲	▲
Control and Monitor	CMS														▲	▲	▲	▲	▲
Fire and Security	FSS															n/a	▲	▲	▲
Traffic Signal/ITS	TRF																n/a	▲	▲
Fare Collection	FAC																	▲	▲
Corrosion Ctrl & Grd	CCG																		▲
Other	OTH																		

GV20170258-277.ai

Figure 4.1-4. Interface Matrix. *Our Systems Integration Team will design an Interface Matrix to ensure all aspects of the project are managed.*

The Safety and Security Certification Plan (SSCP) makes certain technical specifications and construction meets the established safety requirements by ensuring all safety-related tests are completed and that all identified hazards are resolved. The safety content of operating procedures and training materials are reviewed to confirm they meet the established safety requirements. We manage and coordinate the Safety and Security Certification Plan Program the Systems Integration Test Plan Program.

The Systems Integration Test Plan encompasses the Test Plan, Test Procedures, and Test Forms. Test procedures will be developed by the appropriate vendor as it relates to their scope of work and will be incorporated as part of the Systems Integration Test Plan.

The Operational Tests will be performed by Safety and Security and Rail Operations personnel with the support of GLX Constructors and any required sub-contractors, as defined in the test plans.

Identify Key Systems Suppliers and Overall Systems Integrator

GLX Constructors' Lead Designer, STV, holds the role of systems integrator, and will make certain each of the systems successfully function individually and together. Our team has extensive experience with all of the key system suppliers as shown in Figure 4.1-5.

Key Systems Suppliers	Evidence of Previous Experience
Alstom Signaling	Alstom recently purchased General Electric Transportation Systems (GETS), whom GLX Constructors' team member, Balfour Beatty, successfully worked with on the MBTA Greenbush Commuter Rail Line Project.
Ansaldo STS (formerly Union Switch and Signal)	Ansaldo is a national and international provider of train control/signaling systems, engineering, and products and regularly works with the MBTA. GLX Constructors' team member, Balfour Beatty, has a previous working relationship with Ansaldo on the SEPTA Broad Street Subway Signal Upgrade Project.
Xo-Rail (Wabtec)	Xo-Rail is a nationally and internationally successful designer/provider of train control and communications systems. GLX Constructors' team members, Fluor and Balfour Beatty, are currently working with on the Eagle P3 Commuter Rail Project in Denver, CO.
Diverging Approaches Incorporated (DVI)	DVI has successfully performed/delivered transit/commuter rail projects across the country, performing engineering, procurement, systems installations supervision, testing, and final cutover oversight.

Figure 4.1-5. GLX Constructors' Experience with Key Systems Suppliers. *GLX Constructors will bring well-recognized suppliers with relevant systems integration experience to the Project.*


4.1.B TRAIN CONTROL SYSTEM DESIGN

Signaling and Train Control System Narrative

The Signaling and Train Control System (S&TCS) will comply with all the requirements specified in both the Technical Provisions and Specification by tracing the design back to a Requirement Traceability Matrix (RTM). The RTM

will be utilized to develop the Contract Deliverable Requirements List (CDRL) at the onset of the Project which will include all design submittals, document submittals, product submittals, as-builts, reports, and studies. The RTM will generate the ICDs that will support the holistic design approach to the Green Line Extension. The design of the S&TCS will go through multiple design checks throughout the life cycle of the project. This includes the QA/QC process, Intra and Inter-discipline reviews, and over-the-shoulder reviews with the client prior to each deliverable to ensure that all requirements are encapsulated.

S&TCS Architecture. The S&TCS for the Project will extend the existing signal system from its current terminus point at Lechmere Station to the new terminal stations at both College Avenue on the Medford Branch Line and Union Square on the Union Square Branch. The S&TCS will be functionally compatible with the existing MBTA Green Line utilizing a wayside Automatic Block Signal (ABS) system without absolute stop enforcement. The new system will tie into the existing system through a 96-strand fiber optic cable dedicated to the signal system. The new fiber cable will interface both the non-vital microprocessor and the vital microprocessor located within the new Lechmere Central Instrument House (CIH) with the existing Science Park CIH. The signal design technology between the existing system and the new will not change drastically. Vital relays will be greatly reduced with the implementation of microprocessors and lamp driver circuitry. The majority of the external line wire cables will be eliminated when the fiber optic cables are installed.

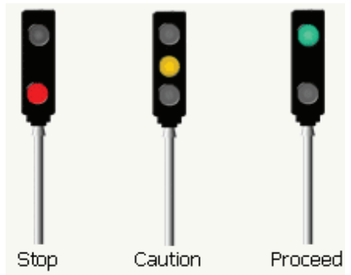

Wayside Signal. ***Each signal layout will be provided with appropriately colored LED lens units.***

The S&TCS major wayside equipment designed for the extension will consist of:

ABS block signaling system for movement authority and safe train separation. Automatic wayside signals will be installed along the alignment between interlocking to support the required headway and run time requirements. Color light signals that are either wall mounted or mast mounted. Each signal layout will be provided with appropriately colored LED lens units. Pedestal mounted signal layouts will include a foundation, split-base junction box, mast, and ladder. The number of aspects range from two to five, depending upon the design requirements.

We will use double rail on the main line and single rail in crossovers and turnout. The track circuit detection system will be immune to the 600-volt traction power system and provide broken rail detection. The insulated joint connections will allow the traction power return current to flow around the insulated joint.

Dual-control power switch machines and layouts will use vital relay control, overload, and point indication.



Impedance Bond (IB). ***The following is an example of an IB which may be used on the Project.***

We will install the following wayside equipment along the ROW:

- Hand throw switch machines with an electric lock.
- Snowmelter heating system.
- Automatic Vehicle Identification (AVI) systems, that is compatible with the existing on board systems. The AVI System will be used as the primary routing of trains through the interlocking.
- Wayside pushbuttons at route request locations.
- Prewired Central Instrument Houses (CIH).
- Prewired wayside junction boxes.



Switch Machine. ***The following is an example which may be used on the Project.***

Description of the Interaction of the S&TCS. The integration between the different systems will provide a holistic design concept to minimize any complications that occur during the design process. Coordination between Track, OCS, Traction Power, and communication subsystems is critical. The design requirements of the train control detection system are critical to provide a safe and reliable system. The light rail vehicle also plays an important role in the signal system design from the block design, track circuit shunting sensitivities, power requirements, and negative returns paths, to the placement of wayside equipment outside of the clearance envelope.

The S&TCS will be designed, installed, and tested, so the interface between the vehicles and the signal system provides a safe and reliable system. This is accomplished by:

- Providing interface documents, so all requirements are identified and addressed.
- Providing state-of-the-art equipment that meet or exceed the requirements as identified in the Project documents.
- Ensuring that the train detection system is able to detect the shunting sensitivity of the LRV.
- Providing optimum viewing of the wayside signals to the train operator and, if necessary, adding repeater signals.
- Interfacing the wayside AVI subsystem with the LRV carborne equipment to make certain the AVI message is transmitted and received.
- Providing interlocking signals to indicate the status of the interlocking and route alignment.

The interface between the signal system and the track design will be coordinated to clearly identify the limits of VMF yard control functions.

“Our designs make certain no single point failure of a component or subsystem (including dependent failure(s)) will cause an unsafe condition.

This will indicate the LRVs are "clear" of the revenue service on the Branch lines. Both the Union Square Branch and the Medford Branch Yard leads will support LRVs operating in either direction; this will be accomplished by locating either wayside pushbuttons and/or AVI loops on the Yard leads to allow for trains entering or exiting revenue service.

Description of the S&TCS Proposed Fall Back Operation. Green Line Operators are required to contact the Operations Control Center Light Rail Dispatcher should they encounter a signal holding red after one minute or is improperly displayed. They may not proceed by the signal unless directed to do so by the Dispatcher or an authorized official – traveling at restricted speed until the clearing signal for that block, watching for switch unaligned, another vehicle, broken rail, or other obstruction. Upon motivation of a signal malfunction, a Signal Maintainer is immediately dispatched to the area. Signals malfunctioning and holding red, or signal failures, result in the institution of a manual block in the affected area. A manual block requires that authorized personnel are placed in the affected area, and serve to clear Green Line trains in the affected area.

The signal system operation on the extension will be designed to support three different modes of operational control:

- Remote from the office
- Local from the CIH
- Field automatic from the AVI system

Under normal operations, the signal system will automatically run in field via the AVI system. Pushbutton will installed to support the AVI system in the case of failure. Remote operations will be utilized for any route that is not supported by the AVI system. Local control operation can be utilized under emergency or maintenance situations.

The design of the Project will ensure that there will be a flawless transition between the existing signal system and the new S&TCS. The new signal system will support all operational requirements, such as headway and run time durations, as specified in the Technical Provisions Section 1.3.1.

Description of the S&TCS Yard Control Strategy and Interface. The strategy for vehicle movement in the Yard and Rail Maintenance Facility will include the use of "yard maps", video monitoring and the installation of clearance markers. Direction from Authorized personnel in accordance with operating rules will dictate all movement within the Yard and Maintenance facility area. A requirement for movement into or out of a maintenance facility requires the assignment of personnel to watch the vehicle move through the bay door area. Other safeguards include the restriction of speed within maintenance facilities to no greater than three (3) miles per hour. All yard and repair facility moves require Operators to be observant of switch position, obstructions on the track and overhead catenary condition.

The VMF yard will be a non-vital yard with no signaling system interaction except when entering and leaving the yard. To prevent the possibility of a runaway rail vehicle from entering the mainline or fouling adjacent tracks, a hand-thrown sliding block derails will be installed on yard leads. Coordination between the MBTA Operations and the Signals and Communication Group will be required to ensure all requirements are addressed.

Description of S&TCS Integration with the Vehicle

We will implement the systems integration process by using a systematic approach to managing system components and interfaces. At the start of the Project, we will hold a meeting with the MBTA Railroad Operations team to review current, applicable MBTA standards and our design approach. This will result in alignment of ICDs so that all requirements are addressed.

To ensure full compatibility of all signal system requirements, we will coordinate all relevant signal system activities, with special attention given to electromagnetic interference (EMI) and signal system compatibility. GLX Constructors will review and evaluate the MBTA's Specifications for all proposed signal equipment to make certain the provided equipment meets the intent of these specifications.

Past Experience. GLX Constructors has extensive experience in relay and microprocessor based designs of interlocking control, ABS and cab signaling systems, block design and block design analysis, highway crossing design with interface to traffic control systems, vehicle and communication systems interface, staging, planning, and construction management services for new train control systems and modifications to existing systems.

In addition to design experience in transit and railroad train control design, GLX Constructors' key team members have experience in installing, testing, and commissioning transit train control systems, including the existing MBTA Green Line, Orange Line, and Red Line segments.

Within the past years, we have provided systems-related services for the MBTA, St. Louis Metro, Charlotte Area Transportation System (CATS), Chicago Metra, Long Island Railroad (LIRR), Metro-North Railroad (MNR) Los Angles MTA (LACMTA) Baltimore MTA, and Portland Tri-Met.

Lessons Learned. Our most significant lessons learned from our past experience is the use of excellent communication. At the Project start, we will comprehensively develop a Systems Integration Management Plan. A properly conceived, managed, and executed Systems Integration Management Plan significantly reduces the potential for schedule impacts, workarounds, and other surprises by making certain that each new system design is properly integrated.

A critical element that will support the reliability and uptime of the communication systems will be the uninterruptible power supply (UPS). All

communication network elements will be supported by the UPS. The UPS will supply battery backup power to communication room equipment including remote and local switches and be sized to support the actual full load for a minimum of 8 hours. Local AC power will serve as the incoming source for the UPS battery.

4.1.C COMMUNICATION SYSTEMS DESIGN

Overall Systems Topology/Systems Connection Diagram

Figure 4.1-6 depicts the typical subsystem interfaces located throughout the Project as it relates to the Communications System. By using internet protocol (IP) devices, the design is able to extensively use network switches and routers to integrate a variety of subsystems.

A key interface is the public address system with the variable message signs. These two subsystems supplement each other by providing audio and visual messages to station passengers. Additional key interfaces are the closed circuit television (CCTV) system with the transit passenger information system and the access control system. Included in the list of key interfaces is the physical interface of the fiber optic backbone. This component is critical to providing all other means of various subsystems to communicate with each other.

The main success of the fiber optic backbone is tying it into the existing fiber infrastructure located at Science Park Station. Secondly, to ensure successful implementation of the fiber optic backbone throughout the extension, we will coordinate with the MBTA to ensure end-to-end connectivity. The fiber optic backbone provides direct interface between the subsystem and the end user for SCADA, Automatic Fare Collection, and other communications systems.

“ Our Train Control System personnel have railroad system engineering backgrounds with over 150 years of combined signals and train control design and field experience.

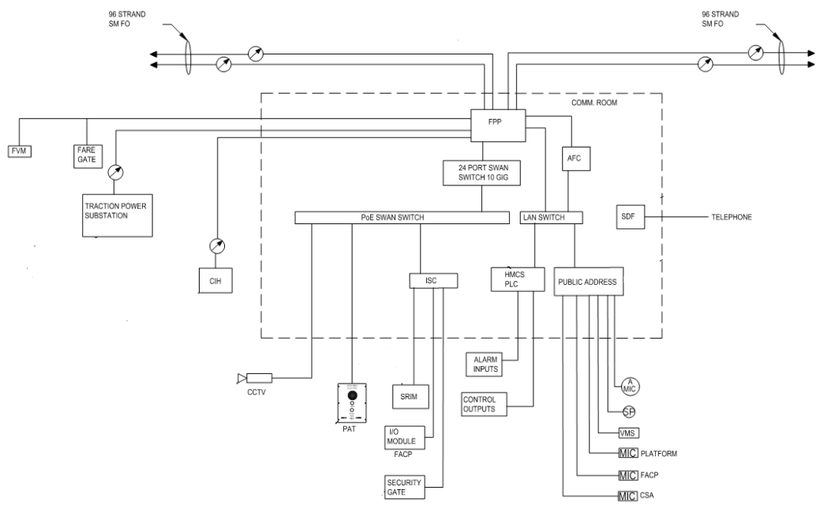


Figure 4.1-6. Communication Block Diagram.

Description of Communications System Design and Functionality

The MBTA's ***fiber optic system*** for the Project will tie into the existing fiber optic backbone at Science Park Station. The MBTA's existing fiber optic backbone, along the ROW, consists of two 96-strand cables. One 96-strand is currently dedicated to Communications system while the other is dedicated to Signal systems. The existing fiber optic cables are located in the existing trough on the viaduct. The Project will extend the infrastructure and fiber optic cables to new subsequent stations and wayside facilities within the scope of the Project. Various subsystems will utilize the fiber optic backbone to communicate throughout the MBTA system including but not limited to the ***Public Address (PA) and Transit Passenger Information System (TPIS), Closed Circuit Television (CCTV), Supervisory Control and Data Acquisition (SCADA) with Hub Monitoring and Control System (HMCS), Access Control System (ACS), and Fare Vending Machines.*** Each passenger station and wayside facility will have one or more of the aforementioned communication subsystems furnished and installed. In addition to interfacing with the fiber optic backbone, many of the communication subsystems will have interface with each other. CCTV will interface with ACS and the Passenger Assistance Telephone (PAT), PA will interface with TPIS and more. Many of the subsystem interfaces will be done via network layering via the sites network switch and router. Some interfaces, for the purposes of performance or safety, will be hardwired connection.

The station PA system will provide coverage throughout the passenger station covering the platform and mezzanine areas. The new PA system will integrate and interface with the existing Rockwell Collins (formerly ARINC) public address and variable message signs (VMS) headend hardware and software located at the operations control center (OCC). The new PA system will consist of loud speakers, microphones, digital signal processors, power amplifiers, and station control units. The system will provide an even audio output sound level throughout the station. The public address system integrate and interface with respect station's VMS. The VMS will be a light emitting diode (LED) scrolling sign that provide image. The integration and interface between the VMS and the PA system will provide the functionality to display text corresponding to the public address announcements. VMS units will all generate arrival messages. VMS units will be located on the station platforms and mezzanine.

The closed circuit television (CCTV) will provide real time internet protocol (IP) based video coverage at the passenger stations and yard. The CCTV will be a conduit to monitor, verify, and manage operations and incidents from the MBTA's OCC. The CCTV will utilizes Power over Ethernet (PoE) cameras that will view and cover public segments of the paid station areas, elevators, bike storage locations, access controlled doors, and pedestrian track crossings The CCTV system will utilizes camera, video servers, video recorders and local/ wide area network to view, transmit and store digital video streams. The CCTV system will be compatible with MBTA's existing video management system. The

CCTV system will integrate with the station's passenger assistance/information telephone (PAT) and elevator assistance telephone system.

Both the passenger and elevator telephone system will be ***Voice over Internet Protocol (VoIP)*** and be compatible with the existing PAT server located at the MBTA's customer call center. The PAT will provide two way voice communication at the passenger stations. PATs will be located at station fare collection area, platforms, and customer service areas. PATs and elevator assistance telephones will be viewable by the CCTV systems. A separate telephone network will be provided using the public switched telephone network (Verizon Centrex). Avaya VoIP telephones will be provided in accordance to the MBTA requirements. These phones will be compatible with the Avaya G450 gateway, PoE, and be mountable. The Avaya telephone will utilize category 6 (CAT-6) cabling infrastructure as it means of transmitting and receiving calls.

The access control system (ACS) portion of the project will be used to secure areas, facilities, rooms, and vehicle parking facilities. The ACS will consist of proximity card readers, electric door strike, magnetic door contacts, infrared request to exit, intelligent door controllers, and system controllers. All components of the ACS will interface and be controlled by the existing MBTA Lenel OnGuard system. Therefore, all ACS devices will be compatible with the existing MBTA Lenel OnGuard system. The ACS doors will be viewable by the CCTV system. The ACS will utilize the security wide area network to provide monitoring and control of system back to OCC.

Fare system interface will provide fiber optic cable connection to the array of fare vending machines located in the passenger stations. Each AFC room will provide cable management and an AFC switch. The AFC room will interface with the wide area network by way of Communications room switch via fiber optic cable. Fare vending machine installations will be based on MBTA requirements.

The Supervisory Control and Data Acquisition (SCADA) with Hub Monitoring and Control System (HMCS) will be provided as mean of automatically and manually monitoring an array of systems and subsystems within the MBTA infrastructure. The system will be wired with all necessary auxiliaries, and PLC programming software. The system will be fully integrated via software and hardware elements into the existing 45 High Street communications pre-processors, this includes integration of modules, points, and devices. SCADA/HMCS will be provided at stations and traction power substations. SCADA/HMCS subsystem interface includes HVAC, electrical, fire alarm, and plumbing systems.

A critical element that will support the reliability and uptime of the communication systems will be the uninterruptible power supply (UPS). All communication network elements shall be supported by the UPS. The UPS shall supply battery backup power to communication room equipment including remote and local switches. The UPS shall be sized to support the actual full load for a minimum of 8 hours. Local AC power shall serve as the incoming source for the UPS battery.

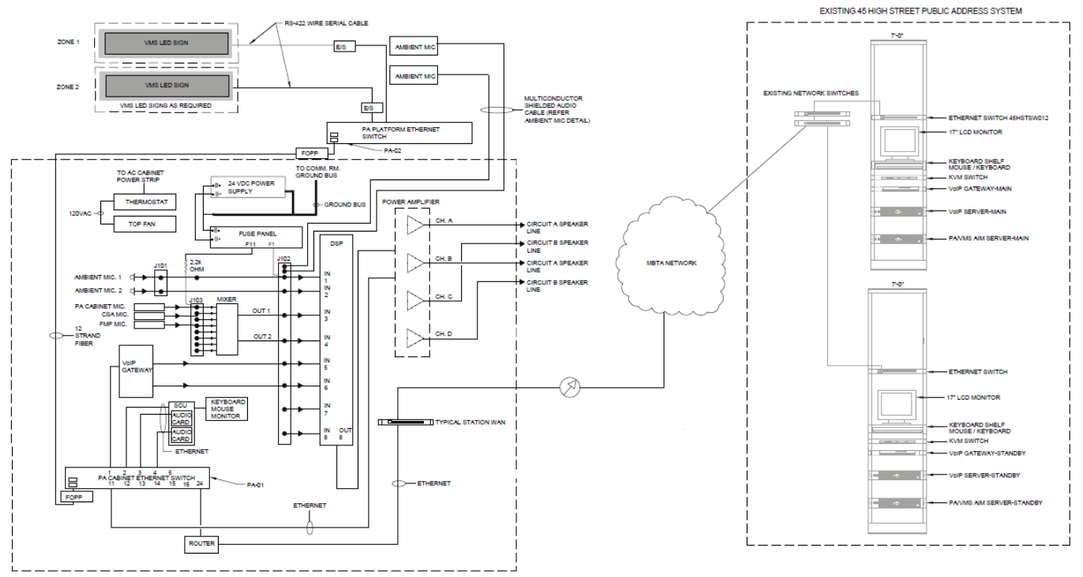


Figure 4.1-7. Project-specific Public Address Block Diagram.

Methods of Providing an Open-Data Link

Figure 4.1-7 demonstrates our approach to providing an open-data link to provide information on vehicle and systems scheduling and announcements.

Description of How the Proposed Communications Systems will Interface with Existing Communication Systems

We will closely coordinate with the MBTA in establishing a deep understanding of the MBTA's existing fiber optic infrastructure. We will identify all physical infrastructure communication ties needed to have a complete system interface as required by the project. GLX Constructors will evaluate existing infrastructure data to coordinate establishing an extension of the wide area network for the communication and signal systems. Integration of new infrastructure will be structured not to impede on existing Green Line operations. Test plans and procedures will provide for the various subsystems to be tested and commissioned. Performance and compliance testing will be conducted for each station and wayside facility subsystems to verify and confirm proper interface and integration between subsystems. Additional testing will confirm proper interface and integration to and between the various remote locations.

4.1.D TRACK WORK SYSTEM DESIGN

We have experience on many large system-intensive railroad projects in narrow corridors similar to the Project. The limited ROW on these constricted corridors requires close coordination between the track and system designers to verify

"Our crosschecks go beyond determining that the footprint of the equipment remains in the ROW; the vehicle clearance envelope needs to be checked, safety walkways around the bungalow or cantilever need to be verified, and grading and drainage need to be provided.

all discipline's equipment will properly fit. Such coordination includes verifying the vertical and horizontal location and size of the equipment, that the existing topography and ROW of site that will allow for equipment installation, and that the economical staging of the equipment installation is possible.

Description of the Overall Approach and Technical Details of the Track Work System

Design of Track Bed Structure to Minimize Noise and Vibration. GLX Constructors will follow all noise and vibrational mitigation requirements of the Project Environmental Assessment for the design of the proposed track bed structure.

Special Track Work Configurations. We have reviewed if the alignments can be revised to utilize standard trackwork. Upon our review, we have revised the alignments for the two custom diamond crossovers shown in the Definition Plans. One of the crossovers is located on the yard lead tracks (Brick Bottom Interlocking as shown in Figure 4.1-8) and one is located at the approach to the Union Square Branch. The diamond crossovers are now composed of standard turnouts.

Description of Design Approach and Criteria Designed to Meet the Noise and Vibration Requirements. GLX Constructors will follow all MBTA or Technical Provision Noise and Vibration Mitigation requirements. We will also follow all noise and vibrational mitigation requirements of the Project Environmental Assessment.

Design Approach and Criteria to Minimize Rail Corrugation. Technical Provision 10.2.3.3 (b) (ii) requires head harden 115 RE rail for the Light Rail tracks.

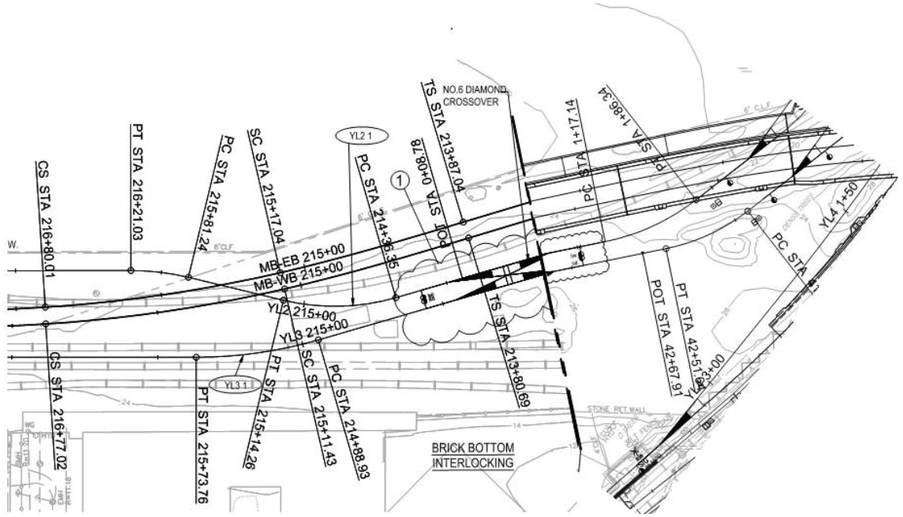


Figure 4.1-8. Brick Bottom Interlocking. *The use standard special trackwork instead of the custom trackwork proposed in the Contract Documents is more cost effective for initial procurement but it is also more cost effective to maintain.*

This type of rail will help mitigate rail corrugation by resisting material flow on the running surface of the rail.

Description and Drawing of the Proposed End of Track Device

Technical Provision 10.2.3.3 (l) (i) – Miscellaneous Track Appurtenances requires either a sliding friction or hydraulic Bumper Posts at the end of tracks. GLX Constructors will use Sliding Friction Bumper Posts at the ends of the Medford Branch, the end of the Union Square Branch, and at the single stub storage track in the storage yard. This is a common, economical type of bumper used throughout the Industry and will supply the stoppage needed for the LRVs used on the system.

Please reference Drawing (S-012 in Section 4.2 for end of track device detail drawings).

Design Narrative Describing Our Approach to Meet Special Track Work Requirements

Description of Design Methods, Standards Used, and Supporting Design Criteria. Our track design is based on the Technical Provisions, Contract Definition Drawings, the MBTA's Standards, the latest AREMA Guidelines, and common industry practices.

Technical Provision Section 10.2.3.3 (k) (xi) requires mainline turnouts to be a minimum size of #8. The Contract Definition Plan have #6's crossovers at the East Somerville Interlocking and a #6 turnout on the US-EB connection to the YL-4 track. The smaller size special track work is needed because of site constraints, and we will be using the same size in these locations. We have kept the same size turnouts in all locations shown in the Definition Plans.

Technical Provision Section 10.2.3.3 (k) (viii) stated emergency crossovers at Sta. 201+00 and Sta. 319+00 on the Medford Branch will be size #6 Electric Lock and we have included these in our plans.

Technical Provision Section 10.2.3.3 (n) (iii) requires yard turnouts to be a minimum size of 150' curve radius, and we will meet this requirement.

As part of the Project, there is no new special track work on the New Hampshire Line. Per Technical Provision 10.1.3.1 (e), the only activity for special track work required on the New Hampshire Line is to shift and lower the #15 Left-Hand turnout on NH-T1 to YL-10.

Description of the Approach to the Project Operations of Track Work Components. GLX Constructors has reviewed the Technical Provisions and will meet these requirements.

Description of Special Track Work Design. The majority of the special trackwork follow the standard MBTA designs. Some required custom designs that generally follow the MBTA standards and the Re-Definition plans drawings.

See the MBTA standards and the track plans for details, including MBTA Special Trackwork Standard Drawings:

- Drawing #2000 – Standard Turnouts General layout
- Drawing #2002 – Standard Crossovers General layout
- Drawing #615 – Trackwork Plan for 150' C.R. Turnout
- Drawing #510 – Arema Modified No. 6 Turnout
- Drawing #2082 – No. 8 Welded Turnout Tie & Rail Layout
- Drawing #2102 – No. 10 Welded Turnout Tie & Rail Layout

Special Track Work Drawings

Special Track Work Geometry, Guardrails, and Restraining Rails. We will follow the Commuter Rail Design Standards Manual and the Technical Provisions to use guardrails at strategic locations and restraining rails on track curves.

The MBTA's Commuter Rail Design Standards Manual (CRDSM) Chapter 4, Part N requires resilient guardrails for the New Hampshire Commuter Line on bridges and hazardous locations like next to high voltage structures. The only bridge that will need guard rail is the Washington Street Bridge and the only Traction Power Substation adjacent to the New Hampshire Commuter Line is Gilman. We will provide guardrail at these locations.

Technical Provision Section 10.2.3.3 (e) requires Guardrail for the Light Rail trackwork to be used at certain locations such as bridges, stations, abutments, etc. Technical Provision Section 10.2.3.3 (d) requires Restraining Rail for the Light Rail trackwork to be used on the inside rails in curves from 100' to 1,000' radius. Curves of less than 100' will have restraining rail on both rails. For details, see MBTA Standards BSTP Drawing No. 900 Bridge Guard Installation Details and Drawing No. 905 Resiliently Fastened Bridge Guard Rail.

For GLX Constructors' Track Geometry details, see Section 4.6 Track Plans.

Proposed Track Structure/Rail Fastening Systems. GLX Constructors will follow the MBTA Commuter Rail Design Standards Manual (CRDSM) and the Technical Provisions in regards to Rail Fastening Systems. The MBTA Commuter Rail Design Standards Manual (CRDSM) Chapter 4, Part J requires resilient fasteners for any new trackwork on the New Hampshire Commuter Line. Technical Provision Section 10.2.3.3 (c) requires a fastening system for the Light Rail trackwork which will electrically isolate the rail from the tie and the ballast. See the MBTA Railroad Operations "Commuter Rail Material Specification No. 9269" and "Resilient fasteners Material Specification No. 9245".

Signals and Communications Infrastructure. See Drawing SYS-007.

4.1.E TRACTION POWER SYSTEM DESIGN

Traction Power Supply Design Process, Software Tools and Prior Evaluation of Load Flow Modeling, and Service Plan Proposed and Description of the Traction Power Supply Design, Failure Modes, and Mitigations

The proposed traction power system design is based on Section 11.1 of the Technical Provisions and supported by Redefinition Task drawings. Our technical and design approach are detailed below.

Utility Power Supply System. The proposed power supply system configuration reflects the modified MBTA 13.8 kV traction power system "spider diagram" that was included with the Redefinition Task drawings and described in the final Volume 2 Technical Provisions. Eversource will provide two independent, redundant underground 13.8 kV supply circuits to the Red Bridge Traction Power Substation (TPSS), and two independent, redundant underground 13.8 kV supply circuits to the Pearl Street TPSS. Two redundant aerial 13.8 kV circuits will be constructed between Pearl Street TPSS and Ball Square TPSS (circuits 0-54-1/RF1 and 0-54-2/RF2, installed on opposite sides of the ROW). If any one of these 13.8 kV supply circuit segments should trip off-line due to an electrical failure or construction accident, the remaining circuits will be capable of sustaining peak operational load indefinitely.

Traction Power Substations. New traction substations will be located at Ball Square, Pearl Street, and Red Bridge. These will be typical, MBTA double-ended (fully redundant) traction power substations equipped with the equipment specified in the Technical Provisions, including: dual 13.8 kV buses; dual 3 MW rectifier-transformer units; bus duct interconnections to rectifiers, 800 V class dc switchgear, and negative drainage board; dc disconnect switches for each dc circuit breaker; station battery system; 15 kV local control and instrument panel; SCADA and substation automation systems (SAS); and technical support equipment including 13.8 kV ground and test devices.

Ball Square and Pearl Street TPSS will each have six dc feeder breakers including two spares, and Red Bridge TPSS will have fourteen dc feeder breakers including three spares. The substations will be site-constructed, with floor plans and equipment arrangements similar to the Redefinition Task drawings, reflecting the equipment clearances as specified in Technical Provision Section 11.1.

The double-ended configuration of these substations mitigates the potential outage of any single piece of equipment due to electrical failure, accident, or maintenance. The substation is designed to operate indefinitely at peak operational load with any single piece of equipment out of service (a single contingency outage condition). Spare 13.8 kV and 600 Vdc circuit breakers will be provided for future or emergency (replacement) usage.

DC Power Distribution System. The dc power distribution system will be sectionalized and configured in accordance with the Redefinition Task drawings and as specified in the Technical Provisions. Power sections 14E, 14W, 13E and 13W will be supplied from Ball Square TPSS. Pearl St. TPSS will be connected to power sections 13E, 13W, 12E and 12W. Red Bridge TPSS will be connected to new power sections 12E, 12W, 11E, and 11W. Existing power section S-8 from Science Park Station to the extension interface will be divided into inbound and outbound power sections 8E and 8W. The outbound end of power sections 8E and 8W will be connected to Red Bridge TPSS, and the inbound end will be supplied by existing cables from North Station TPSS.

Within each TPSS, two 2,000 kcmil cables will be provided between each dc feeder breaker and each TPSS dc feeder disconnect switch. Two 1,000 kcmil cables will be installed between each TPSS dc feeder disconnect switch and each trackside disconnect switch for interface with the OCS. Two 1,000 kcmil aerial supplemental cables will be connected in parallel with the main line OCS for each track and tapped to the OCS as specified in the Technical Provisions.

Normally-open OCS tie switches (TPSS bypass switches) will be provided trackside at the interfaces between adjacent power sections. These switches can be closed to mitigate the outage of a dc feeder circuit resulting from electrical failure, accident, or maintenance.

DC Negative Return System. Ball Square and Pearl St. TPSS will each have four 2,000 kcmil negative return cables installed between the negative drainage board in each substation and the nearest cross-bonded track impedance bond. Red Bridge TPSS will have ten 2,000 kcmil negative return cables; these will be connected to the Medford and Union Square branch track impedance bonds, and to the VMF shop and yard tracks. Sufficient cables are provided to mitigate the outage of any negative return cable due to electrical failure, accident, or maintenance. The running rails for each main line track pair will be supplemented by a common 2,000 kcmil negative return cable that will be installed in the ballast, and connected to track cross bonds.

VMF Shop and Yard Traction Power System. The VMF shop and storage yard OCS will be powered from dc feeder breakers located in the Red Bridge TPSS. One of these feeders will be dedicated to the VMF shop OCS and auxiliary/stinger power switchgear that will provide power to two shop tracks. Normally open disconnect switches in the yard area will mitigate the potential outage of a feeder cable circuit due to electrical failure, accident or maintenance.

Unit Substations. Each of the three traction power substations will be equipped with a double-ended unit substation powered by a feeder from each 13.8 kV TPSS bus as specified in the Technical Provisions. The redundant 13.8 kV supply circuit and associated step-down transformer will mitigate the outage the supply equipment that could result from electrical failure, accident or maintenance. Dual-source substations will also be provided at each passenger station. Each passenger station substation will obtain power from an Eversource 13.8 kV feeder, and one backup feeder from the nearest TPSS. An automatic transfer switch (ATS) connected to these two 13.8 kV sources will automatically switch between them when needed.

Software Tools and Prior Evaluation of Load Flow Modeling. GLX Constructors will conduct a comprehensive load flow simulation study to confirm that the proposed design will perform satisfactorily under the normal operational conditions and single contingency outages described the Technical Provisions. These operational conditions include three-car trains composed of AW3-loaded Breda Type 8 vehicles operating at five minute headways on each branch, and 2.5 minute headways on the shared portion of the extension. The study results will be communicated to MassDOT in a format similar to the December 30, 2016 DC Traction Power Loadflow Report prepared by the AECOM/HNTB Joint Venture that was provided with the GLX RFP. The system and vehicle information contained in the appendices to the December 30, 2016 load flow report will be referenced to build the load flow model, augmented as required by approved system design updates.

GLX Constructors will utilize the latest version of the Electric Traction System Analyzer (ETSA) for the load flow simulation study. An older version of the ETSA software was used by the AECOM/HNTB JV to perform the load flow simulations on which the current Project is based. The author of the ETSA software suite currently works for our Lead Designer. The baseline 3-car operation case from the December 30, 2016 load flow report will be modeled as a first step to compare results and confirm the validity of the load flow model. After the model has been confirmed, the single contingency outage scenarios will be simulated.

Conceptual Traction Power System Single Line Diagram

See Drawing SYS-004 and SYS-005.

4.1.F OVERHEAD CONTACT SYSTEM DESIGN AND TECHNICAL DETAILS

A successful OCS system design is distinguished by safety, high quality, high reliability, and ease of installation and maintenance. Our team will provide these attributes to lower life cycle cost on the Green Line system through unique interdisciplinary knowledge, experience, and proven processes. A contract documents requirements list will include pertinent industry standards and lessons learned from our experience. This list serves as an audit document for the QMP and will be heavily referenced during design and system validation so that our system will be safe and reliable for the MBTA and the public.

Description of the Overall Approach and Technical Details of the OCS

Design requirement documents prepared during the preliminary design stage are the cornerstone to the OCS design. Design requirements will incorporate fundamental properties, such as the MBTA's operating and maintenance plans,

installation and maintenance tolerances, and local climatic, geological, or environmental conditions. We have included functional characteristics such as conductor particulars, pantograph security, half-tension length limits, and structure spacing into the design requirements, creating an improved system.

GLX Constructors will be involved during all stages of the design, installation, and validation to provide cross discipline experience, feedback, and constructability reviews. This increases the speed of design and review while reducing the probability of design changes during construction.

Conductor Typicals. The proposed design will utilize the conductors currently in use in the MBTA system so they may be interchanged with the existing MBTA network. The mainline alignment will be typical catenary construction utilizing balance weight assemblies to auto-tension 4/0 messenger and trolley wires over mainline and crossover tracks. Overlaps will be arranged throughout the alignment to best utilize the 3,000 feet maximum length and placed in tangent track where available to improve clearances. Supplemental feeders will be provided, when necessary, aerially at pole top and tensioned to reduce wind blow-off and maintain safe clearances between other wires, structures, and the public. Supporting the equipment aerially reduces the quantity of disconnect switches and the overall maintenance effort.

The train storage yard alignment will be semi-compensated single 4/0 trolley wire utilizing spring tensioners for all tracks (see example in Figure 4.1-9). The spring nominal tension will be set with coordination with the manufacturer to allow for the least sag at high temperatures while still maintaining the low temperature tension within safe criteria. Tension sections will be arranged around the yard to minimize the difference between the two trolley wires distance to fixed end from the track crossing or overlap point. This will reduce the variation in tension of the two crossing wires allowing for similar sag to reduce pantograph entanglement and maintenance efforts adjusting tensions at high or low temperatures.

Equipment Strategy. GLX Constructors plan to use products matching those mentioned in the Technical Provisions as well as those presently in-service on the MBTA system which have maintained positive performance records. By using well rated, compatible equipment, disruption to the MBTA can be minimized. The tie-in to the existing system at Land Boulevard will be simplified by utilizing the same equipment on the new alignment as the old. No revisions will need to be made to the MBTA's operating or maintenance procedures as the familiarity of the product and system is preserved.

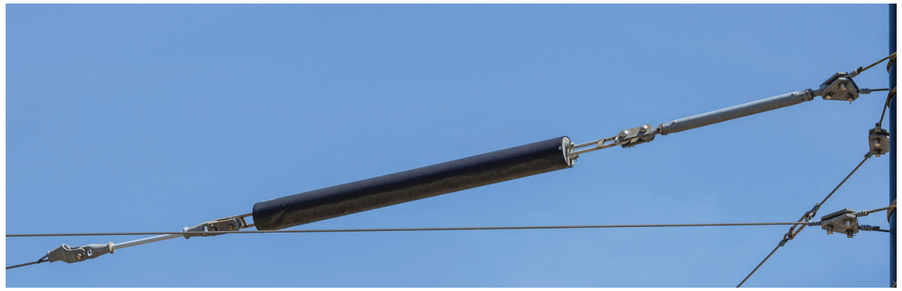


Figure 4.1-9. Example Spring Tensioner. *Tension sections will be arranged around the yard to minimize the difference between the two trolley wires.*

OCS Sectionalisation For Supporting Operations, Maintenance, and Overall Integration

The proposed design will be divided into power sections as mentioned in section 4.1.E.1 DC Power Distribution System and as shown in attached drawing SYS-004 and SYS-005. The sectioning allows discrete segments to be easily de-energized for emergency repair or planned maintenance while still providing service to the public by way of single tracking. The existing power section (S-8) will be further zoned into the same inbound/outbound power sections as the new Project and new supplemental feeders and feeder tap disconnect switches will be installed to support the zoning.

Disconnect switches for the yard power sections will be located centrally to allow easy operation and maintenance of the equipment.

Our design locates an overlap at the last span of the new viaduct which can be installed without demolition of the existing structure. This allows the OCS to be fully installed and tested west of the tie-in and will not be effected by further civil works. Once the old structure is removed, and the new viaduct married, only a short section of OCS will need to be installed and tested to provide the tie-in, reducing the duration for installation and testing.

OCS Pole Arrangements

The maximum allowable span lengths will be based on the calculated pantograph security using the UIC 606-1 leaflet along with AREMA and other industry standard best practices. The maximum span lengths and staggers will be selected such that the contact wire stays within the zone of the carbon strip under all adverse conditions. As the pantographs of the MBTA LRV's are not centered on the trucks, an allowance will be included in the calculation for curves to account for the pantograph centerline deviation from the track center. As necessary, the maximum allowable span lengths will be further reduced to $2\times\sqrt{Rc}$, where Rc is the curve radius, to meet Technical Provision requirements. The 6" safe zone from pantograph centerline as specified in the Technical Provisions will be verified by the pantograph security calculation and may be further reduced to provide safe operation.

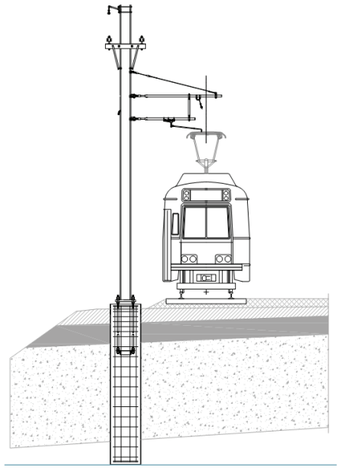


Figure 4.1-10. Typical Side Pole Arrangement. *Catenary above each mainline track will be supported from independent poles located to the sides of the LRV tracks whenever possible to increase the reliability of the system, increase safety of maintenance and account for track center constraints.*

Maximum allowable span lengths for particular track radiuses will be utilized where no other obstructions are limiting, such as special track work, underground utilities, or overhead structures. Span lengths will be gradually adjusted when increasing or decreasing to promote uniform pantograph performance throughout the system. A uniform system height will also be utilized over all unobstructed span lengths simplifying the installation effort and will be set based on the wire tension profile and minimum hanger length after the maximum tangent span length is established.

Poles will be hot dip galvanized steel with anchor base design and will be consistent with MBTA standards and existing poles. Wide flange poles will be utilized for the Medford and Union Square branch. Tubular poles are preferred in the yard due to accommodate the multiple load angles, as shown in Figure 4.1-10. Catenary above each mainline track will be supported from independent poles located to the sides of the LRV tracks to increase the reliability of the system and increase safety of maintenance as depicted in drawing SYS-002. Poles will be selected based on the Allowable Strength Design per the Technical Provisions to utilize only 2/3 the yield strength as well as limiting pole deflection. In addition, the pole selection will be checked using standard load factors according to NESC, AREMA, and AREA.

4.1.G AC VOLTAGE DISTRIBUTION

Typical AC Voltage Services

Typical AC voltage services with details of control and monitoring of services and equipment are shown in Figure 4.1-11.

Our design includes two independent 13.8 kV electrical services from Eversource for the Red Bridge Traction Power Substation (TPSS) and two independent 13.8 kV electrical services for the Pearl Street TPSS. Eversource requires installation of their standard electricity metering equipment at these substations solely for their own use, including potential transformers (PTs), current transformers (CTs), meters and communications. MBTA will need to obtain the same measurements obtained by the utility regarding electricity usage at these metering locations. To ensure this occurs, the digital substation automation system (SAS) that will be provided in each substation will duplicate the electricity metering functions provided by the utility's own metering equipment. The substation automation system includes the 13.8 kV PTs and CTs required for electricity usage measurements, and the necessary energy management software.

The SAS at each TPSS will also provide comprehensive local and remote monitoring of all substation equipment and critical building functions including fire, HVAC and access-related alarms, which will be visible to the SCADA master station at MBTA Power Control. It will provide data transfer, status indication, and control of all substation equipment per MBTA standard operating practice with which our Lead Designer, STV, is exceptionally familiar. Normal substation control will be possible from the SCADA master station, from the local TPSS SAS HMI screen, and from the local TPSS AC circuit breaker control and instrument panel (ACCP).

Unit substations will also be similarly-equipped with SAS for remote monitoring and control via the MBTA SCADA Master Station, as well as local monitoring and control. To assist with energy management, the unit substation SAS will be utilized to provide electricity usage metering of the entire unit substation, as well as sub-metering of individual connected circuits including the Transportation Building. Refer to drawing SYS-006 for a typical unit substation SAS block diagram.

Description of Redundant Supply Methodology and the Application of UPS and Local Utility Feeds

The AC power distribution system is configured to provide full redundancy for all essential GLX project loads. This redundancy will assure system resiliency and reliability as well as simplifying routine maintenance and repairs. This redundancy is achieved at the three traction power substations by the utilization

Activity Grouping	Description	Sheet Reference:	Location of Feed	Cables:
Traction Power Substations	Ball TPSS	TRACTION POWER S-2426 AND S-2436	PEARL ST. TPSS FEED 1 PEARL ST. TPSS FEED 2	13.8kV AC FEED 1 [0-54-1] 13.8kV AC FEED 2 [0-54-2]
	Pearl TPSS	TRACTION POWER S-2426	Eversource Feed 1 Eversource Feed 2	(2) - 13.8kV AC FEEDS
	Red Bridge TPSS	TRACTION POWER S-2450	Eversource Feed 1 Eversource Feed 2	(2) - 13.8kV AC FEEDS
Signal CIH's	Lechmere CIH	TRACTION POWER S-2702	RED BRIDGE SUBSTATION	2#3/0 AWG AND #4 GND
		Lechemere E-100	Lechmere Station	2#1/0 & 1#6G in 2"C
		Lechemere E-100	Lechmere Station	4#1 & 1#6G in 1 1/2"C
	Red Bridge Main CIH	TRACTION POWER S-2705	RED BRIDGE SUBSTATION	4#1/0 AWG , 4#1 AWG AND 3#6 GND
	Brick Bottom CIH	TRACTION POWER S-2706	RED BRIDGE SUBSTATION	4#300 KCMIL, 4#2/0 AWG AND 3#4 GND
	Washington (E. Somerville) Satellite CIH	TRACTION POWER S-2708	PEARL ST. SUBSTATION	8#500 KCMIL AND 4#3 GND
		East Somerville E-100	East Somerville Station	2#4/0 & #4G in 2 1/2" C
		East Somerville E-100	East Somerville Station	4#1/0 & 1#4G in 2"C
	Washington (E. Somerville) Main CIH	TRACTION POWER S-2709	PEARL ST. SUBSTATION	8#500 KCMIL AND 4#3 GND
		East Somerville E-100	East Somerville Station	2#300KCMIL & 1#4G in 3"C
		East Somerville E-100	East Somerville Station	4#2/0 & 1#4G in 2"C
	Gilman CIH	TRACTION POWER S-2716	PEARL ST. SUBSTATION	4#1/0 AWG , 4#1 AWG AND 3#6 GND
	Ball Sq. CIH	TRACTION POWER S-2717	BALL SQ. SUBSTATION	4#1/0 AWG , 4#1 AWG AND 3#6 GND
	College Ave CIH	TRACTION POWER S-2723	BALL SQ. SUBSTATION	6#500 KCMIL AND 3#2/0 AWG GND
		College E-100	College Station	2#1/0 & 1#6G in 2"C
		College E-100	College Station	4#1 & 1#6G in 1 1/2"C
	Red Bridge Satellite CIH	TRACTION POWER S-2725	RED BRIDGE SUBSTATION	4#300 KCMIL, 4#2/0 AWG AND 3#4 GND
	Union Sq. CIH	TRACTION POWER S-2730	RED BRIDGE SUBSTATION	6#500 KCMIL AND 3#3 GND
		Union E-100	Union Square Station	2#1/0 & 1#6G in 2"C
		Union E-100	Union Square Station	4#1 & 1#6G in 1 1/2"C
Passenger Stations	Lechmere Station	TRACTION POWER S-2444	RED BRIDGE SUBSTATION	13.8kV AC FEED [0-52-1]
		Lechemere E-100		13.8kV AC FEED (Eversource)
	East Somerville Station	TRACTION POWER S-2419	RED BRIDGE SUBSTATION	13.8kV AC FEED [0-52-5]
		East Somerville E-100		13.8kV AC FEED (Eversource)
	Gilman Sq. Station	TRACTION POWER S-2426	PEARL ST. SUBSTATION	13.8kV AC FEED [0-53-4]
		Gilman E-100		13.8kV AC FEED (Eversource)
	Magoun Sq. Station	TRACTION POWER S-2432	PEARL ST. SUBSTATION	13.8kV AC FEED [0-53-2]
		Magoun E-100		13.8kV AC FEED (Eversource)
	Ball Sq. Station	TRACTION POWER S-2436	BALL SQ. SUBSTATION	13.8kV AC FEED [0-54-4]
		Ball E-100		13.8kV AC FEED (Eversource)
	College Ave. Station	TRACTION POWER S-2442	BALL SQ. SUBSTATION	13.8kV AC FEED [0-54-3]
		College E-100		13.8kV AC FEED (National Grid)
	Union Sq. Station	TRACTION POWER S-2460	RED BRIDGE SUBSTATION	13.8kV AC FEED [0-52-3]
		Union E-100		13.8kV AC FEED (Eversource)
VMF Building		VMF-E-201		13.8kV AC FEED (Eversource)
Transportation Building		VMF-E-201	VMF BUILDING	3 SETS OF 4 #600KCMIL & #1G IN (3) 4" C AND 4"C SPARE
Pump Stations	Red Bridge	TRACTION POWER S-2706	RED BRIDGE SUBSTATION	(4) 4#500 KCMIL AND (2) #500 KCMIL GND
	Gilman Stormwater Station	Gilman E-100	Gilman Station	4 #4 & #8G IN 1 1/4" C
	East Somerville Station	East Somerville E-100	East Somerville Station	2 SETS OF 4 #350KCMIL & 1#1G IN EXISTING CONDUIT

Figure 4.1-11. Typical AC Voltage Services with Details of Control and Monitoring of Services and Equipment.

“The goal is to prevent failures from occurring and extending the service life of the capital plant. GLX Constructors will provide stray current corrosion control design elements that provide an economic approach to long-term performance.

of two independent 13.8 kV supply lines from Eversource at the Red Bridge and Pearl Street Traction Power Substations (TPSS), and the extension of the two independent 13.8 kV Eversource supply lines from Pearl Street TPSS to Ball Square TPSS. The 13,800-480/277 V unit substations within each TPSS will be double-ended, powered by a 13.8 kV feeder from each TPSS 13.8 kV bus. All critical loads in the TPSS buildings will be powered from automatic transfer switches (ATS) that can connect to either unit substation 480 V bus. Life safety TPSS building loads will also have Uninterruptible Power Supply (UPS) backup.

The passenger station substations at Magoun Square, East Somerville, Union Square, Ball Square, Gilman Square and Lechmere will each be powered by a 13.8 kV feeder from Eversource, as well as a backup 13.8 kV feeder from the nearest TPSS. College Avenue will be powered from a 13.8kV feeder from National Grid, as well as a backup 13.8kV feeder from the nearest TPSS. An ATS will automatically transfer from the normal utility feeder to the backup MBTA feeder in the event of a utility feeder outage. Life safety systems at each passenger station will be backed up by UPS systems as well as a separate UPS system to back-up security and communication systems. Lechmere Station will also be equipped with a natural gas powered emergency generator in accordance with the Technical Provisions.

The VMF Building will obtain power directly from a 13.8 kV Eversource service, augmented by a natural gas powered emergency generator for emergency and communications loads. The VMF Building main 480 V switchgear will feed the Transportation Building via a sub-metered circuit. Life safety loads in each both buildings will also have local UPS backup.

Central instrument House (CIH) signal equipment will be powered by dedicated 480 V feeders from the two nearest TPSS unit substation or passenger station substation; automatic transfer switches at each CIH will enable the signal equipment to be powered from either of these feeders, or from local UPS backup. Power to the communications rooms will be similarly redundant, including local UPS system backup.

Power to the Red Bridge pump station will be provided from two 480 V supply feeders from the Red Bridge TPSS unit substation, one from each 480 V bus. Power to the Gilman Square stormwater pump station and Washington Street pump station will be provided from Gilman Square and East Somerville passenger station substations respectively. The pump stations will be backed up by natural gas powered generators in accordance with the Technical Provisions.

4.1.H CORROSION CONTROL

Description of our Corrosion Control Strategy

GLX Constructors' team member, CorrTech, Inc., will study, evaluate, and mitigate the impact of corrosion on the Project. We will evaluate a variety of structures for corrosion exposure to develop a comprehensive corrosion mitigation program. Once identified, corrosion mitigation methods will be properly developed.

A baseline corrosion survey will be performed to determine soil corrosivity and identify other potential corrosion exposures along the Project corridor. This forms the basis for understanding and defining corrosion exposures that require mitigation. Stray DC current corrosion control design for running rail negative return transit systems will be implemented during final design elements in accordance with the guidance provided in the project Technical Provisions, Section 8.9.1, Stray Current Mitigation.

Methodology and Design for Controlling Corrosion

We will provide detailed specifications for material, surface preparation, application and final installation, dielectric strength evaluation and holiday testing. This will make sure that any stray current generated is contained in the ballast area of the structure and does not flow into viaduct reinforcement.

Precast prestressed concrete piles will be used for foundation support of the Vehicle Maintenance Facility and other ancillary buildings. Electrical continuity within the concrete piles or the steel elements would be established, with test wires and stray current monitoring capabilities provided. Where steel piles are used for foundation support, an allowance will be made for sacrificial steel as well as stray current monitoring capabilities.

Soil nail walls shall be provided with electrical continuity of the shotcrete mesh and reinforcement in the architectural wall. The soil nails are individual electrical elements and must be electrically isolated from each other as well as the reinforcing mesh and rebar. This requires electrical continuity is provided for the shotcrete wall mesh with properly sized mechanical crimps and tack welding of the reinforcing steel, with test stations 250-ft at intervals of physical break.

Mechanically stabilized earth walls, MSE, and modular precast wall sections would not have any metallic components in contact with the soil. No stray current design is required for these walls.

Soldier piles used for permanent retaining walls would be placed in drilled holes and backfilled with concrete. The soldier piles would be galvanized steel within the concrete encasement. The high resistance concrete encasement helps to provide electrolytic isolation and increased resistance to reduce the magnitude of resulting stray current. Electrical continuity of the H-piles will be provided with wire connections or wire mesh connections.

For the at-grade station and structures, all new construction shall be provided with stray current corrosion control. This includes bonding of the reinforcing steel for electrical continuity in pile caps and test stations and underground sections coated with dielectric coating to 12-in above finish grade.

For elevated stations, the use of dielectric coating to 12-in above finish grade of station and building components will be required. This will provide electrolytic separation in lieu of electrical bonding of reinforcing steel.

Qualified individuals within the CorrTech organization, based in New England, would provide the technical support required as related to stray current corrosion control. CorrTech provides in-house personnel who are NACE, API, ASNT UT, NASSCO PACP, EPRI, INPO, and OSHA certified.

Approach and Design Concepts for Reducing Stray Current

GLX Constructors' team member, CorrTech, will work with the Traction Power design staff during final design to develop elements intended to minimize the generation of stray current. These concepts include maximizing rail to earth resistance, minimizing negative return resistances and minimizing track to earth voltage escalations.

Where stray current control elements in the Technical Provisions provide sufficient control, they would be applied in the final design. Where improvements to the stray current control approach can be made, the best practice approach would be developed. GLX Constructors will provide stray current control as detailed in the Technical Provision.

For the Viaduct structures, stray current control relies on the long term performance of a dielectric spray on membrane. GLX Constructors will provide detailed specification for material, surface preparation, application and final installation dielectric strength evaluation and holiday testing. This is critical as to ensure that any stray current generated is contained in the ballast area of the structure and does not flow on viaduct reinforcement.

Methodology for Monitoring and Metering Stray Current during Construction

CorrTech will also provide technical corrosion engineering support to the construction project for the various components of construction. Stray current control components, as they are specified for this Project, involve tack welding of reinforced steel in cast-in-place concrete, test wire and junction box installation, specialized coating application on areas of concrete structures, and QA/QC testing and documentation. GLX Constructors will be responsible for developing specific field test procedures that are required to demonstrate acceptable criteria for acceptance during and at the completion of key structures and corrosion control elements.

Final QA/QC documentation will be provided during the construction work and at project completion. GLX Constructors will provide qualified individuals to perform the field testing associated with the QA/QC oversight.

After construction and prior to energizing the Traction Power Station, a stray current survey will be planned and executed. We will submit a detailed survey plan to the MBTA for review and approval prior to execution of the survey. Test points, test procedures, test equipment, and testing personnel will be identified in the plan. The purpose of the survey is to document the baseline stray current activity on the Project structures and adjacent underground utilities prior to energizing the traction power system.

Once the system is online and in revenue generation, a post stray current survey will be performed. This will follow and monitor changes in stray current activity as determined during the initial stray current survey. Test results and findings will be presented in a final report.

Description of Stray Current Best Practices

GLX Constructors' team member, CorrTech, are active participants in the development and review of NACE, IEEE, and other applicable industry standards. CorrTech develops in-house Standard Operating Practices (SOP) to provide field testing personnel with the means and methods for evaluation and assessment during QA/QC testing. This experience and knowledge allows them to constantly stay abreast of and incorporate current industry best practices.

GLX Constructors' Systems Integration Team will implement the approach as described within this section and will serve in a central role through all phases of design, construction, commissioning, and rail activation. This has proven itself effective on similar projects, and it will provide the MBTA with higher schedule and cost certainty.

RFP		
Drawing Number	**Drawing Title**	**Reference Section or Drawing**
		4.1 (Figure 4.1-5)
		4.2 (S-012)
	GLX Team will use MBTA Standard Drawings	MBTA DWG 2000, 2002, 615, 510, 2082, 2102
	GLX Team will use MBTA Standard Drawings	MBTA DWG 1225, 9269, 9245
SYS-001	OCS Typical Details – Conductor Particulars	
SYS-002	OCS Typical Details – Typical Side Poles – General Arrangement	
SYS-003	OCS Typical Details – Typical Low Clearance – General Arrangement	
SYS-004	Traction Power Single Line Diagram – GLX Main Line	
SYS-005	Traction Power Single Line Diagram – GLX Yard	
SYS-006	Substation Automation System (SAS) – System Block Diagram	
SYS-007	Special Trackwork Equipment Location Layout	

Technical Solutions Drawing Matrix.

AUTO-TENSIONED SIMPLE CATENARY			
CONDUCTOR PARTICULARS	UNITS	CONDUCTOR	
(UNWORN CONDITION)		CONTACT	MESSENGER
CONDUCTOR TYPE	-	4/0 KCMIL GROOVED	4/0 CW EK KCMIL 19 STRAND
MATERIAL	-	HARD DRAWN COPPER	HARD DRAWN COPPER
DIAMETER	IN.	0.482	0.571
CROSS SECTIONAL AREA	SQ. IN.	0.167	0.195
WEIGHT OF CONDUCTOR	LB/FT	0.6419	0.7484
WEIGHT OF SYSTEM (NOTE 1)	LB/FT	1.464	
RADIAL THICKNESS OF ICE (O)	IN.	0.5	0.5
WEIGHT OF ICE (O)	LB/FT	0.611	0.666
WEIGHT OF SYSTEM WITH ICE (O)	LB/FT	2.808	
CONDUCTOR BREAKING STRENGTH	LB	9154	15370
MAXIMUM SPAN	FT	145	
CONDUCTOR TENSIONS AT:			
60o F NO WIND	LB	3000	4000
CONDUCTOR SAG ON MAXIMUM SPAN AT:			
60o F NO WIND	FT	0.0167	0.962
SYSTEM HEIGHT	FT	2.5'-0" (NORMAL)	
CONTACT WIRE HEIGHT AT 60o F	FT	15'-0" (NORMAL)	
MODULUS OF ELASTICITY	PSI	1.70E+07	1.85E+07
COEFFICIENT OF EXPANSION	-/o F	9.40E-06	9.40E-06
MINIMUM FACTOR OF SAFETY	-	3.22	3.84


AUTO-TENSIONED SIMPLE CATENARY			
CONDUCTOR PARTICULARS	UNITS	CONDUCTOR	
(WORN CONDITION)		CONTACT	MESSENGER
PERMISABLE WEAR	% OF AREA	30.00	-
WEIGHT OF SYSTEM (NOTE 1)	LB/FT	1.261	
CONDUCTOR BREAKING STRENGTH	LB	6053	15370
MINIMUM FACTOR OF SAFETY	-	2.26	3.84

SEMI-COMPENSATED SINGLE CONTACT WIRE		
CONDUCTOR PARTICULARS	UNITS	CONDUCTOR
(UNWORN CONDITION)		CONTACT
CONDUCTOR TYPE	-	4/0 GROOVED TROLLEY-80
MATERIAL	-	HARD DRAWN COPPER
DIAMETER	IN.	0.482
CROSS SECTIONAL AREA	SQ. IN.	0.167
WEIGHT OF CONDUCTOR	LB/FT	0.6419
RADIAL THICKNESS OF ICE (O)	IN.	0.5
WEIGHT OF ICE (O)	LB/FT	0.611
WEIGHT WITH ICE (O)	LB/FT	1.252
CONDUCTOR BREAKING STRENGTH	LB	10820
RULING EQUIVALENT SPAN	FT	80
CONDUCTOR TENSIONS AT: (NOTE 2)		
60o F NO WIND	LB	2425
120o F NO WIND	LB	1575
0o F NO WIND	LB	3750
CONDUCTOR SAG ON RULING SPAN AT:		
60o F NO WIND	FT	0.212
120o F NO WIND	FT	0.326
0o F NO WIND	FT	0.137
CONTACT WIRE HEIGHT AT 60o F	FT	16'-0" NOMINAL
MODULUS OF ELASTICITY	PSI	1.70E+07
COEFFICIENT OF EXPANSION	-/o F	9.40E-06
MINIMUM FACTOR OF SAFETY	-	2.89

SEMI-COMPENSATED SINGLE CONTACT WIRE		
CONDUCTOR PARTICULARS	UNITS	CONDUCTOR
(WORN CONDITION)		CONTACT
PERMISABLE WEAR	% OF AREA	30.00
WEIGHT OF CONDUCTOR	LB/FT	0.449
CONDUCTOR BREAKING STRENGTH	LB	7574
CONDUCTOR TENSIONS AT: (NOTE 2)		
60o F NO WIND	LB	2425
120o F NO WIND	LB	1575
0o F NO WIND	LB	3450
CONDUCTOR SAG ON RULING SPAN AT:		
60o F NO WIND	FT	0.148
120o F NO WIND	FT	0.228
0o F NO WIND	FT	0.105
MINIMUM FACTOR OF SAFETY	-	2.20

NOTES:

1. SYSTEM WEIGHTS SHOWN HAVE BEEN CALCULATED BASED ON STANDARD HANGER SPACING AND TYPICAL DESIGN HANGER WEIGHT.
2. EQUIVALENT SPAN FOR FIXED TENSION CALCULATIONS IN Le -80 FT

CONTACT WIRE	MESSENGER WIRE MIDPOINT TIE WIRE	JUMPER WIRE	CURRENT CARRYING HANGER	PARALLEL FEEDER CABLE
				

ANCILLARY WIRES	
DESCRIPTION	USAGE
WIRE ROPE 3/8", 1X7, EHS	TERMINATIONS
WIRE ROPE 3/8", 1X7, EHS	SPAN WIRES
WIRE ROPE, 3/16", FLEXIBLE BRONZE	HANGERS
4/0 AWG, STRANDED SOFT DRAWN COPPER, CLASS G, NON-INSULATED	IN-SPAN JUMPER
4/0 AWG, STRANDED SOFT DRAWN COPPER, CLASS G, INSULATED	FEEDER TAP
1,000 KCMIL, STRANDED SOFT DRAWN COPPER, INSULATED	POSITIVE PARALLEL FEEDER CABLE

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


OCS TYPICAL DETAILS CONDUCTOR PARTICULARS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.
RS					

GV20170258-271.pdf

SCALE: NTS	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	BT	BT	RS	SHEET: SYS-001	

PLOTTED: 09/15/17 2:51PM BY:KINGMK
DRAWING: I:\PROPOSALS\GLX\SYSTEMS\PROPOSAL READY DRAWINGS\OCS\PROPOSAL_DETAIL_DRAWINGS.DWG [SYS-001] 09/11/17 2:54PM

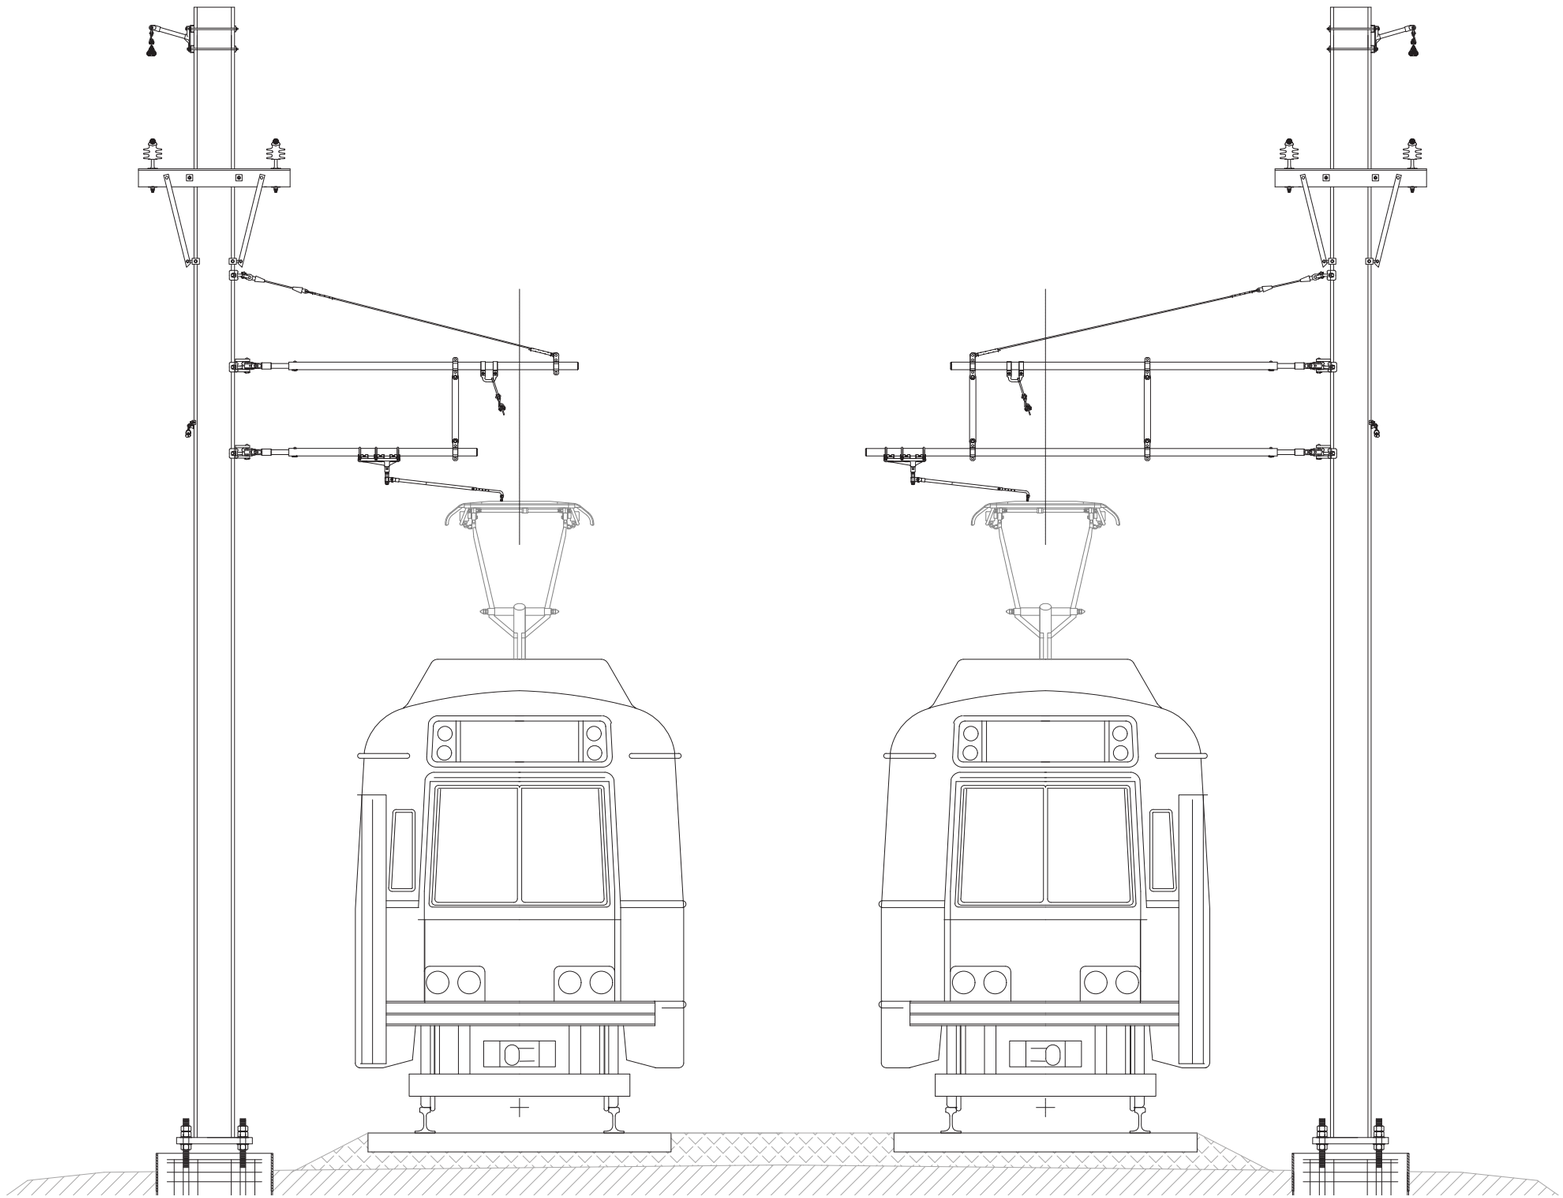

OCS TYPICAL DETAILS
TYPICAL SIDE POLE
GENERAL ARRANGEMENT

1/2"=1'-0" 0 1' 2' 4'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

OCS TYPICAL DETAILS
TYPICAL SIDE POLES
GENERAL ARRANGEMENT


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-271.pdf

SCALE: 1/2" = 1'-0"	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	BT	BT	RS	SHEET: SYS-002	

PLOTTED: 09/15/17 2:52PM BY:KINGMK
DRAWING: I:\PROPOSALS\GLX\SYSTEMS\PROPOSAL READY DRAWINGS\OCS\PROPOSAL_DETAIL_DRAWINGS.DWG [SYS-005] 09/11/17 2:54PM

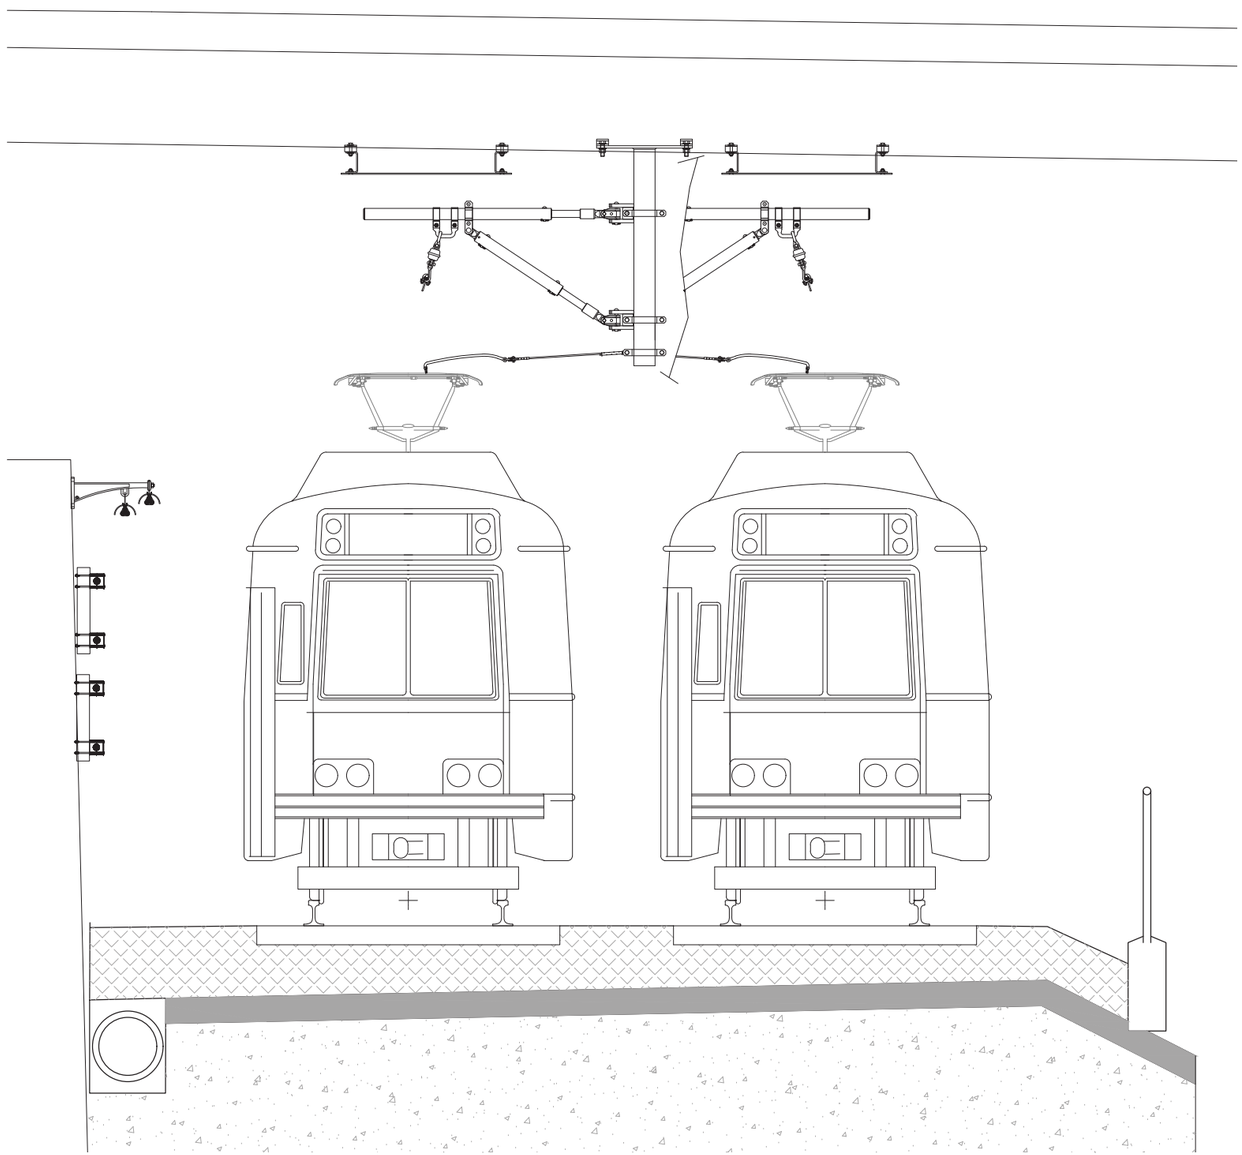

OCS TYPICAL DETAILS
TYPICAL LOW CLEARANCE
GENERAL ARRANGEMENT

1/2"=1'-0" 0 1' 2' 4'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

OCS TYPICAL DETAILS
TYPICAL LOW CLEARANCE
GENERAL ARRANGEMENT

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-271.pdf

SCALE: 1/2" = 1'-0"	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	BT	BT	RS	SHEET: SYS-003	

PLOTTED: 09/15/17 2:52PM BY:KINGMK
DRAWING: I:\PROPOSALS\GLX\SYSTEMS\PROPOSAL READY DRAWINGS\OCS\PROPOSAL_DETAIL_DRAWINGS.DWG [SYS-006] 09/11/17 2:54PM

NOTES:

1. THIS DRAWING IS A CONCEPTUAL AND SIMPLIFIED SINGLE LINE DIAGRAM OF THE PROPOSED TRACTION POWER SYSTEM.
2. 13.8 KV CIRCUIT BREAKERS FOR UNIT SUBSTATIONS AND PASSENGER STATION SUBSTATIONS ARE NOT SHOWN.

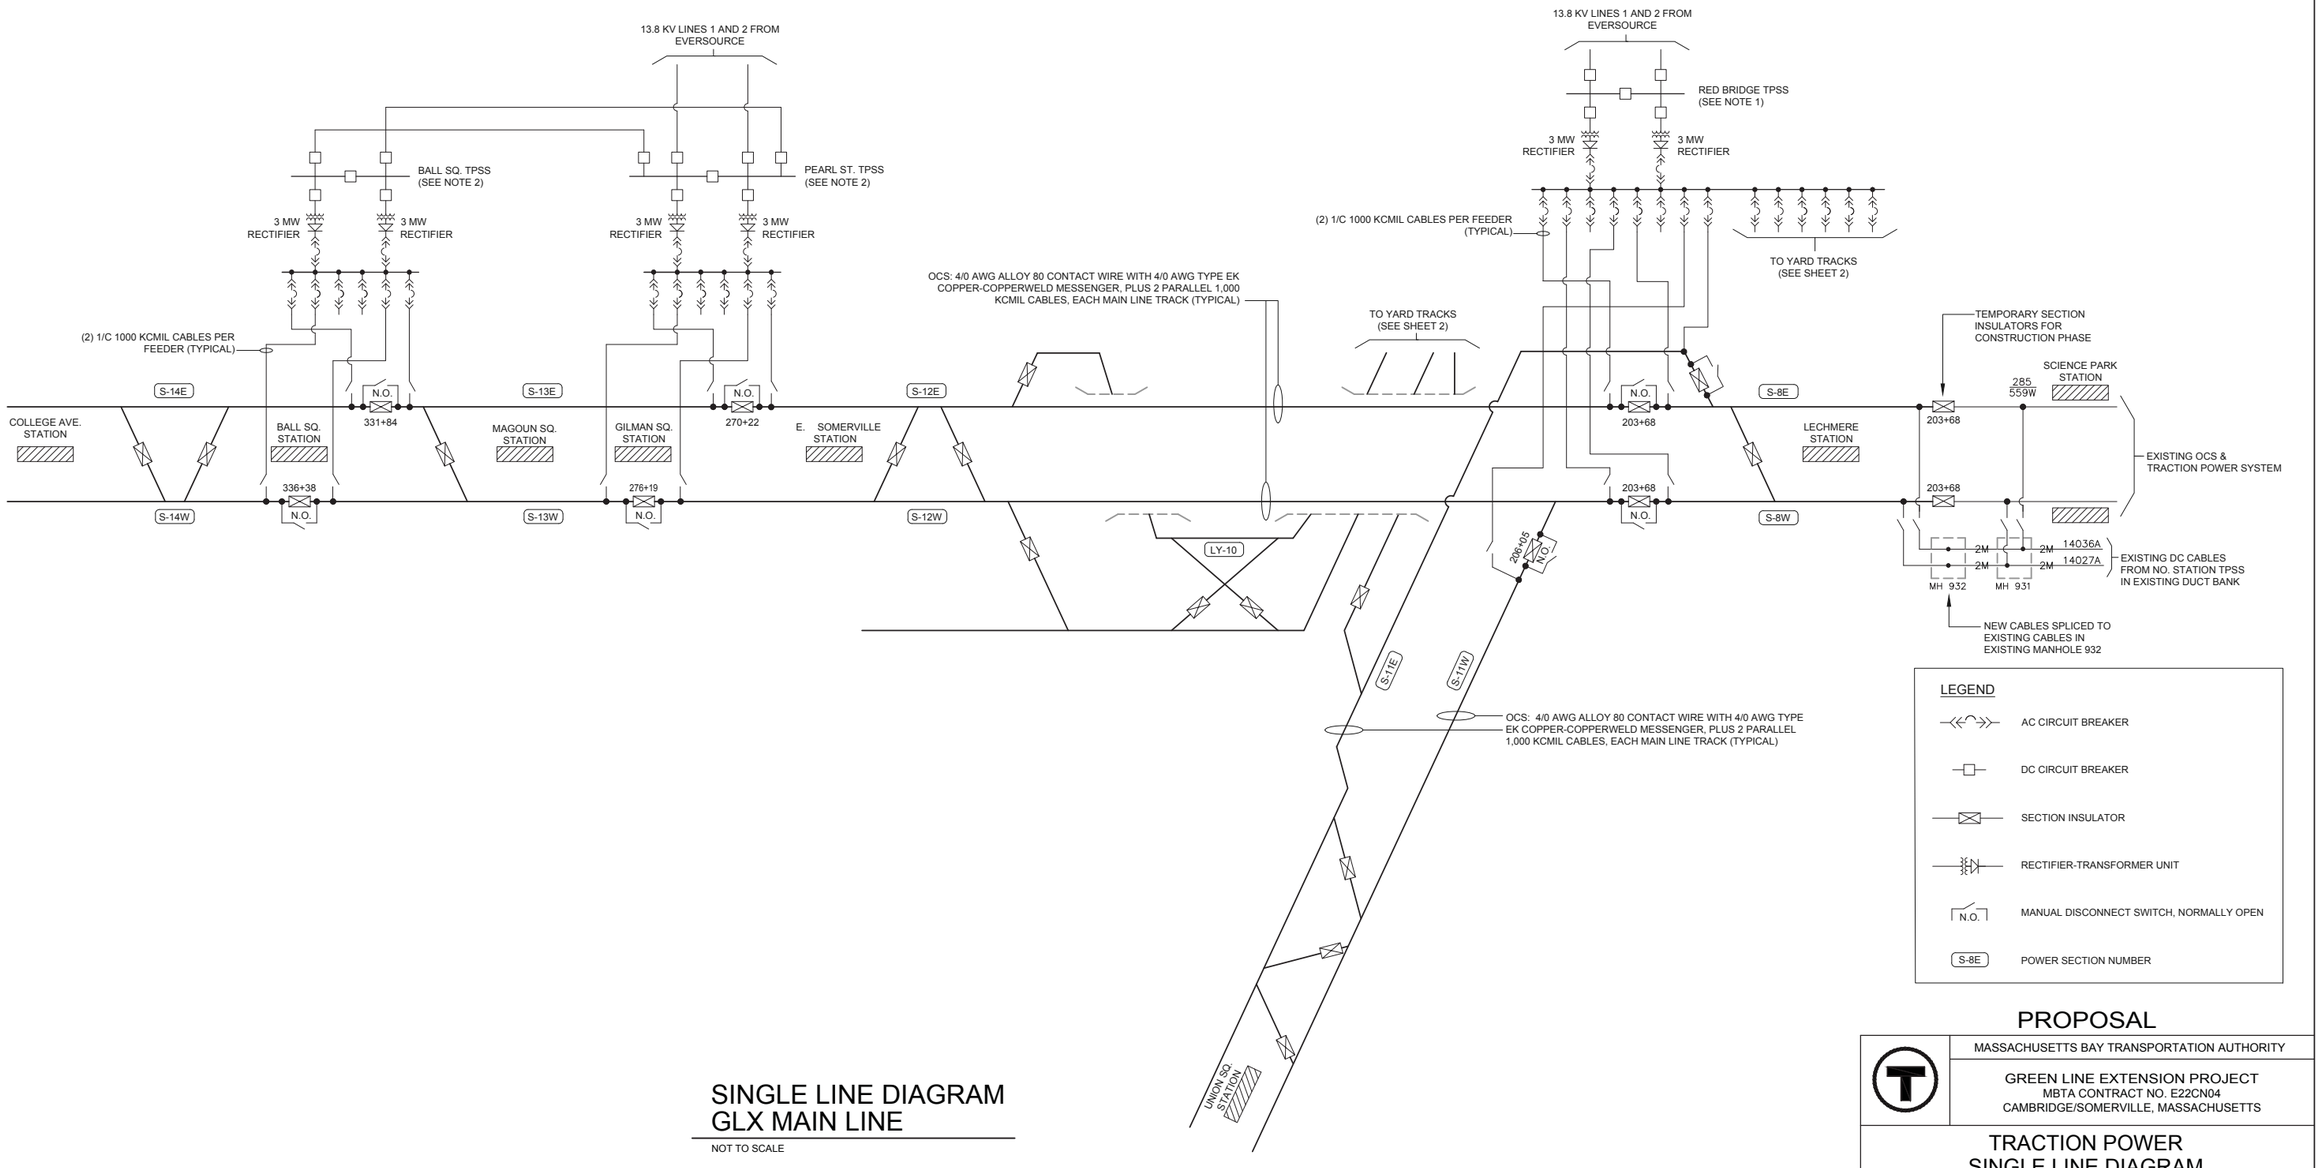

LEGEND

- AC CIRCUIT BREAKER
- DC CIRCUIT BREAKER
- SECTION INSULATOR
- RECTIFIER-TRANSFORMER UNIT
- N.O. MANUAL DISCONNECT SWITCH, NORMALLY OPEN
- S-8E POWER SECTION NUMBER

SINGLE LINE DIAGRAM
GLX MAIN LINE

NOT TO SCALE

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

TRACTION POWER
SINGLE LINE DIAGRAM
GLX MAIN LINE

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-271.pdf

SCALE: NTS	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	JAW	RWBS	RWBS	SHEET: SYS-004	


PLOTTED: 09/15/17 2:54PM BY:KINGAK
DRAWING: L:\PROPOSALS\GLX\SYSTEMS\PROPOSAL READY DRAWINGS\TPSS\SYS-007 TP-SLD-MAIN LINE_REV.DWG [SYS-007] 09/11/17 12:09PM

NOTES:

1. THIS DRAWING IS A CONCEPTUAL AND SIMPLIFIED SINGLE LINE DIAGRAM OF THE PROPOSED TRACTION POWER SYSTEM FOR THE YARD AND VMF.
2. LOCATIONS FOR FEEDER CABLE RISERS AND CONTACT WIRE JUMPERS ARE TO BE DETERMINED.
3. THE YARD AND YARD LEAD OVERHEAD CONTACT SYSTEM IS COMPRISED OF A SINGLE 4/0 AWG ALLOY 80 CONTACT WIRE.
4. THE FOUR TRACKS IN THE VMF WILL BE GROUNDED AND ISOLATED FROM THE YARD TRACKS WITH INSULATED RAIL JOINTS. A SEPARATE NEGATIVE RETURN CABLE WILL CONNECT THE FOUR VMF TRACKS TO THE RED BRIDGE TPSS NEGATIVE BUS.

LEGEND

- SECTION INSULATOR
- C — CONTACTOR
- N.O. — MANUAL DISCONNECT SWITCH, NORMALLY OPEN
- LY-1 — POWER SECTION NUMBER

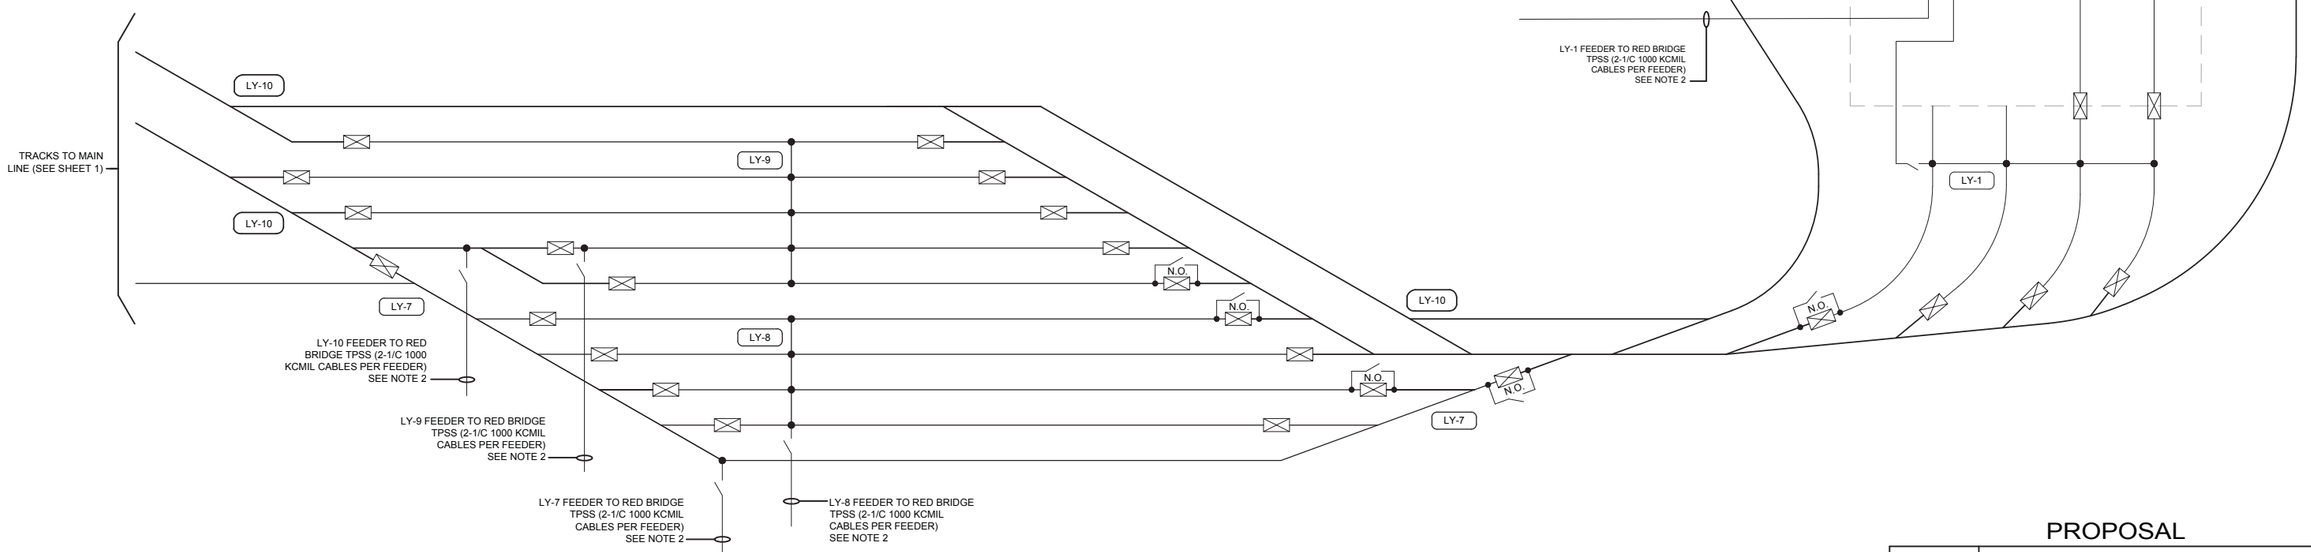

SINGLE LINE DIAGRAM
GLX YARD

NOT TO SCALE

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

TRACTION POWER
SINGLE LINE DIAGRAM
GLX YARD

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-271.pdf

SCALE: NTS	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	JAW	RWBS	RWBS	SHEET: SYS-005	

PLOTTED: 09/15/17 2:57PM BY:KHNGWK
DRAWING: I:\PROPOSALS\GLX\SYSTEMS\PROPOSAL READY DRAWINGS\TPSS\SYS-008 TP-SLD-YARD_REV1.DWG [SYS-008] 09/11/17 12:13PM

ENGINEERING AND MAINTENANCE

LAPTOP PC

CENTRAL CONTROLLER CABINET

POWER

NET

120 VAC

CAT6

HMI DISPLAY

KEYBOARD/ MOUSE

INDUSTRIAL PC

CAT6

FACILITY I/O

- UNIT SUBSTATION
- FIRE ALARM CONTROL PANEL
- ENTRY DOORS
- BATTERY CHARGER
- ETC.

LEGEND:

- SERIAL (RS-485) COMMS
- CAT6 (ETHERNET)
- DUPLEX MM FIBER OPTIC
- 6-FIBER OPTIC

SUBSTATION PRIMARY PLC "A"

CAT6

MAIN COMMS CABINET

SINGLE MODE FIBER OPTIC CONNECTION TO MBTA (SEE NOTE 3)

NOTE 1

SUBSTATION SECONDARY PLC "B"

CAT6

CAT6

CAT6

CAT6 10/100 BASE-TX MODBUS TCP PROTOCOL

ETHERNET SWITCH LAN-A

DUPLEX MM FO

FPP-A

CAT6 10/100 BASE-TX MODBUS TCP PROTOCOL

ETHERNET SWITCH LAN-B

DUPLEX MM FO

FPP-B

TWO 6-FIBER MM FO CABLE

FPP

DUPLEX MM FO

COMM HUB DUAL FO PORTS

CAT6

DIO / IED

STATUS

TRANSFORMER T1

TRANSFORMER T2

NOTE 5

CIRCUIT BREAKER MFPR 1 ... N

CIRCUIT BREAKER I/O (INCLUDING ANALOGS)

RS-485

AC SWITCHGEAR SEE NOTE 6

REMOTE METER DISPLAY

RS-485

ANALOG IN

AC CONTROL PANEL

DC SWITCHGEAR

CAT6 (TYP.)

NOTE 2

CAT6 (TYP.)

FEEDER BREAKER MFPR 1...N

FEEDER BREAKER I/O (INCLUDING ANALOGS)

72-R1 MFPR

72-R1&R2 I/O (INCLUDING ANALOGS)

SUBSTATION BATTERY SYSTEM

NOTE 4

BATTERY MONITOR

INPUTS / OUTPUTS

RECTIFIER #1

ANALOGS

NEGATIVE BOARD

INPUTS / OUTPUTS

RECTIFIER #2

NOTES:

1. PLC IS A "HOT" STANBY.
2. THE NUMBER OF COMMS HUBS WILL VARY DEPENDING ON SWITCHBOARD SIZE.
3. THE SAS MUST BE CAPABLE OF COMMUNICATING IN VALMET SERIES 5 PROTOCOL WITH THE MASTER SCADA STATION AT HIGH STREET

SUBSTATION AUTOMATION SYSTEM BLOCK DIAGRAM SHOWING MAJOR COMPONENTS

NOT TO SCALE

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

SUBSTATION AUTOMATION SYSTEM (SAS) SYSTEM BLOCK DIAGRAM

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


GV20170258-271.pdf


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: NTS | DRAWN BY: JAW | DESIGN BY: RWBS | CHECK BY: RWBS | PLAN NO. | ISSUE

DATE: SEPT. 28, 2017 | SHEET: SYS-006

PLOTTED: 09/15/17 2:58PM BY:KNGMK
DRAWING: I:\PROPOSALS\GLX\SYSTEMS\PROPOSAL READY DRAWINGS\IPSS\SYS-009.DWG [SYS-009] 09/11/17 2:59PM

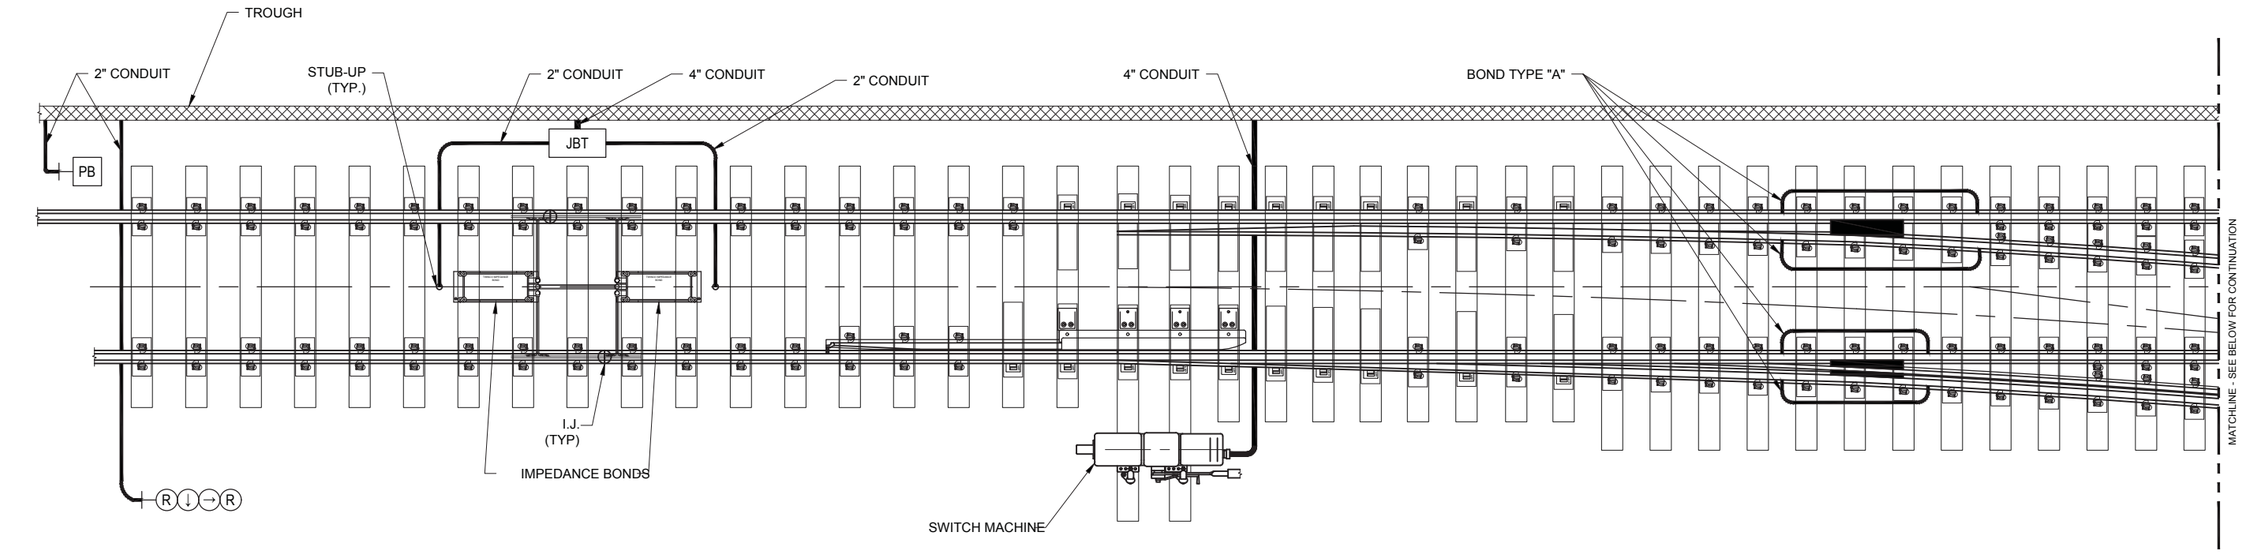

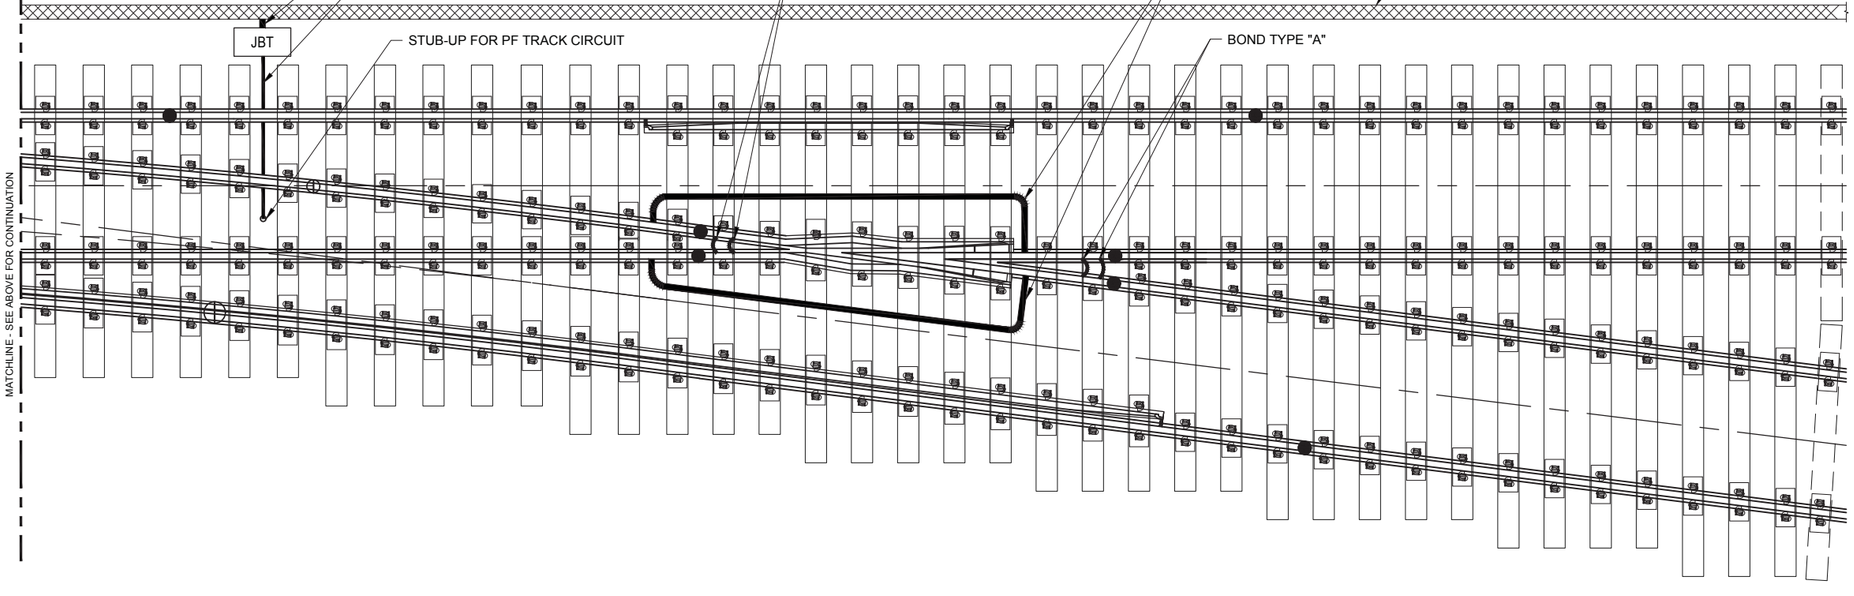

NOTES:

1. PROVIDE HMA UNDERLAYMENT IN ACCORDANCE WITH MBTA RAILROAD OPERATIONS STANDARD DWG NO. 1030.
2. MANUFACTURER SHALL SUPPLY FLANGE BEARING FROG.
3. TURNOUT SHALL BE FULLY GUARDED.
4. GUARD RAIL GAPS ARE REQUIRED AT SPECIAL TRACKWORK.
   4.1. SEE TRACK DETAIL SHEETS FOR FURTHER INFORMATION.

LEGEND

- INDICATES RAILS FURNISHED BY THE MANUFACTURER
- INDICATES RAIL FURNISHED BY THE INSTALLER
- INDICATES INSULATED JOINTS WITH 3/16" OPENING
- INDICATES JOINTS TO BE FIELD WELDED
- INDICATES JOINTS TO BE BOLTED
- AB INDICATES RAIL BRACE LOCATIONS
- A (2) 250 KCMIL RAIL JOINT BONDS
- B (1) 500 KCMIL RAIL JOINT BONDS

SPECIAL TRACKWORK EQUIPMENT LOCATION LAYOUT

1/2"=1'-0" 0 1' 2' 4'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

SPECIAL TRACKWORK
EQUIPMENT LOCATION LAYOUT

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-271.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	LYR	JCT	RAM	SHEET: SYS-007	

PLOTTED: 09/15/17 3:37PM BY:KINGAK
DRAWING: I:\PROPOSALS\GLX\SYSTEMS\PROPOSAL READY DRAWINGS\TRACKWORK\SYS-GL-8012.DWG [SYS-GL-8012] 09/11/17 10:00AM

4.2 ELEVATED GUIDEWAY AND STRUCTURES ALONG THE GUIDEWAY

The proposed solutions for the retaining walls, viaducts, and bridges are based on proven structural systems, which will be designed and built to MBTA and MassDOT Standards. GLX Constructors will deliver reliable structural solutions that meet service life expectations, and economical maintenance costs.

4.2.A STRUCTURES ALONG THE GUIDEWAY

The Lechmere, Medford Branch, and Union Square elevated guideway includes approximately one mile of elevated structure. Other structures along the guideway include bridges, stations, retaining walls, noise walls, and in localized areas an elevated Community Path. This section describes our design and construction approach for these structures.

Viaduct. The elevated guideway will consist of approximately 4,300 feet of viaduct structure and 1,600 feet of earthen embankment supported by Mechanically Stabilized Earth (MSE) retaining walls. The use of MSE walls was approved by the MBTA as part of GLX Constructors (ATC 35). ATC 35 is a significant reduction in long-term maintenance cost for the MBTA. The locations of the MSE supported earthen embankment portions of the elevated guideway are shown on Figure 4.2-1.

The Viaduct structure will match the alignment of the Project Definition Plans, with one exception. GLX Constructors team has identified a recently completed structure within the Northpoint development at approximately STA MB-EB 197+00 that extends into the MBTA permanent easement and conflicts with the viaduct structure, based on the track alignment shown on the Project Definition Plans. We have modified the track alignment extending north from Lechmere Station through STA 197. Based on the information provided by the MBTA, we believe that we have now resolved this bump out conflict, while keeping the viaduct within the MBTA ROW, and meeting all other design criteria.

The proposed Viaduct profile will be adjusted to provide specified vertical clearances while minimizing rail elevation above existing grade. Reduction in rail elevation on the viaduct reduces viaduct height, the over weight of the viaduct structure, results in smaller foundations.

The Medford Branch profile will be lowered by up to 6 feet between STA 186+00 and STA 207+00. This profile change will provide the required track grades and clearances for both a viaduct structure and for MSE wall supported earthen embankment. The proposed Medford Profile revision does not impact the viaduct structures already built in the advanced contract.

Details of the profile lowering include:

1. The maximum profile lowering of 6.5 feet is at STA 198+25 (north of Water Street).

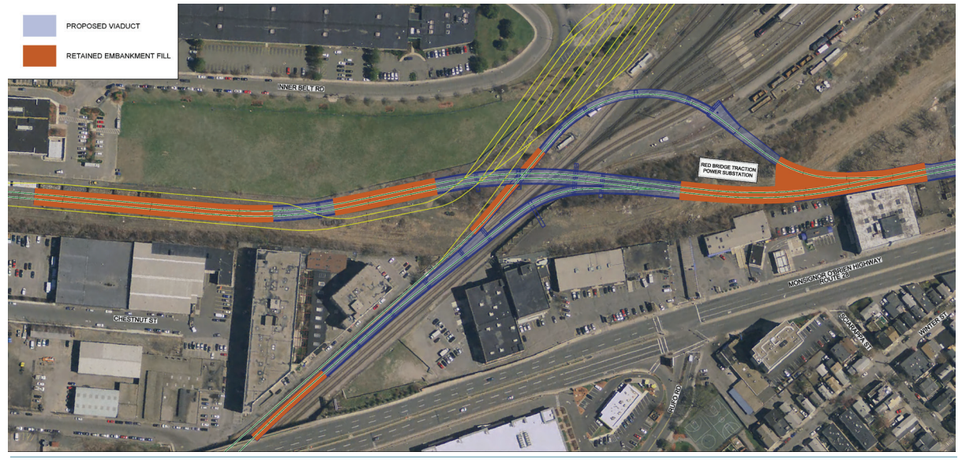


Figure 4.2-1. Locations of MSE supported elevated guideway structure. *MSE supported elevated guideway approved as part of ATC 35reduces risk associated with construction of deep foundation elements and reduces MBTA long-term maintenance costs.*

2. Revised profile over Water Street meets the minimum 16.5 feet Vertical Clearances per Technical Provision 8.7.3.9.

3. Profile over Bus Turn-Around exceeds the minimum 12.5 feet Vertical Clearances per Technical Provision 7.2.3.6.

4. Revised Medford Profile grade does not exceed 2.00%, maximum grade in Technical Provisions 10.2.3.2(d)(ii) for special trackwork.

The profile through the Lechmere Station will be lowered by a maximum of 2 feet at the north end, allowing for a slight reduction in the size of the Lechmere Station. The profile grade through the station is lower than the maximum per the Technical Provision 10.2.3.2(d)(ii) for Station Platforms.

The Union Square Branch east-bound profile was also lowered from STA 0+00 to STA 6+90 to match the revised Medford profile. The Union Square Branch west-bound profile was not lowered.

The Medford Branch Profile may be lowered further in the East Street area by about 4 feet if the MBTA agrees a lowering of the reinstalled historic Lechmere Viaduct. This would allow for substantial to efficiencies at the Lechmere Station.

Track Bed. Ballasted track will be used on the viaduct and will reduce loads generated by expansion/contraction of the continuous welded rail. Ballasted track allows for simpler superstructure deck joints at the termination of each span and acts to reduce dynamic impact on the superstructure system, which provides a better ride for passengers. Ballasted track represents a benefit for the MBTA as track maintenance can be performed with standard equipment.

Steel beams supporting a cast-in-place concrete deck will form the superstructure system. Steel has been selected over concrete because of weight

considerations, ease of erection, and the availability of the steel plate, which had been previously purchased. Steel plate girders, have been selected over tub girders, due to lower fabrication and detailing cost.

Viaduct Structure. We have reviewed the available steel that is now located at the High Steel and Casco Bay Fabrication Plants, as well as the list of available plate sizes and thicknesses. GLX Constructors has performed an independent design verification of the plans produced for the viaduct under the previous Contract, for both the superstructures and substructures. The steel that is available is suitable for reuse using the viaduct pier spacing proposed in the previous contract, with one exception on the Union Square Westbound Viaduct, one span has deflections under live load which were found to exceed allowable, and which will require a slight increase in girder stiffness.

We have identified the following improvements to the previous contract:

- Use of steel plate girders to replace tub girders.
- Elimination of counterweights on single tub girder spans.
- Our design replaces the counterweight/single tub superstructure approach with a three I-Girder system.
- End diaphragm configuration have been reworked to produce a simpler and less fatigue prone system, that we will be simpler to inspect
- Reworking of the proposed deck reinforcing to a more efficient configuration that will also accommodate proper placement and consolidation of deck concrete.
- Reconfiguration of Piers 7 through 11 to eliminate the arch in the underside of the pile cap. The underside arch generates problematic reinforcing bar detailing.
- Use of 30-inch diameter pipe piles instead of drilled shafts to address the uncertainty in determining the depth of rock sockets needed for drilled shafts.
- The use of earthen embankments supported by MSE walls to replace portions of the elevated viaduct structure that reduce long-term maintenance costs and
  risks associated with the installation of deep foundations in highly variable ground conditions.

The design will be performed in accordance with MBTA Guide Specification for Structural Design of Rapid Transit and Light Rail Structures, dated 2005. To address seismic loading, a Multimode Spectral Analysis will be performed in conformance with the AASHTO Code. The multimode analysis is appropriate given the length of the structure, and the variation in pier heights.

Viaduct Foundations. Foundations for the Viaduct will consist of drilled shafts, driven piles and drilled micropiles that will support vertical and lateral loads.

Drilled micropiles will be used to support Piers 1 through 7. The micropiles will be installed below the existing viaduct structure prior to demolition of the existing viaduct so that rail operations can remain active as long as possible. We also propose to utilize micropiles having a higher capacity than those shown on the drawings from the previous contract to reduce the required number of piles at these seven piers. The micropiles are designed to derive their support entirely in bedrock. These seven spans will be broken into their own Design Package. A dedicated Design Package will facilitate completing both the design and construction of the remaining Lechmere Viaduct north of these seven spans prior to commencing demolition activities. These seven replacement spans will be designed and constructed in a manner that will minimize track outage time.

Driven, 30-inch diameter, open ended pipe piles with a wall thickness of 1.25 inches will be used to support Piers 8 through 20. Piles will be designed to have a nominal axial resistance of approximately 600 kips for the Lechmere Branch Viaduct and about 800 kips for the Medford Branch Viaduct. A 1/8-inch allowance for corrosion will be provided both the inside and outside of the piles, as required by the Technical Provisions. A driving shoe will be installed on every drive pile. Aside from the favorable ground conditions, there are essentially three advantages of using piles instead of drilled shafts:

1. Every pile will be driven to a specified driving resistance, and at least two piles in each pier will be dynamically tested using a pile driving analyzer (PDA). Therefore, there will be a higher degree of quality control for a pile foundation compared to drilled shafts, where there will only be a limited number of load tests.
2. Potentially contaminated soil must be removed for drilled shafts. At Pier 18, contaminated soil and groundwater was encountered at a depth of about 65 feet. As a mitigation measure, the design shown on the GMP drawings included the installation of a costly, permanent steel casing at drilled shafts in this location.
3. Piles can be installed more quickly that drilled shafts.

Pending the results of our supplemental explorations, shallow foundations may be used as an alternative to piles at Piers 14 through 17, where the available subsurface information indicates that the thickness of "unsuitable" bearing material in this area is expected to be less than about 10 feet. The use of spread footings at the adjacent 22 Water Street development supports the likelihood of using spread footings in this area. The new Viaduct footings will extend to a depth of about 10 feet below existing grade to avoid imposing lateral pressures on the 22 Water Street foundation wall that extends about 10 below grade.

The remaining piers of the elevated viaduct will be supported on drilled shafts, primarily because the shafts are within the zone of influence of existing active tracks. Drilled shafts have already been installed at Piers 26 and 27 by the previous contractor as shown in Figure 4.2-2. We will review the installation records for these shafts and evaluate whether they are adequate to support the required design loads.



Figure 4.2-2. Installation of Drilled Shafts near Pier 26. *Drilled shafts will be used to support portions of the guideway viaduct to mitigate the impact adjacent railroad tracks.*

In addition to dynamic testing of driven piles, one static load test will be performed for the micropiles and one biaxial load test will be performed on a non-production drilled shaft.

There are five section of the elevated guideway that will be supported on earthen embankments with MSE walls. The maximum wall height will be about 30 feet, and the height will not exceed the width of the retained earth embankment, as a condition of the ATC 35 approval by the MBTA. Figure 4.2-3 depicts the construction of a typical MSE support embankment fill.

In all but one of the five areas where earthen embankments are proposed, the existing ground conditions are suitable to support the weight of the embankment fill without long-term settlement impacts (see Figure 4.2-5). The subsurface conditions along the Medford Branch embankment between Piers 20 and 26 include a thick fill layer and compressible organic and clay soils that will compress under the weight of the embankment fill. Ground improvement will be performed to provide suitable bearing for the embankment, and mitigate settlement. Ground improvement will consist of deep soil mix columns, as shown on Figure 4.2-5, that extend through the compressible organic and clay soils. The deep mixing will transfer the weight of the embankment to the underlying incompressible glacial till stratum. The weight of the embankment fill between deep mixing units will be transferred to the improved ground using biaxial, geogrid reinforcement placed within the bottom section of the wall.



Figure 4.2-3. Schematic Cross Section of Proposed Track Supported by MSE Walls (ATC 35). *ATC 35 provides a structure that will require less maintenance than a viaduct structure.*

Each deep mixing unit will consist of four contiguous, 5-foot diameter columns spaced at 3 ½ feet, and have an unconfined compressive strength of about 250psi. Cement will either be mixed with the existing soil, in-place as the auger is advanced or as it is being withdrawn.

Foundations at the interface of MSE walls and viaduct portions of the elevated guideway will consist of deep foundations or shallow foundation with cast in place columns that extend through the embankment fill. Viaduct foundations will not bear on the MSE embankments. See Figure 4.2-6.

Elevated Community Path. The Community Path rises from the track level heading south to meet and cross the School Street Bridge. With the approval of our ATC 36, the path will connect with the Medford Street and Walnut Street Bridges. Between these bridges we will construct the path on fill retained by new or existing retaining walls wherever practical. Approaching these cross streets, the path rises in elevation to meet the bridges. As the path profile rises to meet these cross roads, the community path will transition on



Figure 4.2-4. Ground Improvement using Deep Mixing Columns. *Deep mixing columns will be installed from existing ground surface and will improve the existing fill, organics and clay soils so that MSE walls can be constructed without long-term settlement concerns.*

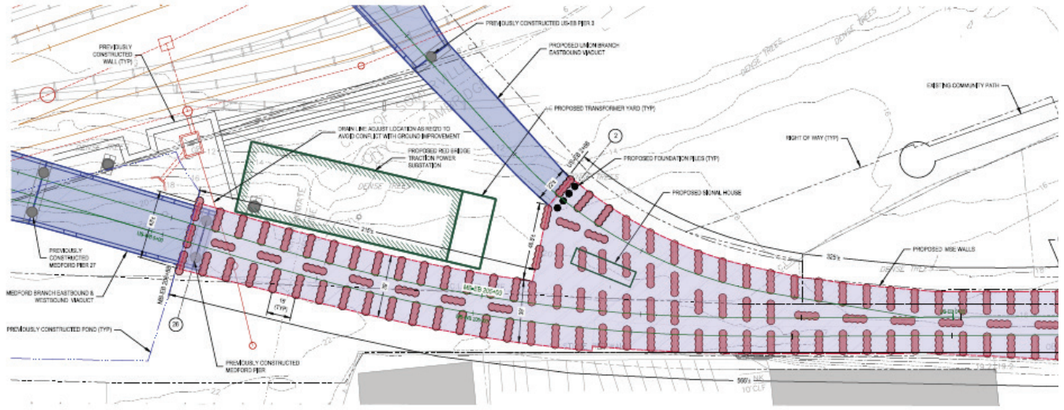


Figure 4.2-5. Proposed Ground Improvement along section of MSE Embankment between Piers 20 and 26.



Figure 4.2-6. Viaduct Foundations at MSE wall interface. *Viaduct foundations will not bear on the MSE embankments.*

to a viaduct structure. We will construct these viaducts with butted prestressed concrete deck beams topped with a concrete wearing surface. Concrete curbs and fencing will be located outside the 12' – 0" wide pathway. Foundations will consist of a single drilled shaft supporting the reinforced concrete pier caps.

Narrative Demonstrating How the Elevated Guideway, Structures Along the Guideway Conform to Requirements

Adding the new Medford Branch (MB) tracks will require widening the existing track bed along several portions of the alignment north of the viaduct structure. To accomplish this, we will construct permanent retaining walls to support the adjacent ground and protect the integrity of the existing buildings and properties. New retaining walls will also be constructed to support the track bed in areas where the adjacent Community Path is depressed. Because of their deterioration, the face of some of the existing crib walls will also be repaired or rehabilitated. In addition to retaining walls, we will replace an existing railroad bridge and lengthen existing vehicular bridges to accommodate the new Green Line tracks and added Community Path.

We have based the type of retaining walls used and the approach to widening the existing bridge structures shown on the Definition and Concept Drawings in the Technical Provisions on site-specific ground conditions, geometry, maintenance, protection of existing structures, and other restraints, such as ROW restrictions and maintenance of railroad operations during construction. The majority of the new retaining walls involve the use of precast concrete elements, which will accelerate wall construction and eliminate the need for special measures associated with cast in place concrete placement in cold or inclement weather.

We will primarily use five types of retaining walls:

1. We will use **modular precast gravity walls** where the retained height is less than approximately 10 feet as shown in Figure 4.2-7. The use of precast elements for these relatively low height walls will shorten the construction schedule. Existing granite block walls may be used, in lieu of precast modular walls for wall heights up to about 4 feet, which match the existing historical granite blocks on the ROW.

2. We will use **drilled in cantilever soldier pile and precast concrete lagging walls** where the height of retained soil is greater than about 10 feet and the ROW restrictions prevent open cut excavations, or where limiting ground movements are required to protect adjacent structures. When there is a sufficient distance between the wall and the ROW, tiebacks may be used to reduce the size of the soldier pile, depth of embedment, and horizontal deflection at the top of the wall. See example in Figure 4.2-8.

3. **Soil nail walls with permanent shotcrete facing** will be used for excavations greater than approximately 10 feet, where soil nails can be installed within the Project's ROW.



Figure 4.2-7. Precast Modular Black Walls. *Modular walls will accelerate wall construction.*

Soil nail walls with permanent shotcrete facing will also be used to rehabilitate the two sections of deteriorated crib walls between McGrath Highway and Central Street. The results of nondestructive testing performed by NDT Corporation in their report dated December 2016 indicates that nearly one half of the transverse structural elements of the two wall sections are deteriorated. Therefore, we will construct a new wall system that not only provides a new facing, but is designed to support all the earth pressure without any contribution of the existing crib wall. See example in Figure 4.2-9.

4. We will use **cast in place reinforced concrete cantilever walls** in place of gravity walls to support new track embankments, at locations where MSE walls are not practical.

5. **Mechanically Stabilized Earth** (MSE) walls will be used around the perimeter of the Vehicle Maintenance Facility and Yard, and for support of the elevated guideways shown in Figure 4.2-10. Horizontal, non-biodegradable, reinforcing geogrid or galvanized steel reinforcing strips will be installed at 12 to 18-inch intervals as the backfill behind the precast concrete walls panels is placed.

Design Criteria and References to the Applicable Standards.

We will design all new retaining walls and noise barriers for a 75-year design life. The new structural elements of retaining walls to be rehabilitated will be designed for a 25-year design life. For the 'rehabilitation' of the existing wall between the McGrath Highway and Central Street, GLX Constructors is providing a new wall system that will exceed the required 25-year design life.

All new retaining walls will be designed to conform with the current American Association of State Highway and Transportation Officials (AASHTO) Load and Resistance Factor Design (LRFD) Code for geotechnical stability and structural component design.

All noise barriers will be designed to conform with the current AASHTO LRFD Code for geotechnical stability and the AASHTO Standard Specifications for Highway Bridges 17th Edition 2002 with latest interims using Load Factor Design (LFD) for concrete design and Allowable Stress Design (ASD) for steel design.

When loading conditions are not defined in AASHTO, such as building surcharge and commuter/freight rail the Massachusetts State Building Code and the American Railway Engineering and Maintenance-of-Way Association will be used, respectively.



Figure 4.2-8. Soldier Pile and Precast Concrete Lagging Wall Construction. *Use where open-cut excavation is precluded and to limit ground movement adjacent to existing structures.*



Figure 4.2-9. Permanent Soil Nail Wall. *Soil nails provide an efficient structural solution where ROW is available.*



Figure 4.2-10. Approximate Limits of MSE Retaining Walls at the Vehicle Maintenance Facility. *MSE walls around the VMF facility allow for the site grade to be raised out of the flood plain and to maximize the use of available space for train storage.*

Design or Specification Measures to Meet Serviceability Criteria.

Measures that are incorporated in our design to enhance the design life of retaining structures and noise walls are detailed below.

- GLX Constructors will provide proper drainage behind all new soldier pile and precast lagging walls and soil nail retaining walls to prevent the buildup of water pressure that could impact the life of the walls or result in maintenance issues. Free draining backfill will be used behind cast-in-place, modular precast concrete block walls and MSE walls to provide proper drainage.

  Drainage behind the walls also prevents water seepage between precast panels or modular wall sections that could cause deterioration and/or discoloring of the concrete. In winter conditions, the seepage would result in the formation of ice on the wall that would be a safety concern for railroad maintenance workers. See example in Figure 4.2-11.

- We will provide a drainage swale, based on ground topography, along the top of soldier pile and soil nail walls for runoff from the back face of the walls.

- GLX Constructors will use precast elements where possible. These elements are fabricated under conditions that are not impacted by the harsh New England weather, and will be of higher quality than cast in place concrete.

- We will use hot dipped galvanized steel for permanent soldier pile and precast lagging systems. Steel angles attached to the pile sections will be attached prior to galvanizing to provide greater protection against corrosion.

- Neoprene rubber pads between precast concrete panels will be used for soldier pile and lagging walls to avoid damage to the precast panels due to overstressing associated with stress concentrations.

- GLX Constructors will use either hardwood lagging or shotcrete (at bridges and other critical areas) as temporary support at soldier pile and precast concrete lagging retaining walls. This will allow the excavation to be completed before installing the permanent precast panels and improve the aesthetics of the walls by allowing better alignment of the panels along the wall. The shotcrete will also allow panels to be replaced between any two adjacent soldier piles without any additional support if they are damaged during the life of the wall. Timber lagging will deteriorate over time, and will not provide the support needed to allow temporary removal of precast panels. Also, the deterioration of the timber lagging will result in ground movements behind the retaining wall that could cause distress to abutting structures. Therefore, we will only use timber lagging in non-critical areas.

- Shotcrete or timber lagging as temporary support for soldier pile and precast lagging walls will be installed using "clips" attached to the soldier pile between the flanges (see Figures 4.2-12 and 4.2-13) rather than using the back flange of the pile. This will require less excavation behind the face of the soldier pile, which will reduce the potential of ground movement behind the wall. Given the depth of the soldier piles that will be used for the higher walls, the reduction in the amount of excavation also accelerates construction.

- Individual segments of Precast modular walls can be easily replaced if damaged.

- Soldier piles will be installed so that the top of the pile is installed out of plumb by the amount of movement that is expected during excavation (after the pile is installed). This will provide a finish wall that is essentially vertical and will not



Light rail track supported by Mechanically Stabilized Earth (MSE) walls. ***GLX Constructors' team members, Balfour Beatty and STV, incorporated the use of low maintenance MSE walls on the Charlotte LYNX Blue Line Light Rail Project in North Carolina.***



Figure 4.2-11. Installation of Drainage Board behind Shotcrete Walls. *Where shotcrete is used, the boards will assure effective drainage behind the completed wall system.*



Figure 4.2-12. Precast concrete panels and drilled soldier piles. *GLX Constructors have experience with designing and installing drilled soldier pile and permanent precast concrete lagging walls using shotcrete as temporary support.*




Figure 4.2-13. Preferred method of temporary lagging installation. *Installing lagging between the soldier piles will reduce the potential of ground movement behind the wall.*



Figure 4.2-14. Drilling Soldier Pile and Permanent Precast Concrete Lagging wall. *Used for wall heights up to 28 feet without impacting adjacent structures.*

have the appearance of tilting that may concern railroad operations or property abutters. Our team has used this approach successfully on this type of wall that was used to retain soil up to 28 feet in height, as shown in Figure 4.2-14. Also, piles will be installed by drilling, rather than driving, to maintain verticality and alignment.

- Coating of noise barrier panels with a penetrating concrete sealer to provide protection from freeze-thaw cycles.
- Limiting noise barrier deflection to 1% of the height of the noise barrier, which is well within the amount the segmental precast concrete panels can tolerate.
- Designing soldier piles structurally to limit wall deflection, rather than to maximizing the structural capacity of the steel section used. This will reduce the risk of potential impacts to adjacent structures.
- Enhancing the overall longevity and durability of the retaining walls and noise barriers by maintaining minimum cover requirements for all reinforcing steel.

Drainage and Waterproofing System for Structures, Type, and Application. All new retaining walls will be designed to be free draining. A drainage board will be installed between the shotcrete and the soil face to provide drainage behind the soldier pile and precast lagging and soil nail retaining walls. The drainage board will be continuous from the top of wall to the base of the walls, and will drain into a crushed stone collector trench that runs along the length of the wall. The water from the collector trench will discharge into the main drainage system along the trackway. Crushed stone placed between the temporary shotcrete used between soldier piles and the precast concrete panels will also facilitate drainage. A drainage swale will also be provided along the top of the wall to divert surface runoff from the retaining walls. Free draining backfill will be used behind cast in place walls and modular precast walls or block walls.

Confirmation that all Structures can be Constructed within the ROW. GLX Constructors will work within the available ROW and easements in the layout and construction of the retaining walls along the guideway. However, the soil nails for retaining wall MW-10 near the College Avenue Station will extend a few feet outside of the ROW, as allowed by the MBTA.

Design to Mitigate Frost Heave. Mitigation measures for frost are incorporated into our design to reduce the risk of foundation heave and lateral load increase.

Steel piles used for the soldier pile retaining walls and noise walls will be installed in predrilled holes that extend below the frost depth.

Block and modular precast walls will be founded at least 18 inches below finish grade and are tolerant to heave. Also, a layer of crushed stone or other non-frost susceptible material will be provided below the gravity walls and below the precast panels used for the soldier pile and lagging walls and noise walls for drainage purposes. Furthermore, precast panels used for the soldier pile and lagging walls are very tolerant to movements. Therefore, vertical frost heave will not be an issue.

In terms of the potential for increased lateral load due to frost, drainage will be provided behind all new retaining walls, including soil nail walls. Our experience with these wall types in similar ground conditions throughout New England indicates that drainage behind the wall is sufficient to mitigate frost impacts.

Structural Drawings of the Elevated Guideway, Structures Along the Guideway

Structural drawings at the end of this section and indicate the retaining and noise wall types proposed for this project. Included in the drawings are section and elevation views and pertinent details to illustrate that the requirements of the Technical Provisions have been met.

4.2.B BRIDGE AND UNDERPASS STRUCTURES

General Approach to Bridge and Underpass Structures

Replacement bridges or modified portions of existing bridges will be designed for a 75-year service life. The Rail Bridge at Washington Street will be designed in conformance with the AREMA Manual for Railway Engineering and the MBTA Guide Specifications for Structural Design of Rapid Transit and Light Rail Structures. The Cooper E-80 plus diesel loading will be the design load for portions of the bridge supporting the commuter rail and maintenance tracks. Design loading for portions of the bridge supporting the Green Line tracks will be in accordance with MBTA Guide Specifications for Structural Design of Rapid Transit and Light Rail Structures.

Roadway bridges will be designed in accordance with the latest edition of the AASHTO LRFD Bridge Design Specifications and the latest edition of the MassDOT LRFD Bridge Manual. The HL-93 truck will be the design loading for replacement bridges or modified portions of existing bridges.

Approach to Modifying Existing Bridges and Constructing New Underpasses. Adding new Green Line tracks and a Community Path will require widening the existing track bed along many sections of the alignment north of the viaduct structure. To accomplish this, we will modify or reconstruct a dozen bridges within the corridor as shown in Figure 4.2-15. Site-specific ground conditions, geometry, constructability, maintenance, protection of existing structures, ROW restrictions, utilities, and maintenance of railroad and roadway operations during construction are all considered in development of our bridge plans.

For bridges to be modified (Lowell Street, Cedar Street, and College Avenue), we will retain as much of the original structure as is feasible. By doing this, we limit construction impacts to existing commuter rail operations and roadway users, while providing the MBTA with cost effective solutions.

As an example, the horizontal clearance between the train envelope and the existing abutment at Cedar Street Bridge is approximately two feet less than required to maintain a safe working distance. Therefore, in lieu of replacing the entire structure with a longer bridge, safety niches will be constructed into the existing abutment, thereby providing safe refuge areas for personnel working near the tracks. One of the wing walls will be reconstructed two feet further from the tracks for the same clearance reason. This work occurs away from the active tracks, does not impact roadway users and retains almost the entire bridge, which was constructed in 1999 and appears to be in relatively good condition.

	Year Built	Proposed Work	Rail Impacts	Roadway Impacts
Lowell Street	2006	Modify Abutment, Install Soil Nails for Lateral Loads	Minor	None
Cedar Street	1999	Install Safety Niches, Relocate One Wing Wall	Minor	None
College Avenue	1996	Remove Bridge Sidewalk, Widen Roadway, Construct Adjacent Pedestrian Bridge	Short Term During Bridge Installation	Minor

Figure 4.2-15. Overhead Structures to be retained and modified. *A summary of the bridges with minor construction activity.*

At the two proposed underpass locations, our approach is to construct a new back span that transforms a single span bridge to a two-span bridge. ATC 36 raises the Community Path to street level at the Walnut Street Bridge and eliminates the requirements for construction of a back span. Through this back span process, we retain one abutment and the existing superstructure, while converting the other existing abutment to a pier that supports the new span.

The benefits of this approach are:

- *no demolition over active tracks;*
- *less disruptive construction activities impacting active tracks; and*
- *better experience for users of the community path and reduced ROW impacts.*

At each of these locations, abutting buildings are close by and the available ROW is limited. For this reason, soldier piles and lagging (SPL) will be used to construct the new abutments. Soldier piles will be installed by drilling, rather than driving, to maintain verticality and limit vibration impacts to adjacent structures. The pile is installed out of plumb by the amount of movement that is expected during excavation (after the pile is installed). Piles will be socketed into bedrock to provide the required bearing and lateral capacities. After setting the soldier piles, the pre-drilled holes will be backfilled up to the finish grade in front of the wall using concrete backfill followed by lean mix or flow fill. Piles will be hot dipped galvanized to provide greater protection against corrosion.

Once the soldier piles are installed and the concrete backfill around the pile has sufficiently cured, the excavation and lagging system will be installed from the top down. Soils will be excavated and shotcrete installed as temporary lagging along the length of the soldier piles using the same technique described in "Design or Specification Measures to Meet Serviceability Criteria" above . When all lifts are complete, a permanent cast-in-place reinforced concrete facing will be attached along the front of the piles. Crushed stone will be placed between the shotcrete and concrete facing and weep holes will be constructed along the base of the permanent concrete façade for drainage. This type of construction was used successfully on the MBTA's Greenbush project.

Upon completing the soldier pile and concrete lagging permanent excavation support system, the abutment bridge seats will be constructed to support the additional span and approach slab. The back span for the School Street Bridge is relatively short and the proposed superstructure is separated-prestressed deck beams composite with a reinforced concrete deck slab. The back span for Medford Street Bridge has a high skew angle and longer span length (approximately 60 feet), and will be constructed using steel stringers composite with a reinforced concrete deck slab.

Proposed Track Structure/Rail Fastening Systems. To eliminate special fastners, we will use a back-span approach in lieu of concrete box culverts for all underpasses, which will eliminate expansion joints below the track bed, as shown in Figure 4.2-16.

GLX Constructors' approach for all overhead structures and underpasses is to use a ballasted track on grade, which is the easiest system to repair and maintain.

Approach to Homogeneous and Uniform Waterproofing System Approach. Over time, many reinforced concrete box culverts begin to leak. This typically occurs from hydrostatic pressures along the expansion and construction joints. Leaks will

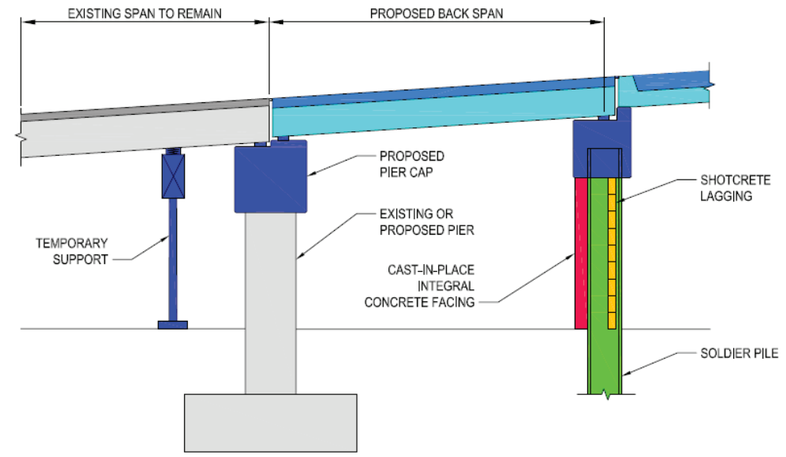


Figure 4.2-16. Proposed Back Span. *Eliminates the need for an underpath structure to improve access and reduce maintenance.*

form where abutting box sections have shifted, and by the eventual breakdown of the joint material or the box waterproofing system. Repairing these leaks is oftentimes both difficult and expensive. By using a new back-span for each of the underpasses, culverts and their associated waterproofing concerns are eliminated.

Reinforced concrete decks for all overhead bridges and overpasses will be protected by either an integral high performance concrete wearing surface or a hot mix asphalt wearing surface and membrane waterproofing that follows MassDOT standards for roadway bridges.

Description of the Site-Specific Approach to Bridge and Underpass Structures

The bridge work required is unique for each structure and varies from full bridge replacement to modest modifications such as frost protection measures or installation of safety niches. As such, our approach to upgrade these structures is also unique and is best described in the subparagraphs that follow.

Replacing the Railroad Bridge over Washington Street. Our approach to replacing the existing Washington Street Bridge entails the removal of the three-span superstructure and the two piers, and construction of a new single span superstructure with new abutments located behind the existing abutments as shown in Figure 4.2-17. The vertical clearance below the bridge will increase to 14' – 6" and coupled with the elimination of two piers, will open up sightlines for pedestrians and motorists. This single span option also eliminates joints in the deck, which are a continuing maintenance concern. The existing bridge will be demolished and reconstructed in two stages, with a minimum of two tracks available to support both the New Hampshire Mainline (NHML) and freight rail operations.

The new span will consist of welded steel thru-girders supporting rolled steel stringers and a metal deck pan. The bridge will support five tracks (1 Freight track, 2 (NHML) Tracks and 2 GLX Tracks) and a separate bay to support the Community Path. Track alignments will be modified from the Definition Plans, by locating the tracks closer together. This track realignment provides a more efficient bridge structure, pulling the community path away from the limited ROW line and improving access to East Somerville Station.

New abutments will be located behind the existing abutments, which will be retained to accelerate construction. Abutment foundations will consist of 4-foot diameter drilled shafts, socketed into the bedrock. A continuous reinforced concrete cap will support the girders and approach slabs. The new drilled shafts will allow for a slightly shorter, more efficient span length.

Construction of a Pedestrian Underpass Behind the Abutment of the Walnut Street Bridge. ATC 36 eliminates the need for construction of a new underpass at the southerly end of the bridge. The Community Path will be raised and cross Walnut Street at street level, thereby providing an additional link between the pathway and local roadway system.

With the exception of potential frost protection measures, OCS protection board installation and modifications to the end posts, and approach guardrail and curbing, no other bridgework will be required. This will have a significant impact to local traffic, as pedestrians and vehicles will no longer be detoured during the construction duration for a new underpass. Another benefit is that disruptions caused by modifications to the large diameter waterline will be eliminated.

Construction of a Track and Pedestrian Underpass Behind the Abutment of Medford Street Bridge. Our approach to modifying the existing Medford Street Bridge retains the existing superstructure, modifies the bridge seat at the south abutment, and the constructs a new back span and abutment (see Figure 4.2-18). A single track of the Green Line (MB-WB) will pass below the new span.

The new span will provide a 5' – 6" sidewalk and a 16' – 6" travel lane in each direction, which will match the existing cross section. The existing 149' – 8 ½" span was constructed in 1983 and is composed of two main longitudinal steel thru-girders with transverse floor beams supporting a reinforced concrete deck and bituminous concrete wearing surface. The bridge was designed for an HS-20 loading and the proposed work will not reduce the current load capacity of the bridge. The new back span will be designed for an HL-93 loading and constructed using longitudinal steel stringers composite with a reinforced concrete deck slab and bituminous concrete wearing surface. Weathering steel will be used, with the ends of the beams either encased in concrete or coated to be consistent with the existing span. Due to the high skew angle, strip seal joints will be used at the interface with the existing span and at the new southerly



Figure 4.2-17. Washington Street Bridge. *Our approach is to replace the existing three-span bridge with a new single span superstructure which will provide better lighting and access for pedestrians.*



Figure 4.2-18. Medford Street Bridge. *Our approach to modifying the existing bridge retains the existing superstructure, modifies the bridge seat, and the constructs a new back span.*

abutment. The span length for the new span is approximately 60 feet between centerline of bearings.

With a limited ROW to the south of the bridge, a soldier pile and lagging system is proposed for the new abutment. The soldier pile and lagging will double as the temporary support of excavation system and then become incorporated into the final foundation structure. After installation of the piles, lagging installation and excavation, a new bridge seat and integral concrete façade will be constructed. This substructure type will keep the construction within the ROW and should minimize construction impacts to nearby structures.

The existing abutment bridge seat and back wall will be removed and rebuilt to support the new span. To do this a temporary shoring system will be installed to support the existing span. Frost protection measures (if needed) will be installed.

The construction of a CP-PL 2 Barrier and Modified Type I Protective Screen is proposed to match the concrete encased thru-girders on the existing span.

Utilities are located on a separate utility bridge just south of the roadway bridge. The utility bridge will be retained, but a support pier and end bent will be removed and replaced in a revised location that provides adequate clearances for the relocated tracks and community path. If needed, the utility support girders will be modified to meet code requirements.



ATC 36 allows relocation of the Community Path from track level to street level at the Medford Street Bridge. In doing this, the proposed underpass span length has been shortened by approximately 24 feet, pulling the proposed abutment further away from the right-of-way and nearby structures. Raising the Community Path allows a reduction in beam size thereby increasing vertical clearance above the track.

Raising the Community Path greatly enhances the user experience, by eliminating a long and narrow tunnel like section below the bridge. The relocated path provides another connection to the local road system, as well as a direct connection to the station.

To implement this ATC, the Community Path will connect with Medford Street just south of the proposed underpass span. The path approaching the bridge from the west will be constructed on fill behind new retaining walls and will have a direct connection to the station. A pedestrian viaduct similar to the proposed Community Path Viaduct at the School Street Bridge will bring the path back down to track level on the easterly side.

Construction of a Pedestrian Underpass Behind the Abutment of the School Street Bridge. Our approach to modifying the existing School Street Bridge entails retention of the existing superstructure, replacement of the south abutment and the construction of a new back span and abutment. A single track of the Green Line (MB-WB) will pass below the new span.

The new span will provide a 6' – 3" sidewalk and a 16' – 0" travel lane in each direction, matching the existing cross section. The existing 73' – 6" span is composed of adjacent prestressed concrete box beams with a concrete deck and integral concrete wearing surface. The bridge was designed for an HS-20 loading and the proposed work will not reduce the current capacity of the bridge. The new back span will be designed for an HL-93 loading and constructed of separated prestressed concrete box beams with a concrete deck and integral concrete wearing surface.

With a limited ROW to the south of the bridge, a soldier pile and lagging system is proposed for the new abutment. The soldier pile and lagging will double as the temporary support of excavation system and then become incorporated into the final foundation structure. After installation of the piles, lagging and excavation, a new bridge seat and integral concrete façade will be constructed. This substructure type will keep the construction within the ROW and should minimize/eliminate any construction impacts to several nearby structures.

The existing granite abutment will be removed and replaced with a reinforced concrete pier (columns and pier cap) supported on a reinforced concrete spread footing. To construct the pier, a temporary shoring system will be installed to support the existing span.

The construction of a CP-PL 2 Barrier and Modified Type I Protective Screen is proposed to match the existing span, however an S3-TL4 Bridge Rail can be used if preferred by the Authority.

There is a temporary utility bridge located atop the easterly sidewalk and a temporary pedestrian/utility bridge, located adjacent to the easterly side of the roadway bridge. Utilities carried by these bridges will be relocated back onto the reconstructed roadway bridge. Both temporary structures will be removed and the bridge and approach sidewalk areas will be repaired.

The Community Path crosses School Street and intersects at the northwest and southeast corners of the bridge. Due to a limited ROW, an elevated pedestrian viaduct will be designed to abut the northwest corner of the bridge and an opening will be made in the existing bridge railing for path access. Similar path access will be provided at the southeast corner, although the abutting path may either be on fill behind a new wall or an elevated viaduct similar to the other corner.

Demolition and Reconstruction of the Southeast Wingwall of the Cedar Street Bridge. Our approach to modifying the existing Cedar Street Bridge entails retention of the existing superstructure and modification to the South abutment and wingwall. The substructure modifications will provide horizontal clearance for the Green Line (MB-WB).

Refuge/Safety niches will be installed in the southerly abutment at a maximum spacing of 20' – 0". At niche locations, existing concrete will be removed to specified limits with the new reinforced concrete doweled in to the existing. The southeast wing wall will be removed and replaced

The bridge was built in 1999 and designed for an HS-20 loading. The proposed work will not impact the current load capacity of the bridge. Construction will be performed with minimal impacts to pedestrian and vehicle traffic.

Removing the South Stone Masonry Abutment of the Lowell Street Bridge. Our approach to modifying the existing Lowell Street Bridge entails retention of the existing superstructure and modification to the south abutment to provide horizontal clearance for the Green Line (MB-WB).

The south abutment on the current bridge is constructed with drilled shafts and a reinforced concrete abutment cap/bridge seat. A granite abutment from an earlier bridge is located in front of the drilled shaft abutment and retains the fill below the abutment cap but does not provide any vertical support for the bridge. The granite abutment will be removed for rail clearances and a new soil nail wall system will be installed adjacent to the drilled shafts and designed to support the lateral loads.

The bridge was built in 2006 and designed for an MS22.5 loading. The proposed work will not impact the current load capacity of the bridge. Construction will be performed with minimal impacts to pedestrian and vehicle traffic.

Demolition of the Existing Broadway Bridge and Reconstruction of a New Bridge. Our approach for the Broadway Bridge is to demolish the existing single span bridge and construct a new two span bridge. The new bridge will provide a 5' – 0" bicycle lane and a 12' – 0" travel lane in each direction, an 8' – 8" northerly sidewalk and a 7' – 6" southerly sidewalk. S3-TL4 Bridge Railings and modified Type I Protective Screen will be installed on both sides.

The superstructure for the new bridge will consist of six longitudinal rolled stringers that act compositely with the reinforced concrete deck slab. The deck slab will have an integral concrete wearing surface. Weathering steel will be used, with the ends of the beams either encased in concrete or coated to provide corrosion protection. Stringers will be continuous to eliminate the need for a joint over the pier. Due to the high skew angle, strip seal joints will be used at both abutments.

The easterly abutment will be a full height cantilevered abutment with the footing supported by drilled shafts. The center pier will consist of concrete columns and a concrete cap with the footing supported by drilled shafts. The westerly abutment will be located behind an MSE wall which will be constructed beyond the clear zone for the MB-EB track. The perched westerly abutment will consist of a solid reinforced concrete stem and footing supported by drilled shafts.

A separate utility bridge supports several utilities and is adjacent to the southerly side of the bridge. This bridge will be retained, and painted. The soldier pile and lagging wall at the utility bridge will be modified and coordinated with the approach retaining wall construction along the ROW.

Removal of the Sidewalk on the North Side of the College Avenue Bridge and Construction of New Right-Turn Lane. Our approach to modifying the existing College Avenue Bridge entails retention of the existing superstructure, modification to the northerly sidewalk and construction of a pedestrian bridge just north of the existing bridge and utility bridge.

The existing 5' – 0" northerly sidewalk will be removed to provide a right hand turning lane on the bridge. The sidewalk will be replaced with a safety curb dowelled into the existing prestressed box beams. An S3-TL4 Bridge Railing and modified Type I Protective Screen will be installed. The bituminous concrete wearing surface and waterproofing membrane will be removed and replaced across the entire structure and new sawed and sealed joints will be installed. New endposts will be installed at the ends of the bridge.

Constructing a New Pedestrian/Bike Bridge over the Tracks by the MWRA Utility Support. To compensate for removal of the northerly sidewalk, a new pedestrian bridge will be constructed. The bridge will be a prefabricated truss structure with a span of 95' – 0". The pedestrian bridge will have a 12' – 0" wide concrete wearing surface. Approaches to the pedestrian bridge consist of ramps that tie back in to the approach sidewalk on either end of the roadway bridge. These ramps will meet all ADA slope and accessibility requirements. MSE Walls will be used in the construction of the approach ramps.

Plan, Cross Sections, and Elevations Showing the Structural Form and Design Interpretation

Bridge sketch plans/preliminary plans are included at the end of this section.

4.2.C GEOTECHNICAL ENGINEERING

GLX Constructors' Geotechnical Design Discipline Lead, Bob Palermo, P.E., has 40 years of experience with foundation construction and has extensive knowledge of the ground conditions and engineering properties of the soil and bedrock in the greater Boston area. During the Proposal phase, Bob was involved in all geotechnical aspects of the work and is an integral part of GLX Constructors. He has worked closely with structural engineers on the project team on foundation and retaining wall design. During construction, he will remain involved to assure the design criteria established during final design are properly implemented.

Summary of the Identified Geotechnical Conditions, Constraints, Concerns, and Outstanding Issues

The ground conditions depicted on these figures are based primarily on borings conducted along the proposed track alignment. However, at the northern end of the alignment, the track level is depressed relative to the ground on either side over most of its length because the current track bed was constructed by excavation. Therefore, the conditions described below for the northern portion of the alignment do not necessarily reflect the actual conditions along the proposed retaining walls or

outside the project ROW. To understand the ground conditions at the retaining wall and noise wall locations, transverse sections were developed where there was boring information at the top of slope adjacent to the alignment. This information was used as a basis to develop design soil profiles along each of the retaining and noise walls.

The project can be broken down into four basic areas in terms of ground conditions:

1. **Lechmere/Medford Branch Viaduct (STA 178+00 to STA 223+00).** The southern end of this section is characterized by a relatively thick layer of competent soils consisting of relatively dense sand/silty sand, glaciomarine and glacial till overlying a thin layer of weathered bedrock. Whereas, at the northern end, ground conditions consist of a thinner layer of glacial till overlying a weathered bedrock up to about 90 feet in thickness. A layer of organics and clay was encountered between Piers 1 and 8 and between Piers 19 and 27.

2. **Medford Branch Track (STA 223+00 to STA 374+00).** North of the Medford Branch Viaduct, ground conditions along the track bed generally consist of a thin layer of fill overlying relatively dense glacial till. Bedrock varies from about 50 feet below existing grade to just a few feet below grade. It should be noted that about 2/3 of this section is in an area that required excavation of existing soils during original construction. Therefore, the profiles along the bottom of the trackway do not represent the ground conditions along the proposed retaining wall and noise walls. In order to assess ground conditions along the walls, subsurface profiles along the wall alignments were developed based on the borings taken from the top of slope on either side of the trench. The profiles included in the drawings indicate that glacial till is higher than indicated on the track profiles, and that bedrock is occasionally above the existing elevation of the track ballast.

3. **Union Square Track (STA US WB 3+00 to STA 39+00).** East of approximately STA 10+00, ground conditions generally consist of up to 10 feet of fill overlying medium dense to very dense sandy soils and/or glacial till. A layer of weathered bedrock varying in thickness from about 10 to 60 feet thick was encountered below a relatively thin layer of glacial till between approximately Elevations -10 and -40 feet. The top of bedrock is highly erratic, based on the available borings. West of STA 10+00, the subsurface profile consists of 10 to 15 feet of fill overlying a silty clay layer up to 30 feet thick. A discontinuous layer of organic soils up to 14 feet thick was encountered below the fill along this section of the alignment, including the Union Station area. The silty clay layer is underlain by a glacial till deposit that is generally about 10 feet thick. However, between STA 13+00 and STA 18+00, the glacial till is up to 35 feet in thickness. The glacial till is underlain by weathered bedrock, where it was penetrated by the borings.

4. **Vehicle Maintenance Facility and Yard.** Subsurface conditions generally consist of fill underlain by sand, clay, glacial till, weathered rock and bedrock. Organic soils were encountered in borings performed to the east of the existing tracks, outside of the proposed VMF facility. The top of glacial till/weathered rock/bedrock is typically less than about 40 feet below existing grade. It is also noted that only three borings were performed within the footprint of the proposed VMF building. Therefore, additional borings will need to be performed during final design to better characterize ground conditions within the building footprint.

Constraints and Concerns. Based on our review of the available subsurface information provided, we have identified the following constraints and concerns will need to be considered during final design:

- There is limited subsurface information along many of the retaining walls. Therefore, conservative assumptions were made to advance the retaining wall design currently shown on the Plans. For example, bedrock may be encountered at a higher elevation than currently anticipated, thus requiring additional bedrock drilling for retaining wall and noise wall piles.

- The quality of the bedrock is not well defined. Many of the recent borings were advanced in the bedrock without rock coring and associated laboratory testing. At boring location NVB-24, three borings were performed (i.e. NVB-24A, NVB-24B and NVB-24C. One of these borings indicated that the borehole was advanced using a roller bit, while relatively good quality bedrock was cored in the other two adjacent boreholes. This was also the general location of where the O-cell test was performed by the previous contractor on a drilled shaft.

- None of the rock cores from borings performed by Parsons Brinckerhoff (PB) were available for our designers to review.

- There is limited information available regarding the existing buildings along the alignment. The condition of the 13 existing buildings that are located within our preliminary zone of influence are of particular concern, since mitigating measures required to protect these structures may be underestimated. Also, the nature and condition of buildings between Station MB 192 and MB 199 are unknown.

- The existing fill at the south end of the alignment is expected to contain numerous obstructions and few test pits are included in the RFP documents.

Outstanding Issues

- No long-term monitoring data available on groundwater levels.

- No Foundation information for the existing buildings where the VMF will be constructed.

- The soil/rock classification included on the boring logs provided with the RFP appears to be inconsistent between the various geotechnical engineers.

- The bedrock elevation appears to slope from one side of the alignment to the other. However, often there is little information provided to reliably determine the actual top of rock along both sides of the trackway, due to the limited number of borings. In some areas, the borings along the track bed indicated that the top of bedrock is within a few feet of the ground surface. However, without boring along both sides of the alignment, it is not clear whether the rock was removed to that level or it is the naturally occurring rock level.

- As shown in Figure 4.2-19, the quality of the bedrock appears to be highly variable and erratic, especially in the area of the Viaduct. Thus, the design of drilled shaft foundations will be difficult, and will need to be conservative to account for the variability in ground conditions

Interpretation of the Geotechnical and Hydrogeological Conditions

The anticipated general ground conditions along the alignment are described in Section 4.2.C. However, to better understand the ground conditions at the retaining wall and noise wall locations, transverse sections were developed where there was boring information at the top of slope adjacent to the alignment. This information was used as a basis to develop design soil profiles along each of the retaining and noise walls. Soil profiles were also developed at each station and bridge location.

Due to access limitations, borings were not performed along the actual retaining and noise wall locations. Therefore, supplemental explorations will be required during final design to confirm the assumption made during the preliminary design that is currently depicted on the drawings and described herein.

Summary of Geotechnical and Hydrogeological Design Properties

Geotechnical design parameters were developed based on the information contained on the boring logs and the laboratory results included in the RFP documents for the preliminary design of the retaining walls and foundations shown on the structural drawings. Our team's extensive experience with the design of similar retaining structures and foundations on local projects such as the Central Artery/Tunnel project, the Wynn Casio and the MBTA North Station Project was also considered in developing these design parameters.

The geotechnical parameters used for the design of the soldier pile and lagging retaining walls and the noise walls are contained in Figure 4.2-20. The parameters for the fill are relative only to the existing fill material, which varies in consistency and density. The friction angle was intentionally selected as conservative, subject to completion of supplemental explorations during final design. For the design of gravity retaining structures and MSE walls, a friction angle of 34 degrees will be used for compacted structural fill.

The soil and bedrock parameters used for the design of the drilled shaft and micropile foundations are shown on the drawings for the Viaduct and the bridge foundations and are included in Table 2. These parameters are based in large part on the local experience of our Geotechnical Design Discipline Lead, Bob Palermo, on projects



Figure 4.2-19. Variability in Bedrock quality. *These photographs demonstrate the extreme variability if the quality of the bedrock. The photo on the left shows competent rock core, and the photo on the right is a sample of rock that was obtained with a standard split spoon soil sampling device.*

such as the Central Artery/Tunnel project, the New Boston Garden, and the new Wynn Boston Casino. We also reviewed the results of four load tests for drilled shafts socketed into bedrock performed at the Woods Memorial Bridge in Medford, Massachusetts.

During preliminary design, we conservatively ignored the contribution of the soils overlying the glacial till stratum, including the relatively thick sand layer between approximately STA 191+00 and 201+00. We will revisit this assumption during final design.

The depth of the drilled shafts shown on the drawings are based primarily on static loading conditions. Some of the shaft depths are actually deeper than required based on the geotechnical parameters to take into account the effect of seismic loads that were only estimated during preliminary design, A more rigorous seismic analysis will be performed during final design that may result in shorter shaft lengths, particularly for Piers 32 through 37, where the required embedment for axial load support is relatively small.

Outline of Additional Geotechnical Investigations, Laboratory Testing, and Analyses

We have developed a preliminary program of supplemental subsurface explorations and laboratory testing that will be performed immediately after NTP. The exploration program will be performed in phases are consistent with the final design and construction schedule. Based on the results of these explorations, the preliminary program described herein may be modified to reflect the actual ground conditions encountered.

Supplemental Geotechnical Investigations. Supplemental explorations will be performed to confirm the quality of the information indicated on the available exploration logs, and to satisfy the Project requirements for the minimum number of borings described in Table 15.1-2 of the Technical Provisions. Confirmatory borings are primarily anticipated to be required in portions of the alignment where current subsurface information is not available, and in areas of thick weathered rock where deep foundations with rock sockets are proposed along the Medford and Union Square viaducts. These supplemental explorations will be observed and logged by GLX Constructors.

Preliminary Design Soil Properties					
Soil Starta	Total Unit Weight (pcf)	Submerged Unit Weight - (pcf)	Friction Angle - degrees	Uniaxial Compressive strength (psi)	Conhesion (psf)
Fill	125	63	30	–	–
Sand	128	66	32	–	–
Till	135	73	39	–	–
WRx	135	73	0	–	4,000
Rx	155	–	–	3,500	–

Figure 4.2-20. Preliminary Design Soil Properties. *Preliminary Geotechnical Design Parameters for Soldier Pile Walls and Noise Walls.*

Figure 4.2-21 summarizes the required minimum number of boring required, and indicates the number of supplemental explorations that we will perform.

At the viaduct pier and abutment locations, one supplemental boring will be performed at each drilled shaft location. At Piers 1 through 7, which will be supported on micropiles due to limited overhead clearance below the existing viaduct, two borings will be performed at each pier to confirm rock quality for the rock socketed portion of the micropiles. At locations of previously constructed viaduct foundations at Piers 26 and 27, one boring will be performed at each shaft location to confirm subsurface conditions needed to validate the design of the as-built drilled shaft foundations. Also, in order to evaluate the results drilled shaft load test performed by the previous contractor, one boring will be performed at the location of the Osterberg test shaft location.

Geotechnical Feature	Minimum Number of Total Borings	Minimum Number of Supplemental Borings Required	Number of Supplemental Explorations to be Performed
Track Subgrade	In accordance with AREMA	Not Specified	0
Vehicle Maintenance Facility	8 within Footprint	6	8
Stations	6 per station	0	7
Viaduct Piers and Abutments	1 at each caisson and each abutment	26	26
Bridge Piers and Abutments	In accordance with AASHTO and the MassDOT LRFD Bridge Manual	2	12
Retaining Walls and Noise Barriers	2 at each retaining wall and noise barrier. Max. spacing of 200 feet between borings.	20 for Noise Walls 21 for Retaining Walls	20 for Noise Walls 29 for Retaining Walls
Traction Power Substations and other Ancillary structures	As required by applicable code.	0	4
Embankments and Cuts	In accordance with FHWA NHI-01-031 Subsurface Explorations – Geotechnical Site Characterization	0	4
Micropiles at Piers 1 – 7	Not Specified	N/A	14
Previously Completed Drilled Shafts and Osterberg Test Shaft Locations	Not Specified	N/A	7
	Total	**75**	**131**

Figure 4.2-21. Proposed Supplemental Explorations. *Our exploration program will meet or exceed the required minimum number of explorations specified.*

Confirmatory borings will be performed at retaining and noise wall locations in order to evaluate the top of rock variability (i.e., potential sloping bedrock surface) and to confirm required foundation lengths. We will perform more borings than the minimum number specified, because many of the existing borings provide the information needed for design.

Two confirmatory borings will be performed at each of the Ball Square and Gilman Square Station traction power substations.

In addition, borings will be performed as needed to evaluate soil and rock conditions along areas of proposed utilities, drainage structures and OCS foundations. The supplemental boring information will be used to evaluate if shallow weathered rock and bedrock will be able to be removed using conventional earth moving equipment.

In addition to the boring identified in Figure 4.2-21, we will perform refraction tomography testing to evaluate the quality and rippability of the bedrock along the proposed 66-inch drain line at the north end of the project where the bedrock is relatively shallow. The assessment of the rippability of bedrock will be based on the bedrock compressional wave velocity.

Laboratory Testing. Additional laboratory testing will consist primarily of unconfined compression tests to evaluate the strength and elastic modulus of the bedrock for the design of drilled shafts. Between approximately STA 200 and 223, the available borings indicate that the weathered bedrock is up to about 90 feet in thickness. Many of the reference geotechnical reports included in the RFI documents indicate a relatively low skin friction value. We believe that the strength of this material is understated, and we expect that the additional laboratory testing will justify higher skin friction values that will result in shorter drilled shaft lengths. Additional tests in the area of the O-cell test on the drilled shaft will allow us to better evaluate the results of the load test, and extrapolate these results to other production shafts.

Laboratory strength tests will also be performed on samples of weathered bedrock and bedrock at the north end on the alignment, where this material may be encountered during installation of the 66-inch drain line. Here, the purpose of the testing is to evaluate methods of rock removal.

Preliminary Hydrogeological Impact and Associated Risk Assessment

Depending on the duration, depression of the groundwater level outside of excavations will generally result in settlement of structures and utilities if there are compressible soils such as clay and organic soils. However, these soils only exist south of the yard lead crossing (STA 208+00), at the Vehicle Maintenance Facility and Yard, and along the Union Branch alignment.

At the northern end of the alignment, excavations are required for stations, utility installation and retaining wall construction. There are no compressible soils that will result in ground movements, even if the groundwater was depressed for an extended period. The soils in this area that overly the bedrock consist of dense glacial till soils that are relatively incompressible and impervious thus limited the zone of influence of depressed groundwater levels.

Anticipated Soil Groundwater Control Strategy for the Construction Period. Except for the installation of the 66-inch drain and other smaller diameter/shallower utilities along the alignment, excavation associated with new track construction or retaining wall construction will not be required below the bottom of the existing sub ballast. Much of the excavation for drainage and utilities will be less than 4 feet deep, and above the measured groundwater level, in areas where compressible soils are anticipated.

The excavation for the 66-inch drain is about 15 feet below existing grade, and about 5 feet below the groundwater level. The soils in this area of the alignment consist of granular fill and very dense glacial till, and are not subject to compression due to groundwater lowering, even if it did occur.

Construction dewatering is expected to be accomplished with conventional sump pumps, during relatively short durations. Therefore, there is no adverse impact associated with construction.

Anticipated Groundwater Control Strategy for all Subsurface Excavations. Groundwater levels will not be lowered below existing levels, since the finish grades will not be lower that they are now. However, as a mitigation measure, seepage collars will be constructed at approximately 200-foot intervals along deep utilities that run along the alignment to mitigate the potential for drainage. At each location, the trench excavation will be backfilled with a 2 to 4-foot wide zone of low permeability material that will serve as a dam that isolate each segment of trench between the seepage collars.

“To reduce the number of explorations and increase the efficiency of the supplemental exploration program, geotechnical and environmental sampling locations will be coordinated by our team to reduce impacts to the surrounding communities and active train traffic.

Preliminary Geotechnical Impact Assessment and Associated Risks

The Zone of Influence reference in the Contract Documents is only defined for establishing the number of structures where preconstruction condition surveys are required to be performed. Therefore, a preliminary Zone of Influence has been established as a basis to evaluate the probable limits of potential impacts to adjacent structures due to retaining wall construction. Our preliminary Zone of influence is based on a 1.5H:1V line extending from the bottom of excavation at the retaining wall to the 4 feet below grade outside the excavation and is shown on the retaining wall drawings. This is based primarily on published empirical correlations of ground movement and estimated wall deflections from the structural design of the retaining walls. Finite element analyses have also been performed that suggest that, for the ground conditions along the retaining walls the Zone of Influence shown on the drawings actually extend further away from the walls than required. This is also more conservative that the Zone of Influence specified for the preconstruction condition surveys. The Zone of Influence that we have used during preliminary design is shown on the individual retaining wall profile drawings.

Based on our preliminary, conservative limits of the Zone of Influence, there are 13 buildings that could be impacted by proposed construction. The primary impact of this conservative approach is that the retaining walls in front of these structures will be more conservatively designed to resist seismic loads. The depth of the foundation of the existing buildings was assumed to be only 4 feet below existing grade. If there are basements, the Zone of Influence will be further reduced.

A preliminary assessment of all buildings within the Zone of Influence have been performed based on the information currently available.

Where the estimated ground movements were expected to result in more than “cosmetic” damage, as described by Burland et al. 1977 and Borcardin and Cording, 1989, the stiffness of the retaining wall was increased to reduce ground movements to acceptable levels. This was accomplished either by using heavier soldier pile sections, reducing the spacing of soldier piles, increasing the embedment depth of the piles or providing a tieback near the top of the soldier pile. If measures movements exceed those anticipated during design and appear to impact adjacent structures, larger soldier pile sections will be used, or piles will be installed at closer spacings.

Our Geotechnical Design Discipline Lead has performed similar impact assessments on major urban construction projects such as the Central Artery/ Tunnel project in Boston, the Second Avenue Subway Project in NYC.

An automated geotechnical instrumentation monitoring program will be used to monitor retaining wall movements on a near real time basis during and after construction. Monitoring prisms will be established on permanent soldier piles at spacing of not more than 24 feet. If allowed by building Owners, monitoring prisms will also be established on the 13 buildings that fall within the Zone of Influence. A dedicated website will be established to store and display automated monitoring results.

Tracks and other structures will be monitored manually by surveyors in accordance with the project requirements.


Vibrations will be monitored during pile driving at Piers 8 through 24. We will also monitor vibrations periodically during drilling of soldier piles and soil compaction to confirm that these activities do not result in excessive vibrations at adjacent structures.

“The proposed monitoring program has been successfully implemented on the Tappan Zee Bridge Replacement Project to monitor the impacts of pile installation for the new bridge on the existing adjacent, and is accessible to all project participants.

GLX Constructor's approach is to provide simple structures that are straightforward to install and accelerate construction. The structures will be designed to meet the structural design life expectations and simplify future maintenance.


ITP Request	RFP		
	Drawing Number	Drawing Title	Reference Section or Drawing
A5.2.2.A.2	S-001	Soldier Pile and Lagging Wall Elevation, Section and Details	
A5.2.2.A.2	S-002	MSE Wall Elevation, Section and Details	
A5.2.2.A.2	S-003	Modular Precast Block Wall Elevation, Section and Details	
A5.2.2.A.2	S-004	Cast in Place Concrete Wall Elevation, Section and Details	
A5.2.2.A.2	S-005	Soil Nail Wall Section and Details	
A5.2.2.A.2	S-006	Soil Nail Crib Wall Replacement Wall Section and Details	
A5.2.2.A.2	S-007	Soil Nail Wall & Crib Wall Replacement Typical Elevations	
A5.2.2.A.2	S-008	Sheet Pile Wall Elevation, Section and Details	
A5.2.2.A.2	S-009	Noise Barrier Elevation, Section and Details	
A5.2.2.A.2	S-010	Retaining Wall MW-5 Plan and Subsurface Profile	
A5.2.2.A.2	S-011	Retaining Wall MW-10 Plan and Subsurface Profile	
A5.2.2.A.2	S-012	Bumping Post Detail	
A5.2.2.A.2	S-013	Lechmere Viaduct Split Framing Plan, Typical Section, Pier Elevation and Geotech	
A5.2.2.A.2	S-014	Medford Branch Viaduct Framing Plan, Typical Section, Pier Elevation and Geotech	
A5.2.2.A.2	S-015	Union Square Branch Viaduct Framing Plan, Typical Section, Pier Elevation and Geotech	
A5.2.2.A.2	S-016	ATC 35 Mse Plan View	
A5.2.2.A.2	S-017	ATC 35 Typical Section	
A5.2.2.A.2	S-018	ATC 35 Ground Improvement At MSE Walls	
A5.2.2.A.2	S-019	Washington Street Bridge – Plan & Elevation	
A5.2.2.A.2	S-020	Washington Street Bridge – Typical Section	
A5.2.2.A.2	S-021	Medford Street Bridge – Plan and Notes	
A5.2.2.B.3	S-022	Medford Street Bridge – Section and Elevation	
A5.2.2.B.3	S-023	School Street Bridge – Plan and Notes	
A5.2.2.B.3	S-024	School Street Bridge – Elevation	
A5.2.2.B.3	S-025	School Street Bridge – Cross Sections	
A5.2.2.B.3	S-026	Cedar Street Bridge – Plan and Elevation	
A5.2.2.B.3	S-027	Lowell Street Bridge – Plan and General Notes	
A5.2.2.B.3	S-028	Lowell Street Bridge – Elevation	
A5.2.2.B.3	S-029	Broadway Bridge – Plan & Elevation	
A5.2.2.B.3	S-030	Broadway Bridge – Typical Transverse Section	
A5.2.2.B.3	S-031	College Avenue Bridge – Typical Sections	
A5.2.2.B.3	S-032	College Avenue Pedestrian Bridge – General Plan and Elevation	

Technical Solutions Drawing Matrix.

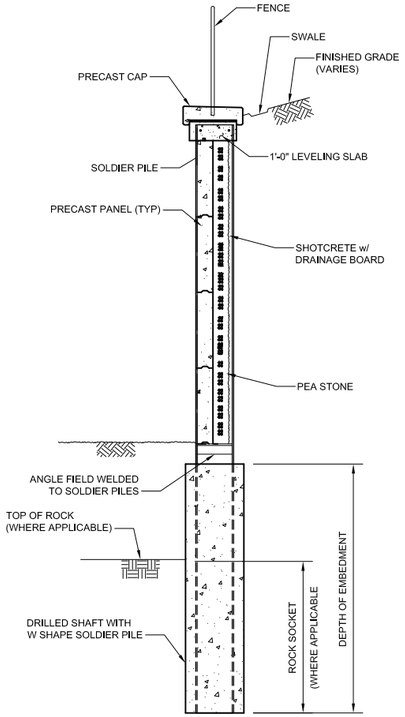


TYPICAL SOLDIER PILE AND LAGGING (SPL) WALL

1/4"=1'-0" 0 2' 4' 8'

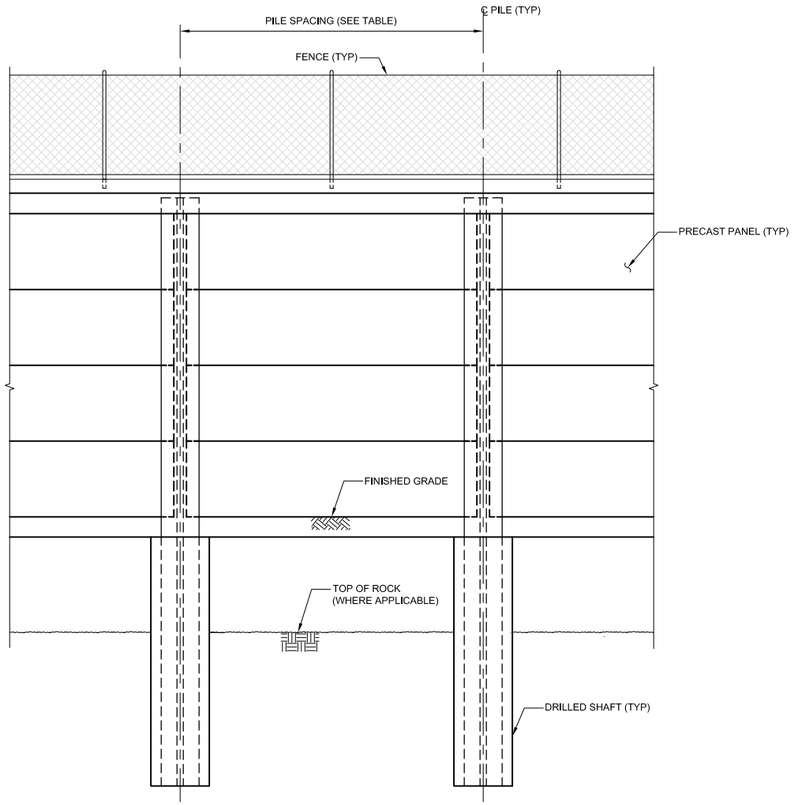

TYPICAL SOLDIER PILE AND LAGGING (SPL) WALL ELEVATION

1/4"=1'-0" 0 2' 4' 8'

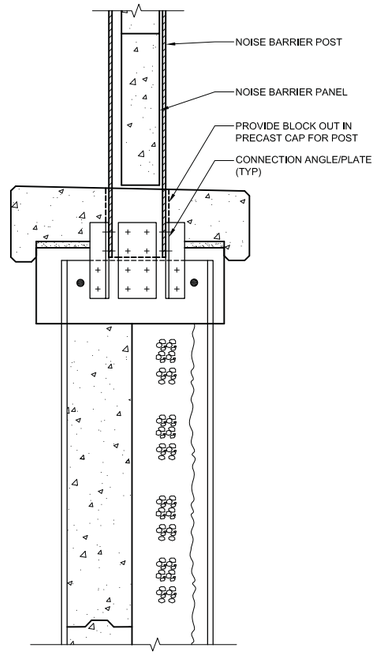


NOISE BARRIER DETAIL

1"=1'-0" 0 1' 2'

NOTES:

1. CIP CONCRETE SHALL BE F'c = 4,000 psi.
2. PRECAST CONCRETE SHALL BE 5,000 psi.
3. ALL STRUCTURAL STEEL SHALL BE ASTM A572, A709 OR A992 GRADE 50 HOT DIPPED GALVANIZED.
4. REINFORCING STEEL SHALL BE ASTM A615 GRADE 60.

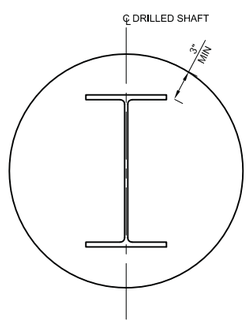

SECTION - SOLDIER PILE WITH DRILLED SHAFT

1"=1'-0" 0 1' 2'

SOLDIER PILE AND LAGGING WALL TABLE

WALL	STATION START	STATION END	OFFSET (FT) FROM MB-EB	OFFSET (FT) WALL FACE-TEMP EASE	OFFSET (FT) WALL FACE-PERM EASE	PILE SIZE	PILE SPACING (FT)	SHAFT DIAMETER (FT)	EXPOSED FACE (FT)	PILE LENGTH (FT)	SOIL EMBEDMENT (FT)	ROCK SOCKET (FT)	NOTES
ME-1	247+47	248+98	42	10-16	10-16	W24x76	8	3	14	29	15	-	
ME-2	309+63	313+00	39-40	3-16	3-16	W21x44	8	3	10	19	5	4	
	313+00	314+50	39-40	3-10	3-4	W24x68	8	3	12	27	15	-	
	314+50	316+00	39-40	4	4	W21x48	8	3	10	23	13	-	
	316+00	319+50	39-40	4-10	4-10	W21x48	8	3	10	22	9	3	
	319+50	320+50	39-40	10	10	W21x44	8	3	10	23	13	-	
ME-2.1	321+25	323+25	42	12	12	W14x30	8	3	6	15	9	-	
ME-3	223+01	225+50	40-45	15	6	W21x48	8	3	12	20	2	6	STATIONS ARE NH-T1
	225+50	227+50	40-45	15-20	6-20	W24x55	8	3	13	21	2	6	STATIONS ARE NH-T1
	227+50	231+05	40-45	18-20	18-20	W21x44	8	3	9	15	3	3	STATIONS ARE NH-T1
MW-0.7	235+25	235+75	52-61	-	-	W18x35	8	3	9	22	11	2	
MW-0.8	236+25	236+99	52-61	-	-	W18x35	8	3	9	22	11	2	
MW-36.2	258+31	259+50	22	100-150	100-150	W24x84	8	3	13	30	17	-	
	259+50	261+58	22	35-100	35-100	W24x229	8	3	18	42	24	-	TIEBACK MAY BE USED
MW-36.3	262+86	265+00	24	35	29-35	W14x53	8	3	10	23	13	-	
	265+00	266+38	24	35	29-35	W24x104	8	3	15	34	19	-	
MW-36.4	267+94	268+50	34	35	35	W30x261	8	3.5	24	51	14	13	TIEBACK MAY BE USED
	268+50	269+50	34	19-35	19-27	W24x229	8	3	21	45	14	10	TIEBACK MAY BE USED
	269+50	270+78	34	23-38	23-38	W24x162	8	3	20	41	13	8	
	270+94	275+18											
MW-5	276+00	278+00	24-40	14	5-10	W24x279	8	3	24	48	24	-	
	278+00	279+25	24-40	14-16	10-16	W24x94	8	3	12	30	18	-	
MW-7	296+40	298+75	22	10-28	2-10	W24x84	8	3	15	28	5	8	
MW-8.1	327+00	329+75	20-31	8-15	2-5	W16x40	8	3	7	20	13	-	
MW-8.15	331+39	332+39	40	11	11	W24x131	8	3	16	33	9	8	

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

SOLDIER PILE AND LAGGING WALL ELEVATION, SECTION AND DETAILS


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DH	EE	EE	SHEET: S-001	

PLOTTED: 09/22/17 2:16PM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\RETAINING WALLS_PROPOSAL DRAWINGS\S-001 SOLDIER PILE AND LAGGING WALL.DWG [LAYOUT1] 09/22

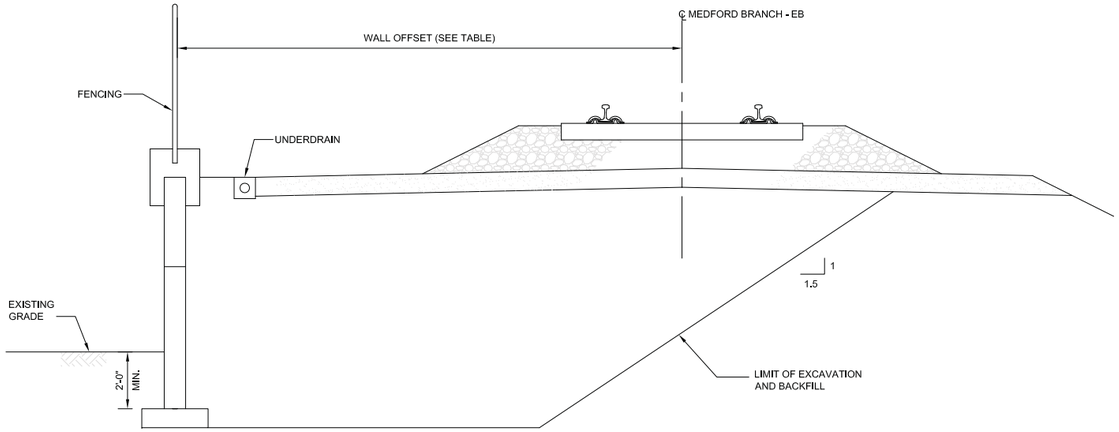

MSE WALL

3/8"=1'-0" 0 2' 4' 6'

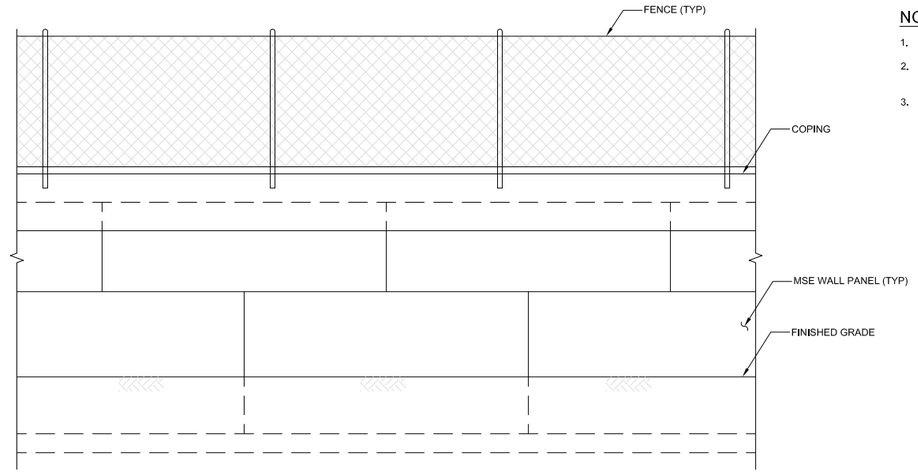


MSE WALL ELEVATION

3/8"=1'-0" 0 2' 4' 6'


NOTES:

1. PRECAST CONCRETE SHALL BE 5,000 PSI.
2. REINFORCING STEEL SHALL BE ASTM A615 GRADE 60.
3. PROVIDE CANTILEVERED COPING WITH MOMENT SLAB AT TITAN CAR WASH.

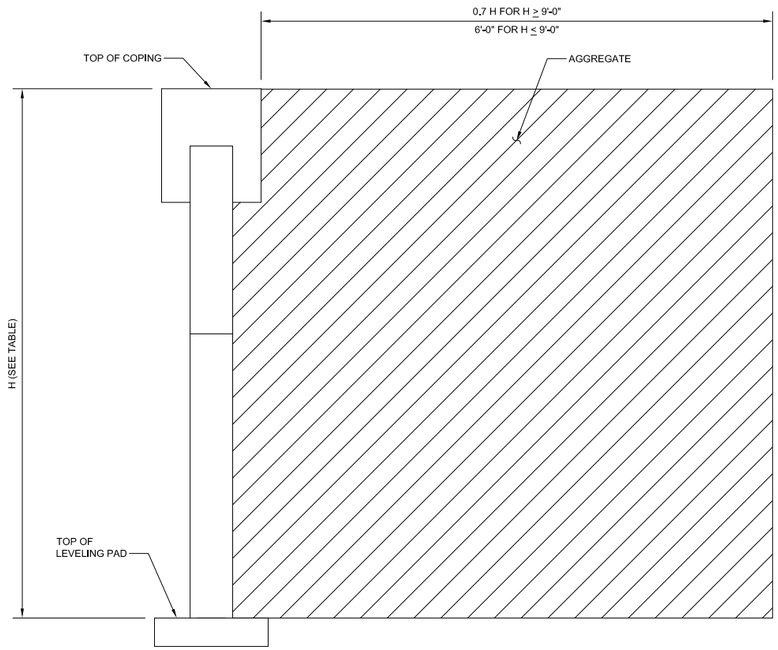

ASSUMED AREA OF REINFORCED ZONE

3/4"=1'-0" 0 1' 2' 3'

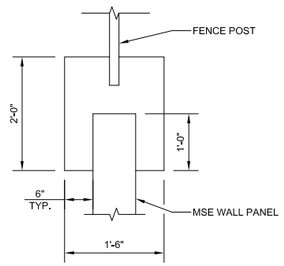

COPING DETAIL

3/4"=1'-0" 0 1' 2' 3'

MSE WALL TABLE					
WALL	STATION START	STATION END	OFFSET	HEIGHT, H (FT)	NOTE
MW-8,2	343+56	345+20	18	13	SEE NOTE 3
MW-9	345+80	348+50	20	8	
	348+50	351+00	20	7	
	351+00	353+54	20	6.25	

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


MSE WALL
ELEVATION, SECTION AND DETAILS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DH	EE	BD	SHEET: S-002	


PLOTTED: 09/22/17 2:16PM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\RETAINING WALLS-NOISE WALLS_PROPOSAL DRAWINGS\S-002 MSE WALL DETAILS.DWG [LAYOUT1] 09/21/17 4:32PM

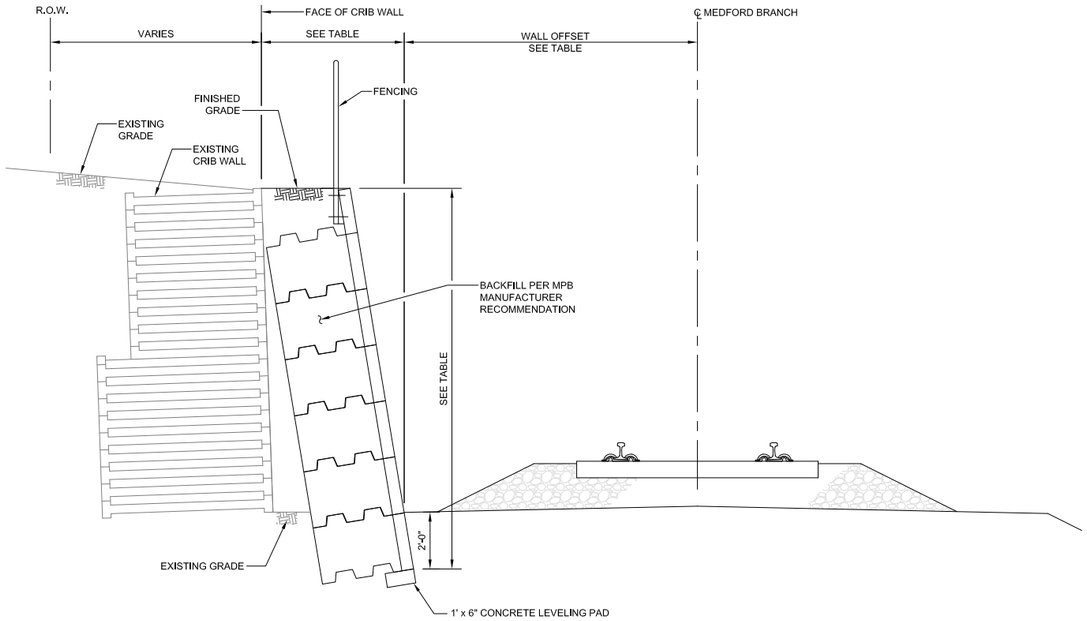

MODULAR PRECAST BLOCK WALL SECTION AT CRIB WALL

3/8"=1'-0" 0 2' 4' 6'

MODULAR PRECAST BLOCK WALL AT CRIB WALL TABLE						
WALL	STATION		OFFSET FROM MB-EB (FT)	MINIMUM DISTANCE BETWEEN FACE OF CRIB WALL AND FACE OF MPB WALL	AVERAGE TOTAL HEIGHT (FT)	NOTES
	START	END				
MCE-1	248+97	252+42	38	4.5	11	SEE NOTE 5
MCW-1	247+03	251+28	32	5.5	12	SEE NOTE 5

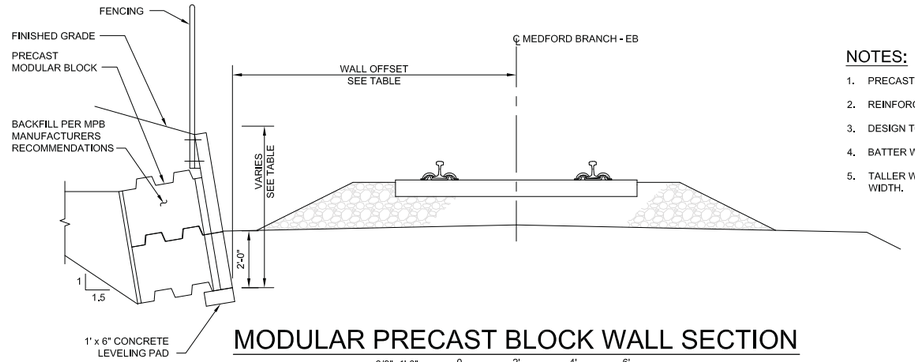


MODULAR PRECAST BLOCK WALL SECTION

3/8"=1'-0" 0 2' 4' 6'

NOTES:

1. PRECAST CONCRETE SHALL BE 5,000 PSI.
2. REINFORCING STEEL SHALL BE ASTM A615 GRADE 60.
3. DESIGN TO BE PERFORMED BY WALL MANUFACTURERS .
4. BATTER WALL AS REQUIRED BY DESIGN.
5. TALLER WALL SECTIONS MAY REQUIRE INCREASED BASE WIDTH.


MODULAR PRECAST BLOCK WALL TABLE					
WALL	STATION		OFFSET FROM MB-EB	TOTAL HT (FT)	NOTES
	START	END			
ME-0.5	216+49	217+00	30	8	
	217+00	217+53	30	6	
ME-2.2	327+25	327+75	40	7	
ME-2.3	328+25	328+75	40	5	
ME-2.5	363+75	364+25	40	8	
MW-36.1	257+27	258+31	22	7.5	
MW-5.5	279+25	280+75	25	10	
	280+75	281+25	25	8	
MW-6.5	295+75	296+40	23	6	
MW-7.5	298+75	299+75	22	10	
MW-7.6	298+00	299+00	36	6	
	299+00	299+50	36	8	
	299+50	300+50	36	12	SEE NOTE 5
	300+50	301+25	36	6	
MW-8	322+75	323+25	22	4	
	323+25	324+75	22	6	
	324+75	327+00	22	7.5	
MW-9.5	360+75	361+50	22	10	
	361+50	362+00	22	12	SEE NOTE 5
	362+00	362+80	22	15	SEE NOTE 5

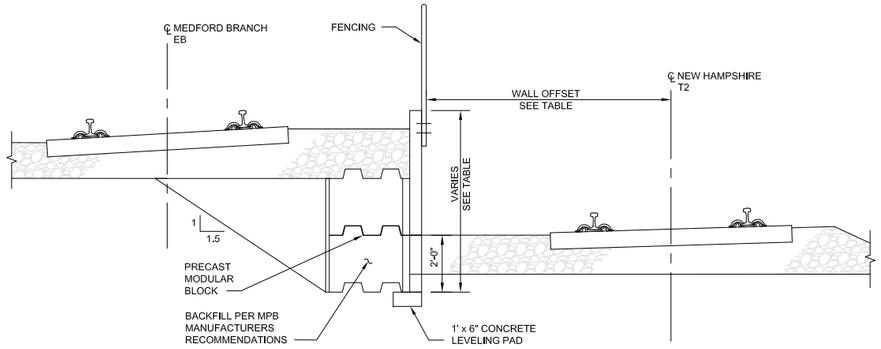

MODULAR PRECAST BLOCK WALL SECTION AT BALLAST RETAINING WALL

3/8"=1'-0" 0 2' 4' 6'

MODULAR PRECAST BLOCK WALL AT BALLAST RETAINING WALL TABLE					
WALL	STATION (MB-EB)		OFFSET FROM NH-T2	TOTAL HT (FT)	NOTES
	START	END			
BR-1	261+00	262+50	9	6	
	262+50	268+00	9	7	
	268+00	269+00	9	6	

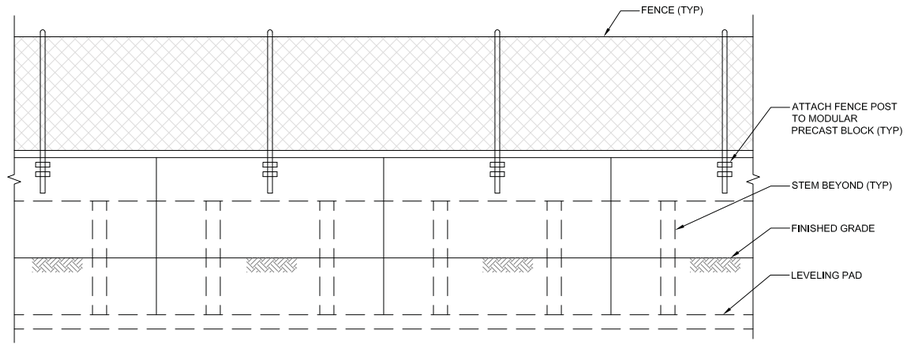

MODULAR PRECAST BLOCK WALL ELEVATION

3/8"=1'-0" 0 2' 4' 6'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MODULAR PRECAST BLOCK WALL ELEVATION, SECTION AND DETAILS


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-272.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DH	EE	EE	SHEET: S-003	

PLOTTED: 09/22/17 2:17PM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\RETAINING WALLS+NOISE WALLS_PROPOSAL DRAWINGS\S-003 MODULAR PRECAST BLOCK WALL.DWG [LAYOUT] 09/22/17

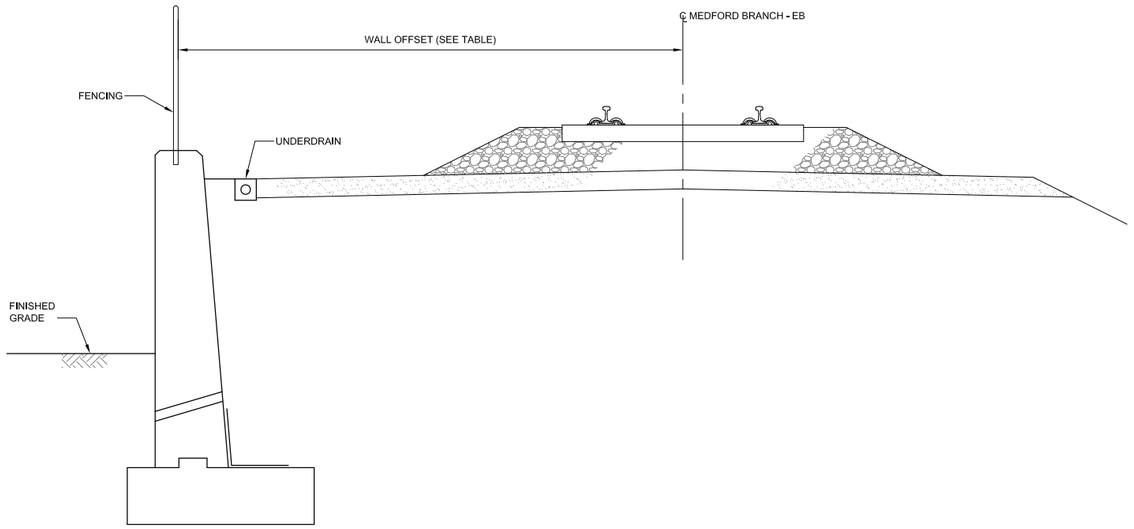


CAST IN PLACE CONCRETE WALL

3/8"=1'-0" 0 2' 4' 6'

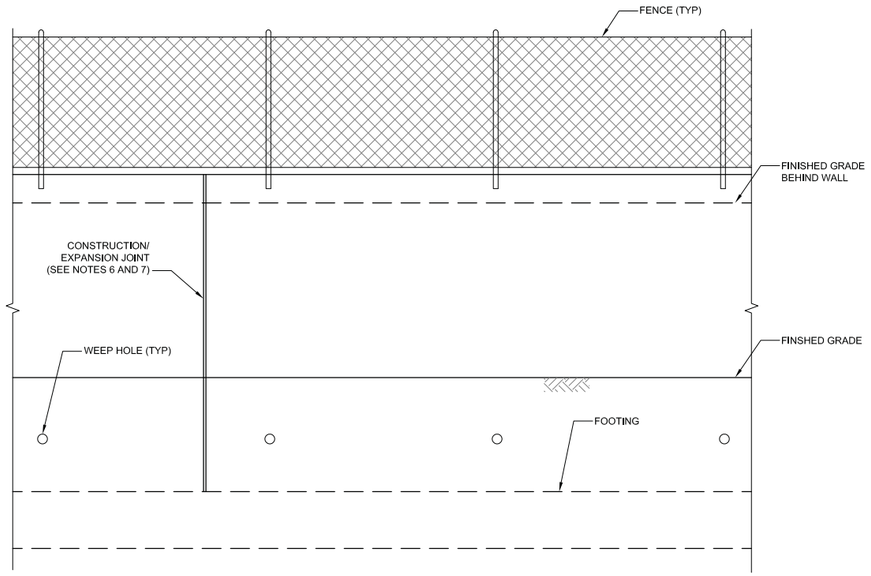

CAST IN PLACE CONCRETE WALL ELEVATION

3/8"=1'-0" 0 2' 4' 6'

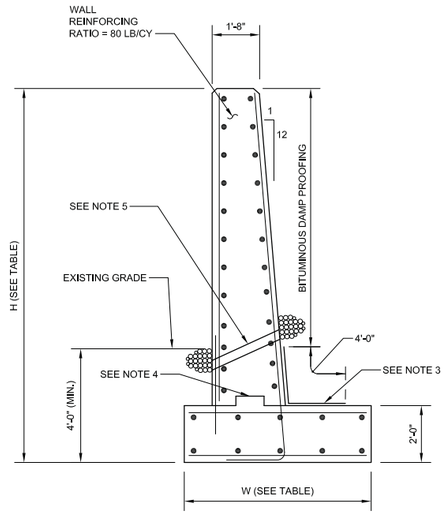

TYPICAL SECTION

3/8"=1'-0" 0 2' 4' 6'

CAST IN PLACE CONCRETE WALL TABLE					
WALL	STATION		OFFSET	H,HEIGHT(FT)	W, FOOTING WIDTH (FT)
	START	END			
MW-0.5	234+20	235+50	40	10	6
	235+50	237+03	40	18	10

NOTES:

1. CONCRETE SHALL BE 4,000 PSI.
2. REINFORCING STEEL SHALL BE ASTM A615 GRADE 60.
3. MEMBRANE WATERPROOFING AND CEMENT CONCRETE BLOCKS LAID IN MORTAR.
4. CONSTRUCTION JOINT WITH KEY.
5. 4" DIAMETER WEEP HOLE AT 10' ON CENTER WITH 1" CUBIC YARD CRUSHED STONE AT EACH END OF WEEP HOLE.
6. MAXIMUM CONSTRUCTION JOINT SPACING = 40'-0".
7. MAXIMUM EXPANSION JOINT SPACING = 100'-0".

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


CAST IN PLACE CONCRETE WALL ELEVATION, SECTION AND DETAILS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DH	ZY	EE	SHEET: S-004	


PLOTTED: 09/22/17 2:17PM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\RETAINING WALLS-NOISE WALLS_PROPOSAL DRAWINGS\S-004 CIP WALL DETAILS.DWG [LAYOUT] 09/22/17 10:13AM

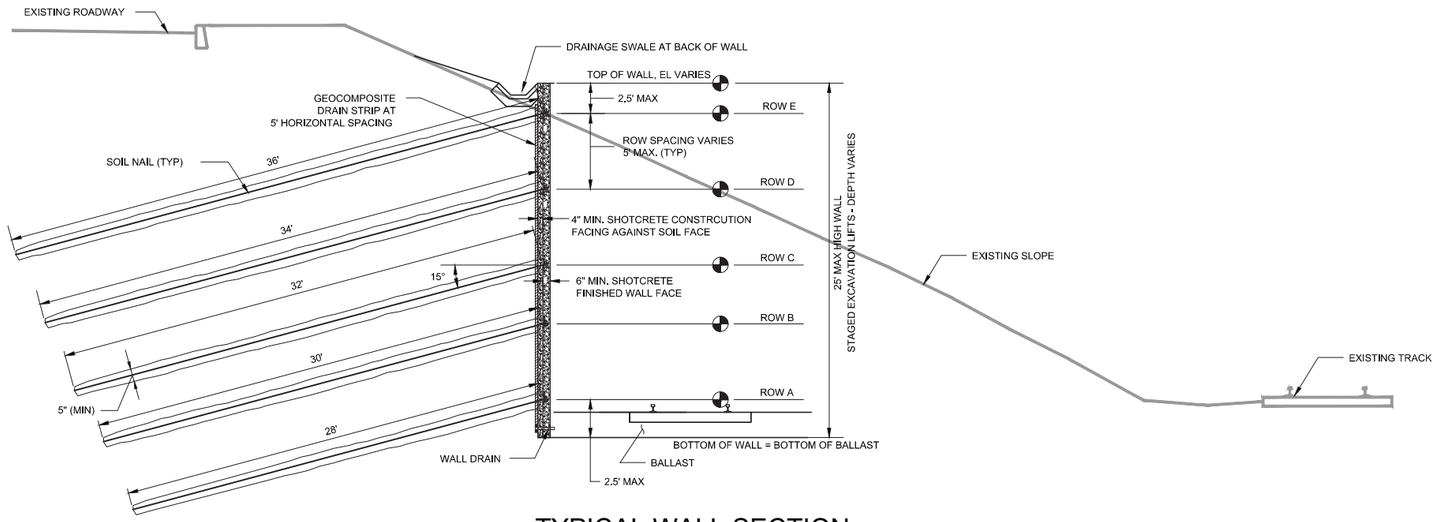

TYPICAL WALL SECTION

NOT TO SCALE

SECTION NUMBER	STATION FROM	STATION TO	NUMBER OF LEVELS	MAXIMUM WALL HEIGHT	LENGTH	QUANTITY
1	374+00	371+82	3	15 FEET	ROW C = 32 FT LONG	44
					ROW B = 30 FT LONG	44
					ROW A = 28 FT LONG	44
2	371+82	369+72	4	20 FEET	ROW D = 34 FT LONG	42
					ROW C = 32 FT LONG	42
					ROW B = 30 FT LONG	42
					ROW A = 28 FT LONG	42
3	369+72	366+67	5	25 FEET	ROW E = 36 FT LONG	62
					ROW D = 34 FT LONG	62
					ROW C = 32 FT LONG	62
					ROW B = 30 FT LONG	62
					ROW A = 28 FT LONG	62
4	364+79	364+12	4	20 FEET	ROW D = 34 FT LONG	13
					ROW C = 32 FT LONG	13
					ROW B = 30 FT LONG	13
					ROW A = 28 FT LONG	13
5	364+12	363+93	3	15 FEET	ROW C = 32 FT LONG	5
					ROW B = 30 FT LONG	5
					ROW A = 28 FT LONG	5

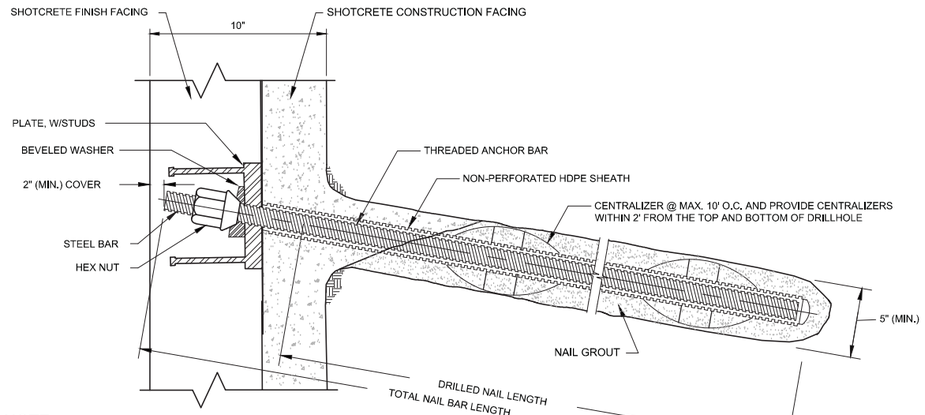

NOTE:


3" BAR COVER APPLIES ONLY WHEN EPOXY COATED REBAR WITH CUT THREADS ARE USED. FOR FULL LENGTH EPOXY COATED THREADBAR, 3" COVER REQUIREMENT IS NOT REQUIRED.

TYPICAL SOIL NAIL DETAIL & CORROSION PROTECTION REQUIREMENTS

NOT TO SCALE


NOTES:

1. ALL REINFORCING STEEL SHALL BE GRADE 60.
2. THREADED ANCHOR BAR SHALL BE GRADE 60.
3. REFER TO ALL NOTES AND SPECIFICATIONS.

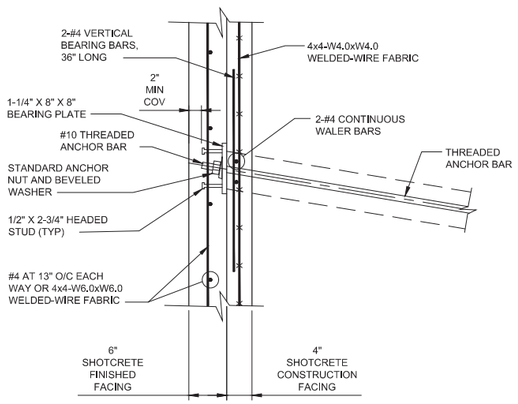

TYPICAL SOIL NAIL HEAD AND WALL DETAIL

1"=1'-0" 0 1' 2'

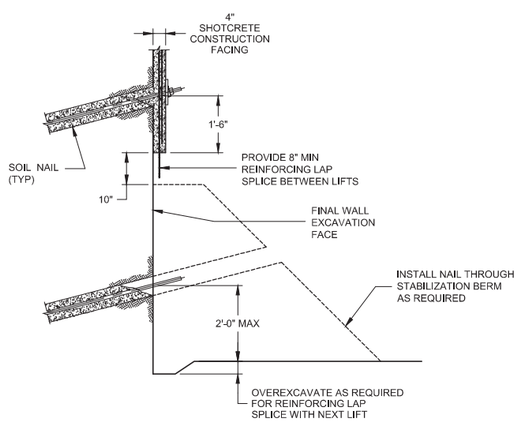

TYPICAL EXCAVATION DETAIL

NOT TO SCALE

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


SOIL NAIL WALL
SECTION AND DETAILS

ISSUE	DATE	DESCRIPTION	BY	CHKD	APP.

GV20170258-272.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DL	STS	RJP	SHEET: S-005	

PLOTTED: 09/22/17 12:24PM BY:DEBORAH.LANDI
DRAWING: \\GZANOR2\KFP\2018\01.P000061.BRJP\FIGURES\CAD\GZA-SEC DET-RW-MW-10-PROPOSAL.DWG [S-005] 09/22/17 11:42AM

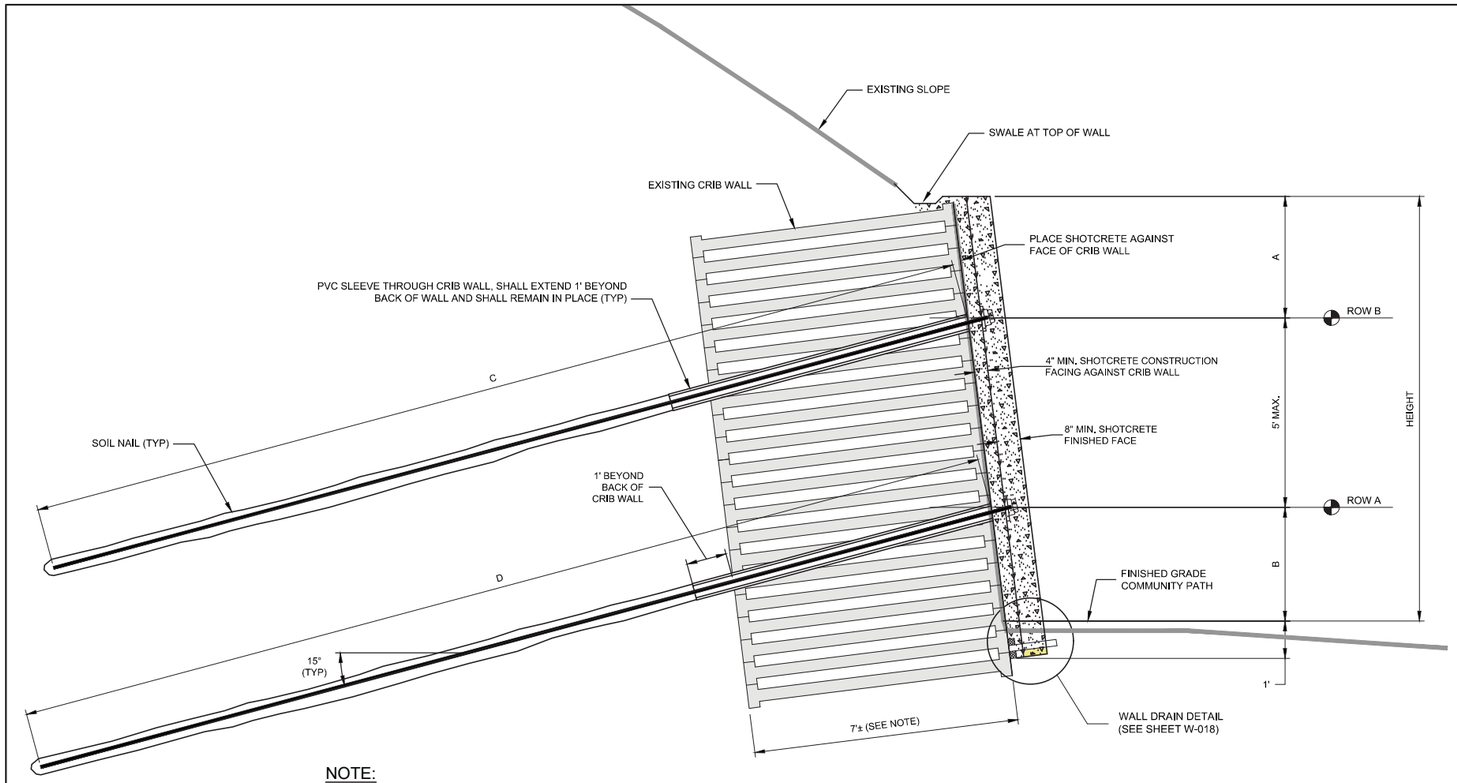

NOTE:
WALL WIDTH BASED ON INFORMATION CONTAINED IN REPORT ENTITLED "NONDESTRUCTIVE TESTING CRIB WALLS ME-1 AND MW-2 EVERGREEN WALLS ME-4 AND ME-5 FOR THE GREEN LINE EXTENSION PROJECT SOMERVILLE, MASSACHUSETTS" PREPARED BY NDT CORPORATION DATED DECEMBER 2016.

TYPICAL WALL SECTION


1/2"=1'-0" 0 1' 2' 4'

CRIB WALL SCHEDULE

WALL DESIGNATION	HEIGHT (FT)	STATION (MB-EB)		A (FT)	B (FT)	C (FT)	D (FT)	MIN. DISTANCE TO ROW FROM TOP OF WALL (FT)
		FROM	TO					
MCW-2	12'	252+79	258+25	3'	3'	34'	34'	35'
MCW-3	9'	285+41	289+08	2'	2'	25'	26'	26'


NOTES:

1. ALL REINFORCING STEEL SHALL BE GRADE 60.
2. THREADED ANCHOR BAR SHALL GRADE 60.
3. REFER TO ALL NOTES AND SPECIFICATIONS.

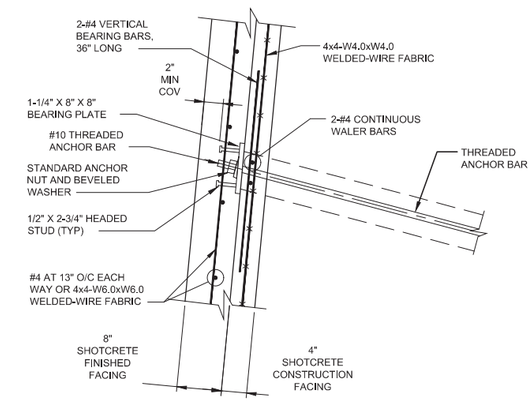

TYPICAL SOIL NAIL HEAD AND WALL DETAIL

1"=1'-0" 0 1' 2'

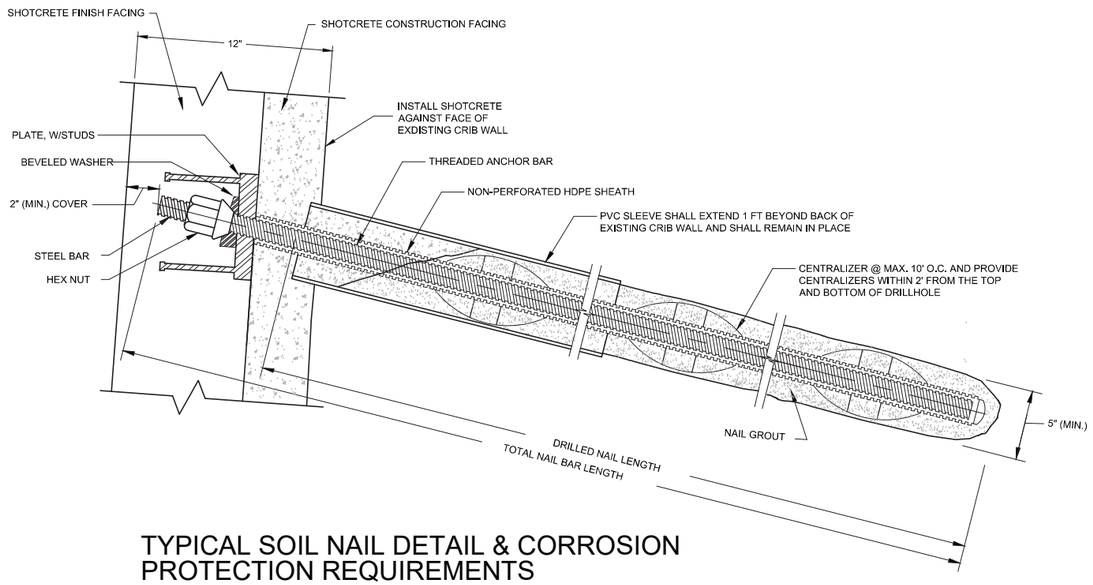

TYPICAL SOIL NAIL DETAIL & CORROSION PROTECTION REQUIREMENTS

NOT TO SCALE

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


SOIL NAIL CRIB WALL REPLACEMENT SECTION AND DETAILS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DL	STS	RJP	SHEET: S-006	

PLOTTED: 09/22/17 12:23PM BY:DEBORAH.LANDI
DRAWING: \\GZANOR2\RPA\2018\01.P000061.18RJP\FIGURES\CAD\GZA-SEC DET-RW-MW-10-PROPOSAL.DWG [S-006] 09/22/17 11:42AM

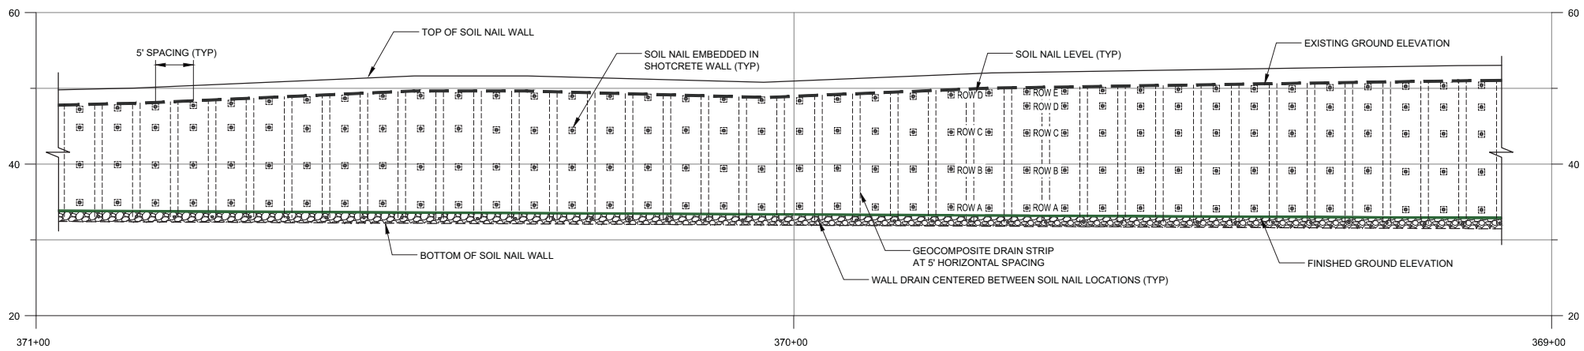

SOIL NAIL WALL - TYPICAL ELEVATION

1"=10' 10' 5' 0 10'

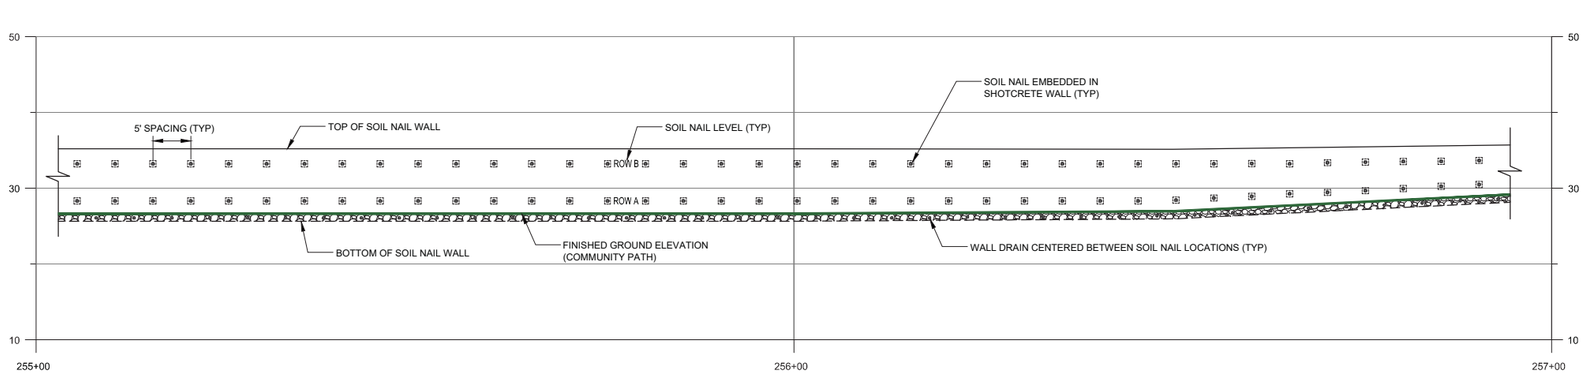

CRIB WALL REPLACEMENT - TYPICAL ELEVATION

1"=10' 10' 5' 0 10'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


SOIL NAIL WALL &
CRIB WALL REPLACEMENT
TYPICAL ELEVATIONS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DL	STS	RJP	SHEET: S-007	

PLOTTED: 09/22/17 11:42AM BY:DEBORAH.LANDI
DRAWING: \\GZANOR2\RFP\2018\01.P0006118RJP\FIGURES\CAD\GZA-SEC DET-RW-MW-10-PROPOSAL.DWG [S-007] 09/22/17 11:39AM

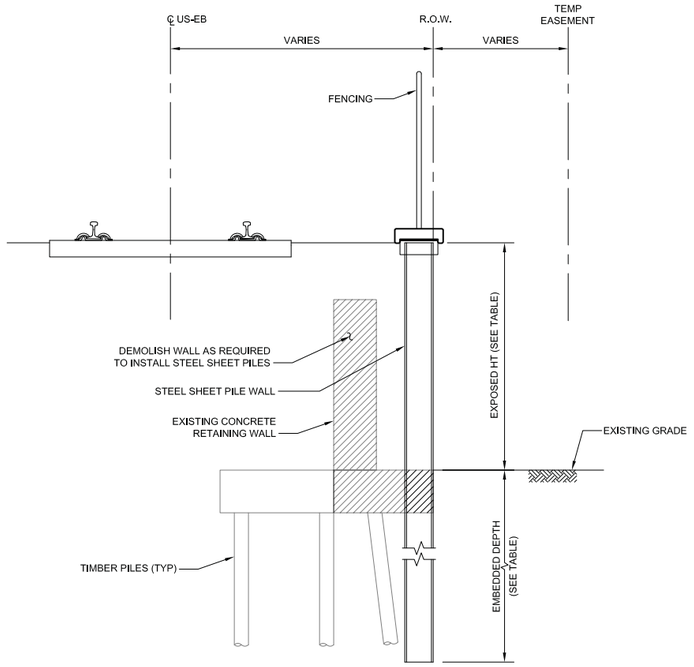

SHEET PILE RETAINING WALL

3/8"=1'-0" 0 2' 4' 6'

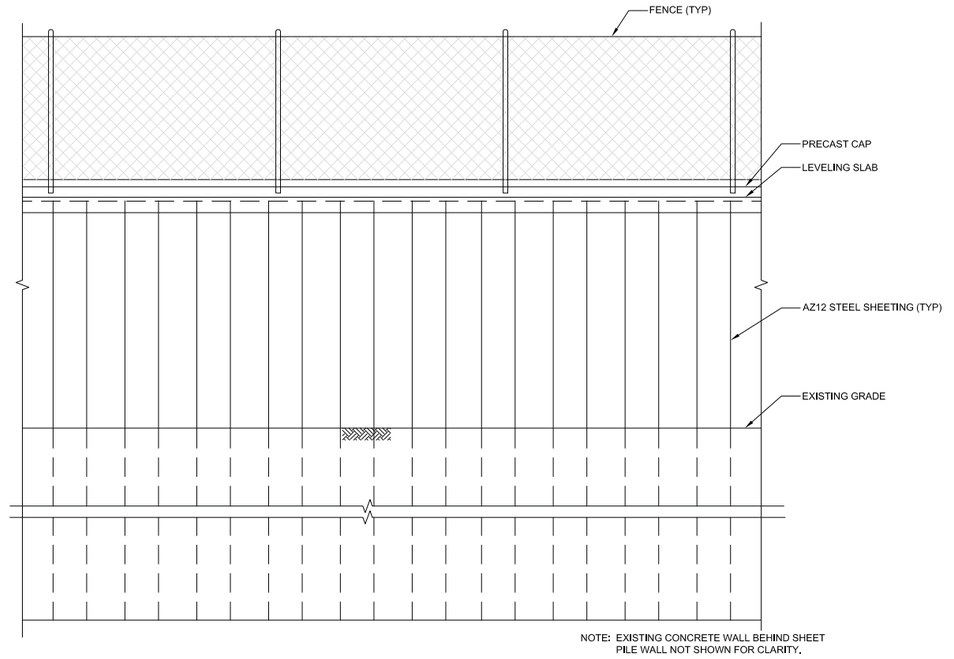


NOTE: EXISTING CONCRETE WALL BEHIND SHEET PILE WALL NOT SHOWN FOR CLARITY.

SHEET PILE RETAINING WALL ELEVATION

3/8"=1'-0" 0 2' 4' 6'

NOTES:

1. STEEL SHEETS SHALL BE GRADE 50, HOT DIPPED GALVANIZED.
2. PRECAST CONCRETE.
3. CAST IN PLACE CONCRETE
4. REINFORCING STEEL.
5. AVERAGE EMBEDMENT DEPTH REQUIRED SHOWN. EXISTING TIMBER PILES WILL INTERFERE WITH STEEL SHEETS SO ACTUAL LENGTHS WILL NEED TO BE ADJUSTED ACCORDINGLY.



PRECAST CAP DETAIL

3/4"=1'-0" 0 1' 2' 3'

SHEET PILE RETAINING WALL TABLE						
WALL	STATION (UNION SQUARE BRANCH)		EXPOSED HT (FT)	AVERAGE EMBEDMENT DEPTH (FT)	STEEL SHEET SIZE	NOTES
	START	END				
UN-2	28+80	31+00	9	28	AZ12	SEE NOTE 5
	31+00	34+00	4	15	AZ12	SEE NOTE 5

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


SHEET PILE WALL
ELEVATION, SECTION AND DETAILS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DH	EE	EE	SHEET: S-008	

PLOTTED: 09/22/17 2:18PM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\RETAINING WALLS-NOISE WALLS_PROPOSAL DRAWINGS\S-008 SHEET PILE WALL.DWG [LAYOUT] 09/22/17 10:14AM

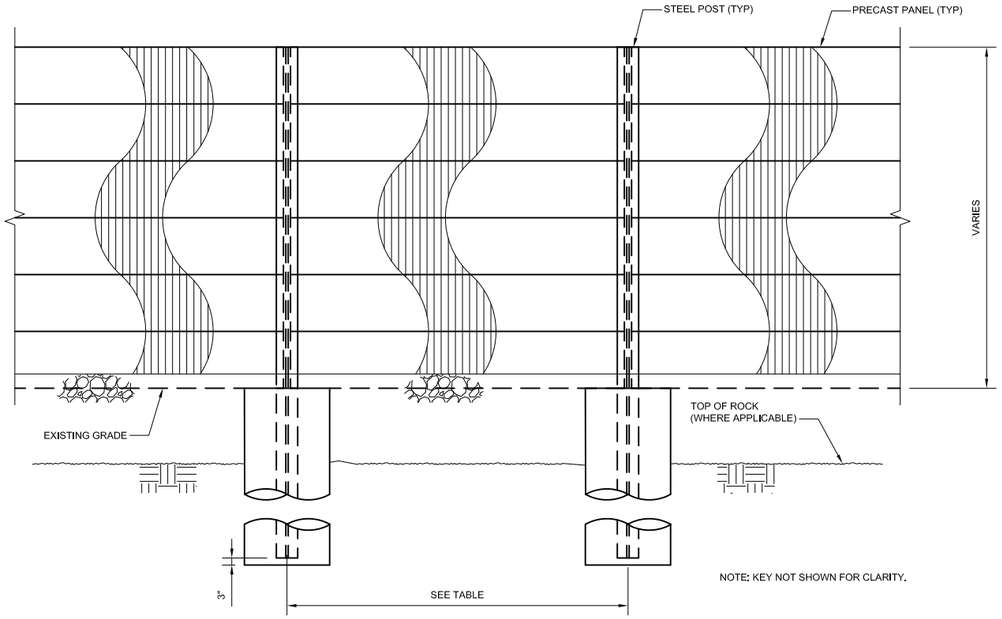

NOISE BARRIER ELEVATION

3/8"=1'-0" 0 2' 4' 6'

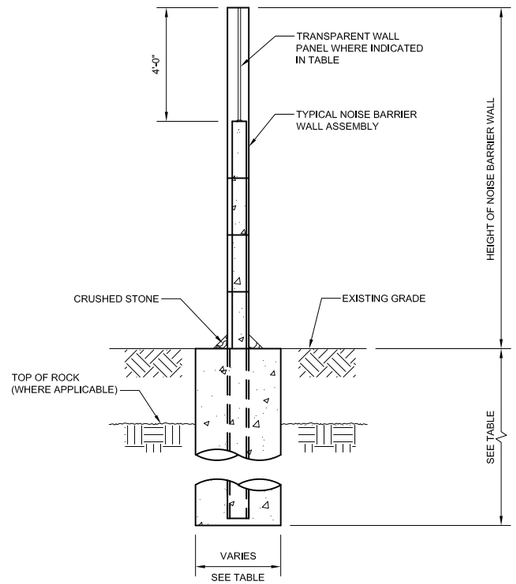


TYPICAL NOISE BARRIER WALL

3/8"=1'-0" 0 2' 4' 6'

NOTES:

1. CIP CONCRETE SHALL BE F'c = 4,000 psi.
2. PRECAST CONCRETE SHALL BE 5,000 psi.
3. ALL STRUCTURAL STEEL SHALL BE ASTM A572, A709 OR A992 GRADE 50 HOT DIPPED GALVANIZED.
4. REINFORCING STEEL SHALL BE ASTM A615 GRADE 60.
5. CONCRETE PANELS SHALL BE COATED WITH CONCRETE SEALER.
6. ABSORPTIVE TREATMENT SHALL HAVE A MINIMUM NOISE REDUCTION COEFFICIENT RATING OF 0.7 OR GREATER.
7. NOISE BARRIERS SHALL HAVE A SOUND TRANSMISSION CLASS RATING OF 30 OR GREATER.




DETAIL

3"=1'-0" 0 3" 6" 9"

NOISE BARRIER TABLE

BARRIER	STATION START	STATION END	OFFSET (FT)	PILE SIZE	PILE SPACING (FT)	SHAFT DIAMETER (FT)	EXPOSED FACE (FT)	PILE LENGTH (FT)	SOIL EMBEDMENT (FT)	ROCK SOCKET (FT)	ABSORPTIVE TREATMENT	STRENGTH RATIO	DEFLECTION RATIO	NOTES
N-1A	192+74	195+53	8	W8x35	12	-	12	12	-	-	BOTH SIDES	0.41	0.34	MOUNTED ON VIADUCT/MSE WALL
N-1B	192+25	199+00	10.2	W8x35	12	-	13	13	-	-	TRACK SIDE	0.48	0.44	MOUNTED ON VIADUCT/MSE WALL
N-2A	211+53	218+91	10.3	W8x35	12	-	8	8	-	-	TRACK SIDE	0.18	0.10	MOUNTED ON VIADUCT/MSE WALL
N-2B	039+80	215+00	12	W8x35	12	1.5	10	20	10	-	TRACK SIDE	0.63	0.26	
	215+00	218+12	12	W8x35	12	1.5	8	17	9	-	TRACK SIDE	0.43	0.13	
N-3A	012+32	018+68	11 TO 8	W12x40	12	2	12	24	12	-	TRACK SIDE	0.82	0.14	DESIGNED FOR VEHICLE IMPACT. TOP 4 FT. IS ACRYLIC PANELS.
N-3B	005+84	011+48	16 TO 8	W12x40	12	2	12	24	12	-	BOTH SIDES	0.82	0.14	DESIGNED FOR VEHICLE IMPACT. TOP 4 FT. IS ACRYLIC PANELS.
N-6	254+03	254+50	67 TO 47	W12x50	12	2	16	35	19	-	TRACK SIDE	0.84	0.34	
	254+50	256+00	67 TO 47	W10x45	12	2	14	32	13	5	TRACK SIDE	0.87	0.36	
	256+00	256+50	67 TO 47	W12x53	12	2	17	32	15	-	TRACK SIDE	0.89	0.38	
	256+50	257+00	67 TO 47	W12x65	12	2	19	35	16	-	TRACK SIDE	0.84	0.42	
	257+00	262+00	67 TO 47	W12x58	12	2	18	33	15	-	TRACK SIDE	0.87	0.40	
	262+00	262+32	67 TO 47	W12x65	12	2	16	33	17	-	TRACK SIDE	0.87	0.25	
N-7	276+29	279+00	45 TO 48	W12x40	12	2	14	26	7	5	TRACK SIDE	0.69	0.29	
	279+00	280+50	45 TO 48	W8x35	12	1.5	12	23	6	5	TRACK SIDE	0.87	0.45	
	280+50	282+00	45 TO 48	W8x35	12	1.5	10	20	5	5	TRACK SIDE	0.63	0.26	
	282+00	284+00	45 TO 48	W8x35	12	1.5	8	17	9	-	TRACK SIDE	0.28	0.13	
	284+00	284+64	45 TO 48	W8x35	12	1.5	10	20	10	-	TRACK SIDE	0.63	0.26	
N-9A	298+06	301+11	41	W12x50	12	2	18	31	8	5	TRACK SIDE	0.87	0.49	
N-9B	300+48	303+50	73 TO 41	W12x58	12	2	18	39	11	10	TRACK SIDE	0.88	0.40	
	303+50	304+34	73 TO 41	W12x72	12	2	20	42	12	10	TRACK SIDE	0.84	0.44	
N-10	305+35	306+00	44 TO 41	W8x35	12	1.5	8	24	16	-	TRACK SIDE	0.47	0.13	
	306+00	308+50	44 TO 41	W12x45	12	2	15	33	18	-	TRACK SIDE	0.81	0.32	
	308+50	309+63	39 TO 51	W8x35	12	1.5	10	23	13	-	TRACK SIDE	0.72	0.26	
	309+63	313+00	39 TO 51	W21x44	8	-	10	-	-	-	TRACK SIDE	-	-	MOUNTED ON RETAINING WALL
	313+00	314+50	39 TO 51	W24x58	8	-	8	-	-	-	TRACK SIDE	-	-	MOUNTED ON RETAINING WALL
N-11	320+22	321+09	40.5 TO 49	W8x35	12	1.5	10	30	20	-	TRACK SIDE	0.70	0.26	
N-12	321+55	324+85	43.5	W10x33	12	2	12	26	14	-	TRACK SIDE	0.88	0.33	
N-14A	330+39	332+21	42	W12x40	12	2	16	28	12	-	TRACK SIDE	0.87	0.44	
N-14B	333+62	336+00	38	W12x45	12	2	17	29	12	-	TRACK SIDE	0.87	0.46	
	336+00	336+29	38	W12x40	12	2	15	27	12	-	TRACK SIDE	0.77	0.36	
N-15	223+1	225+50	48 TO 56	W21x48	8	-	8	-	-	-	TRACK SIDE	-	-	MOUNTED ON RETAINING WALL
	225+50	227+00	55 TO 47	W24x55	8	-	10	-	-	-	TRACK SIDE	-	-	MOUNTED ON RETAINING WALL
	227+00	231+05	47 TO 53	W21x44	8	-	8	-	-	-	TRACK SIDE	-	-	MOUNTED ON RETAINING WALL
	231+05	235+42	47 TO 53	W8x35	12	1.5	8	21	13	-	TRACK SIDE	0.53	0.13	
N-17	037+23	041+94	14 TO 11	W12x40	12	2	16	28	12	-	TRACK SIDE	0.87	0.44	

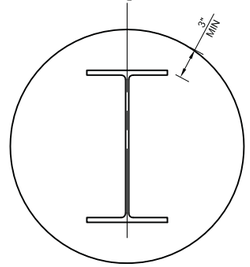

SECTION - POST WITH DRILLED SHAFT

1"=1'-0" 0 1' 2'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


NOISE BARRIER ELEVATION, SECTION AND DETAILS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-272.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DH	EE	EE	SHEET: S-009	

PLOTTED: 09/22/17 2:18PM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\RETAINING WALLS-NOISE WALLS_PROPOSAL DRAWINGS\S-009 NOISE BARRIER WALL DETAILS.DWG [LAYOUT] 09/22/17

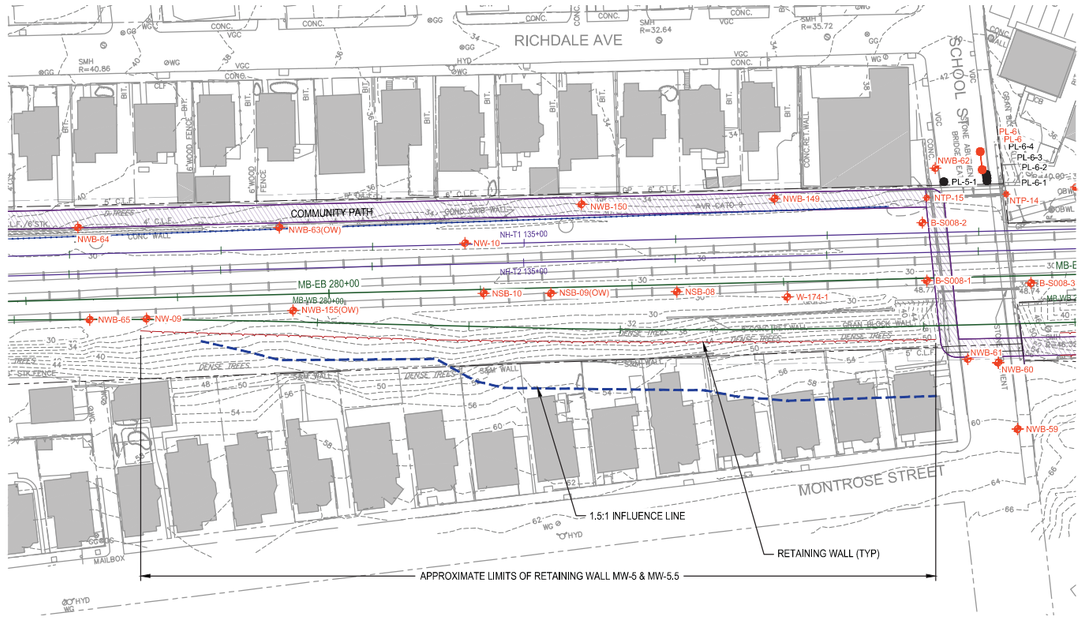


PLAN

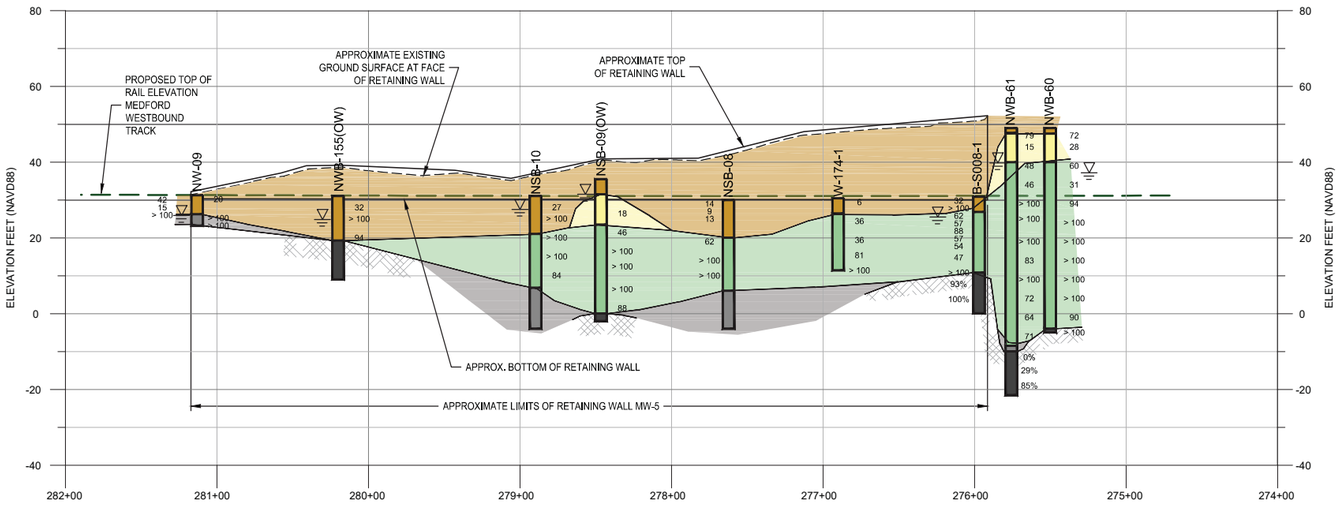

SUBSURFACE PROFILE - MEDFORD WESTBOUND TRACK

LEGEND

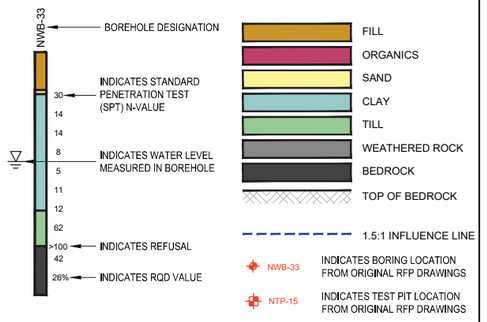

VERTICAL SCALE IN FEET
0 10' 20' 40' 60'
0 25' 50' 100' 300'
HORIZONTAL SCALE IN FEET

NOTES:

1. EXISTING GROUND PROFILE DEVELOPED FROM CONTOURS PROVIDED IN EXISTING BASE MAP DRAWING FILE ISSUED WITH RFP DOCUMENTS.
2. SUBSURFACE INFORMATION INCLUDING GROUNDWATER ELEVATIONS ARE BASED ON BORINGS PROVIDED IN THE RFP DOCUMENTS. BORINGS OBSERVED BY OTHERS.
3. BORING LOCATIONS AND SUBSURFACE INFORMATION SHOULD BE CONSIDERED APPROXIMATE.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


RETAINING WALL MW-5
PLAN & SUBSURFACE PROFILE

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-272.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DL	STS	RJP	SHEET: S-010	

PLOTTED: 09/22/17 9:58AM BY:DEBORAH LANDI
DRAWING: \\GZANOR2\RFP\2018\01.P000061:18RJP\FIGURES\CAD\GZA-PROFILE-RW-PROPOSAL.DWG [S-010] 09/22/17 9:57AM

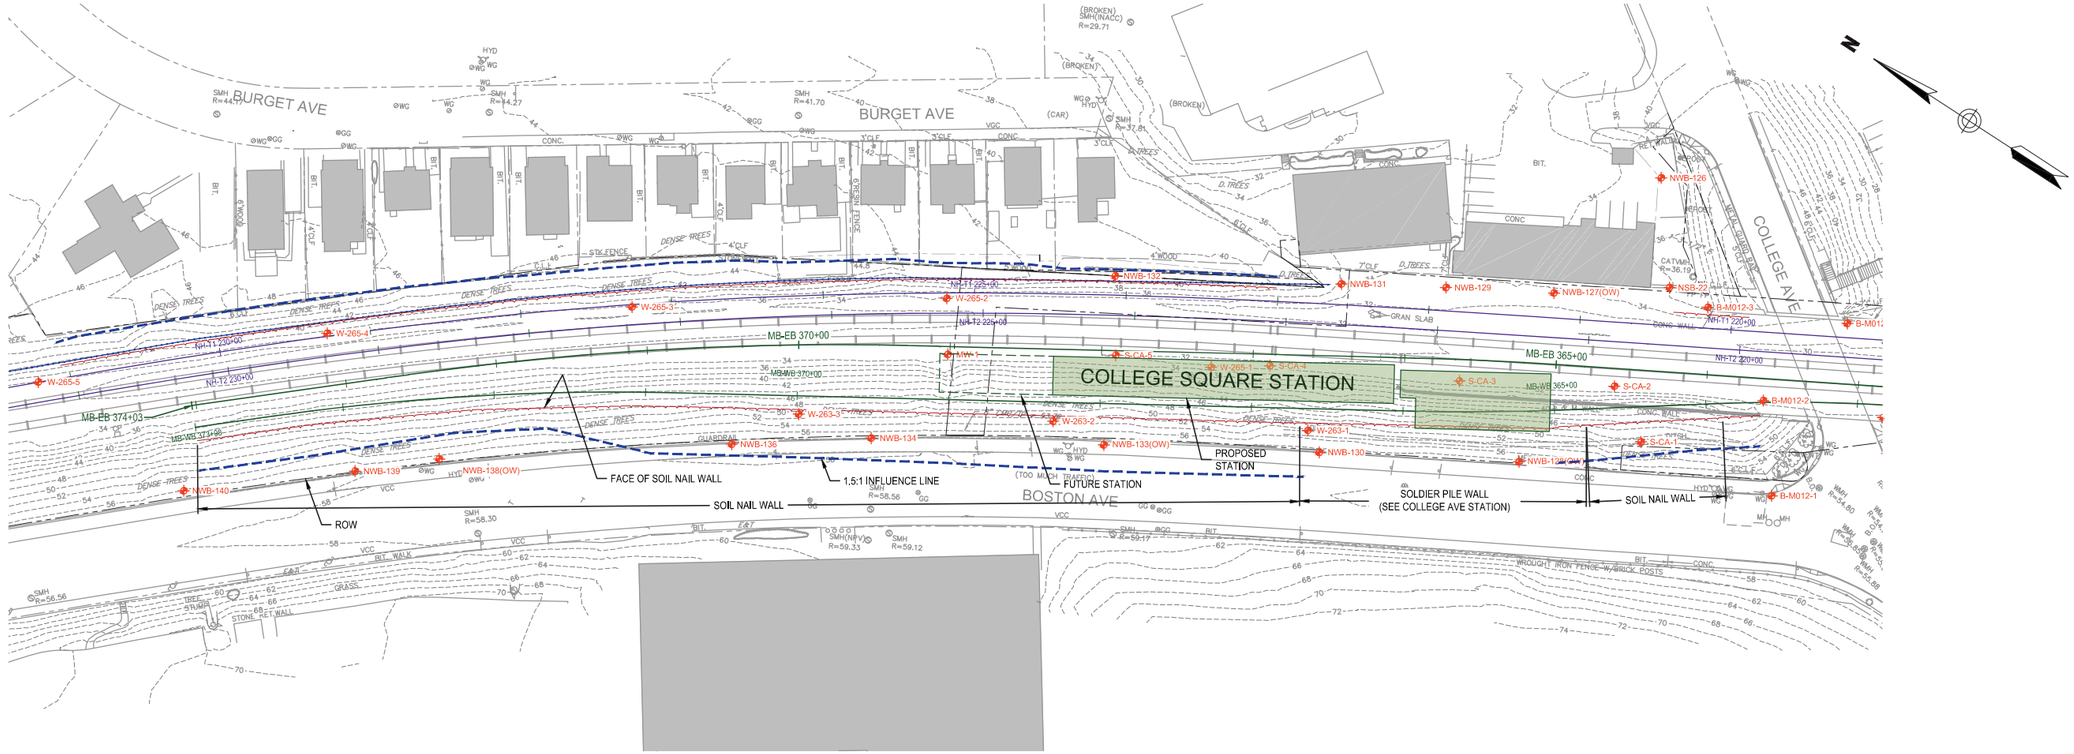

PLAN

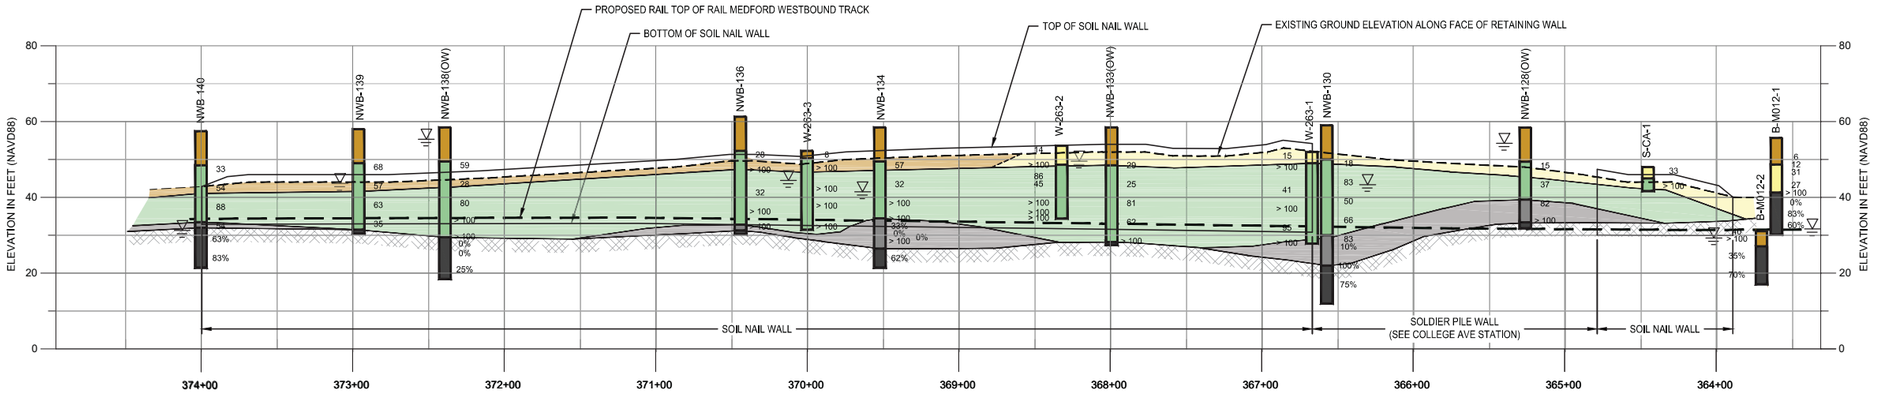

SUBSURFACE PROFILE - MEDFORD WESTBOUND TRACK

LEGEND

- BOREHOLE DESIGNATION
- INDICATES STANDARD PENETRATION TEST (SPT) N-VALUE
- INDICATES WATER LEVEL MEASURED IN BOREHOLE
- INDICATES REFUSAL
- INDICATES RQD VALUE
- FILL
- ORGANICS
- SAND
- CLAY
- TILL
- WEATHERED ROCK
- BEDROCK
- TOP OF BEDROCK
- INDICATES BORING LOCATION FROM ORIGINAL RFP DRAWINGS
- INDICATES TEST PIT LOCATION FROM ORIGINAL RFP DRAWINGS

VERTICAL SCALE IN FEET
0 10' 20' 40' 60'
HORIZONTAL SCALE IN FEET
0 25' 50' 100' 300'

NOTE:
1. EXISTING GROUND PROFILE DEVELOPED FROM CONTOURS PROVIDED IN EXISTING BASE MAP DRAWING FILE ISSUED WITH RFP DOCUMENTS.
2. SUBSURFACE INFORMATION INCLUDING GROUNDWATER ELEVATIONS ARE BASED ON BORINGS PROVIDED IN THE RFP DOCUMENTS. BORINGS OBSERVED BY OTHERS.
3. BORING LOCATIONS AND SUBSURFACE INFORMATION SHOULD BE CONSIDERED APPROXIMATE.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

RETAINING WALL MW-10
PLAN & SUBSURFACE PROFILE


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-272.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DL	STS	RJP	SHEET: S-011	


PLOTTED: 09/22/17 10:01AM BY:DEBORAH LANDI
DRAWING: \\GZANOR2\RFP\2018\01.P000061\18RJP\FIGURES\CAD\GZA-PROFILE-RW-PROPOSAL.DWG [S-011] 09/22/17 10:00AM

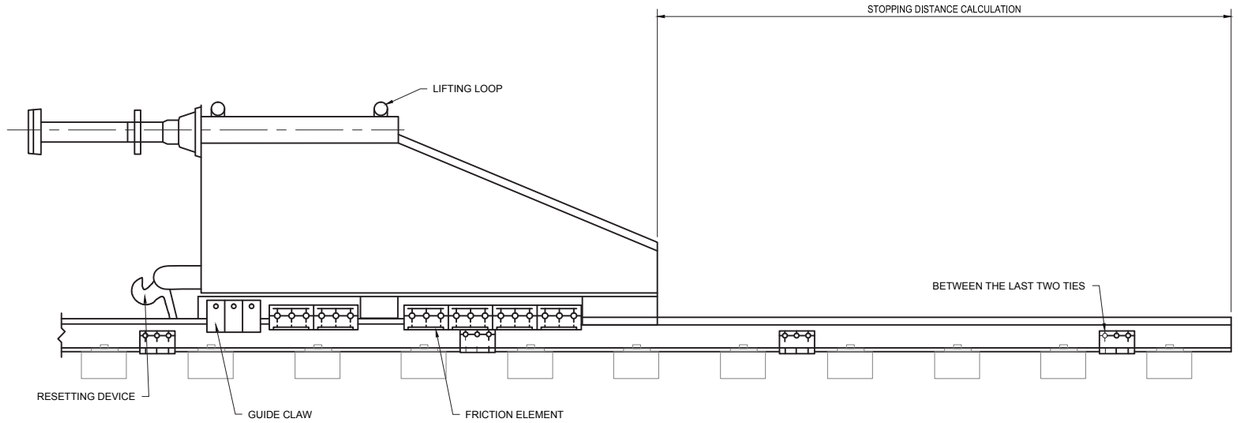

ELEVATION

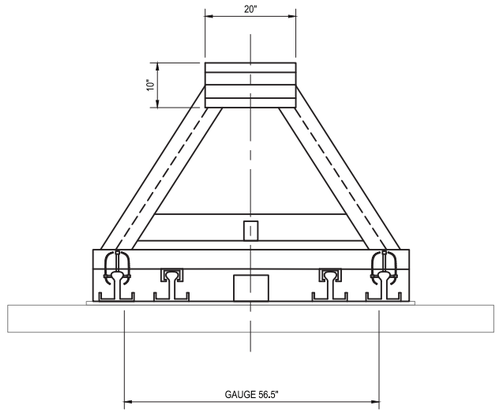

BUMPER FACE

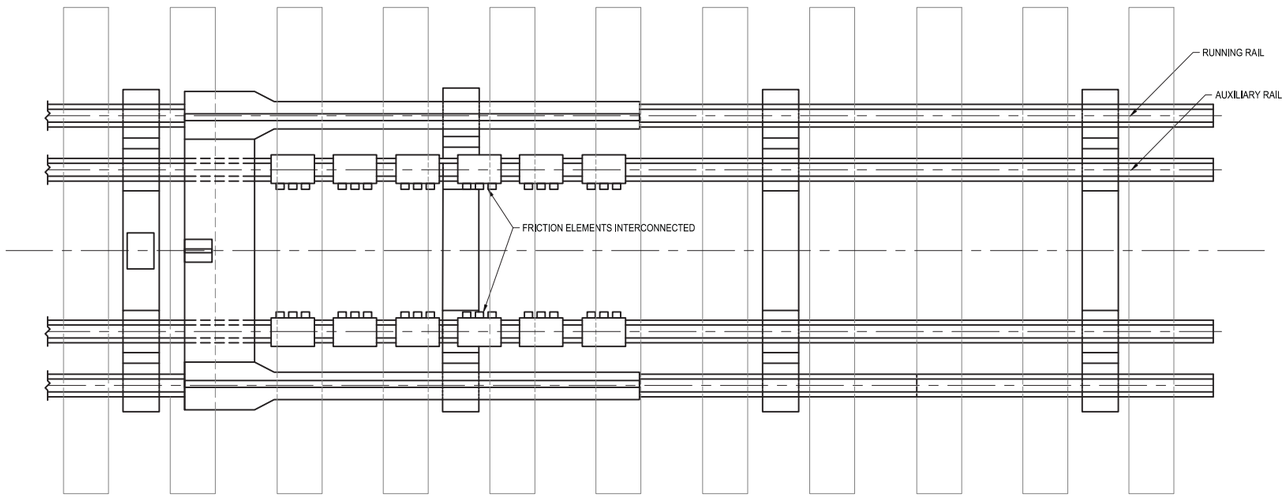

PLAN

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


BUMPING POST DETAIL

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf


SCALE: NO SCALE	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: S-012	

PLOTTED: 09/22/17 1:51PM BY:HARTD
DRAWING: L:\PROPOSALS\GLX\TECH DESIGN\RETAINING WALLS-NOISE WALLS_PROPOSAL DRAWINGS\S-012 BUMPING POST DETAILDWG [S-012] 09/22/17 9:23AM

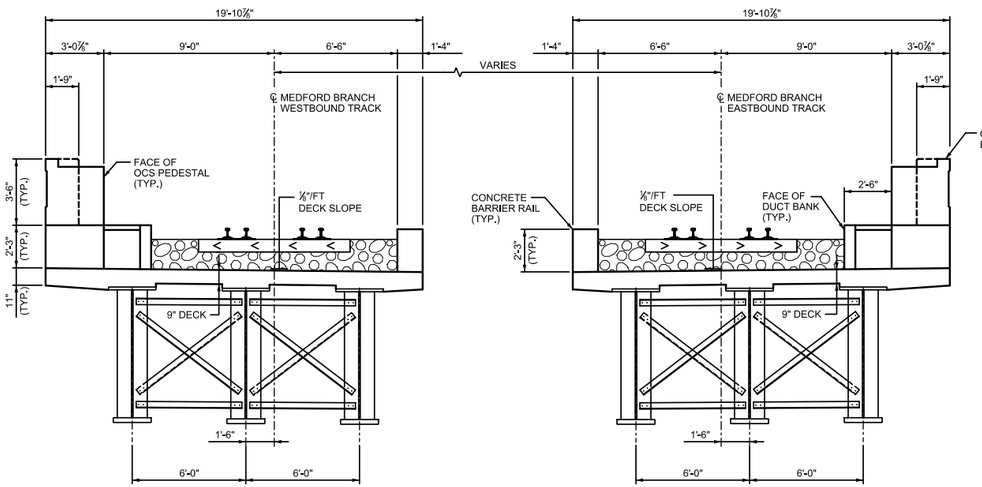

TYPICAL SECTION SPAN LEV-11


¼"=1'-0" 0 2' 4' 8'

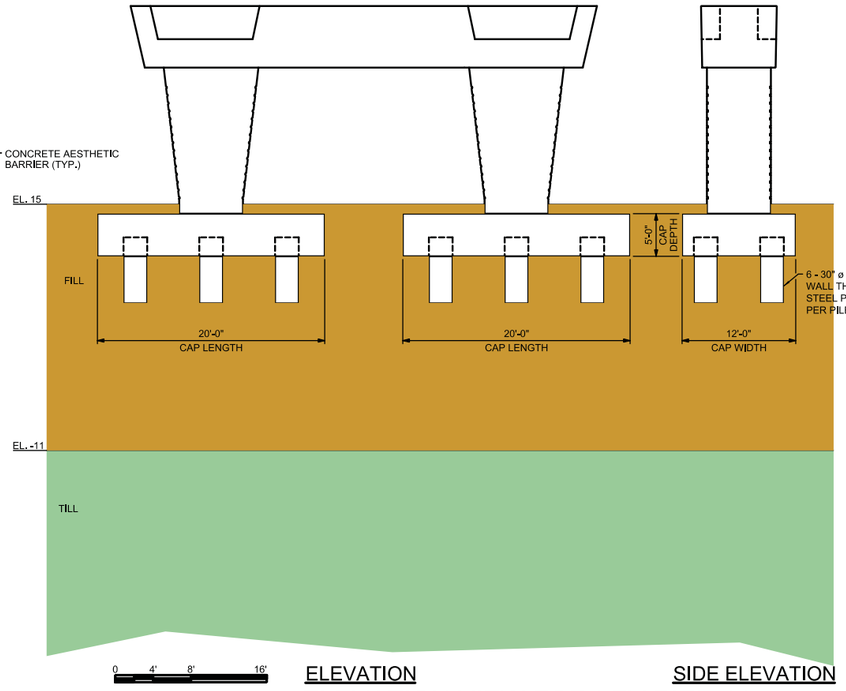

0 4' 8' 16'

ELEVATION SIDE ELEVATION

ELEVATION VIEW FOR LEV PIER 11

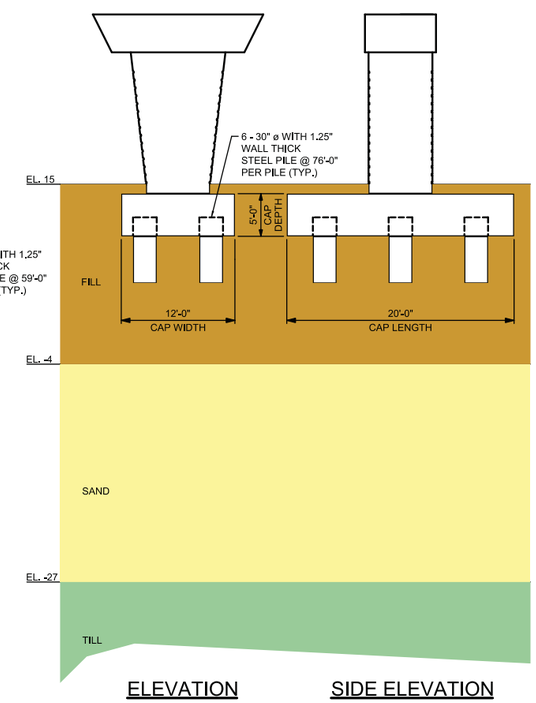


ELEVATION SIDE ELEVATION

ELEVATION VIEW FOR LEV PIER 12

0 4' 8' 16'

WORKLINE & ℄ MEDFORD BRANCH EB

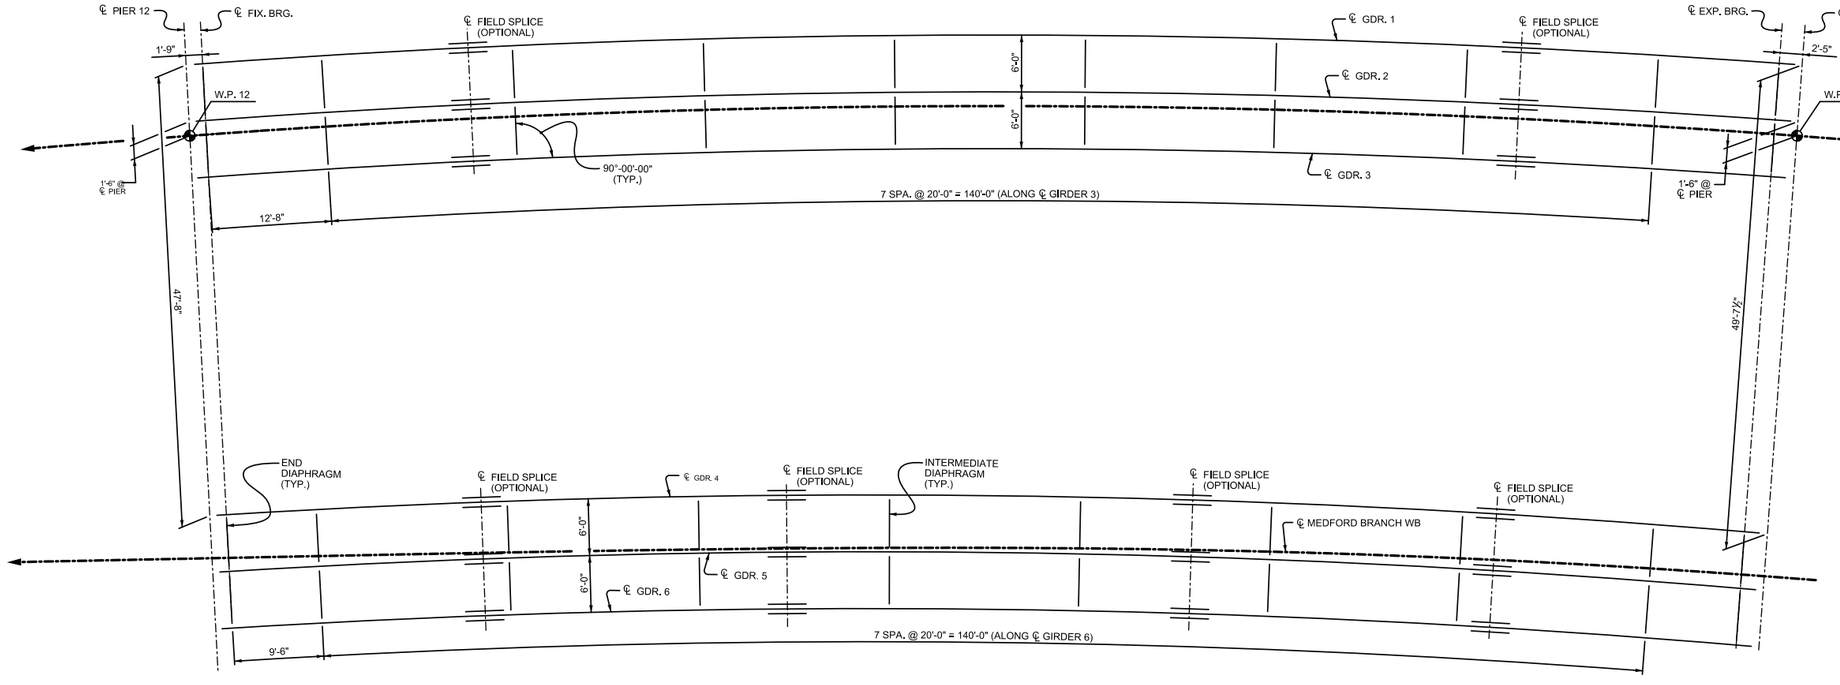

FRAMING PLAN SPAN LEV-11

1/8"=1'-0" 0 4' 8' 16'

NOTES:

1. SPAN SHOWN IS REPRESENTATIVE SPAN OF THE LECHMERE VIADUCT SPLIT SECTION.
2. STRATIGRAPHY AT PIER 11 BASED ON BORINGS NVB-68 AND NVB-12. ACTUAL CONDITIONS MAY VARY.
3. STRATIGRAPHY AT PIER 12 BASED ON BORINGS NVB-14, NVB-15, AND NVB-82. ACTUAL CONDITIONS MAY VARY.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


LECHMERE VIADUCT SPLIT FRAMING PLAN, TYPICAL SECTION, PIER ELEVATION & GEOTECH

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	ATH	NML	TBQ	SHEET: S-013	.

9/21/2017 1:23:10 PM I:\PROPOSALS\2017\GLX\Drawings\Proposal Drawings\S-017 Lechmere Viaduct Split Framing Plan, Typical Section, Pier Elevation & Geotech.dgn

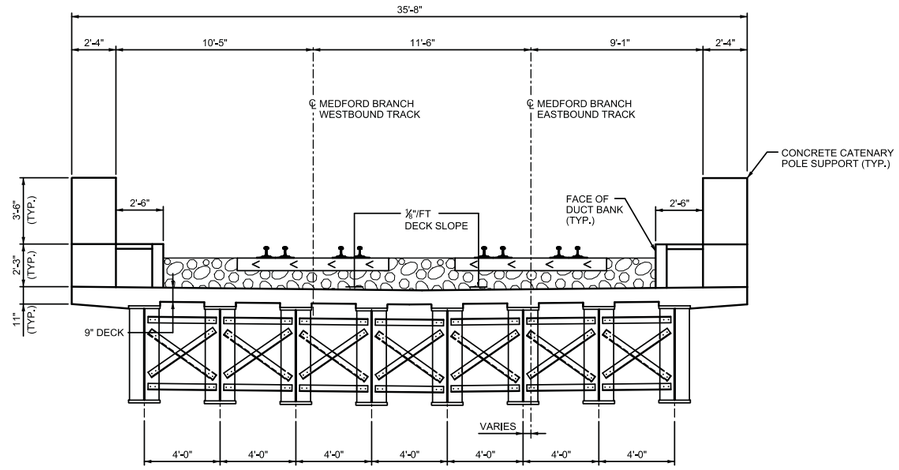

TYPICAL SECTION SPAN MBV-29


⅛"=1'-0" 0 2' 4' 8'

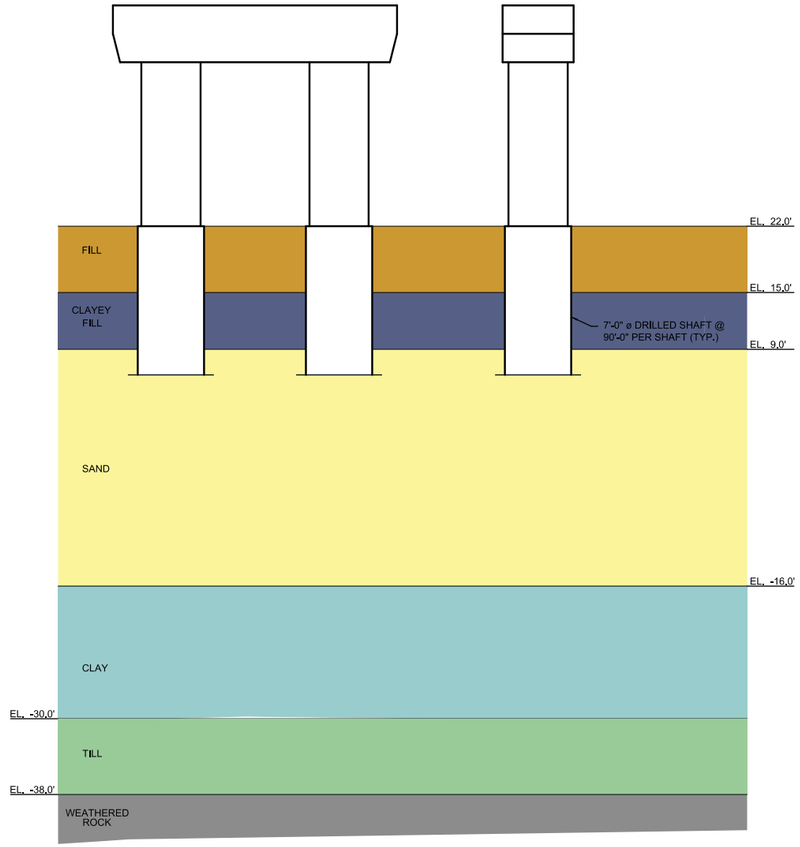

ELEVATION SIDE ELEVATION

ELEVATION VIEW FOR MBV-29

0 4' 8' 16'

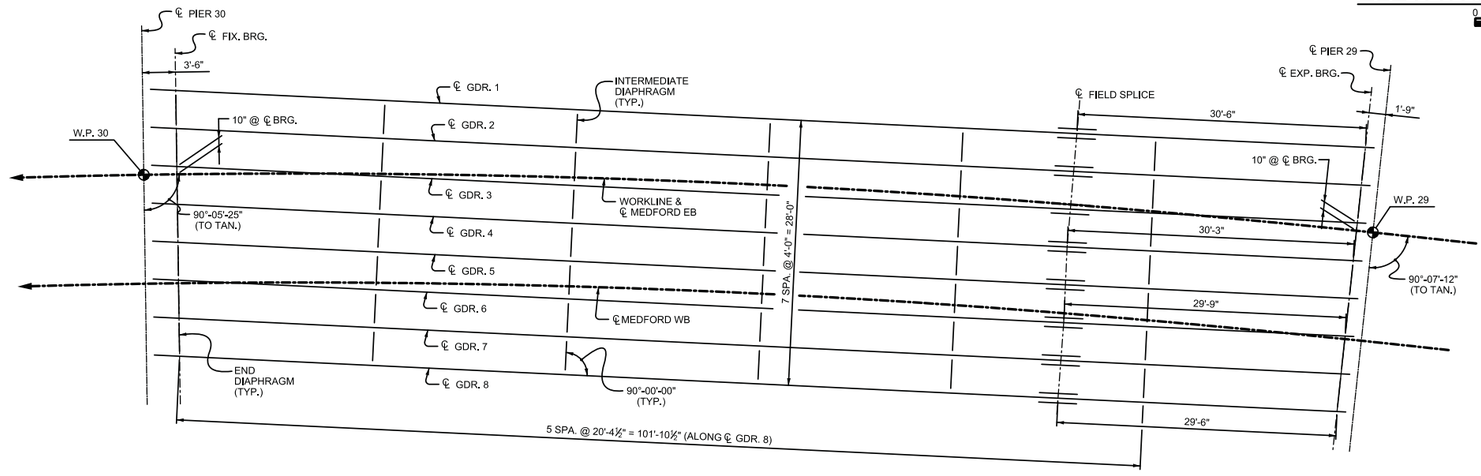

FRAMING PLAN SPAN MBV-29

⅛"=1'-0" 0 4' 8' 16'

NOTES:

1. SPAN SHOWN IS REPRESENTATIVE SPAN OF THE MEDFORD BRANCH VIADUCT SECTION.
2. STRATIGRAPHY SHOWN BASED ON BORINGS NVB-42 AND NVB-78/78A. ACTUAL CONDITIONS MAY VARY.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH VIADUCT FRAMING PLAN, TYPICAL SECTION, PIER ELEVATION & GEOTECH


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	ATH	NML	TBQ	SHEET: S-014	.

9/21/2017 1:26:18 PM I:\PROPOSALS\2017\GLX\Drawings\Proposal Drawings\S-019 Medford Branch Viaduct Framing Plan, Typical Section, Pier Elevation & Geotech.dgn

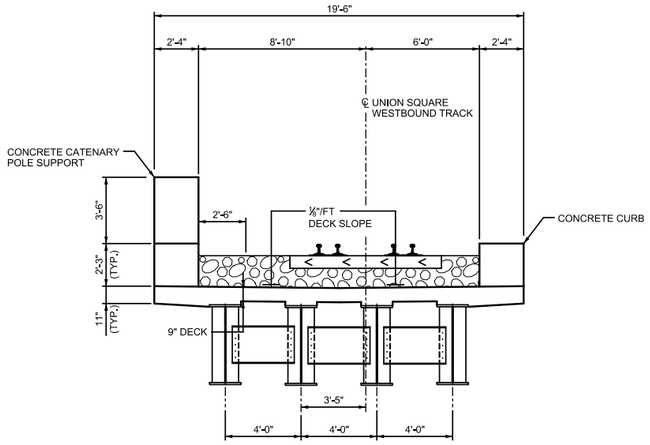

TYPICAL SECTION SPAN UWV-7


⅛"=1'-0" 0 2' 4' 8'

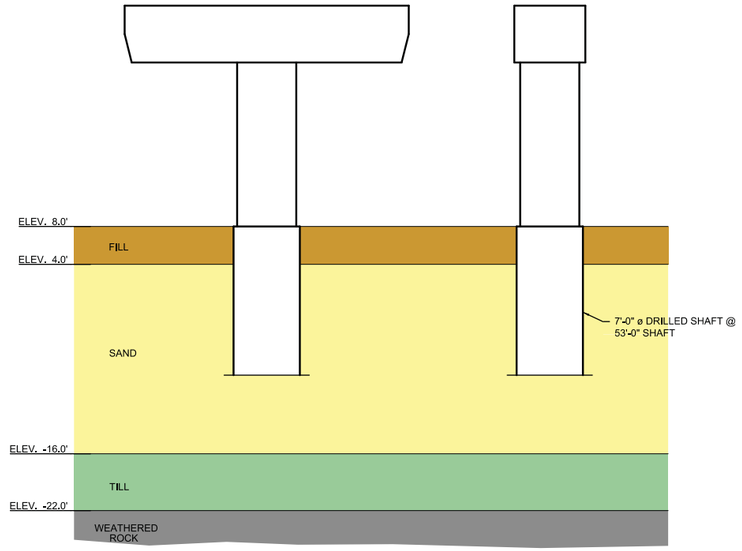

ELEVATION SIDE ELEVATION

ELEVATION VIEW FOR UWV-7


0 4' 8' 16'

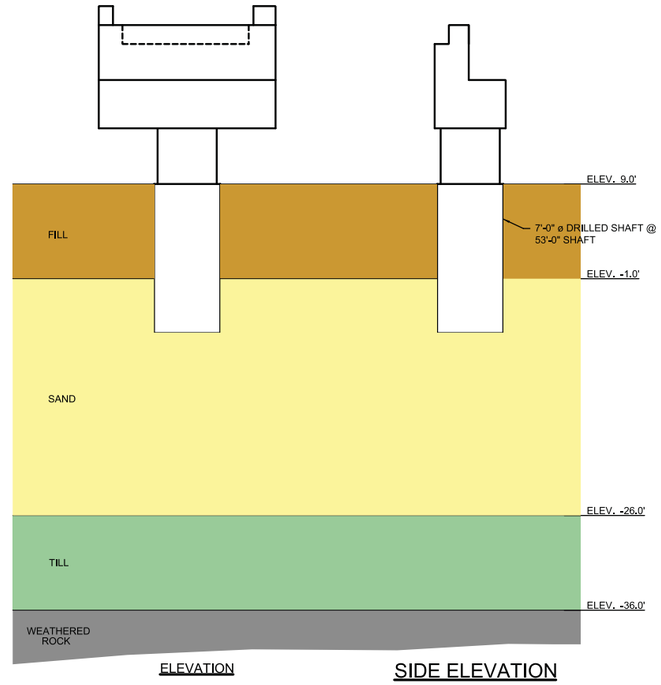

ELEVATION SIDE ELEVATION

ELEVATION VIEW FOR UWV ABUTMENT

0 4' 8' 16'

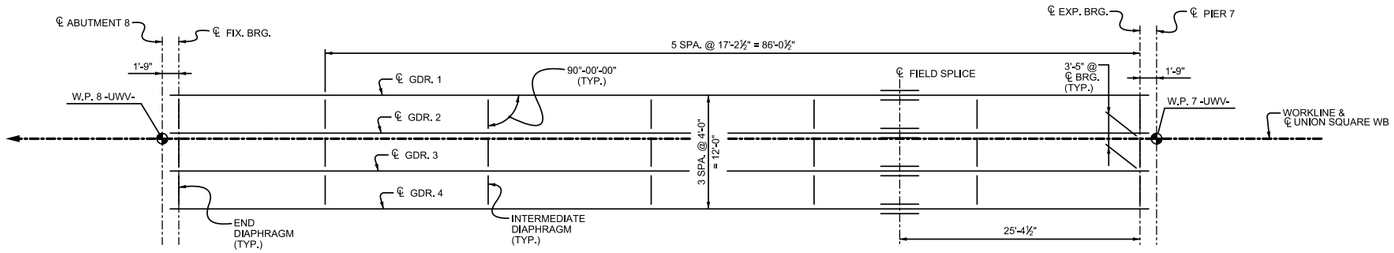



FRAMING PLAN SPAN UWV-7

⅛"=1'-0" 0 4' 8' 16'

NOTES:

1. SPAN SHOWN IS REPRESENTATIVE SPAN OF THE UNION SQUARE BRANCH VIADUCT SECTION.
2. STRATIGRAPHY AT UWV ABUTMENT BASED ON BORING W-508-2. ACTUAL CONDITIONS MAY VARY.
3. STRATIGRAPHY AT UWV-7 BASED ON BORING W-508-1. ACTUAL CONDITIONS MAY VARY.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

UNION SQUARE BRANCH VIADUCT
FRAMING PLAN, TYPICAL SECTION,
PIER ELEVATION & GEOTECH


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-272.pdf


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	ATH	NML	TBQ	SHEET: S-015	.

I:\PROPOSALS\2017\GLX\Drawings\Proposal Drawings\S-021 Union Square Broch Viaduct Framing Plan, Typical Section, Pier Elevation & Geotech.dgn
9/21/2017 1:32:16 PM

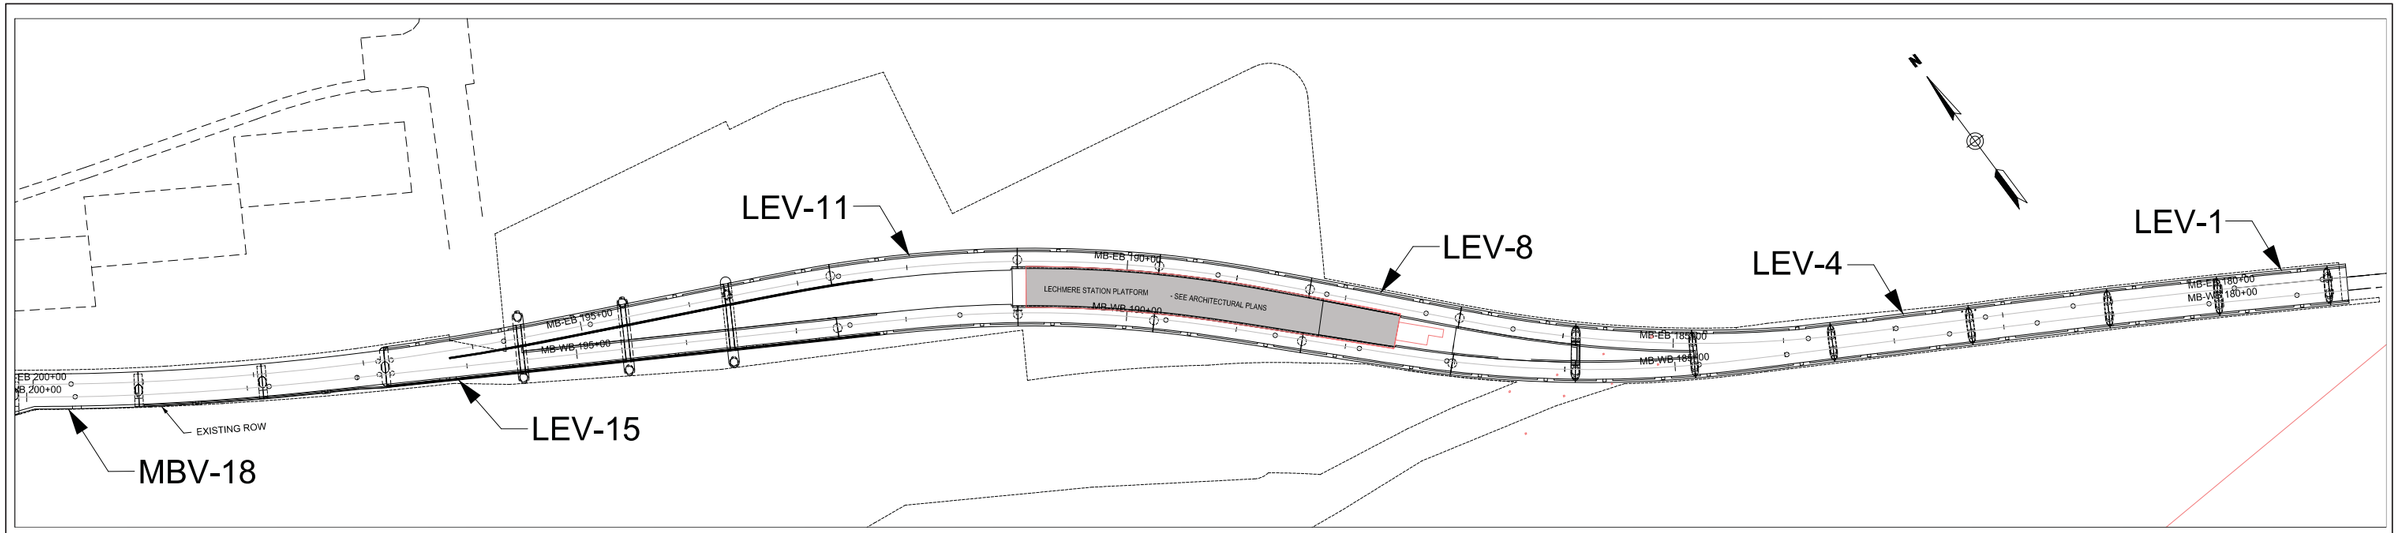

PLAN

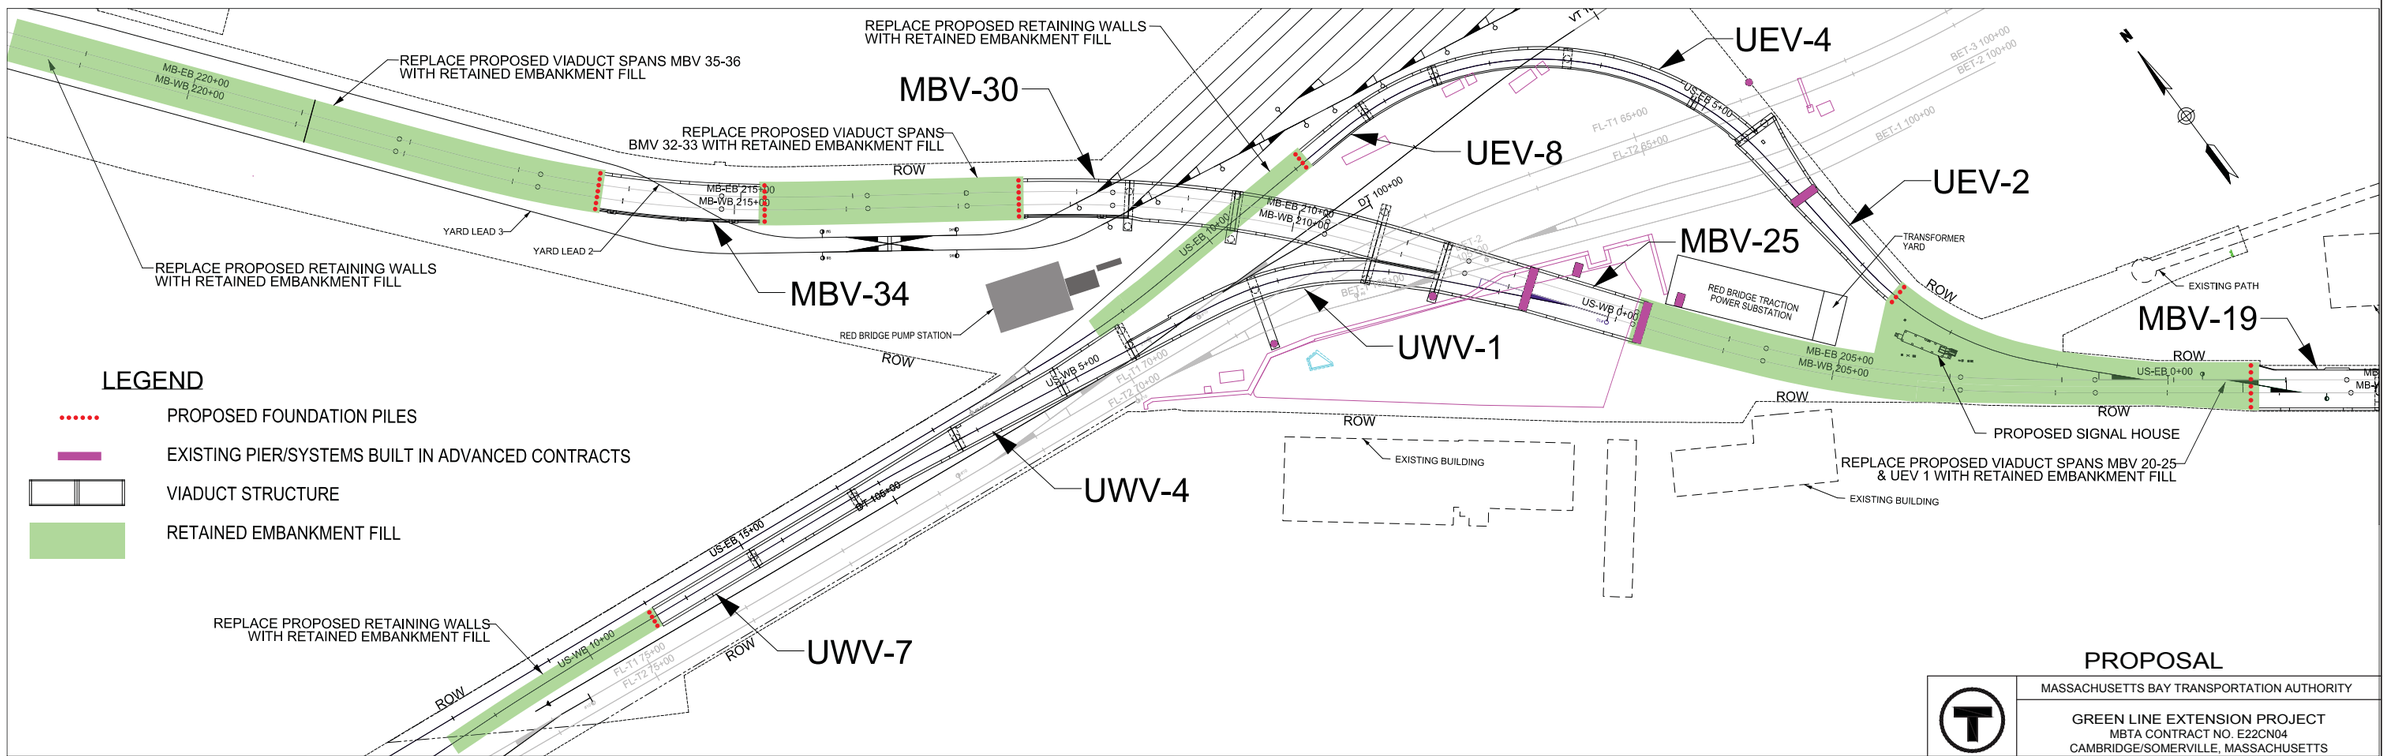

LEGEND

- PROPOSED FOUNDATION PILES
- EXISTING PIER/SYSTEMS BUILT IN ADVANCED CONTRACTS
- VIADUCT STRUCTURE
- RETAINED EMBANKMENT FILL

PLAN

VIADUCT NAMING CONVENTION

LEV-4 - LECHMERE VIADUCT SPAN 4
MBV-19 - MEDFORD VIADUCT SPAN 19
UEV-2 - UNION SQUARE EB VIADUCT SPAN 2
UWV-7 - UNION SQUARE WB VIADUCT SPAN 7

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

ATC 35 - MSE
PLAN VIEW


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-272.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: NTS	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	PJB	PJB	JM	SHEET: S-016	


PLOTTED: 09/13/17 12:00PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\ATC_MSE_PLAN_VIEWS.DWG [BASE OPTION] 09/13/17 11:59AM

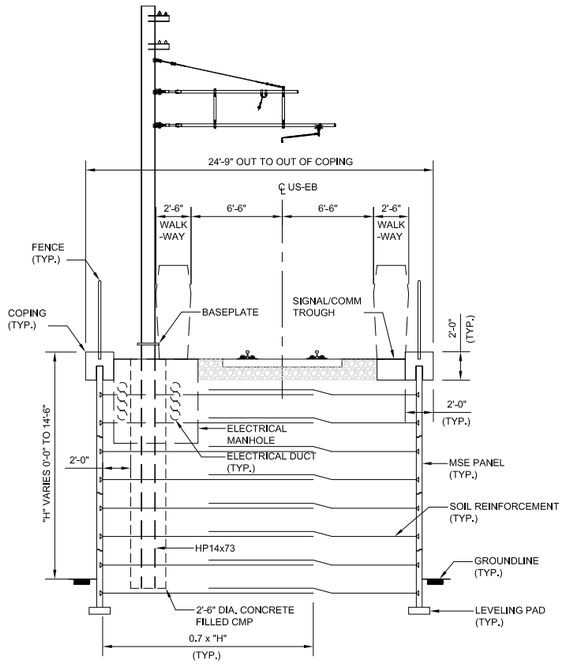

SECTION

3/16"=1'-0" 0 3' 6' 12'


SINGLE TRACK WITH OCS POLES ON FOUNDATION IN SELECT FILL
STA. 8+87 TO STA. 10+90 (US-EB)

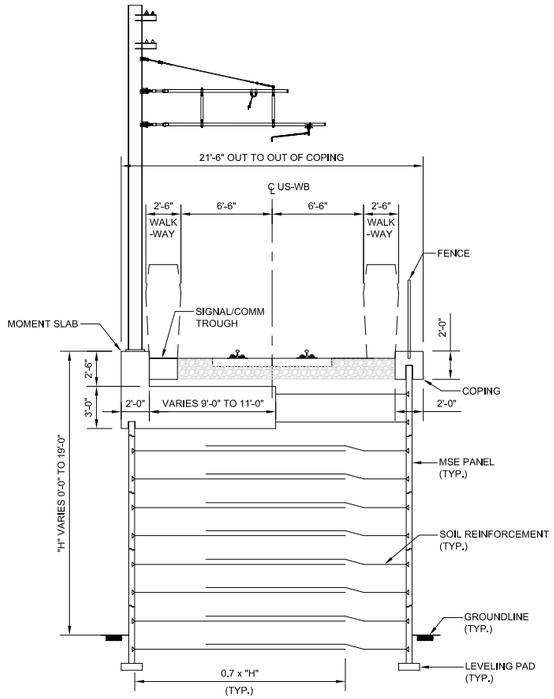

SECTION

3/16"=1'-0" 0 3' 6' 12'


SINGLE TRACK WITH OCS POLES ON MOMENT SLAB
STA. 10+90 TO STA. 11+30 (US-EB)
STA. 9+31 TO STA. 11+47 (US-WB)

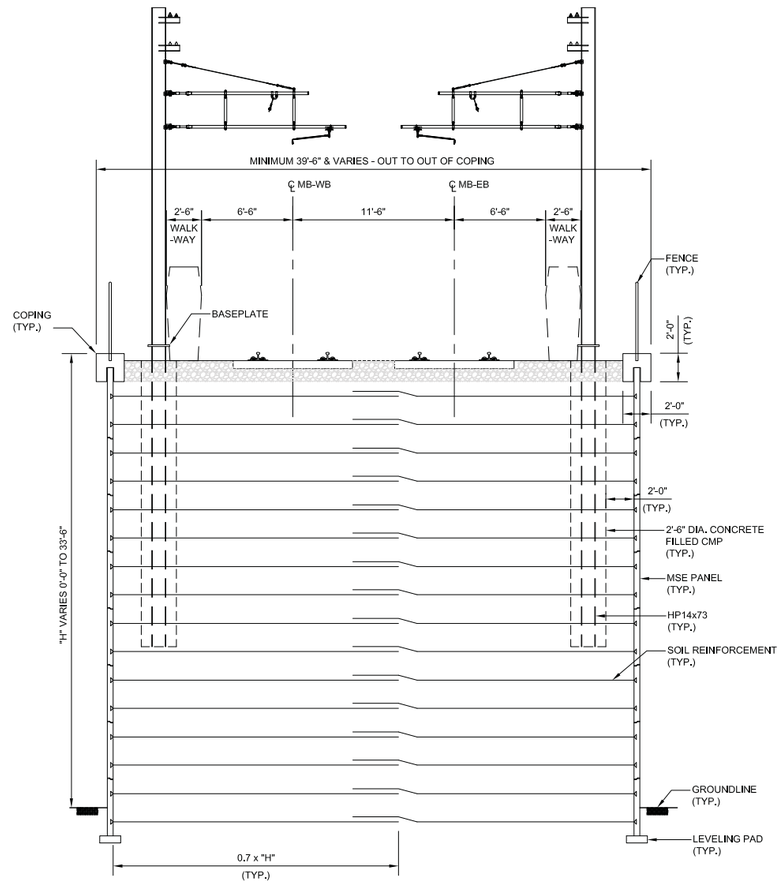

SECTION

3/16"=1'-0" 0 3' 6' 12'

DOUBLE TRACK WITH OCS POLES
STA. 204+25 TO STA. 206+86
STA. 212+48 TO STA. 214+84
STA. 216+23 TO STA. 221+68

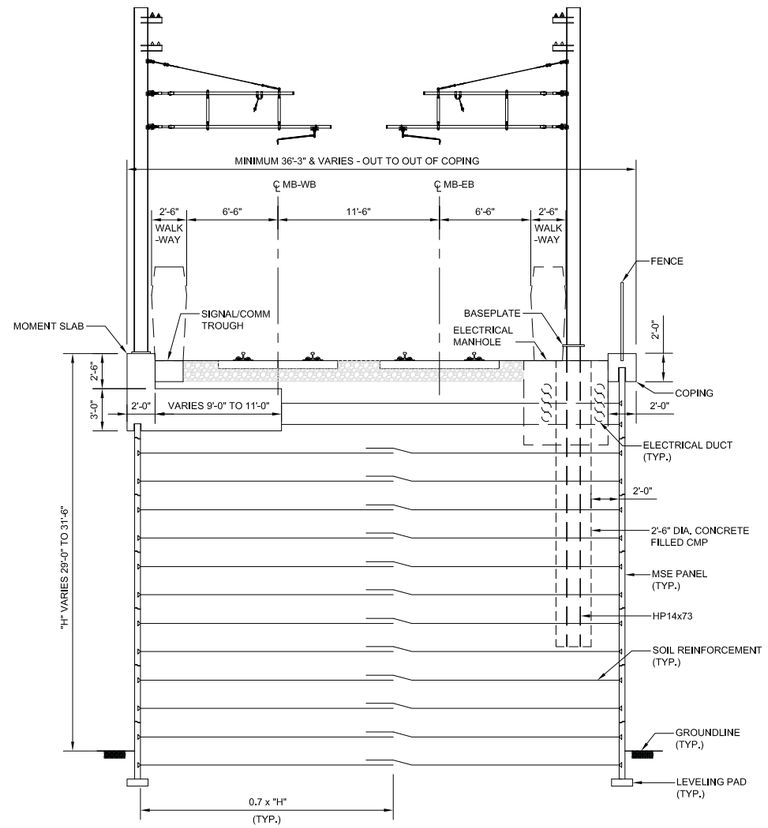

SECTION

3/16"=1'-0" 0 3' 6' 12'

DOUBLE TRACK WITH OCS POLES
STA. 201+24 TO STA. 204+25

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


ATC 35
TYPICAL SECTION

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	DM	STB	SB	SHEET: S-017	.


CV20170258.272.pdf

PLOTTED: 09/22/17 2:33PM BY:MACHALDM
DRAWING: P:\BRIDGES\GREEN LINE – BOSTON–NC\RETAINING WALLS\FROM BOSTON\17080\WSE WALL OCS POLES EXHIBIT.DWG [LAYOUT] 09/22/17 2:33PM

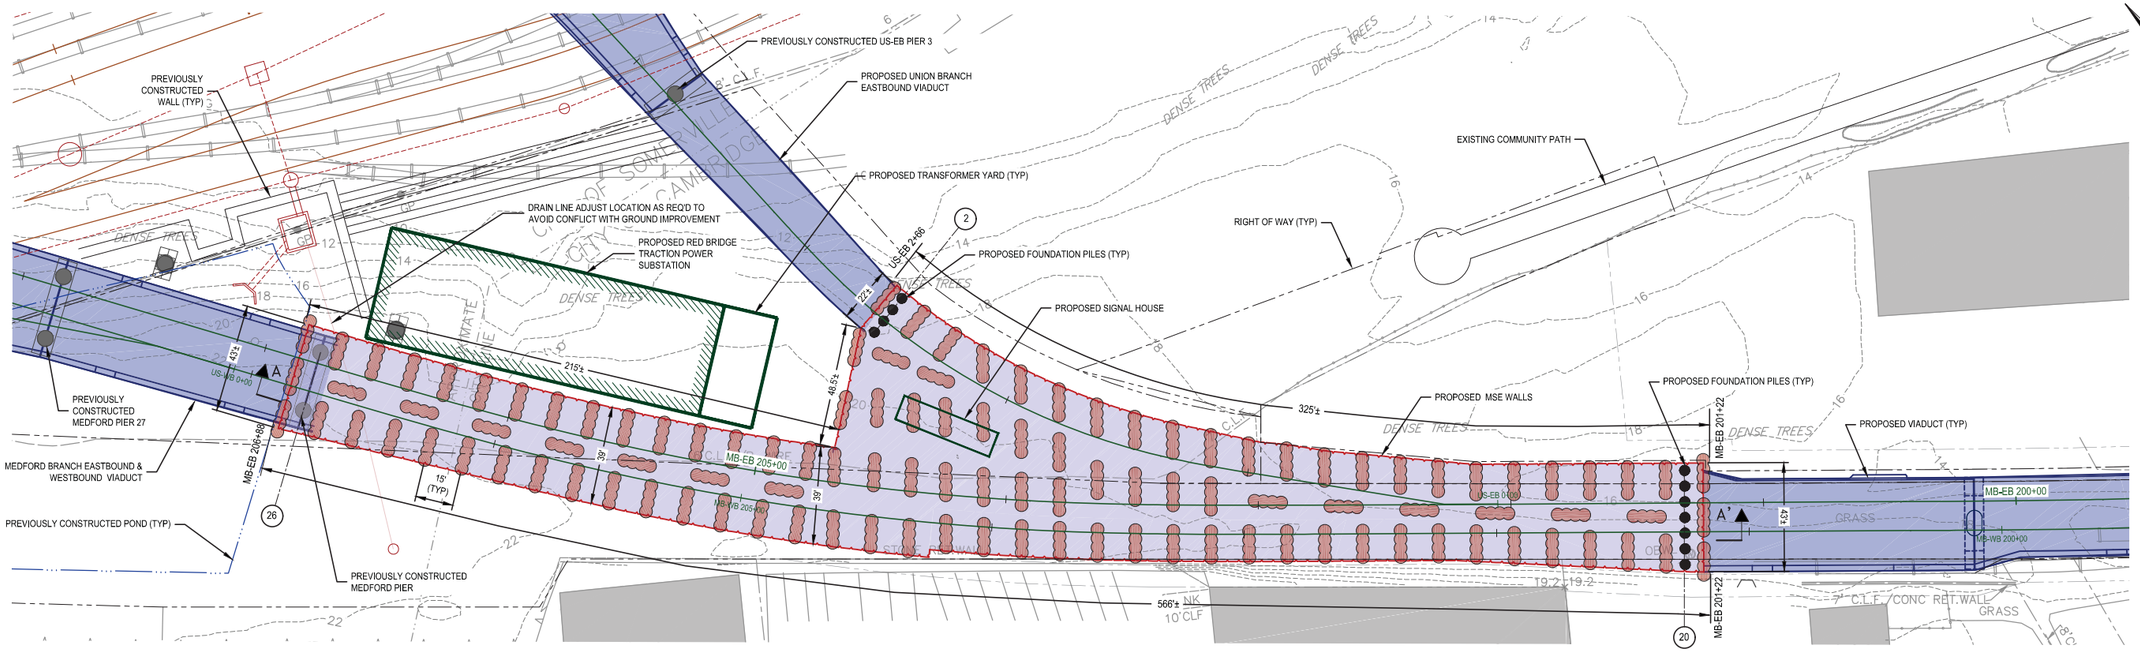


GROUND IMPROVEMENT PLAN

1"=30'

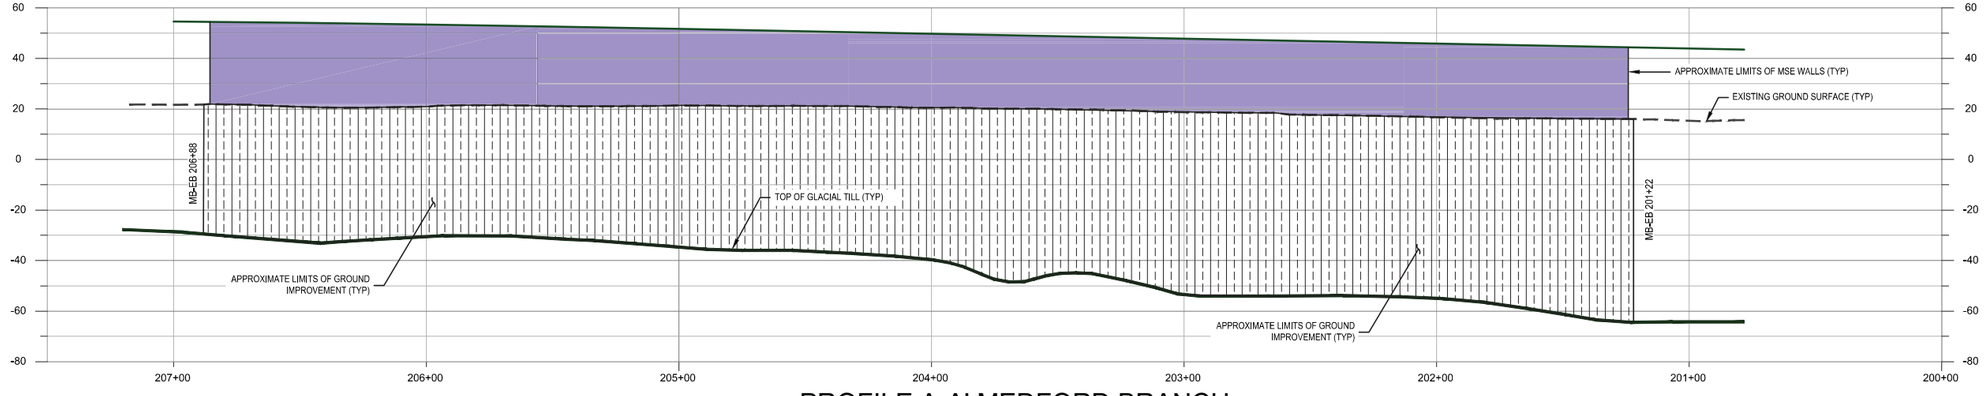

PROFILE A-A' MEDFORD BRANCH (MB-EB 200+00 TO 207+00)

1"=30'

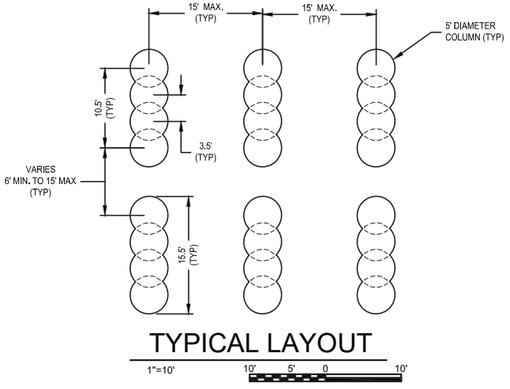

TYPICAL LAYOUT

1"=10'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


ATC 35
GROUND IMPROVEMENT
AT MSE WALLS


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-272.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DL	STS	RJP	SHEET: S-018	

PLOTTED: 09/22/17 11:44AM BY:DEBORAH.LANDI
DRAWING: \\GZANOR2\RFP\2018\01.P000061:18RJP\FIGURES\CAD\GZA-GROUND IMPROVMENT-BASE.DWG [GROUND IMPROV] 09/22/17 9:48AM

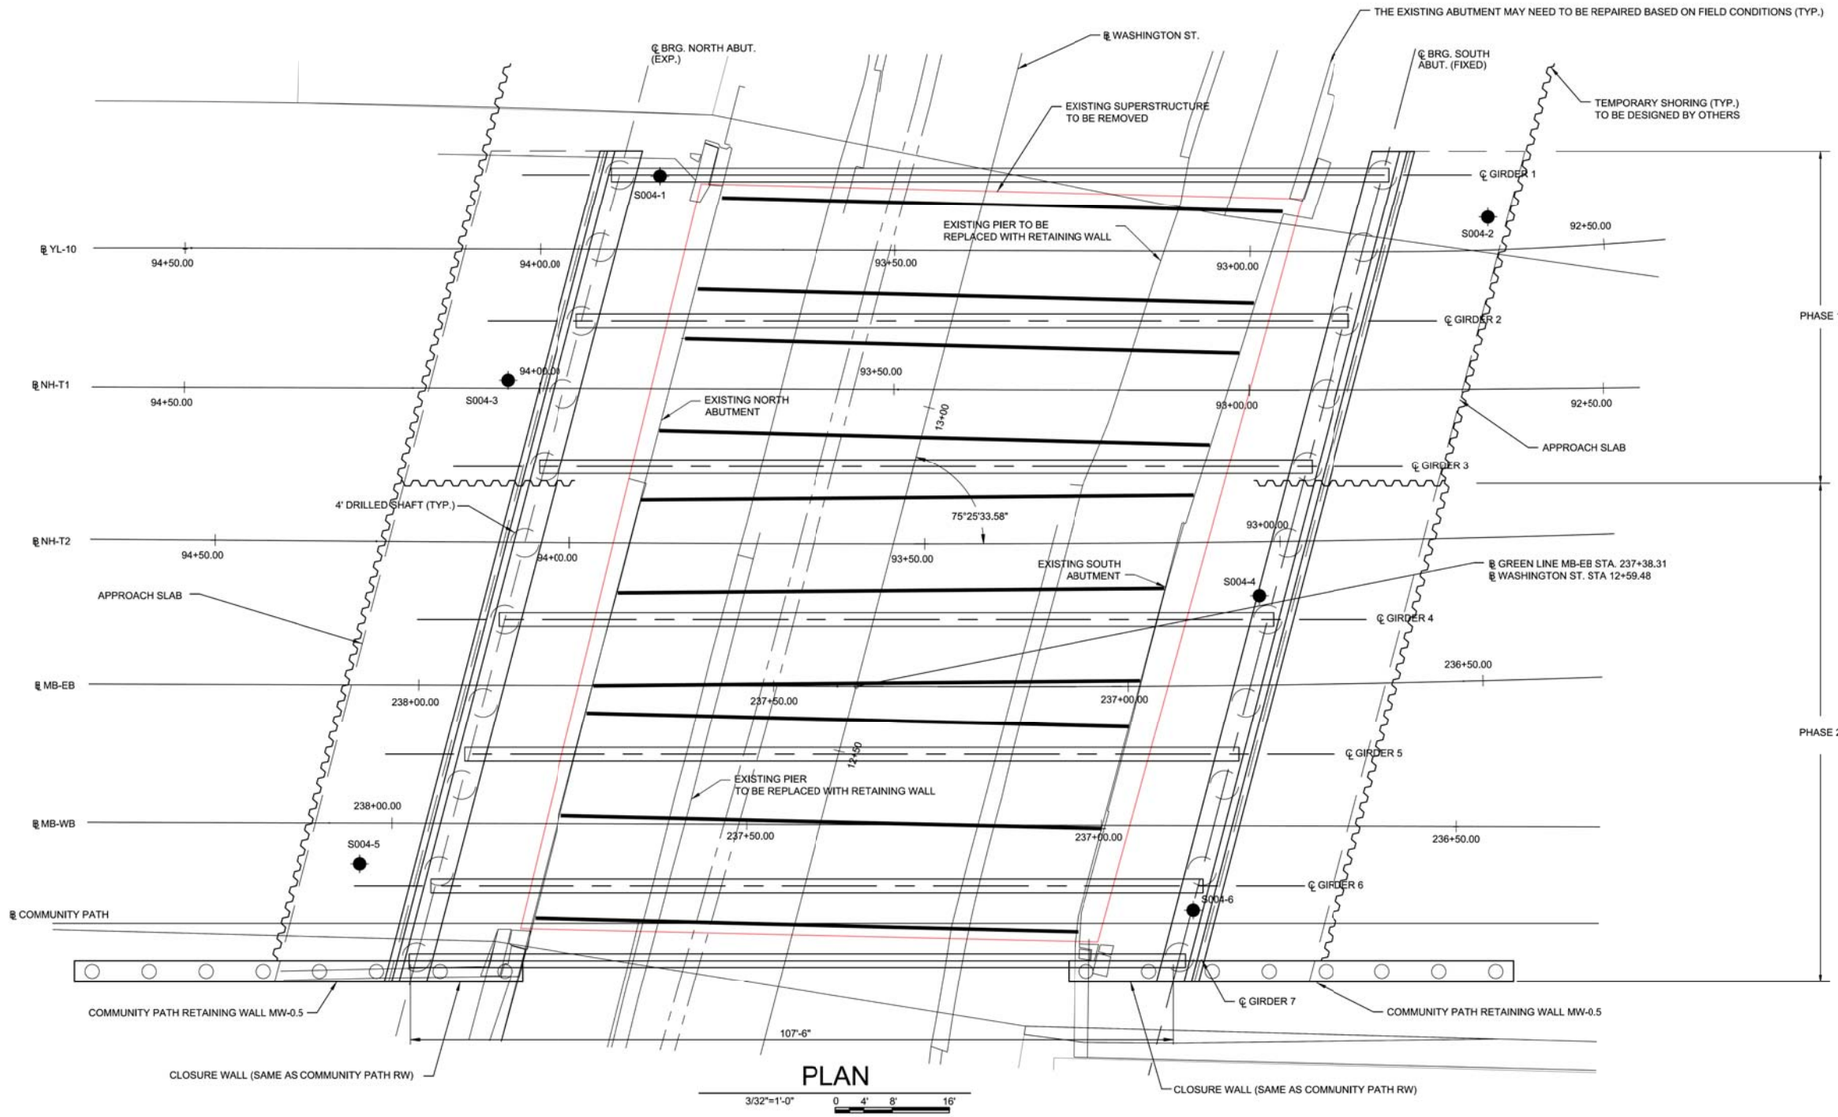

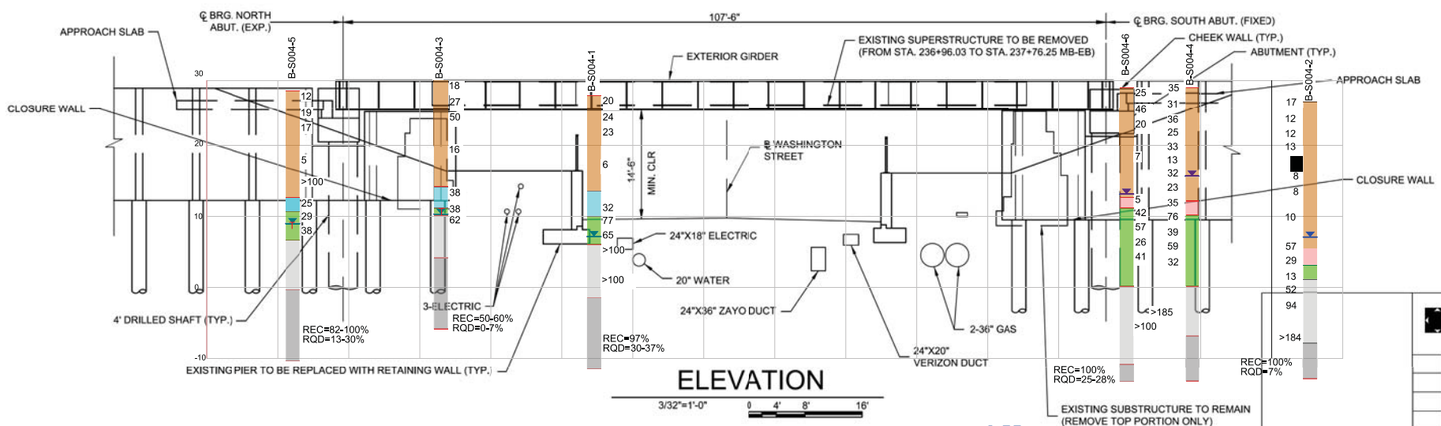



NOTES:

STRUCTURAL STEEL
ALL STRUCTURAL STEEL SHALL CONFORM TO ASTM A709, GRADE 50, PAINTED, UNLESS OTHERWISE NOTED.

CAST-IN-PLACE CONCRETE
ALL CAST-IN-PLACE CONCRETE SHALL BE IN ACCORDANCE WITH THE SPECIFIED MINIMUM COMPRESSIVE STRENGTH (f'c) AND CONCRETE CLASS AT 28 DAYS.

f'c = 4000 PSI, 3#8" MAX. AGGREGATE FOR ABUTMENTS, WINGWALLS, BACKWALLS, STATION ENTRANCE CAP, AND WASHINGTON STREET WALLS.

f'c = 4000 PSI, 3#4" MAX. AGGREGATE FOR APPROACH SLABS.


f'c = 4000 PSI, 3#8", CEMENT CONCRETE FOR DRILLED SHAFTS. THE CLEAR SPACING BETWEEN STEEL REINFORCING BARS SHALL BE AT LEAST 17#8"

REINFORCING STEEL
REINFORCING STEEL SHALL CONFORM TO THE REQUIREMENTS OF ASTM DESIGNATION A706, GRADE 60.

BEARINGS
BEARINGS SHALL BE 14 EA ELASTOMERIC BEARINGS PLACED AT THE CENTER OF THEIR RESPECTIVE GIRDER.

LEGEND

APPROXIMATE BORING LOCATION

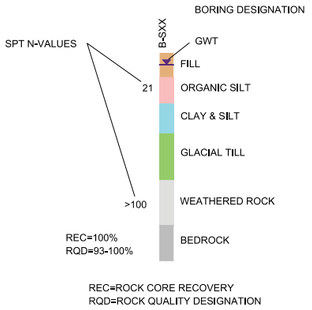

REC=ROCK CORE RECOVERY
RQD=ROCK QUALITY DESIGNATION

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

WASHINGTON STREET BRIDGE PLAN & ELEVATION


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


GV20170258-272.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SM	JY	AR	SHEET: S-019	

tion Bridge GP&E_Print — Proposal.dwg

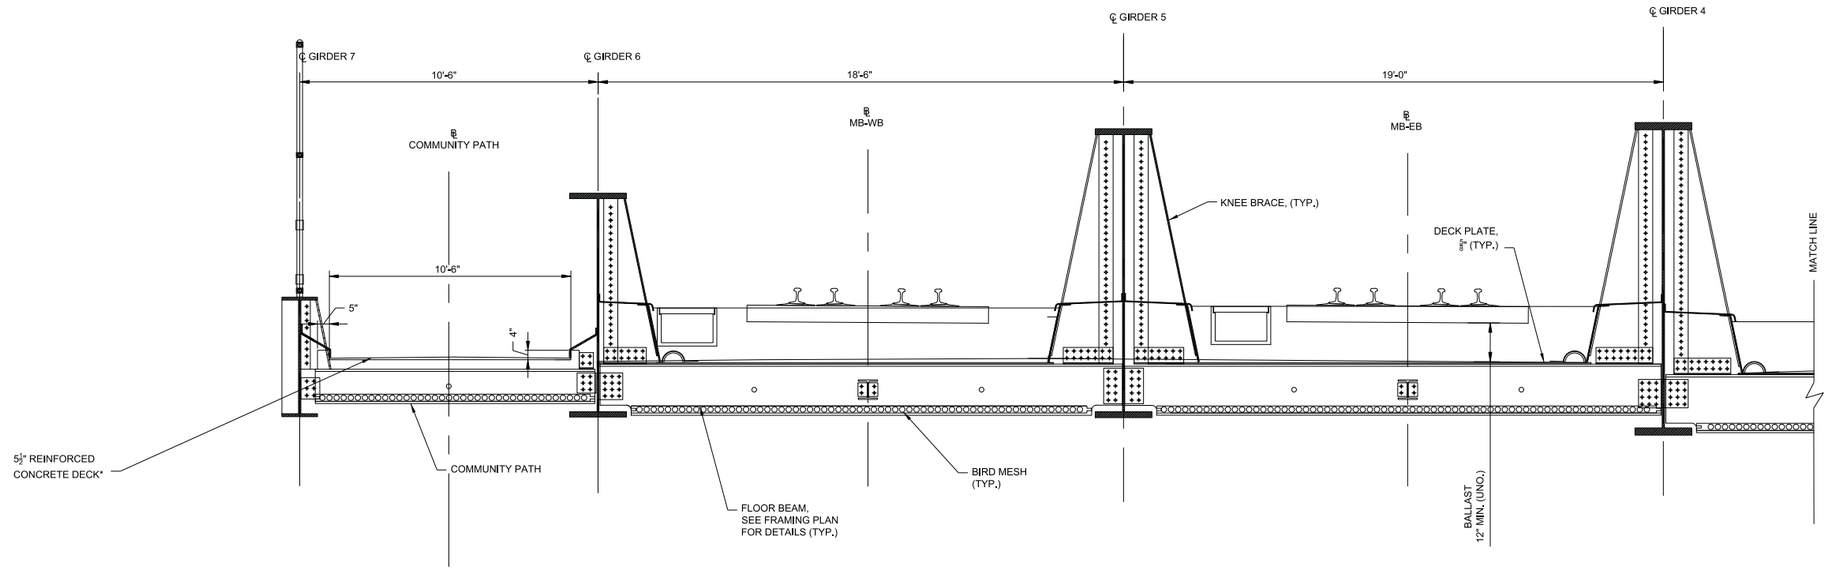

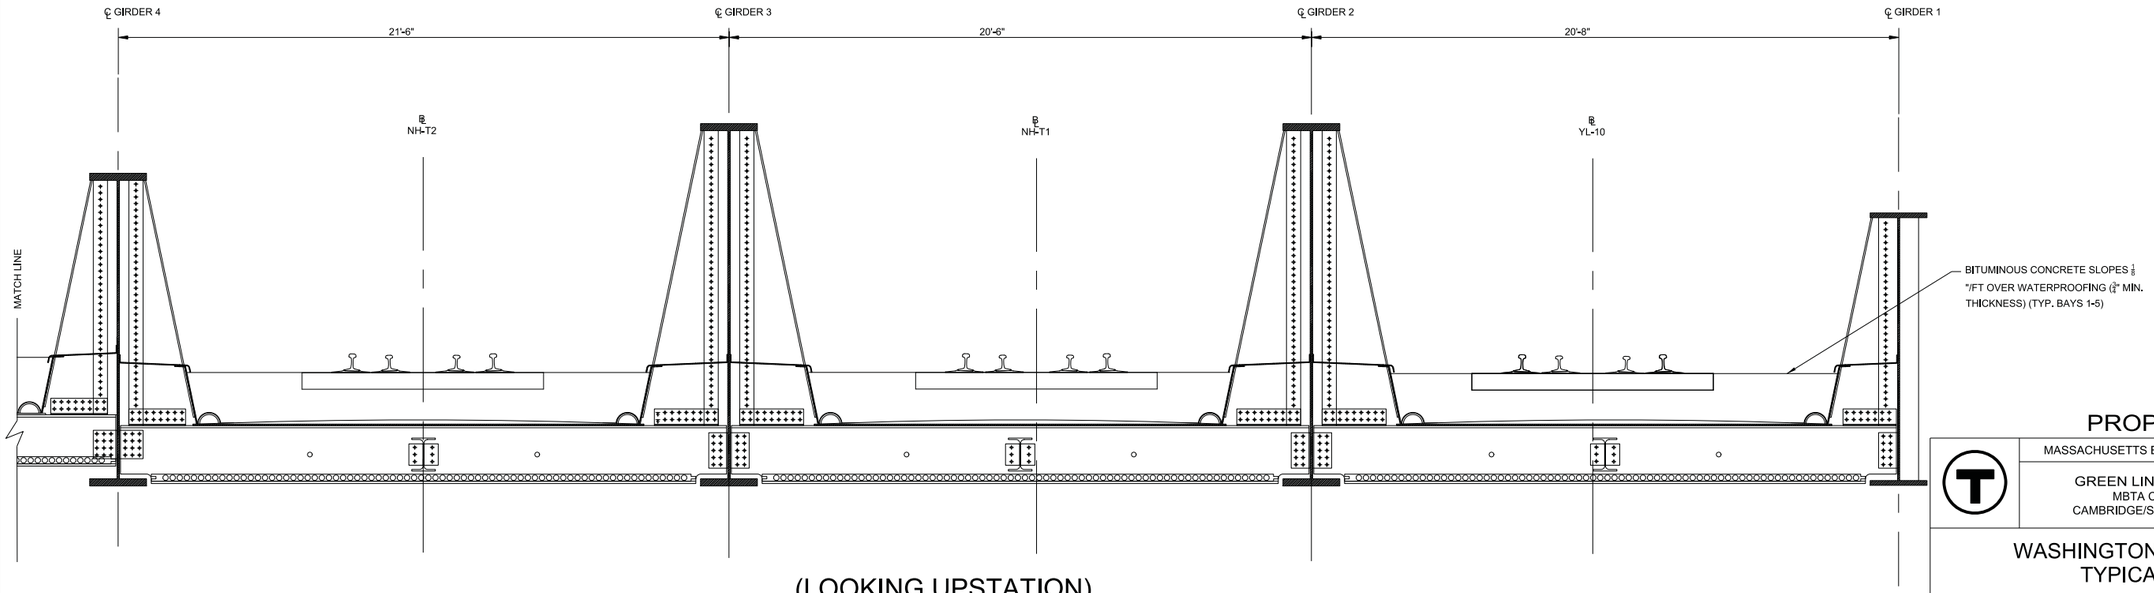

(LOOKING UPSTATION)

TRANSVERSE SECTION

3/8"=1'-0" 0 2' 4' 6'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

WASHINGTON STREET BRIDGE TYPICAL SECTION


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SM	JY	AR	SHEET: S-020	

Friday, September 22, 2017 AT 11:55 AM
P:\Bridges\PROJECTS\CURRENT\Green Line Extension DB - MassDOT\Washington St Bridge\Typical Section_Print - Proposal.dwg

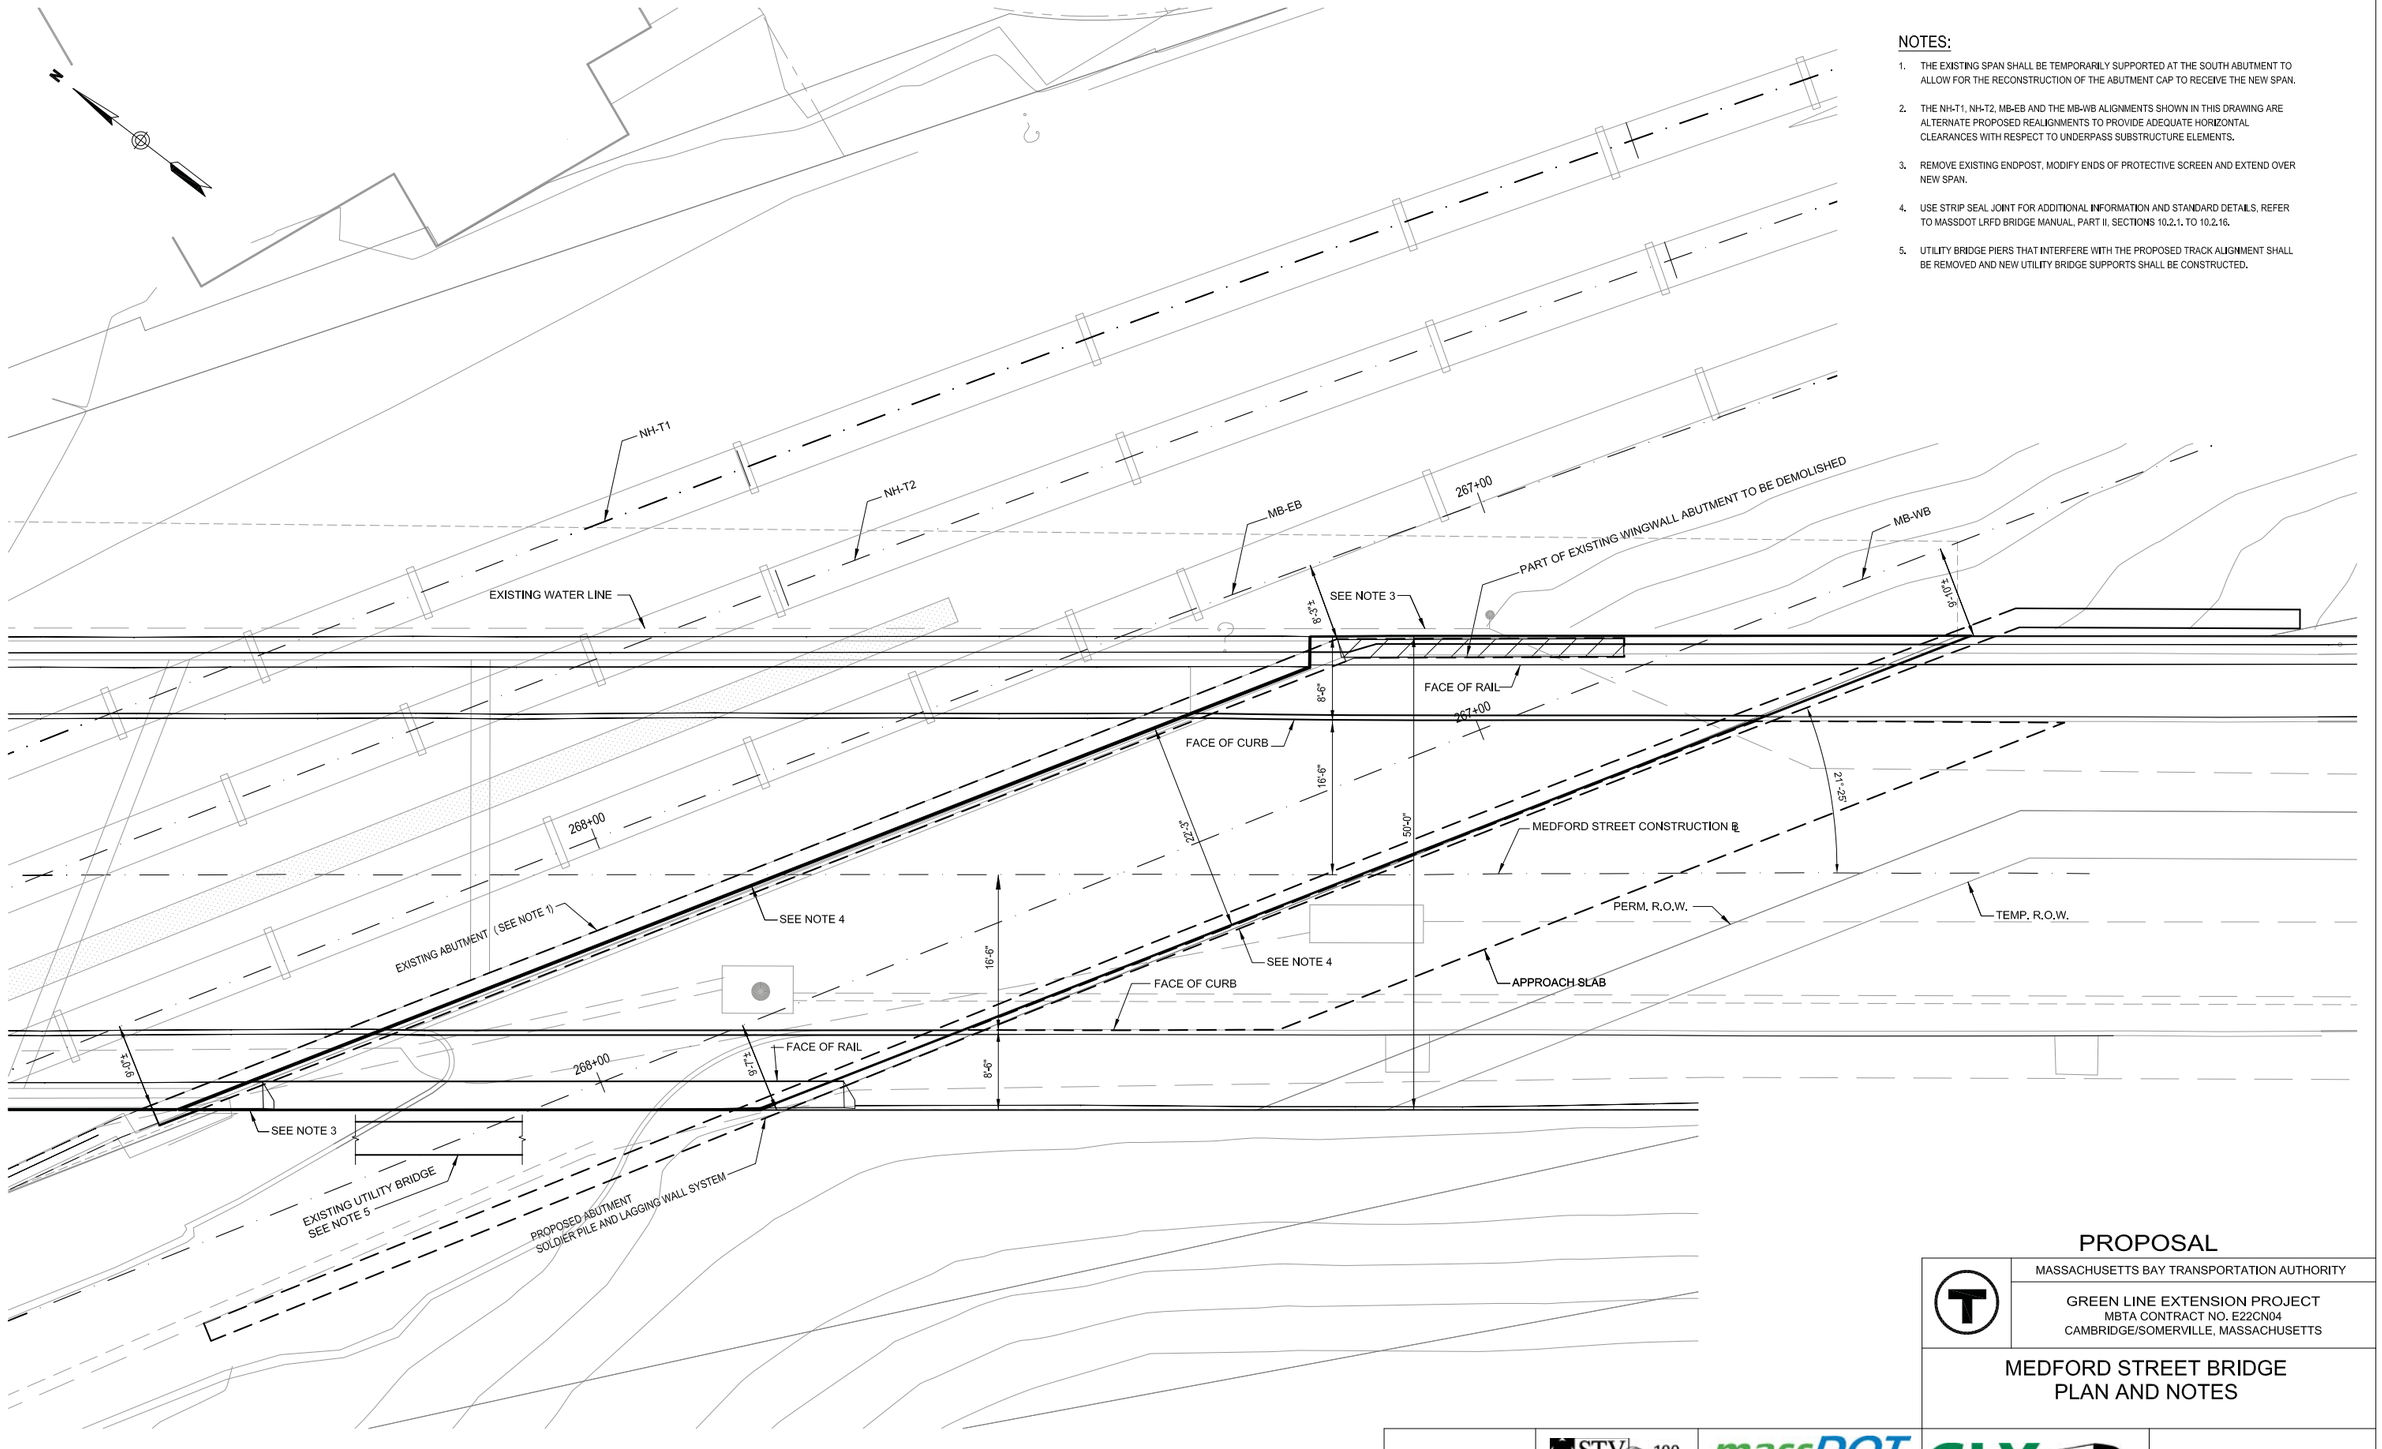

NOTES:

1. THE EXISTING SPAN SHALL BE TEMPORARILY SUPPORTED AT THE SOUTH ABUTMENT TO ALLOW FOR THE RECONSTRUCTION OF THE ABUTMENT CAP TO RECEIVE THE NEW SPAN.
2. THE NH-T1, NH-T2, MB-EB AND THE MB-WB ALIGNMENTS SHOWN IN THIS DRAWING ARE ALTERNATE PROPOSED REALIGNMENTS TO PROVIDE ADEQUATE HORIZONTAL CLEARANCES WITH RESPECT TO UNDERPASS SUBSTRUCTURE ELEMENTS.
3. REMOVE EXISTING ENDPOST, MODIFY ENDS OF PROTECTIVE SCREEN AND EXTEND OVER NEW SPAN.
4. USE STRIP SEAL JOINT FOR ADDITIONAL INFORMATION AND STANDARD DETAILS, REFER TO MASSDOT LRFD BRIDGE MANUAL, PART II, SECTIONS 10.2.1. TO 10.2.16.
5. UTILITY BRIDGE PIERS THAT INTERFERE WITH THE PROPOSED TRACK ALIGNMENT SHALL BE REMOVED AND NEW UTILITY BRIDGE SUPPORTS SHALL BE CONSTRUCTED.

MEDFORD STREET BRIDGE PLAN

1/8"=1'-0" 0 4' 8' 16'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD STREET BRIDGE PLAN AND NOTES


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf


SCALE: 1/8"=1'-0"	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SMH	GEE	JM	SHEET: S-021	

PLOTTED: 09/22/17 9:51AM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\BRIDGES_PROPOSAL DRAWINGS\MEDFORD_ST PROPOSAL.DWG [SHEET 01 - PLAN] 09/21/17 11:34AM

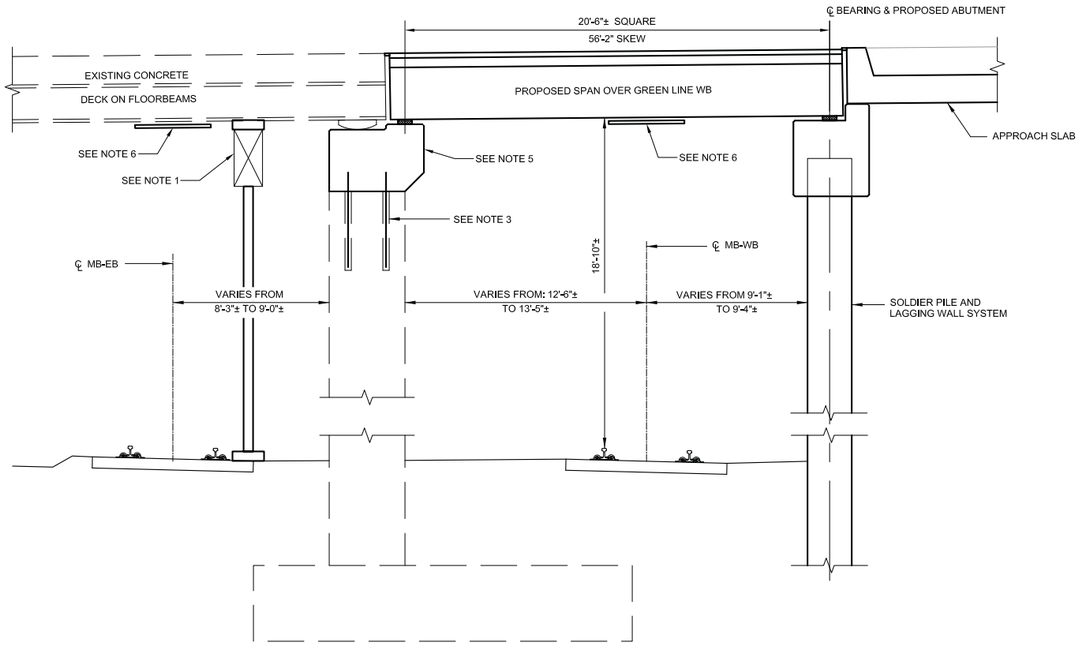

MEDFORD STREET BRIDGE ELEVATION

1/4"=1'-0" 0 2' 4' 8'

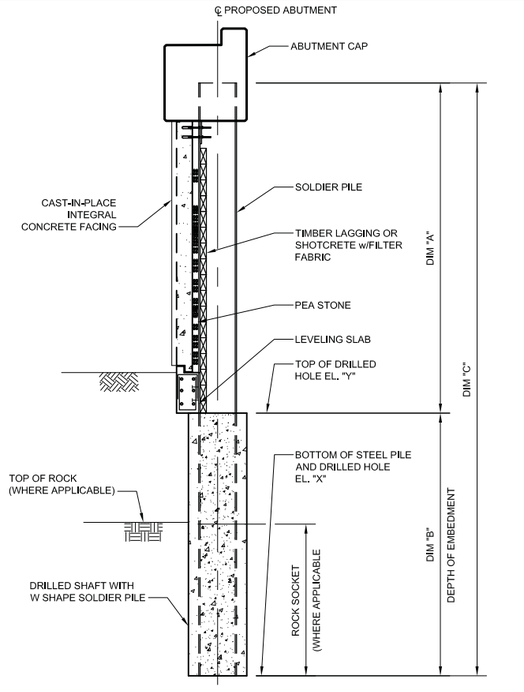


TYPICAL SOLDIER PILE AND LAGGING (SPL) WALL

1/4"=1'-0" 0 2' 4' 8'


NOTES:

1. EXISTING SPAN SHALL BE TEMPORARILY SUPPORTED AT SOUTH ABUTMENT END TO ALLOW RECONSTRUCTION OF CAP TO RECEIVE NEW SPAN.
2. TEMPORARY RELOCATION, SUPPORT, AND/OR REPLACEMENT OF EXISTING UTILITIES SHALL BE PROVIDED AND COORDINATED WITH MBTA AND MASSDOT.
3. DRILL AND GROUT 3/4" DOWELS SPACED 24" O.C.
4. REMOVE EXISTING APPROACH SLAB AND WINGWALL.
5. DEMOLISH AND RE-BUILD EXISTING ABUTMENT CAP. SEE DETAIL THIS SHEET.
6. PROVIDE OCS PROTECTIVE BOARD BELOW UTILITIES. SEE SYSTEM DRAWINGS FOR DETAILS.

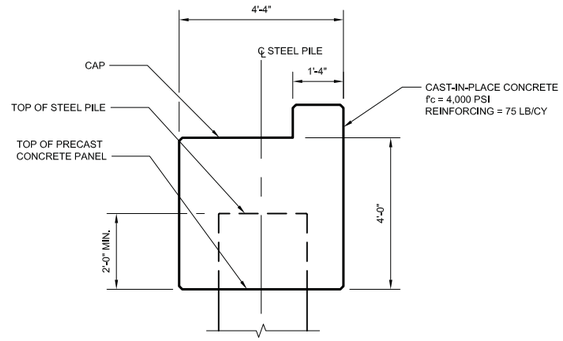

CAP DETAIL

1/2"=1'-0" 0 1' 2' 4'

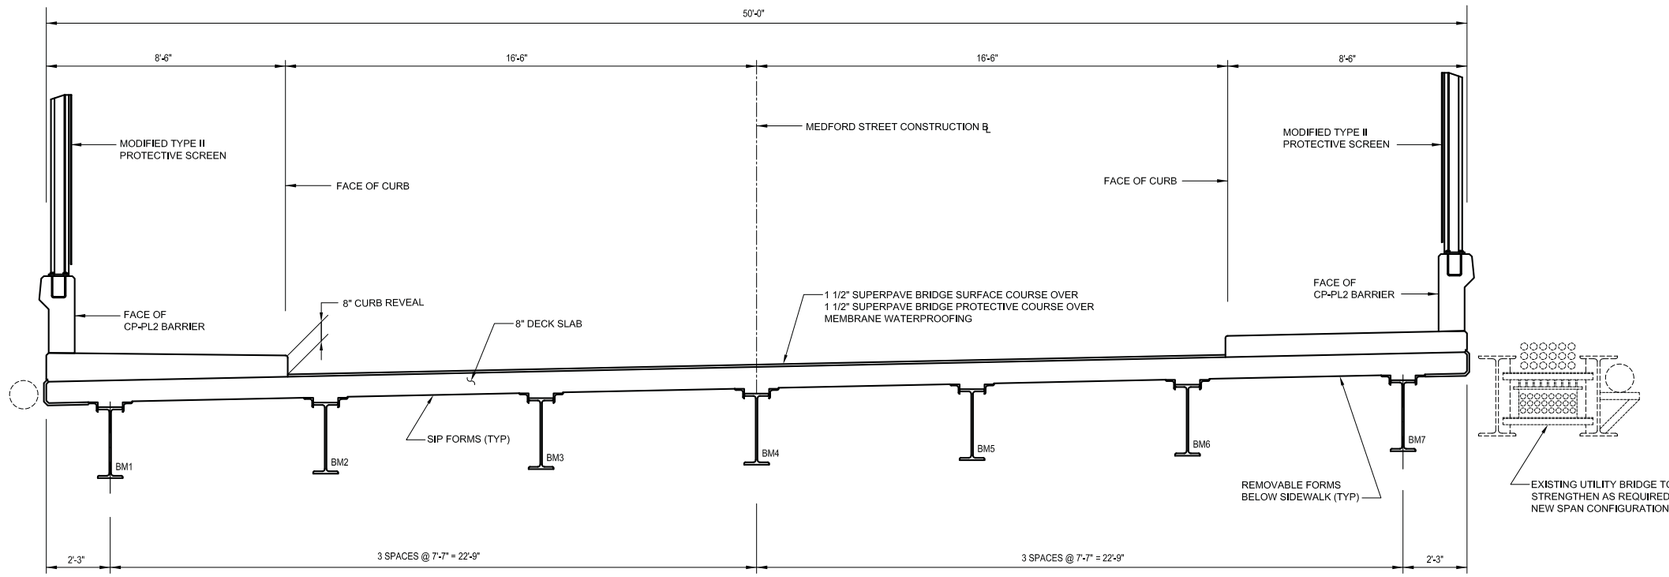


TYPICAL SECTION

3/8"=1'-0" 0 2' 4' 6'

ALL DIMENSIONS ARE PERPENDICULAR, UNLESS OTHERWISE NOTED.

NOTES:

1. CONCRETE IN THE BRIDGE DECK SHALL HAVE A MINIMUM 28-DAY COMPRESSION STRENGTH OF 4,000 PSI, WITH A MAXIMUM AGGREGATE SIZE OF $\frac{3}{4}$", AND 685-PCY CEMENT CONTENT.
2. CONCRETE IN THE SIDEWALKS AND BARRIERS SHALL HAVE A MINIMUM 28-DAY COMPRESSION STRENGTH OF 5,000 PSI, WITH A MAXIMUM AGGREGATE SIZE OF 3/4", AND 685-HP CEMENT CONCRETE.
3. ALL REINFORCING STEEL SHALL BE DEFORMED AND SHALL CONFORM TO AASHTO M 31, GRADE 60.
4. STEEL BEAMS DESIGNED COMPOSITE WITH CONCRETE DECK. CONSIDER 2-7/8"Ø SHEAR STUDS SPACED AT 6" FOR THE FIRST 5'-0" OF BEAM AT EACH END, AND SPACED AT 12" FOR THE REST.

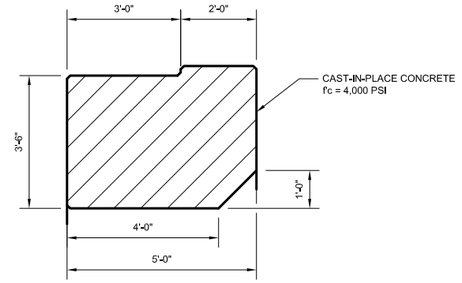

EXISTING ABUTMENT CAP MODIFICATION

1/2"=1'-0" 0 1' 2' 4'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD STREET BRIDGE SECTION AND ELEVATION


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf

SCALE: AS NOTED | DRAWN BY | DESIGN BY | CHECK BY | PLAN NO. | ISSUE

DATE: SEPT. 28, 2017 | SMH | GEE | JM | SHEET: S-022

PLOTTED: 09/22/17 9:52AM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\BRIDGES_PROPOSAL DRAWINGS\MEDFORD_ST PROPOSAL.DWG [SHEET 02 - ELEVATION] 09/21/17 11:34AM

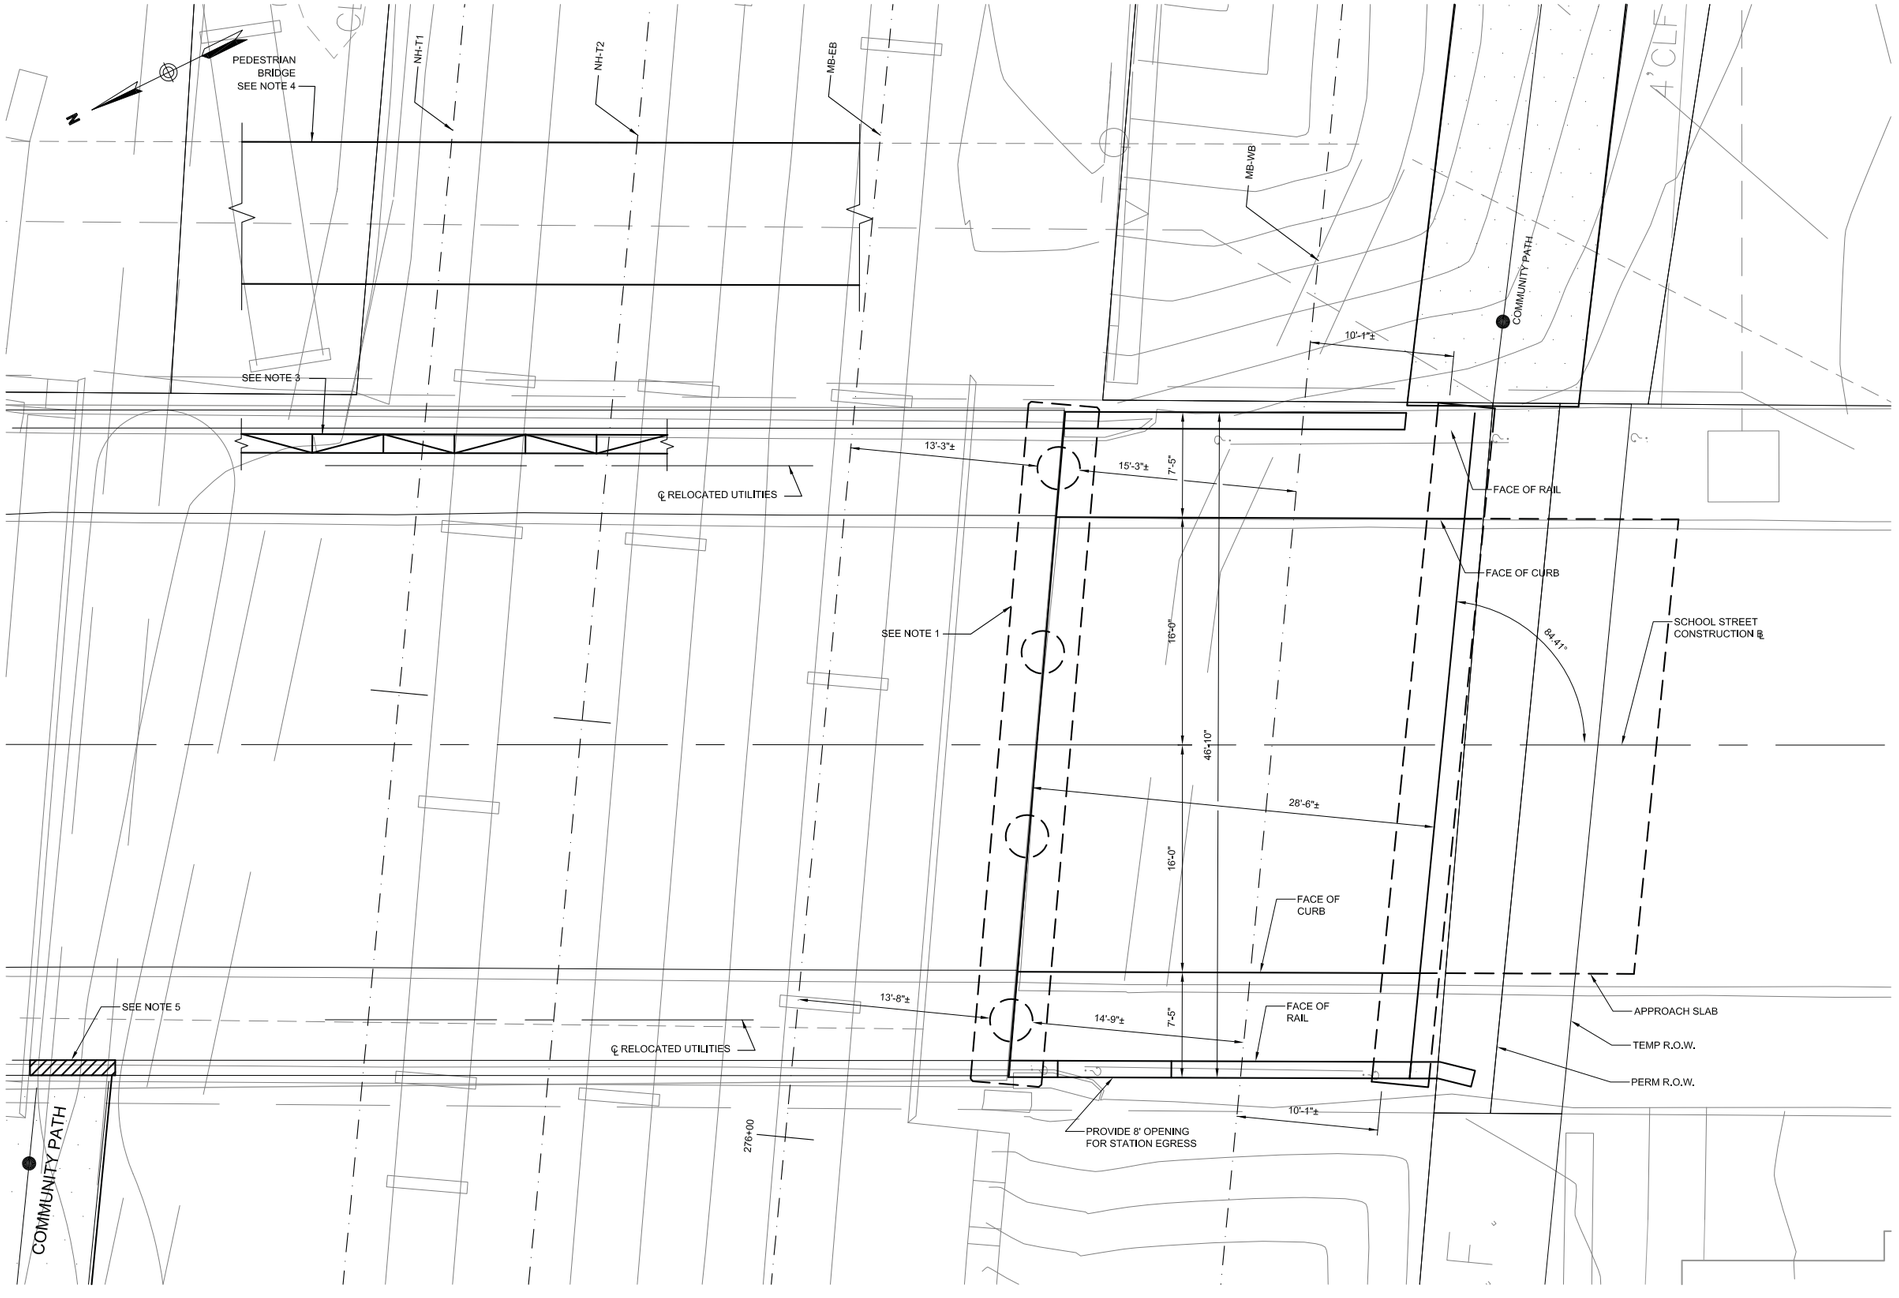

SCHOOL STREET BRIDGE PLAN

3/16"=1'-0" 0 3' 6' 12'

NOTES:

1. THE EXISTING SPAN SHALL BE TEMPORARILY SUPPORTED AT THE SOUTH ABUTMENT TO ALLOW FOR THE DEMOLITION OF THE ABUTMENT AND THE CONSTRUCTION OF NEW PIER TO RECEIVE THE NEW SPAN.
2. USE STRIP SEAL JOINT. FOR ADDITIONAL INFORMATION AND STANDARD DETAILS REFER TO MASSDOT LRFD BRIDGE MANUAL, PART II, SECTIONS 10.2.1. TO 10.2.16.
3. THE EXISTING TRUSS SUPPORTING UTILITIES ON THE SIDEWALK OF THE EXISTING BRIDGE SHALL BE REMOVED AND THE EXISTING SIDEWALK REPAIRED.
4. THE UTILITIES ON THE PEDESTRIAN BRIDGE SHALL BE MOVED TO THE VEHICULAR BRIDGE. THIS PEDESTRIAN BRIDGE SHALL BE DEMOLISHED.
5. REMOVE EXISTING CONCRETE BARRIER AND FENCE TO PROVIDE 12' OPENING FOR COMMUNITY PATH.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

SCHOOL STREET BRIDGE
PLAN AND NOTES

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-272.pdf

SCALE: 3/16"=1'-0"	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DEH	GEE	JM	SHEET: S-023	

PLOTTED: 09/22/17 9:57AM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN BRIDGES_PROPOSAL DRAWINGS\SCHOOL_ST PROPOSAL.DWG [S-026 - PLAN] 09/21/17 11:56AM

NOTES:

1. THE EXISTING SPAN SHALL BE TEMPORARILY SUPPORTED AT THE SOUTH ABUTMENT TO ALLOW FOR THE DEMOLITION OF THE ABUTMENT AND THE CONSTRUCTION OF A NEW PIER TO RECEIVE THE NEW SPAN.
2. NEW MULTICOLUMN PIER.
3. PROVIDE OCS PROTECTIVE BOARD BELOW UTILITIES. SEE SYSTEM DRAWINGS FOR DETAILS.

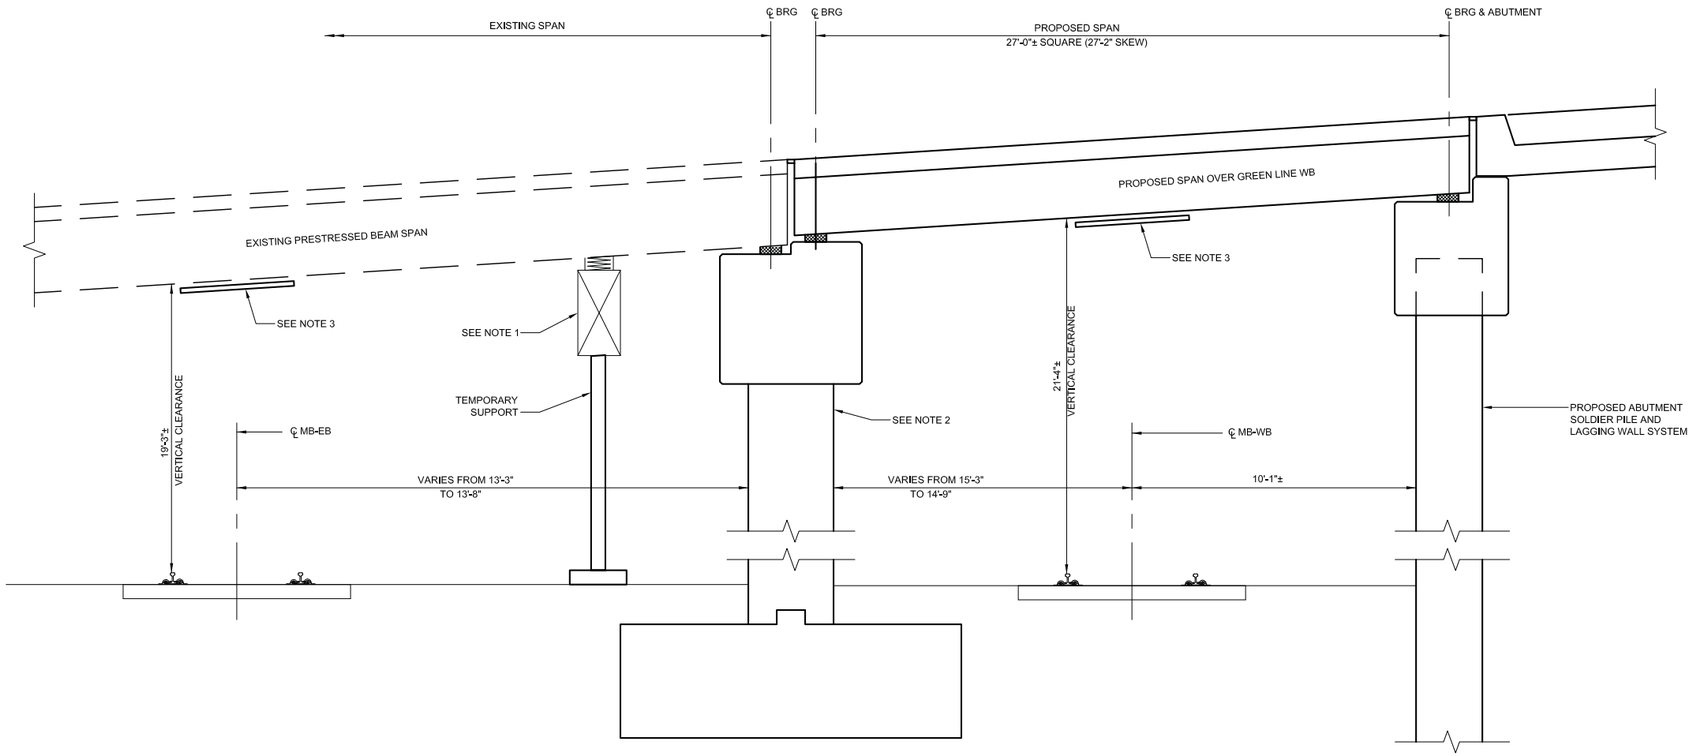

SCHOOL STREET BRIDGE ELEVATION

3/8"=1'-0" 0 2' 4' 6'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


SCHOOL STREET BRIDGE ELEVATION

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DEH	GEE	JM	SHEET: S-024	

PLOTTED: 09/22/17 9:58AM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\BRIDGES_PROPOSAL DRAWINGS\SCHOOL_ST PROPOSAL.DWG [S-027 - ELEVATION] 09/21/17 11:56AM

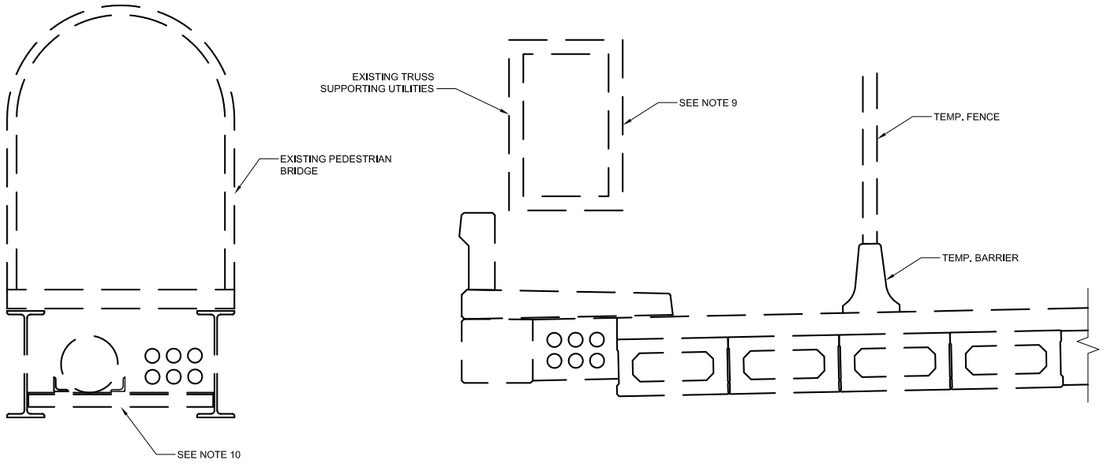


CROSS SECTION AT EXISTING SPAN

3/8"=1'-0" 0 2' 4' 6'

NOTES:

1. CONCRETE IN THE BRIDGE DECK SHALL HAVE A MINIMUM 28 DAY COMPRESSION STRENGTH OF 4,000 PSI, WITH A MAXIMUM AGGREGATE SIZE OF 3/4", AND 585 PCY CEMENT CONTENT.
2. BARRIERS, SIDEWALK AND SAFETY CURB CONCRETE SHALL HAVE A MINIMUM 28 DAY COMPRESSION STRENGTH OF 5,000 PSI, WITH A MAXIMUM AGGREGATE SIZE OF 3/4" AND 685 HP CEMENT CONCRETE.
3. CONCRETE IN DECK BEAMS SHALL HAVE A MINIMUM 28 DAY COMPRESSION STRENGTH OF 6,500 PSI. NO PRESTRESSED SHALL BE TRANSFERRED TO THE CONCRETE UNTIL IT HAS ATTAINED A MINIMUM COMPRESSIVE STRENGTH OF AT LEAST 4,500 PSI.
4. ALL REINFORCING STEEL SHALL BE DEFORMED AND SHALL BE COATED TO CONFORM TO AASHTO M 31, GRADE 60.
5. PRESTRESSING STRANDS SHALL BE 0.6" DIAMETER, UNCOATED, SEVEN-WIRE, LOW-RELAXATION STEEL STRANDS CONFORMING TO AASHTO M 203, GRADE 270.
6. VOIDS IN THE DECK BEAMS SHALL TERMINATE 3'-9" FROM END OF SPAN AND 7" ON EITHER SIDE OF THE TRANSVERSE TENDON CENTERLINE AT MIDSPAN. THE TOP OF ALL BEAMS SHALL RECEIVE A RAKE FINISH.
7. USE CP-PL2 RAILING / BARRIER. REFER TO MASSDOT LRFD BRIDGE MANUAL, PART II, SECTIONS 9.4.1 TO 9.4.9.
8. BRIDGE DECK SHALL BE GROOVED TRANSVERSELY USING MULTI-BLADED, SELF-PROPELLED ,SAWCUTTING EQUIPMENT.
9. THE EXISTING TRUSS SUPPORTING UTILITIES ON THE SIDEWALK OF THE EXISTING BRIDGE SHALL BE REMOVED AND THE EXISTING SIDEWALK REPAIRED.
10. THE UTILITIES ON THE PEDESTRIAN BRIDGE SHALL BE MOVED TO THE VEHICULAR BRIDGE. THIS PEDESTRIAN BRIDGE SHALL BE DEMOLISHED.

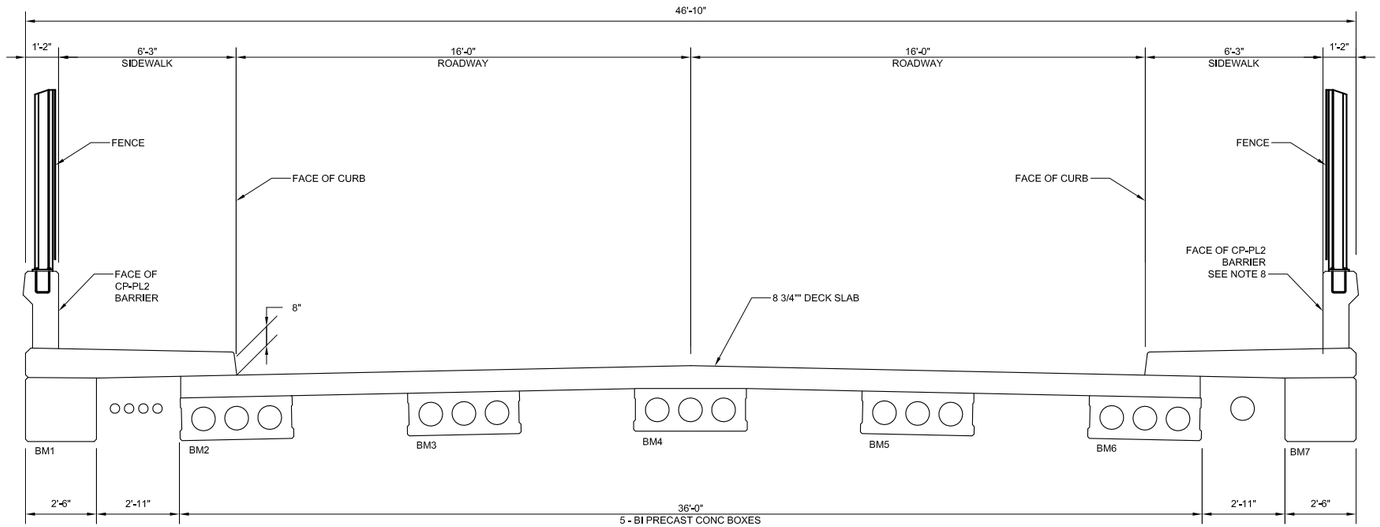

TYPICAL BRIDGE SECTION PRECAST CONCRETE DECK BEAM OPTION

3/8"=1'-0" 0 2' 4' 6'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

SCHOOL STREET BRIDGE
CROSS SECTIONS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DEH	GEE	JM	SHEET: S-025	

PLOTTED: 09/22/17 9:59AM BY:HARTD
DRAWING: L:\PROPOSALS\GLX\TECH DESIGN\BRIDGES_PROPOSAL DRAWINGS\SCHOOL_ST PROPOSAL.DWG [S-028 - TRANSVERSE SECTION] 09/21/17 11:56AM




CEDAR STREET BRIDGE PLAN


3/32"=1'-0" 0 6' 12' 24'

NOTES:


1. THE EXISTING WINGWALL AT THE SOUTHEAST CORNER OF THE BRIDGE SHALL BE DEMOLISHED, AND A NEW WINGWALL SHALL BE CONSTRUCTED
2. SAFETY NITCHES 1'-10" DEEP X 2'-0" WIDE X 7'-0" HEIGHT SPACED 20'-0" O.C. SHALL BE FORMED IN THE EXISTING SOUTH ABUTMENT STEM. SEE DETAIL THIS SHEET.

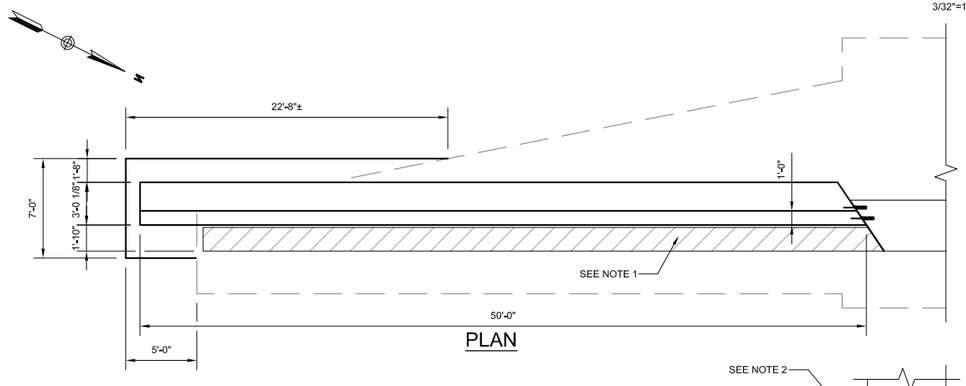

PLAN

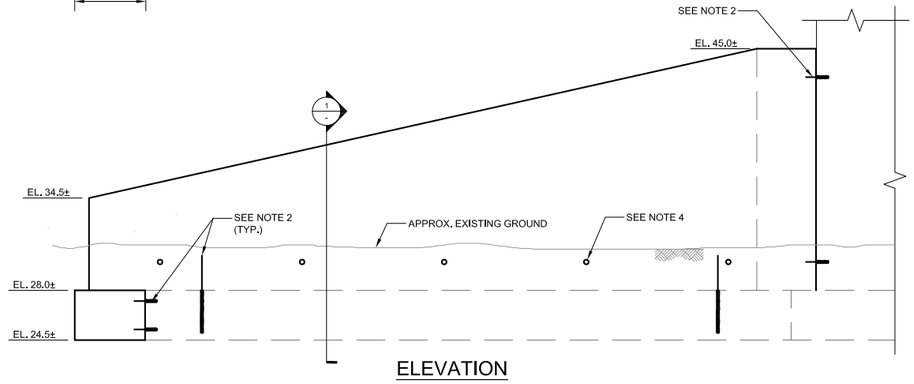


ELEVATION



SECTION 1

CEDAR STREET BRIDGE WINGWALL DETAILS

3/16"=1'-0" 0 3' 6' 12'

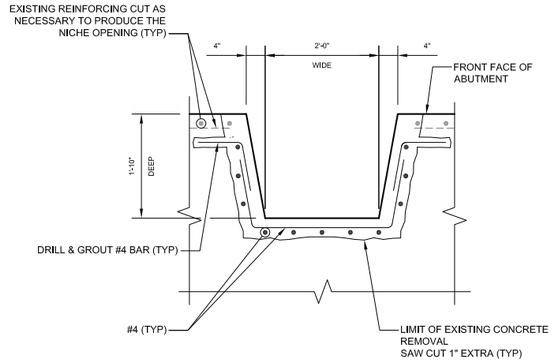

REFUGE NICHE DETAIL

3/4"=1'-0" 0 1' 2' 3'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

CEDAR STREET BRIDGE
PLAN AND ELEVATION


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-272.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DEH	GEE	JM	SHEET: S-026	

PLOTTED: 09/22/17 10:01AM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\BRIDGES_PROPOSAL DRAWINGS\CEDAR_ST PROPOSAL.DWG [SHEET 01 - PLAN] 09/08/17 4:40PM

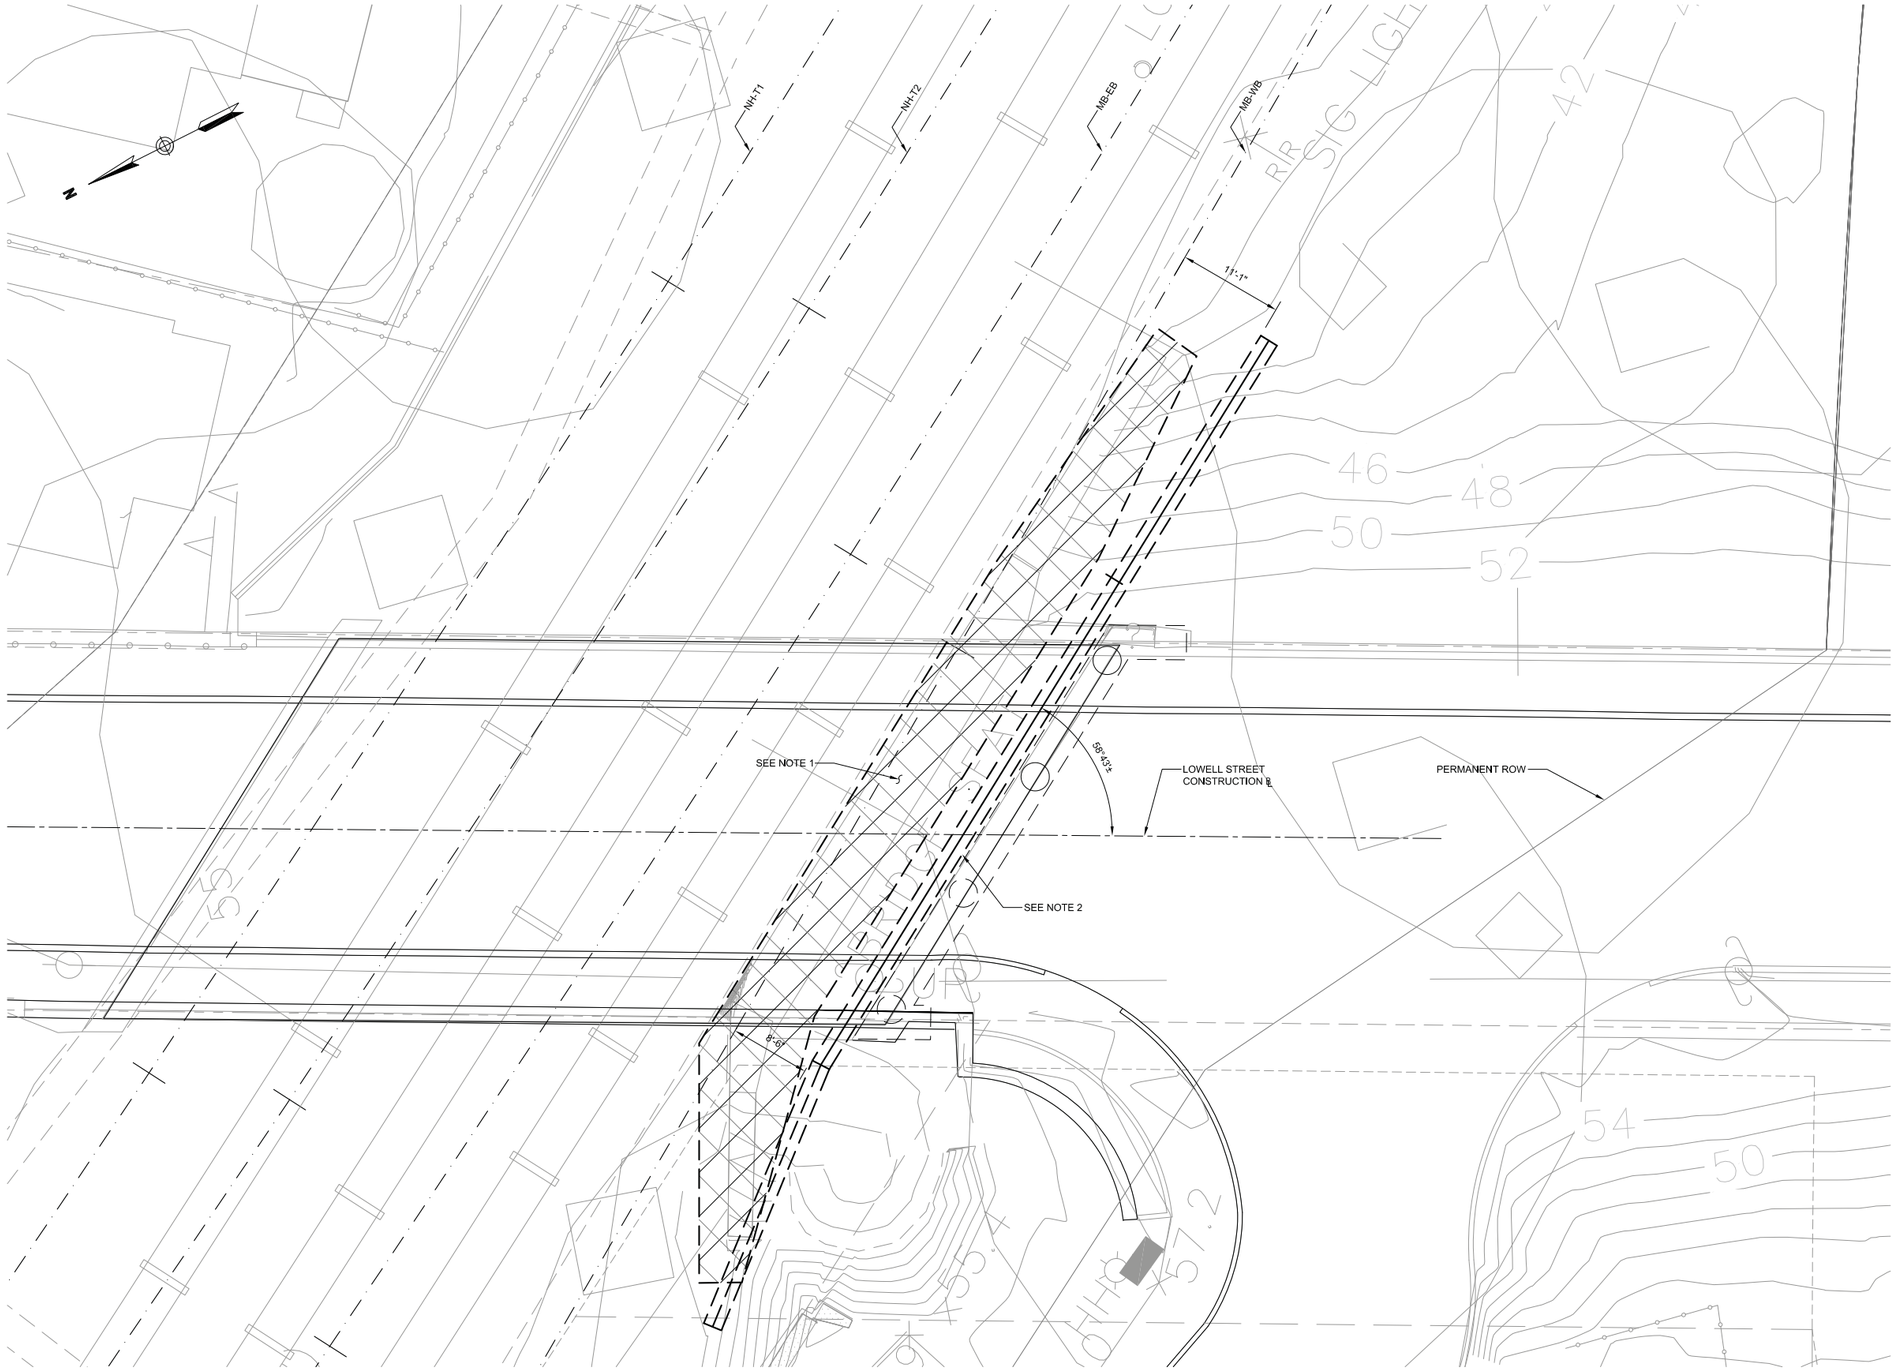

NOTES:

1. EXISTING STONE MASONRY SOUTH ABUTMENT SHALL BE DEMOLISHED TO PROVIDE ADEQUATE HORIZONTAL CLEARANCE TO MB-EB AND MB-WB.
2. A RETAINING WALL SYSTEM SHALL BE PROVIDED IN FRONT OF EXISTING DRILLED SHAFT AND CAP AT THE SOUTH ABUTMENT.

LOWELL STREET BRIDGE PLAN

1/8"=1'-0" 0 4' 8' 16'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

LOWELL STREET BRIDGE
PLAN AND GENERAL NOTES


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-272.pdf

SCALE: 1/8"=1'-0"	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DEH	GEE	JM	SHEET: S-027	

PLOTTED: 09/22/17 10:02AM BY:HARTD
DRAWING: I:\PROPOSALS\GLX TECH DESIGN\BRIDGES_PROPOSAL DRAWINGS\LOWELL_ST PROPOSAL.DWG [SHEET 01 - PLAN] 09/21/17 11:58AM

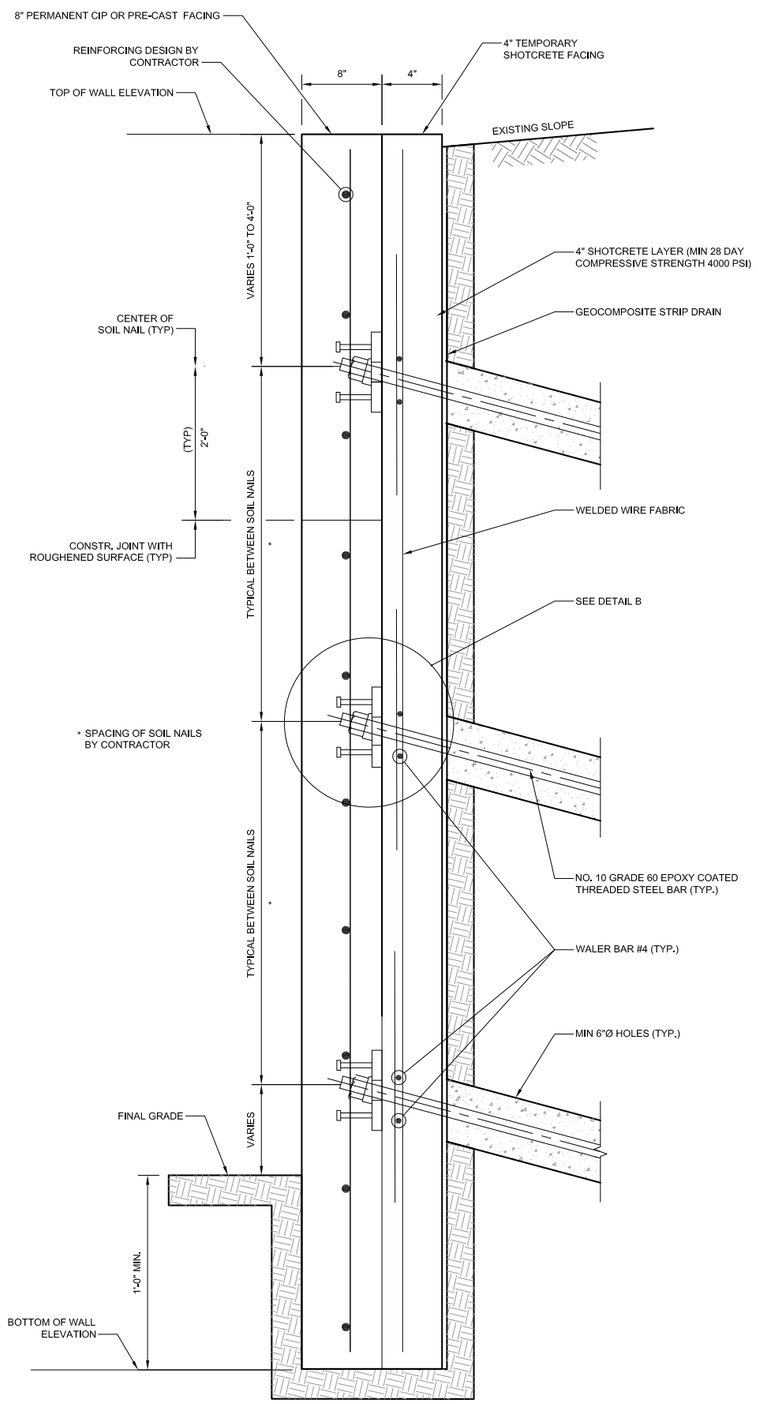


ALTERNATE GROUTED SOIL NAIL WALL TYPICAL SECTION

NOT TO SCALE

NOTES:

1. EXISTING STONE MASONRY SOUTH ABUTMENT SHALL BE DEMOLISHED TO PROVIDE ADEQUATE HORIZONTAL CLEARANCE FROM CL OF MB-EB AND MB-WB.
2. A RETAINING WALL SYSTEM SHALL BE PLACE IN FRONT OF THE EXISTING DRILLED SHAFT AND CAP AT THE SOUTH ABUTMENT.
3. CONFIGURATION AND NUMBER OF TIE-BACKS TO BE DETERMINED BY VENDOR. THE POSSIBLE INTERFERENCE WITH THE EXISTING TIE-BACK SYSTEM FOR THE EXISTING BRIDGE S-17-015 AND RETAINING WALLS AT THE SOUTH ABUTMENT SHALL BE INVESTIGATED.
4. PROVIDE OCS PROTECTION BOARD BELOW UTILITIES. SEE SYSTEM DRAWINGS FOR DETAILS.

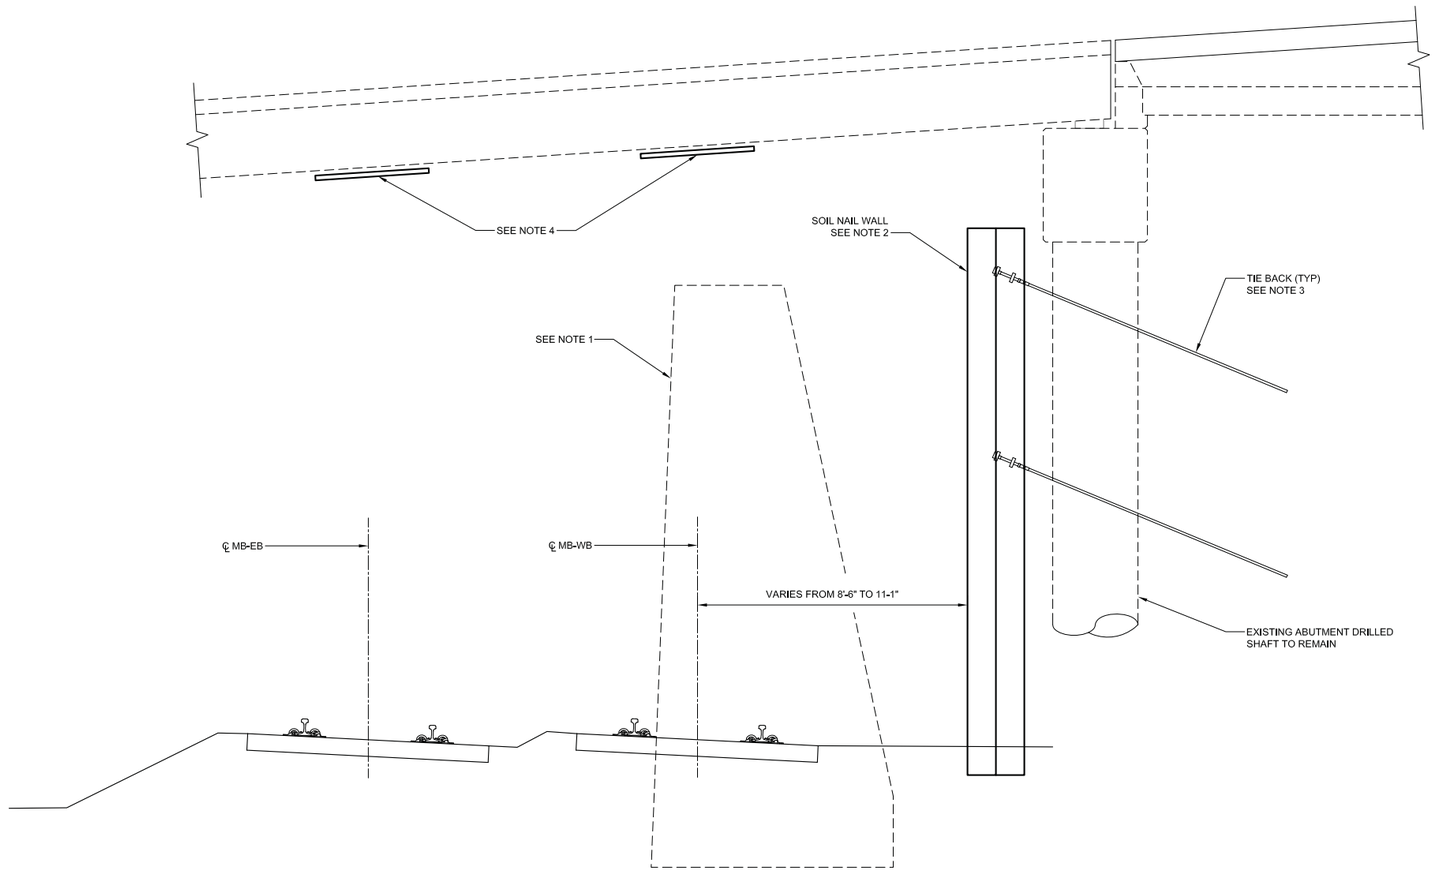

LOWELL STREET BRIDGE ELEVATION

3/8"= 1'-0" 0 2' 4' 6'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

LOWELL STREET BRIDGE ELEVATION


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-272.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	DEH	GEE	JM	SHEET: S-028	

PLOTTED: 09/22/17 10:03AM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\BRIDGES_PROPOSAL DRAWINGS\LOWELL_ST PROPOSAL.DWG [SHEET 02 – ELEVATION] 09/21/17 11:58AM

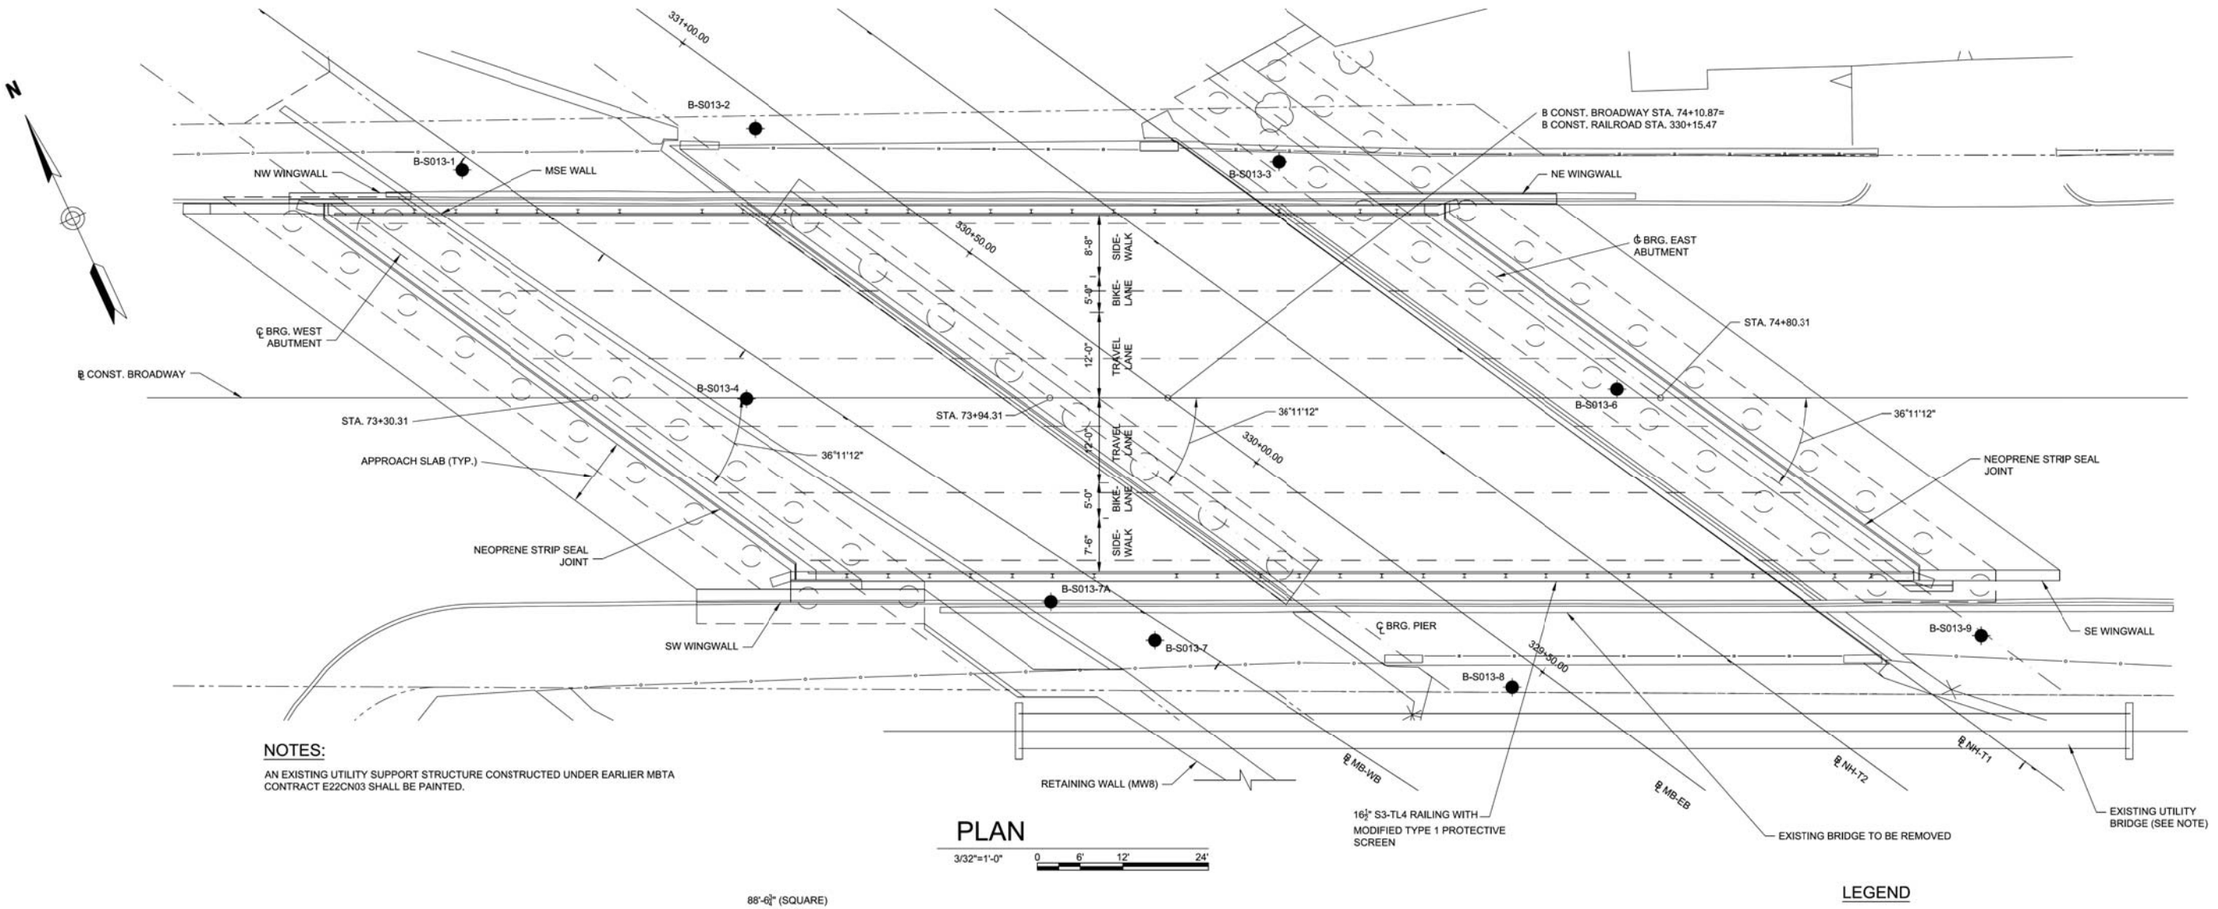


NOTES:

AN EXISTING UTILITY SUPPORT STRUCTURE CONSTRUCTED UNDER EARLIER MBTA CONTRACT E22CN03 SHALL BE PAINTED.

PLAN

3/32"=1'-0" 0 6' 12' 24'

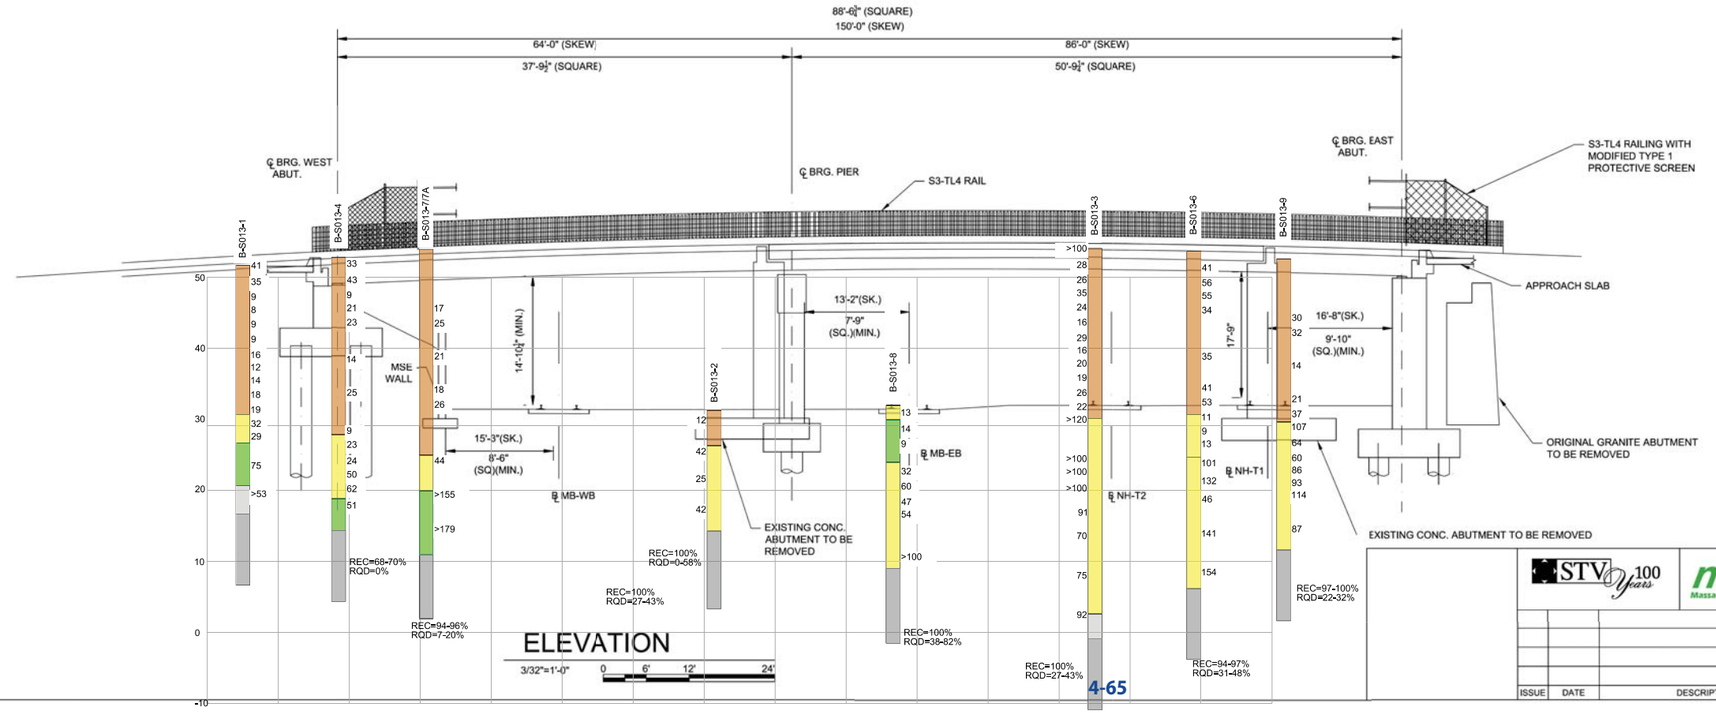

ELEVATION

3/32"=1'-0" 0 6' 12' 24'

LEGEND

- APPROXIMATE BORING LOCATION
- B-SXX — BORING DESIGNATION
- GWT
- SPT N-VALUES — 21 — >100
- ORGANICS /FILL
- SAND
- CLAY, SILT & TILL
- WEATHERED ROCK
- BEDROCK
- REC=ROCK CORE RECOVERY
- RQD=ROCK QUALITY DESIGNATION
- REC=100% RQD=93-100%

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

BROADWAY BRIDGE PLAN & ELEVATION


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-272.pdf


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	AR	AC	SHEET: S-029	

Friday, September 22, 2017 AT 11:51 AM
P:\Bridges\PROJECTS\CURRENT\Green Line Extension DB - MassDOT\Broadway St Bridge\GP&E_Broadway - Proposal.dwg

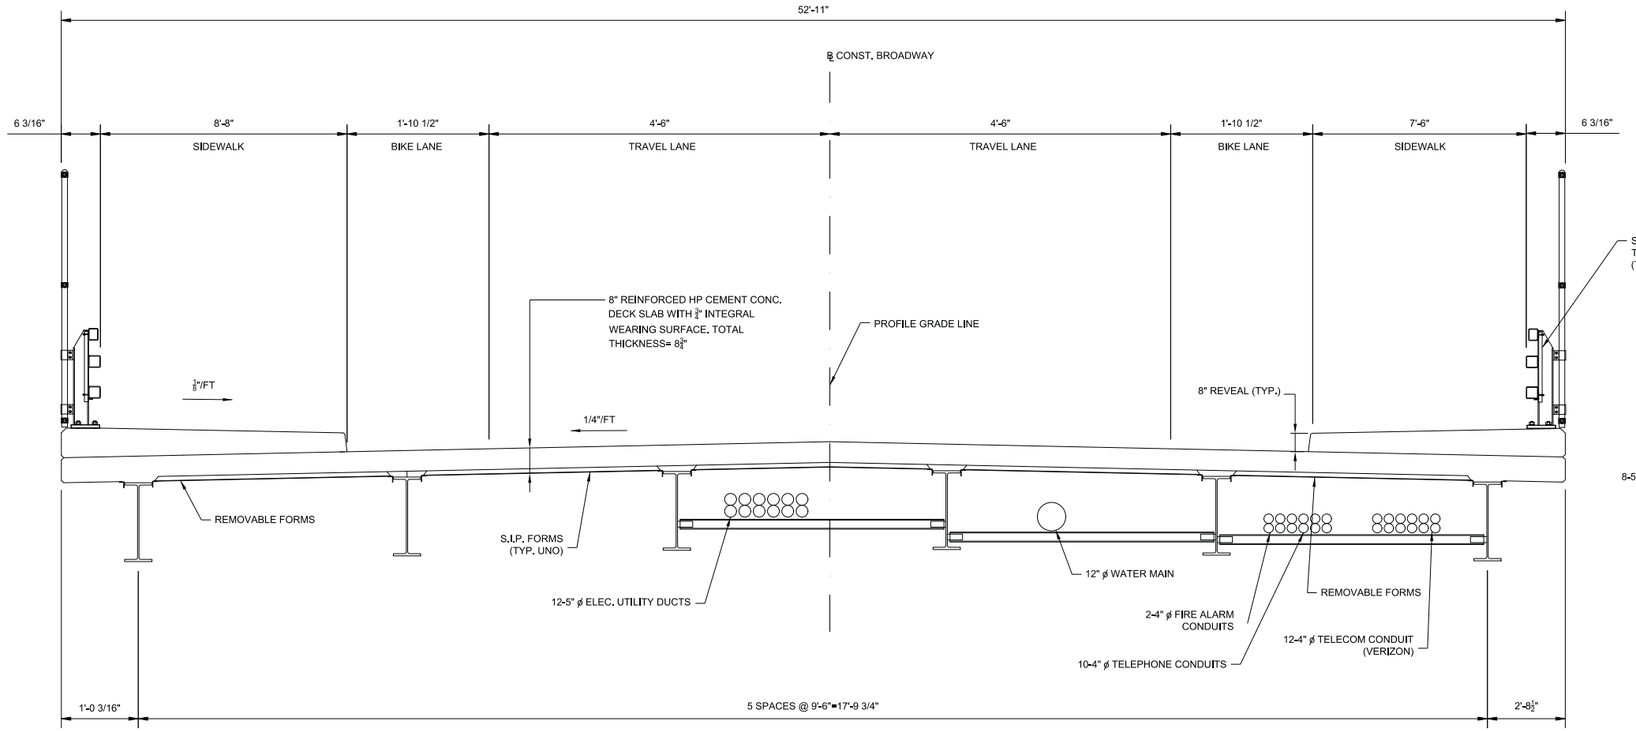

TRANSVERSE SECTION

3/8"=1'-0" 0 2' 4' 6'



UTILITY BRIDGE TRANSVERSE SECTION

3/8"=1'-0" 0 2' 4' 6'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

BROADWAY BRIDGE
TYPICAL TRANSVERSE SECTION


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-272.pdf


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	AR	AC	SHEET: S-030	

Friday, September 22, 2017 AT 11:52 AM
P:\Bridges\PROJECTS\CURRENT\Green Line Extension DB - MassDOT\Broadway St Bridge\Typical Section_Print - Proposal.dwg

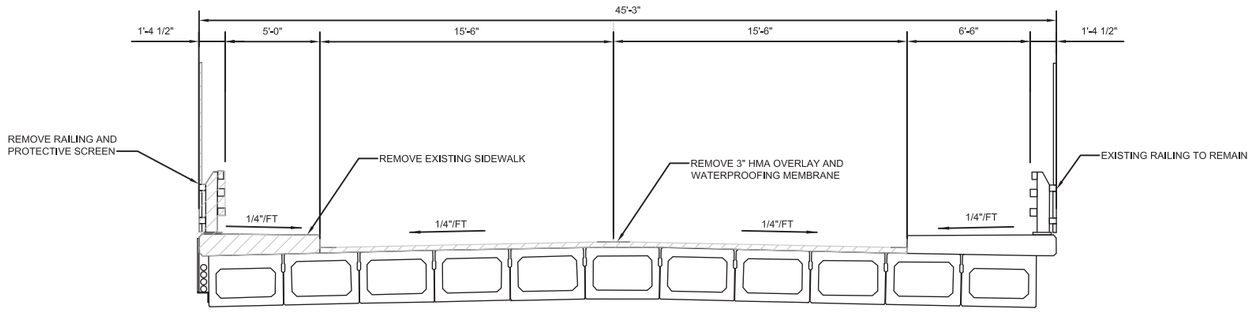


TYPICAL SECTION - REMOVAL

NOT TO SCALE

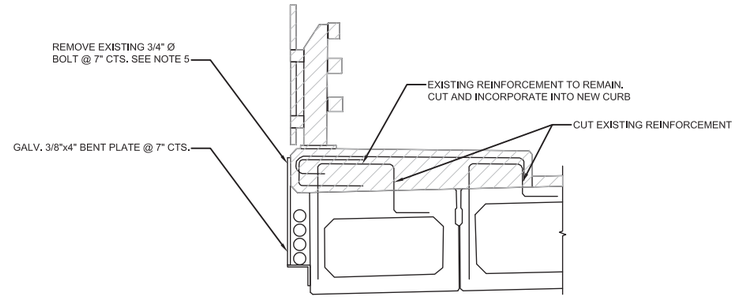


SECTION THRU SIDEWALK

NOT TO SCALE

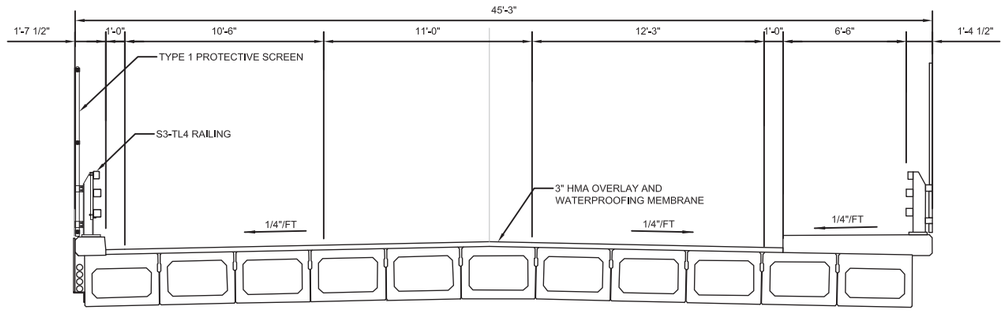

TYPICAL SECTION - PROPOSED

NOT TO SCALE

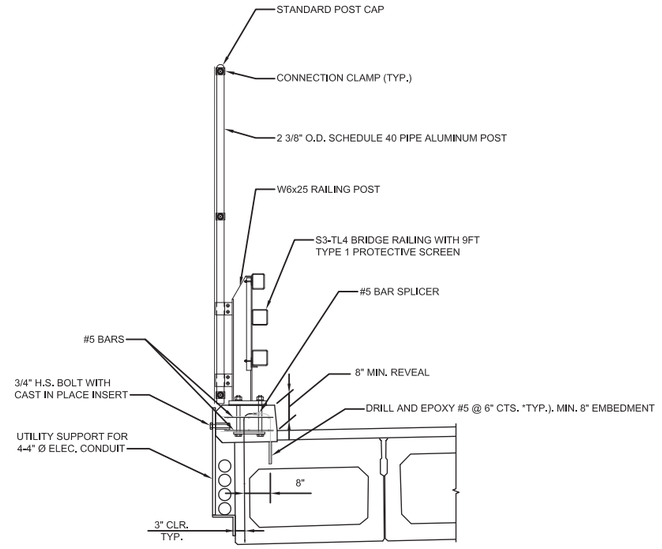

SECTION THRU SAFETY CURB

NOT TO SCALE

NOTES:

1. CONTRACTOR SHALL USE PACHOMETER TO LOCATE AND MARK EXISTING REINFORCING BEFORE DRILLING ANCHORS INTO EXISTING BEAMS.
2. SIDEWALK CONCRETE SHALL BE 5000 PSI, 3/4" 635 SILICA FUME MODIFIED CEMENT CONCRETE.
3. SIDEWALK AND CURB REINFORCING SHALL BE EPOXY COATED.
4. TEMPORARILY SUPPORT EXISTING UTILITIES AS REQUIRED TO COMPLETE WORK.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

COLLEGE AVENUE BRIDGE TYPICAL SECTIONS


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-272.pdf


SCALE: N.T.S.	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	JMP	JMP	SB	SHEET: S-031	.

PLOTTED: 09/22/17 2:35PM BY:PATTS,M
DRAWING: L:\PROPOSALS\2017\0002820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CJ_BRIDGE\COLLEGE AVE HIGHWAY BRIDGE\FINAL\S-51.DWG [S-51] 09/22/17 1:35PM

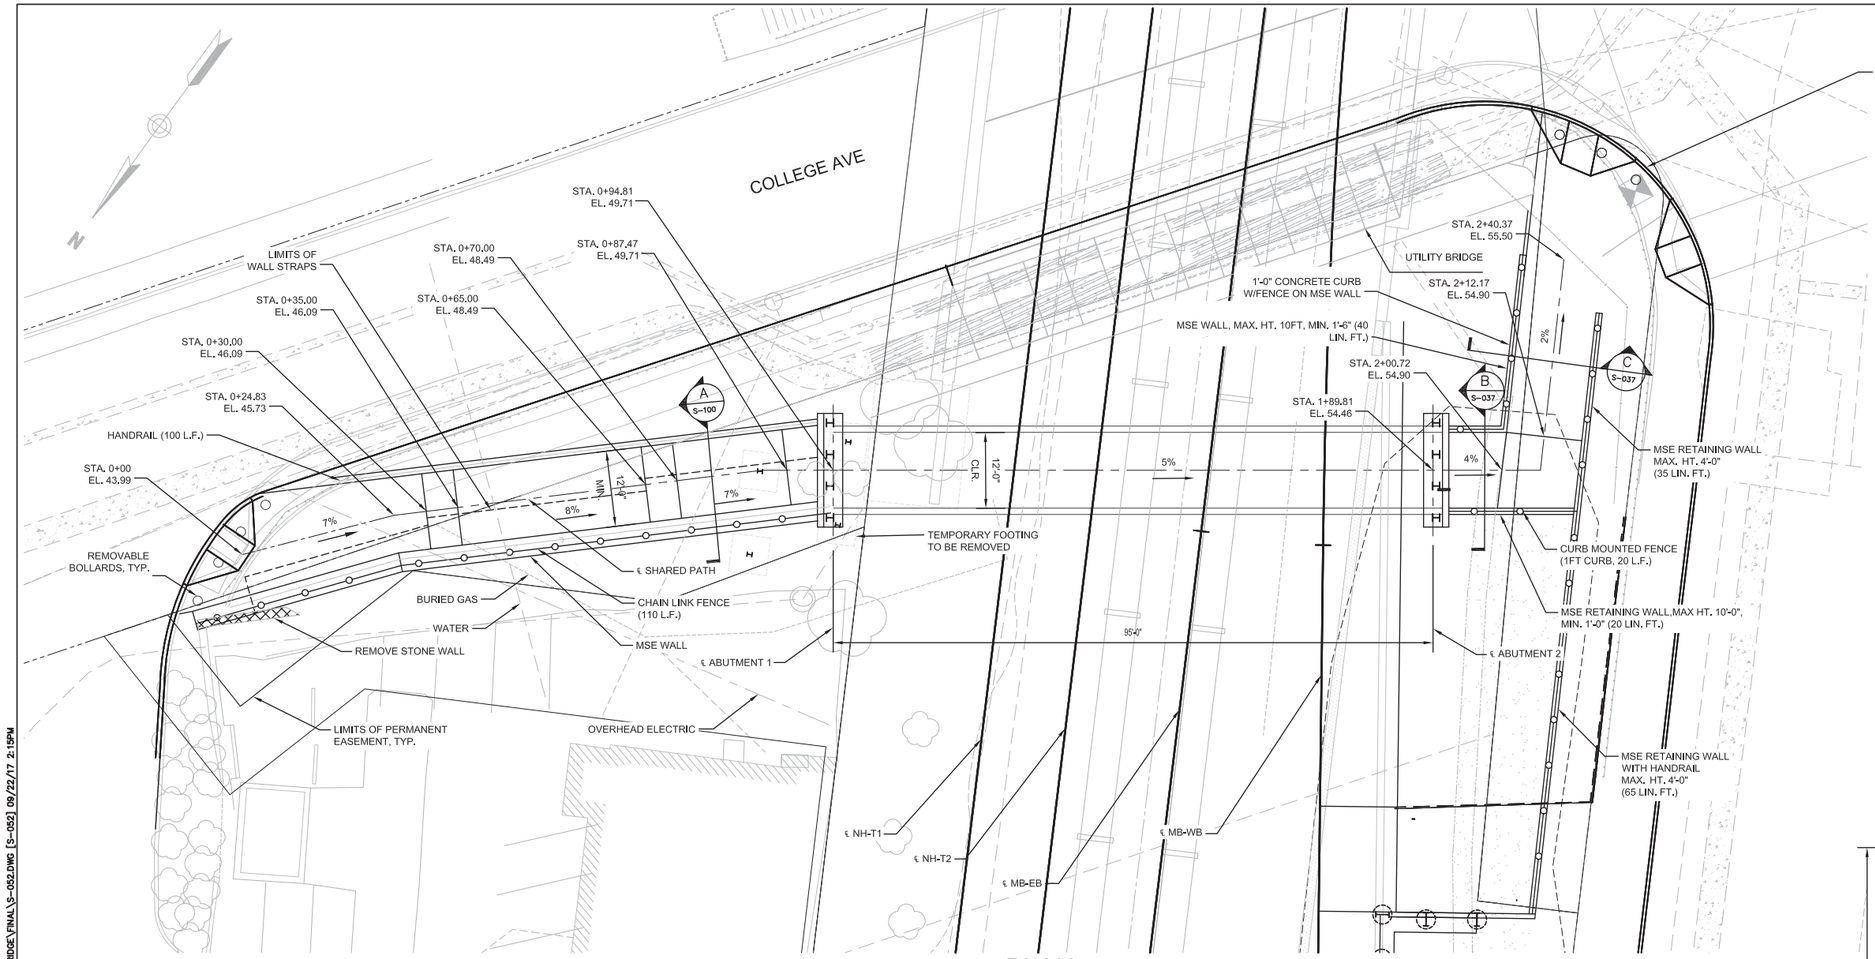


PLAN

NOT TO SCALE

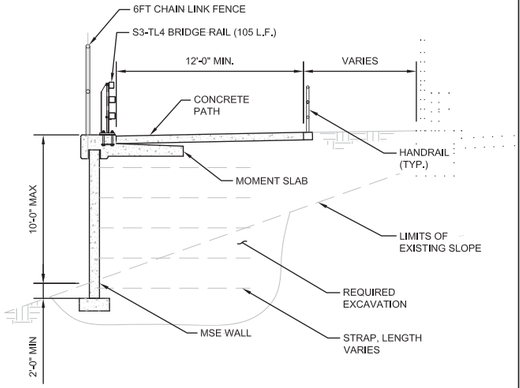


SECTION A

NOT TO SCALE

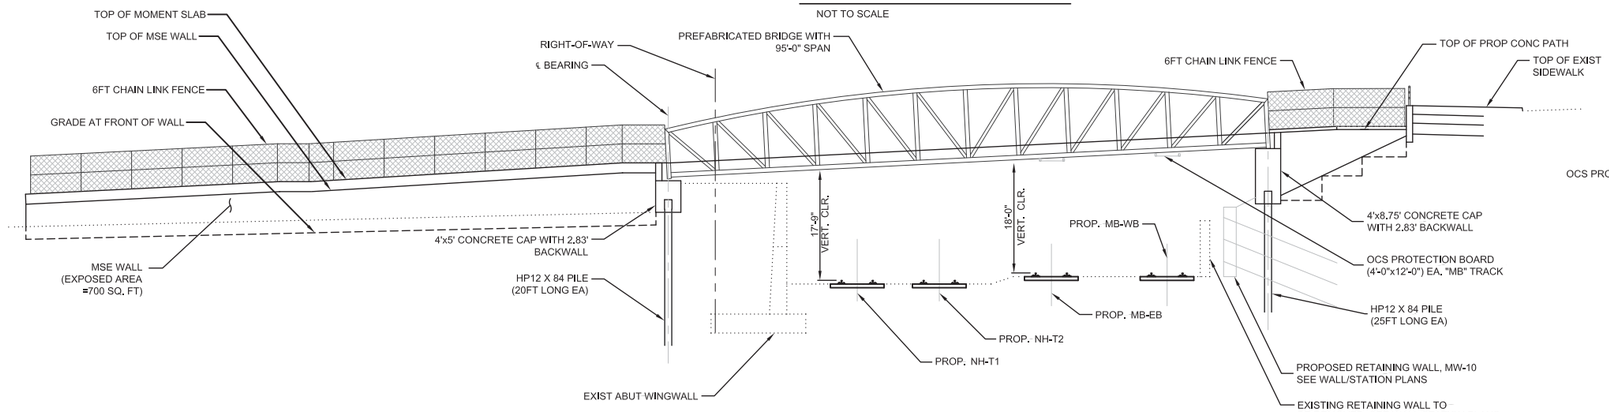

ELEVATION

NOT TO SCALE

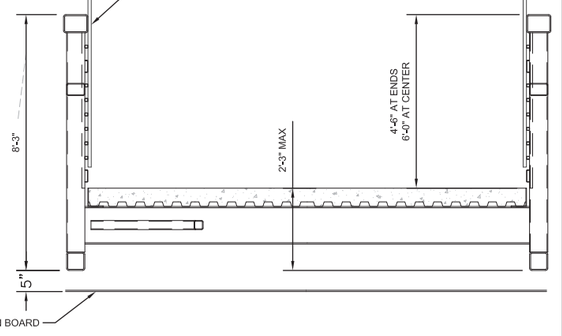

TYPICAL SECTION THROUGH BRIDGE

NOT TO SCALE

NOTES:

1. THE EXISTING CONDITIONS SHOWN ON THIS PLAN ARE BASED UPON A COMPOSITE OF AERIAL MAPPING AND FIELD SURVEY PREPARED BY VANASSE HANGEN BRUSTLIN, INC. ON OR BEFORE MARCH, 2011, AERIAL MAPPING PREPARED BY COL-EAST, INC. ON OR BEFORE JUNE 2011 AND SURVEY PERFORMED BY BRYANT ASSOCIATES ON OR BEFORE OCTOBER 2011.
2. THE VERTICAL DATUM IS NAVD 88 NORTH AMERICAN VERTICAL DATUM OF 1988 AND DERIVED BY CONTROL ON A PLAN ENTITLED "EXISTING CONDITIONS" DATED MARCH 11, 2011 PREPARED BY VANASSE HANGEN BRUSTLIN, INC.
3. TOP OF RAIL ELEVATIONS ARE BASED ON ADVANCE CONTRACT TUFFS INTERLOCKING PROFILE WORK DATED FEB 1, 2017.
4. APPROACH RAMP, SIDEWALK AND BRIDGE TO MEET ADA REQUIREMENTS.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

COLLEGE AVENUE PEDESTRIAN BRIDGE GENERAL PLAN AND ELEVATION

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-272.pdf

SCALE: N.T.S.	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	JMP	JMP	SB	SHEET: S-032	.

PLOTTED: 09/22/17 2:15PM BY KATIE M
DRAWING: X:\PROJECTS\2017\0052800 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CI_BRIDGE\COLLEGE AVE PED BRIDGE\FINAL\S-052.DWG [S-052] 09/22/17 2:15PM

4.3 STATIONS

Each of the seven proposed stations of the Green Line Extension DB Project will serve the community safely and efficiently. Station access and intuitive pedestrian traffic has been carefully thought out and translated into a cost effective design that will suit its riders. Well programmed stations will accommodate ridership numbers safely and consistently during all seasons of year.

Our Lead Designer, STV has served the MBTA for more than 35 years and led the design of multiple passenger stations for light rail, commuter rail, and bus rapid transit, including the Copley Station accessibility upgrade, New Balance Commuter Rail Station Public-Private Partnership, Courthouse Station, and Greenbush Line Rail Restoration Design-Build. Our team's experience and understanding of light rails stations will deliver a high-quality solution that meets the Project schedule.

4.3.A APPROACH TO MEETING THE ARCHITECTURAL REQUIREMENTS

At Gilman Square Station, we have proposed a design to raise the community path and keep it at grade level between Medford Street and School Street. This decision allowed the station entry to connect to the community path with a small elevated platform crossing over the inbound track. This connection now provides two primary access points to the station. This eliminated a 250-foot elevated walkway that had previously only connected Medford Street and a dangerous enclosed 200-foot obscured stretch of the community path that extended below Medford Street.

Each station presented its own opportunity to address individual challenges within each station design. The street level stations, East Somerville Station, Ball Square Station and Union Square Station, are exercises in accessibility and simplicity. At Lechmere Station our proposed design was driven by safety, as our team noticed challenges with obscured views and surveillance. This challenge created an opportunity to simplify the layout and increase sightlines. At-grade stations with headhouses presented challenges with vertical circulation and durable building materials. Gilman Square Station, Magoun Square Station and College Station utilize simple layouts that minimize the need to turn and present at logical progressions from approach, entry and finally boarding the train.

Durable design is imperative to the success of these stations and their ability to effectively serve the public today and in the future. Durability is addressed by selecting appropriate materials and providing a means of maintaining them. Sealed and hardened concrete will primarily compose the headhouses with galvanized and painted structural steel to maximize protection against corrosion. Similarly, all shop fabricated metals will be hot-dipped galvanized and painted. Building joints will be protected by means of flashings and mechanical fastenings. Roofing materials will be specified to have a minimum of a 25-year warranty, thermoplastic membranes being used at enclosed rooms and elevator hoistways with prefinished standing seam metal roofs at stairs, ramps, and bicycle storage areas.

"Our design at Gilman station is a key differentiator that significantly improves safety, enhances circulation while reducing project costs.

Durable design is imperative to the success of these stations and their ability to effectively serve the public today and in the future.

Our architectural design approach to the Green Line station platforms meets the MBTA's design standards and all state and local code requirements while providing a logical, refined appearance. All required circulation clearances will be met to the satisfaction of the MBTA, Americans with Disabilities Act (ADA), and state requirements for public safety.

Approach to Accommodating Passenger Flows

Crime Prevention through Environmental Design Principles. All station elements are visible to the public from a variety of vantage points. At Lechmere Station, Gilman Square Station, Magoun Square Station and College Avenue Station, the entry sequence to the station is direct and unobscured. At each of these entrances, a rider will pass through a security grille and have the option to take stairs or an elevator to the platform. In each case, any single point is visible from multiple angles. Stairs and elevators are open to public view from at least two sides by means of transparent materials or open air enclosures. This will meet the requirements of the MBTA's Boston Center for Independent Living agreement for enhanced accessibility for people with disabilities.

Our open platform design is conducive to Crime Prevention Through Environmental Design (CPTED) principles. It increases visibility while minimizing areas of entrapment for the users, and it reduces isolation. Shelters will be surrounded by transparent acrylic-type material to maintain visibility and reduce likelihood of vandalism and lighting levels will meet the MBTA standards and provide sufficient levels of light to for public safety. We will incorporate Customer Assistance Areas, which will immediately communicate with the MBTA's security and/or police, per MBTA requirements. We will also utilize closed circuit security cameras for safety and surveillance needs.

Design Approach and Strategies to Achieving Full Accessibility. Providing full accessibility is paramount to the success of all seven stations. Codes such as 521 CMR will govern design in the case of handrails, guardrails, sloped surfaces etc. Many of the design concepts already employed at the stations such as direct line of sight, intuitive circulation and logical progression from station approach to the platform consider full accessibility. Further, a clear dimension of 6'-0" walkways, ramps, and stairs is held as a minimum clearance in all stations.

At Magoun Square Station a sloped walkway 15'-0" wide lead pedestrians to the station headhouse. This walkway is straight, does not create any pinch points and leads riders to a staircase and elevator that discharges them at the station platform level. This pedestrian progression occurs without requiring a change in direction, it simply leads riders on the most logical, direct and accessible path.

To achieve the accessibility requirements, all platform elements are centered. This will allow for a minimum of 3'-0" circulation and 6'-0" clearance for platform width, from the edge of the platform to any obstruction, such as shelters, poles, or signage.

"While meeting regulatory requirements, we have placed platform elements in such a way to maximize passenger comfort.

Approach to Achieving an Excellent Customer Experience in the Design of Stations. Within the seven stations, there are ultimately three distinct design types:

- The three at-grade station types, (East Somerville, Ball Square and Union Square)
- The elevated approach (Magoun Square, Gilman Square Station and College Avenue)
- The elevated platform (Lechmere)

While these three station types are unique and provide the opportunity to create interesting design solutions, it is crucial to provide a recognizable connection between all seven stations tying them together as one cohesive design. Our primary design approach in cultivating excellent customer experiences is simplicity. Simplicity in our design proposal is translated through a recognizable design feature and intuitive circulation by minimizing directional change. These design features create a logical, comfortable, and accessible progression from approach to the station, accessing the platforms, and utilizing the trains.

The platform design considers the importance of the user experience, including:

- Incorporating video message boards that keep riders informed about train arrival and departure times
- Providing strategically placed benches and shelters to keep riders safe from the natural elements
- Integrating a barrier-free design for wheelchair accessibility on the platform and into the shelters
- Including a minimum of three benches will be available at each platform to provide a resting area for riders

In addition, Customer Assistance Areas are available for informational purposes or for safety and security measures as necessary. Wayfinding signage and maps will be clearly visible and regularly interspersed along the platform coordinated with the MBTA wayfinding design standards, and we will have sufficient lighting to provide an added layer of safety in the evenings.

Approach to Ensuring Each Station is Clearly Identified

Each station is identified with proper signage to direct pedestrians to the station entrance. Station architecture and signage will be legible and recognizable for pedestrians and motorists.

As riders approach the platform, the MBTA's standard signage will be first, foremost, and obvious. Signage frames with the station name, maps for inbound and outbound lines, and an overall MBTA system line map will be clearly visible.

Approach to Interfaces with Existing Right-of-Way

Each station will be located either within the existing right of way or the acquired right of way. Each station will provide ADA-compliant access to existing sidewalk or the proposed community path.

Interfaces with Adjacent Vehicular Traffic. Stations will interact with traffic on the adjacent roadways in three ways:

1. Increased pedestrian traffic to and from the station will conflict with vehicular traffic at the surrounding intersections. GLX Constructors will make physical improvements to affected intersections and optimize traffic signals to minimize delay and maximize safety and accessibility for all users. Improvements such as constructing an over-the-track pedestrian bridge to access the station as shown on College Avenue Station, and utilizing the Community Path to enter the station on Gilman Square Station and East Somerville.
2. Pedestrians have a tendency to use the curbside as a drop off and pick up space. Station designs will account for this behavior by either creating formal drop-off areas to help organize passengers' movements, or by including features to discourage stopping on the street where it would be dangerous or disrupt the flow of traffic.
3. Station features will be easily visible. The architecture and signage will be recognizable, attractive, and legible for both pedestrians and motorists.

Interfaces with Bicycle Paths. A bicycle-friendly design will extend from Green Line stations to virtually all of Somerville and Medford. Our team is familiar with this area and with cyclists' needs. For example, the touchdown points, where station walkways meet the street, will account for different directions and passengers arriving to station entrances. These entrances will be located as close as possible to crosswalks, so they can be reached safely from either side of the street. Bicycle infrastructure at the station, such as bike cages and racks, will be located as close as possible to where cyclists would naturally dismount. By doing so, bicyclists will not have to push their bikes through crowds, and they are not tempted to ride on sidewalks, which is a safety concern.

Description of the Shelter Design

The shelter design will conform to the platform's light pole spacing and available width. Once light pole spacing and final platform width is determined, accommodating the seating lengths and space for wheelchair access between light poles will determine width. The depth of shelters will be determined by the width of the narrowest platform with clear access route dimensions, as provided by station platform standards. As that is determined, the dimensions will be applied to the remainder of the station platforms. The minimum number of shelters for the open platforms is indicated in the technical provisions.

Approach to Materials and Finishes. Shelters will be designed using many types of metals, such as stainless steel, galvanized steel, painted steel, anodized or painted aluminum, or other materials, such as woods and structural plastics. In our experience, metals are the most effective material that requires the least amount of maintenance.

Approach to Envelopes. Our approach to designing the shelter envelopes is CPTED-compliant with transparent appearances that eliminate any hidden areas within or around the shelter.

We will use clear acrylic, or other clear forms of plastic or safety glazing, for the shelter envelope to deliver transparency. The glazing panels at the shelter perimeter and roof will be vandalism proof. From a safety perspective, this will allow the light from the light poles to penetrate through the roof and adequate lighting in the shelters.

Approach to Weather Protection. With the open platform approach, it is imperative to provide a sufficient number of platform shelters for riders during inclement weather. Platform shelter quantity shall be determined by the technical provisions within the RFP. The shelter construction will contain strengthened glazing panels (acrylic and/or polycarbonate) with a framing system to protect from year-round weather patterns. The roofing panels will slope outward so that water drips away from openings. Glazing panels will be anchored to structure, gasketed, and sealed to prevent water from dripping and vapor from migrating into the shelter.

Methodology Used to Determine the Number and the Size of Shelters at Each Station. In determining the number and size of the shelters at each station, we studied the MBTA's trends for selecting shelter types, design, and construction. We reviewed half a dozen shelters that are customizable and have a progressive design. These shelters also have interchangeable components that accommodate the shelter's layout, which we determine by the requirements established in the Technical Provisions.

Approach to Organization of Required Platform Equipment, Elements, and Amenities. Largely, the organization of platform elements, equipment, and amenities will be dictated by the MBTA's standards indicated in the Technical Provisions.

Signage with maps will be located closest to platform entrances, while signage with advertisements will be located furthest from the entrances. Signage that offers customer assistance will be sheltered, and it will be located in front of the second door of the lead train facing both the inbound and outbound tracks. Message boards and fare vending machine locations are similarly indicated in the Technical Provisions, and they require careful coordination with other platform elements.

Shelters and benches will be equally spaced between signage requirements and light poles. Light poles are spaced to maximize the lighting level requirement at the heights indicated in the Technical Provisions. All additional elements and amenities, such as the official's booth, trash receptacles, and sand and salt sheds, will be efficiently interspersed throughout the platform.

4.3.B ARCHITECTURAL DRAWINGS OF EACH STATION

Architectural drawings of each station are included at the end of this section.

Context Plans, Signage, Lighting, Catenary, and Fare Collection Equipment

Lechmere Station. As the only station that is part of the Green Line Extension DB Project with an elevated platform, it was important to thoughtfully identify the challenges and opportunities associated with design a station of this type. Visibility and intuitive connection becomes more of a challenge. Therefore, direct access and two primary points of entry help to increase the station's ability to be recognizable. Sightline views from five streets reveal transparent stair enclosures, glass elevators and station signage that will clearly indicate that riders are to progress to an upper level where train are boarded. After riders make their way to the lower level of the head house and proceed to the upper level, they simply arrive at the platform at the top of either a stair or elevator.

Union Square Station. The lollipop signs located on Prospect Street and a clear street connection intuitively guide riders to the entry of Union Square Station. From this vantage point, the roll up security grill supporting the Union Station sign is clearly visible between the track ends. At the east end of the platform a second means of egress is at the south end of the platform and exits the ROW.

East Somerville Station. East Somerville Station is accessed either from Washington Street via the lower community path, or the upper community path. For those entering from Washington Street, the station is marked by a lollipop sign at the sidewalk. A second lollipop sign will be placed at the upper community path landing parallel to the platform. A second means of egress is provided at the north end of the platform on to the upper community path.

Gilman Square Station. Accessed via the Community Path at grade level between Medford Street and School Street, a short platform over the inbound tracks serves as the station's entry. Space accommodations for the catenary equipment have been made under this platform. This simple connection engages the community path and provides two primary access points to the station via Medford Street and School Street. Bike storage is available along the community path directly across from the roll-up security grill at the station entry. Entry through security grill leads to the station headhouse with a stair and elevator discharging on the platform. A second means of egress is located at the west end of the platform with an at-grade walkway leading to a covered switchback ramp terminating at the School Street Bridge.

Magoun Square Station. Access to the station from the Lowell Street Bridge is indicated by a lollipop sign at the beginning of a slightly sloped walkway to the station headhouse. Access directly off of Lowell Street begins at an elevated platform spanning over the inbound track where bike storage and fare vending machines are available. The sloped walkway provides direct sightlines to headhouse where stairs and an elevator discharge riders directly on to the platform. This station is highlighted by a single direct means access with no direction changes and an intuitive approach and exit from the platform.

Ball Square Station. Visibility of the Ball Square Station is highlighted in the design in order to approach the challenge of a single access point. This access point is located close the intersection of Boston Avenue and Broadway Street in order to increase exposure to pedestrians. Bike storage and MBTA signage occupies the station's frontage along Boston Ave. Along the bike cage, sloped walkways guide riders to the station's entry where a roll up security grill secures the station. Emergency egress is provided at the north side of the platform with a sloped walkway guiding riders to a point of safety.

College Avenue Station. College Station is just outbound of the College Avenue Bridge. Riders enter the station headhouse from a sidewalk along Boston Avenue. The access to the headhouse bridges the rail line. Space accommodations for the catenary equipment have been provided under this structure. The MBTA station signage will be visible from a new pedestrian bridge paralleling the existing College Avenue Bridge, as well as, along Boston Avenue. A direct line of sight to a stairway leading to the platform is visible upon entry to the station house via a roll up security grill along the Boston Ave station entry. Riders may follow a walkway adjacent to the stairway to access two elevators with covered queuing space. Upon discharge from the stairway and elevators, a short pathway at the lower level of the headhouse allows access on the platform. Similar to Magoun Station an accessible safety dispersal area will be provided at the north end of the platform.

Fare Collection Equipment. The fare collection equipment will be provisioned by providing fiber optic cabling and network connectivity infrastructure at each station. Fare vending machines are provided under the MBTA's AFC2.0. Fare entrance gate arrays are expected to be no longer part of the fare collection program at the time of completion for the Project.

The Supervisory Control and Data Acquisition (SCADA) with Hub Monitoring and Control System (HMCS) will be automatically and manually monitor an array of systems and subsystems within the MBTA's infrastructure, including ancillary facilities.

Lighting. LED full, cut off pole-mounted lighting fixtures are provided on platforms where the highest lighting levels are desired, which is 35 foot candle on average, and 55 foot candle along the platform edge. Poles are spaced at 15 feet on center with the appropriate number of fixtures to achieve these foot candle levels and as not to encroach on the travel path along the platform and passenger waiting areas, as dictated by MBTA standards.

Lighting on entrance and exit paths to the platform will also be provided by pole-mounted lighting fixtures, except where overhangs or structures are present. In these spaces, a combination of both pendant and surface mount lighting fixtures have been selected and will be designed to provide appropriate lighting levels in accordance with MBTA standards and life safety requirements.

All fixtures selected will be rough service type, appropriate for outdoor conditions, and will be mounted at a height such that access for maintenance and cleaning can be achieved via step ladders.

All lighting will be controlled centrally through a photocell and timeclock combination, which will allow the MBTA to control on/off for outside of revenue hours.

HVAC and Plumbing. Lechmere and College Station have occupied rooms that require heating, ventilating, and air conditioning for the comfort of the MBTA's staff. Systems will be designed to meet state code requirements, specifically the International Energy Conservation Code and the International Mechanical Code.

Unoccupied spaces, including emergency electrical, communications, and EMF rooms are provided with electric unit heaters and ductless split air conditioners to control the space conditions. Main electrical rooms are provided with electric heat for the winter and exhaust fans for summer ventilation. Elevator control rooms are provided with electric heat, ductless split cooling and ventilated per the requirements of 524 CMR, the Board of Elevator Regulations. Elevator hoist ways have vents as required under 524 CMR. The condensers for cooling at Gilman, Ball, Magoun, East Somerville, and Union Stations are located outside the communication rooms at grade, typically between the two tracks at the end of the stations. The condensers for Lechmere and College are located on roofs or at grade away from passenger traffic.

At Lechmere Station, the Police Reporting Station and Bus Operation booth are served by a variable refrigerant flow heat pump for heating and cooling, with ventilation air through an energy recovery ventilator for energy savings. The toilet room and janitors closet are heated by baseboard heaters and exhausted with the energy recovery ventilator. At College Station, the Operators Lounge is heated and cooled by a variable refrigerant flow heat pump, and an energy recovery ventilator provides fresh air to the Operator's Lounge and exhaust for the toilet and janitor's closet. Baseboard heat is provided to the toilet and janitor's closet.

The station plumbing design for all stations will follow all state codes and will comply with ADA codes. Plumbing systems at College Station and Lechmere include toilet and lavatories in the men's and women's rooms, and service sinks in the janitors closets. Kitchen-type sinks are also provided in the Lechmere

kitchenette and the College Station Operator's Lounge. Hot water is provided by instantaneous, tankless water heaters. Locking exterior frost-proof hose bibbs are provided at both stations for wash down purposes. All plumbing fixtures will be served by an incoming domestic water service and sanitary system. Storm drainage and downspouts will be routed from roof areas of the vertical circulation elements (elevator and stair headhouses) at College, Gilman, and Magoun Stations down to a closed drainage system at all stations, which is typically located within the track bed below the subgrade, with the exception of Lechmere which the closed system will be below street level.

Additional Details or Key Dimensions to Demonstrate Technical Provisions are Met or Exceeded

- Stairs and ramps will be covered with standing seams roofs that extend 5'-0" beyond the top and bottom landing or stair run. Similarly, elevator entry/exits are covered by a 5'-0" deep overhang.
- Walkways with slopes below 4.5 percent transition from walkways or headhouses down to the platform as shown in the included drawings. Stations are designed to accept a 6" topping slab in the future, bringing the top of platform at to a height of 14" above top of rail.
- Platform light poles attach to the top of 6" concrete pedestal. Light poles can be removed and re-fastened after the 6" topping slab is complete. This will not impact the existing slab or light pole foundation. Shelter's benches and other platforms elements will be attached to the new slab with concrete anchors or epoxy anchors.
- All platforms, with the exception of Lechmere, are 225' feet long with varying widths, however not any smaller the 20'-0" in width. A 75'-0" space for extension has been allowed for future extension.
- All stairs are designed to have 7" maximum riser heights and 12" tread lengths.
- All handrails are 1½" outside diameter heavy wall 316L stainless steel and will be continuous.
- Elevator queuing space extended at minimum of 9'-0" deep from elevator doors and does not extend into a main path of travel.
- Areas of rescue assistance, 5'-0" x 9'-0" deep, are located adjacent to elevator doors and do not encroach on the main path of travel.


GLX Constructors' has carefully reviewed the Volume 2 Technical Provisions section 12.1 through 12.5 and the related project definition plans as they relate to the design and operation of the seven Green Line Extension Project stations. Based on our collective experience and understanding of the Project requirements, we have developed a design approach for each of the seven stations which emphasizes:

- *Intuitive direct circulation*
- *Durable building materials*
- *Rider safety*
- *Ease of maintenance*
- *Logical design principles*

ITP Request	RFP		
	Drawing Number	Drawing Title	Reference Section or Drawing
Lechmere			
A5.2.3.B.1			4.3(STA-001); 4.6(C-004)
A5.2.3.B.2	STA-001	Lechmere Station – Site Plan – Street Level	
A5.2.3.B.2	STA-002	Lechmere Station – Lobby Level Plan	
A5.2.3.B.2	STA-003	Lechmere Station – Platform Level Plan	
A5.2.3.B.2	STA-004	Lechmere Station – Platform and Furnishings	
A5.2.3.B.2	STA-005	Lechmere Station – Platform and Furnishings	
A5.2.3.B.3	STA-006	Lechmere Station – Elevations	
East Somerville			
A5.2.3.B.1			4.3(STA-007); 4.6(C-009)
A5.2.3.B.2	STA-007	East Somerville Station – Site Plan	
A5.2.3.B.3	STA-008	East Somerville Station – Platform and Furnishings	
Gilman Square Station			
A5.2.3.B.1			4.3(STA-009); 4.6(C-014)
A5.2.3.B.2	STA-009	Gilman Square Station – Site Plan	
A5.2.3.B.2	STA-010	Gilman Square Station – Overall Plan	
A5.2.3.B.2	STA-011	Gilman Square Station – Emergency Egress Ramp Elevations	
A5.2.3.B.2	STA-012	Gilman Square Station – Building Sections	
A5.2.3.B.3	STA-013	Gilman Square Station – Platform and Furnishings	
Magoun Square			
A5.2.3.B.1			4.3(STA-014); 4.6(C-017)
A5.2.3.B.2	STA-014	Magoun Square Station – Site Plan	
A5.2.3.B.2	STA-015	Magoun Square Station – Overall Plans	
A5.2.3.B.2	STA-016	Magoun Square Station – Building Sections	
A5.2.3.B.3	STA-017	Magoun square Station – Platform and Furnishings	

ITP Request	RFP		
	Drawing Number	Drawing Title	Reference Section or Drawing
Ball Square			
A5.2.3.B.1			4.3(STA-018); 4.6(C-020)
A5.2.3.B.2	STA-018	Ball Square Station – Site Plan	
A5.2.3.B.3	STA-019	Ball Square Station – Platform and Furnishings	
College Avenue			
A5.2.3.B.1			4.3(STA-020); 4.6(C-023)
A5.2.3.B.2	STA-020	College Avenue Station – Site Plan	
A5.2.3.B.2	STA-021	College Avenue Station – Station Platform Floor Plan	
A5.2.3.B.2	STA-022	College Avenue Station – Boston Ave Floor Plan	
A5.2.3.B.2	STA-023	College Avenue Station – Building Sections	
A5.2.3.B.3	STA-024	College Avenue Station – Platform and Furnishings	
Union Station			
A5.2.3.B.1			4.3(STA-025); 4.6(C-031)
A5.2.3.B.2	STA-025	Union Station – Site Plan	
A5.2.3.B.3	STA-026	Union Station – Station Platform and Furnishings	

Technical Solutions Drawing Matrix.

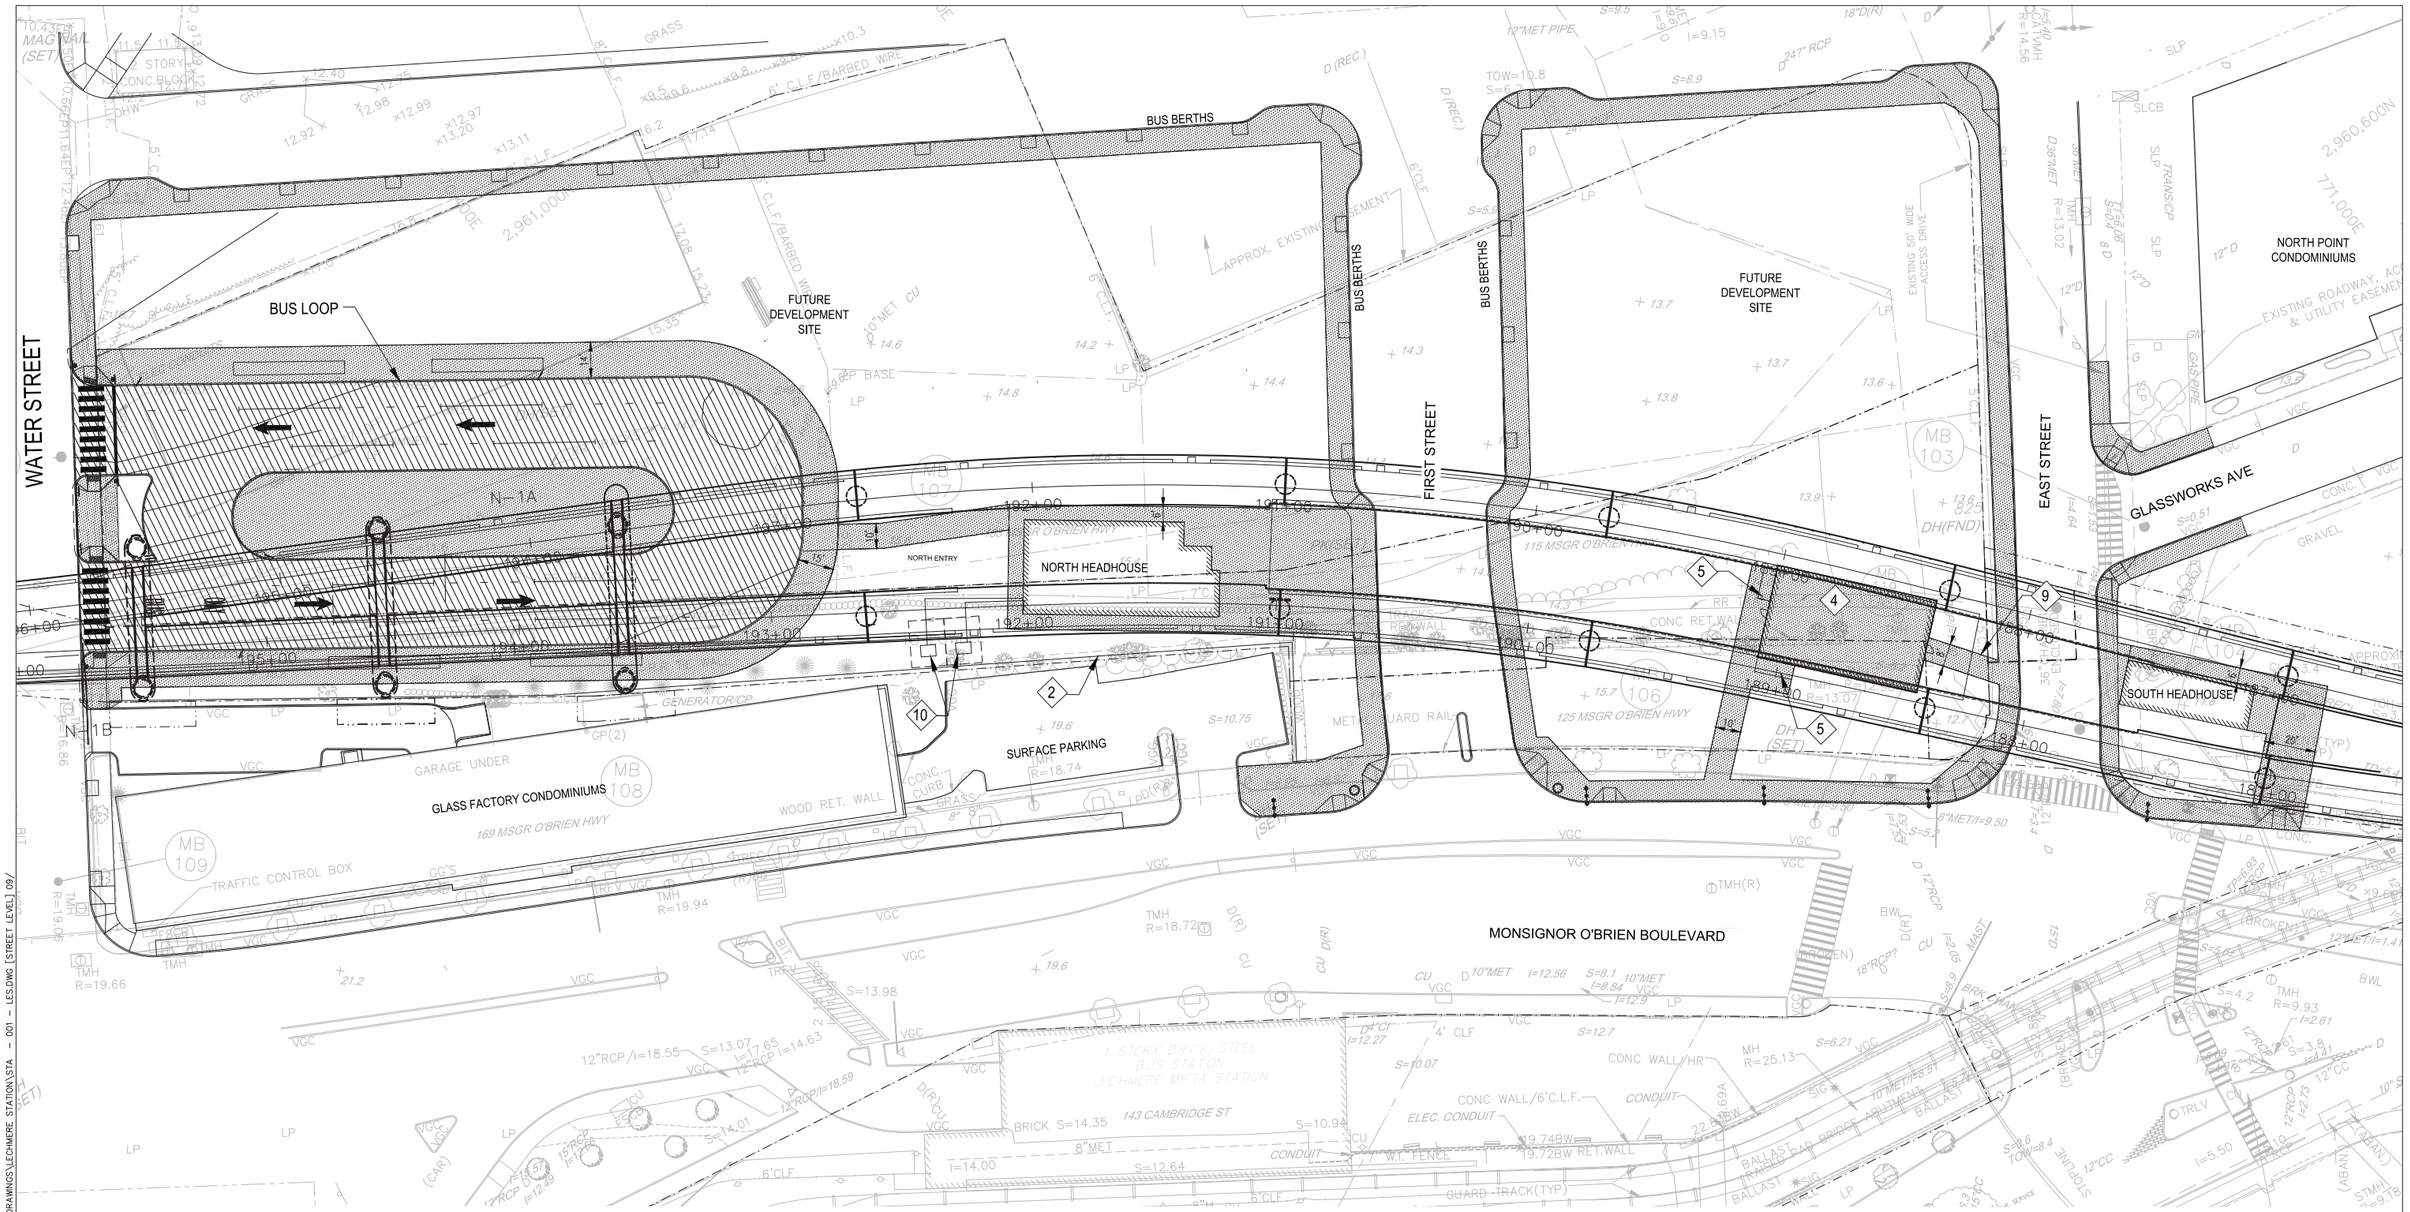

1 SITE PLAN
SCALE: 1"=30'

KEYNOTES

2 CHAINLINK FENCE
4 BICYCLE STORAGE
5 BICYCLE RACK
9 ACCESSIBLE PATH
10 TRANSFORMER

LEGEND

PROPOSED CONCRETE
PROPOSED ASPHALT

0 30' 60'
SCALE: 1"=30'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

LECHMERE STATION
SITE PLAN - STREET LEVEL


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT 28, 2017	YQT	YQT	MWR	SHEET: STA-001	


PLOTTED: 09/14/17 11:56AM BY: TANGYQ
DRAWING: I:\PROPOSALS\2017\C0062820 0002 GLX GREEN LINE STATIONS\CIVIL SITE DRAWINGS\LECHMERE STATION\STA - 001 - LES.DWG [STREET LEVEL] 09/

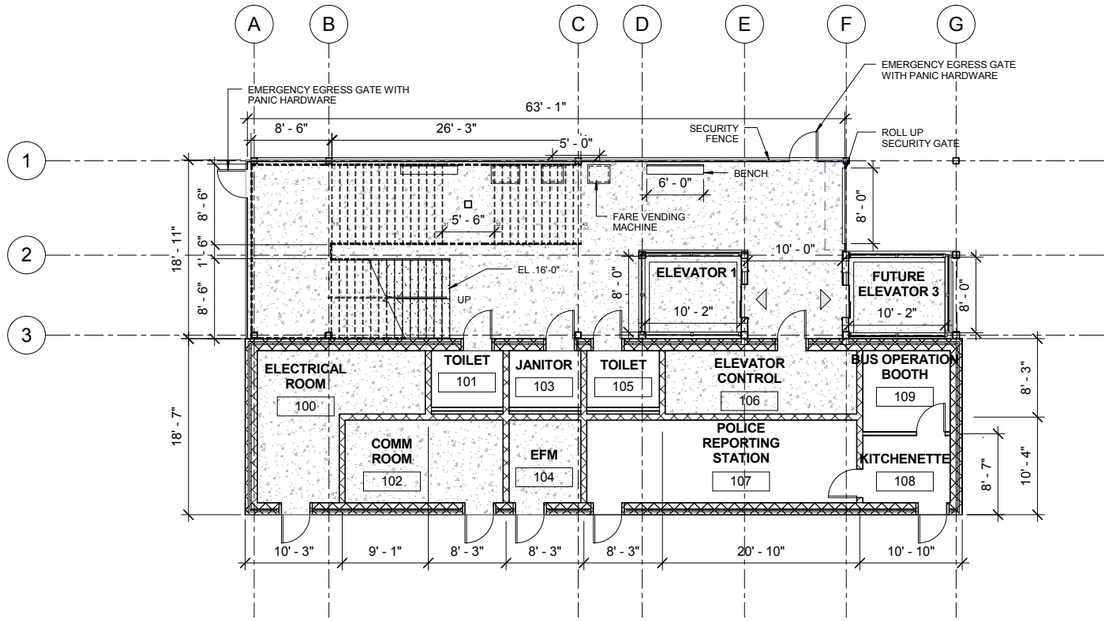

LOBBY LEVEL- STATION NORTH ENLARGED

2 / 002 — 1/8" = 1'-0"


0 4' 8' 16'

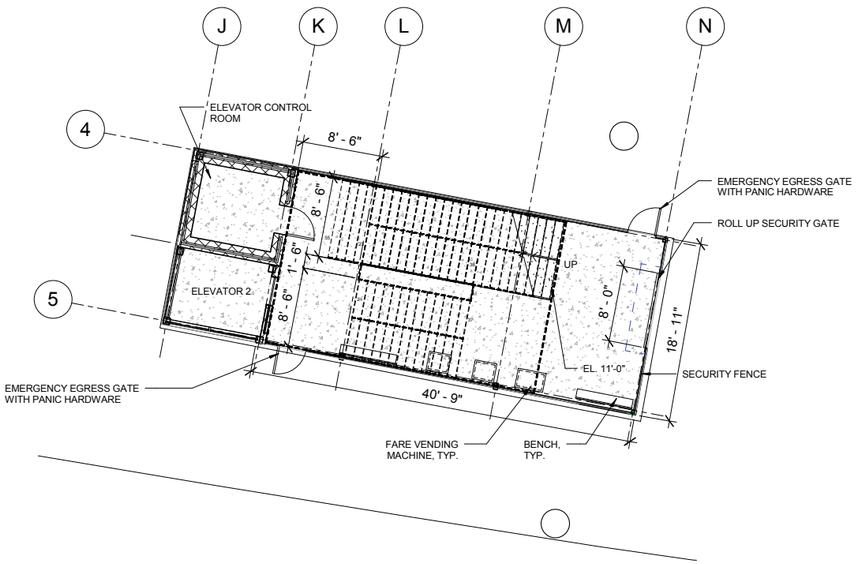

LOBBY LEVEL- STATION SOUTH ENLARGED

3 / 002 — 1/8" = 1'-0"

0 4' 8' 16'

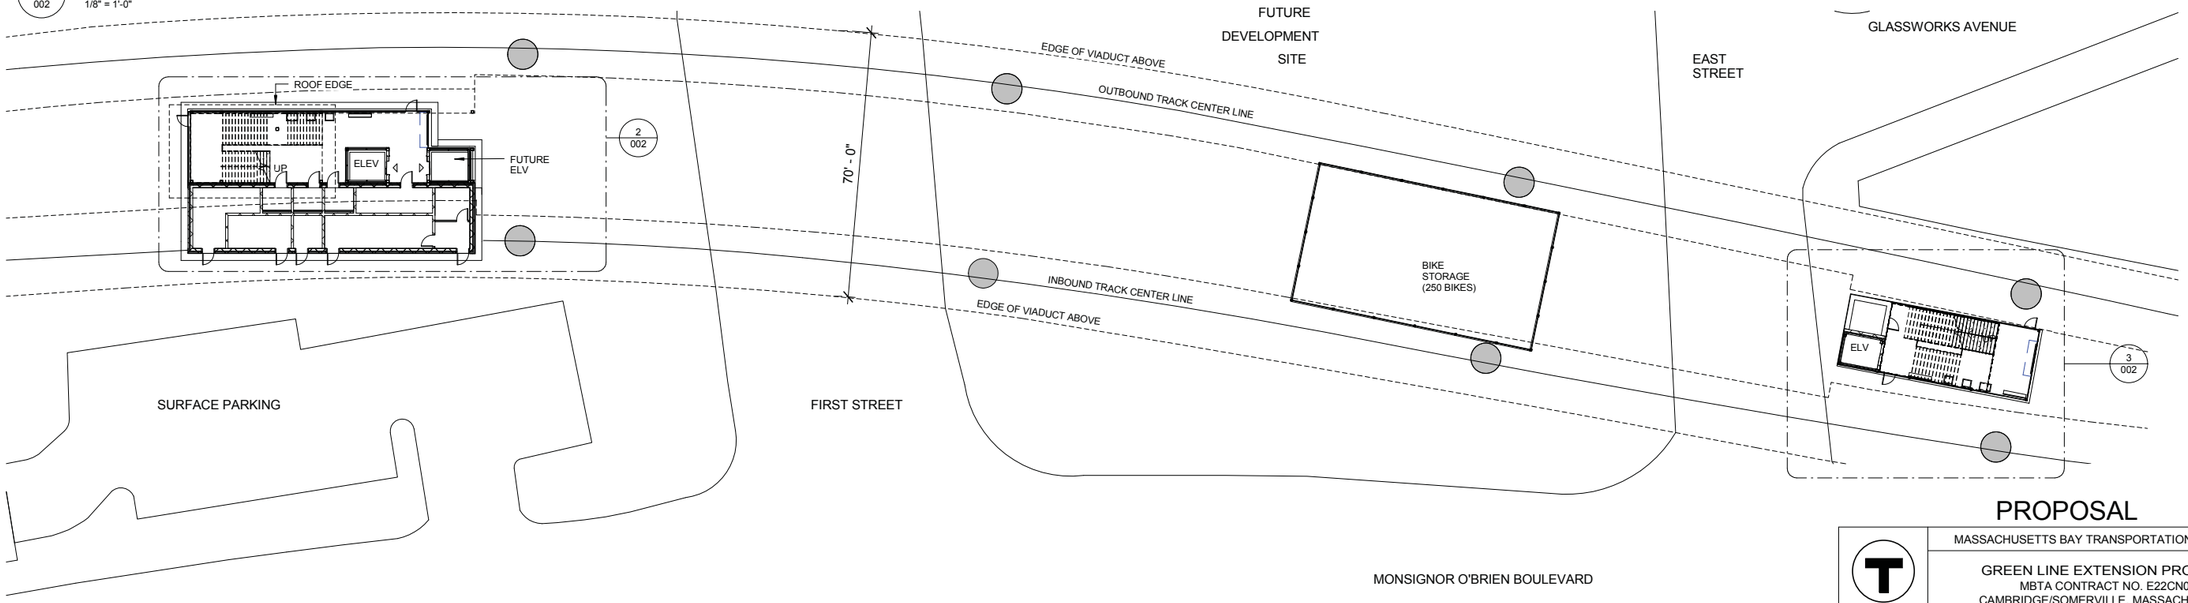

LOBBY LEVEL NORTH

1 / 006 — 1" = 20'-0"

20' 10' 0 20'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


LECHMERE STATION
LOBBY LEVEL PLAN

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf


SCALE: As indicated	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	MS	SM		SHEET: STA-002	

9/14/2017 1:45:16 PM
C:\Users\shelbuaj\Documents\Lechmere_A3D0000_Shelbuaj.rvt

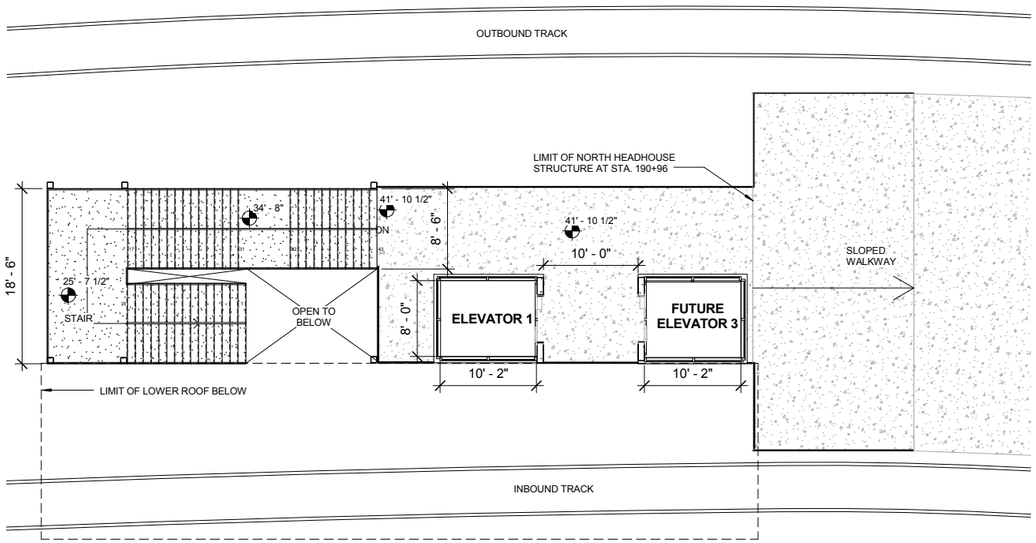


2 / 003 PLATFORM LEVEL - STATION NORTH ENLARGED

1/8" = 1'-0"

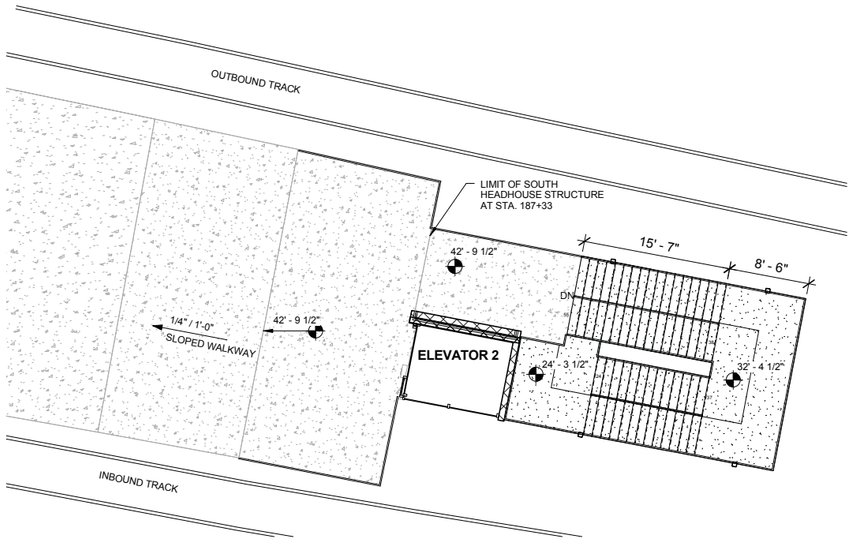

3 / 003 PLATFORM LEVEL - STATION SOUTH ENLARGED

1/8" = 1'-0"

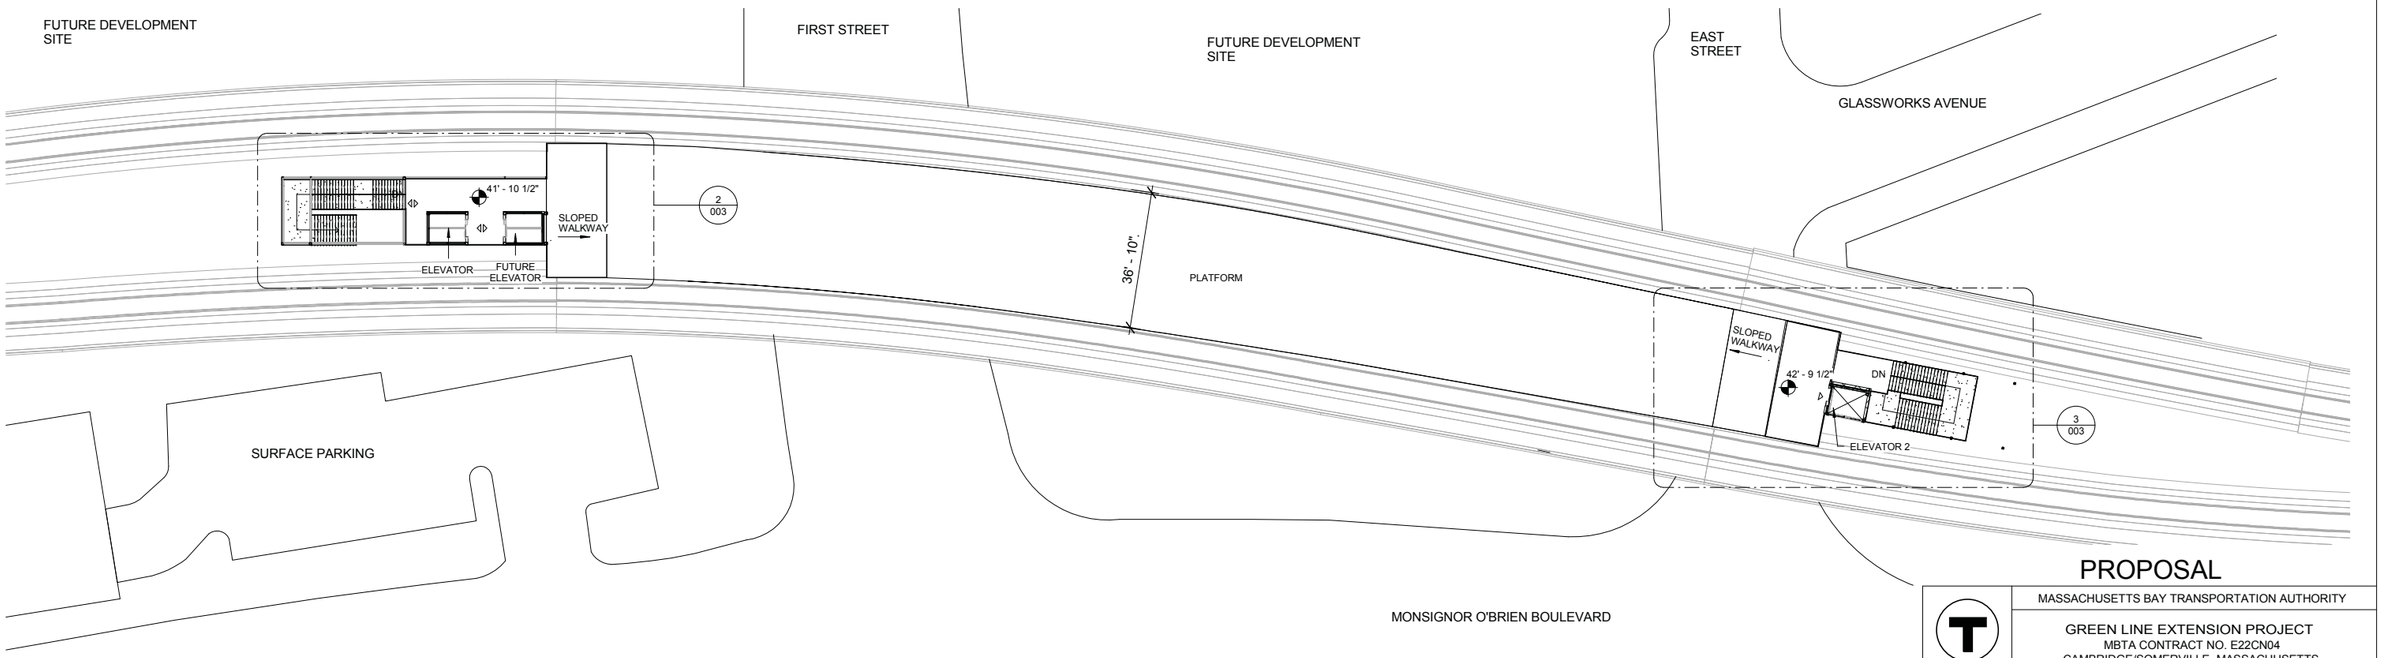

1 / 006 PLATFORM LEVEL STATION PLAN

3/64" = 1'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

LECHMERE STATION
PLATFORM LEVEL PLAN

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-273.pdf

SCALE: As indicated	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	MS	SM		SHEET: STA-003	

9/14/2017 1:53:05 PM
C:\Users\shelbuaj\Documents\Lechmere_A3D0000_Shelbuaj.rvt


KEYNOTES

10 - PLATFORM
11 - CUSTOMER ASSISTANCE AREA & BENCH
12 - SHELTER
14 - TACTILE EDGE
15 - OFFICIALS BOOTH
16 - EMERGENCY EGRESS @ RAISED PLATFORMS
17 - EMERGENCY GATE @ RAISED PLATFORMS
20 - SIGNAGE MAP ASSEMBLY
36 - LIGHT POLE
40 - WASTE RECEPTACLES
41 - SALT STORAGE BIN
42 - SAND STORAGE BIN
43 - STARTER'S BOOTH @ (UNION & COLLEGE STATION)
44 - VARIABLE MESSAGE SIGNS (VMS)

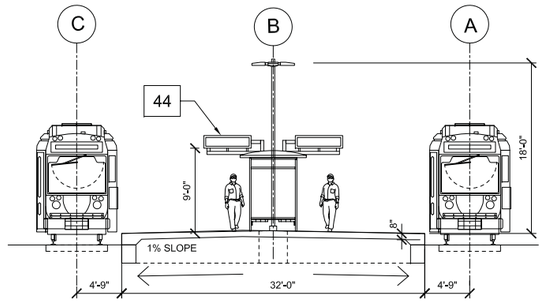

PLATFORM ELEVATION - 2

1/8"=1'-0" 0 4' 8' 16' TYPE 4

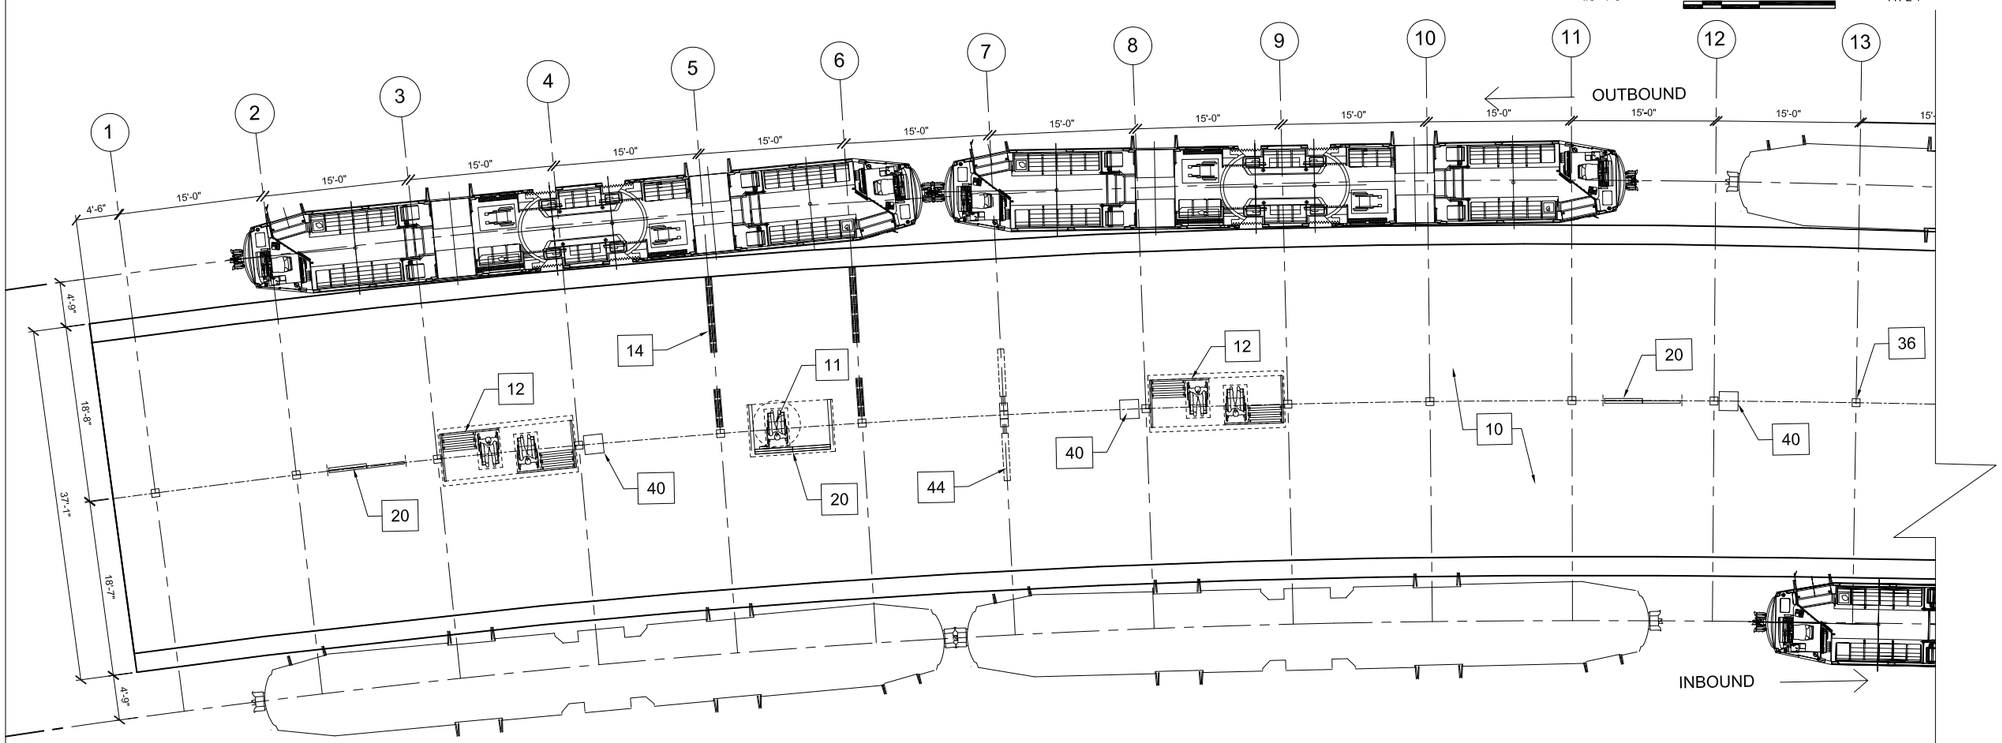


PLATFORM FLOOR PLAN - PART 1

1/8"=1'-0" 0 4' 8' 16' TYPE 4 DATE: 7-14-17

TYPE 4-WIDTH VARIES (32'-0" to 37'-0")
LECHMERE STATION

TOTAL LENGTH @ CENTER LINE OF PLATFORM=339'-4"

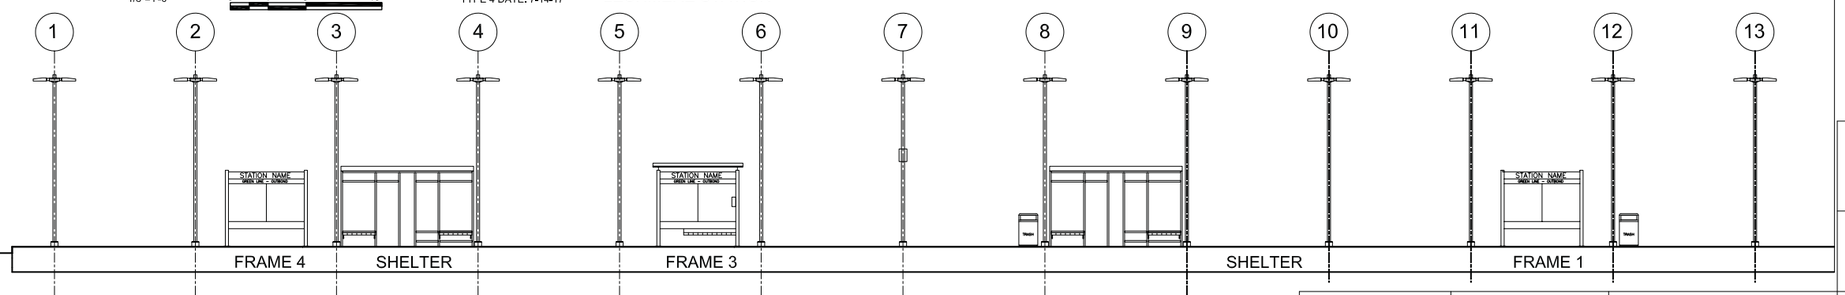

PLATFORM ELEVATION - PART 1

1/8"=1'-0" 0 4' 8' 16' TYPE 1A DATE: 7-14-17

PLATFORM TYPE 4 - LECHMERE- 32'-0" to 37'-0" WIDE PLATFORM

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

LECHMERE STATION
PART 1, STATION PLATFORM
ELEVATION AND SECTION

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	EMT	SHEET: STA-004	.


KEYNOTES

10 - PLATFORM
11 - CUSTOMER ASSISTANCE AREA & BENCH
12 - SHELTER
14 - TACTILE EDGE
15 - OFFICIALS BOOTH
16 - EMERGENCY EGRESS @ RAISED PLATFORMS
17 - EMERGENCY GATE @ RAISED PLATFORMS
20 - SIGNAGE MAP ASSEMBLY
36 - LIGHT POLE
40 - WASTE RECEPTACLES
41 - SALT STORAGE BIN
42 - SAND STORAGE BIN
43 - STARTER'S BOOTH @ (UNION & COLLEGE STATION)
44 - VARIABLE MESSAGE SIGNS (VMS)

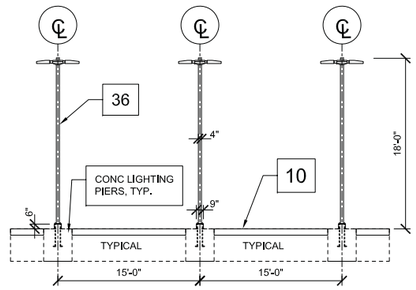


LIGHT POLE SPACING

1/8"=1'-0" 0 4' 8' 16'

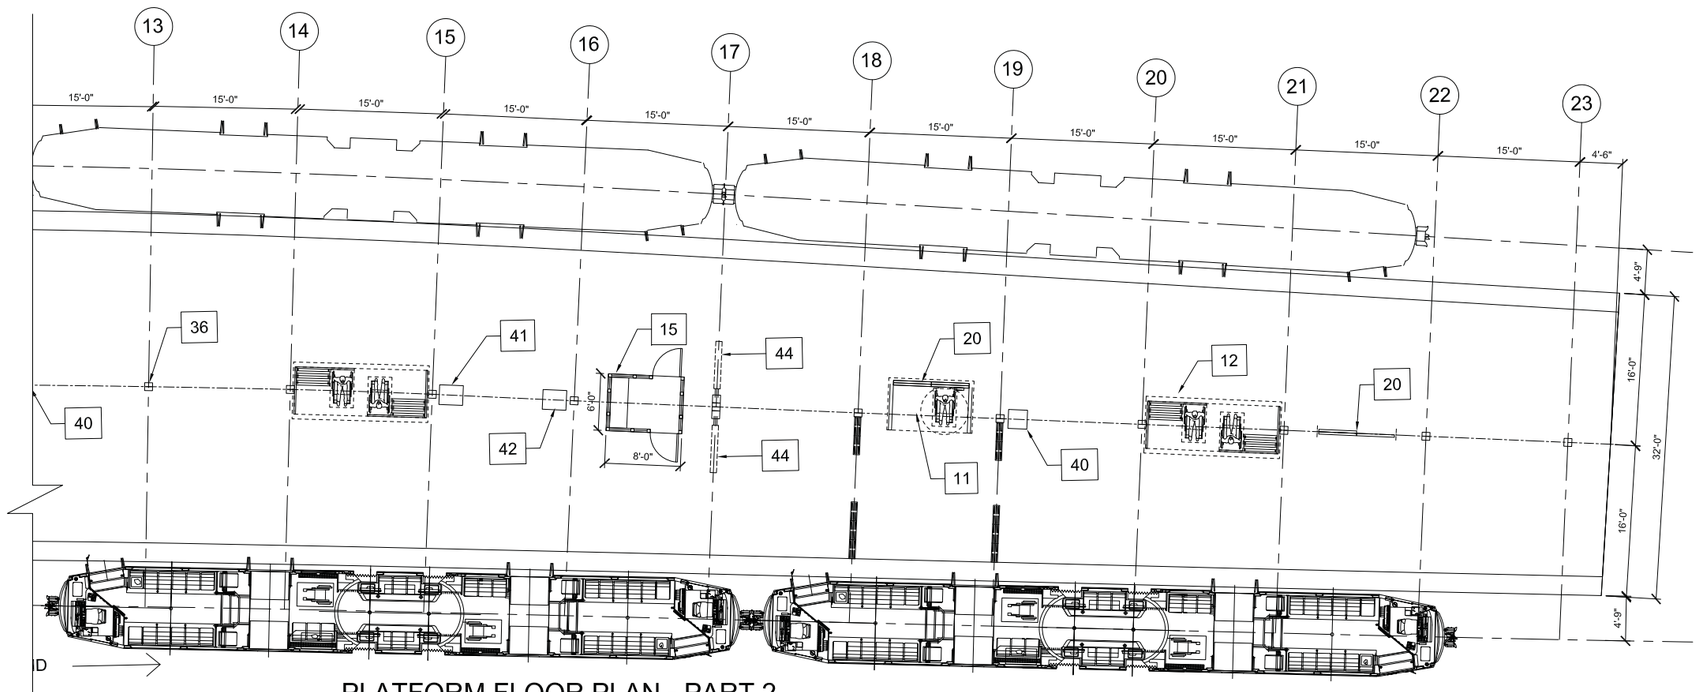

PLATFORM FLOOR PLAN - PART 2

1/8"=1'-0" 0 4' 8' 16' TYPE 4 DATE: 7-14-17

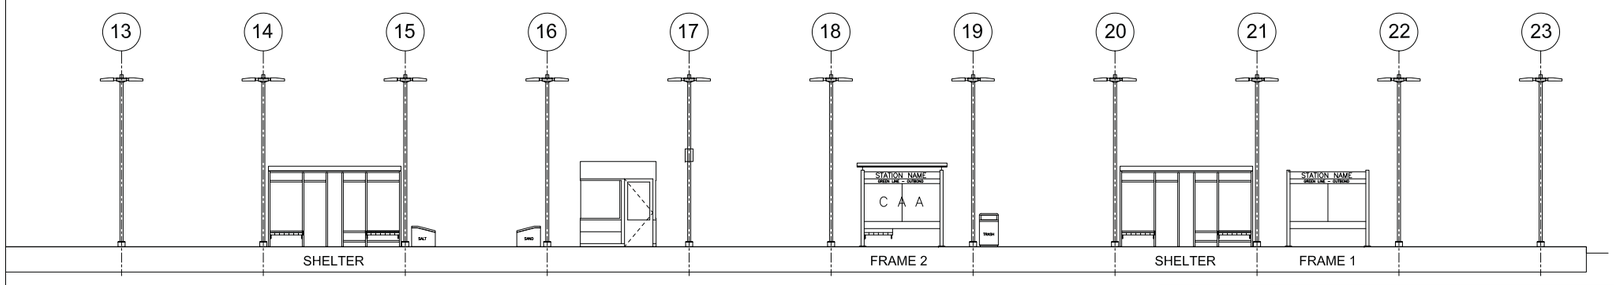

PLATFORM ELEVATION - PART 2

1/8"=1'-0" 0 4' 8' 16' TYPE 1A DATE: 7-14-17

PLATFORM TYPE 4 - LECHMERE- 32'-0" to 37'-0" WIDE PLATFORM

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


LECHMERE STATION
PART 2, STATION PLATFORM
ELEVATION AND SECTION

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	EMT	SHEET: STA-005	.

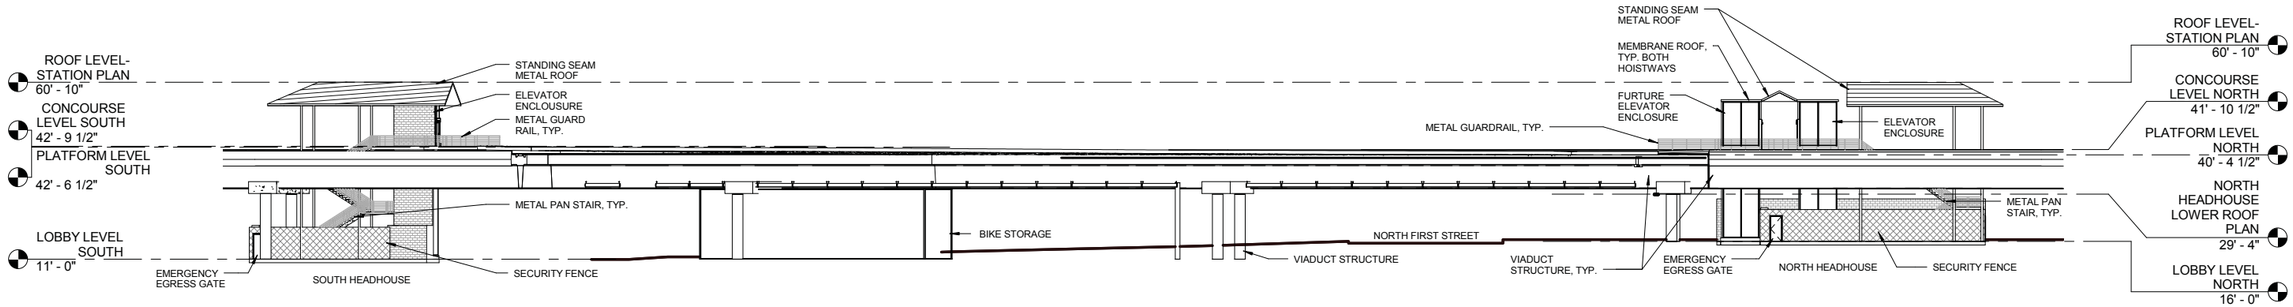


1 EAST ELEVATION

3/64" = 1'-0"

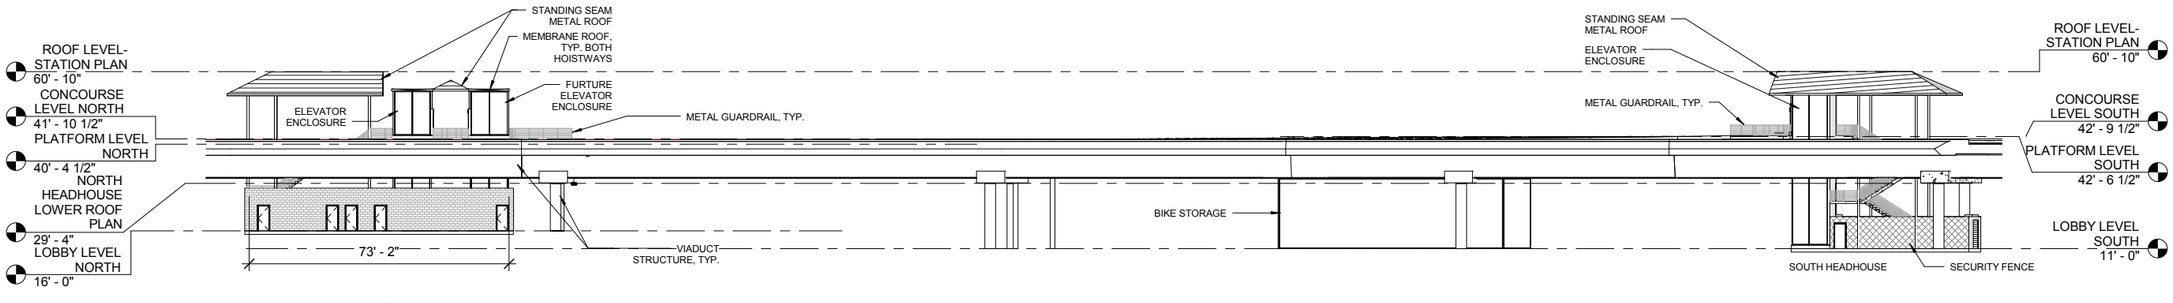

2 WEST ELEVATION

3/64" = 1'-0"

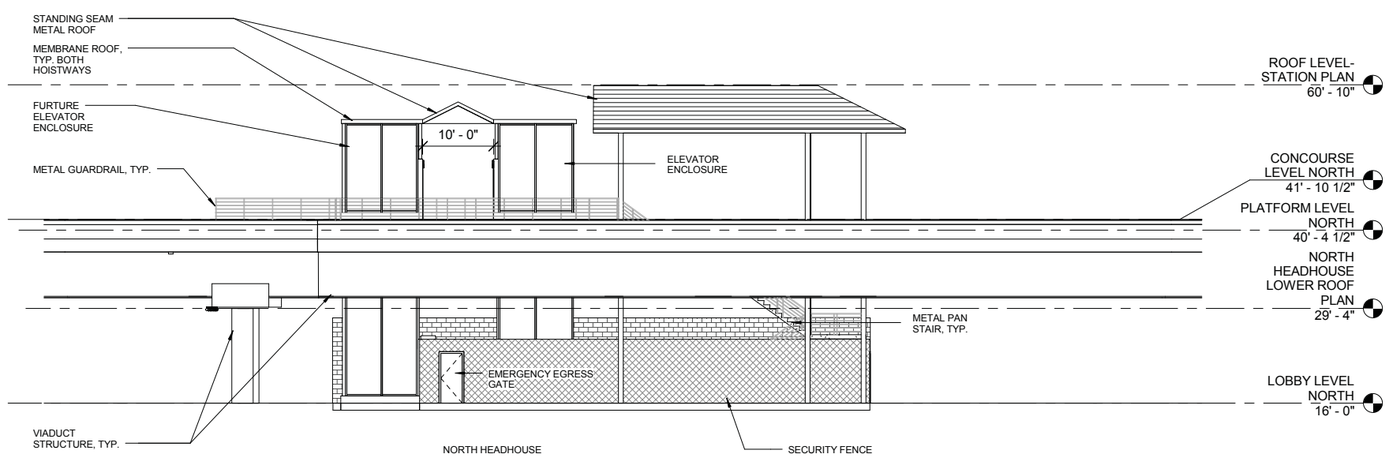

3 EAST ELEVATION - NORTH HEADHOUSE

3/32" = 1'-0"

9/14/2017 2:05:30 PM
C:\Users\shelbuaj\Documents\Lechmere_A3D0000_Shelbuaj.rvt

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY


GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

LECHMERE STATION
ELEVATIONS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: As indicated	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	AH	SM		SHEET: STA-006	

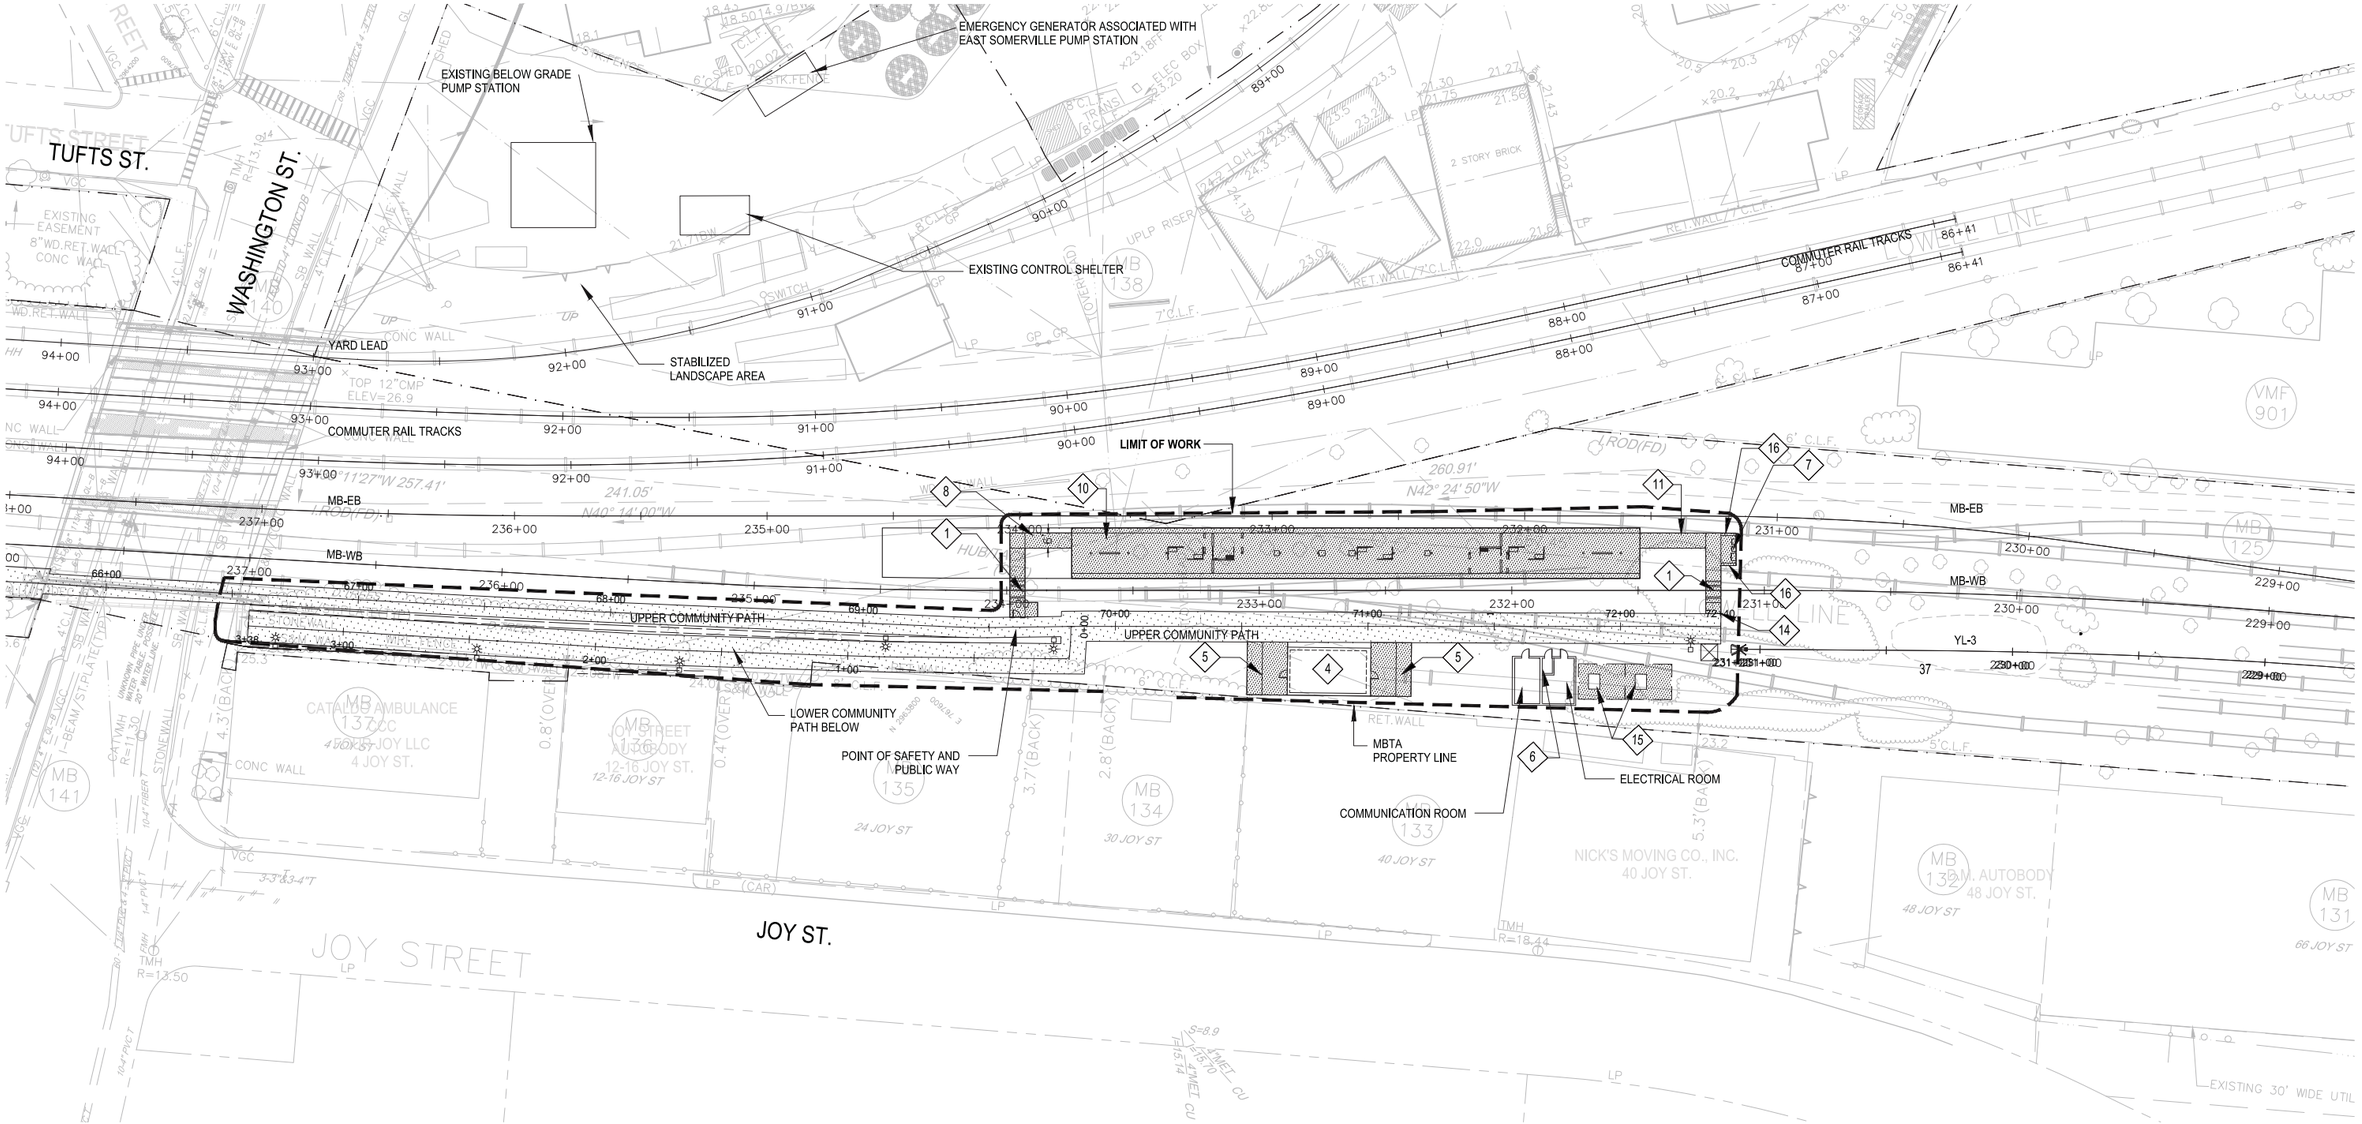

1 SITE PLAN
SCALE: 1"=30'

KEYNOTES

1. TRACK CROSSING
4. BICYCLE STORAGE
5. BICYCLE RACK
6. EFM ROOM
7. FARE COLLECTION MACHINES W/ 7' ROOF
8. EMERGENCY EGRESS SLOPED WALK
10. PLATFORM
11. SLOPED WALK
14. ROLL UP SECURITY GRILLE W/ ADJACENT AFTER HOURS PERSONNEL GATE
15. TRANSFORMER
16. BENCHES

SHEET NOTES

1. PLATFORM LENGTH TO BE 225' WITH A POTENTIAL EXTENSION OF 300'
2. SEE PROPERTY LINE DRAWINGS FOR SCOPE OF WORK

LEGEND

PROPOSED CONCRETE

COMMUNITY PATH ASPHALT

N

0 30' 60'
SCALE: 1" = 30'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

EAST SOMERVILLE STATION
SITE PLAN

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT 28, 2017	YQT	YQT	MWR	SHEET: STA-007	

PLOTTED: 09/14/17 11:43AM BY: TANGYQ
DRAWING: I:\PROPOSALS\2017\0062820 0002 GLX GREEN LINE STATIONS\CIVIL SITE DRAWINGS\EAST SOMERVILLE STATION\STA - 007 - ESS.DWG [SITE PLAN]


KEYNOTES

10 - PLATFORM
11 - CUSTOMER ASSISTANCE AREA & BENCH
12 - SHELTER
14 - TACTILE EDGE
15 - OFFICIALS BOOTH
16 - EMERGENCY EGRESS SLOPED WALK
17 - EMERGENCY EGRESS GATE & GUARDRAIL
20 - SIGNAGE MAP ASSEMBLY
36 - LIGHT POLE
40 - WASTE RECEPTACLES
41 - SALT STORAGE BIN
42 - SAND STORAGE BIN
43 - STARTER'S BOOTH @ (UNION & COLLEGE STATION)
44 - VARIABLE MESSAGE SIGNS (VMS)

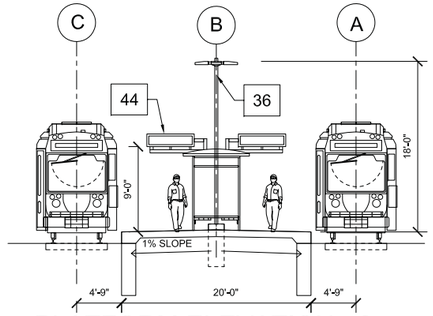


PLATFORM ELEVATION - 2

1/8"=1'-0" 0 4' 8' 16' TYPE 1A

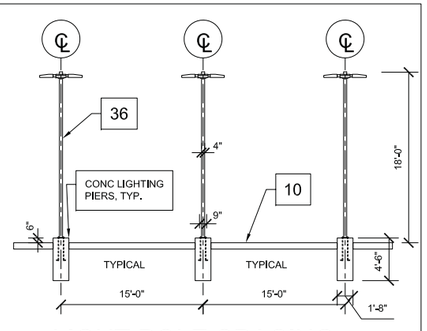

LIGHT POLE SPACING

1/8"=1'-0" 0 4' 8' 16'

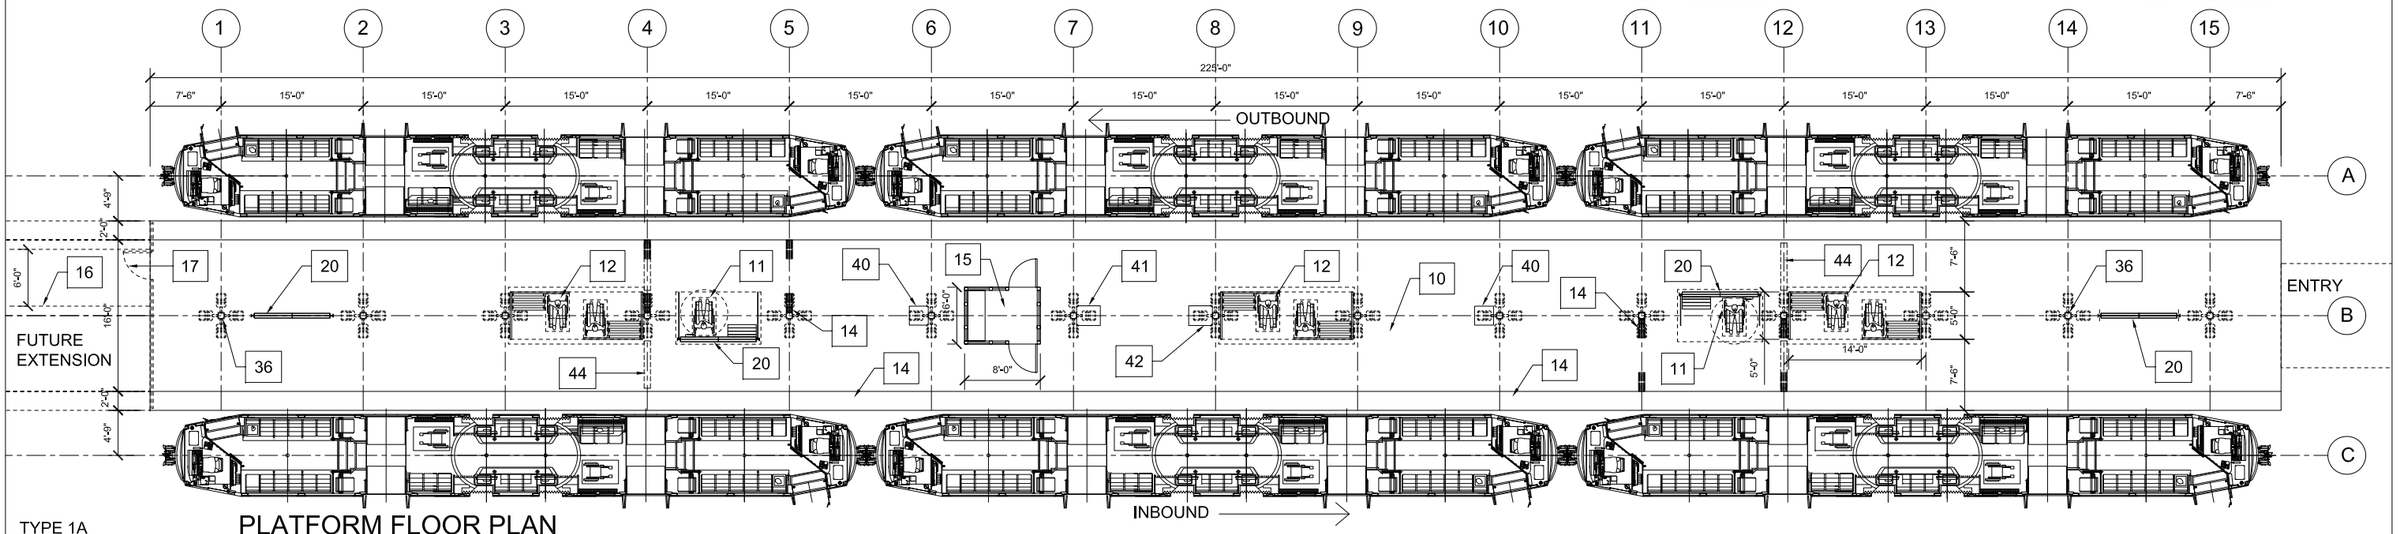


INBOUND

PLATFORM FLOOR PLAN

1/8"=1'-0" 0 4' 8' 16' TYPE 1A DATE: 7-14-17

TYPE 1A
E. SOMERVILLE

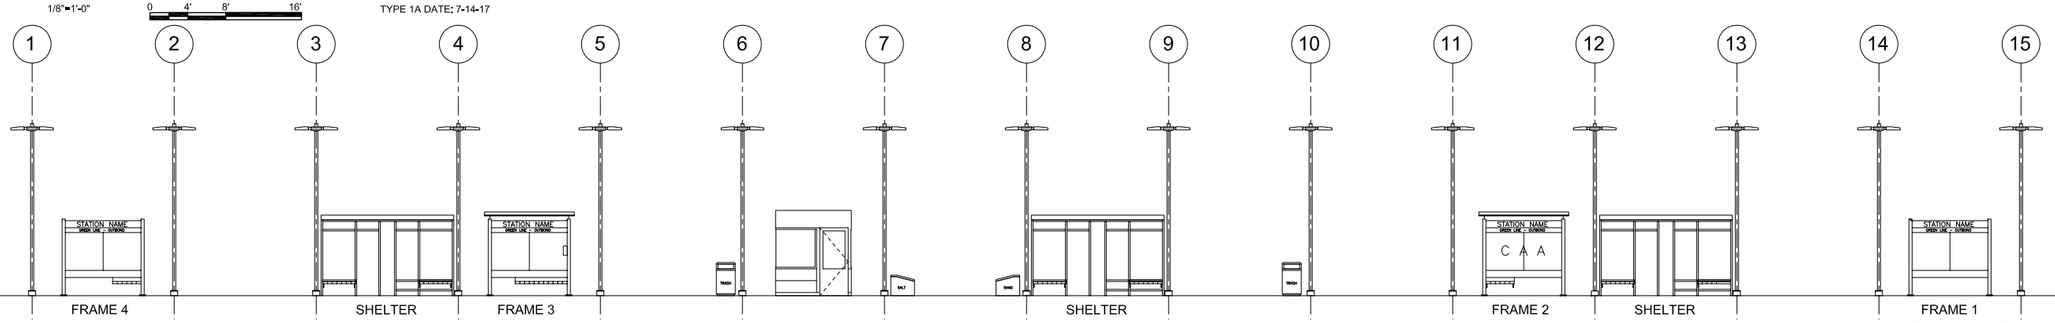

PLATFORM ELEVATION - 1

1/8"=1'-0" 0 4' 8' 16' TYPE 1A DATE: 7-14-17

PLATFORM TYPE 1A = EAST SOMERVILLE- 20'-0" WIDE PLATFORM

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


EAST SOMERVILLE STATION
STATION PLATFORM AT GRADE
ELEVATION AND SECTION

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	EMT	SHEET: STA-008	.

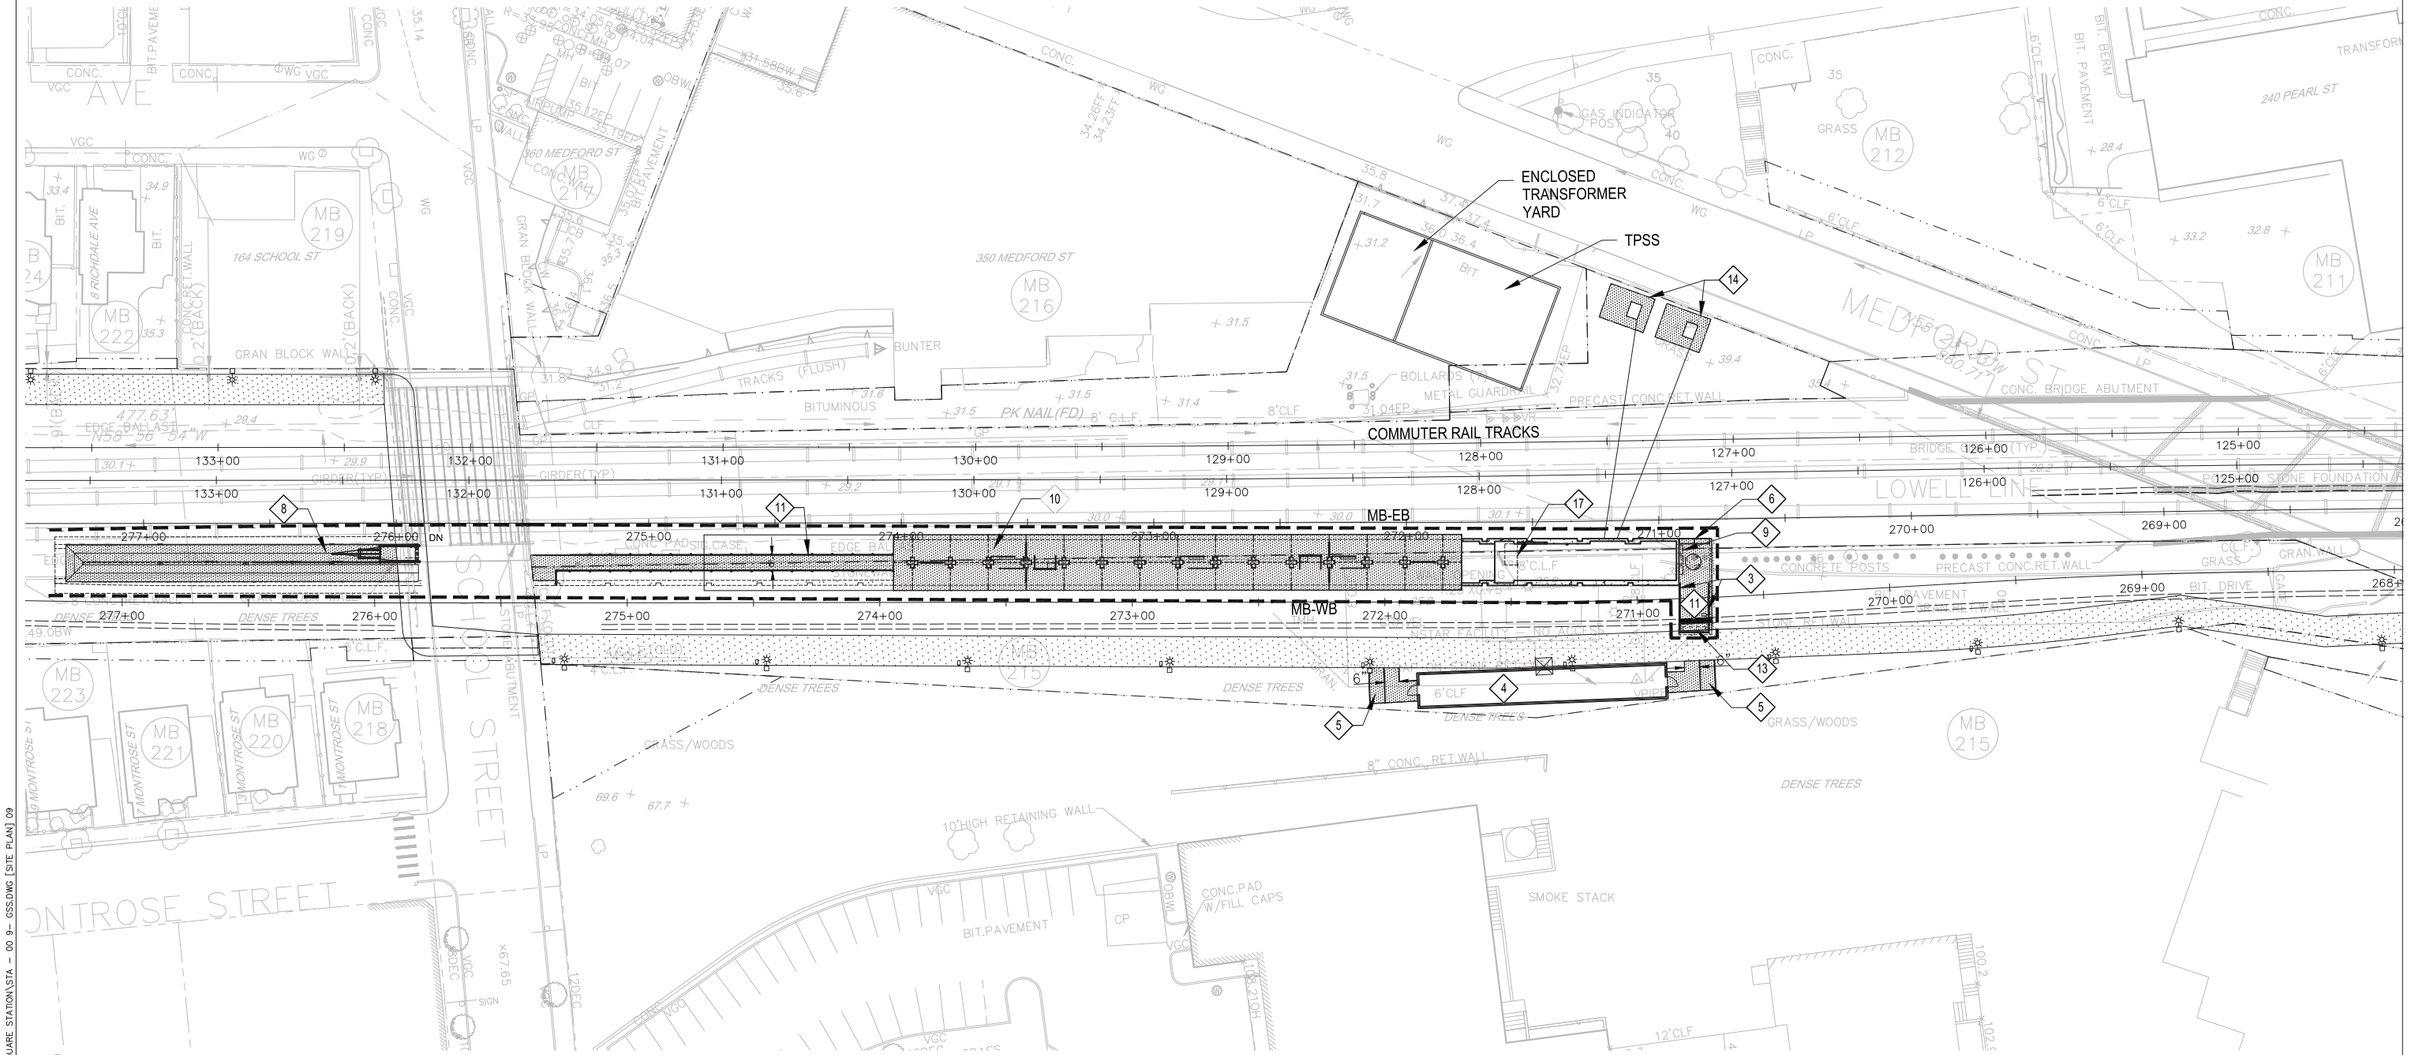

1 SITE PLAN
SCALE: 1:30

KEYNOTES

3. MISSILE BARRIER
4. BICYCLE STORAGE
5. BICYCLE RACK
6. BENCHES
8. COVERED EMERGENCY EGRESS RAMP
9. FARE VENDING MACHINES
10. PLATFORM
11. WALKWAY
13. ROLL UP SECURITY GRILL
14. TRANSFORMERS
17. ELEVATOR

SHEET NOTES

1. PLATFORM LENGTH TO BE 225' WITH A POTENTIAL EXTENSION TO 300'

LEGEND

- COMMUNITY PATH ASHALT
- PROPOSED CONCRETE

N

0 30' 60'
SCALE:1"=30'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

GILMAN SQUARE STATION
SITE PLAN


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT 28, 2017	YQT	YQT	MWR	SHEET: STA-009	


PLOTTED: 09/14/17 11:46AM BY: TANGYQ
DRAWING: I:\PROPOSALS\2017\0062820 0002 GLX GREEN LINE STATIONS\CIVIL SITE DRAWINGS\GILMAN SQUARE STATION\STA - 00 9- GSS.DWG [SITE PLAN] 09



OVERALL PLAN AT PLATFORM LEVEL

1" = 30'-0"

30' 15' 0 30'

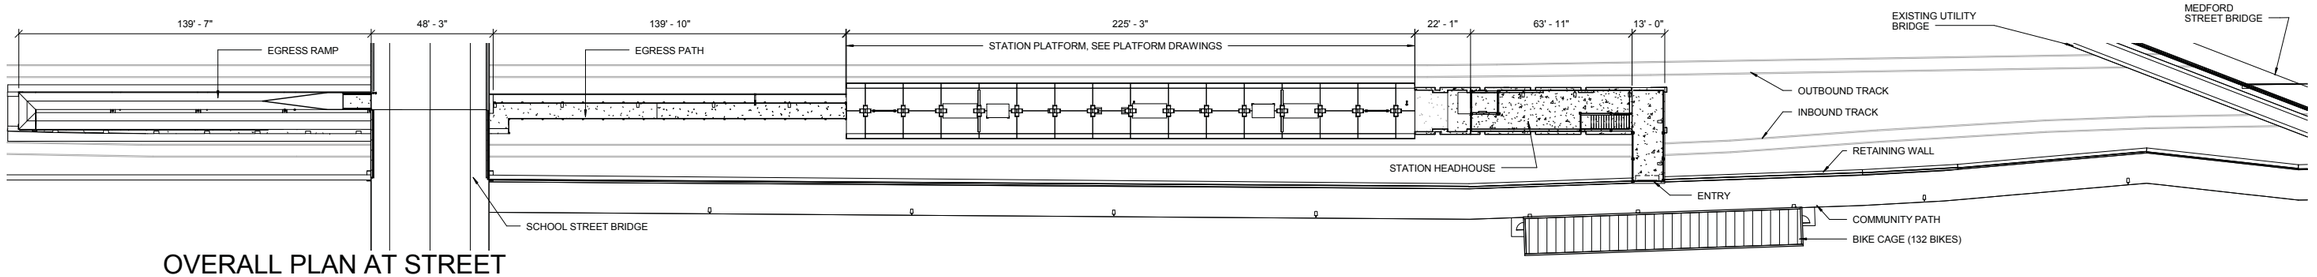

OVERALL PLAN AT STREET LEVEL

1" = 30'-0"

30' 15' 0 30'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


GILMAN STATION
OVERALL PLANS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: STA-010	


9/14/2017 2:20:33 PM
C:\Users\shelbuaj\Documents\Gilman_A-300000_Shelbuaj.rvt

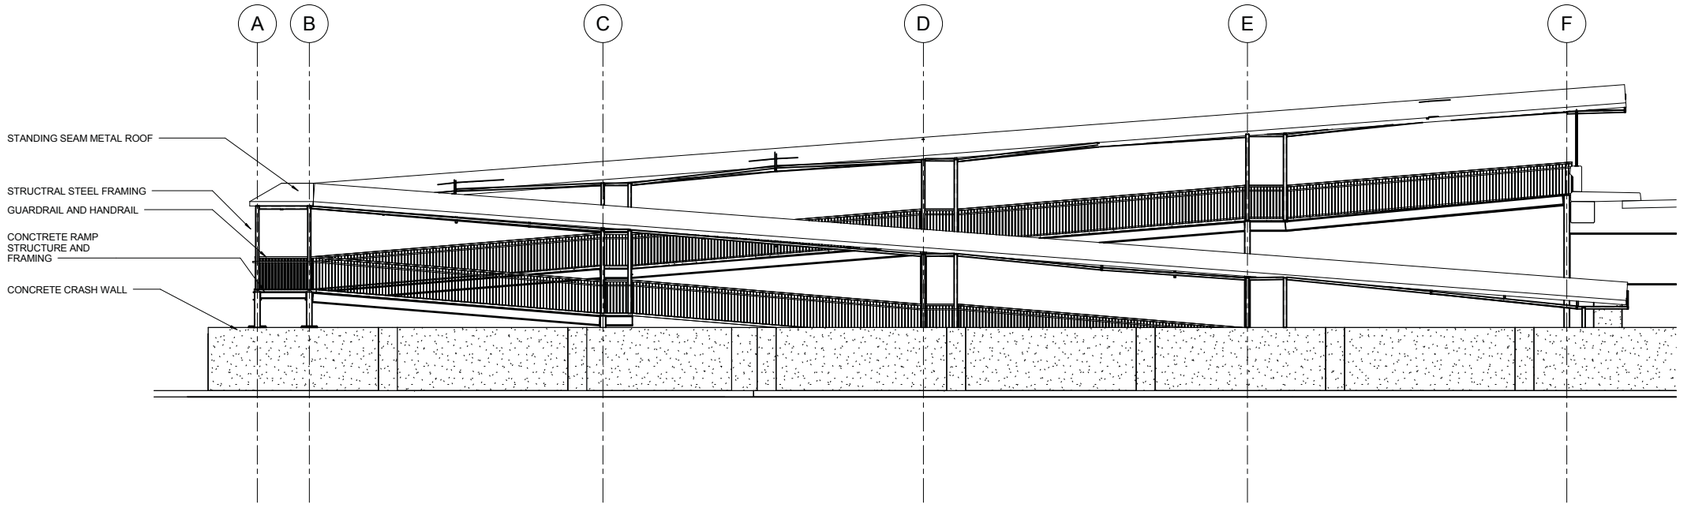

WEST ELEVATION AT COVERED EMERGENCY EGRESS RAMP

1 / A-104

1/8" = 1'-0"

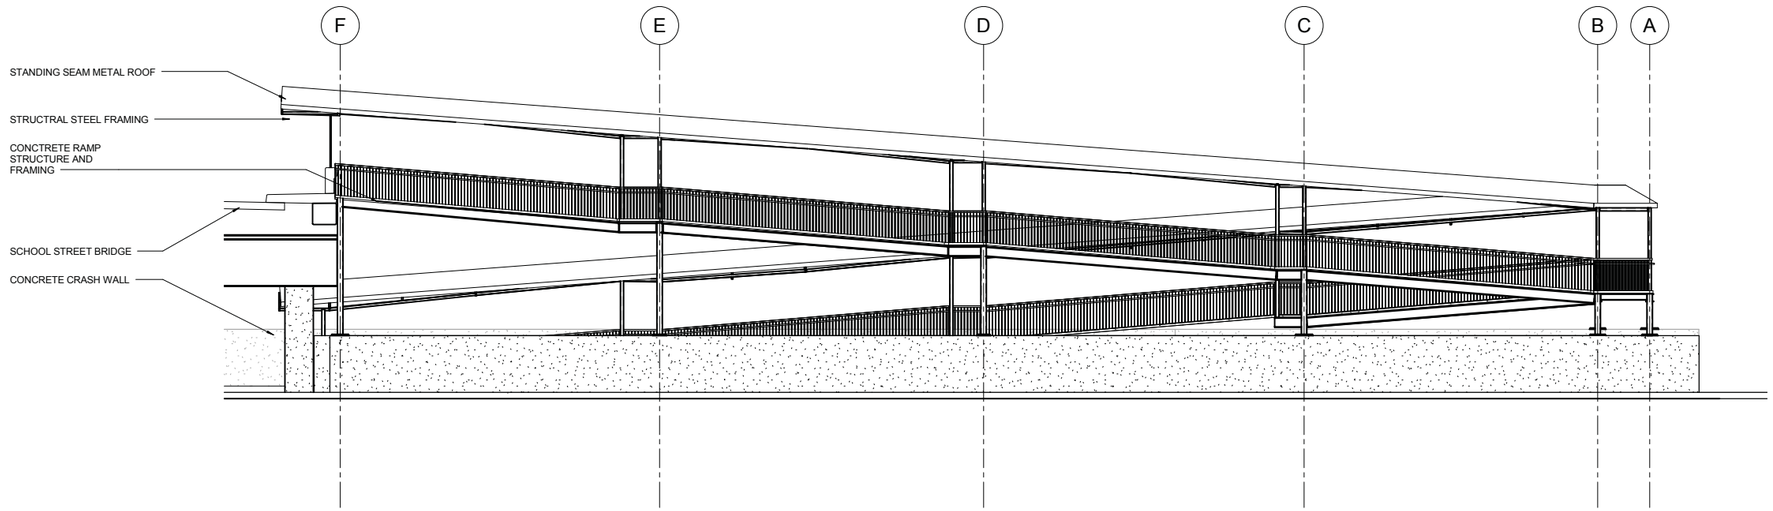

EAST ELEVATION AT COVERED EMERGENCY EGRESS RAMP

2 / A-104

1/8" = 1'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

GILMAN STATION
COVERED EMERGENCY EGRESS
RAMP ELEVATIONS


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: STA-011	

9/14/2017 2:25:20 PM
C:\Users\shelbuaj\Documents\Gilman_A-3D0000_Shelbuaj.rvt

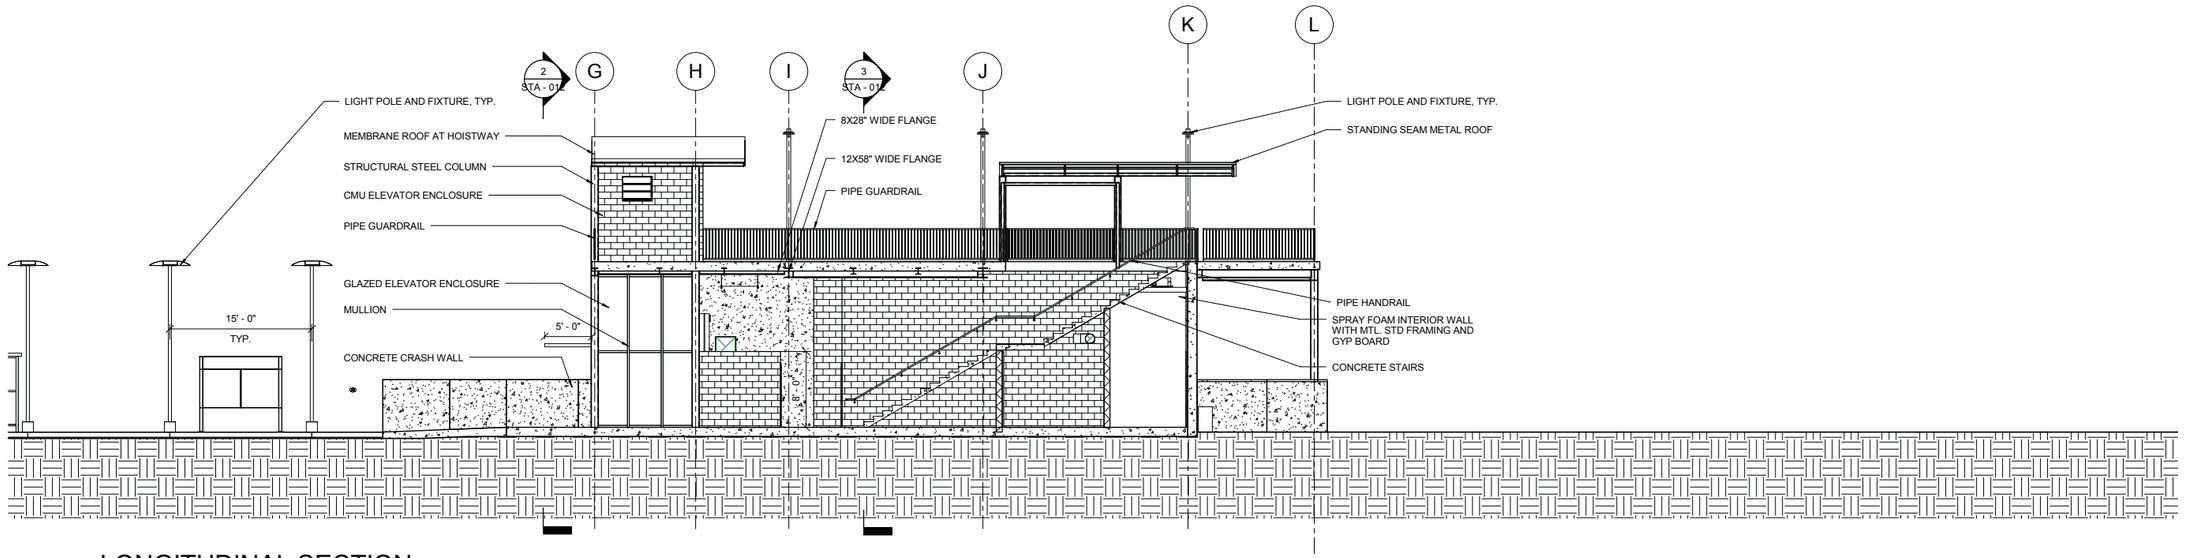


1 A-102 — LONGITUDINAL SECTION

1/8" = 1'-0"

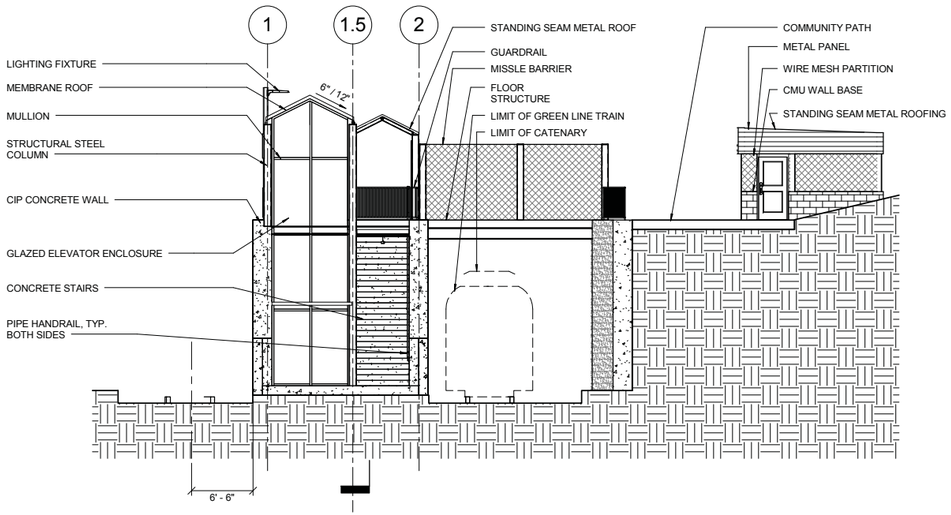

2 A-102 — TRANSVERSE SECTION 1

1/8" = 1'-0"

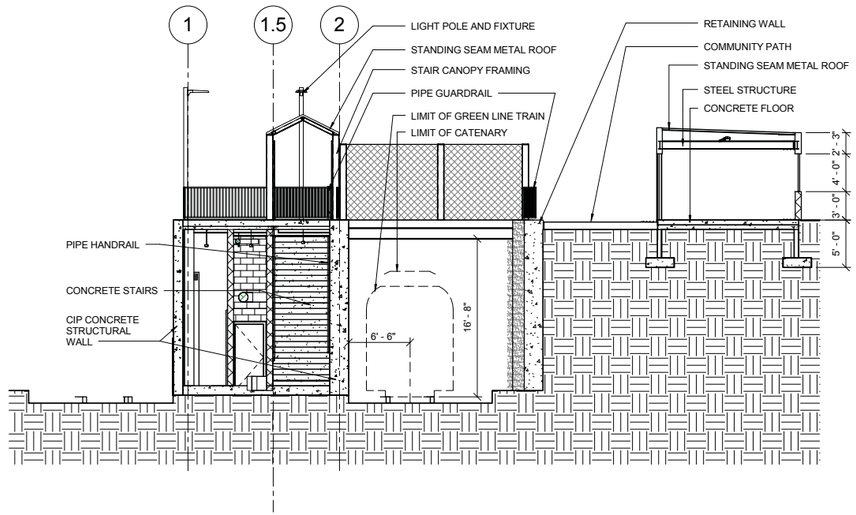

3 A-102 — TRANSVERSE SECTION 2

1/8" = 1'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

GILMAN STATION BUILDING SECTIONS

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-273.pdf


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: STA-012	

9/19/2017 12:00:19 PM
C:\Users\packarsj\Documents\Gilman_A-3D0000_packarsj.rvt


KEYNOTES

10 - PLATFORM
11 - CUSTOMER ASSISTANCE AREA & BENCH
12 - SHELTER
14 - TACTILE EDGE
15 - OFFICIALS BOOTH
16 - EMERGENCY EGRESS SLOPED WALK
17 - EMERGENCY EGRESS GATE & GUARDRAIL
20 - SIGNAGE MAP ASSEMBLY
36 - LIGHT POLE
40 - WASTE RECEPTACLES
41 - SALT STORAGE BIN
42 - SAND STORAGE BIN
43 - STARTER'S BOOTH @ (UNION & COLLEGE STATION)
44 - VARIABLE MESSAGE SIGNS (VMS)

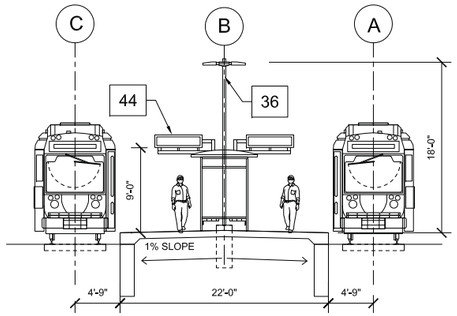


PLATFORM ELEVATION - 2

1/8"=1'-0" 0 4' 8' 16' TYPE 2A

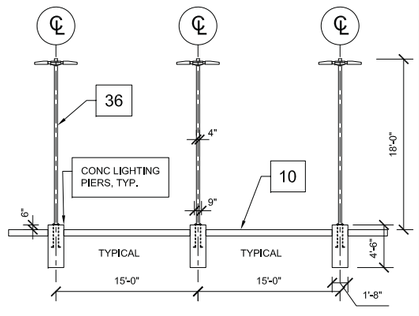

LIGHTING POLE SPACING


1/8"=1'-0" 0 4' 8' 16'

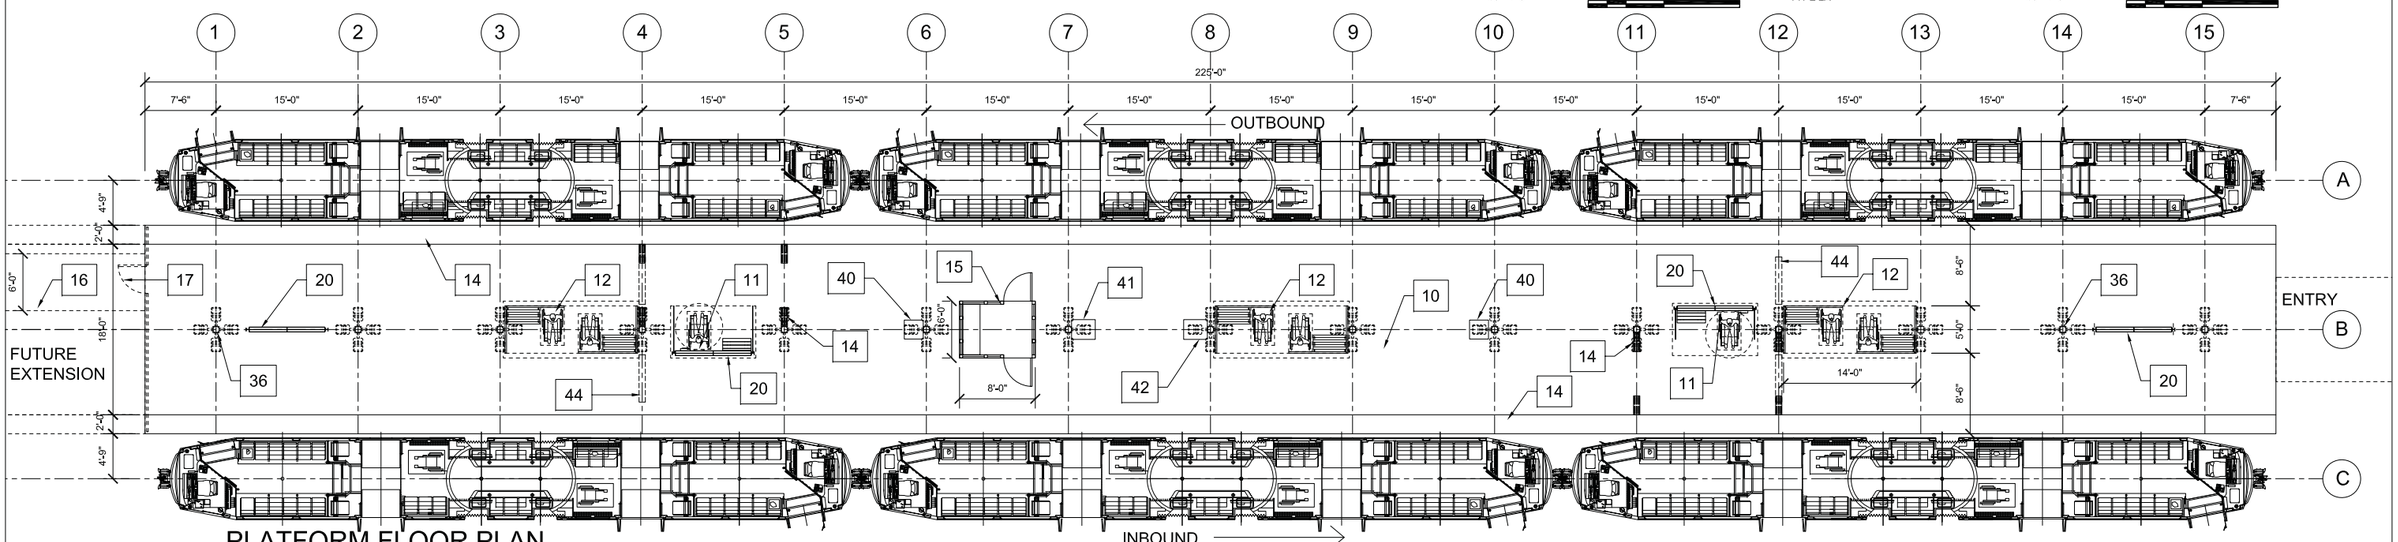

PLATFORM FLOOR PLAN

1/8"=1'-0" 0 4' 8' 16' TYPE 2A DATE: 7-14-17

TYPE 2A-(22'-0")
GILMAN SQUARE

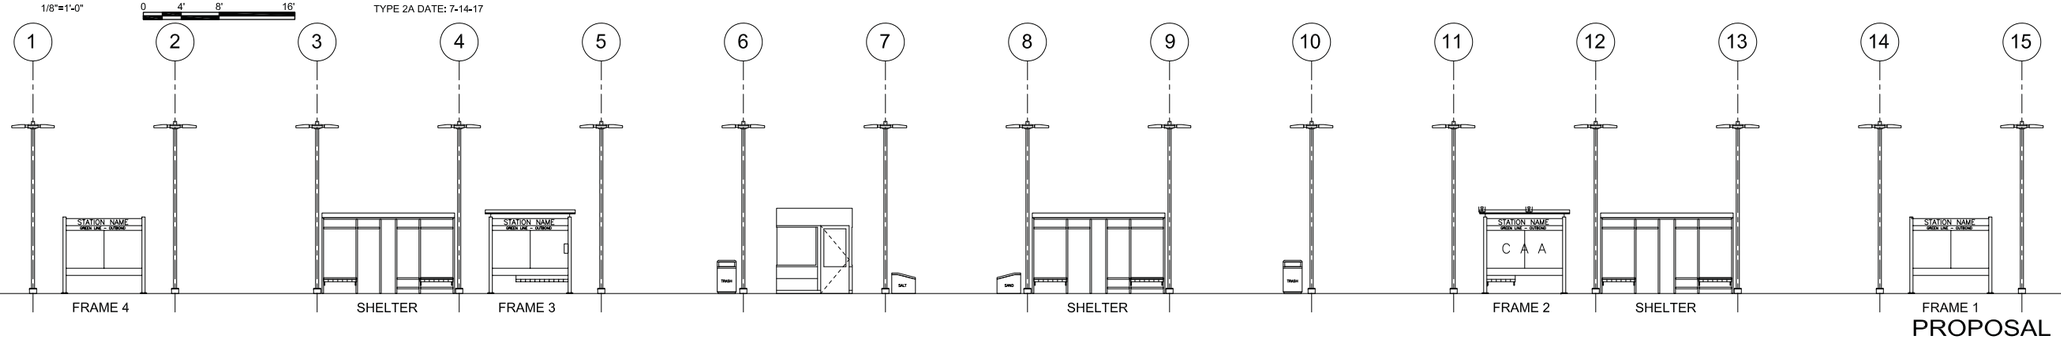

PROPOSAL

PLATFORM ELEVATION - 1

1/8"=1'-0" 0 4' 8' 16' TYPE 2A DATE: 7-14-17

PLATFORM TYPE 2A - GILMAN SQ. 22'-0" WIDE PLATFORM

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


GILMAN STATION
STATION PLATFORM AT GRADE
ELEVATION AND SECTION

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	EMT	SHEET: STA-013	.

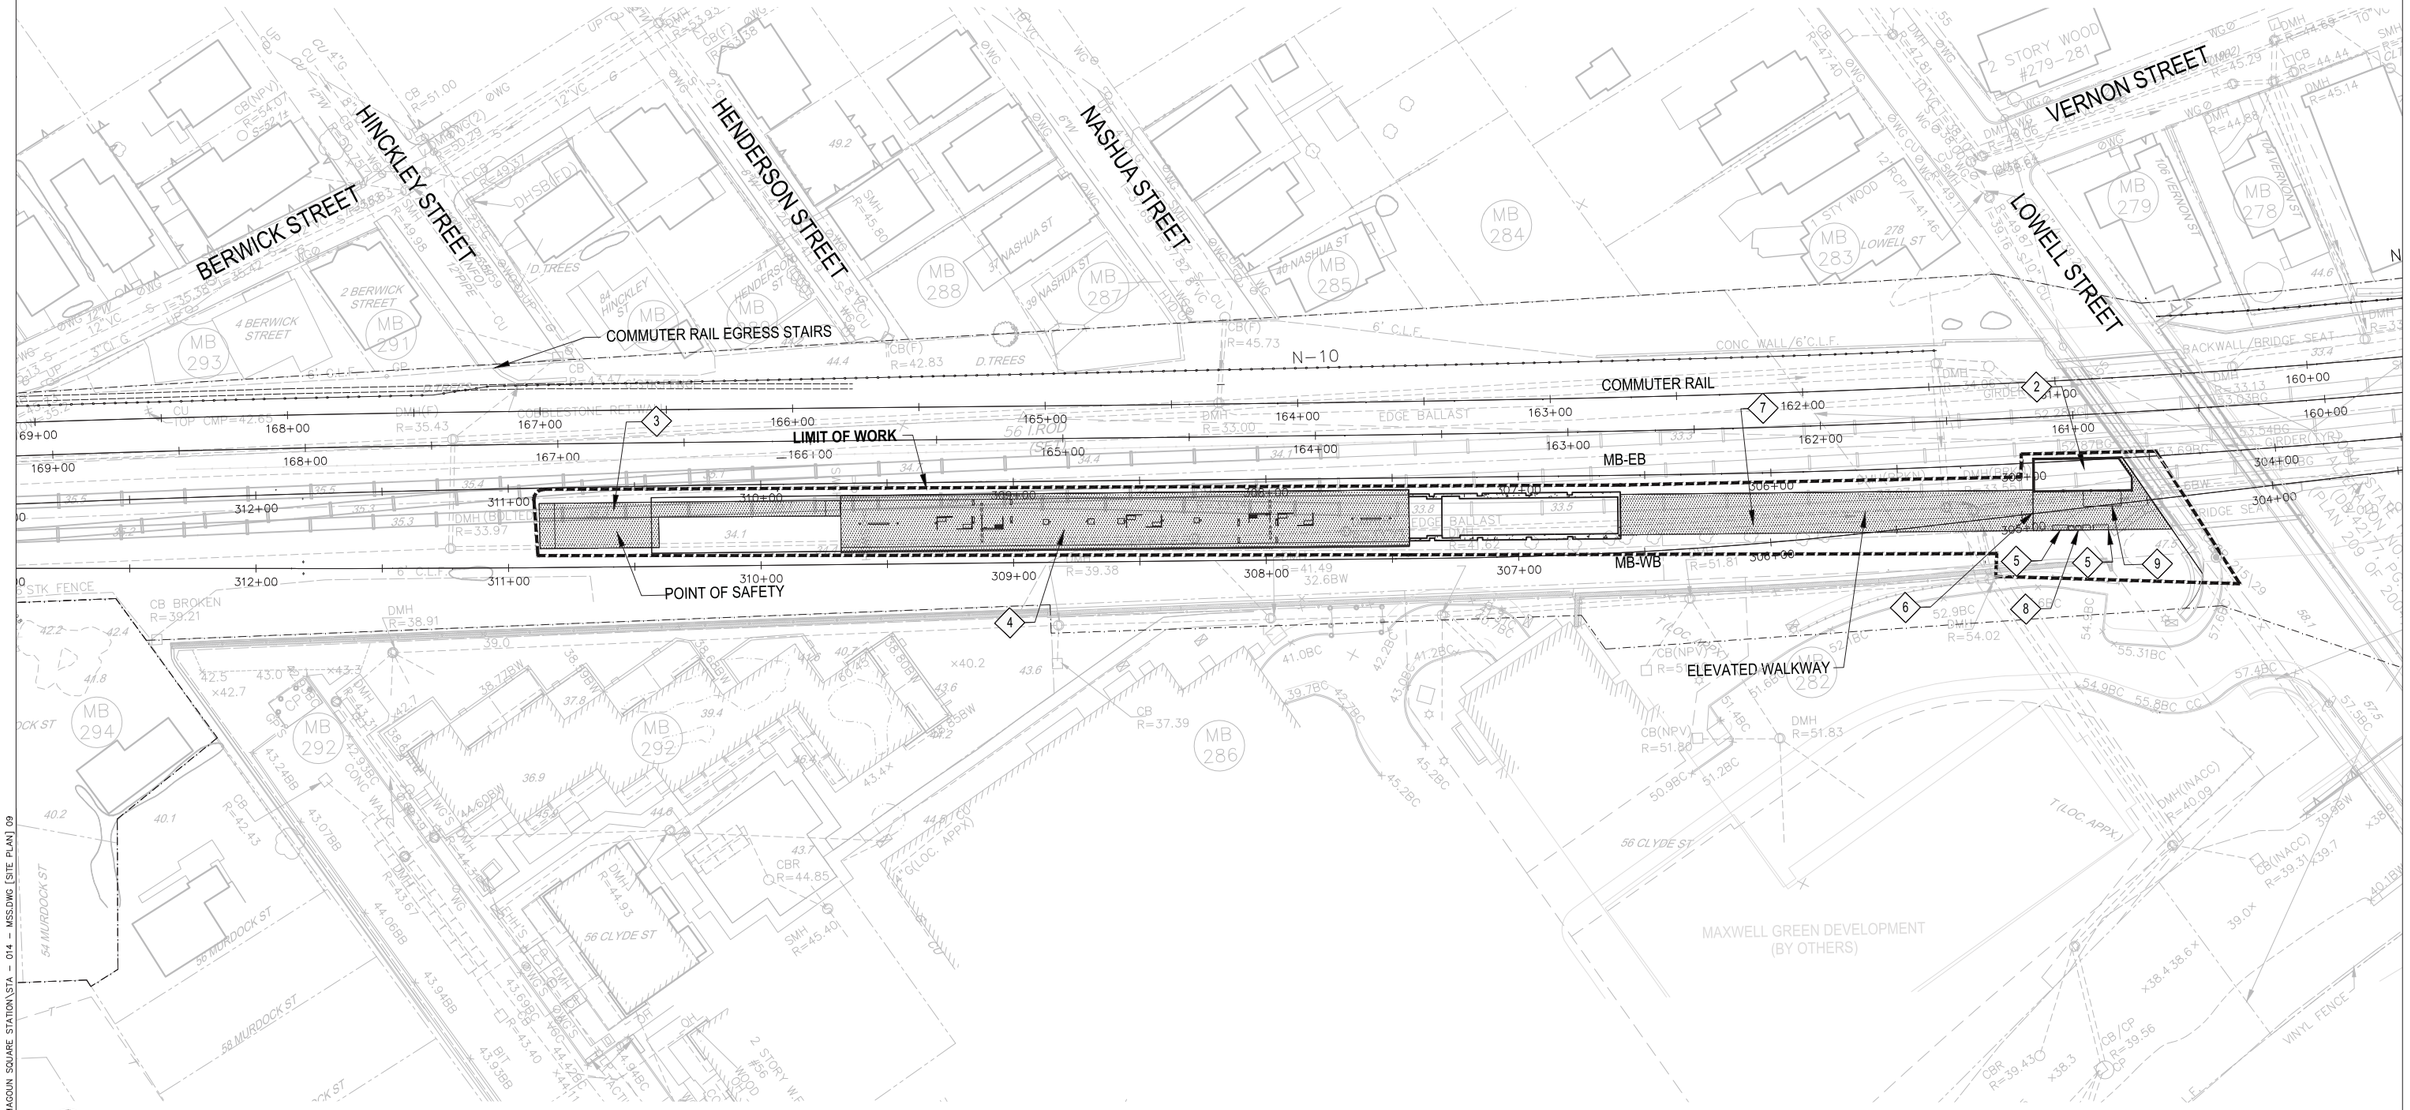

1 SITE PLAN
SCALE: 1"=30'

KEYNOTES

2. BICYCLE STORAGE
3. EMERGENCY EGRESS SLOPED WALK
4. PLATFORM
5. BENCHES
6. ROLL UP SECURITY GRILL
7. RAISED SLOPED WALKWAY
8. FARE MACHINES
9. BICYCLE RACK

SHEET NOTES

1. PLATFORM LENGTH TO BE 225' WITH A POTENTIAL EXTENSION TO 300'

LEGEND

PROPOSED CONCRETE

N

0 30' 60'
SCALE: 1" = 30'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MAGOUN SQUARE STATION SITE PLAN


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-273.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT 28, 2017	YQT	YQT	MWR	SHEET: STA- 014	


PLOTTED: 09/14/17 12:04PM BY: TANGYQ
DRAWING: I:\PROPOSALS\2017\0062820 0002 GLX GREEN LINE STATIONS\CIVIL SITE DRAWINGS\MAGOUN SQUARE STATION\STA - 014 - MSS.DWG [SITE PLAN] 09



OVERALL PLAN AT PLATFORM LEVEL

1" = 30'-0"

30' 15' 0 30'



OVERALL PLAN AT STREET LEVEL

1" = 30'-0"

30' 15' 0 30'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


MAGOUN STATION
OVERALL PLANS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: STA-015	


9/14/2017 4:13:38 PM
C:\Users\shelbuaj\Documents\Magoun_A_300000_Shelbuaj.rvt

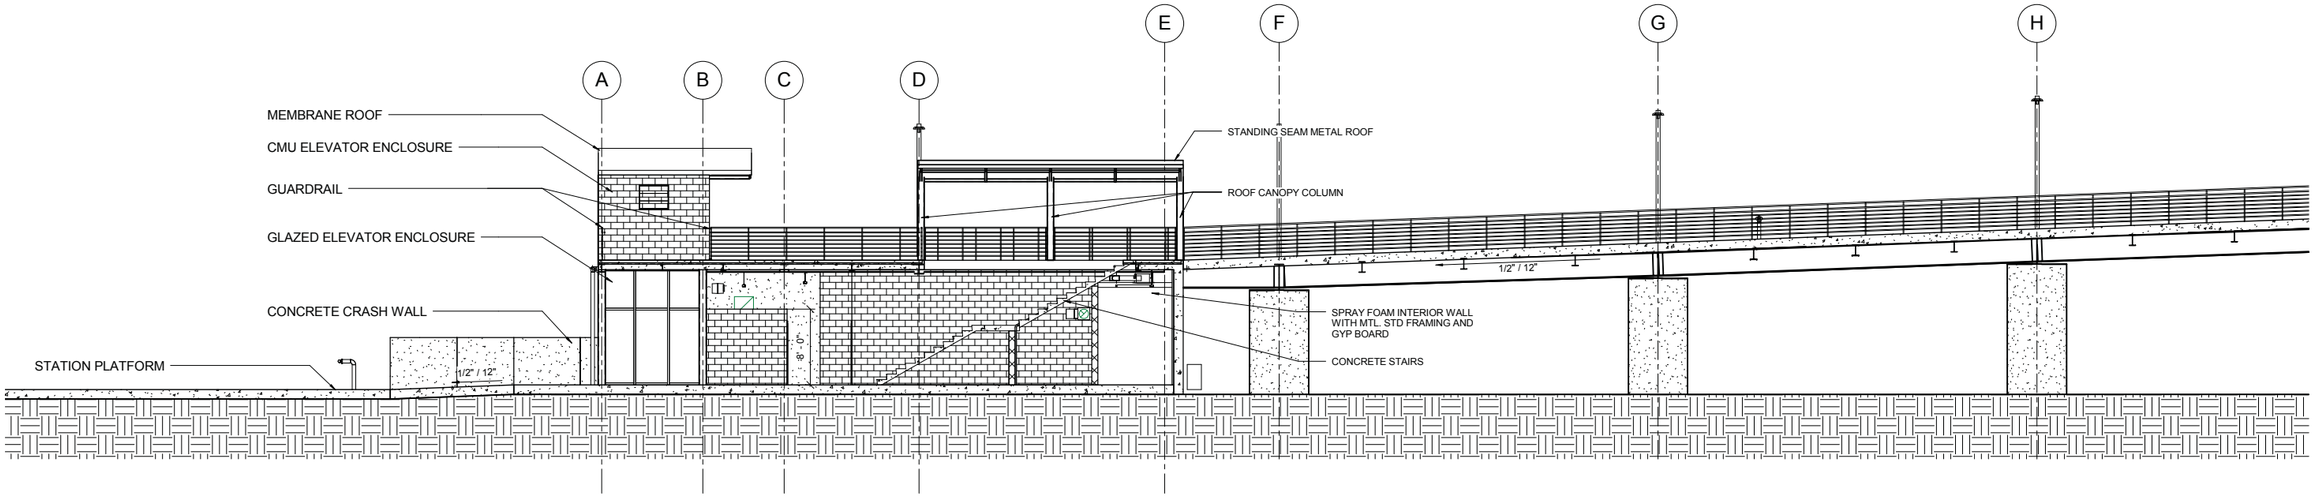

LONGITUDINAL SECTION

2 / A-102


1/8" = 1'-0"

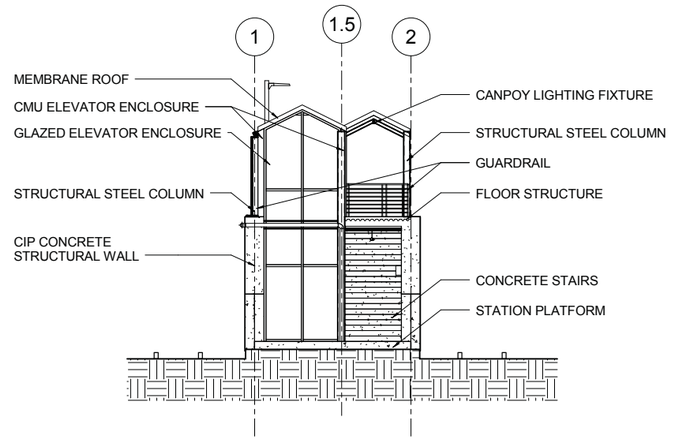

TRANSVERSE SECTION 1

3 / A-102

1/8" = 1'-0"

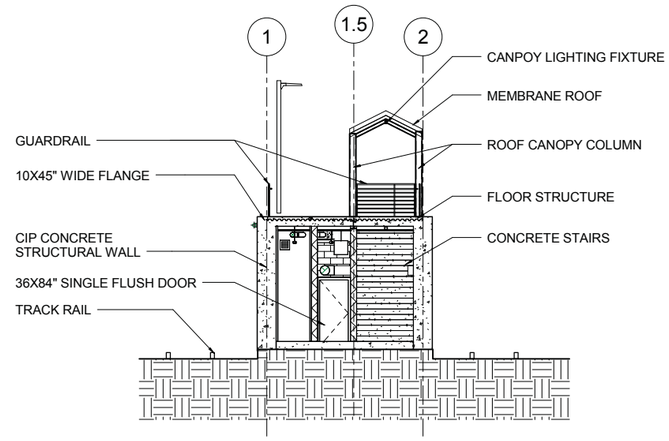

TRANSVERSE SECTION 2

1 / A-103

1/8" = 1'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MAGOUN STATION
BUILDING SECTIONS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: STA-016	

9/14/2017 4:14:27 PM
C:\Users\shebuaj\Documents\Magoun_A_3D0000_Shebuaj.rvt


KEYNOTES

10 - PLATFORM
11 - CUSTOMER ASSISTANCE AREA & BENCH
12 - SHELTER
14 - TACTILE EDGE
15 - OFFICIALS BOOTH
16 - EMERGENCY EGRESS SLOPED WALK
17 - EMERGENCY EGRESS GATE & GUARDRAIL
20 - SIGNAGE MAP ASSEMBLY
36 - LIGHT POLE
40 - WASTE RECEPTACLES
41 - SALT STORAGE BIN
42 - SAND STORAGE BIN
43 - STARTER'S BOOTH @ (UNION & COLLEGE STATION)
44 - VARIABLE MESSAGE SIGNS (VMS)

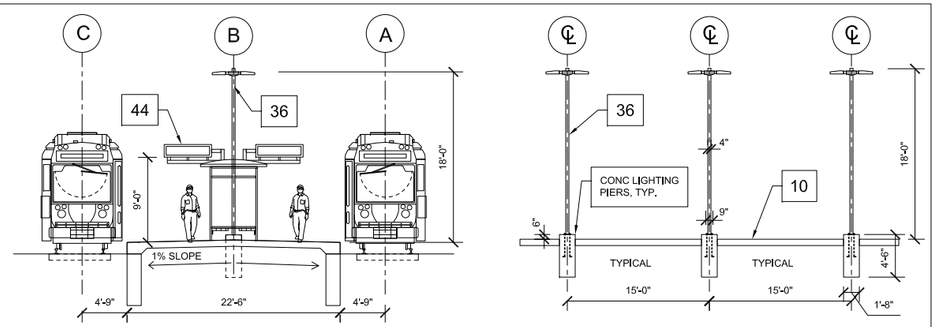

PLATFORM ELEVATION - 2


1/8"=1'-0" 0 4' 8' 16' TYPE 3

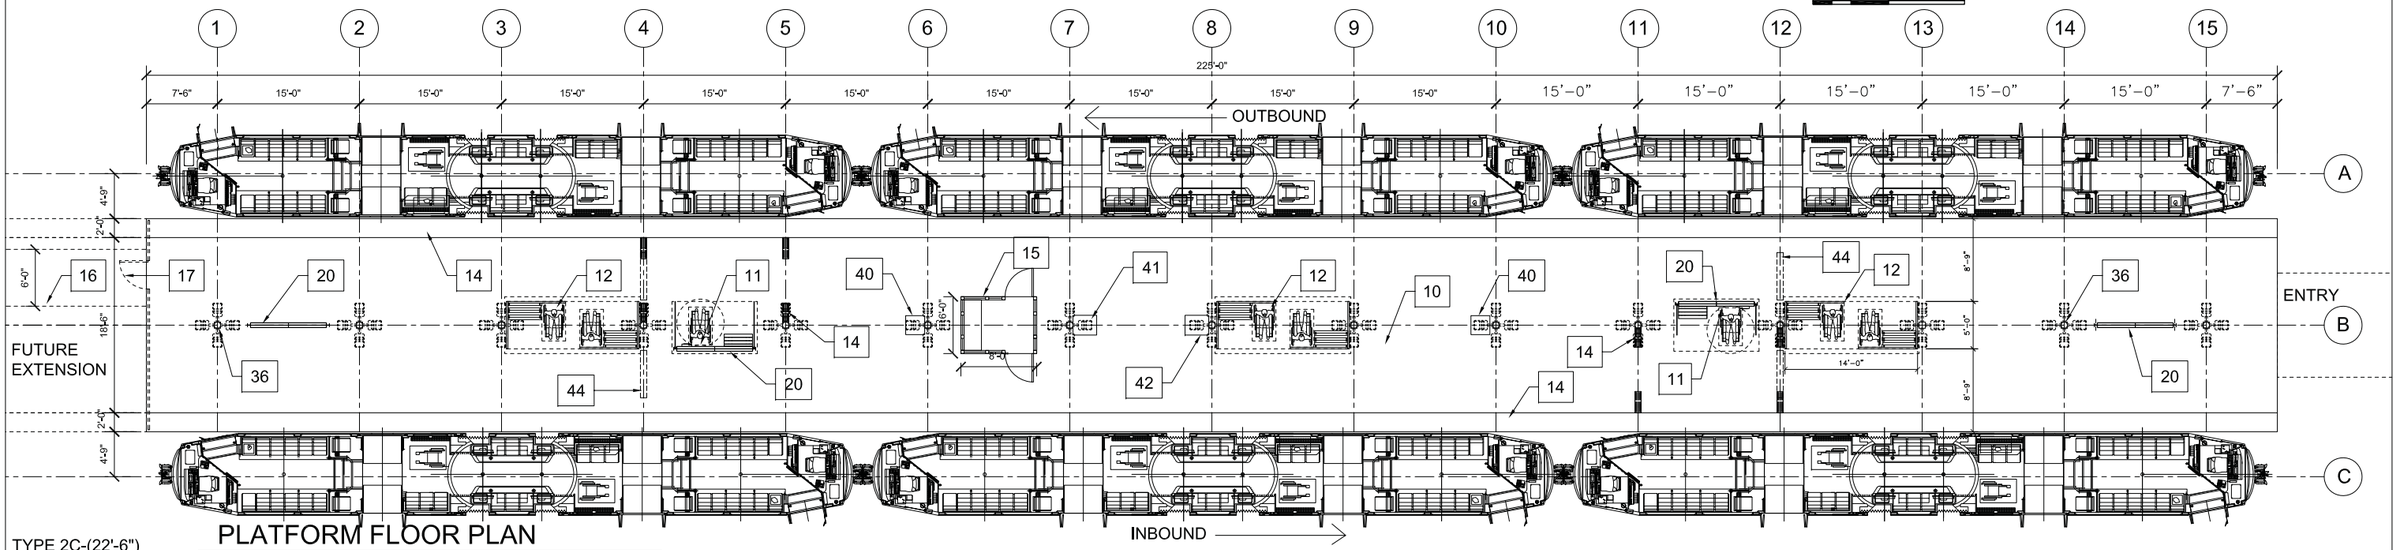

PLATFORM FLOOR PLAN

1/8"=1'-0" 0 4' 8' 16' TYPE 3 DATE: 6-30-17

TYPE 2C-(22'-6")
MAGOUN ST.

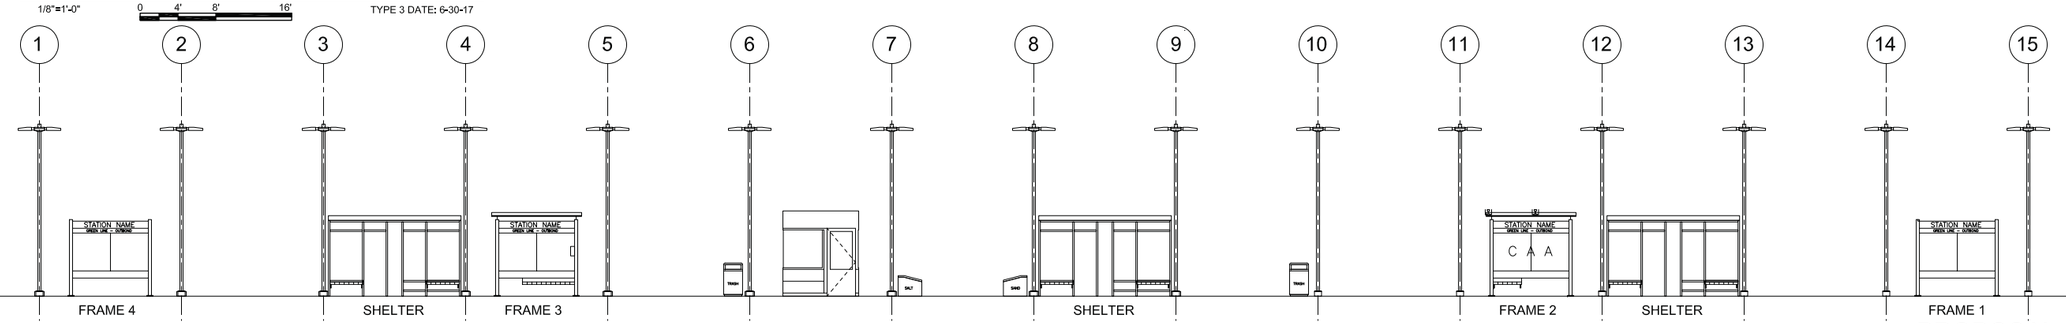

PROPOSAL

PLATFORM ELEVATION - 1

1/8"=1'-0" 0 4' 8' 16' TYPE 3 DATE: 6-30-17

PLATFORM TYPE 2C - MAGOUN SQUARE STATION - 22'-6" WIDE PLATFORM

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


MAGOUN STATION
STATION PLATFORM AT GRADE
ELEVATION AND SECTION

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	EMT	SHEET: STA-017	.

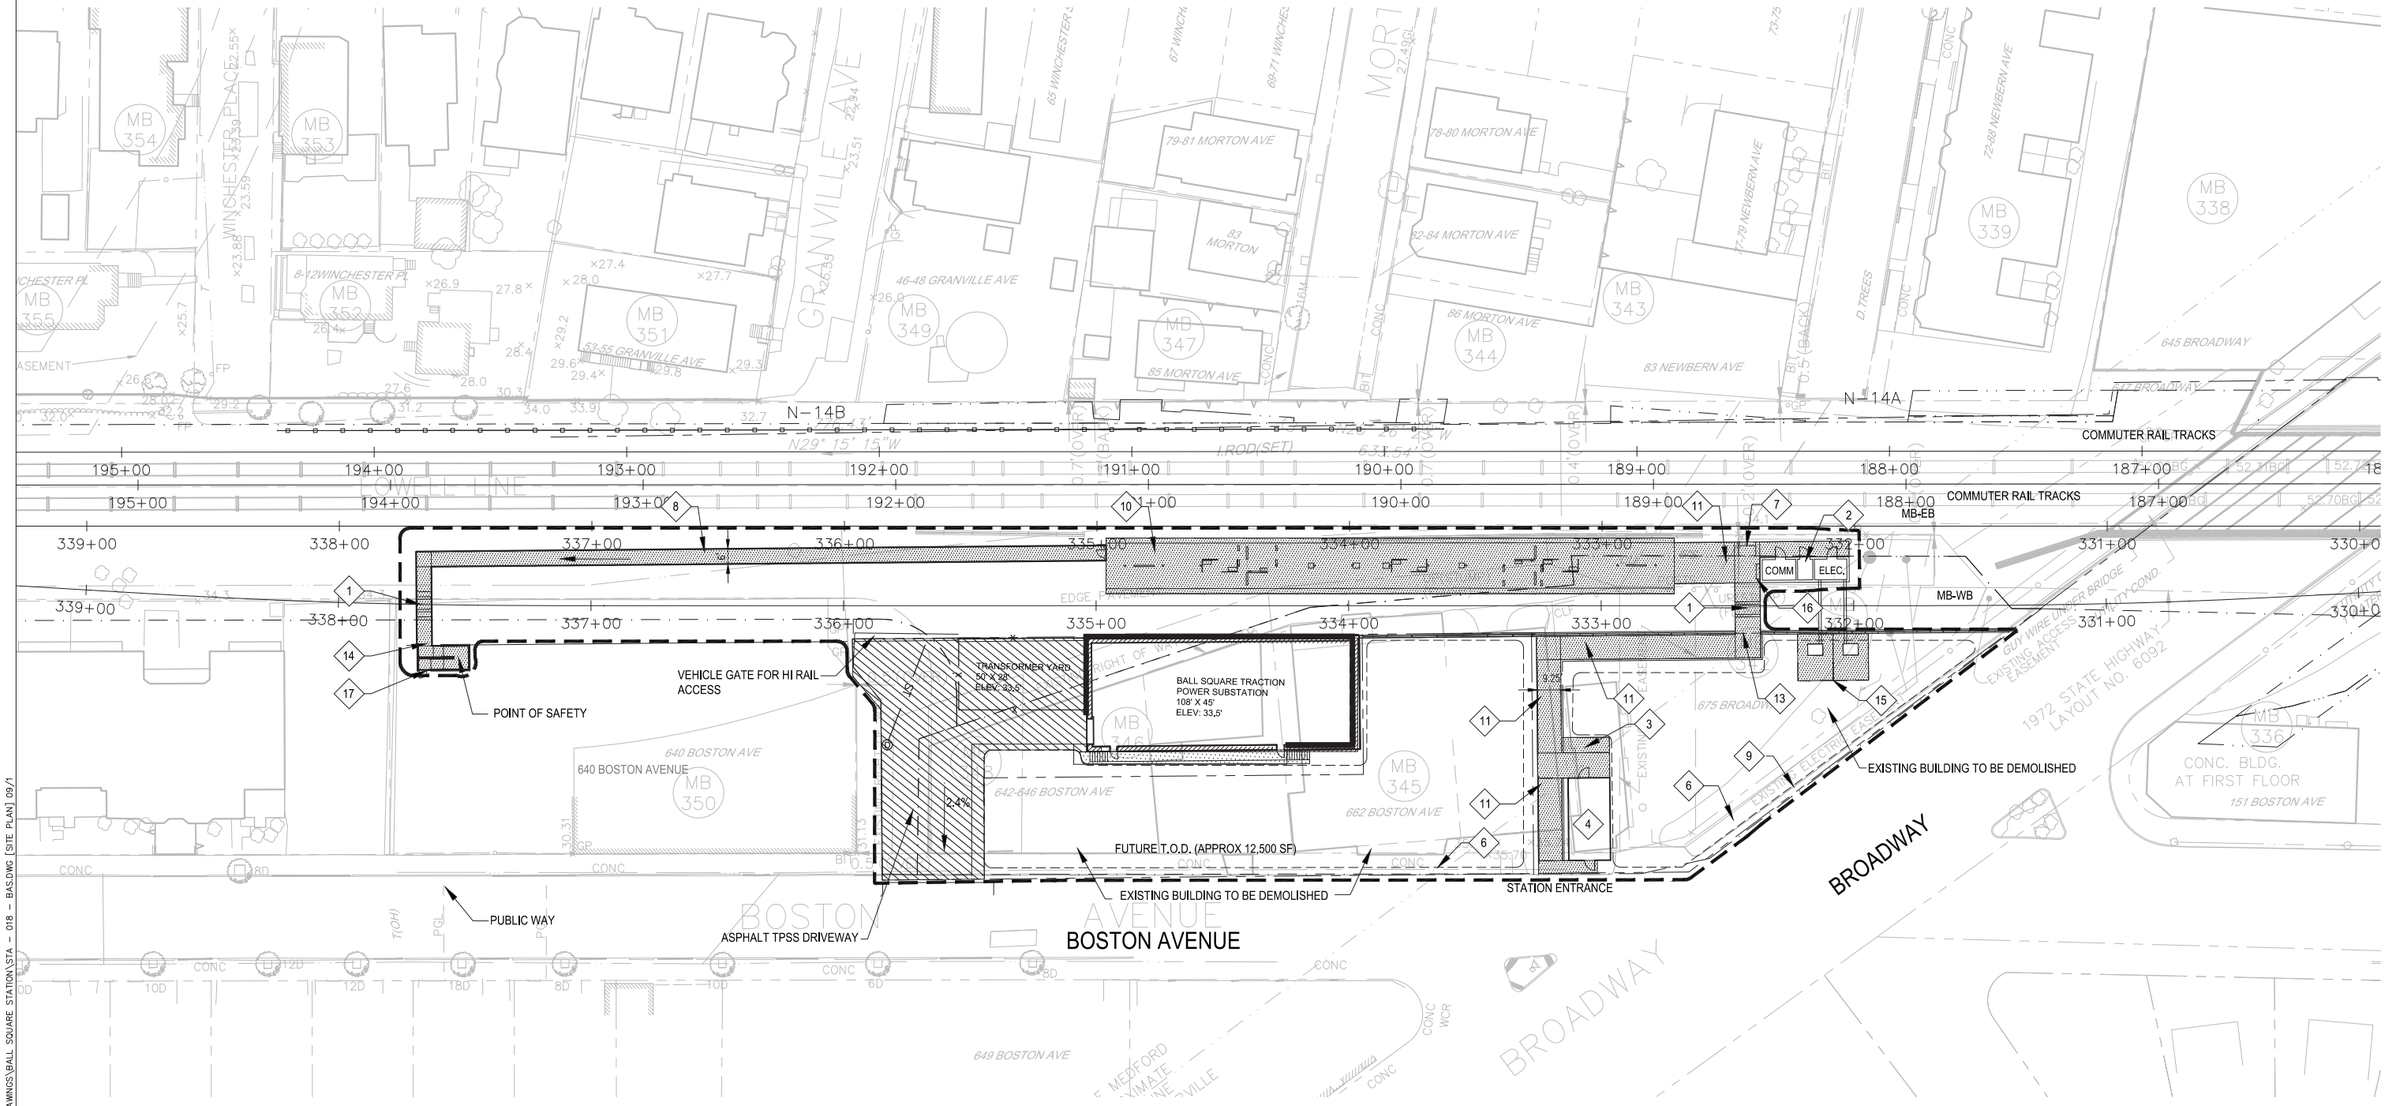

1 SITE PLAN
SCALE: 1"=30'

KEYNOTES

1. TRACK CROSSING
2. EFM ROOM
3. BICYCLE RACK
4. BICYCLE STORAGE
6. GRAVEL
7. FARE COLLECTION MACHINES W/ 7' ROOF
8. EMERGENCY EGRESS SLOPED WALK
9. CONCRETE SIDEWALK - BROOM FINISH
10. PLATFORM
11. SLOPED WALK
13. ROLL UP SECURITY GRILLE W/ ADJACENT AFTER HOURS PERSONNEL GATE
14. EMERGENCY EGRESS RAMP
15. TRANSFORMERS
16. BENCHES
17. EMERGENCY EGRESS GATE

SHEET NOTES

1. PLATFORM LENGTH TO BE 225' WITH A POTENTIAL EXTENSION TO 300'.

LEGEND

PROPOSED CONCRETE

PROPOSED ASPHALT PAVEMENT

0' 30' 60'
SCALE: 1" = 30'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

BALL SQUARE STATION
SITE PLAN - STREET LEVEL

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT 28, 2017	YQT	YQT	MWR	SHEET: STA-018	

4-92

PLOTTED: 09/14/17 11:38AM BY: TANGYQ
DRAWING: I:\PROPOSALS\2017\0062820 0002 GLX GREEN LINE STATIONS\CIVIL SITE DRAWINGS\BALL SQUARE STATION\STA - 018 - BAS.DWG [SITE PLAN] 09/1


KEYNOTES

10 - PLATFORM
11 - CUSTOMER ASSISTANCE AREA & BENCH
12 - SHELTER
14 - TACTILE EDGE
15 - OFFICIALS BOOTH
16 - EMERGENCY EGRESS SLOPED WALK
17 - EMERGENCY EGRESS GATE & GUARDRAIL
20 - SIGNAGE MAP ASSEMBLY
36 - LIGHT POLE
40 - WASTE RECEPTACLES
41 - SALT STORAGE BIN
42 - SAND STORAGE BIN
43 - STARTER'S BOOTH @ (UNION & COLLEGE STATION)
44 - VARIABLE MESSAGE SIGNS (VMS)

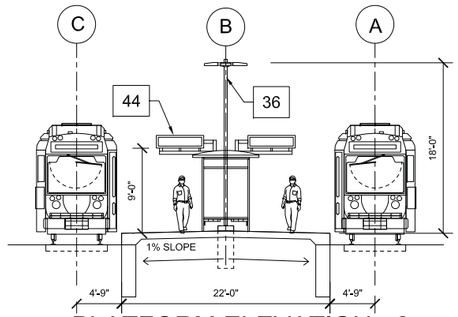


PLATFORM ELEVATION - 2

1/8"=1'-0" 0 4' 8' 16' TYPE 2B

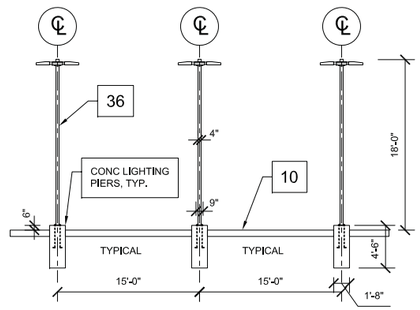

LIGHTING POLE SPACING


1/8"=1'-0" 0 4' 8' 16'

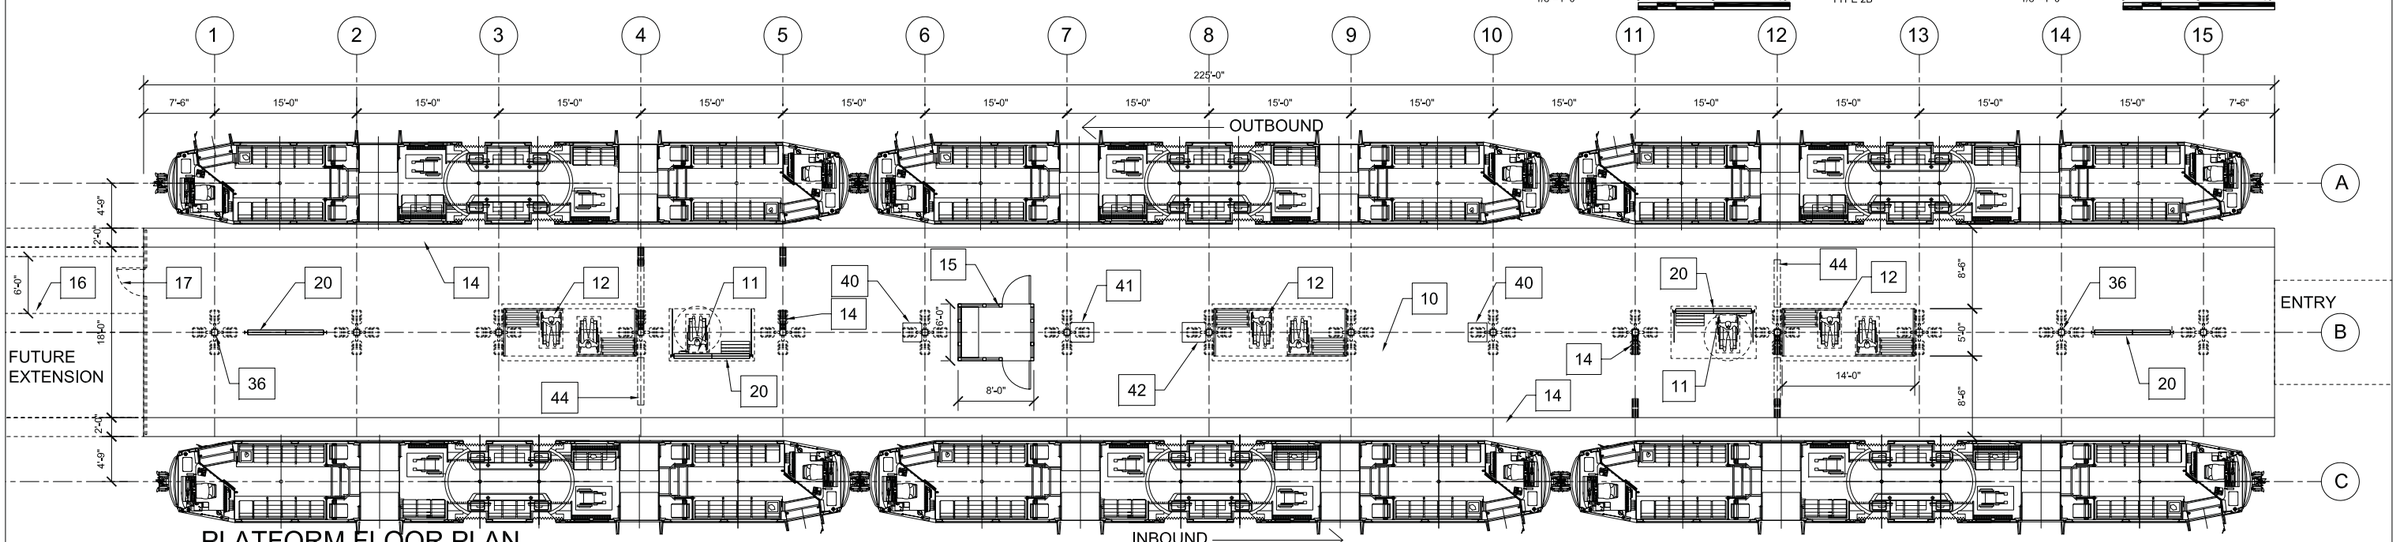

PLATFORM FLOOR PLAN

1/8"=1'-0" 0 4' 8' 16' TYPE 2B DATE: 7-14-17

TYPE 2B-(22'-0")
BALL SQ.

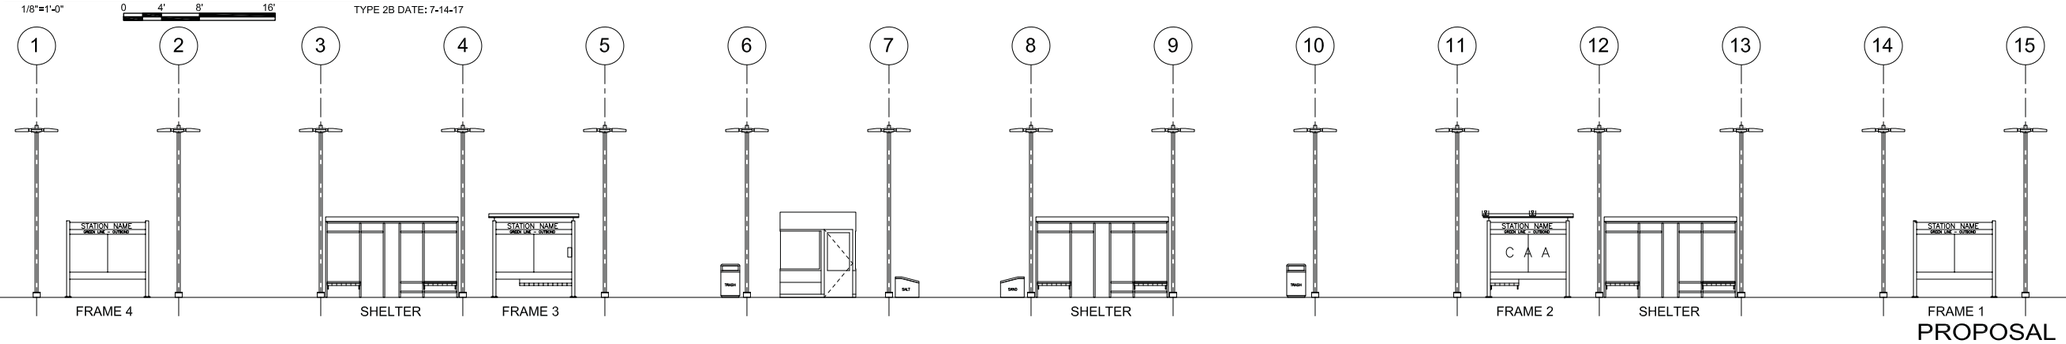

PLATFORM ELEVATION - 1

1/8"=1'-0" 0 4' 8' 16' TYPE 2B DATE: 7-14-17

PLATFORM TYPE 2B - BALL SQUARE - 22'-0" WIDE PLATFORM

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


BALL SQUARE STATION
STATION PLATFORM AT GRADE
ELEVATION AND SECTION

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	EMT	SHEET: STA-019	.

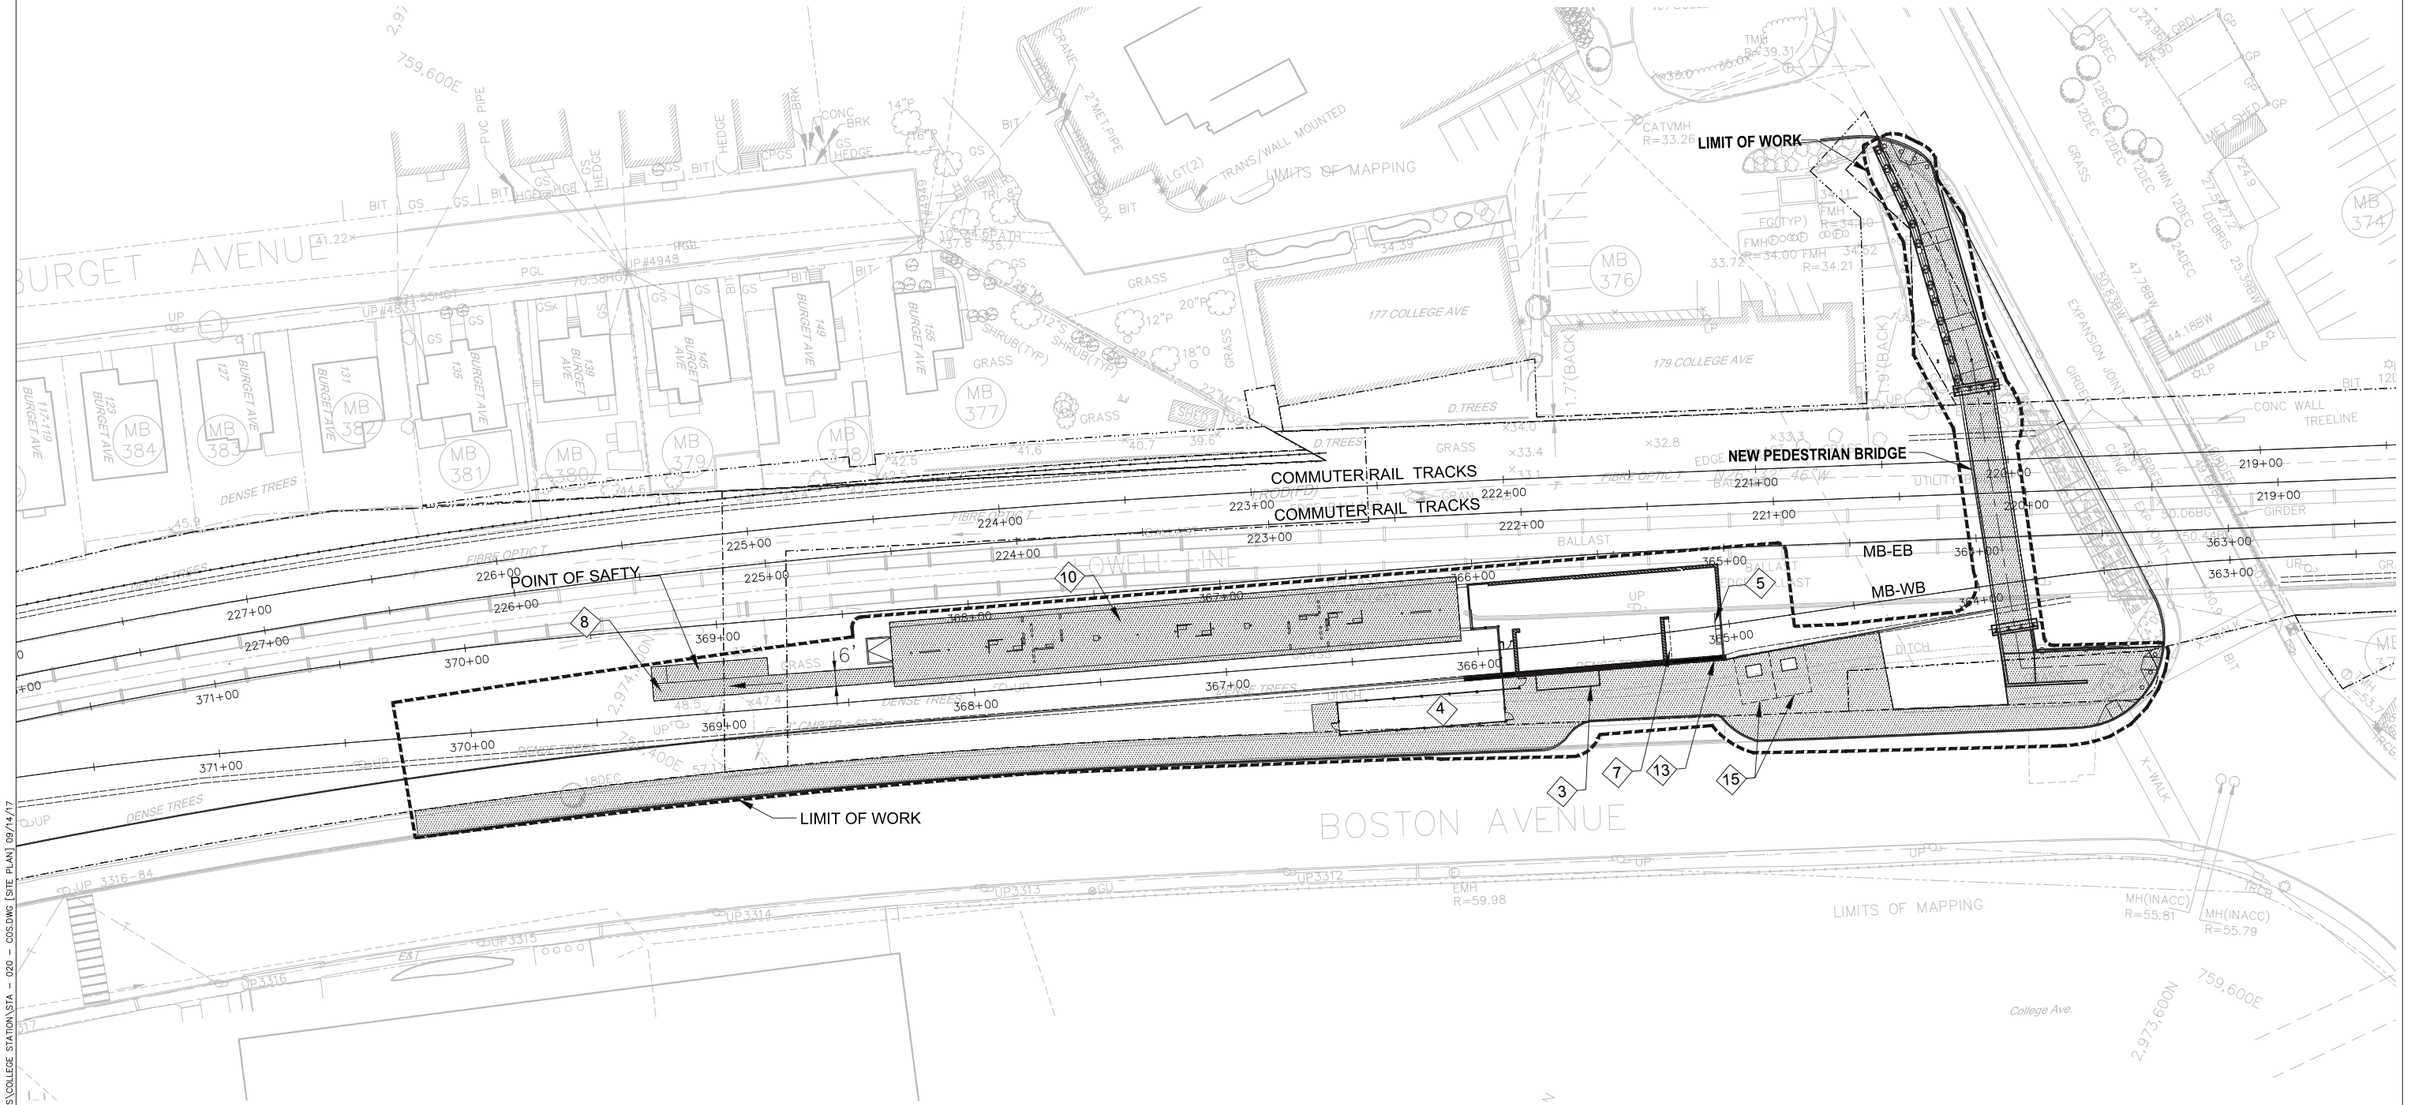

1 SITE PLAN
SCALE: 1"=30'

KEYNOTES

3. BICYCLE RACK
4. BICYCLE STORAGE
5. BENCHES
7. FARE VENDING MACHINES W/9' ROOF
8. EMERGENCY EGRESS SLOPED WALK
10. PLATFORM
13. ROLL UP SECURITY GRILLE
15. TRANSFORMER

SHEET NOTES

1. PLATFORM LENGTH TO BE 225' WITH A POTENTIAL EXTENSION TO 300'.
2. SEE PROPERTY LINE DRAWINGS FOR LIMIT OF WORK

LEGEND

PROPOSED CONCRETE

0 30' 60'
SCALE: 1" = 30'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

COLLEGE AVENUE STATION
SITE PLAN - STREET LEVEL


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT 28, 2017	YQT	YQT	MWR	SHEET: STA-020	

PLOTTED: 09/14/17 11:40AM BY:TANGYQ
DRAWING: I:\PROPOSALS\2017\0062820 0002 GLX GREEN LINE STATIONS\CIVIL SITE DRAWINGS\COLLEGE STATION\STA - 020 - COS.DWG [SITE PLAN] 09/14/17

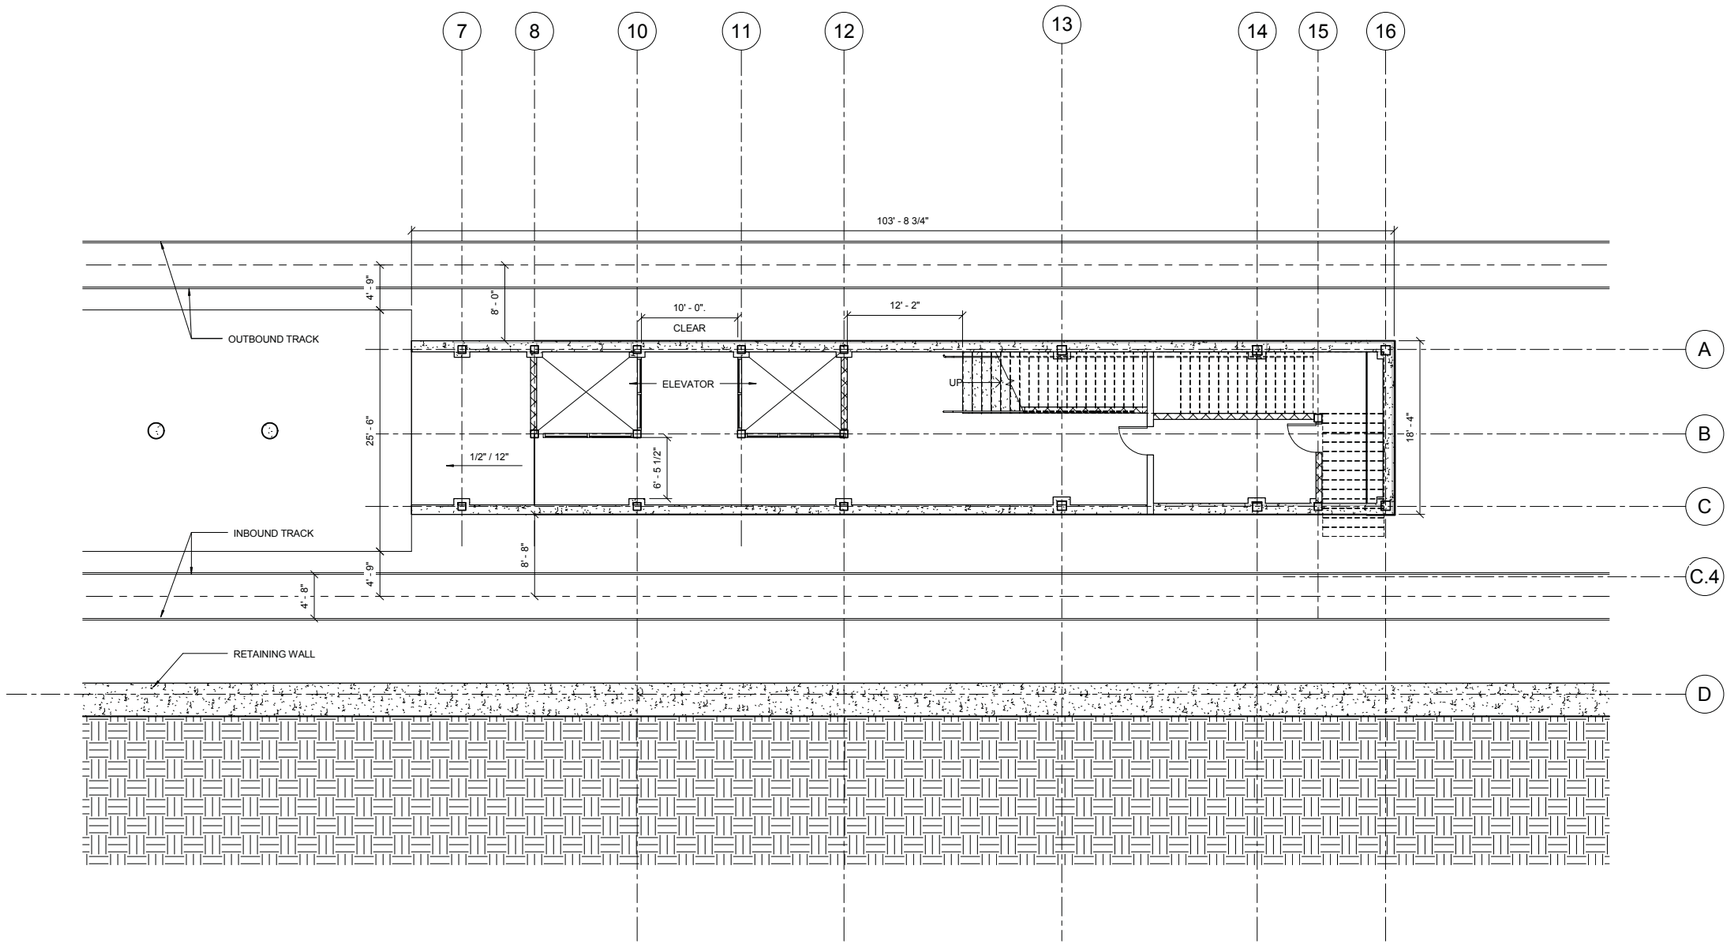

STATION PLATFORM - HEADHOUSE

1/8" = 1'-0"

0 4' 8' 16'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

COLLEGE STATION
STATION PLATFORM FLOOR PLAN


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: STA-021	

9/14/2017 3:04:30 PM
C:\Users\shelbuaj\Documents\College_A_3D0000_Shelbuaj.rvt

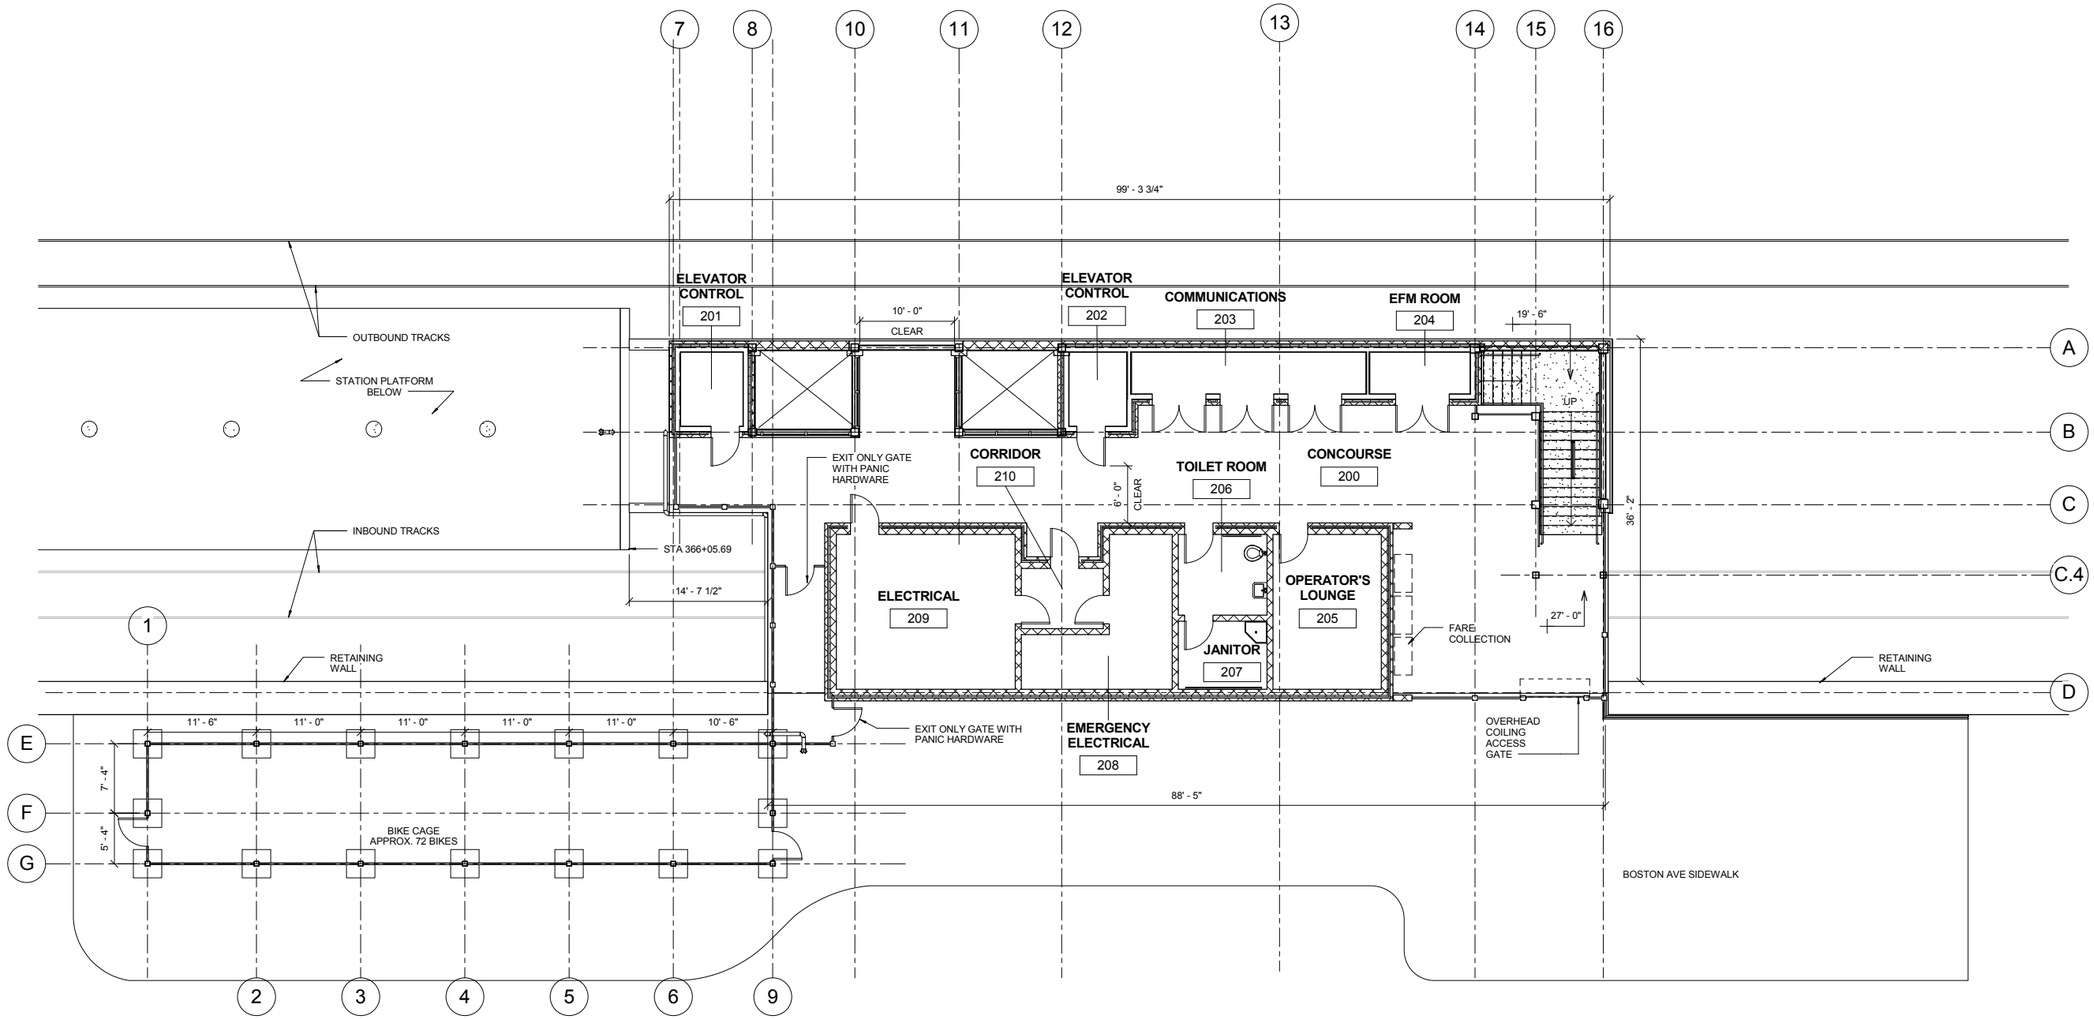

STATION HEADHOUSE - STREET LEVEL

1/8" = 1'-0"

0 4' 8' 16'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

COLLEGE STATION
BOSTON AVE FLOOR PLAN


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: STA-022	


9/14/2017 3:21:57 PM
C:\Users\shelbuaj\Documents\College_A_3D0000_Shelbuaj.rvt

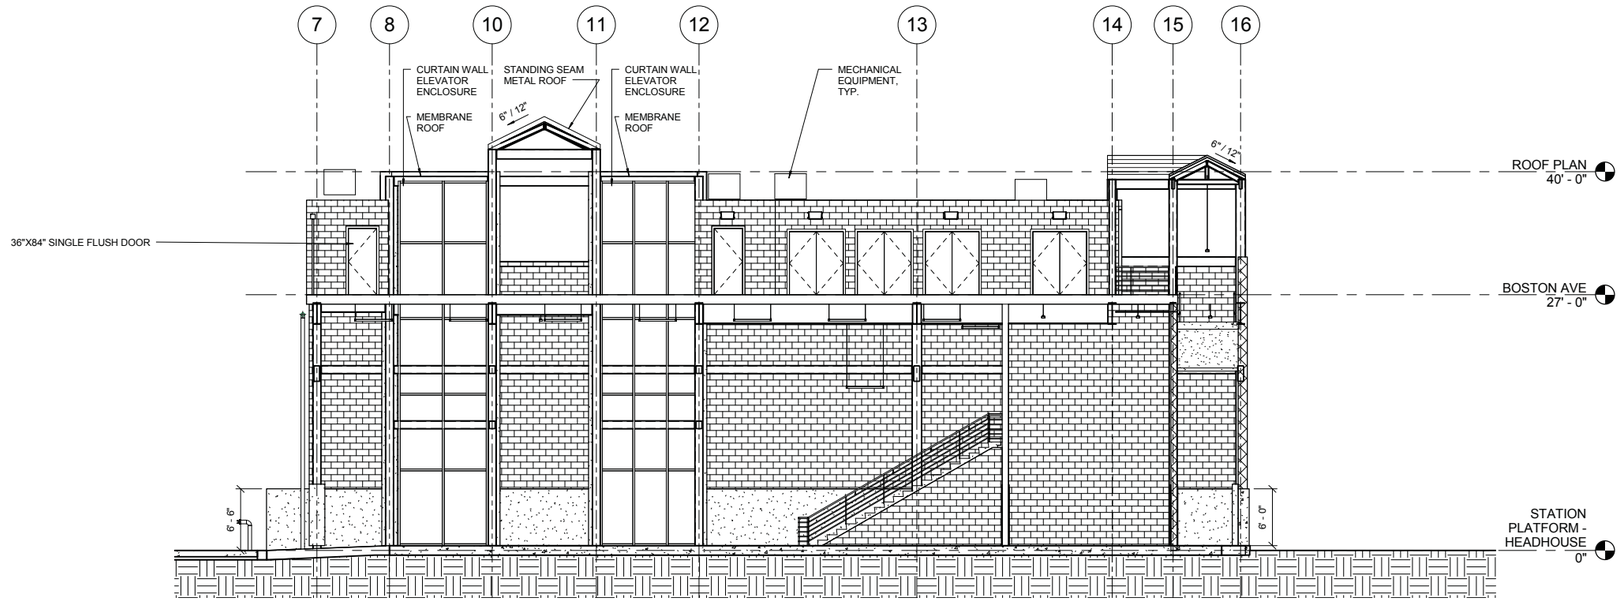

1 / A-105

LONGITUDINAL SECTION 1

1/8" = 1'-0"

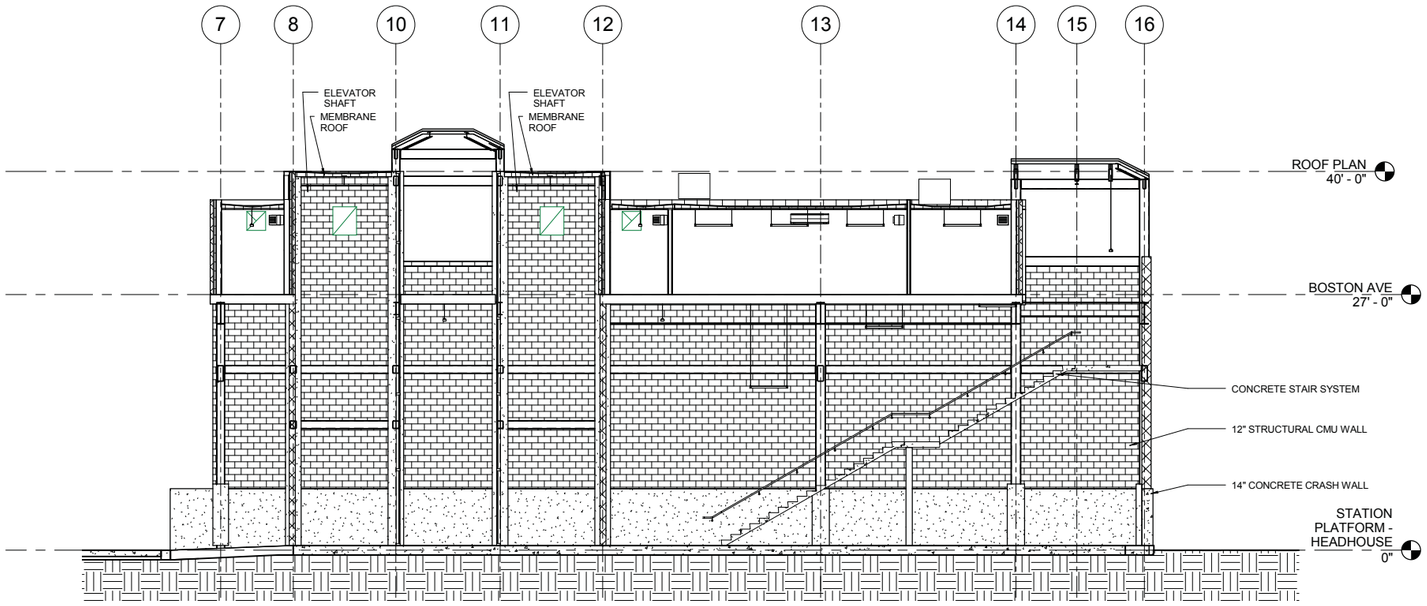

2 / A-105

LONGITUDINAL SECTION 2

1/8" = 1'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

COLLEGE STATION
BUILDING SECTIONS

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: STA-023	

9/14/2017 3:36:26 PM
C:\Users\shelbuaj\Documents\College_A_3D0000_Shelbuaj.rvt


KEYNOTES

10 - PLATFORM
11 - CUSTOMER ASSISTANCE AREA & BENCH
12 - SHELTER
14 - TACTILE EDGE
15 - OFFICIALS BOOTH
16 - EMERGENCY EGRESS SLOPED WALK
17 - EMERGENCY EGRESS GATE & GUARDRAIL
20 - SIGNAGE MAP ASSEMBLY
36 - LIGHT POLE
40 - WASTE RECEPTACLES
41 - SALT STORAGE BIN
42 - SAND STORAGE BIN
43 - STARTER'S BOOTH @ (UNION & COLLEGE STATION)
44 - VARIABLE MESSAGE SIGNS (VMS)

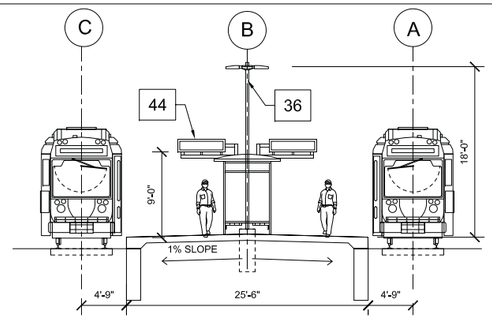


PLATFORM ELEVATION - 2

1/8"=1'-0" 0 4' 8' 16' TYPE 3

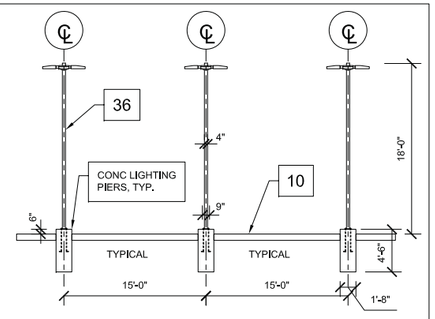

LIGHT POLE SPACING


1/8"=1'-0" 0 4' 8' 16'

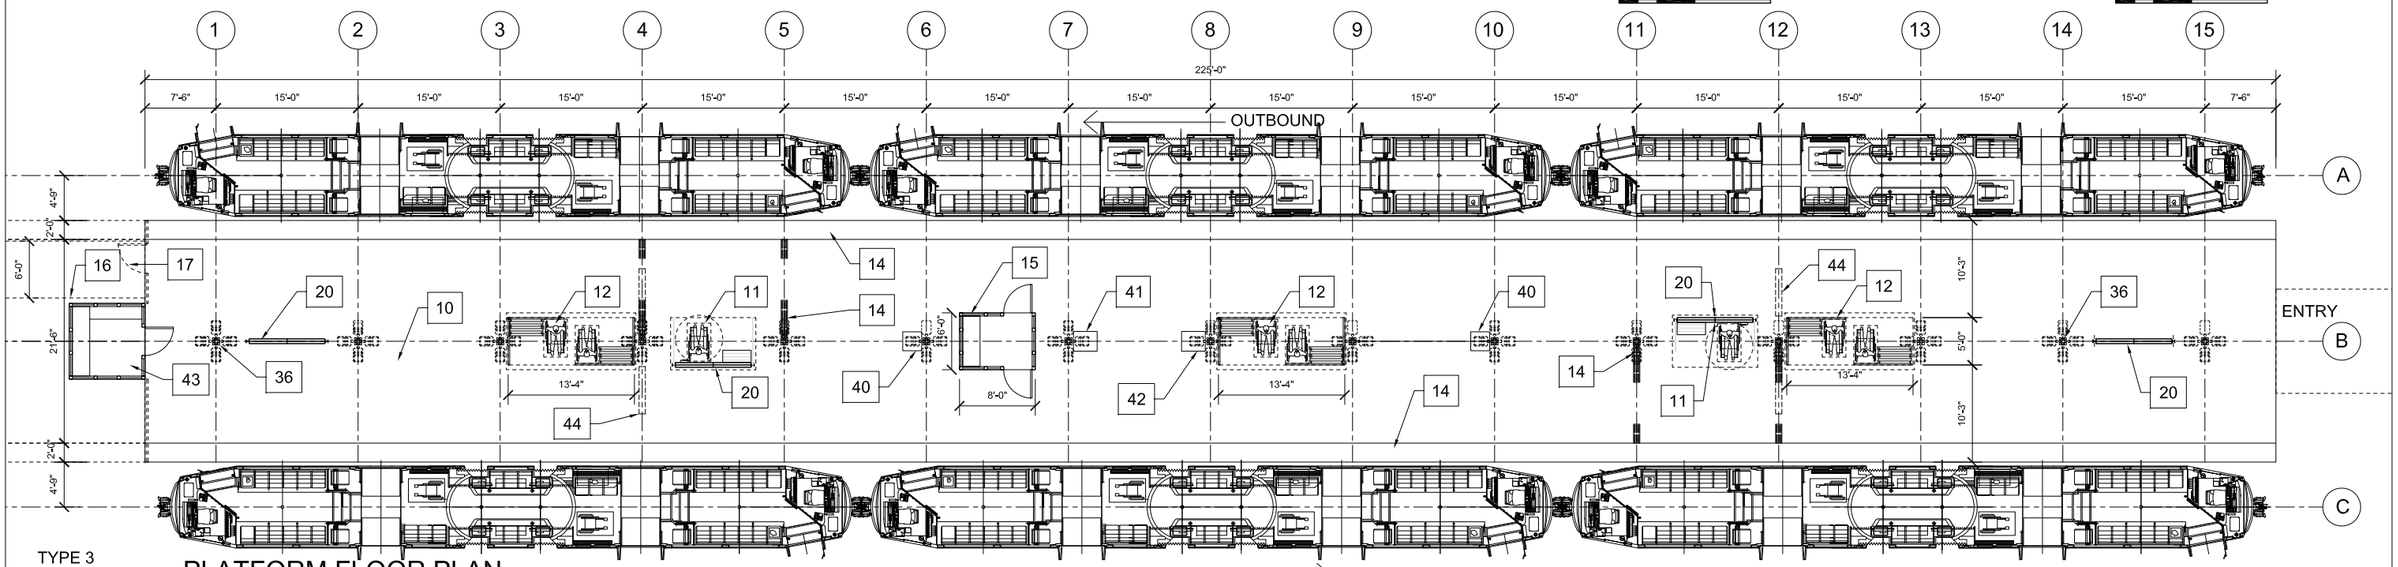

TYPE 3
COLLEGE AVE.

PLATFORM FLOOR PLAN

1/8"=1'-0" 0 4' 8' 16' TYPE 3 DATE: 7-14-17

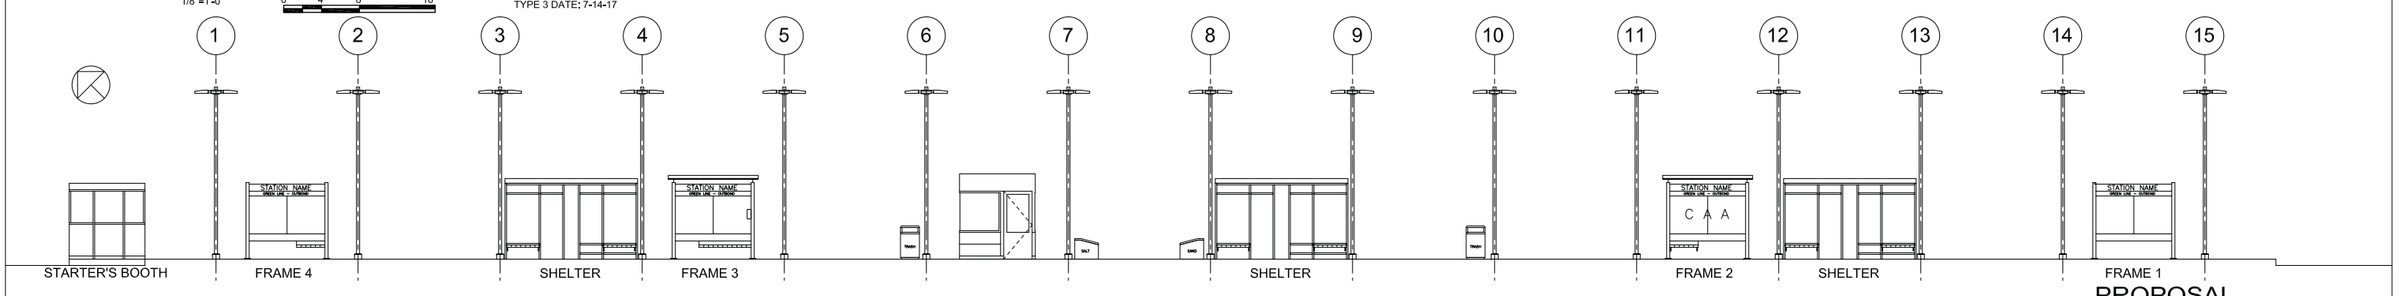

PROPOSAL

PLATFORM ELEVATION - 1

1/8"=1'-0" 0 4' 8' 16' TYPE 3 DATE: 7-14-17

PLATFORM TYPE 3 - COLLEGE AVE. - 25'-6" WIDE PLATFORM

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


COLLEGE STATION
STATION PLATFORM AT GRADE
ELEVATION AND SECTION

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	EMT	SHEET: STA-024	.

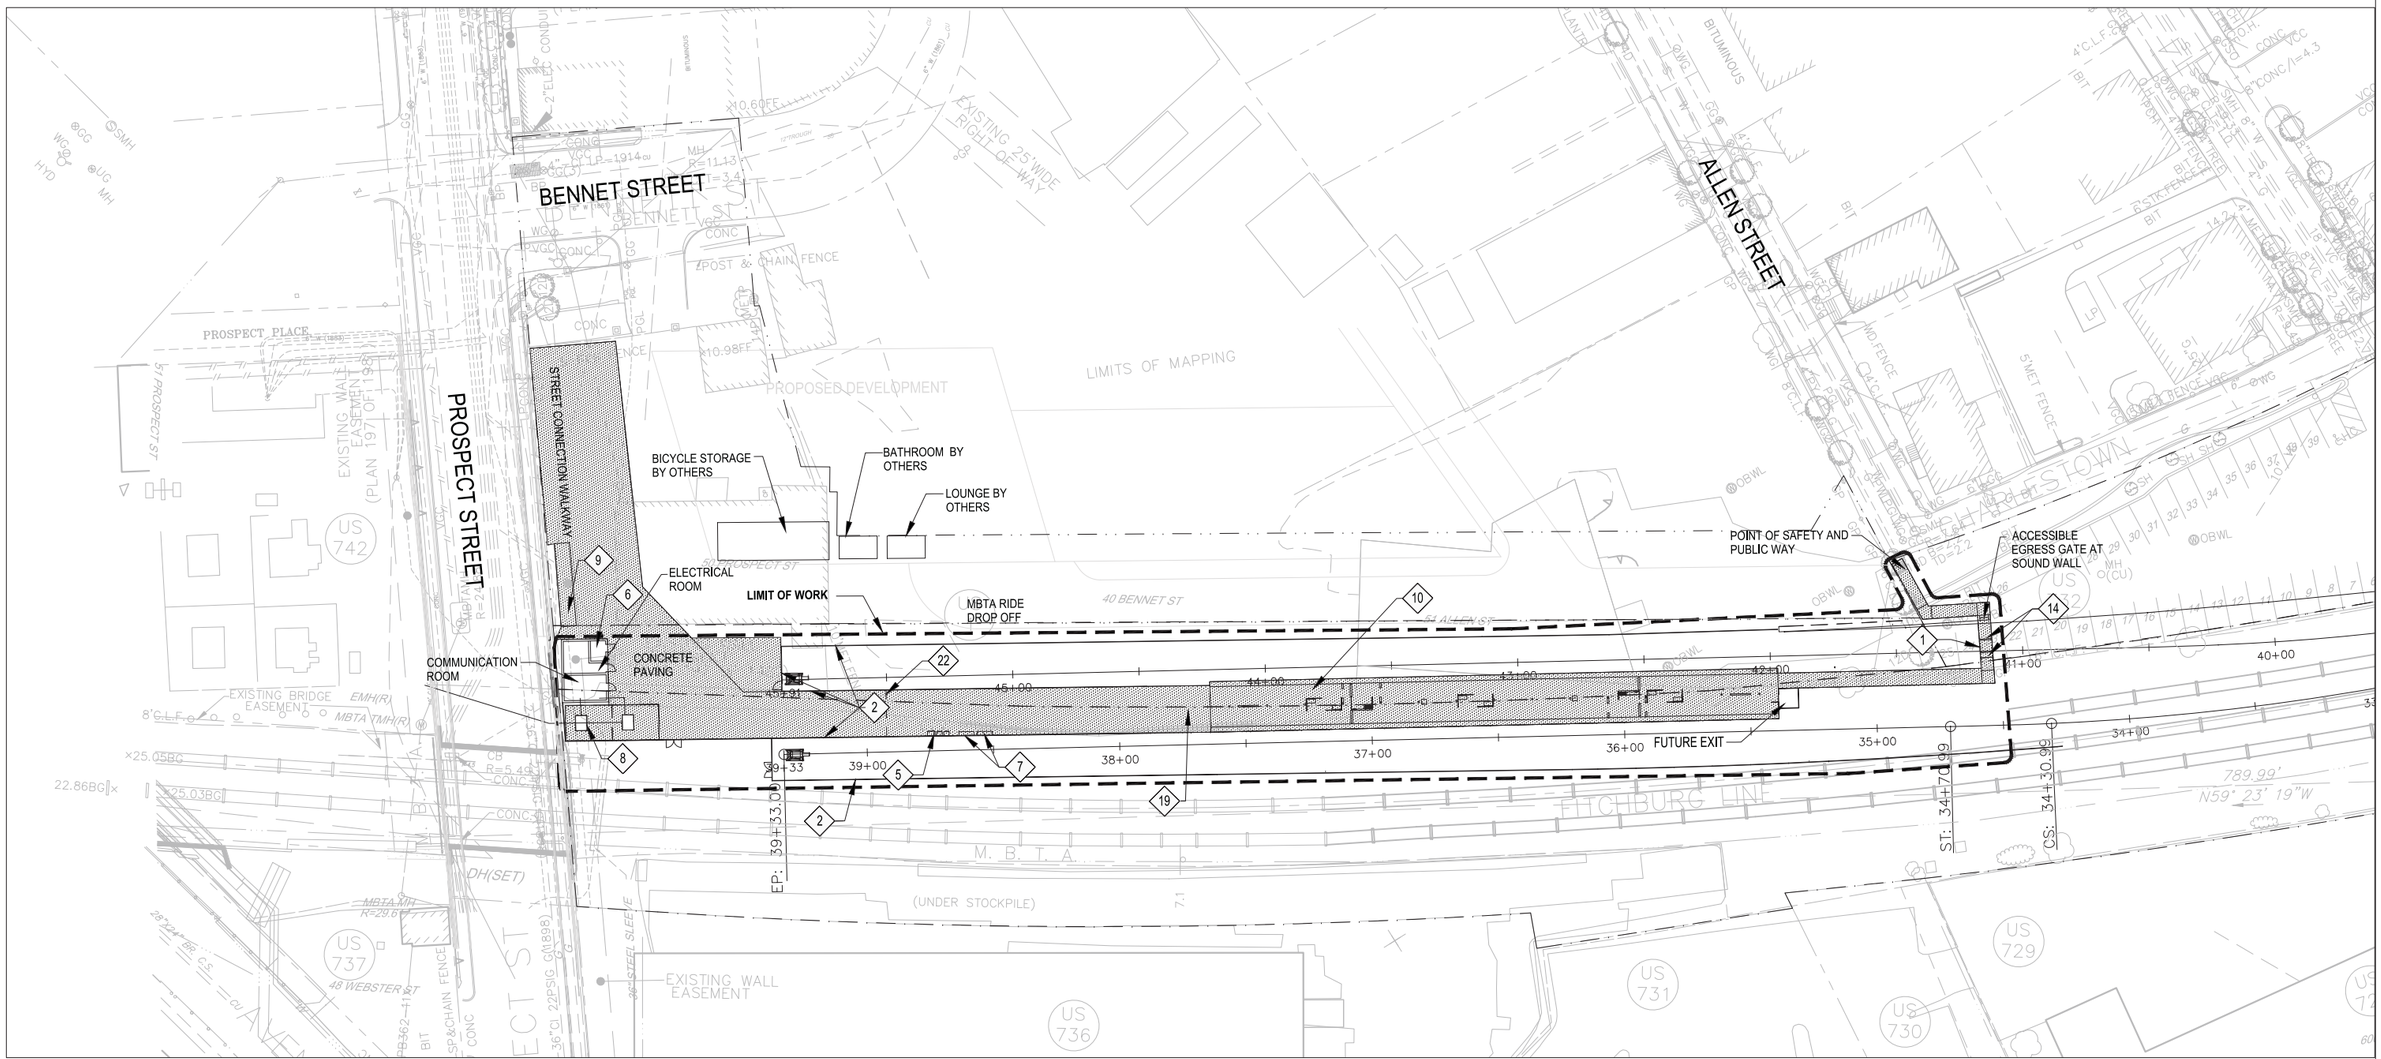

1 SITE PLAN
SCALE: 1"=30'-0"

KEYNOTES

1. TRACK CROSSING
2. CHAINLINK FENCE
4. BICYCLE STORAGE
5. FARE VENDING MACHINES W/ 9' ROOF
6. EFM ROOM
7. BENCHES
8. TRANSFORMER
9. BICYCLE RACK
10. PLATFORM
14. 2 FT WIDE TACTILE EDGE
19. SLOPED WALKWAY
22. ROLL UP SECURITY GRILLE W/ ADJACENT AFTER HOURS PERSONNEL GATE

SHEET NOTES

1 PLATFORM LENGTH TO BE 225' WITH A POTENTIAL EXTENSION TO 300'

LEGEND

PROPOSED CONCRETE

N

0' 30' 60'
SCALE: 1" = 30'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

UNION SQUARE STATION
SITE PLAN

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT 28, 2017	YQT	YQT	MWR	SHEET: STA-025	0

PLOTTED: 09/14/17 12:17PM BY:TANGYQ
DRAWING: I:\PROPOSALS\2017\0062820 0002 GLX GREEN LINE STATIONS\CIVIL SITE DRAWINGS\UNION SQUARE STATION\STA - 025 - USS.DWG [SITE PLAN] 09/


KEYNOTES

10 - PLATFORM
11 - CUSTOMER ASSISTANCE AREA & BENCH
12 - SHELTER
14 - TACTILE EDGE
15 - OFFICIALS BOOTH
16 - EMERGENCY EGRESS SLOPED WALK
17 - EMERGENCY EGRESS GATE & GUARDRAIL
20 - SIGNAGE MAP ASSEMBLY
36 - LIGHT POLE
40 - WASTE RECEPTACLES
41 - SALT STORAGE BIN
42 - SAND STORAGE BIN
43 - STARTER'S BOOTH @ (UNION & COLLEGE STATION)
44 - VARIABLE MESSAGE SIGNS (VMS)

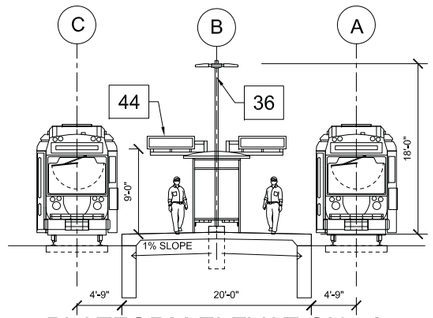


PLATFORM ELEVATION - 2

1/8"=1'-0" 0 4' 8' 16' TYPE 1B

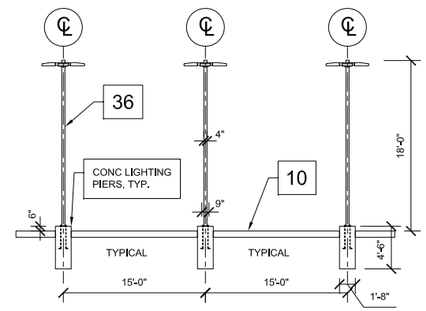


LIGHT POLE SPACING

1/8"=1'-0" 0 4' 8' 16'

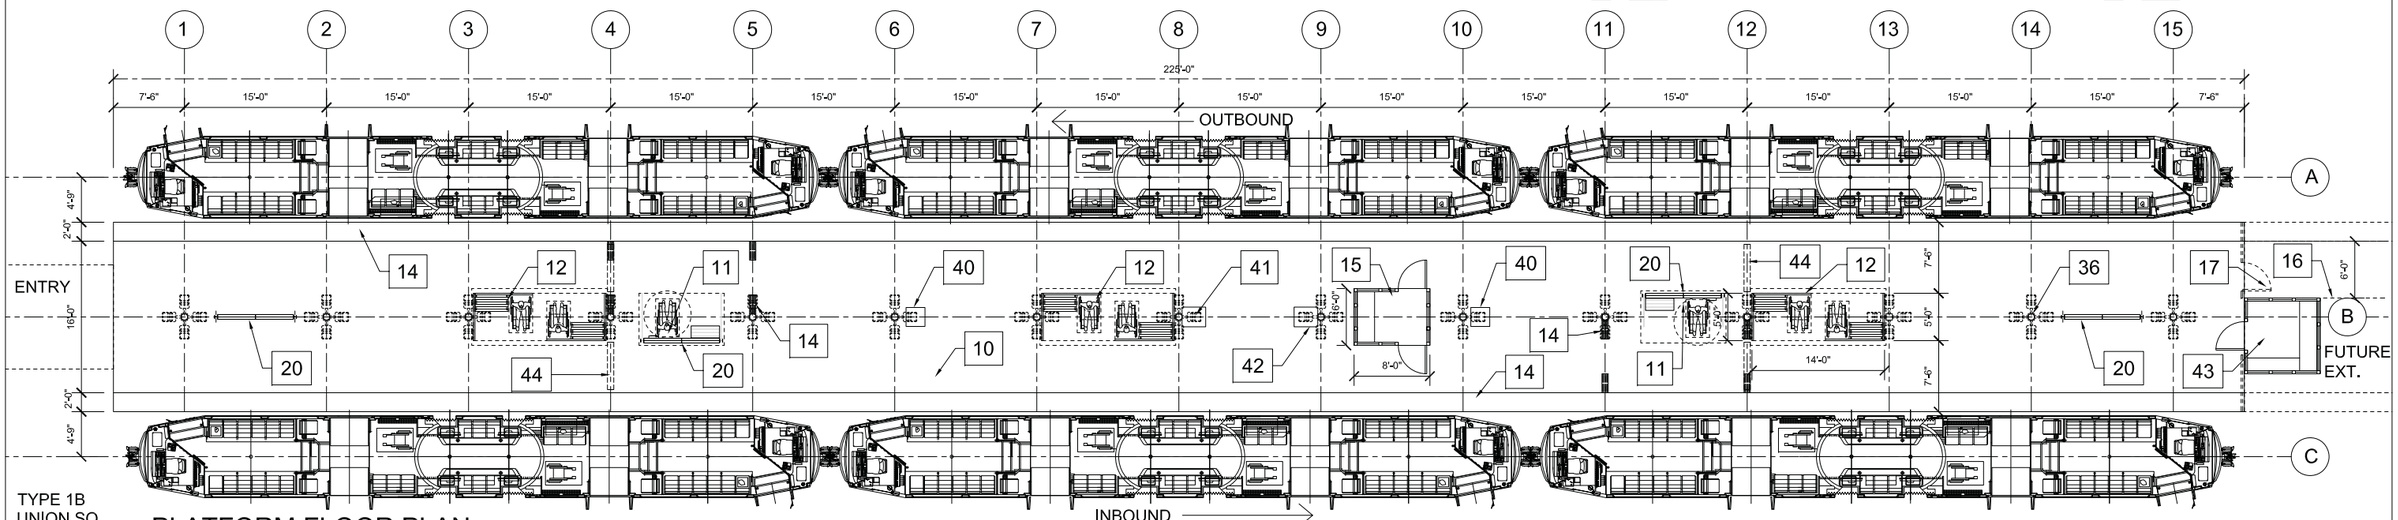

PLATFORM FLOOR PLAN

1/8"=1'-0" 0 4' 8' 16' TYPE 1B DATE: 7-14-17

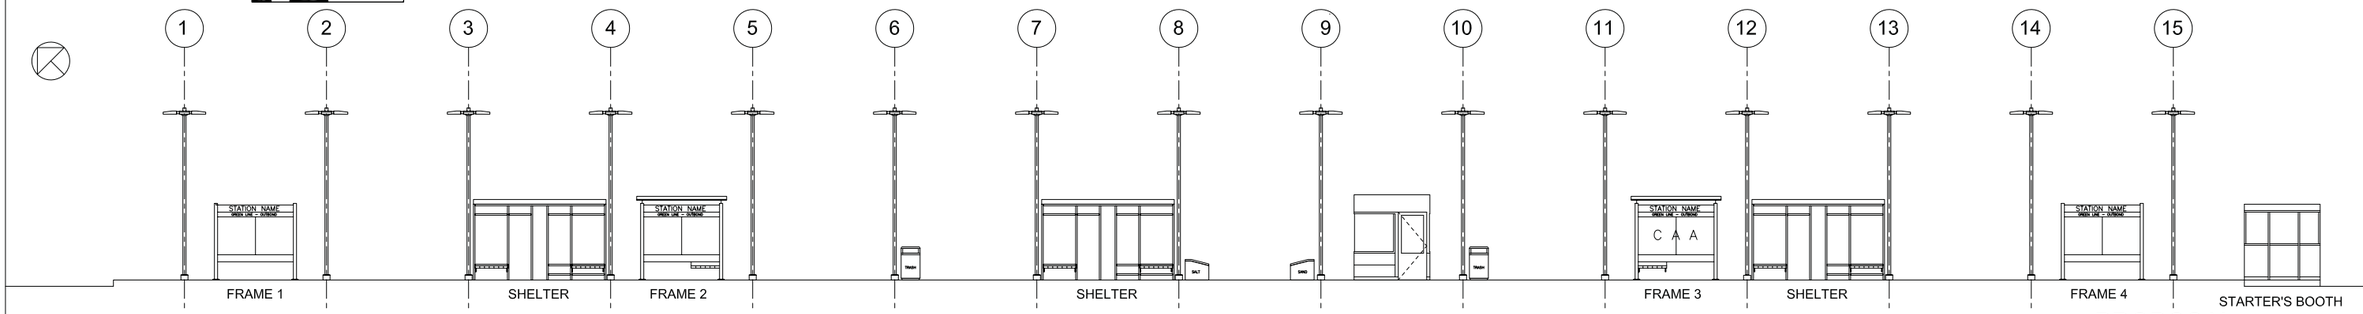

PLATFORM ELEVATION - 1

1/8"=1'-0" 0 4' 8' 16' TYPE 1B DATE: 7-14-17

PLATFORM TYPE 1B - UNION SQUARE - 20'-0" WIDE PLATFORM

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

UNION SQUARE STATION
STATION PLATFORM AT GRADE
ELEVATION AND SECTION

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-273.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS		SHEET: STA-026	.

4.4 LANDSCAPING AND STATION SIGNAGE DESIGN

The Green Line alignment landscaping is an outward expression of the MBTA's desire to enhance the public's perception toward the Project. Conforming to the requirements of the Technical Provisions, the landscaping softens the hardscapes of the Project and improves rider experience. Although the opportunity for landscaping within an urban area is limited, GLX Constructors has complemented the historic greater Boston area by assimilating the taste of the community path walkers and transit riders to the favorable, durable landscaping aesthetics.

The landscape architecture component for the Project involves preparing plans that address the site-specific needs of each station, Traction Power Sub Station, and Pump Stations. Attractive and viable plants will be designed for the stations to help mark access points, stabilize steep slopes, restore disturbed areas, and screen off station buildings. We will coordinate with third party developers to integrate the station plantings with adjacent developments. All landscaping will be designed to visually complement surrounding areas.

4.4.A LANDSCAPE ARCHITECTURE

Approach and Site Specific Designs Conformance to Landscape Requirements

"We will test and review soils, and proposed plantings will be selected to be low-maintenance, native, and drought-tolerant species that will grow in typical Northeast United States weather conditions."

One of our first tasks will be to conduct a Planting Inventory Survey to identify the existing vegetation, evaluate the condition of the plants, and determine how to best manage and/or protect these plantings. We will also complete a Tree Protection and Maintenance Plan to identify trees on abutting properties that need to be protected and cared for throughout the construction process. As required in all transportation corridor settings, the plantings will be durable, will not reduce sightlines for any mode of transportation, will not compromise the sightlines of surveillance cameras or security lighting, and will not create a nuisance of any kind.

Plantings will be installed per the Technical Provisions, to include:

- Providing minimum topsoil depths of 6 inches for seeded areas, 18 inches for shrub plantings, and 36 inches for tree plantings
- Mulching shrub and tree planting beds
- Providing tree pits that are three times the rootball diameter
- Installing salt tolerant plants resistant to snow stockpiling
- Locating snow stockpiling areas for each site.

In accordance with the MBTA's design review process, the landscape architecture plans will be shared with GLX Constructors and the MBTA for review and comment, and revisions made accordingly.

Site-Specific Landscaping Requirements

Stations. Each Green Line Station will be individually evaluated site-specific landscape architecture. For example, the East Somerville, Gilman Square, Ball Square, and College Avenue Stations will require stabilizing steep slopes, marking access points, and selecting and placing appropriate vegetative screening. The planting design process for the historic Lechmere, Gilman Square, and Ball Square Stations will allow for the required Memorandum of Agreement (MOA) design review. In the case of Union Station, the coordination with third-party developers will be required to integrate the MBTA's station planting approach with the developers' adjacent properties.

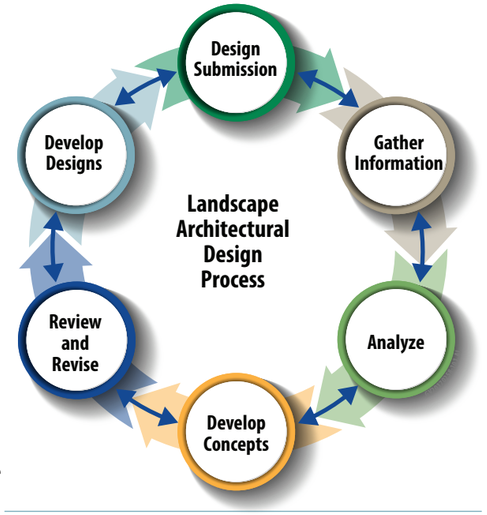


Figure 4.4-1. Landscape Architectural Design Process. *GLX Constructors' Creative Process to Developing the Landscape's Architectural Design.*

- **Lechmere Station.** We will fulfill two third-party agreements describing the tree replacements east of the historic viaduct.
- **East Somerville Station.** Requires stabilizing a steep slope between the corridor rail fence and Washington Street Pump Station. This includes furnishing 12 inches of planting medium, drought-tolerant erosion control seed mix, and slope stabilization fabric.
- **Union Square Station.** We will coordinate the work and phasing activities with the third-party developer for the surrounding areas.
- **Magoun Station.** Located in an urban environment and built on a structure that will not support plants. So there are no landscape architectural plans for Magoun Station. However, GLX Constructors will complement the station design with as much greenery over the hardscape as site conditions will allow.
- **Gilman Square Station (Historic).** We will screen the Traction Power Sub Station with trees and shrubs as shown in Figure 4.4-2. We will also provide 6 inches of planting medium and drought-tolerant erosion control/restoration mix with slope stabilization fabric at disturbed areas between corridor fence, the retaining wall/community access path, and above the retaining wall on the existing steep hillside.
- **Ball Square Station.** The work at Ball Square Station consists of shrub and grass plantings to mark the station entrance and the stabilization of an adjacent steep slope off of the Broadway Street Bridge. In the course of this work, we will provide 6 inches of planting medium and drought tolerant erosion control/restoration mix installed with slope stabilization fabric.

- **College Avenue Station.** We will incorporate plants at the station entrance as shown in the Project Definition Plans and in Figure 4.4-3. Which specify installing deciduous flowering trees, 13-15 feet in height, placed no closer than 10 feet from the corridor fence, shrubs 24-36 inches in height, spaced at 30-36 inches on center, woody groundcover, and perennial plantings spaced at 18 inches on center with mulch provided for all planting beds.

We will also stabilize the sloped area above the proposed retaining wall and the Boston Avenue sidewalk extending the length of the retaining wall. We will do this by installing 6 inches of planting medium, drought-tolerant erosion control/restoration mix with slope stabilization fabric, and shrubs with stabilizing root systems.

Vehicle Maintenance Facility. This planting design will mark the entrance to the facility from Third Avenue and Inner Belt Road and create a natural accent to this urban industrial site, including creating a meadow for the future Transportation Building (TSP). The Inner Belt Road entrance and parking lot planting design incorporates plants as shown in the Project Definition Plans. At the future TSP site, we will install 6 inches of planting medium and drought-tolerant seed mix. The shrubs will be 24-36 inches in height and spaced at 30-36 inches on center. Woody groundcover will be provided, and perennial plantings will be spaced at 18 inches on center. The specified trees will be deciduous and chosen for their canopy shape with a minimum initial caliper of 3-3.5 inches. We will mulch all plant beds.

Traction Power Substations. The Traction Power Substations (TPSS) at Gilman Square and Ball Square will be screened with vegetation to limit the view of the power facilities. Coniferous trees with an initial height of 8-10 feet will be used, as well as a variety of other trees and shrubs, to create an effective and attractive screen. The TPSS at Gilman Square is between the station platform and Medford Street. The TPSS at Ball Square is located between the station platform and Boston Avenue.

Transit Corridor. In addition to completing the existing Planting Inventory Survey, GLX Constructors will direct the development of a Tree Protection and Maintenance Plan for abutting properties. The Planting Inventory Survey will identify existing vegetation impacted by the Project, and evaluate the condition of the plants to determine the best way to protect them. The Tree Protection and Maintenance Plan will identify trees on abutting properties that need to be protected and cared for throughout the construction process.

Planting Criteria

All plantings will be installed per the requirements as stated in the Technical Provisions. These include selecting native New England plant material that is drought tolerant, disease resistant, low maintenance, and produce no appreciable vegetative litter.

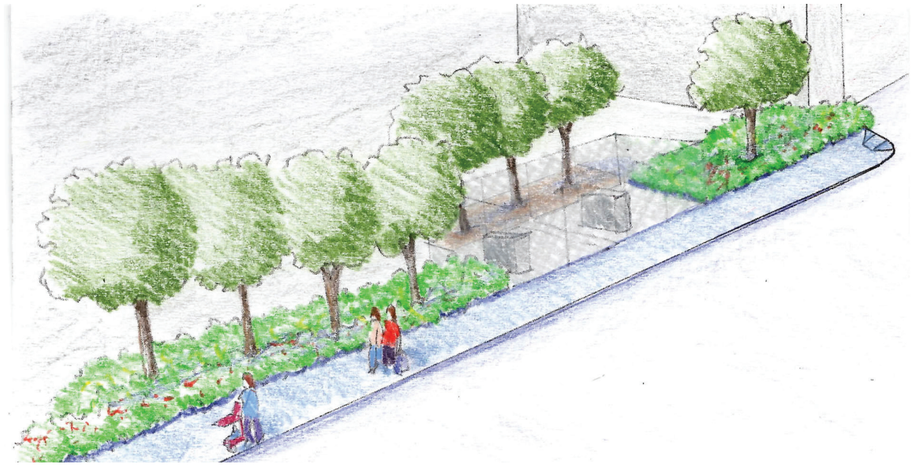


Figure 4.4-2. Streetscape on Medford Street at Gilman Square Station. *Landscaping elements were included to screen the TPSS with trees/shrubs.*

The plant material will conform to American Standard for Nursery Stock ANSI Z60.1 and will have a one-year planted material guarantee of watering and maintenance period, as specified in the Landscape Maintenance Plan. The street trees will conform to the municipality specifications, including compliance to pedestrian, bicycle, and vehicle passage standards. The proposed deciduous trees will have a minimum caliper of 3-3.5 inches and the evergreen trees will be a minimum height of 8-10 feet. These trees will be selected to minimize leaf litter on the tracks, will be located a minimum of 10 feet from the ROW fence, and will avoid conflict with any utilities. All plants and seed mixes will be suitable for Zone 5 planting zone.

We will obtain and review soil tests of stockpiled or base loam intended for planting medium, an analysis of proposed amendments such as compost, other organics and/or sand, and an analysis of proposed ratios of all planting medium components or blended planting mediums. Submittals will also include verification of subgrade compaction prior to placing planting medium, and the procurement, placement method, and management of placing the planting medium.

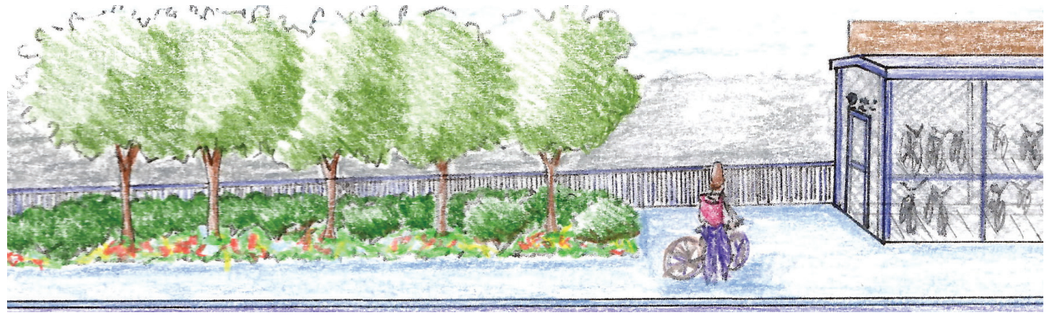


Figure 4.4-3. College Station Entrance Plaza and Bicycle Storage Facility.

Site Amenities and Furnishings

At the Community Path, we will identify and specify the type and location of bench, trash, and recycling receptacles to be installed. These selections will comply with the City of Somerville's to best integrate this new path with the existing multi-use path system. This work will be designed and completed as specified in the Technical Provisions, including placing furnishing at every 1,000 feet and at each side of roadway intersections. The benches, trash, and recycling receptacles will be placed on concrete slabs. Trash and recycling receptacles will be placed on each side of the street at each at-grade street crossing of the Community Path.

Third Party Agreement Requirements

A Third-Party Agreement pertaining to vegetation requirements calls out the replacement of all trees to the east of the Lechmere viaduct at 7-13 East Street, 1 Leighton Street, and 1-5 East Street in Cambridge. An additional Third Party Agreement for 360 Medford Street, Somerville, specifies that nine new trees meeting the City of Somerville standards will be installed at that site. Careful consideration will be given to the type and size of the existing trees to be replaced in Cambridge, and to the tree types that flourish in Somerville, such as planting new trees in a pit that is three times the width of the new tree's rootball. All trees will be installed as specified in the Technical Provisions.

Landscape Drawings for Stations

Renderings for Typical Grading, Materials, Site Amenities, and Furnishings



Figure 4.4-4. View of Third Avenue Entrance to Vehicle Maintenance Facility. *Typical grading, materials, site amenities for the Third Avenue Entrance to the VMF.*

4.4.B WAYFINDING, SIGNAGE, AND VISUAL DISPLAY

Overall Visual Elements Strategy

Because there are three different types of stations along the alignment, each station type requires a different visual element strategy. Visual elements will be developed based on each station type's characteristics, which are detailed in Figure 4.4-5.

Elevated	Depressed	On-Grade
Lechmere	Gilman, Magoun, and College	Union, East Somerville, and Ball
▸ Station entrance is on grade under viaduct with elevators and stairs up to center platform. ▸ Two entrances, one at each end of the platform, which also serve as exits. ▸ Intermodal station with bus loop and RIDE stop.	▸ Station entrance is on grade under viaduct with elevators and stairs up to center platform. ▸ Two entrances, one at each end of the platform, which also serve as exits. ▸ Intermodal station with bus loop and RIDE stop.	▸ Station entrance is at track level between end of tracks at Union, and at track level requiring and on grade track crossing at East Somerville and Ball. ▸ There is one entrance, and an exit used only in emergencies. ▸ Union is intermodal with RIDE stop.

Figure 4.4-5. Station Types along the Alignment. *The overall visual elements strategy will be based on the specifications of each station.*

Approach to Placement and System Integration of Signage and Common Elements

The station signage components are the common denominator of the MBTA's system-wide visual elements strategy. Signs act to confirm intuitive wayfinding, and to distinguish between accessible and non-accessible wayfinding when they are not in parallel. They also set precedent for scale, color, materials, and detailing when interfacing with the MBTA's customers. Moreover, they comprise a tried-and-true system, are modern, and have proven themselves adaptable to new technologies introduced over time.

The Green Line Extension's alignment and the distribution of stations along its corridor, located at accessible points, have resulted in several different configurations of stations.

While the exact nature of the access to the platform varies, each station's presence is pronounced by one or more MBTA or lollipop signs as shown in Figure 4.4-6 at the sidewalk or Community Path. Each has an associated bicycle storage facility and an entrance properly defined by the entrance sign bearing the station's name at the roll up security grille, a street/lobby sign informing incoming passengers of their inbound, outbound and system-wide options, and the platform signs, which dictate the design of the platform.

These elements are complemented by track signs bearing the name of the inbound and outbound destination and the "Emergency Exit Only" sign, which clearly demarcates the end of the platform and the public realm.

At Lechmere Station, the entrance/exit sign and security grille are incorporated into the fence capturing both the bottom of the stair and elevator. These are adjacent to one another and the elevator is signed. The street/lobby sign displaying the rapid transit and green line maps are also located on the secure side with the fare machines and associated benches.

While there is ample space for queuing at the machines, it is evident that this is a dedicated circulation route leading to one destination only—the platform. Vertical circulation is parallel and the top of the stair meets up again with the platform elevator stop, also signed. Arrival at the platform is confirmed by another entrance sign, stating "GREEN LINE – ALL TRAINS." The platform side of which indicates that the main entrance is also an exit.

Each side of the platform includes track signs stating the destination of the train and length of wait predicted by the variable message signs as shown in Figure 4.4-7. The inbound and outbound directions of the tracks determine the sequence of information provided on either side of the platform, which is set by associating a Customer Assistance Area with the lead train. The platforms influence the location of all the other elements on the platform, including the shelters.

Boarding passengers will see a repetition of the rapid transit line map and either a green line inbound or outbound map. Neighborhood maps are provided for disembarking passengers, which they will encounter again as they exit past the street/lobby sign at the station entrance. The emergency egress at the inbound end of the platform opposite the entrance is also signed.



Figure4.4-6. Bike Storage Facility. *Example of typical signage and space provided to dismount an stow bicycles in the storage facility.*



Figure 4.4-7. Variable Message Signs at Platform at Ball Square Station.

Approach to Provide Intuitive Wayfinding

At East Somerville Station, which is one of the three on-grade stations, there are two T signs, both of which will be encountered entering from Washington Street onto the Lower Community Path where the first is located. The second is located at the landing between the Lower and Upper Community Paths, and it is the only one encountered when inbound on the path. Given the distance of the station platform off the street, it is necessary to provide signage at both points; both an entrance sign and a street/lobby sign are proposed in each location.

Regrading the Lower Community Path, within the definition of a sloped walkway, to shift the landing from opposite the inbound end of the platform to opposite the outbound end of the platform separates the actual station entrance from the bicycles through traffic on the path.

The dedicated entrance walkway from the landing parallels the station platform, which provides full visibility from one side to the other across the inbound track and ROW fence. However, it also provides adequate space to dismount and stow a bicycle in the storage facility without interfering with pedestrians entering the station. At this point, the ROW fence is an obvious location for a transparent, linear art piece. The station entrance, consisting of a roll up security grille carrying the station entrance sign, is fully visible from the Upper Community Path and the landing. To limit time spent in the ROW, the station entrance is purposely located close to the track crossing at the entrance end of the platform, where the fare vending machines are located.

Approach to Accessible and Non-Accessible Wayfinding Routing

At Gilman Square Station, located between the Medford Street and School Street bridges, the access to the center platform is from the Community Path. The elevated path and station-side entrance bridge remove the need for a track crossing, providing system-wide benefits. In addition to a staircase, an elevator to the platform provides universal access. The elevator and stairs are both pass-through, and allow users an uninterrupted path from bridge to top of elevator or stairs, down either, then enter directly on to the platform below.

This configuration also allows for a physical expression that is interesting, especially because both the entrance bridge and platform are exposed to the public realm, and the connecting stair and elevator elements are transparent. The architectural language originates with the signage and associated furnishings, which drive the platform design such that the platform itself becomes an element, and which extend out past the station entrance and are visible to the surrounding community. Figure 4.4-8 Shows the Gilman Square Station bike storage facility.

At both the Medford and School Street ends of this segment of the Community Path, there will be a T sign announcing the presence of the station. The station entrance will be defined by the overhead GILMAN STATION sign. The bike storage facility opposite it will carry its own signage, and allow for the street/lobby sign. The fare vending machines and associated benches are immediately inside the entrance and are again available at the elevator. Properly sized and located, these elements combine to form a cohesive whole that is recognized as a station belonging to the Green Line. The sequence is familiar and predictable, offering immediate feedback and assurance to someone in unfamiliar territory that they are on the right track.

The landscape and station signage design for the Project will provide an aesthetically positive environment. The greenery, plants, and signage will alleviate the harshness of the large, urban facility by screening some of the more industrial transit components – all while providing key indicators for the traveling paths. These designs will contribute to the safety of the corridor as they clearly define the designated pedestrian areas and welcome riders to the Green Line.



Figure 4.4-8. Gilman Station Bike Storage Facility. *Stations and associated facilities have identifiable elements and signage to form a cohesive and recognizable design.*

ITP Request	RFP		
	Drawing Number	Drawing Title	Reference Section or Drawing
A5.2.4.A.2			Landscaping drawings are represented by the graphics and renderings provided with the section narrative.
A5.2.4.A.3			Landscaping drawings are represented by the graphics and renderings provided with the section narrative.
A5.2.4.B.2	LS-001	Ball Square Station Site Plan - Static and Variable Message Signage	
	LS-002	Ball Square Station Static and Variable Message Signage @ Station Platform	
A5.2.4.B.3			Landscaping drawings are represented by the graphics and renderings provided with the section narrative.

Technical Solutions Drawing Matrix.




EYE VIEW OF BICYCLE ENCLOSURE LOOKING EASTWARD



EYE VIEW AT STATION ENTRANCE



ACTIVE WAYFINDING SIGNAGE AT STATION PLATFORM

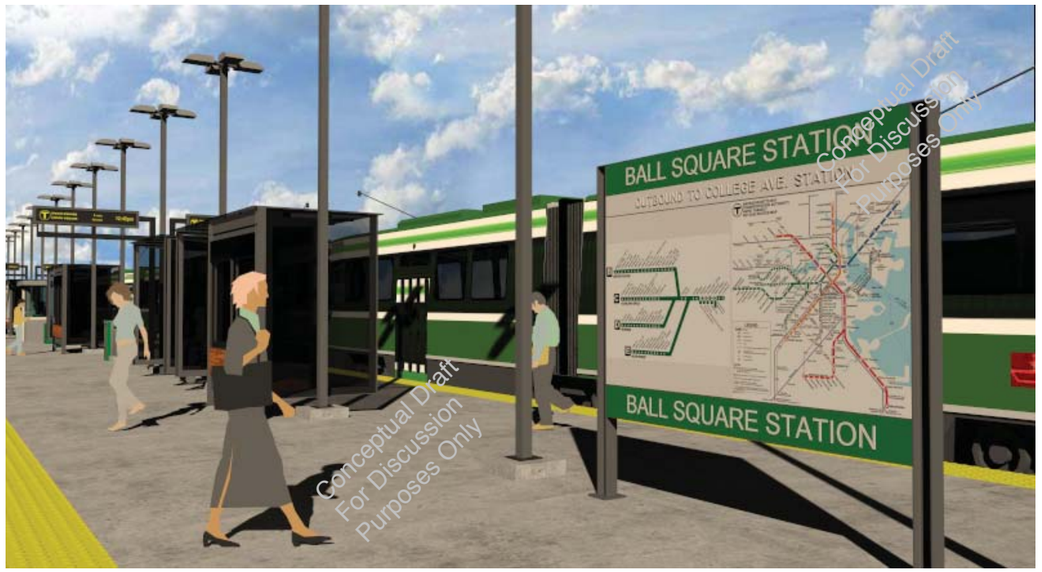

PASSIVE WAYFINDING SIGNAGE AT STATION PLATFORM

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

BALL SQUARE STATION SITE PLAN
STATIC AND VARIABLE MESSAGE SIGNAGE

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-274.pdf

SCALE: N.T.S.	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	ND	SHEET: LS-001	

PLOTTED: 08/22/17 4:19PM BY:DESIMOP
DRAWING: C:\USERS\DESIMOP\APPDATA\LOCAL\MICROSOFT\WINDOWS\TEMPORARY INTERNET FILES\CONTENT.OUTLOOK\JRNXCRUP\PROPOSAL BORDER.DWG [MODEL] 08/1



AERIAL VIEW FROM BROADWAY EASTWARD



AERIAL VIEW FROM BOSTON AVE NORTHWARD



EYE VIEW FROM BOSTON AVE LOOKING EAST



EYE VIEW FROM BROADWAY LOOKING WEST

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

BALL SQUARE STATION STATIC AND VARIABLE MESSAGE SIGNAGE @ STATION PLATFORM

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-274.pdf

ISSUE	DATE	DESCRIPTION	BY	CHKD	APP.

SCALE: N.T.S.	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	ND	SHEET: LS-002	

PLOTTED: 08/22/17 4:17PM BY: DESMOP
DRAWING: C:\USERS\DESMOP\APPDATA\LOCAL\MICROSOFT\WINDOWS\TEMPORARY INTERNET FILES\CONTENT.OUTLOOK\3RNXCRUP\PROPOSAL BORDER.DWG [MODEL] 08/1

4.5 VEHICLE MAINTENANCE FACILITY

Green Line commuters expect that their daily commute take place in a safe, clean, and reliable vehicle. It is imperative that Light Rail Vehicles (LRV) are serviced daily at the Vehicle Maintenance Facility (VMF) to meeting operational needs. Similarly, a carefully programmed Transportation Building is important to support the operations at the VMF, LRV storage track yard, and revenue service along the ROW. Reliable Green Line operations will be delivered by a durable VMF and Transportation Building that are designed and built to perform for decades to come.

Our Lead Designer, STV, has worked with the MBTA the Orange Line Carhouse Project, which recently broke ground in July 2017. Based on STV's MBTA knowledge and GLX Constructors' experience delivering similar infrastructure facilities nation-wide, our team will provide constructible designs that meet the expectations of MBTA earlier and deliver the Project on schedule.

4.5.A ARCHITECTURAL DESIGN

Twentieth century architect Louis Sullivan, the inventor of the modern high rise, coined the phrase "form follows function." We have conceived a design where the form is functional and provides a safe, durable, and accessible working environment for the MBTA's maintenance personnel. The same is true with the Transportation Building. This facility has been designed to provide a pleasant and inviting working environment as well as a productive and efficient space for the MBTA Operations personnel to execute their daily operations.

Approach to Meeting the Architectural Requirements

The architectural elements of the VMF are designed to be compatible with the existing Green Line No. 7 and 8 cars that feature high-level seating, with much of the equipment being mounted below floor as well as the newer Type 9 cars that feature low-level floors and most of the vehicle equipment maintenance will focus on the rooftop of the vehicles. Shop pits are designed to accommodate maintenance functions while also addressing the need for maintenance of roof-mounted equipment. Heavy equipment will need to be removed from beneath the vehicle on all vehicle types by in-floor rotating lifts. Adequate access for forklifts to the vehicle sides at pit level has been provided.

There are three standard considerations that must be accounted for when designing shop facilities: ergonomics and safety, durability and maintainability. Materials should be selected that match the operator's existing facilities to simplify maintenance and new materials should be considered if those materials can demonstrate significant improvements in life-cycle cost.

When considering the maintenance and repair of rail vehicles, a facility must allow for efficient work flow and minimize day-to-day service and operations disruptions. Consumable and spare part housing should be located close to where they will be used or installed. The proper tools should be located at or near that location as well. For example, if an overhead crane is needed to replace roof-mounted HVAC unit, that crane can access the HVAC nearby storage area much more quickly than a storage area that is far away.

Similar considerations must be given to undercar components. Maintenance and service of the equipment require pit access from underneath or the side of the car and the replacement of these larger components and is more easily performed on a flat surface with track and body hoists, portable lift tables, and forklifts.

Life Safety Codes and Relevant Applicable Standards, Addressing Workplace Safety. Life and work place safety considerations are paramount when designing industrial facilities like the VMF. The design has considered the DC traction power electrification system that will require increased safety measures from operations personnel. Employees will be working on the top, underneath and all around LRVs while near adjacent tracks where LRVs are entering and exiting the building. Fork lift safety and awareness is also important due to the movement of parts and materials throughout the building. Fail safe measures and countermeasures will be required to make certain the traction power system is denergized when an LRV is being worked on and vice versa when the system is reenergized. This will be accomplished through interlocking, visual, audible devices, and strategically-placed signage.

At the outset, GLX Constructors will meet with the MBTA to validate the VMF space program and confirm a full understanding of the how the MBTA envisions the VMF's operation and function. This alignment will set the Standard Operating Procedures (SOP) for the facility. The SOP's as our baseline, we will evaluate the facility as a whole for life and work place safety. We will drill down to activities in the individual shop areas and how they will interface with their adjacencies and employee safety measures. This SOP alignment process will also be employed for the Transportation Building.

Control of stray current will be handled and addressed as another important component considered as it relates to workers safety in the VMF and yard areas surrounding the Transportation Building.

Other considerations for life and work place safety include but are not limited to:

- **Appropriate Separation of Work Tasks.** Good design creates both geometric separation and, in many cases, physical separation between the numerous workplace activities. This applies to the obvious separation of office and administrative staff from maintenance operations, but also to the separation of technicians doing bench work on electronics and other small assemblies. Proper design separates these activities either by distance, acoustic treatments, or both.
- **Adequate Sight Lines.** Designs will focus on increasing sight lines to promote worker awareness of other activities in their area and adjacent areas. The greater the sight lines, the more time a worker has to react to a potentially hazardous situation.

- **Adequate Lighting.** Lighting must be designed to provide enough lighting without creating high levels of contrast or glare. Taking advantage of Somerville's climate and sun angles, the introduction of daylighting throughout the facility can support a safe work environment

- **Adequate Work Clearances.** Adequate space must be provided for safe workplace activities. Designing adequate clearances will require to planning for fall protection, if required by the MBTA. Clearances must take into account the clearance envelope required for rooftop mounted systems and their enclosures. This issue has been a major factor in the design of vehicle lifts, bridge cranes, and the OCS system along Tracks 1 and 2 of the VMF.

Sections 13.1 and 13.4 of the Technical Provisions state the codes and standards that should be used and followed in the design of the VMF and Transportation Building. These include 780CMR MA State Building Code, 521CMR Architectural Access Board, and the MBTA Guidelines & Standards and Guide to Access. Life safety codes such as NFPA 13 – fire protection and NFPA-72 fire alarm as well as applicable OSHA regulations will be considered in the design of these buildings.

Net and Gross Floor Area Summary for all VMF Facilities. The total area of the VMF is approximately 54,000 G.S.F. which is in line with the Volume 2 Project Definition Plans. We have enhanced the column grid lines to eliminate conflicts between maintenance equipment, working envelopes, accessibility, and overall flow throughout the VMF. The overall floorplate, interior rooms and the space program remains as is and depicted in the Volume 2 Project Definition Plans and outlined in Section 13.1 of the Technical Provisions. The net square footage will be established when:

- The overall program is validated with the MBTA

- An in-depth and detailed code summary and analysis has been performed to identify all occupancy uses within the building

- The details of wall assemblies, such as required for fire separation, have been developed and established

Section 13.4 of the Technical Provisions calls for the Transportation Building to be approximately1,425 square feet. The overall floorplate, interior rooms, and the space program remains as depicted in the Volume 2 Project Definition Plans.

An Architectural Design Description of All Buildings within the VMF Site. There are two buildings within the VMF site perimeter and boundaries, the VMF itself and the Transportation Building.

- **Transportation Building.** The Transportation Building is a one-story building approximately 24'x 60'. The exterior wall assemblies and roof assemblies will be specified to meet all applicable energy codes and the requirements and criteria set forth under Volume 2 Technical Provisions, Section 13.4 including passing NFPA 285. The building will also have interior partitions/walls as shown on the Volume 2 Project Definition Plans, Exhibit 2B; Dwg. TSP-A-1000 along with two sets of ramps and stairs, one set on either side of the building. The length of the ramps and rise/runs will be based on the height of the finished floor above finished grade. Our proposed design intends to support the building on a series of spread footings and raised pedestals foundations to avoid having the building floor system be in contact with the ground. Otherwise a gas vapor barrier system will have to be employed beneath the concrete floor slab based on the environmental Activities Use Limitations (AUL) currently in place in this area of the VMF site.

- **Vehicle Maintenance Facility.** The VMF is a one story building approximately 162'x 333' which matches the overall dimensions as shown on the Volume 2 Project Definition Plans, Exhibit 2B; Dwg. MAF-A-1100. The architectural and structural floor plans, framing plans, Exterior Building elevations, Building cross sections and typical wall sections are included at the end of this section. These plans/drawings are based on these dimensions and in accordance with the space program requirements and room criteria requirements and criteria set forth under Volume 2 Technical Provisions, Sections 13.1, 13.2 and 13.3. We believe the drawings best describe the overall architectural description for this buildings, however, some key architectural items include but are not limited to the following:

  - Exterior wall assemblies of the typical wall sections will pass NFPA 285.

  - The various roof heights were set based on the space program set forth in Section 13.1. Note the highest roof level is governed by the 10-ton bridge crane servicing the area over Tracks 3 and 4.

Narrative Describing How the VMF will Accommodate Specific MBTA Requirements. GLX Constructors will meet with the MBTA to confirm a full understanding of the maintenance program and requirements. Based on this alignment, we will configure the shop to reliably perform these functions and fully support MBTA's daily car count requirement.

Narrative Describing the Quality of Physical Working Environment. We will design the VMF to provide a safe and functional working environment. Travel paths for vehicles, materials, and workers will be carefully planned and laid out with appropriate floor striping. Proper signage in strategic locations and key decisions points will provide clear and safe travel pathways through work zones.

Clear lines of sight, aisle widths, and clearances will be provided in conjunction with code-required egress. These safety features will also apply to the exterior building.

We will ergonomically design the VMF to be easily maintained, which will allow maintenance and cleaning staff to safely perform their work. Materials and finishes selected for walls and floors will be durable, slip resistant, and easily

cleaned. In addition, material surfaces will minimize reflection to reduce glare. Light fixtures and lamps will not alter color rendition and lighting intensity will be designated to match the specific function of the space.

Integration of Key Systems. The overhead door system at each end of the VMF for tracks will operate and be interfaced with the OCS to insure a smooth transitioning of the LRVs from the yard into and out of the building.

A detailed description of how GLX Constructors envisions the OSC system will need to integrate, interface, interlock, and operate in unison with, on its own, and with other systems is provided further on in this Section.

Integration of Structures. The VMF's structure maximizes function and productivity in two ways:

1. We have deleted the longitudinal column line between Tracks 1 and 2 to optimize the inspection area work space for equipment and personnel.

2. Three lateral columns lines have been deleted and remaining column lines repositioned to optimize transverse movements of personnel and equipment through the building. This provided substantial space improvement between Tracks 3 and 4 and the maintenance and storage areas.

Integration of Equipment. Integration of equipment related to building support systems and maintenance equipment have been considered. Structural support of large roof top HVAC will be provided to utilize the superstructure of the building while optimizing the distribution of ductwork. The ductwork will be routed to avoid moving bridge cranes and the OCS system. Ductwork will be routed vertically down to the pit levels where it will not be damaged by moving equipment or encroach on personnel work spaces.

Large pieces of maintenance equipment such as the vehicle lifts, bridge cranes, and truck washing equipment will be procured early in the Project to set pit dimensions, access points, and working envelopes. This will enable our team to the foundation design and make any necessary adjustments to building heights.

Integration of Materials. Isolation of dissimilar materials and separation of various systems will be is as important as compatibility of materials because of the DC traction power in the building. Stray current considerations within the building for architectural and structural components will be incorporated as a passive or induction system or both. Special coating might also be required in some instances to combat and restrain stray current. A continuous nonconductive (i.e. fiber glass panel system) will need to be placed between the OCS wires over Tracks 1 and 2 and the underside of the building's steel superstructure framing and roof assembly to insure any arcing does not migrate to the aforementioned building components. Paints, sealants, and coating systems will be compatible with materials they are being applied to and also the environment they will perform in. GLX Constructors will plan and design the materials in compliance with the criteria set forth in the RFP.

A Discussion of How Accessibility will be addressed at the VMF.
Specific codes will play an important roles in establishing accessibility inside and outside the building, including the following:

- 521 CMR
- OSHA regulations, such as OSHA Section 1910 which concerns ladders, stairs and passageways in and around equipment and pit access.



MBTA Orient Heights Blue Line Car House. A similar door system will be used at the VMF to accommodate the OCS.

Fully addressing accessibility requires a detailed Code Summary review for the entire building. The Code Summary review will set the building's occupancy use and lead to identifying path of travel limitations, routing, egress points, fire separation, fire protection coverage, and many other potential requirements.

Our understanding of the work that will be taking place in the VMF and Transportation building, our past experience, and the previous work performed by the MBTA has allowed us to reason that building occupancy use for the VMF will likely be categorized as B, S-1, (possibility S-2) and the previously identified F-1 use groups, whereas, the Transportation Building will likely be B-use group category only.

A detailed Code Summary analysis and review will be one of the first tasks performed in the early stages of design. Once complete, GLX Constructors will arrange a meeting with the local Building Inspector to review our Code Summary and make certain we are aligned with the Inspector requirements.

Roadway access to and from the site and around the buildings themselves will be important for personnel, service vendors, and fire department. Emergency access will be reviewed with the City of Somerville Fire Department early on in the design process.

Approach to Achieving Durability. Our approach to achieving durability includes:

- **Maintainability.** Our Lead Designer has produced designs that require less maintenance because they are functionally adaptable and constructed from materials that are appropriate for their application. This is evident in the recently completed renovation design of the MBTA Orange Line Carhouse, which included a combination of precast concrete panels and metal wall panel system for the exterior building wall envelope.
- **Design for Natural and Industrial Environmental Conditions.** Materials will be specified that are suitable in the industrial environment for both the VMF and Transportation buildings. We recognize how the natural environment affects materials and their sustainability over significant life cycle periods. Materials will be specified for zero maintenance whenever possible.

- **Select Materials for Durability.** Our design will select materials that minimize maintenance over their life cycle while meeting performance criteria.
- **Abuse and Stain Resistant Materials in Heavy-Use Areas.** We will incorporate materials that can withstand abuse and maintain the intended finish. Materials will be chosen to be compatible with the broad range of lubricants, solvents, and heavy wash use in areas such as loading docks, truck wash, and other areas where abusive environmental conditions are prevalent.

Description of the Noise and Vibration Impact Mitigation. Noise and vibration generating equipment such as air compressors, pumps, and vehicle lifts will be acoustically isolated from office spaces in the building. The HVAC mechanical equipment will be located away from office spaces and vibration isolated. To reduce vibration transmission from HVAC units, vibration-isolation systems will be incorporated. Interior partitions, such as walls, floors, and ceilings, will be designed to reduce the transmission of noise to other parts of the building. The noise reducing partitions will meet an STC class of 45 or greater.

GLX Constructors will address exterior noise and vibration with the VMF and yard design to be compliant with the mitigation requirements of the Project. Noise and vibration sources at the facility will include:

- Noise from the maintenance facility building
- Auxiliary equipment from GLX cars idling in the yard
- Car movements entering and leaving the yard
- Potential wheel squeal from tight radius curves in the yard
- Impact noise and vibration from special track work and turnouts in the yard
- Noise from the maintenance facility parking lot

The contributions from these sources will be combined with the projected levels from Green Line operations to project total future noise and vibration at nearby sensitive locations. Noise mitigation will be provided for moderate noise impacts when the existing day-night average noise levels (Ldn) exceed 65 dBA (exterior). We will mitigate noise for impacts with no significant outdoor land use if the interior Ldn is above 45 dBA from GLX Project sources, or if single-event maximum noise levels (Lmax) are projected to be above 65 dBA (interior). Noise impact and mitigation locations will be confirmed during final design.

Ground-borne vibration from Green Line trains will be below the applicable impact criteria. Vibration mitigation will be included where necessary to meet the project vibration criteria.

Light Trespass Mitigation Techniques. All fixtures located on the property will be dark-skies compliant – full cutoff fixtures that limit the intensity of light in the 80 to 90 degree region of the fixture. In addition, shielding will be used where light spill to adjacent properties is of particular concern.

Architectural Drawings

Architectural drawings for the VMF are included at the end of this section.

4.5.B MECHANICAL, ELECTRICAL, AND PLANT

GLX Constructors will select electrical and mechanical systems based on best engineering practices, MBTA requirements, code compliance, energy efficiency, ease of maintenance. GLX Constructors will use their experience on transportation maintenance facilities in selecting equipment and making design decisions while adhering to the criteria and requirements outlined under the RFP Technical Provisions and Project Definition Plans.

General Design Approach to Electrical Systems, including Redundancy and Emergency Power and Equipment Selection. GLX Constructors will work with the MBTA to define all of the required power and lighting needs, and to develop an electrical design for the VMF that allows performance of the day-to-day functions. The following systems will take into account the rugged environment of the VMF and its intended longevity.

- **Redundancy.** Redundant power feeds are not required for the VMF. The VMF will be fed from one utility feed with a generator back up (to portions of the building) and an uninterruptible power supply for life safety loads, as will the Transportation Building.
- **Emergency Power.** The VMF will have generator back-up power supplied from a natural gas 200kW generator through an automatic transfer switch. From downstream distribution equipment, back-up power will be provided to a 277/480V, 3 phase, 4 wire 200A emergency panel and a 150A, 120/208V, 3 phase, 4 wire communications panel.

We will back up life safety loads by an uninterruptible power supply (UPS) capable of providing 90 minutes of back-up power. The UPS will be fed through a manual transfer switch (MTS). The normal side of the MTS will feed from the station distribution normal power, and it will have an emergency feed connected to a quick connection on the exterior of the building to a temporary generator if needed.

General Design Approach to Provision PA, Fire Alarm Systems, Security, and Other Required System Elements. GLX Constructors will work with the MBTA to define all of the required system elements as defined below.

- **PA.** Understanding the importance of clarity and proper amplification, GLX Constructors will provide a Public Address (PA) system that uses portions of the fire alarm system speakers in accordance with NFPA 72 and the City of Somerville Fire Department's requirements. The system will provide a uniformly-distributed sound level of 12db, provide interface with the Avaya phone system for paging, and meet the requirements of the Technical Provisions.

"With the Technical Provisions requirements and the MBTA's standards as our foundation, our engineering expertise will complete a design that provides reliable power, lighting, and low voltage systems to the Vehicle Maintenance Facility.

- **Fire Alarm Systems.** The fire alarm system's addressable fire alarm control panel will be compatible with the MBTA's existing central monitoring system, including SCADA, Building Management System (BMS), and Direct Digital Control (DDC). The system will connect with the MBTA's Operations Control Center (OCC) and the City of Somerville Fire Department.

  All devices will be placed in accordance with applicable codes, and be appropriate for the space in which they are placed. The full system will be commissioned upon construction completion.

- **Security.** Our security design is based on a high definition (HD) internet protocol, (IP) closed circuit television (CCTV) system that is integrated with an Access Control System (ACS). Providing HD and IP systems will allow MBTA to throttle the resolution of the video streams to meet security needs as threat conditions change. The IP feature will provide remote capability.

  The CCTV system design will provide coverage of critical areas, such as VMF and Transportation Building entrances and exits, equipment and storage rooms with high-value contents, and the MBTA personnel work areas. The goal is to deter internal and external threats. The ACS will control and monitor access to the facility and various rooms within. The ACS can provide instant status of all doors connected to the system.

  Integrated subsystems will allow the MBTA to react effectively to emergencies.

- **Other Required Systems.** The VMF and the Transportation Building require various communications systems, including but not limited to a local area network, telephone system, and maintenance/vehicle radio systems. The team will include a Synchronous Optical Network (SONET) node into the design of the VMF and Transportation Building to establish connectivity to the MBTA's Wide Area Network (WAN).

  A fare-collection maintenance station will be located in the VMF. The requirements for this room and equipment will be closely coordinated with other disciplines to make certain enough workspace has been allocated for machine delivery and equipment maintenance.

- **Traction Power/OCS.** The VMF will require a 600-volt DC power system to move the Green Line vehicles in and out of the maintenance areas and to provide a source of auxiliary power for vehicle on-board systems during maintenance activities. Automatic control of the traction power system is required to protect personnel against electrical shock hazard while they are working in the maintenance areas. The traction power system in the VMF Building will consist of the following elements: DC switchboard, cable distribution system, overhead contact system (for tracks 1 and 2), trolley stinger (for Tracks 3-4), auxiliary house power plugs, emergency trip system, and gate interlock system.

The DC switchboard will receive 600 volt power from two 1,000 kcmil feeder cables that originate at Red Bridge Traction Power Substation through a main disconnect switch/contractor. Power received is then distributed out to the overhead contact system and the auxiliary house power plugs through feeder cubicles consisting of a manual disconnect switch and an electrical contractors. The DC switch board will be located in room separate from the main ac electric room.

The cable distribution system transmits power from the switch to both the overhead contact system and auxiliary house power plugs. Feeders to the OCS will be 500 kcmil cables in 3" FRE conduits run along the ceiling trusses. Feeders to the trolley stingers will consist of 2/0 AWG cables in 2" FRE conduit between switchboard and the overhead rail. Feeders to the auxiliary house power plugs will consist of 2/0 AWG cables in 2" FRE conduits run along the shortest route between the switchboard and the contractor boxes.

The overhead contact system consists of the overhead contact trolley wire and all associated hardware required to support the wire in place. Tracks 1-2 in the VMF will be provided with an OCS allowing vehicles to move in and out of the facility through the pantograph system. The contact wire will run approximately 16 feet over the center of track and will be provided with an insulated joint to electrically isolate each end of track within the VMF. This will allow the staff to perform maintenance on a married pair at one end of the track while simultaneously allowing the other end of the track to remain under power for movement of vehicles. Each segment of trolley wire will have its own feeder cable from the DC switchboard.

The trolley stinger will consist of an overhead rail, traveling power contractor box, and trolley bug stick which will attach to the vehicle pantograph. The trolley stinger will allow maintenance staff to move vehicles on Tracks 3 and 4 under power without the benefit of an overhead contact wire. The overhead rail will carry 600 volt dc power along the length of the building adjacent to the track. The traveling contractor box will slide along the length of the rail and will close in when power is needed. The trolley bug stick will connected to the contractor box through a hanging cable. The trolley big stick will be fused to protect personnel when attaching to the vehicle pantograph.

The auxiliary house power plugs consists of a contractor box and cord/plug assembly that will provide a source of DC power for the on-board systems when the pantograph is not connected to the overhead contact system. The cord and plug assembly allows the maintenance personnel to connect the power feeder into an on-board receptacle inside the vehicle. The contractor box allows for the maintenance personnel switch the power on and off as needed. The auxiliary house power plugs will be located on the floor adjacent to each of the four VMF tracks.

"The building fire protections systems will be designed and selected based current codes and the requirements of FM Global. We will select systems based on an area's purpose and if it is temperature-controlled. We will use a full wet fire sprinkler system, interconnected with the fire alarm system, for areas within the VMF and Transportation building. All Project areas will have readily available fire extinguishers in accordance with applicable codes.

An emergency trip system will be provided to allow maintenance personnel to remotely open power the power feeders in case of emergency or hazardous conditions. The system consists of local trip stations and a main control panel to be located in the foreman's office. Trip stations will located adjacent to each track maintenance area. The button will trip and lock out the local feeder circuit at the DC switchboard and send an alarm to the main control panel. After the condition is clear, the alarm is reset at the main panel which releases the lockout allowing the feeder circuit to be reclosed for service.

The control system for the traction power equipment will include a gate interlock system which ties the DC switchboard to the raised platform access gates. Each platform gate will be provided with lock that is held in place while the local power feeder circuit is closed preventing personnel from entering an area with live power present. The lock is released when the power source is opened allowing personnel to enter under safe conditions. Power cannot be turned back on until personnel leave the area and the gates are closed.

General Design Approach to Mechanical Systems including HVAC, Plumbing, and Drainage Systems, and Equipment Selection. The mechanical systems design will provide a safe, comfortable, and productive work environment for the activities of the maintenance staff activities.

- **HVAC.** HVAC systems will be based on ASHRAE and current codes, including the Massachusetts Energy Code. We will use Trane Air Conditioning Economics (TRACE) software to perform heating, ventilating, and cooling calculations.

All sheet metal ductwork will comply with Sheet Metal and Air Conditioning Contractors' National Association's duct construction standards.

Fire and smoke dampers will be provided in fire-rated partitions. Air registers grilles and diffusers will be selected to provide the required throw and spread, with minimal noise in occupied rooms. Intake and exhaust louvers will be storm-rated in accordance with the Air Movement and Control Association's requirements. Ventilation systems will be provided with demand control ventilation.

The VMF's heating and ventilation systems will include gas fired rooftop units, indoor radiant heaters, and unit heaters.

The rooftop units will provide 100% outdoor air supply into the maintenance facility through drum louver diffusers mounted up high, which discharge downward at an adjustable angle to reach the finished floor. We will extract exhaust airflow through low-exhaust registers in maintenance pits and along column lines and in high-duct mounted exhaust registers. The heating and ventilating units serving the shop areas will utilize high efficiency gas burners, energy recovery from leaving exhaust air, and variable frequency drives for variable airflow capacity.

The fan speeds of the variable capacity heating and ventilating units will automatically modulate in response to variations in carbon dioxide gas concentrations. If carbon monoxide gas concentration rises above 25 parts per million, the carbon monoxide gas detection monitoring and control systems will operate to automatically index the associated zones' ventilation system to the high-speed, 100% outside air mode of operation, in accordance with OSHA and NIOSH standards for time-weighted average exposure limits.

In addition to the rooftop equipment, gas fired radiant heaters will be provided over maintenance pit areas to heat the area around the tracks for occupant comfort. Areas with clearance constraints for installing radiant heat will be provided with gas fired unit heaters. This heating capacity will be for the non-ventilation building losses and will handle the demand of the building during unoccupied hours when the ventilation system is turned off.

- **Plumbing and Drainage.** We will design the VMF's plumbing systems in accordance with 248 CMR, which includes selecting products from the approved-products list that meet the EPA's WaterSense criteria. We will incorporate proper backflow prevention for all domestic and industrial water systems.

Domestic hot water heating will be designed in accordance with American Society of Heating, Refrigerating, and Air-Conditioning Engineers (ASHRAE) requirements. Before use, we will commission the domestic hot water heating system.

Insulation will conform to the Massachusetts Energy Code. Sanitary wastes will be collected separate from industrial wastes. Industrial wastes will flow through an approved oil water separator before discharging to the sanitary waste system. Clear condensate wastes will direct to the storm water system. Leak detection alarms will route to the automated control system and the MBTA's Operations Control Center.

Storm drainage systems for buildings and canopies will conform to 248 CMR. Compressed air systems will be designed in accordance with the American Society of Plumbing Engineers (ASPE) manual.

- **Equipment Selection.** Mechanical and plumbing equipment will meet the needs of the Project, and applicable code requirements. Designers will evaluate each space or system and select equipment based on the demands and intent of the design. Experience on past projects, maintenance considerations, and manufacturer recommendations will all be used in evaluating equipment for the design.

Main Mechanical Equipment Schedules. As shown in Drawing VMF-014 at the end of this section, the HVAC equipment consists of heating and ventilating air handlers with energy recovery, gas fired unit heaters, exhaust fans, and variable refrigerant flow split systems, electric baseboard heat, and infrared heaters.

The plumbing equipment consists of the following:

- Two gas fired hot water heaters that serve the building
- Emergency eye wash/shower fixtures throughout the building
- An air compressor, air receiver, and dryer located in Compressor Room 114 on the northwest side of the building
- Kitchen sink located in both break rooms
- Mop sink located in each janitor's closet
- Shower and two lavatories in each locker room
- Drinking fountain just outside the locker rooms

Building Automated Control System. An automated control system will operate and manage the mechanical systems, including heating, ventilating, air conditioning, lighting controllers, domestic hot water, drainage alarms, and air compressor equipment. The system will meet ASHRAE 135 standards for BACnet, an open-source protocol for Building Automation and Control Networks.

The mechanical HVAC equipment will have zone sensors and thermostats in the maintenance areas to control the ventilation system and supplemental heaters. Local thermostats will control systems in staff and support spaces. These systems and equipment will connect to the BMS for monitoring and control by the MBTA.

The BMS system will connect to the SCADA/Programmable Logic Controller system to report all alarms and monitored points to the MBTA Operations Control Center. This will allows real-time alerts for high or low temperatures, equipment status, water leak detection, and other alarms.

Proposed Electrical Utility Service Supply Point. We will work directly with the utility company to develop an efficient use of space that meets their requirements while minimizing impacts to the VMF. Per the RFP the Transportation Building electrical service is being fed from the VMF. Please refer to Drawings VMF-002 and VMF-003 at the end of this section.

Electrical Drawings

Electrical Site Layout Showing Location of Incoming Electrical Services, Switchgear, and Duct Banks to Each Building, Substation, and Traction Power Substation. We have engineered an efficient and cost effective utility co transformer location. The location shown on the civil site and utility plan attempts to minimize the length of secondary conduits between the utility transformer and main electric room in the NE corner of the VMF. In addition, all site conduit and duct bank runs take the most direct path and route to their intended location to minimize voltage drop and feeder lengths. Please reference drawings VMF-002 and VMF-003 at the end of this section.

> **GLX Constructors Team Member, Middlesex, regularly performs work for local utilities that has included major projects for Eversource. Our team is equipped with the knowledge to quickly negotiate, design, and build to Eversource requirements.**

Single Line Diagram, Preliminary Sizing of Equipment and Feeders. Our Team's expertise with previous maintenance facility projects, including our recent involvement with the design of the MBTA Orange Line Wellington Car House renovations has allowed us to apply historical data to assist in establishing the properly-sized electric service for the VMF. From historical billing data and the existing main switchgear size at the Wellington Carhouse, our team has projected that a maintenance facility of this size and type will require approximately 17 Watts/s.f. which equates to a service size of 2000A at 480V, 3 phase, and 4 wire. This assumption has been bolstered by our development of the baseline one-line schematic diagram of the main electrical power distribution system, based on the aforementioned wattage/square foot criteria and load requirements for the major maintenance equipment for the VMF.

Please reference drawings VMF-010 at the end of this section and the expected electrical demand calculations below.

Location Points for Tie-in to Local Electrical Utility. Please reference drawings VMF-002 and VMF-003 at the end of this section.

Riser Diagrams for Fire Alarms and Miscellaneous Systems. Fire Alarm system devices shown in the one line Fire Alarm system schematic diagram drawing have been located in accordance with code requirements. The main fire alarm control panels within the VMF have been centrally located. Digital annunciators have been shown and their locations will be confirmed by the team during design. For riser diagrams for fire alarms and miscellaneous systems, please refer to Drawing VMF-011 at the end of this section.

Mechanical Drawings to Indicate Design Intent of All Building Services Mechanical Systems

HVAC. The VMF mechanical systems design is focused around the Service Floor Area. The heating and ventilating is accomplished by eight roof-mounted air handling units. Refer to drawing VMF-013 for the roof plan of these equipment and drawing VMF-012 for the interior ductwork from these units.

COMMERCIAL SERVICE LOAD CALCULATION

STV 100 Years
One Financial, Third Floor
Boston, MA
617 482 7298
www.stvinc.com

Job Description: Vehicle Maintenance Facility - GLX
Calc By: SO
Calc Check By: CM

220.42	General Lighting				
	Table 220.12 Load by occupancy	2	VA/sqft		
	Floor Area=	53280	sqft	106560	VA
	Total=	53280	sqft		
220.42	Lighting Load Feeder Demand Factors				
	If not Dwelling, Hospitals, Hotels Warehouse then 100%			106560	VA
	Total Lighting Demand Load=			106560	VA
220.44	Receptacle Loads - Other than Dwelling Units				
	1W/sqft	53280	sqft	53280	VA
220.44	Demand Factors for Non-Dwelling Receptacle Loads (Table 220.44)				
	First 10kVA at 100%			10000	VA
	Over 10kVA at 50%			21640	
	Total Receptacle Demand Load=			31640	VA
220.51	Largest of Fixed electric Space Heating or A/C load:				
220.60	Non-Coincident Loads				
	Heating		A/C		
	417000 VA		157000 VA	417,000	Heating Load
			0 VA	157,000	A/C Load
				417,000	VA
	Transportation Building			265,920	VA
	Motor Loads				

220.5 Qty	Description	VA(W)
6	Exhaust Fan	69810
2	Car Hoists	332400
1	Wheel Truing	99720

Qty	Description	VA(W)
1	Parts Lift	39888
1	Truck Hoist	39888
1	10 Ton Crane	39888
1	7.5 Ton Crane	26592

Total Motor Load= 648,186 VA

Total Calculated Demand Load in Volt-Amperes= 1,469,306 VA
Total Calculated Demand Load in Amperes= 1,769.40 A at Service Voltage: 480 VA
(No demand was taken for Motor Loads) Phase: 3
SERVICE REQUESTED= 2000 A
* select higher load and mult by voltage

Figure 4.5-1. Commercial Service Load Calculation.



Figure 4.5-2. Roof-Mounted Air Handling Unit. *Example.*

The supply of heating and ventilation air down to the floors is accomplished with drum louver diffusers mounted high, discharging downward at an adjustable angle to reach finished floor.

Summer ventilation of the shop area is accomplished with six rooftop exhaust fans and is designed to draw additional air through the overhead doors.

The staff support spaces connected to the shop area are all designed to consider the airflow between spaces. Heating and cooling is accomplished with variable refrigerant flow systems. Ducted split systems are located above the ceiling of all occupied spaces. Ventilation air is provided to each split system by a dedicated energy recovery device with fixed plate heat exchanger, which will exchange energy from the locker room exhaust air to pretreat incoming ventilation air. Supplemental heat is provided by electric baseboard in the event the system experiences winter issues due to ice buildup or below zero temperatures.

The storage rooms are designed with dedicated air handing units to both heat and ventilate the space. Wall mounted louvers and inline exhaust fans will provide summer ventilation.

A similar type system will also be employed for the HVAC system for the Transportation Building.

Fire Protection. To confirm existing water pressure in the vicinity of the VMF site, our team performed a hydrant flow test to form the basis of our hydraulic calculations. This determined a fire pump was not required for the VMF. This allowed the fire protection main double check valve and alarms as well as the main domestic water service backflow preventer to be housed in the allocated square footage in the Fire Protection Rm No. 118 called out in the Volume No. 2 Project Definition plans.

A wet fire sprinkler system with two zones will be provided, one zone for the East side of the building, the other for the West side. The fire sprinkler system was designed in accordance with NFPA 13.

The hydraulic calculations, based on the hydrant flow test, indicate that a 10" fire sprinkler pipe to the building, with two 8" fire sprinkler risers with alarm assemblies is sufficient to provide fire protection to comply with NFPA 13.

A wet-type fire protection system will also be provided for the Transportation Building.

Plumbing. Natural gas, sanitary waste, industrial waste, domestic cold water, domestic hot water, and compressed air systems have been sized for the VMF building. Gas, sanitary water, domestic cold, and hot water system will also be provided for the Transportation Building in accordance with 248 CMR and the International Plumbing Code.

Drainage. The storm drainage system is sized in accordance with 248 CMR and the International Plumbing Code. Roof drains have been identified at all low points which are shown on Drawing No. VMF-005. Double roof drains are provided to comply with applicable codes for overflow protection. Roof storm drainage is collected inside the building via a network of piping which exit the VMF building at three separate locations shown on Drawing No. VMF-002 which in turn discharge to the underground storm water piping. The roof drainage system for the Transportation Building will be collected via a system of gutters and down spouts which will be collected and discharged to underground storm water piping. Refer to Drawing No. VMF-003.

4.5.C INDUSTRIAL PROCESS AT VEHICLE MAINTENANCE FACILITY

The VMF design will accommodate daily inspections and interior cleaning demands required for 43 LRVs, while facilitating light servicing, inspection, and maintenance tasks. The run-through track configuration will accommodate varying work-flow configurations.

Design Approach Using Narrative and Design Drawings, Demonstrating How GLX Constructor's VMF Design Conform to Requirements

Description of the Functional Design Concept Proposed for the VMF. The VMF is designed with four run-through tracks, each capable of accommodating two pairs of vehicles and allowing 16 total vehicles to be housed at once. Tracks 1 and 2 have pit/pedestal track configurations, and they are equipped with overhead DC power systems that will allow the vehicles to enter and exit the shop using their own power. This configuration will facilitate:

- Easy vehicle movements for inspection and maintenance tasks
- Access beneath the vehicles to perform inspection of the brake discs
- Fluid change-outs

We have configured Track 3 with a flat floor maintenance/inspection position for two vehicles on half of the track. A flat floor with a wheel truing machine pit for wheel re-profiling composes the other two vehicle maintenance positions.

We have provided Track 4 with car hoist equipment at the north and south ends of the shop that accommodates lifting one vehicle at each half of the shop. This facilitates change-out of the trucks. The car hoist position at the north end of the shop is equipped with perpendicular shop rails that allow easy transfer of trucks from the lifting position into the truck repair shop.

There will not be an overhead DC power system along Tracks 3 and 4 so that the area can be served by a 10-ton bridge crane to handle trucks and roof-mounted equipment. The VMF will have space provided to accommodate rolling platforms. The platforms have not been included in our proposal per the Technical Provisions.

A 7.5 Bridge crane in the loading dock area will accommodate supply deliveries that cannot be transported via forklift to various shops and storage areas throughout the VMF. The bridge crane also picks wheel sets and truck assemblies from Track 4 and transports them to the truck shop and wash area.

Interface of the VMF with the Main Line. Efficient entry and exit from the new Inner Beltway yard is critical due to the yard being the terminus point for two light rail branch lines. The mainline interface must support the requirement that D-Line service run at a five-minute headway and the E-Line service run at a six-minute headway.



Figure 4.5-3. Rendering of service pit areas in the VMF.

Although yard switches will be hand thrown, we will accomplish main line interfaces from the yard leads by activating push button boxes, which have proven to be a safer, more reliable design than routing onto the main line via AVI-activated switches.

Because switches are interlocked with the signal system, Operators' push button requests will not activate switches if the signal system determines the routing is not safe. For an additional layer of safety, we will install switch heaters at switches that control access from the main line to the yard leads.

Storage on the yard leads at strategic junctures will allow for immediate insertion into revenue service of 'hot spares' should a train become disabled or should the Operation Controls Center (OCC) or field supervision call for extra service.

Storage of the Revenue Vehicles. The yard will have the capacity to safely store 43 vehicles and will support the ability to populate the D Line with 42 cars and the E Line with 34 cars in an efficient manner, requiring less dead heading and inefficient run cuts emanating from the Riverside Yard. Yard illumination will meet the MBTA's lighting standard requirements for ambient foot candles.

Paved walkways, painted with non-slip coating, help prevent slips, trips, and falls. Distinct clearance lines provide critical information to Operators and Yard Shifters regarding appropriate stopping/parking locations to avoid potential accidents. Probing antennas can easily examine stored vehicles prior to their next service run to make certain customers' latest transactions are properly captured.

Proposed Shop Equipment List for the VMF. We will provide over 140 pieces of equipment in the VMF as indicated by the following list of equipment types, identifiers, and quantities.

Equipment ID #	Description	Quantity
1005	PEG TOOLBOARD	6
1234	SPILL CONTAINMENT PALLET	3
1270	STORAGE RACK, 72 BIN	10
1290	OIL FILTER CRUSHER	2
1295	BULK STORAGE RACK	4
1325	PALLET RACK, 3 LEVEL	9
1330	PALLET RACK, 3 LEVEL	1
1340	PALLET RACK, 3 LEVEL	7
1345	PALLET RACK, 3 LEVEL	6
1511	SHELVING UNIT (2 STARTERS/2 ADD-ON)	4
1516	SHELVING UNIT	18
2123	TRASH COMPACTOR	1
2129	VERTICAL BALER	1
2629	VISE	14

Equipment ID #	Description	Quantity
3025	PARTS CLEANING TANK	8
3050	HIGH PRESSURE WASHER NG	1
5041	DEIONIZED WATER PORTABLE CART	2
7522 7706	AIR PISTON PUMP	2
7706	WASTE FLUIDS RECEIVER	4
7937	INTEGRAL PUMP, WASTE TANK	1
8002	PORTABLE WORK PLATFORM	8
8005	ROOF WORK PLATFORM (FUTURE)	2
8117	WORKBENCH	14
9105	10 TON BRIDGE CRANE	1
9126	7.5 TON BRIDGE CRANE	1
9307	NARROW AISLE ELECTRIC FORKLIFT	1
9400	IN-GROUND LRV HOIST	2
9443	TRUCK REPAIR HOIST	1
9705	TWO STOP PARTS LIFT	2
9815	PALLET JACK	4

Figure 4.5-4. Proposed Shop Equipment List for the VMF.

The fixed LRV Hoists (Equipment ID 9400) on Track 4 of the VMF will be high pressure hydraulic hoists. These hoists use less hydraulic fluid than typical hydraulic hoist systems, and they provide an advantage over screw jack hoists by making it possible for the lifting frame to rotate 90 degrees to align with perpendicular tracks. This simplifies the movement of trucks from beneath the vehicle into the truck shop and eliminates the need for separate turntable equipment.

There are two main storage areas within the VMF which utilize many different types of storage equipment to move anything ranging from traditional pallet racks to small parts storage bins. The storage area west of Track 1 has narrow aisles between storage racks; therefore, it requires a Narrow Aisle Electric Forklift (Equipment ID 9307) to load and unload the pallet racks. The Narrow Aisle Electric Forklift has forks that rotate 180 degrees, which allows it to operate in reduced-width aisles. The narrow aisles and high pallet storage minimize floor space and maximize the storage volume.

Narrative on the Industrial Design. We will develop an industrial design that promotes efficient performance of the maintenance functions necessary to meet daily car counts and keep the Green Line fleet in a State of Good Repair (SOGR).

A clear definition of facility requirements and function are important in developing plans for the repair shops, service and inspection areas, and ancillary facilities. We understand the objectives of this facility are to insure the reliability of the overall fleet, minimize maintenance for unscheduled repairs, and provide a system for maintaining a clean fleet. We will meet those objectives and deliver a quality industrial design by implementing the following design standards.

- Design facilities consistent with property constraints, track and yard constraints, and operational philosophies, as well as the operating maintenance practices of the MBTA.
- Design and develop buildings that will be durable, cost-effective, aesthetically pleasing, and easily maintained.
- Developing an operational work flow plan based on our industrial engineering expertise that will properly accommodate the required functions, while optimizing personnel and efficient interaction with operating equipment.
- Incorporate safe, durable, and proven service equipment.
- Design utility systems that will provide for proper drainage, water supply, lighting, ancillary power, waste disposal, and communications, which are consistent with the objectives of the facilities.
- Use proven functional design elements for each area required in the facility. For example, a design for a repair bay will be developed based on previous proven designs and current design parameters used by the MBTA.
- Create facilities that are safe, productive, warm in the wintertime, cool in the summertime, and engineered to increase productivity while eliminating accidents.
- Place of ducts, piping, and conduits to promote access and increase sight lines.
- Place controls so that the operator views are unobstructed.
- Increase ventilation rates or induce positive room pressures at locations where work operations are known to potentially diminish air quality.

Drawings of the Design Approach for the VMF

Site Plans. Drawings that demonstrate how the design for the VMF will conform to the requirements of the Volume 2, Technical Provisions, Section 10 are included at the end of this section.

Proposed Track throughout the VMF. We have developed track plans for the VMF/Car Storage Yard with the following:

- Three yard Lead Tracks
- Eleven car storage tracks
- Two ladder tracks
- A loop track around the facility

- A storage track adjacent to the VMF building
- Four VMF tracks within the building

Crossovers are provided to allow for cars to access the VMF building from any storage track. We have designed track horizontal alignments within the VMF/Car Storage Yard that follow Section 10.2 of the Technical Provisions. These alignments replicate the Definition Plan's horizontal alignments except for the loop track to improve the grading at Third Avenue entrance.

GLX Constructors has designed track vertical profiles within the VMF/Car Storage Yard that follow Section 10.2 of the Technical Provisions.

Track Construction Details, Diagrammatic Representation, and Proposed Limits for Each Track Type. Please reference proposed track drawings at the end of Section 4.6 of this document.

4.5.D BUILDING STRUCTURES AT THE VEHICLE MAINTENANCE FACILITY

Approach to Demonstrating How the Design for the VMF, Stations, Underpasses, and Associated Facilities Conform to Structural Requirements

Design Criteria and References to the Applicable Standards. The VMF's structural design will conform to the specific requirements as identified in the Technical We understand that the order of precedence of these requirements will be those specifically identified in the Technical Provisions, followed by the codes and standards in Section 13.2.2 in the order listed.

Design or Specification Measures to Meet Serviceability Criteria. We will use a combination of construction, expansion, and contraction joints in the design of all concrete structures to control the effect of expansion and shrinkage associated with concrete curing. These measures, along with control joints, will mitigate the extent of any potential shrinkage cracking.

Description of the Structural Elements, Including, Support of Excavation, Foundation, Floor, Roof, Framing System, and Lateral Load Resisting System. The foundation system will be a combination of pile caps and grade beams. Piles are located under pile caps at each building column. These pile caps are connected by a series of grade beams, which will support the floor slabs and transfer tributary loads to the piles. Some piles will support the slab under Tracks 3 and 4 and the associated pits for lifts and wheel truing.

The floor slabs will be structural slabs supported by the grade beam system. The only exception will be the slabs in the area of Tracks 3 and 4, which, as noted earlier, will be directly supported by piles.

The building superstructure will be a steel frame structure comprising rolled shape columns supporting two bridge cranes and the roof structure. The roof framing system will be composed of joist members for the transverse girders and longitudinal purlins.

Moment connections between the joist girders and the columns will provide for the lateral load resisting system. Longitudinal load resistance will be provided by bracing in one or more bays in each of the exterior longitudinal column lines.

We do not anticipate excavation support for constructing the VMF foundation system. Based on the area's geotechnical information, the groundwater table is high (3 to 5-feet below existing grade) and dewatering may be required at the deep pits on Track 3 and 4.

Narrative of the Waterproofing System, Type, and Application. The waterproofing system will be a fluid applied membrane waterproofing system, consisting of a membrane adhered to the vertical surface of the pits with an adhesive. When necessary, a mud slab will be poured after the piles are driven to provide a smooth and level surface for the waterproofing membrane. To secure a watertight system, we will provide a proper length of lap joints where the horizontal and vertical sections of the membrane intersect.

Design to Mitigate Frost Heave. To mitigate frost heave, we will place the top of pile caps, also the bearing surface for the grade beams, at least 4-feet below grade.

Confirmation That All Structures Can Be Constructed within the Project ROW, including Consideration for Any Temporary Structures and Shoring That May Be Required. GLX Constructors has carefully reviewed the required work and compared this effort against the documents provided by the MBTA with the RFP. In all cases, we do not anticipate that temporary shoring or temporary structures will be required to construct the VMF and Transportation Buildings, trackwork, retaining walls, utilities, or any other site related work or project elements.

Representative Structural Drawings

Drawings requested for the following sections are included at the end of this section.

Support of Excavation Systems. The design of the VMF only requires excavation to construct the depressed and pit portions of the floor, pile caps, grade beams and utilities. Open cut excavations will be used to construct these portions of the facility. No excavation support systems are currently anticipated.

Foundations, Floor, Roof, and Structural Framing Systems, including Materials and Spans. The foundations for the VMF will consist of 14-inch square, 100-ton precast prestressed concrete (PPC) that will transfer the structural loads from the building structure and ground floor slab through the existing unsuitable fill and underlying clay layers to the underlying glacial till and weathered bedrock/bedrock.

Please reference the foundation, floor, roof, and framing plans at the end of this section.

Column Spacing and Layout. Column spacing and layout are provided by drawing VMF-004 at the end of this section.

Drainage and Waterproofing System. The Project will reduce impervious areas and create less runoff than the current site condition. Positive drainage for the VMF will be divided in two sections. The southern section which discharges to Red Bridge Pump Station and the northern section which discharges into an existing system along tracks near the west edge of the commuter rail facility.

We will provide detention systems for both buildings such that proposed storm water runoff volume and rate does not increase. Water quality improvements will be further evaluated in design development.

Waterproofing systems will be applied to the deep pits at Tracks 3 and 4.


Demonstration That All Structures Can Be Constructed Within the Lands Including Consideration for Any Temporary Structures and Shoring That May Be Required. As depicted by the drawings at the end of this section, all structures can be constructed in the lands based on the documents provided by the MBTA with the RFP. Temporary structures or shoring are not anticipated to construct the VMF facility.

Design to Mitigate Frost Heave for Temporary and Permanent Structures. The top of the pile caps and bottom of grade beams will be constructed to be at least 4-feet below grade for frost protection.

GLX Constructors has reviewed the Volume 2 Technical Provisions and the applicable Project Definition Plans, for the VMF and Transportation Building. By virtue of past experience and anticipated alignment sessions with the MBTA we will fully understand and design the VMF and Transportation Building to effectively serve and support the Green Line Extension.

ITP Request	RFP		
	Drawing Number	Drawing Title	Reference Section or Drawing
A5.2.5.A.2.a	VMF-001	Overall Site Plan	
A5.2.5.A.2.b	VMF-002	VMF Site Plan	
A5.2.5.A.2.b	VMF-003	Transportation Building Site Plan	
A5.2.5.A.2.c	VMF-004	Floor Plan	
A5.2.5.A.2.c	VMF-005	Roof Plan	
A5.2.5.A.2.d	VMF-006	Exterior Elevations	
A5.2.5.A.2.d	VMF-007	Building Sections	
A5.2.5.A.2.d	VMF-008	Building Sections	
A5.2.5.A.2.f			4.5 (VMF-007, VMF-008)
A5.2.5.A.2.g			4.5 (VMF-007, VMF-008)
A5.2.5.A.2.h	VMF-009	Wall Sections	
A5.2.5.B.2.a			4.5 (VMF-002, VMF-003)
A5.2.5.B.2.b	VMF-010	Electrical One Line Diagram	
A5.2.5.B.2.c			4.5 (VMF-002)
A5.2.5.B.2.d	VMF-011	Electrical Fire One Line	
A5.2.5.B.3	VMF-012	Mechanical Overall Work Plan	
A5.2.5.B.3	VMF-013	Mechanical Roof Plan	
A5.2.5.B.3	VMF-014	Mechanical HVAC Equipment Schedule	
A5.2.5.B.3	VMF-015	Vehicle Maintenance Facility Plumbing and Fire Protection Floor Plan	
A5.2.5.C.1			4.5 Narrative
A5.2.5.C.2.a			4.5 (VMF-002)
A5.2.5.C.2.b			4.6 (C-050, C-051, C-052)
A5.2.5.D.2	VMF-016	Foundation Plan	
A5.2.5.D.2	VMF-017	Pit Slab Plan	
A5.2.5.D.2	VMF-018	Main Floor Slab Plan	
A5.2.5.D.2	VMF-019	Framing Plan – Column and Track Pedestals	
A5.2.5.D.2	VMF-020	Roof Framing Plan	
A5.2.5.D.2	VMF-021	Longitudinal Building Section	
A5.2.5.D.2	VMF-022	Transverse Building Section	
A5.2.5.D.2	VMF-023	3D Representation	

Technical Solutions Drawing Matrix.

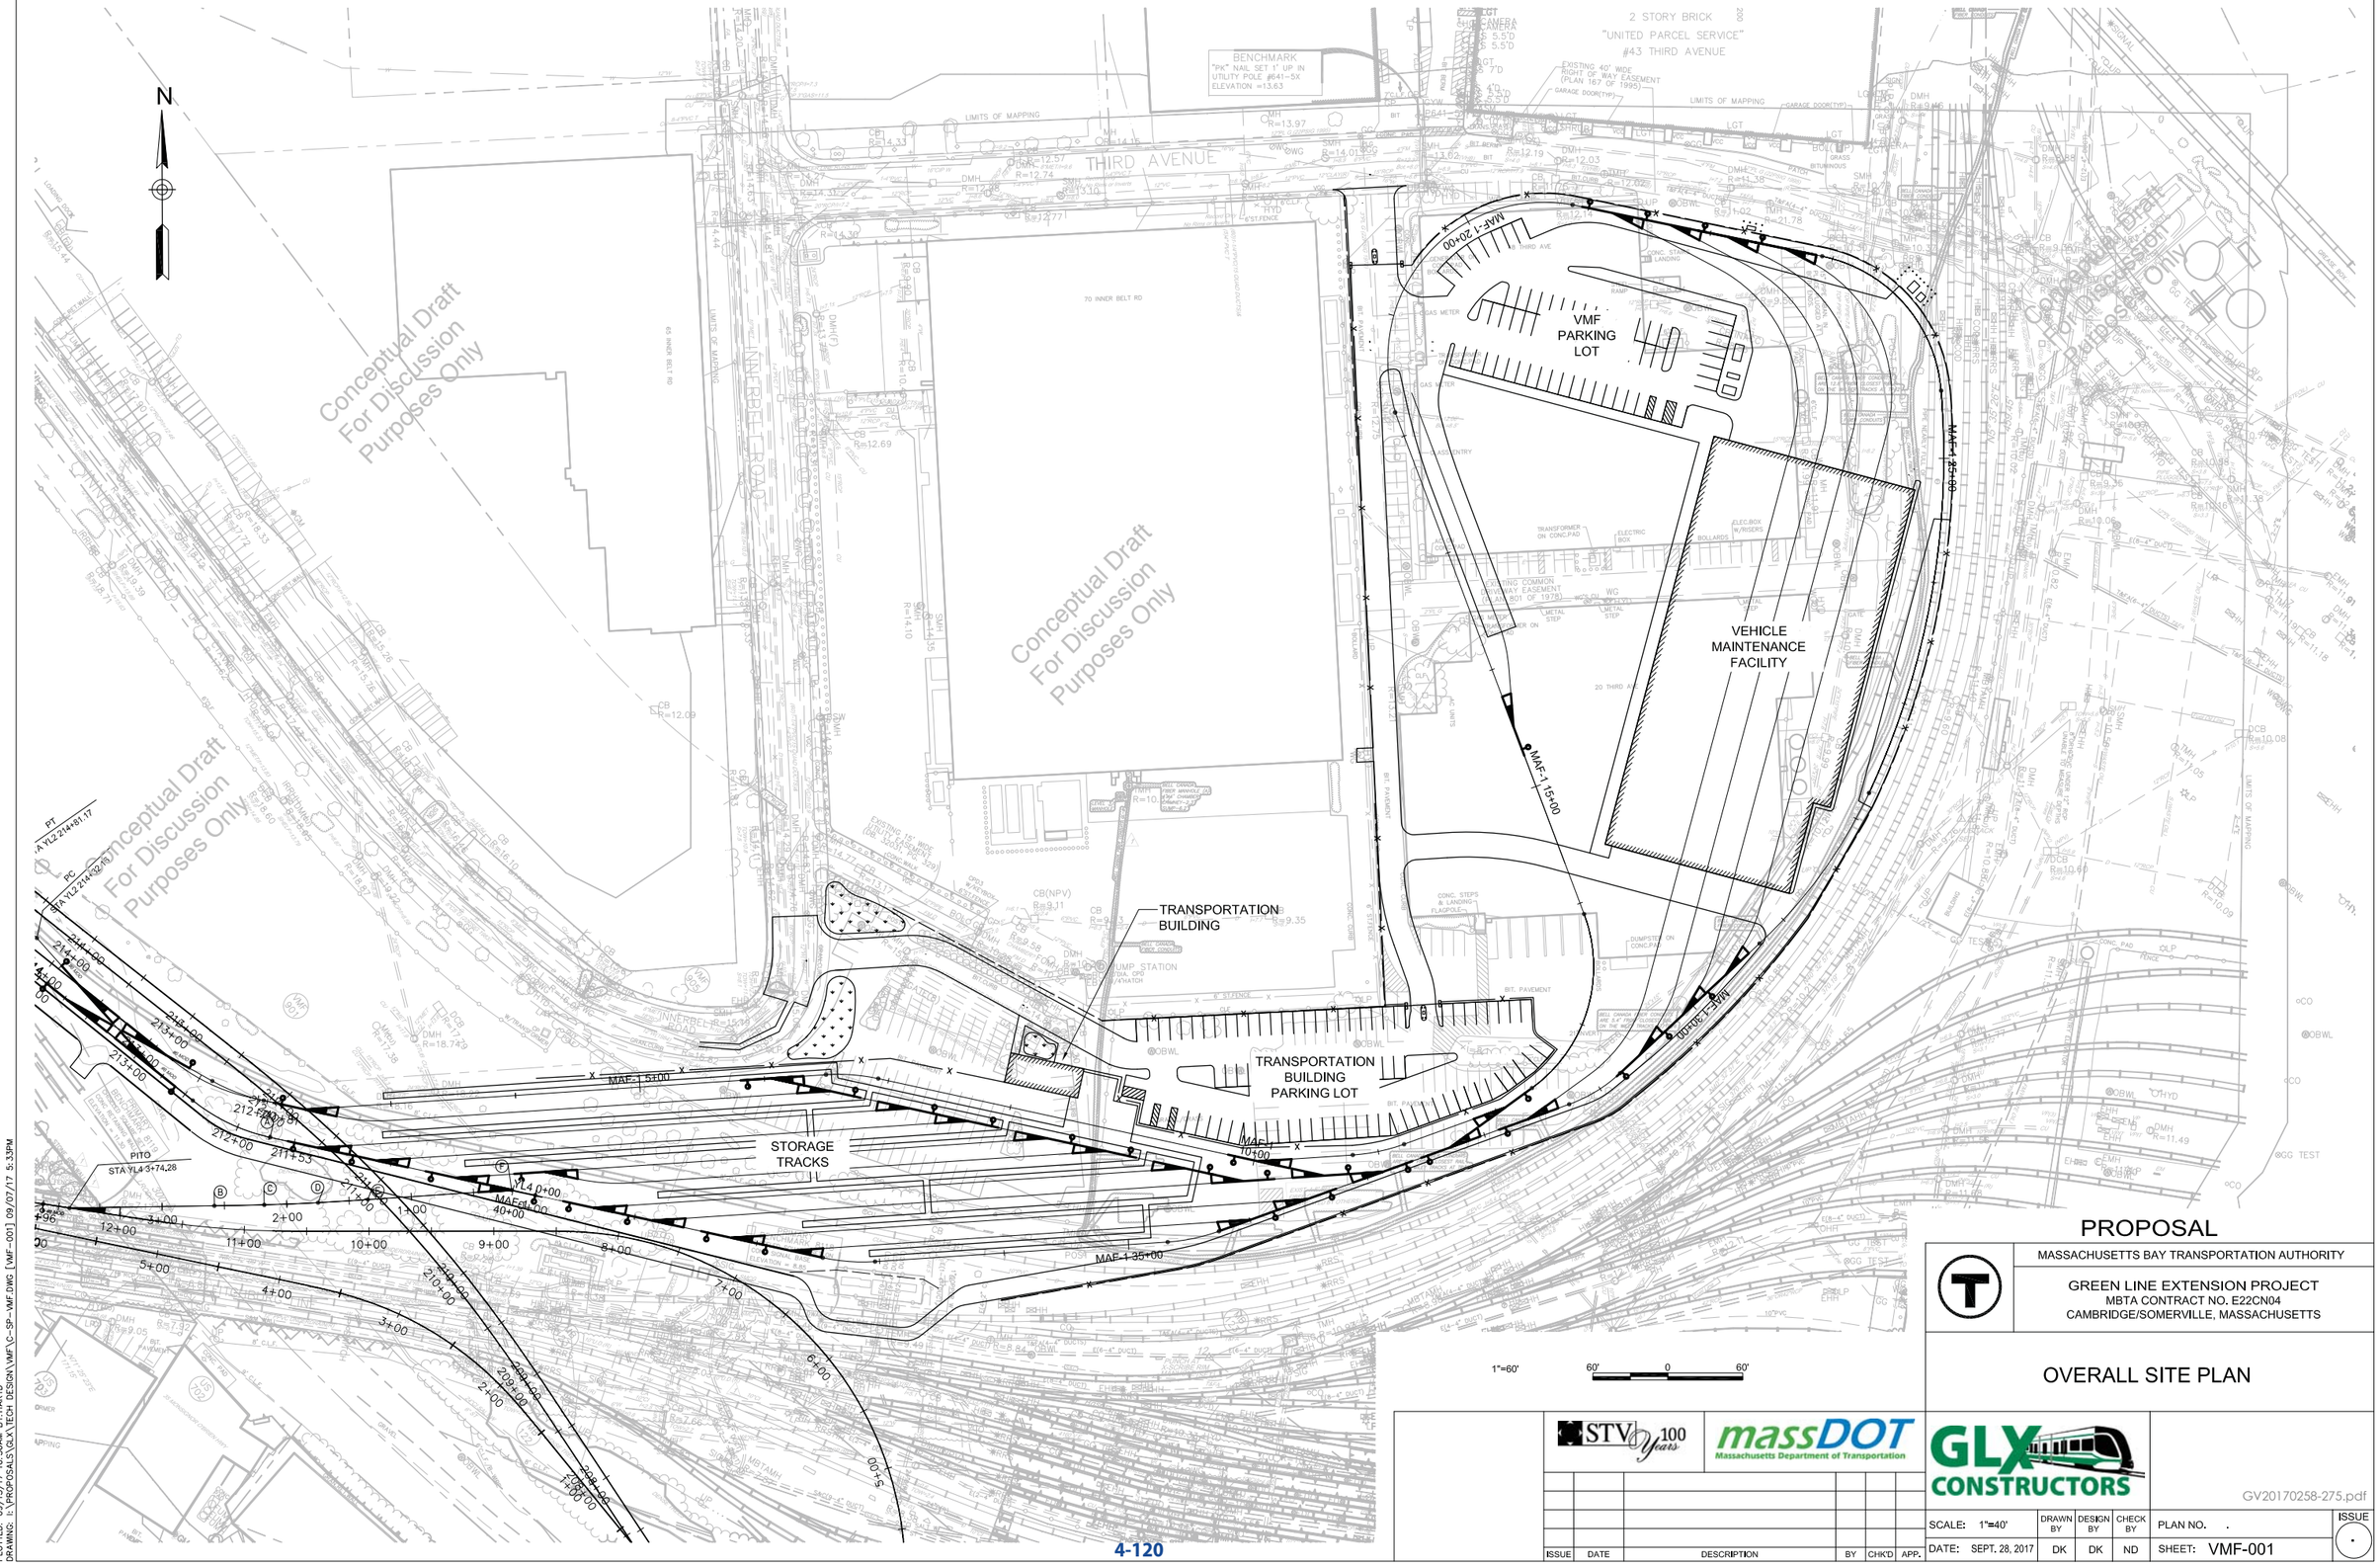

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

OVERALL SITE PLAN

1"=60'

60' 0 60'

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-275.pdf

SCALE: 1"=40'	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	DK	DK	ND	SHEET: VMF-001	.

PLOTTED: 09/13/17 10:56AM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\VMF\C-SP-VMF.DWG [VMF-001] 09/07/17 5:33PM

SUBSURFACE DETENTION CHAMBER
VMF EMPLOYEE PARKING (65 SPACES)
GAS METER
GAS FIRED EMERGENCY GENERATOR
2-5" C POWER DUCT BANK
1500 KVA TRANSFORMER
METER
GATE AND CARD READER
PERIMETER SECURITY FENCE
RETAINING WALL
TRASH COMPACTOR & BALER
2-4" C EMERGENCY POWER DUCT BANK
9-3" C POWER DUCT BANK
4-4" C TEL, FA, AND SECURITY DUCT BANK
10" FIRE PROTECTION
4" DOMESTIC WATER
DC NEGATIVE MANHOLE (5 BETWEEN VMF AND RED BRIDGE TPSS)
VEHICLE MAINTENANCE BUILDING (FF EL = 18.50)
8" GAS
6" SANITARY
OIL/WATER SEPARATOR
DC POSITIVE MANHOLE (6 BETWEEN VMF AND RED BRIDGE TPSS)
MATCHLINE - SEE DRAWING No. C-027
6-4" C POWER AND SYSTEMS DUCT BANK FROM VMF
2-5" C POSITIVE TRACTION POWER DUCT BANK & 2-5" C NEGATIVE TRACTION POWER DUCT BANK
MAF-1 20+00
MAF-1 15+00
MAF-1 25+00

Conceptual Draft For Discussion Purposes Only

NOTE:
SEE SHEET C-031 FOR LIGHTING FIXTURE SCHEDULE.

1"=40'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VMF SITE PLAN


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-275.pdf

SCALE: 1"=40'	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	DK	DK	ND	SHEET: VMF-002	.

PLOTTED: 09/13/17 11:10AM BY:HARTD
DRAWING: E:\PROPOSALS\GLX\TECH DESIGN\VMF\C-SP-VMF.DWG [VMF-002] 09/13/17 11:07AM

LUMINAIRE SCHEDULE											
LUMINAIRE MARK	DESCRIPTION	MANUFACTURER	CAT. NUMBER	DLC LISTED	LAMPS TYPE	MOUNTING	VOLTAGE	WATTAGE	DISTRIBUTION	POLE HEIGHT	ARM LENGTH
LP1	SHOEBOX LUMINAIRE	BEACON	VPS-60NB-136-3K-T2-480V	X	LED	POLE	480	136	TYPE III	30'	5'
LP2	SHOEBOX LUMINAIRE	BEACON	VPS-48NB-110-3K-T3-480V	X	LED	POLE	480	110	TYPE II	30'	5'
LP3	SHOEBOX LUMINAIRE	BEACON	VPS-60NB-137-3K-T3-480V	X	LED	POLE	480	136	TYPE III	30'	5'
LP4	SHOEBOX LUMINAIRE	BEACON	VP-L-64NB-135-3K-T3-480V	X	LED	POLE	480	135	TYPE III	35'	0'
LP5	SHOEBOX LUMINAIRE	BEACON	VP-L-64NB-135-3K-T3-480V	X	LED	POLE	480	135	TYPE III	35'	14'

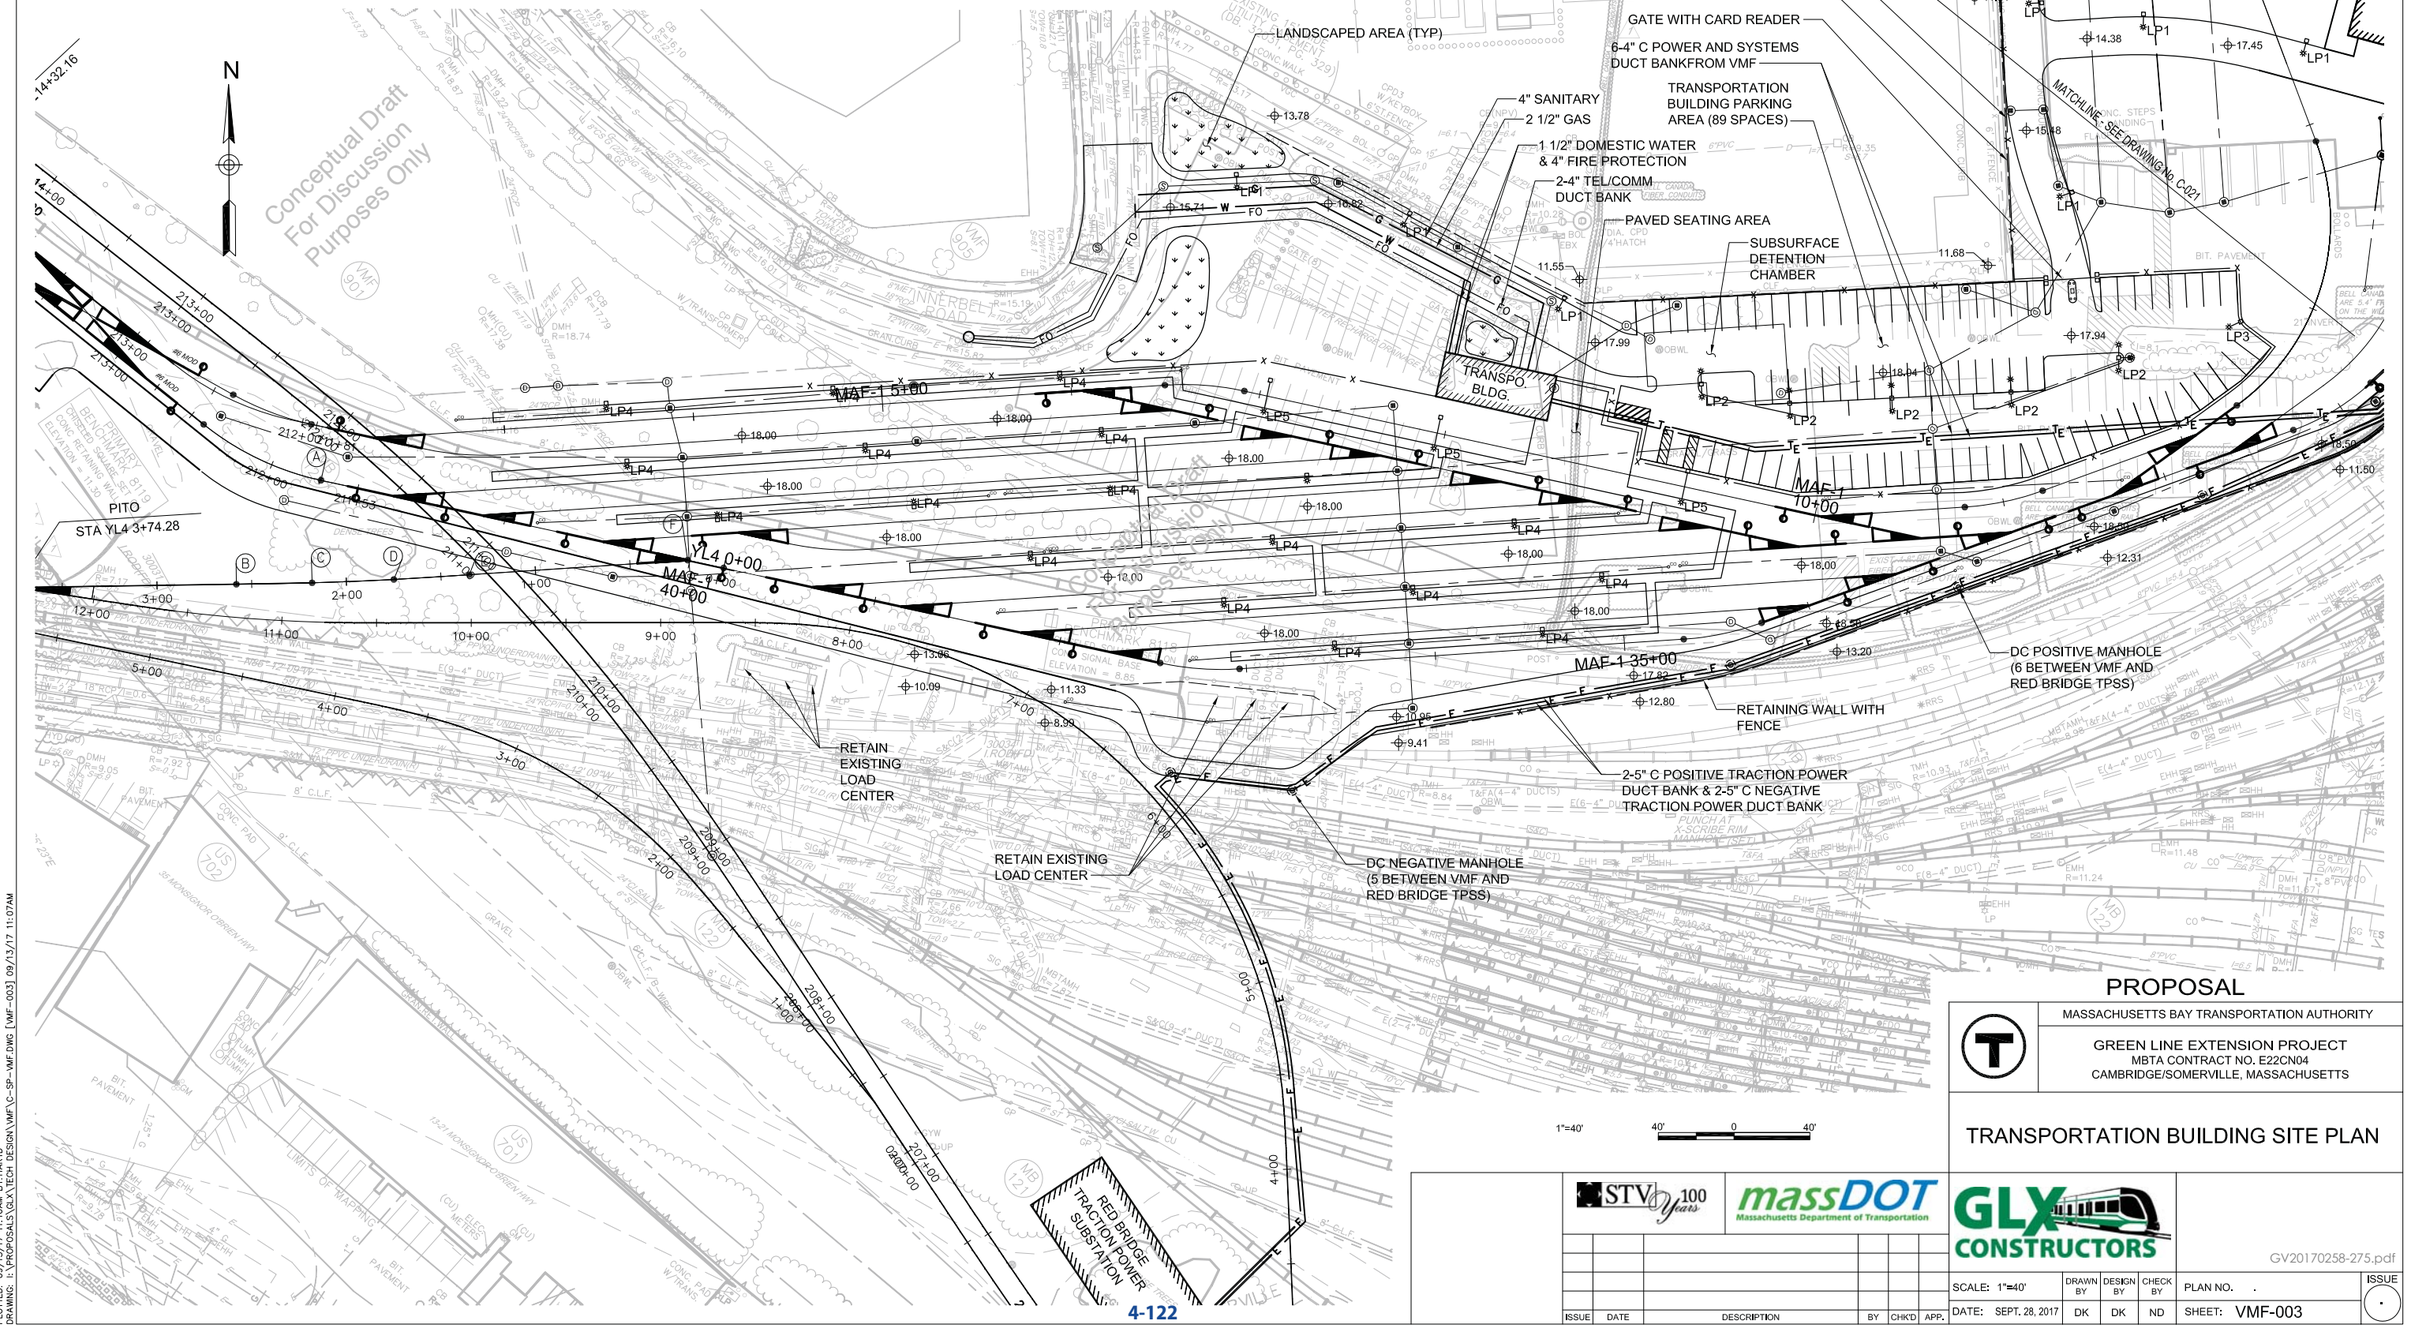

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

TRANSPORTATION BUILDING SITE PLAN


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-275.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: 1"=40'	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	DK	DK	ND	SHEET: VMF-003	.

PLOTTED: 09/13/17 11:16AM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\VMF\C-SP-VMF.DWG [VMF-003] 09/13/17 11:07AM

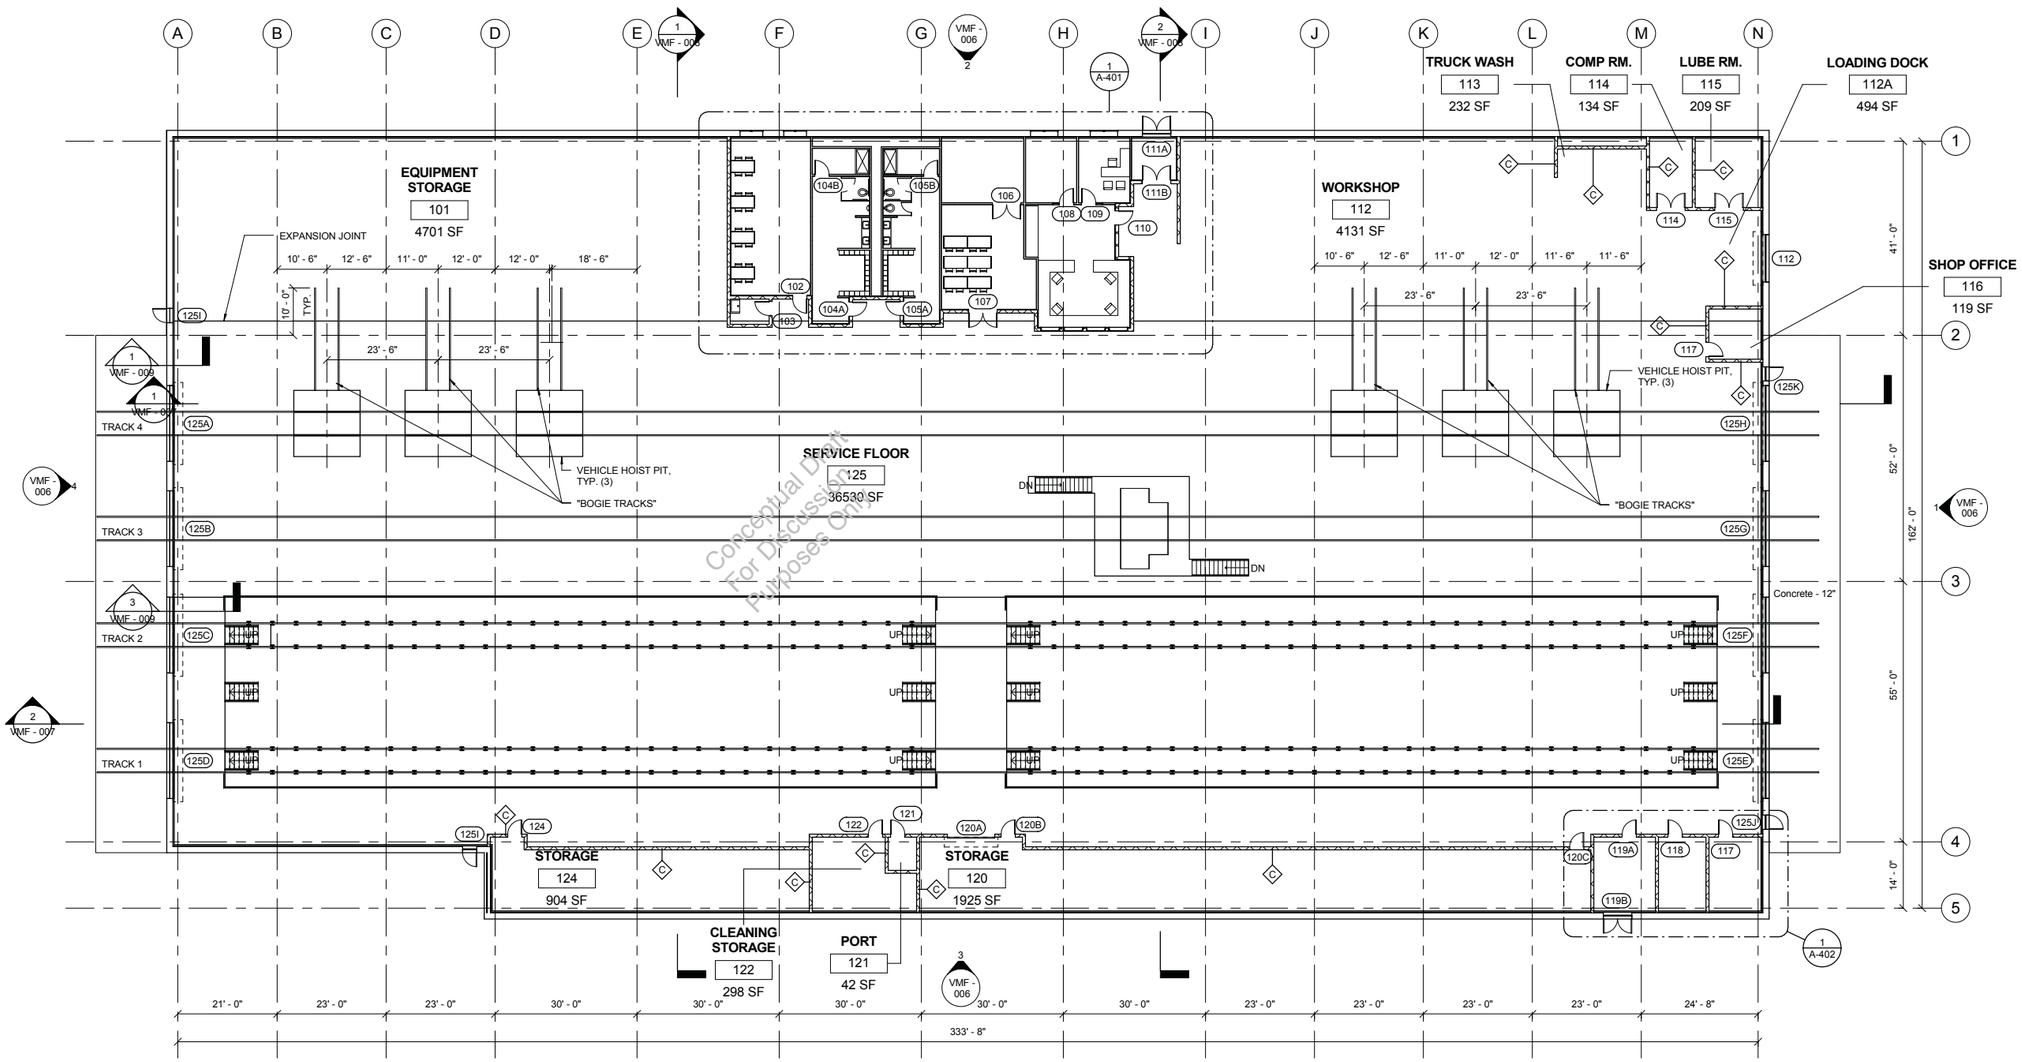

FIRST FLOOR PLAN

1/16" = 1'-0"

0 8' 16' 32'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE E□TENSION PRO□ECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY
FLOOR PLAN

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


GV20170258-275.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP	ND	SHEET: VMF-004	

Conceptual Draft For Discussion Purposes Only

9/21/2017 1:25:17 PM
\\shgroup.stvinc.com\v3\DGPA\Vol3\Proposals\Green Line Extension\90_CAD Models and Sheets\07_A_Architectural\VMF_A_3D0000.rvt

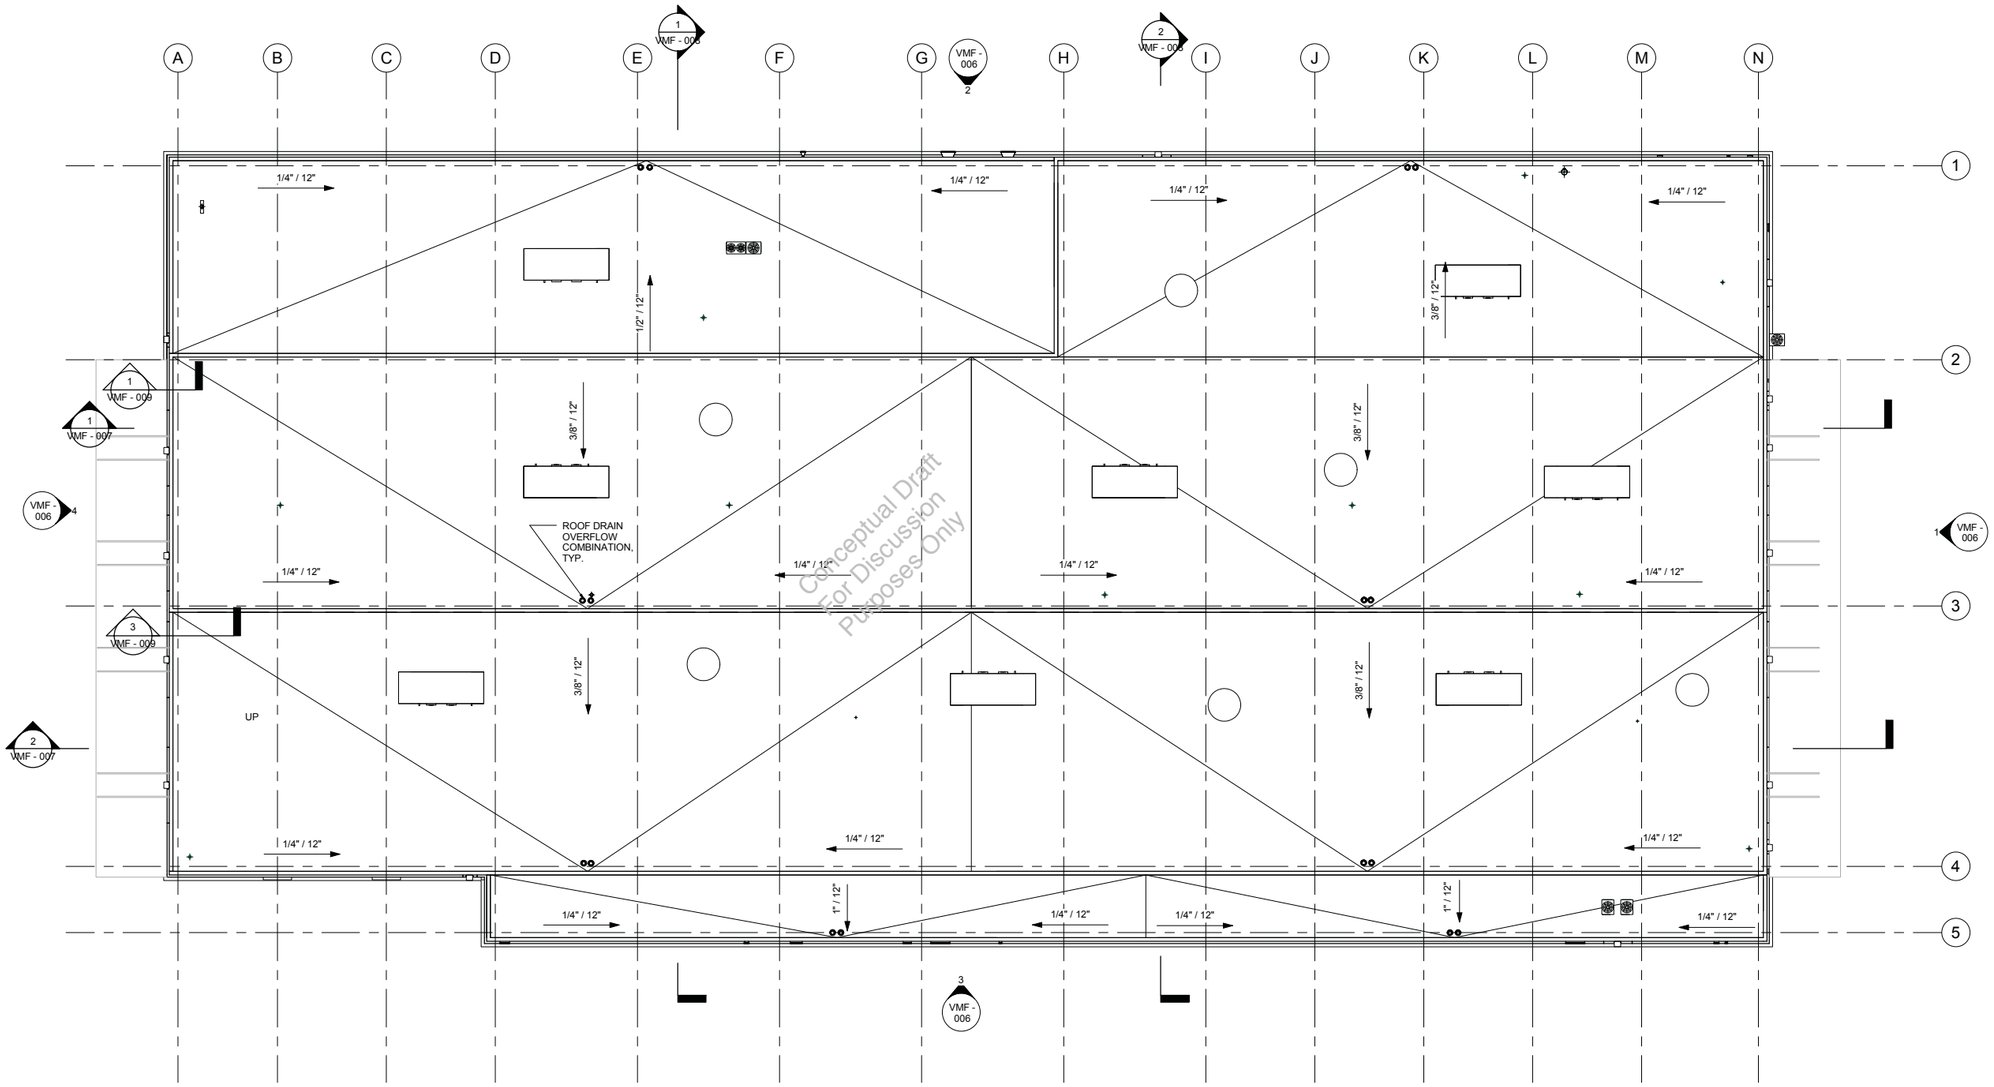

ROOF PLAN

1/16" = 1'-0"

Conceptual Draft For Discussion Purposes Only

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


VEHICLE MAINTENANCE FACILITY
ROOF PLAN

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-275.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP	ND	SHEET: VMF-005	

9/21/2017 1:25:18 PM
\\stvgroup.stvinc.com\v3\DGPAV\o3\Proposals\Green Line Extension\90_CAD Models and Sheets\07_A_Architectural\VMF_A_3D0000.rvt

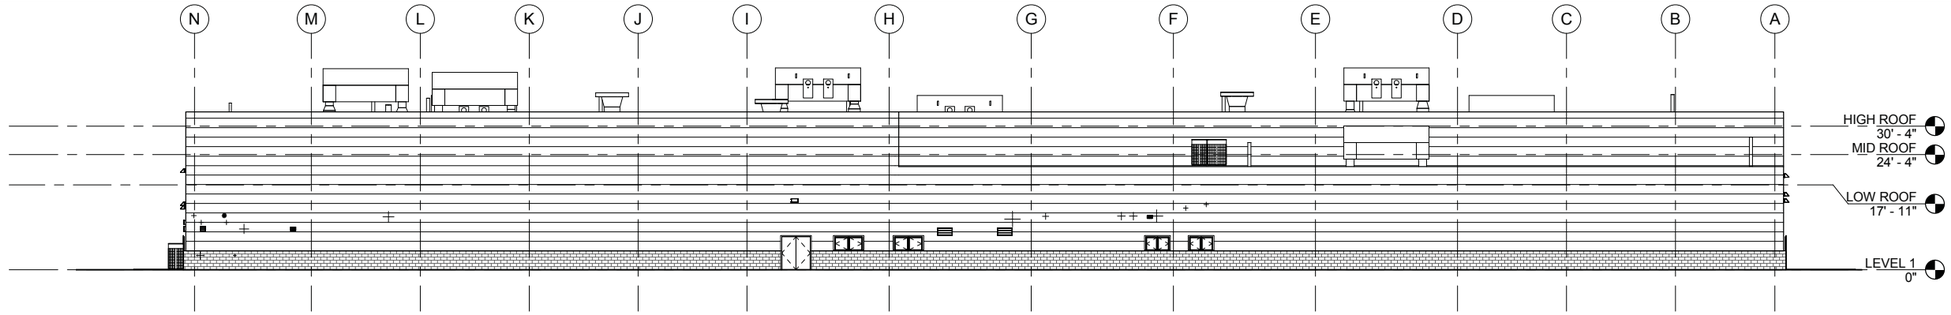


2 VMF - 004

NORTH ELEVATION

1/16" = 1'-0"

0 8' 16' 32'

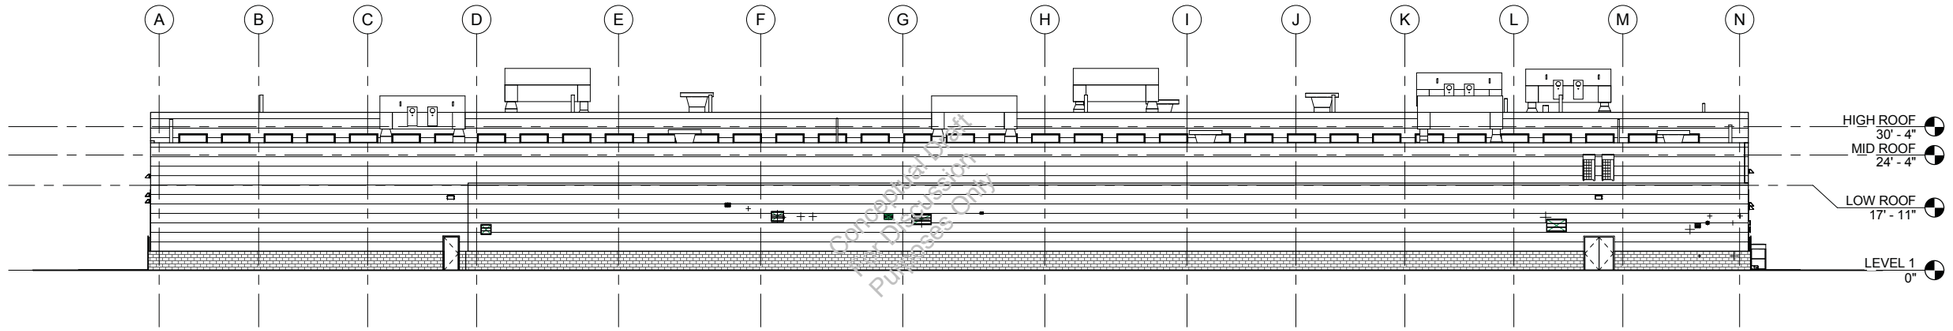


3 VMF - 004

SOUTH ELEVATION

1/16" = 1'-0"

0 8' 16' 32'

Conceptual Draft
For Discussion
Purposes Only

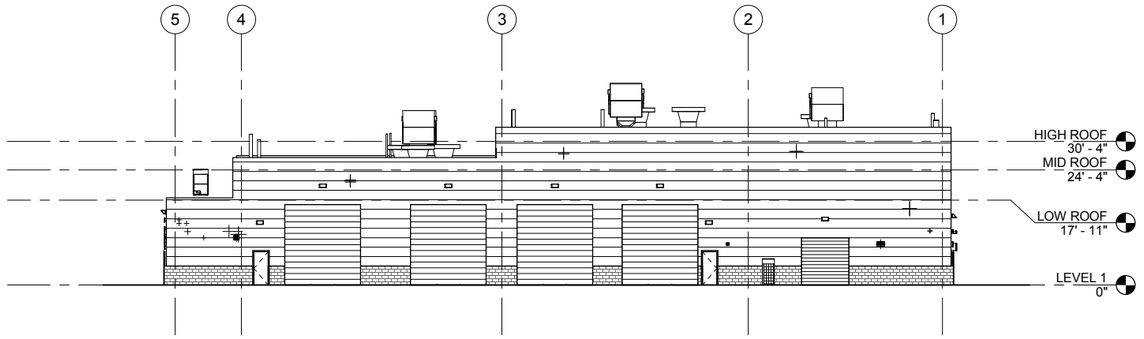


1 VMF - 004

EAST ELEVATION

1/16" = 1'-0"

0 8' 16' 32'

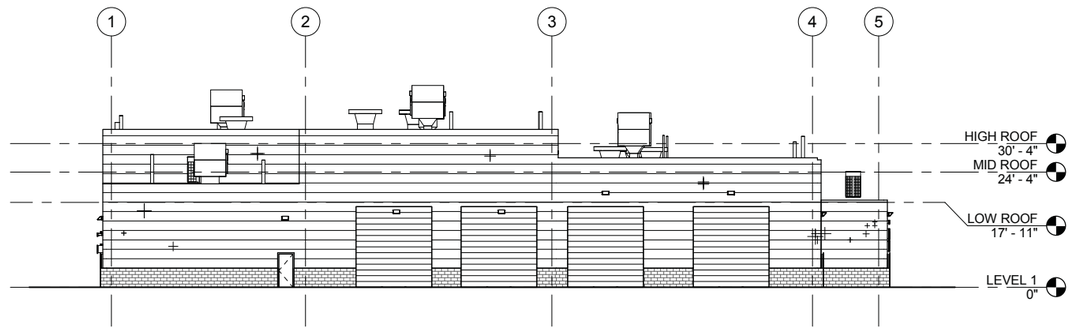

4 VMF - 004

WEST ELEVATION

1/16" = 1'-0"

0 8' 16' 32'

Conceptual Draft
For Discussion
Purposes Only

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY
EXTERIOR ELEVATIONS


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-275.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP	ND	SHEET: VMF-006	

9/21/2017 1:25:25 PM
\\stvgroup.stvinc.com\v3\DGPA\V03\Proposals\Green Line Extension\90_CAD Models and Sheets\07_A_Architectural\VMF_A_3D0000.rvt

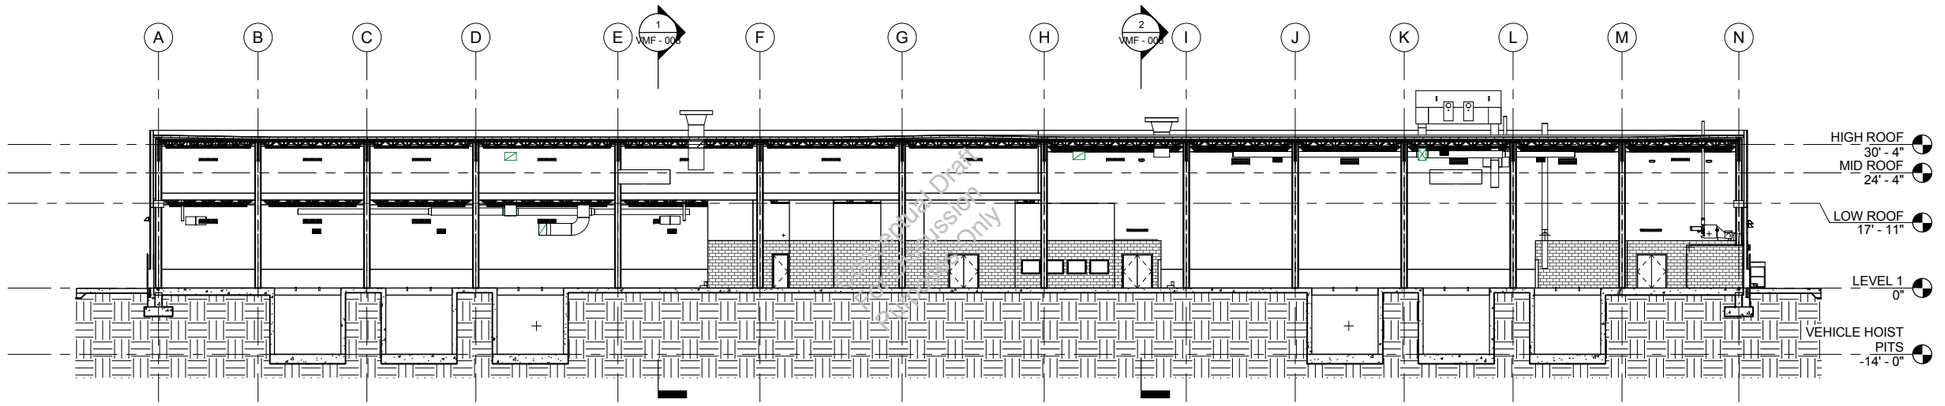

1 VMF - 004 LONGITUDINAL SECTION

1/16" = 1'-0"

0 8' 16' 32'

2 VMF - 004 LONGITUDINAL SECTION

1/16" = 1'-0"

0 8' 16' 32'

Preliminary Draft
Not for Construction
Permitting Only

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY BUILDING SECTIONS


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-275.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP	ND	SHEET: VMF-007	

9/21/2017 1:25:29 PM
\\shgroup.stvinc.com\v3\DGPA\vol3\Proposals\Green Line Extension\90_CAD Models and Sheets\07_A_Architectural\VMF_A_3D0000.rvt

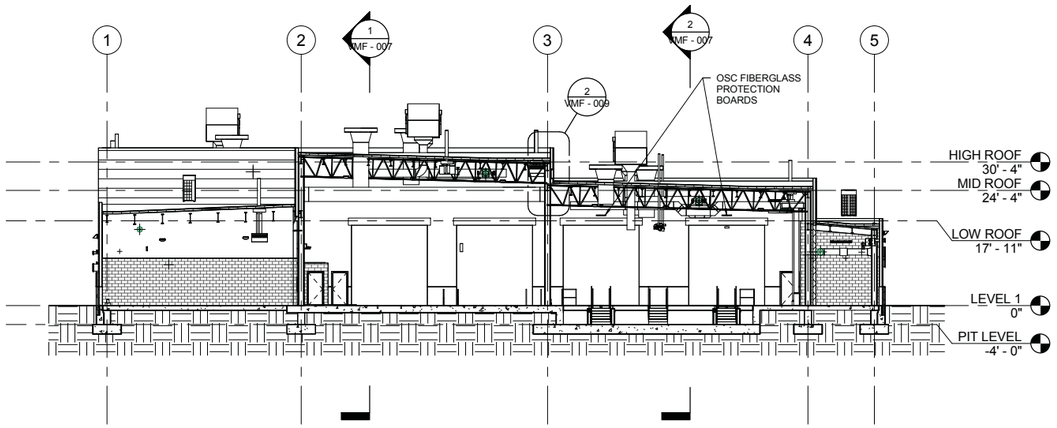


1 VMF - 004

TRANSVERSE SECTION

1/16" = 1'-0"

0 8' 16' 32'

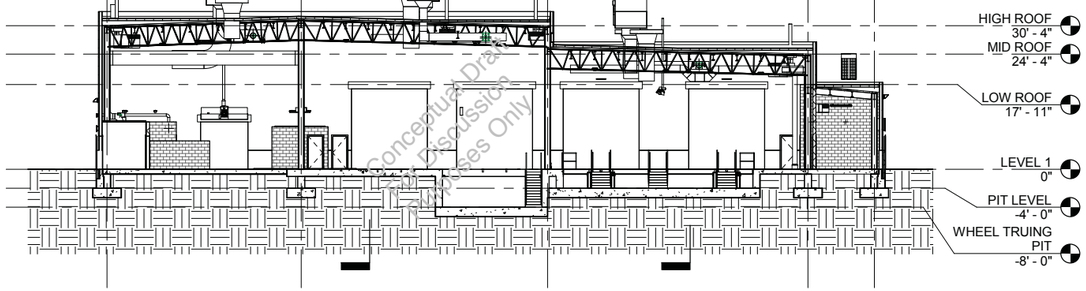

2 VMF - 004

TRANSVERSE SECTION

1/16" = 1'-0"

0 8' 16' 32'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


VEHICLE MAINTENANCE FACILITY
BUILDING SECTIONS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-275.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP	ND	SHEET: VMF-008	

9/21/2017 1:25:32 PM
\\stvgroup.stvinc.com\v3\DGPAV\o3\Proposals\Green Line Extension\90_CAD Models and Sheets\07_A_Architectural\VMF_A_3D0000.rvt

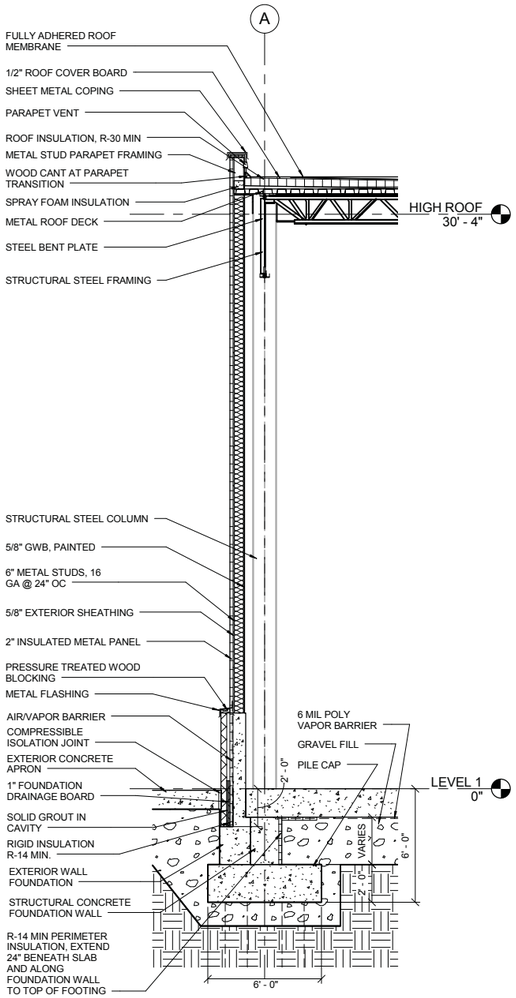


1 VMF - 004

TYPICAL WALL SECTION

1/4" = 1'-0"

0 2' 4' 8'

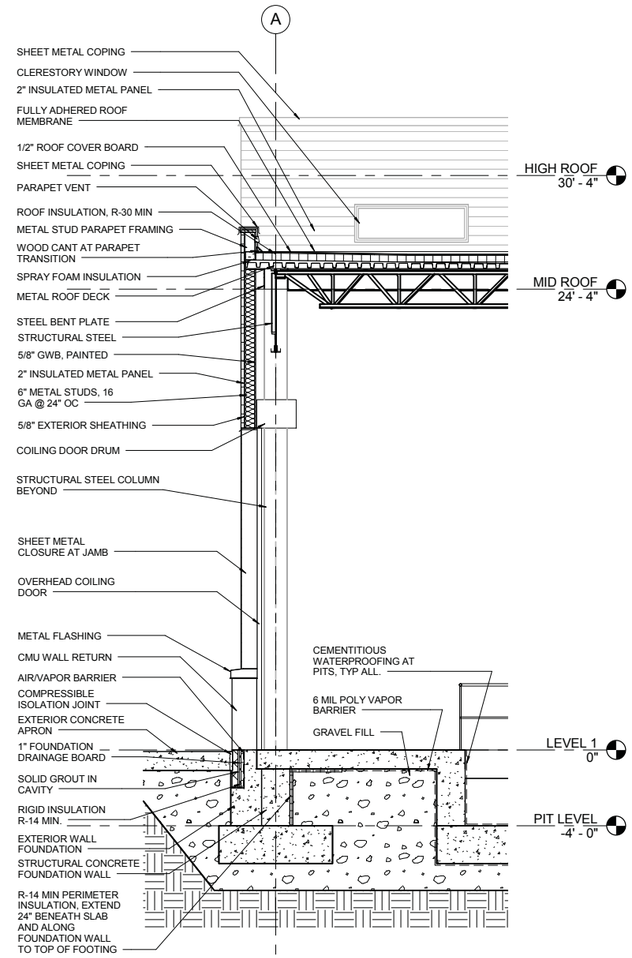


3 VMF - 004

WALL SECTION AT OVERHEAD COILING DOOR

1/4" = 1'-0"

0 2' 4' 8'

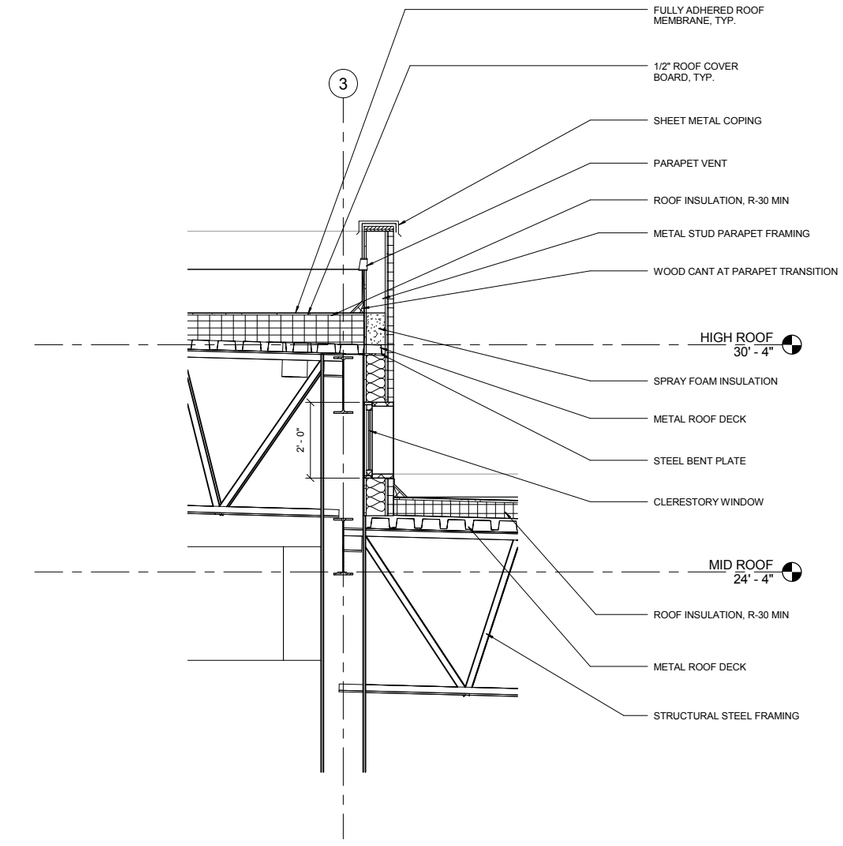

2 VMF - 008

DETAIL AT CLERESTORY

1/2" = 1'-0"

0 1' 2' 4'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY WALL SECTIONS


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-275.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP	ND	SHEET: VMF-009	

9/21/2017 1:25:32 PM
\\stvgroup.stvinc.com\v3\DGPA\Vol3\Proposals\Green Line Extension\90_CAD Models and Sheets\07_A_Architectural\VMF_A_3D0000.rvt

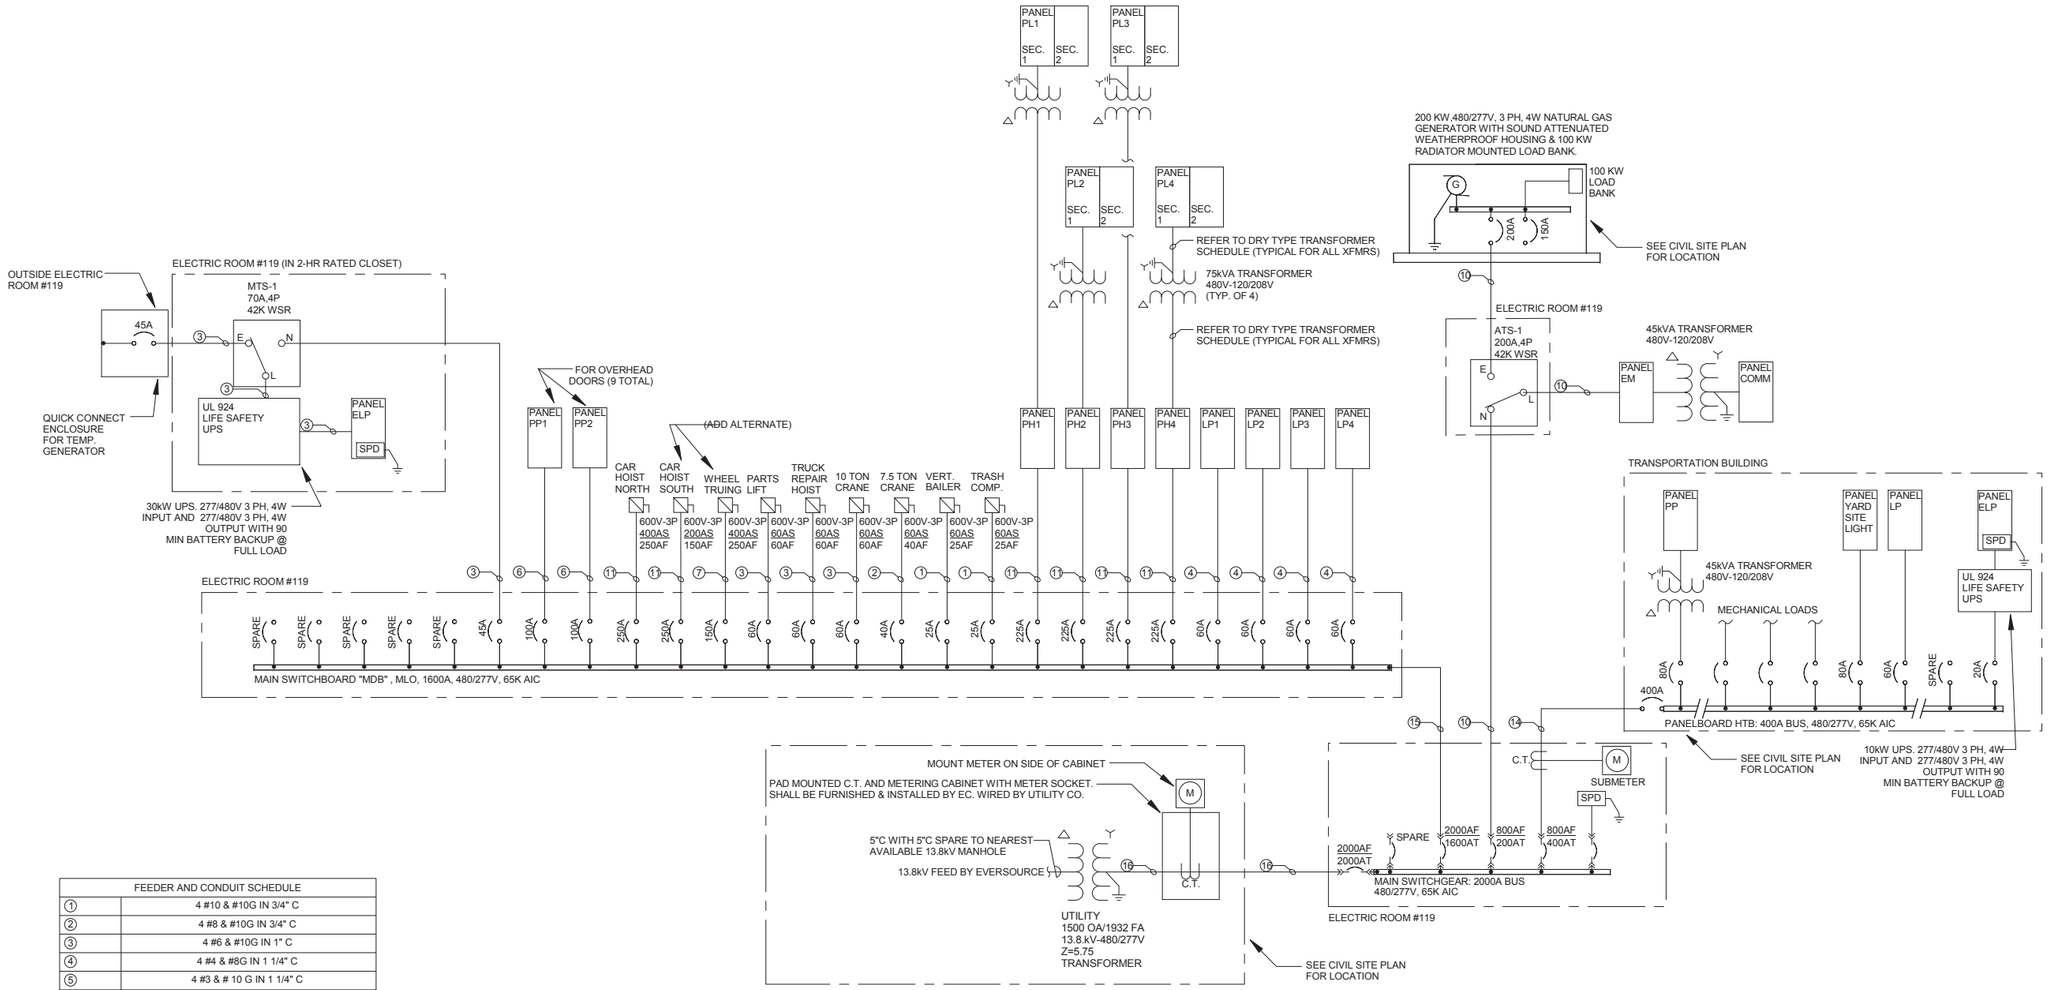

FEEDER AND CONDUIT SCHEDULE	
①	4 #10 & #10G IN 3/4" C
②	4 #8 & #10G IN 3/4" C
③	4 #6 & #10G IN 1" C
④	4 #4 & #8G IN 1 1/4" C
⑤	4 #3 & # 10 G IN 1 1/4" C
⑥	4 #1 & # 6 G IN 1 1/2" C
⑦	4 #1/0 & # 6G IN 2" C
⑧	4 #2/0 & # 6G IN 2" C
⑨	4 #3/0 & # 6G IN 2" C
⑩	4 #4/0 & # 4G IN 4" C WITH (1) 4"C SPARE
⑪	4 #250KCMIL & #4G IN 3" C
⑫	4 #350KCMIL & #4G IN 3" C
⑬	4 #500KCMIL & #3G IN 4" C
⑭	3 SETS OF 4 #600KCMIL & #1G IN (3) 4" C AND 4"C SPARE
⑮	5 SETS OF 4 #400KCMIL & 4/0 G IN (5) 3"C
⑯	6 SETS OF 4 #400KCMIL & 250KCMIL G IN (6) 3"C AND (3) 3" SPARES

DRY TYPE TRANSFORMER SCHEDULE					
SIZE KVA	PRIMARY OVERCURRENT PROTECTION (480V)	SECONDARY OVERCURRENT PROTECTION (208V)	480V PRIMARY FEEDER	120/208V SECONDARY FEEDER	GROUNDING CONDUCTOR, SYSTEM BONDING JUMPER AND EQUIPMENT BONDING JUMPER
45	80A, 3P	150A, 3P	3#1 & 1#8G IN 1 1/4"C	4#1/0 & 1#6G IN 2"C	1#6 IN 3/4"C
75	150A, 3P	250A, 3P	3#2/0 & 1#6 IN 1 1/2"C	4-250 KCMIL & 1#2G IN 3"C	1#2 IN 3/4"C

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY ELECTRICAL ONE-LINE DIAGRAM


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-275.pdf

SCALE:NOT TO SCALE	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SO	SO	ND	SHEET: VMF-010	

9/21/2017 2:31:35 PM
C:\Users\packarsj\Documents\VMF_MEP_300000_packarsj.rvt

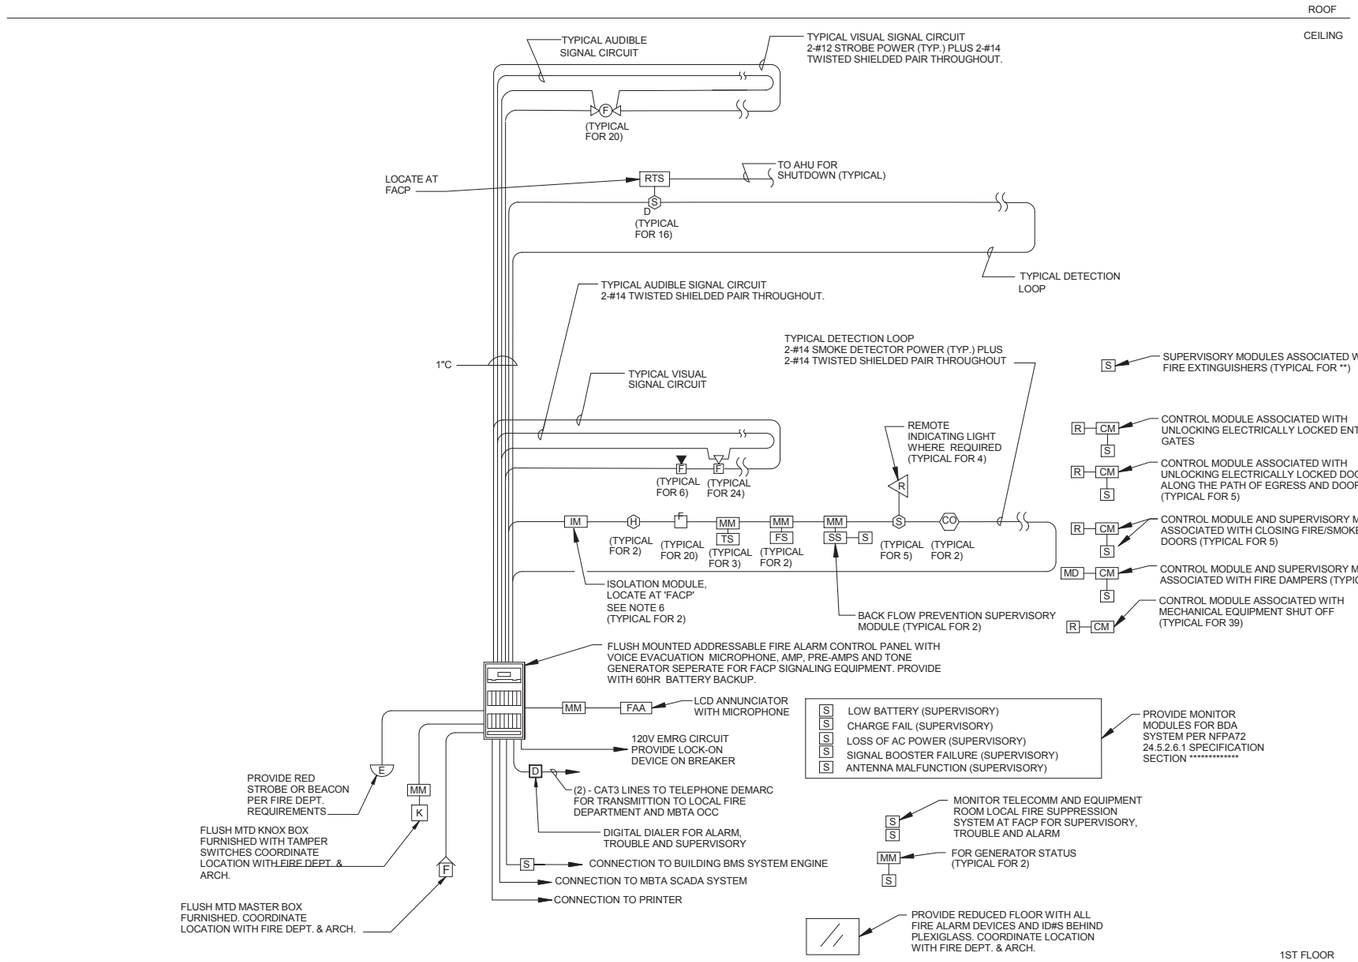

1 FIRE ALARM RISER DIAGRAM

SCALE: NTS

FIRE ALARM SYSTEM NOTES

1. CONTRACTOR SHALL REFER TO THE NOTES ON THE FA LEGEND, NOTES PROVIDED ON THIS SHEET, CONTRACT SPECIFICATIONS AND DRAWINGS FOR QUANTITY OF DEVICES, SPARE CAPACITY, TYPE OF DEVICES, WIRING OF DEVICES, ETC.
2. SUBMIT AS PART OF SHOP DRAWINGS COMPLETE FLOOR PLANS & RISERS WITH ALL DEVICES SHOWN AND WITH DEVICE ADDRESSES.
3. PROGRAMMING OF ADDRESSES SHALL BE COORDINATED WITH THE FIRE DEPARTMENT TO MATCH THE LOCAL FIRE DEPT. LABELING PROTOCOL DEVICE ADDRESS DESCRIPTIONS TO BE ISSUED TO THE ENGINEER AND FIRE DEPT. FOR APPROVAL PRIOR TO FINAL PROGRAMMING.
4. TYPICALLY ALL HORN/STROBE UNITS SHALL BE WIRED SO THAT THE STROBES ARE SYNCHRONIZED WHERE MULTIPLE DEVICES ARE IN THE SAME FIELD OF VIEW PER NFPA 72 AND SO THAT ALL BUILDING HORN/STROBES CAN BE SILENCED SIMULTANEOUSLY.
5. ALL DEVICES SHALL BE LABELED WITH CLEAR TAPE WITH BLACK INK, TYPED. LABEL SHALL IDENTIFY LOOP# AND DEVICE NUMBER.
6. FIRE ALARM WIRING SHALL BE CLASS A; FAULT ISOLATOR MODULES SHALL BE INSTALLED IN THE FACP TO PROTECT SIGNAL LINE CIRCUITS WHEN THEY LEAVE THE FACP AND WHEN THEY RETURN TO THE FACP. ALSO, FAULT ISOLATOR MODULES WILL BE PROVIDED BETWEEN FLOORS AND/OR FOR EVERY 18 ADDRESSABLE DEVICES.
7. FIRE ALARM WIRING TERMINATIONS SHALL BE MADE ON TERMINAL BLOCKS; NO SPLICES ARE ALLOWED. NUMBER OR CIRCUITS TO BE DETERMINED BY THE CONTRACTOR.
8. CONTRACTOR SHALL PROVIDE ALL NECESSARY HARDWARE AND SOFTWARE FOR A COMPLETE AND OPERABLE SYSTEM.
9. CONTRACTOR SHALL PROVIDE ENOUGH BATTERY CAPACITY FOR THE FIRE ALARM SYSTEM TO OPERATE FOR 60 HOURS IN A NON-ALARM CONDITION AND CAPABLE OF OPERATING IN ALARM FOR 10 MINUTES AT THE END OF THE 60 HOUR PERIOD.
10. CONTRACTOR SHALL REFER TO HVAC DRAWINGS FOR EXACT LOCATION OF HVAC UNITS AND FOR LOCATIONS OF DUCT MOUNTED SMOKE DETECTORS. DUCT DETECTORS FURNISHED AND WIRED BY E.C. INSTALLED BY HVAC.
11. ALL REMOTE TEST STATIONS SHALL BE KEYED AND MOUNTED ADJACENT TO THE FACP OR AS DIRECTED BY LOCAL FIRE DEPT. LABEL EACH UNIT.
12. ALL TAMPER AND SUPERVISORY SWITCHES SHALL BE WIRED AS LOCAL SUPERVISORY ALARM CONDITION UPON ACTIVATION. TROUBLE OR SUPERVISORY SHALL BE SELF RESTORING. TRANSMIT SIGNAL TO CENTRAL STATION, BUT DO NOT ALARM BUILDING.
13. ALL FLOW SWITCHES SHALL BE CONNECTED AS ALARM CIRCUIT TO GENERATE A GENERAL ALARM ON THE SYSTEM.
14. CONTROL MODULES SERVING MECHANICAL EQUIPMENT, MOTORIZED FIRE/SMOKE DAMPERS AND OTHER EMERGENCY FUNCTIONS SHALL BE LOCATED WITHIN 3 FEET OF THE CONTROLLED CIRCUIT OR APPLIANCE.
15. ELECTRICALLY HELD DOOR LOCKS ALONG THE PATH OF EGRESS SHALL BE CONNECTED TO THE FIRE ALARM SYSTEM VIA A CONTROL MODULE AND INTERFACE RELAY. DEVICE SHALL BE PROGRAMMED TO DROP OUT IN THE CASE OF A GENERAL ALARM TO FAIL OPEN THE LOCK. REFER TO ARCHITECTURAL AND SECURITY PLANS FOR DOORS WITH ELECTRICALLY HELD LOCKS.
16. FIRE AND SMOKE DOORS MAGNETICALLY HELD OPEN SHALL BE CONNECTED TO THE FIRE ALARM SYSTEM VIA A CONTROL MODULE AND INTERFACE RELAY. DEVICE SHALL BE PROGRAMMED TO DROP OUT IN THE CASE OF A GENERAL ALARM TO SHUT THE DOOR. REFER TO ARCHITECTURAL AND SECURITY PLANS FOR DOORS WITH HOLDERS

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


VEHICLE MAINTENANCE FACILITY ELECTRICAL ONE-LINE DIAGRAM

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-275.pdf

SCALE: NOT TO SCALE	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	RF	RF	ND	SHEET: VMF-011	

9/21/2017 3:53:23 PM
C:\Users\packarsj\Documents\VMF_MEP_300000_packarsj.rvt

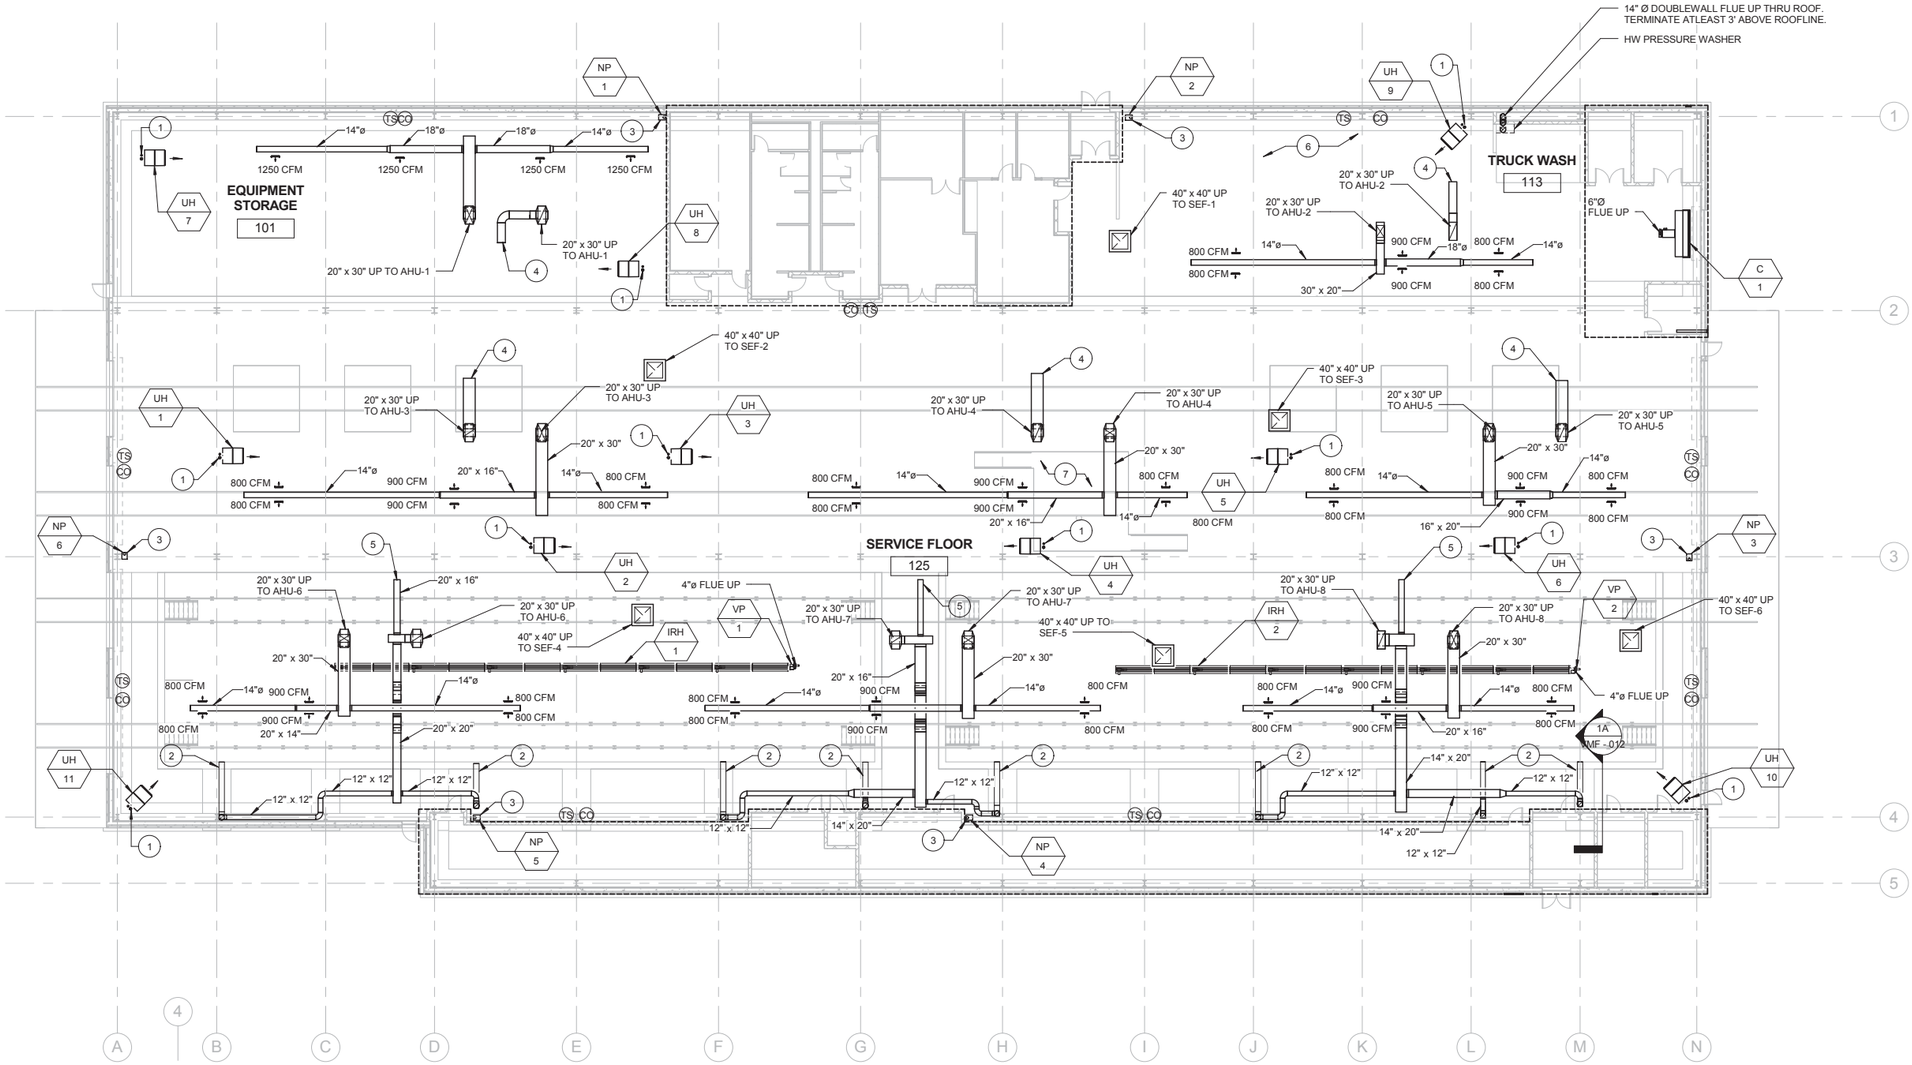

MECHANICAL GENERAL NOTES

1. STORAGE 101 & SERVICE FLOOR 125:
HEATING AND VENTILATION PROVIDED BY ROOF MOUNTED AHU-1 THRU 8 TO MAINTAIN SPACE SETPOINT (ADJ.). SUMMER VENTILATION PROVIDED BY ROOF MOUNTED EXHAUST FANS SEF-1 THRU 6, VENTILATION MAKEUP AIR VIA OPEN TRAIN DOORS AND ADJACENT SPACES. SUPPLEMENTAL SPACE HEATING PROVIDED BY SPACE GAS-FIRED UNIT HEATERS. ALL EQUIPMENT SERVED BY SPACE AVERAGING TEMPERATURE SENSORS. REFER TO PLAN FOR ADDITIONAL INFORMATION.


2. TRUCK WASH 113: DETAILS TO BE PROVIDED.

3. SPACE CO & NOx :
COMBINATION CO & NOX DETECTORS (PPM ADJ.) SHALL BE LOCATED THROUGHOUT STORAGE 101, SEVICE FLOOR 125, TRUCK WASH 113, AND ANY OTHER SPACES CONTAINING FUEL BURNING EQUIPMENT. DETECTORS SHALL BE LOCATED AT WALL PERIMETER AND ON COLUMNS 4' A.F.F. INTERLOCK DETECTION SIGNAL WITH AUDIBLE STROBE/ALARM AND SEF-1 THRU 6 AND AHU-1 THRU 8 OPERATION.

4. FIRE DAMPERS, SMOKE DAMPERS, AND COMBINATION FIRE/SMOKE DAMPERS SHALL BE PROVIDED AT ALL DUCT PENETRATIONS OF FIRE, SMOKE, AND FIRE/SMOKE BARRIERS WHERE REQUIRED. PROVIDE DUCT SMOKE DETECTORS AS REQUIRED.

MECHANICAL NEW WORK NOTES

1. ROUTE EXHAUST FLUE AND COMBUSTION AIR INTAKE UP FROM UNIT HEATER(S). CONNECT TO CONCENTRIC VENT KIT AT ROOF LINE. REFER TO MANUFACTURER'S RECOMMENDATIONS FOR FINAL ROUTING AND FLUE SIZING.
2. 14"Ø PIT EXHAUST, BALANCE TO 1500 CFM (TYP.)
3. ROUTE PVC CONDENSATE DRAINS, APPROPRIATELY SIZED AND PITCHED, FROM ALL HIGH EFFICIENCY GAS BURNING EQUIPMENT TO CONDENSATE NEUTRALIZER BASINS. PUMP POST-NEUTRALIZED CONDENSATE TO NEAREST FLOORDRAIN, PROVIDE DRAIN ANTI-TRIP DEVICES AT ALL PATH OF TRAVEL DRAIN CROSSINGS. PROVIDE PROTECTIVE BOLLARDS AS NECESSARY TO SHIELD NEUTRALIZER BASINS FROM DAMAGE.
4. AHU RETURN AIR: 50% OF TOTAL CFM SHALL BE VIA LOW RETURN AND 50% OF TOTAL CFM SHALL BE VIA HIGH RETURN.
5. RETURN AIR SHALL BE VIA HIGH RETURN
6. WELDING SPOT CAPTURE EQUIPMENT PROVIDED BY INDUSTRIAL ENGINEERING. REFER TO MANUFACTURER'S RECOMMENDATIONS FOR EXHAUST MATERIAL, ROUTING, AND SIZING, AS REQUIRED.
7. PROVIDE 420 CFM OF EXHAUST IN THE WHEEL TRUING PIT. EXHAUST CFM SHALL BE PROVIDED BY ROOF TOP AHU'S.

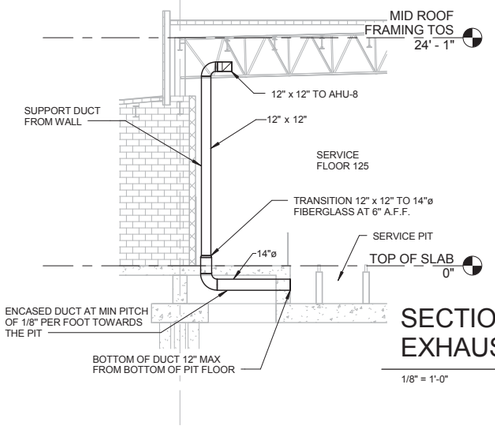

SECTION 1A TYPICAL PIT EXHAUST

1/8" = 1'-0" 0 4' 8' 16'

OVERALL VMF WORK PLAN

1/16" = 1'-0" 0 8' 16' 32'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY
MECHANICAL OVERALL WORK PLAN

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-275.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KJM	CPD	ND	SHEET: VMF-012	

9/21/2017 2:31:40 PM
C:\Users\jpackars\Documents\VMF_MEP_3D0000_packarsj.rvt

MECHANICAL GENERAL NOTES


1. ALL MECHANICAL EQUIPMENT SHALL LOCATED ATLEAST 10' FROM EDGE OF ROOF.

2. ALL MECHANICAL EXHAUST OUTLETS SHALL BE LOCATED ATLEAST 25' FROM AHU INTAKES.

MECHANICAL NEW WORK NOTES

(1) 20" x 30" SUPPLY AIR AND RETURN AIR DUCT DN THRU ROOF. (TYP. FOR AHU-1 THRU 8).

(2) 40" x 40" EXHAUST AIR DUCT DN THRU ROOF. (TYP. FOR SEF-1 THRU 6).

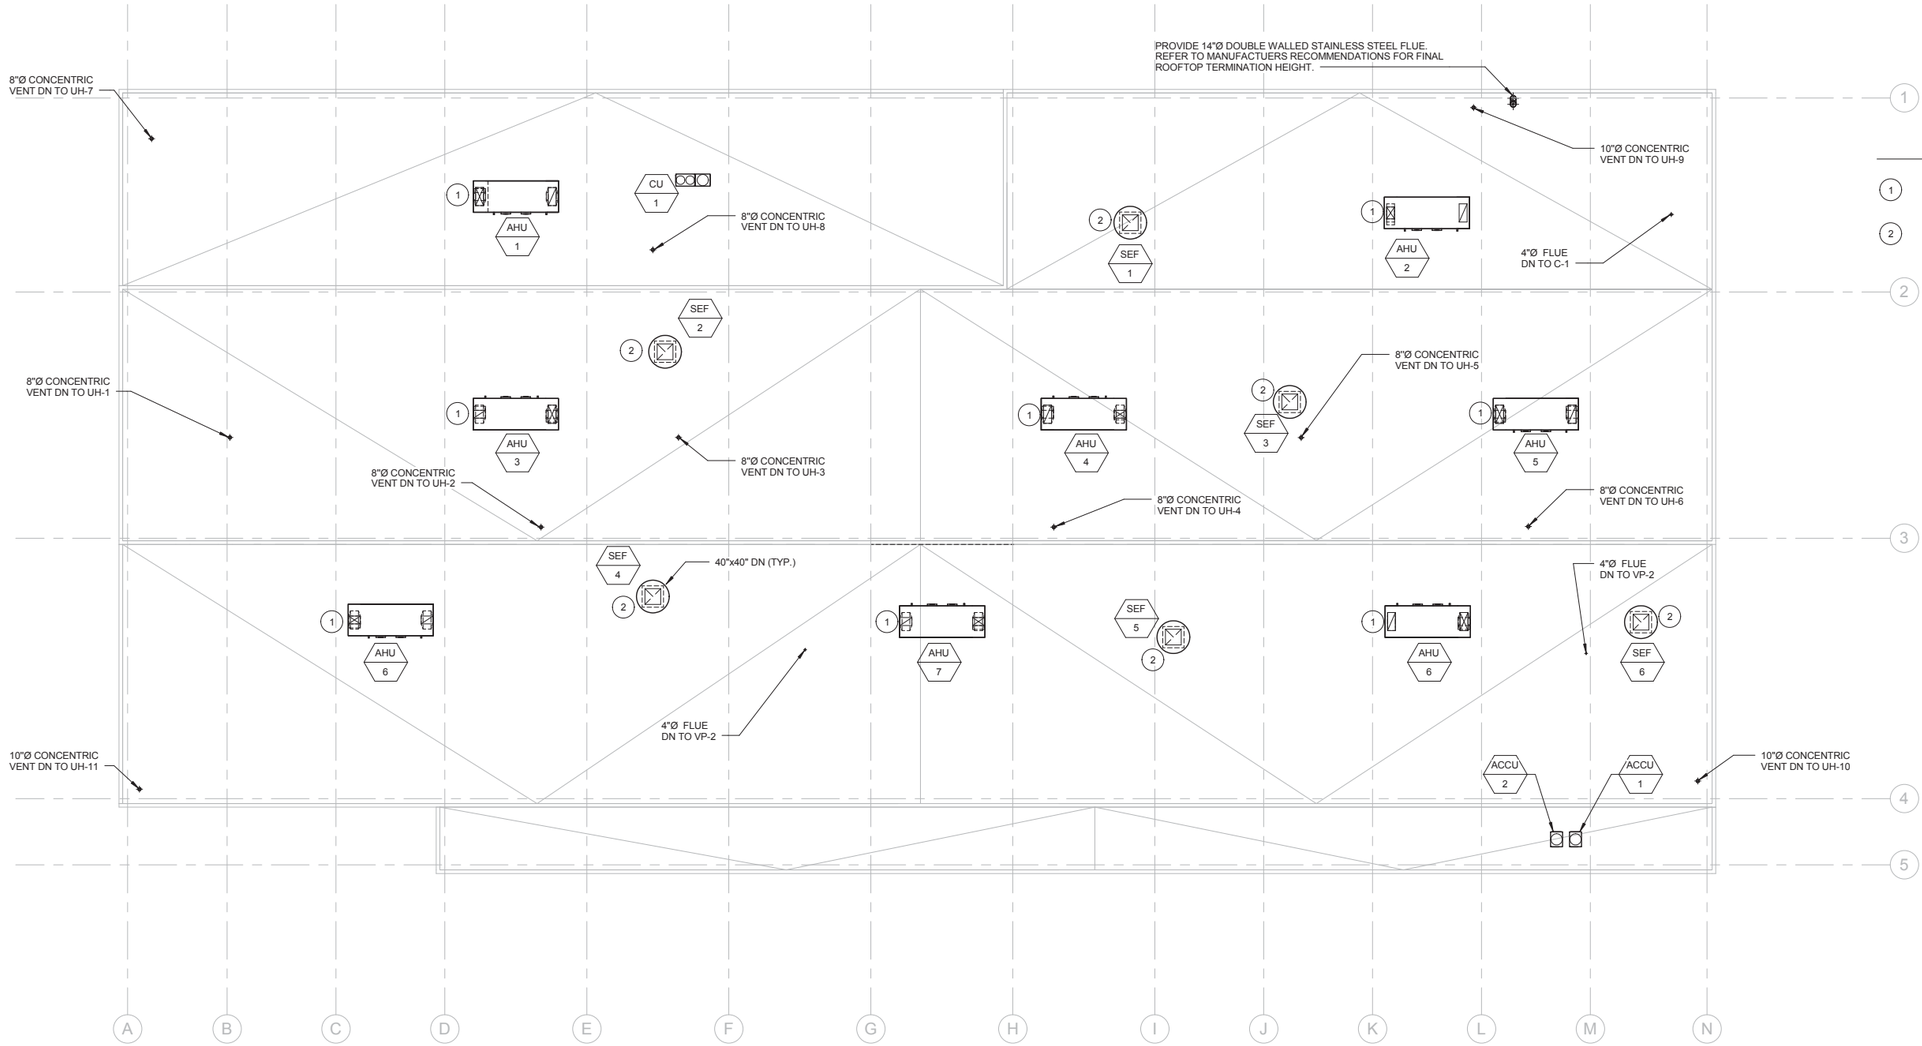

VMF ROOF PLAN

1/16" = 1'-0"

0 8' 16' 32'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY
MECHANICAL ROOF PLAN

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-275.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KJM	CPD		SHEET: VMF-013	

9/21/2017 2:31:41 PM
C:\Users\packarsj\Documents\VMF_MEP_3D0000_packarsj.rvt

HEATING AND VENTILATOR WITH PLATE AND FRAME ENERGY RECOVERY SCHEDULE

SYMBOL	BASIS OF DESIGN	AREA SERVED	LOCATION	EXHAUST FAN							SUPPLY FAN								NATURAL GAS HEATING						AIR-TO-AIR "PLATE-TYPE" HEAT EXCHANGER					VOLTS / PH / HZ	FLA	MOP	WEIGHT (LB)	FILTER	REMARKS
				TOTAL CFM	MIN. CFM	QTY.	ESP	RPM	BHP	MOTOR HP	MOTOR RPM	TOTAL CFM	MIN. CFM	QTY	ESP	RPM	BHP	MOTOR HP	MOTOR RPM	INPUT MBH	OUTPUT MBH	MIN. BURNER EFF.	GAS (IN WG)	EAT (°F)	LAT (°F)	EXHAUST - EAT (DB °F)	EXHAUST - LAT (DB °F)	SUPPLY - EAT (DB, °F)	SUPPLY - LAT (DB, °F)	MIN EFF % (SENS. / TOTAL)					
AHU-1,2,3,4, 5,6,7,8	JCI (YORK)	VMF	ROOF	5,000	2,500	1	1.5	1357	1.82	5	1725	5,000	4,500	1	1.5	1357	1.82	5	1725	435	405	93	5" - 10"	15.3	80	65	34	7	46	68 / 49	460 / 3 / 60	-	-	8,220	2" MERV 8	ALL

REMARKS:
1. PROVIDE FUSED DISCONNECT SWITCH,(SINGLE POINT POWER CONNECTION FOR UNIT) UNIT MOUNTED CONVENIENCE RECEPTACLE, AND UNIT MOUNTED LIGHTING POWERED BY SEPARATE ELECTRICAL CIRCUIT. COORDINATE WITH EC.
2. PROVIDE WITH VFD FOR FAN CONTROL FOR ALL FANS
3. PROVIDE WITH HEAT TRACING AT 5 WATTS PER LINEAR FOOT FOR CONDENSATE LINES INSIDE BURNER HOUSING AND BETWEEN BURNER HOUSING AND BELOW ROOF LEVEL. INSULATE CONDENSATE PIPING OUTSIDE OF BURNER HOUSING AND WHERE REQUIRED BY MANUFACTURER.
4. PROVIDE WITH RAINHOOD AND BIRD SCREEN FOR ALL INTAKE AND EXHAUST OPENINGS
5. INSTALL PER MANUFACTURER'S INSTALLATION INSTRUCTIONS
6. PROVIDE DUCT SMOKE DETECTORS IN THE SUPPLY AND RETURN DUCTWORK, TO BE WIRED BY ELECTRICAL
7. NATIONALLY RECOGNIZED TESTING LABORATORY(NRTL) CERTIFIED TO UL #1995
8. PROVIDE WITH ENERGY RECOVERY BYPASS, PROVIDE WITH DUCT MOUNTED SOUND ATTENUATORS ON SUPPLY AND RETURN DUCT MAINS EXTERNAL TO UNIT.
9. PROVIDE WITH CONDENSATE NEUTRALIZER KIT.

ENERGY RECOVERY VENTILATOR SCHEDULE

SYMBOL	MAKE / MODEL	ROOM(S) SERVING	TYPE	SUPPLY & EXHAUST FAN DATA										WINTER DATA				SUMMER DATA				WEIGHT (LBS)	REMARKS
				SUPPLY AIR FLOW (CFM)	EXHAUST AIR FLOW (CFM)	ESP (IN WG)	FAN SPEED	RPM	MOTOR ELECTRICAL DATA					OA EAT (DB/WB)(F°)	RA EAT (DB/RH)(F°)	SA LAT (DB/WB)(F°)	ENERGY TRANSFER (BTU)	OA EAT (DB/WB)(F°)	RA EAT (DB/WB)(F°)	SA EAT (DB/WB)(F°)	ENERGY TRANSFER (BTU)		
									QTY.	FLA	MCA	MOP	VOLTS/PH/HZ										
ERV- 1	RENEWAIRE / HE1.5XINH	104 TO 112	STATIC PLATE, ENTHALPY CORE	1048	1048	1	VAR.	VAR.	2	1.1	2.5	15	480 / 3 / 60	7.4 / 0	70	38.7	-	90.8 / 73.3	75 / 62	97.4	-	464	1,2,3,4
ERV- 2 / ERV- 5	RENEWAIRE / BR70	115,116 / 117	STATIC PLATE, ENTHALPY CORE	50	50	0.35	VAR.	VAR.	1	1	-	-	120 / 1 / 60	7.4 / 0	55	31.2	-	90.8 / 73.3	104	97.4	-	38	1,2,3,4
ERV- 3	RENEWAIRE / 450IN	121	STATIC PLATE, ENTHALPY CORE	250	250	1	VAR.	VAR.	1	0.8	1	15	480 / 3 / 60	7.4 / 0	55	31.2	-	90.8 / 73.3	104	97.4	-	199	1,2,3,4
ERV- 4	RENEWAIRE / EV200	122,123,124	STATIC PLATE, ENTHALPY CORE	175	175	0.4	VAR.	VAR.	1	1.5	-	-	120 / 1 / 60	7.4 / 0	55	31.2	-	90.8 / 73.3	104	97.4	-	68	1,2,3,4

REMARKS:
1. PROVIDE WITH NON-FUSED DISCONNECT AND ONBOARD 24 VAC POWER
2. PROVIDE WITH SEISMIC RESTRAINTS AND VIBRATION ISOLATORS
3. PROVIDE WITH MERV 8, 2" PLEATED FILTERS FOR BOTH SUPPLY AND EXHAUST
4. PROVIDE ELECTRIC HEATING COIL ON OA DUCT, REFER TO ELECTRIC HEATING COIL SCHEDULE.

CONDENSATE BASIN

SYMBOL	MAKE / MODEL	MAX FLOW (GAL/HR)	PUMP ELECTRICAL (V/PH/HZ)	WEIGHT (LBS)	REMARKS
NP-(1 THROUGH 6)	AXIOM/ NT25-P	40	120/ 1/ 60	55	ALL

REMARKS:
1. PROVIDE WITH REPLACEMENT LIPHTER NEUTRALIZATION MEDIA, 1 KIT PER BASIN. PROVIDE POST-NEUTRALIZER COND. PUMP

ELECTRIC BASEBOARD

SYMBOL	MAKE / MODEL	WATT / LF.	LENGTH (FT.)	PUMP ELECTRICAL (V/PH/HZ)	WEIGHT (LBS)	REMARKS
EB	BERKO / 25008	312.5	SEE PLANS	277/ 1/ 60	18.5	ALL

REMARKS:
1. PROVIDE DISCONNECT SWITCH. CONTROL WIRING BY MC, POWER WIRING BY EC.

UNIT HEATER / CABINET UNIT HEATER SCHEDULE

SYMBOL	MAKE / MODEL	TYPE	AIRFLOW (CFM)	HEATING SECTION						ELECTRICAL DATA				WEIGHT (LBS)	REMARKS
				FUEL TYPE	MIN GAS PRESSURE (IN. W.G)	MAX GAS PRESSURE (IN. W.G)	INPUT (MBH)	OUTPUT(MBH)	OUTPUT(KW)	VOLTS / PH / HZ	MOP	FLA	FAN (HP / W)		
UH-1,2,3,4,5,6,7,8	REZNOR/ UEAS	INDIRECT	2256	GAS	9	14	131	121.8	-	120 / 1 / 60	15	3.8	0.25 HP	230	1,2,3,4,5,6,7
UH-9,10,11	REZNOR/ UEAS	INDIRECT	4430	GAS	9	14	260	239.2	-	120 / 1 / 60	15	3.8	0.5 HP	360	1,2,3,4,5,6,7
UH-12,13,14,15,16	QMARK / IUH	ELECTRIC	270	-	-	-	-	-	7.5	460 / 3 / 60	-	7.2	6 W	26	2,4,5,7
UH-17,18,19,20	QMARK / IUH	ELECTRIC	1000	-	-	-	-	-	20	460 / 3 / 60	-	19.3	1 / 10 HP	78	2,4,5,7
CUH-1	QMARK / IUH	ELECTRIC	1800	-	-	-	-	-	30	460 / 3 / 60	-	36.9	1 / 3 HP	140	4,5,7

REMARKS:
1. PROVIDE MANUFACTURERS OPTIONAL 50-90 DEGREE DOWN TURN NOZZLE.
2. PROVIDE NON-FUSED DISCONNECT. CONTROL WIRING BY MECH. POWER CONNECTION BY ELECTRICAL.
3. PROVIDE VERTICAL COMBUSTION AIR/ VENT KIT INCLUDING CONCENTRIC ADAPTOR.
4. PROVIDE WITH GALVANIZED AIRCRAFT CABLES, MIN. 1/8" (QUANTITY FOUR) PER UNIT.
5. PROVIDE WITH MANUFACTURER INTEGRAL CONTROLS, TRANSFORMER FOR 24V CONTROLS, BACNET CONNECTION.
6. PROVIDE WITH AIR DESTRATIFICATION FAN CONTROL
7. INSTALL PER MANUFACTURERS INSTALLATION INSTRUCTIONS.

OUTDOOR - SPLIT CONDENSER UNIT SCHEDULE

SYMBOL	MAKE	MODEL	SERVING	LOCATION	NOMINAL COOLING CAPACITY (TONS)	COOLING RATED CAPACITY @95°F (BTU)	HEATING RATED CAPACITY (BTU)	SEER	REFRIGERANT	AMBIENT AIR TEMP (°F)	ELECTRICAL			WEIGHT	REMARKS
											VOLTS/ PH/ HZ	MCA	MOP		
CU-1	YORK - VRF	HYVAHP	VMF - AREA A	VMF - LOW ROOF	24	288,000	324,000	-	R-410A	95	480 / 3 / 60	-	-	-	ALL
CU-2	YORK - VRF	DHR	SHOP OFFICE 117 ROOF	SHOP OFFICE 117 ROOF	2	24,000	28,000	-	R-410A	95	208 / 1 / 60	-	-	-	ALL
ACCU-1	YORK	DCP	TELECOM 119	TELECOM 119 ROOF	3	36,000	N/A	-	R-410A	95	208 / 1 / 60	-	-	-	ALL
ACCU-2	YORK	DCP	ELECTRICAL 120	ELECTRICAL 120 ROOF	3	36,000	N/A	-	R-410A	95	208 / 1 / 60	-	-	-	ALL

REMARKS:
1. PROVIDE WITH DISCONNECT SWITCH.
2. INSTALL PER MANUFACTURER'S INSTALLATION INSTRUCTIONS.
3. PROVIDE WITH WIND BAFFLES.
4. PROVIDE LOW AMBIENT KIT.

FAN SCHEDULE

SYMBOL	BASIS OF DESIGN	MODEL	TYPE	LOCATION	AREA SERVED	CFM	DRIVE	MOTOR HP	MOTOR BHP	EXTERNAL STATIC PRESSURE (IN WC)	FAN RPM	VOLTS / PH / HZ	WEIGHT (LBS)	REMARKS
SEF-(1 THROUGH 6)	GREENHECK	GB-500-100	CENTRIFUGAL	ROOF	SERVICE FLOOR	30,000	BELT	10	-	0.5	442	460 / 3 / 60	580	1,4,8,9,10
EF-1	GREENHECK	SQ-85	INLINE	ROOM 116	ROOM 116, 115	475	DIRECT	1/10	-	0.25	1725	120 / 1 / 60	49	1,4,5,6,11
EF-2	GREENHECK	SQ-120	INLINE	ROOM 124	ROOM 124, 123, 122	1,615	DIRECT	1/2	-	0.25	1725	120 / 1 / 60	63	1,4,5,6,11
EF-3	GREENHECK	SQ-140	INLINE	ROOM 121	ROOM 121	2,595	DIRECT	1	-	0.25	1725	460 / 3 / 60	103	1,4,5,6,11
EF-4	GREENHECK	SQ-70	INLINE	ROOM 118	ROOM 118	244	DIRECT	1/10	-	0.25	1725	120 / 1 / 60	34	1,4,5,6,11

REMARKS:
1. INSTALL PER MANUFACTURER'S INSTALLATION INSTRUCTIONS
2. PROVIDE WITH 18" HIGH ROOF CURB AND BIRDSCREEN.
3. PROVIDE WITH TEFC MOTOR OUTSIDE OF AIR STREAM AND AMCA SPARK RESISTANCE 'B' RATING
4. PROVIDE WITH REMOTE MOUNTED UNIT CONTROLLER AND DISCONNECT SWITCH
5. PROVIDE WITH INLINE DAMPER (24 VAC)
6. PROVIDE WITH VIBRATION ISOLATION HANGERS AND SEISMIC RESTRAINTS
7. NATIONALLY RECOGNIZED TESTING LABORATORY(NRTL) CERTIFIED TO UL 705 - POWER VENTILATOR FOR SMOKE CONTROL, PROVIDE ALL REQUIRED OPTIONS & ACCESSORIES.
8. PROVIDE WITH MOTOR STARTER AND DISCONNECT SWITCH
9. PROVIDE WITH BACKDRAFT DAMPER (FAN SELECTION SHALL ACCOUNT FOR DAMPER STATIC PRESSURE)
10. PROVIDE WITH 12" HIGH SEISMIC ROOF CURB AND BIRDSCREEN
11. PROVIDE GALVANIZED AIRCRAFT CABLES, MIN. 1/8" (QUANTITY FOUR) PER UNIT

INDOOR UNIT - SPLIT SYSTEM SCHEDULE

SYMBOL	MAKE / MODEL	LOCATION (AREA SERVED)	ASSOCIATED CONDENSING UNIT	COOLING CAPACITY (MBH)	HEATING CAPACITY (MBH)	AIRFLOW (CFM)	E.S.P (IN. W.G.)	ELECTRICAL		WEIGHT (LBS)	REMARKS
								VOLTS / PH / HZ	MOP		
HP-1	JCI-YORK / HIDH	BREAK ROOM: 104 PORT ROOM: 105	CU-1	48	54	1236	0.5	208 / 1 / 60	-	-	1, 2, 4, 6, 7
HP-2	JCI-YORK / HIDH	MENS LOCKER: 106	CU-1	36	40	1190	0.5	208 / 1 / 60	-	-	1, 2, 3, 5, 6, 7
HP-3	JCI-YORK / HIDH	WOMENS LOCKER: 107	CU-1	36	40	1190	0.5	208 / 1 / 60	-	-	1, 2, 3, 5, 6, 7
HP-4	JCI-YORK / HIDH	STORAGE: 109 TRAINNING ROOM: 108	CU-1	72	81	2047	0.5	208 / 1 / 60	-	-	1, 2, 4, 6, 7
HP-5	JCI -YORK / HIDI	BREAK ROOM: 110 OFFICE: 111 WORK ROOM: 112	CU-1	96	108	2542	0.5	208 / 1 / 60	-	-	1, 2, 4, 6, 7
HP-6	JCI -YORK / DHR	SHOP OFFICE: 117	CU-2	23.8	27.2	826	0.5	208 / 1 / 60	-	-	1, 2, 4, 6, 7
AC-1	JCI -YORK / DCP	TELECOM ROOM: 118	ACCU-1	36	-	736	-	208 / 1 / 60	-	-	1, 2, 4, 5
AC-2	JCI -YORK / DCP	ELECTRICAL ROOM: 119	ACCU-2	36	-	736	-	208 / 1 / 60	-	-	1, 2, 4, 5

REMARKS:
1. PROVIDE WALL MOUNTED THERMOSTAT, MANUFACTURER INTEGRAL CONTROLS AND DISCONNECT SWITCH.
2. INSTALL PER MANUFACTURER'S INSTALLATION INSTRUCTIONS.
3. PROVIDE WITH OPTIONAL FILTER BOX OR EQUAL, AND FILTERS.
4. PROVIDE MANUFACTURERS OPTIONAL CONDENSATE PUMP KIT.
5. PROVIDE LEAK DETECTION KIT AND AUXILIARY DRAIN PAN. PAN SHALL BE LOCATED BELOW UNIT AS WELL AS EXTEND BELOW CONDENSATE PIPING THAT IS INSTALLED OVER ELECTRICAL EQUIPMENT.
6. PROVIDE WITH LITTLE GIANT VCMX-20 CONDENSATE PUMP AND RECEIVER. TRAP UNIT DRAIN INTO CONDENSATE RECEIVER PER MANUFACTURER REQUIREMENTS.
7. PROVIDE WITH SUSPENSION ACCESSORIES AND ISOLATION TYPE HANGERS.

AIR CURTAIN

SYMBOL	BASIS OF DESIGN	MODEL	LOCATION (AREA SERVED)	SUPPLY FAN				FURNACE NATURAL GAS HEATING					ELECTRICAL DATA			WEIGHT (LB)	REMARKS
				TOTAL CFM	MAX FPM NOZZLE	DOOR HEIGHT (FT.)	MOTOR HP	INPUT MBH	FLUE (IN)	GAS INLET (IN)	MIN GAS PRESSURE (W.G)	MAX GAS PRESSURE (IN. W.G)	VOLTS / PH / HZ	FLA	MOP		
C-1	BERNER	IDC12-2120G	VEHICLE ROLLUP DOOR	3268	5079	10	2 @ .5	145	6	3/4	.5	14	480 / 3 / 60	4.9	15	249	ALL

REMARKS:
1. PROVIDE DISCONNECT SWITCH AND SINGLE POINT POWER CONNECTION FOR MOTOR PANEL AND TRANSFORMER FOR HEATER.
2. PROVIDE WITH MANUFACTURER UNIT CONTROLLER WITH BACNET CONNECTION, UNIT MOUNTED THERMOSTAT AND DOOR ACTIVATION SWITCH
3. PROVIDE SEISMIC RESTRAINTS
4. INSTALL PER MANUFACTURER'S INSTALLATION INSTRUCTIONS
5. NATIONALLY RECOGNIZED TESTING LABORATORY(NRTL) CERTIFIED TO UL #1995
6. PROVIDE STAINLESS AIR CURTAIN CABINET, TRANSITION AND HEATERS OPTION FOR AIR CURTAINS IN CAR WASH BAY.

INFRARED HEATER SCHEDULE

SYMBOL	BASIS OF DESIGN MAKE / MODEL	LOCATION (AREA SERVED)	DESCRIPTION	MAX INPUT (BTU/HR)	MIN GAS PRESSURE (W.G)	MAX GAS PRESSURE (IN. W.G)	TUBE LENGTH	TUBE MATERIAL	NUMBER OF BURNERS/ ELEC. CONNECTIONS	VOLTS / PH / HZ	FUEL	REMARKS
IRH-1 & 2	R & G / CRV-B2	MAINTENANCE SHOP	INFRARED HEATER	120,000	4.5"	14"	CUSTOM	HOT ROLLED STEEL	6	120 / 1 / 60	NATURAL GAS	ALL

VACUUM PUMP (FOR INFRARED HEATERS)

SYMBOL	BASIS OF DESIGN MAKE / MODEL	SERVING	DESCRIPTION	HP	VOLTAGE / PH / HZ	FULL LOAD AMP'S	REMARKS
VP-1 & 2	EP- 100	IRH-1 & 2	VACUUM PUMP	1/3	120 / 1 / 60	6.6 / 3.33	ALL

REMARKS:
1. SEE MOUNTING DETAILS ON DETAIL SHEETS
2. PROVIDE WITH NON-FUSED DISCONNECT. UNIT SHALL BE HARD WIRED TO DISCONNECT
3. PROVIDE WITH PROGRAMMABLE THERMOSTAT WITH BACNET CONNECTION

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY
MECHANICAL HVAC
EQUIPMENT SCHEDULE


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-275.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KJM	CPD	ND	SHEET: VMF-014	

9/21/2017 2:31:42 PM
C:\Users\packarsj\Documents\VMF_MEP_3D0000_packarsj.rvt

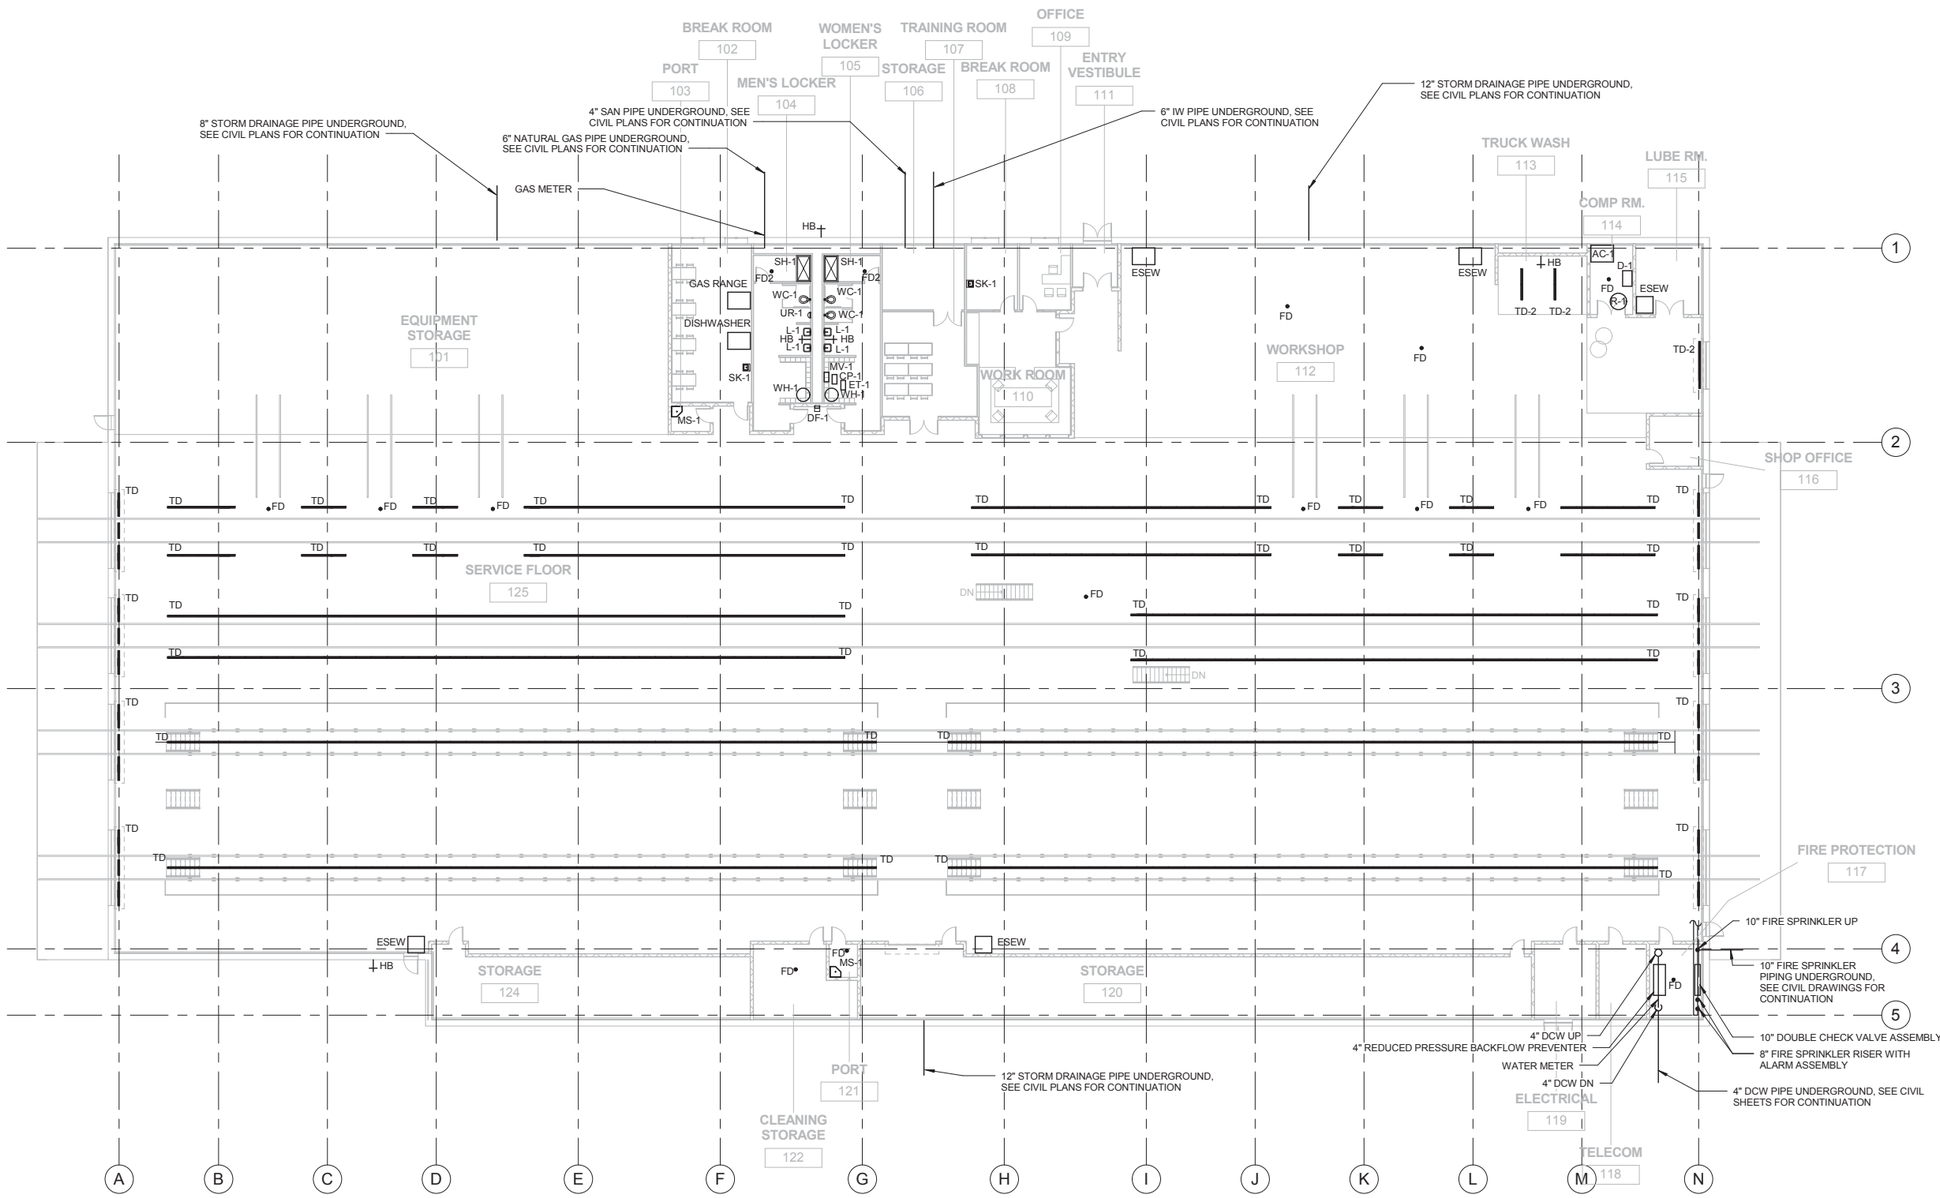

FIRST FLOOR PLAN

1/16" = 1'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


VEHICLE MAINTENANCE FACILITY
PLUMBING AND FIRE PROTECTION
FLOOR PLAN

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-275.pdf

SCALE:	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	JLO	JLO	JO	SHEET: VMF-015	

9/22/2017 6:18:52 PM
C:\Users\jpackars\Documents\VMF_MEP_3D0000_packarsj.rvt

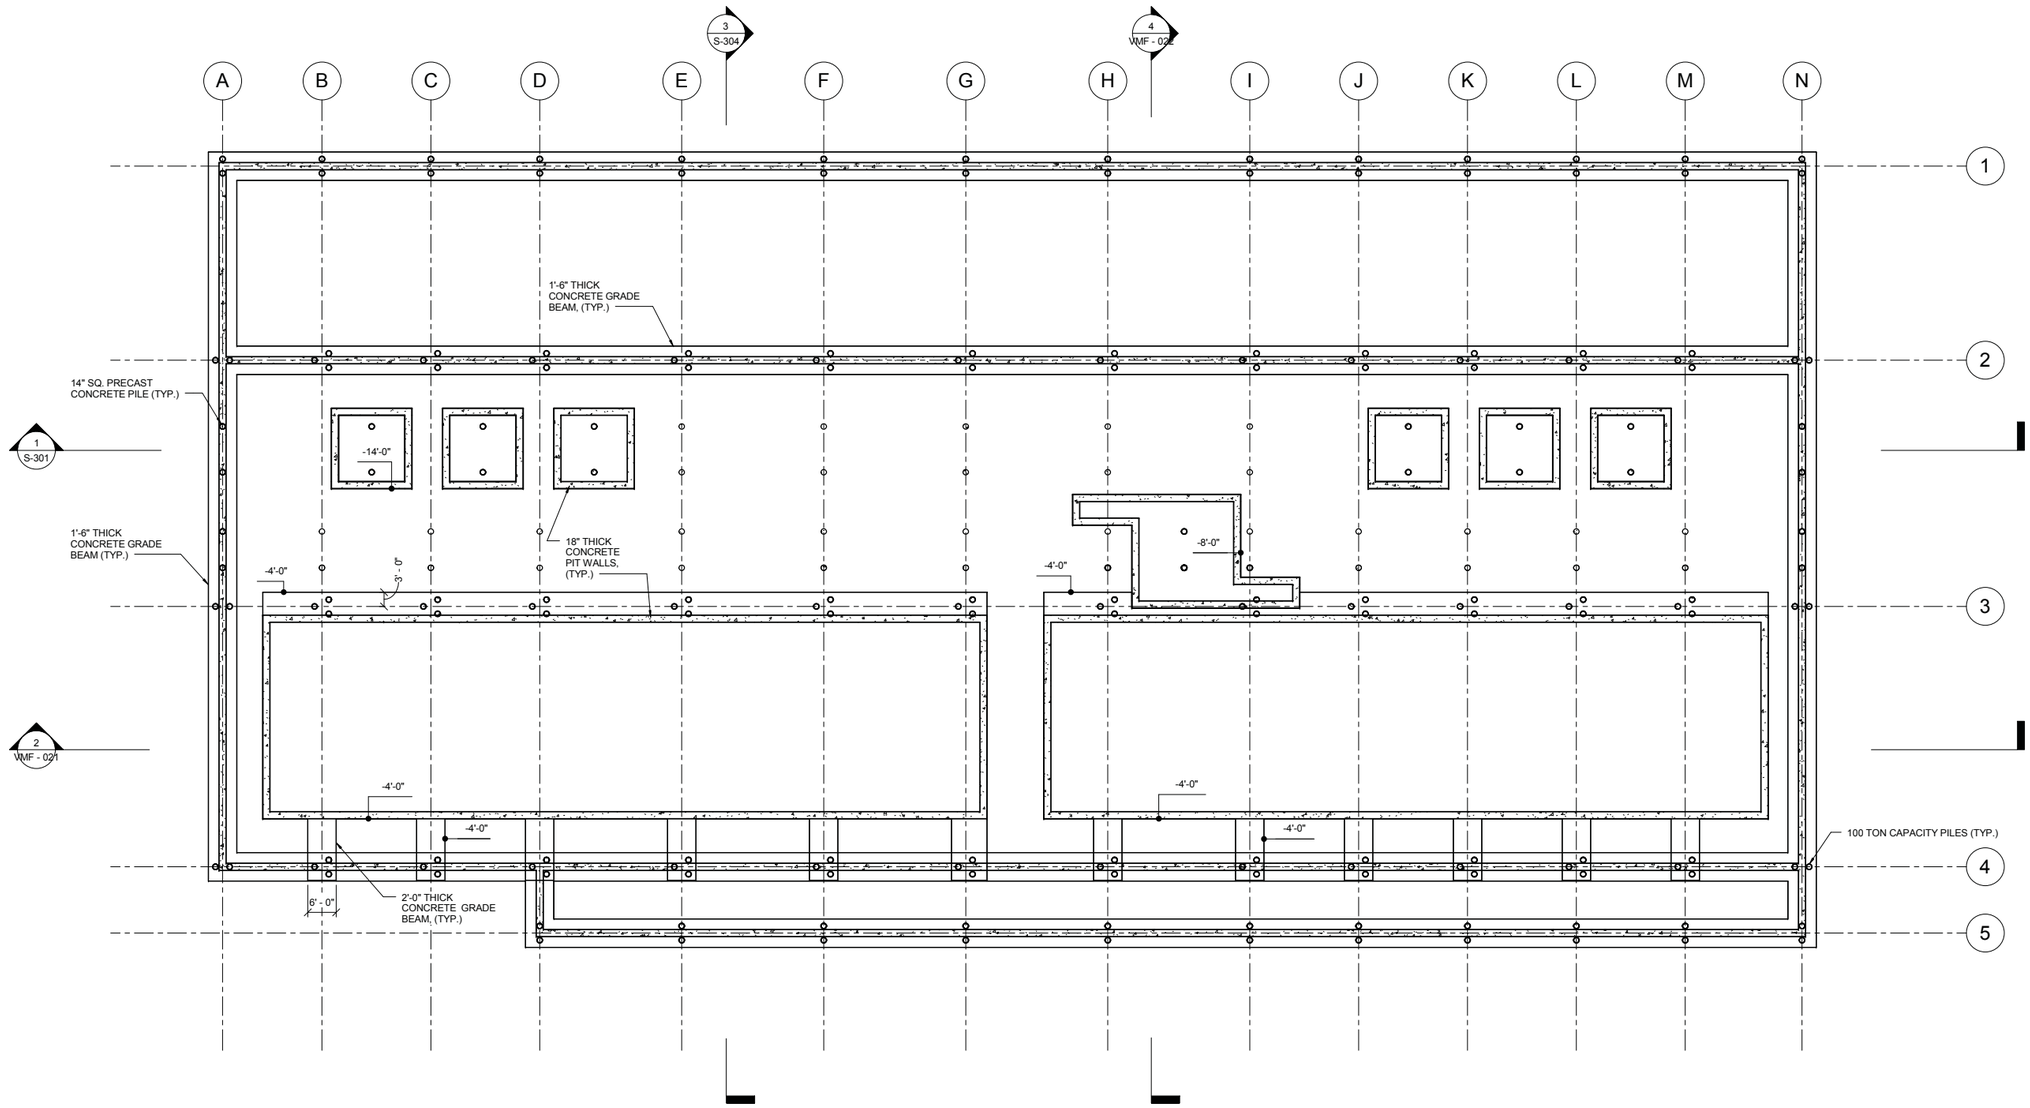

FOUNDATION PLAN

1/16" = 1'-0"

0 4' 8' 16'

NOTE:

ALL PILES CENTERED ON COLUMN LINES 1, 5, A, AND N. TRACKS 3 AND 4 ARE TO BE 70 TON CAPACITY U.N.O.
ALL OTHER PILES ARE TO BE 100 TON CAPACITY U.N.O.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


VEHICLE MAINTENANCE FACILITY
FOUNDATION PLAN

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-275.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	ZS	AD	ND	SHEET: VMF-016	

9/21/2017 1:58:44 PM
C:\Users\packanj\Documents\VMF_S_3D0000_packanj.rvt

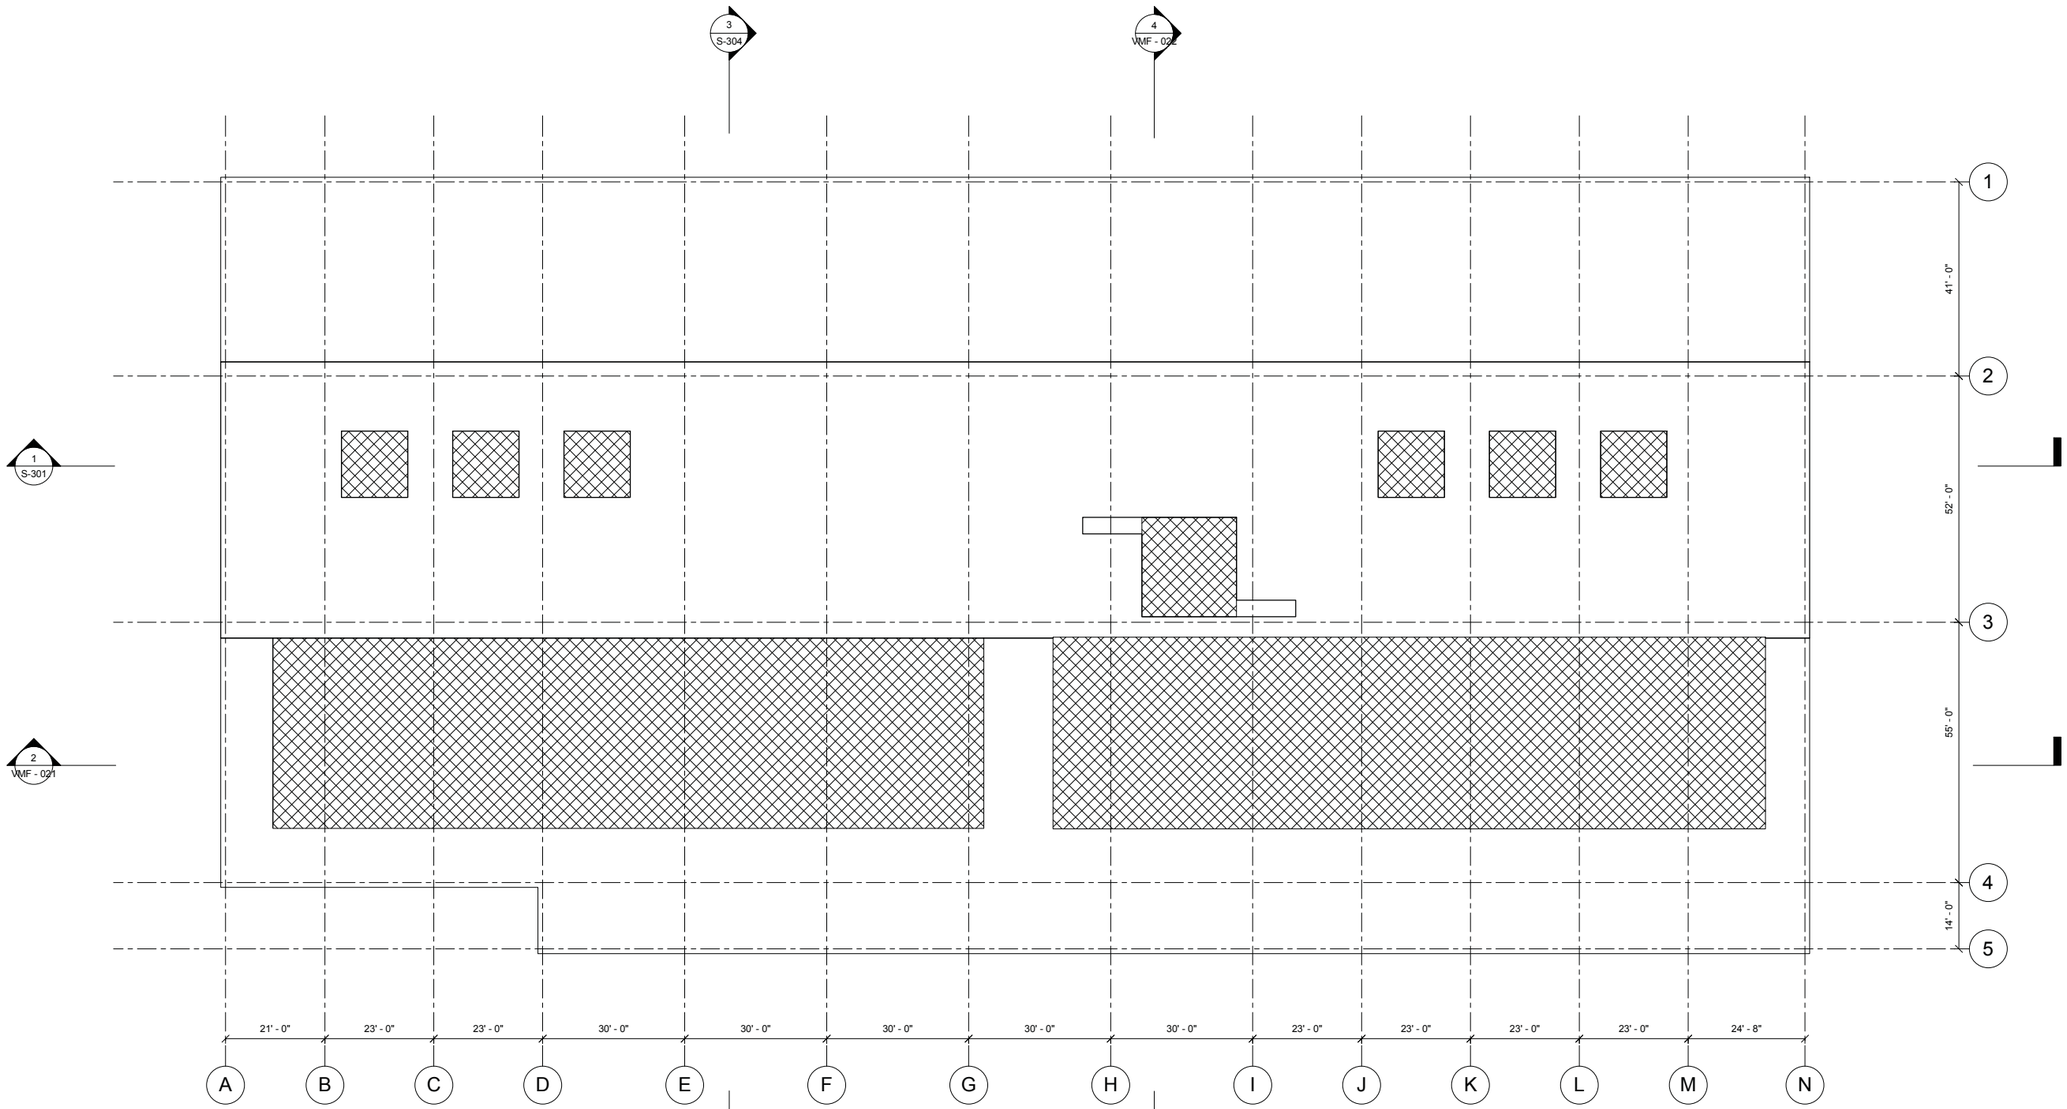

PIT SLAB PLAN

1/16" = 1'-0"

0 8' 16' 32'

LEGEND

2' THICK SLAB

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY
PIT SLAB PLAN


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-275.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	ZS	AD	ND	SHEET: VMF-017	

9/21/2017 1:58:45 PM
C:\Users\packarsj\Documents\VMF_S_3D0000_packarsj.rvt

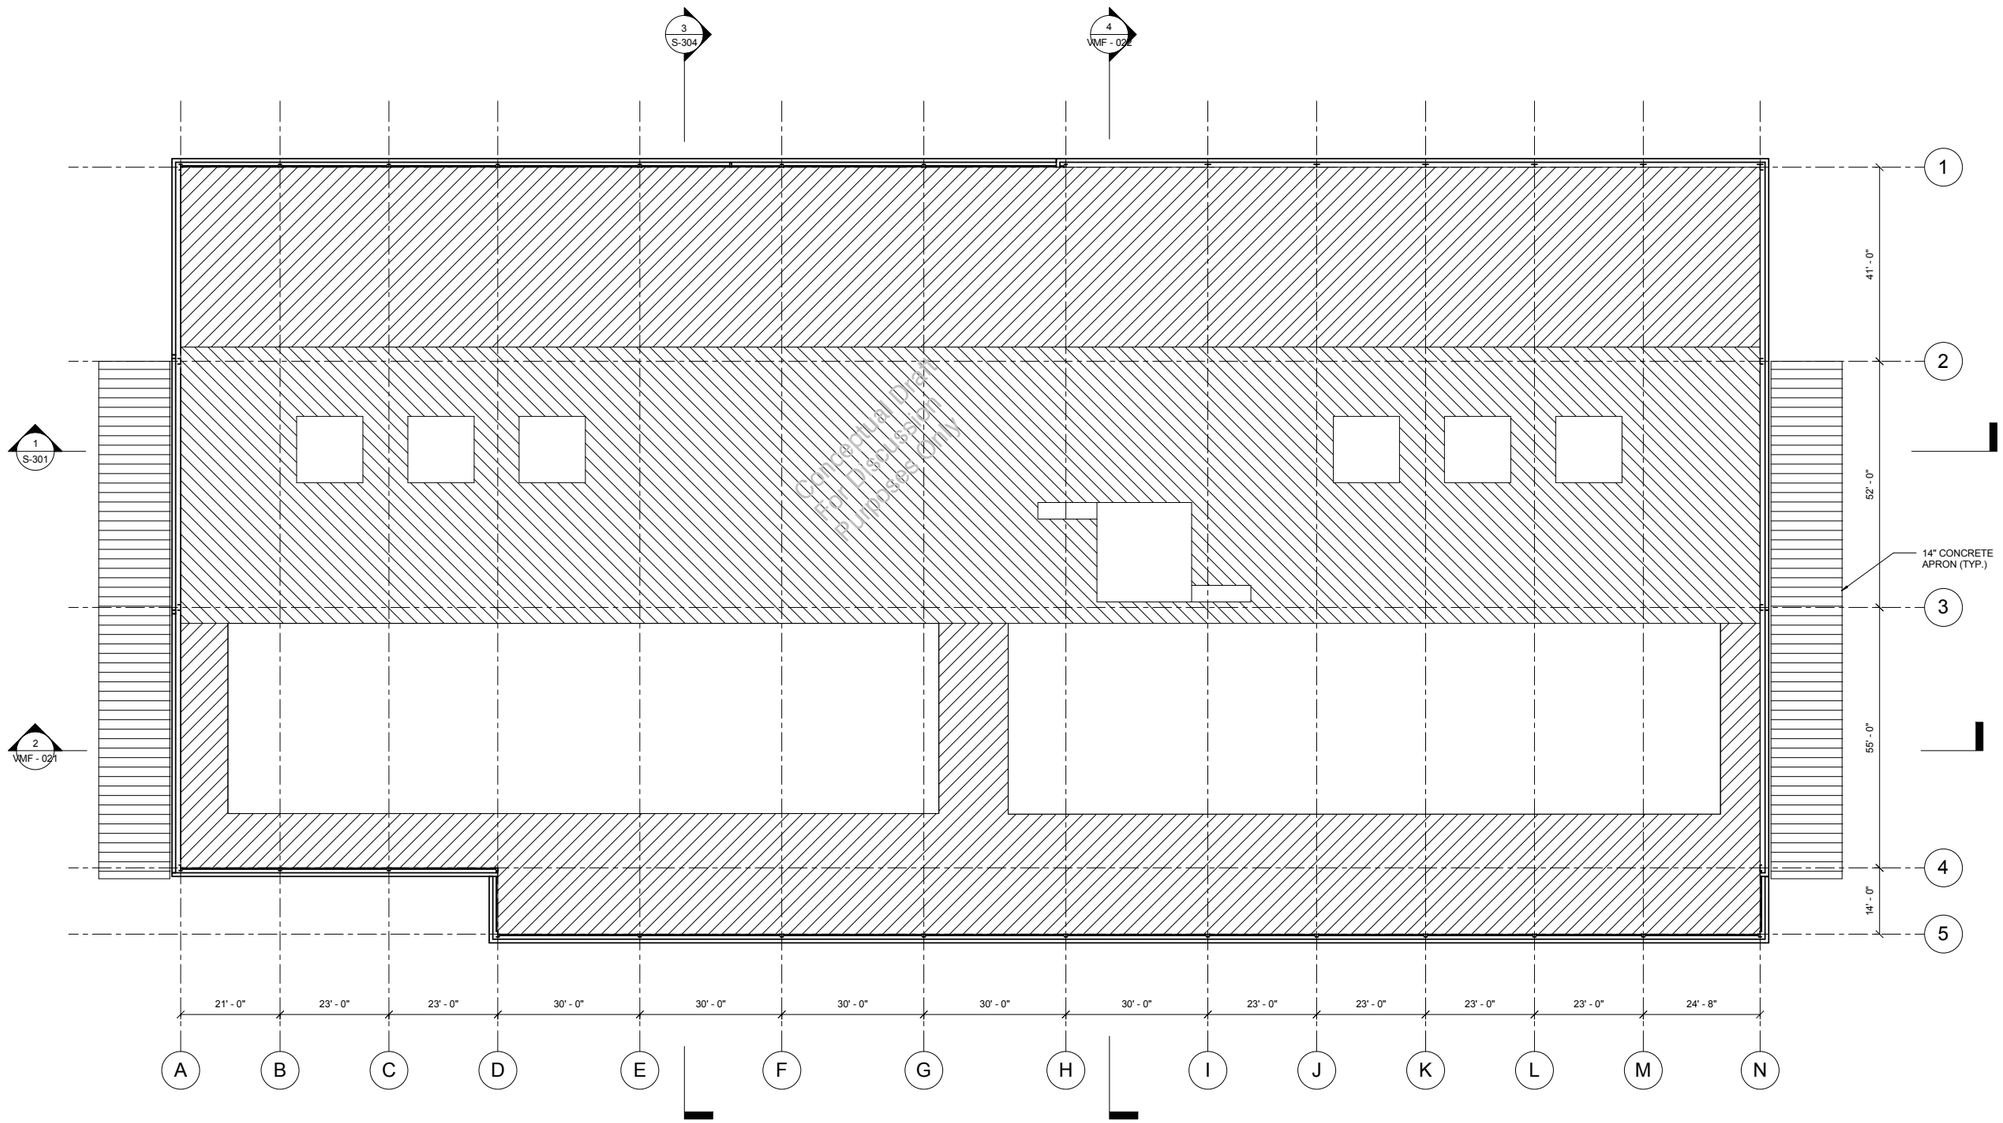

Contractual Drawing
For Display &
Purposes Only

MAIN FLOOR SLAB PLAN

1/16" = 1'-0"

0 8' 16' 32'

LEGEND

- 18" THICK SLAB
- 12" THICK SLAB
- 14" THICK SLAB

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY
MAIN FLOOR SLAB PLAN


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-275.pdf

ISSUE	DATE	DESCRIPTION	BY	CHKD	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	ZS	AD	ND	SHEET: VMF-018	

9/21/2017 1:58:46 PM
C:\Users\jackarsj\Documents\VMF_S_3D0000_jackarsj.rvt

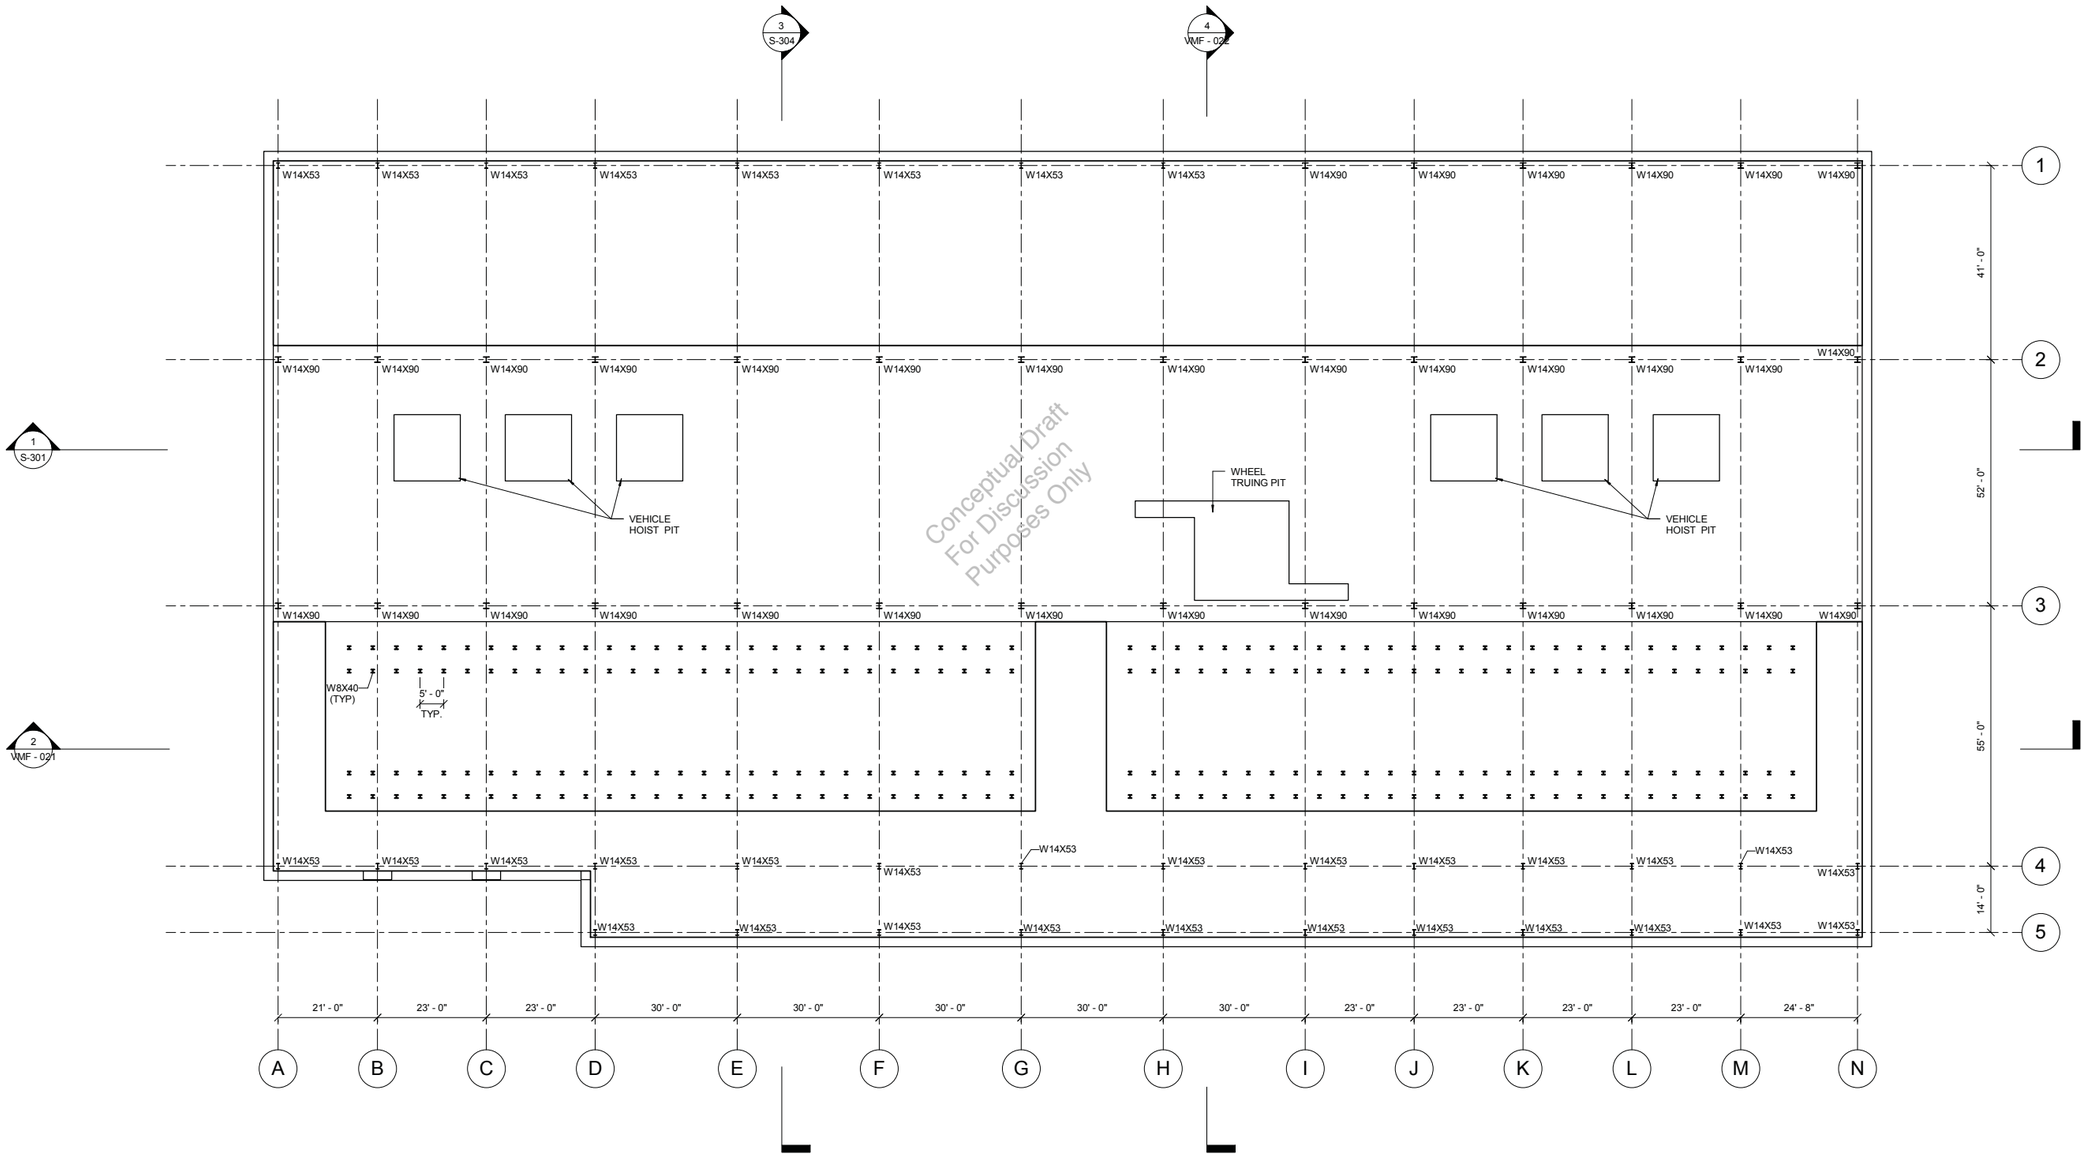

FRAMING PLAN

1/16" = 1'-0"

0 8' 16' 32'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


VEHICLE MAINTENANCE FACILITY
FRAMING PLAN
COLUMN AND TRACK PEDESTALS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-275.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	ZS	AD	ND	SHEET: VMF-019	

9/21/2017 1:59:47 PM
C:\Users\packarsj\Documents\VMF_S_3D0000_packarsj.rvt

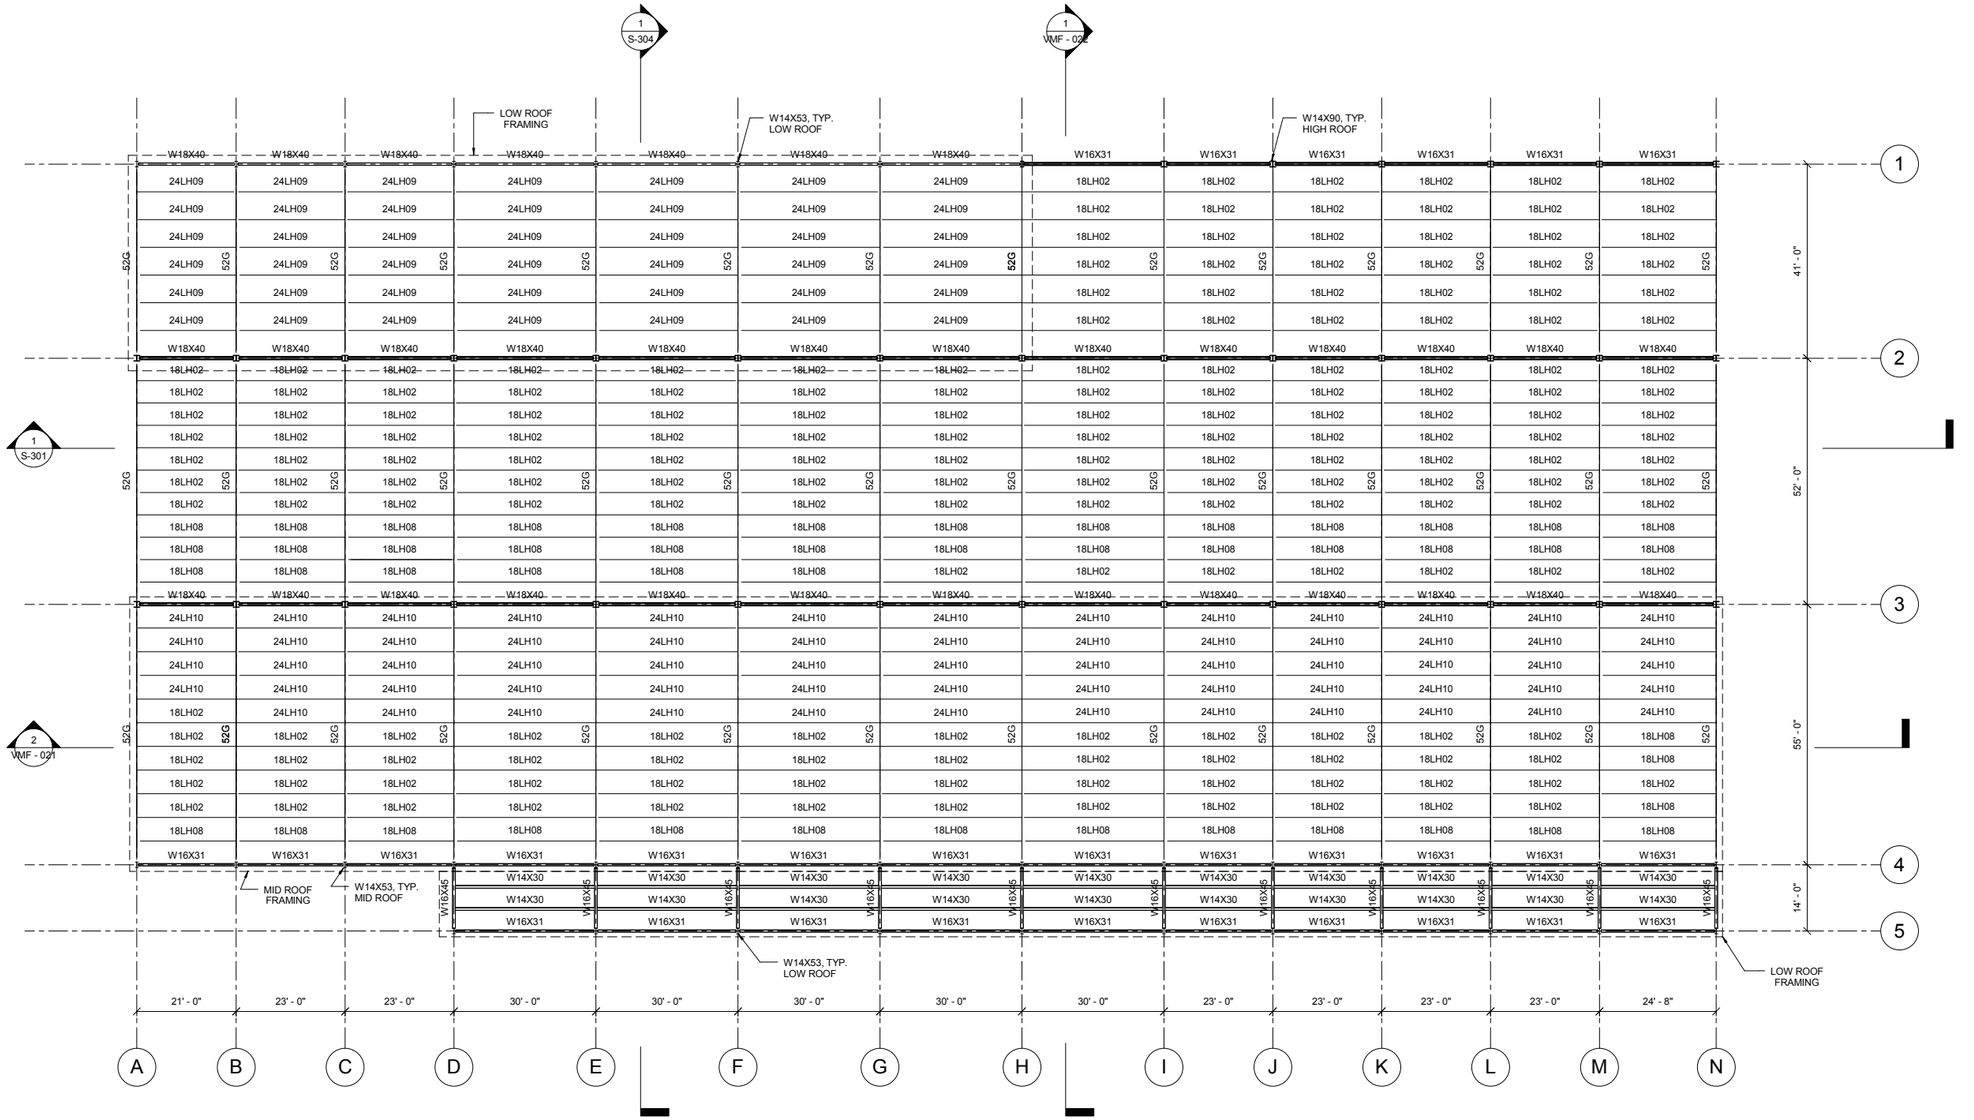

HIGH ROOF FRAMING PLAN

1/16" = 1'-0"

0 8' 16' 32'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


VEHICLE MAINTENANCE FACILITY
ROOF FRAMING PLAN

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-275.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	ZS	AD	ND	SHEET: VMF-020	


9/21/2017 1:58:48 PM
C:\Users\packarsj\Documents\VMF_S_3D0000_packarsj.rvt

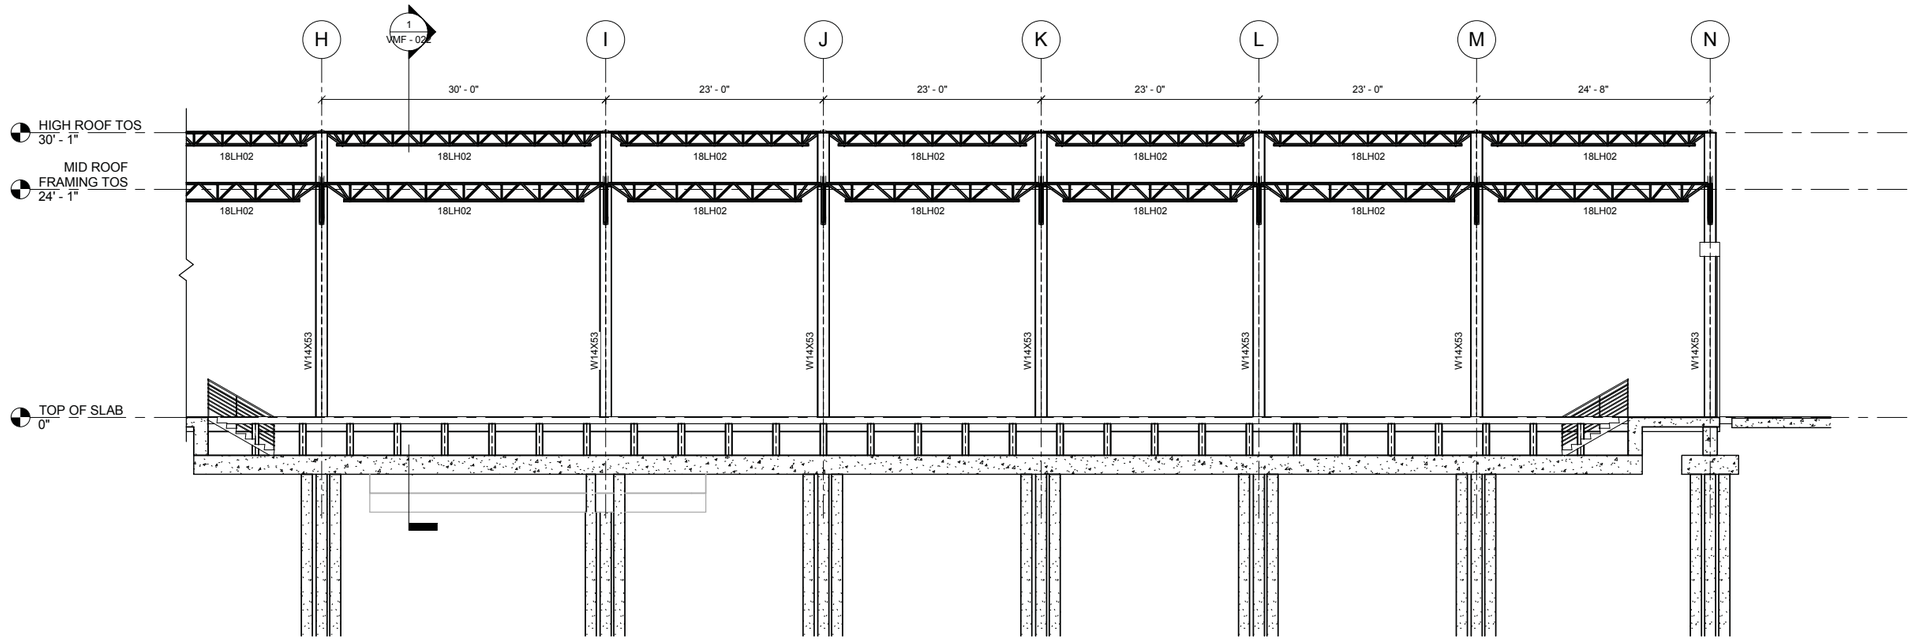

1 S-304 LONGITUDINAL SECTION PART A

1/8" = 1'-0"

0 8' 16' 32'

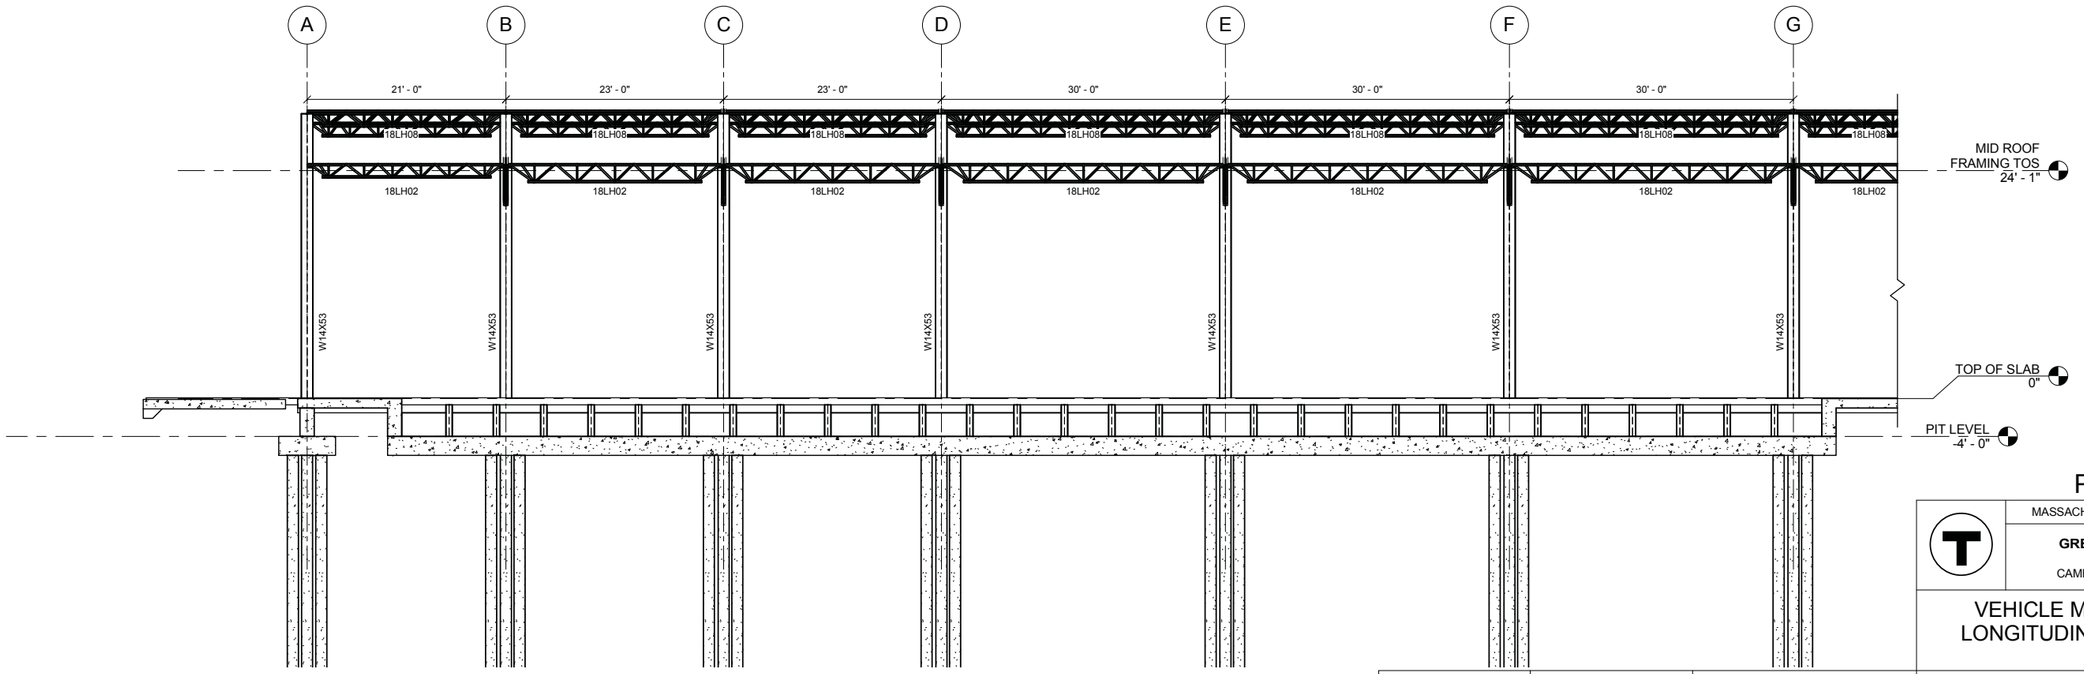

2 S-105 LONGITUDINAL SECTION PART B

1/8" = 1'-0"

0 8' 16' 32'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


VEHICLE MAINTENANCE FACILITY
LONGITUDINAL BUILDING SECTIONS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-275.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	ZS	AD	ND	SHEET: VMF-021	

9/21/2017 1:58:50 PM
C:\Users\packarsj\Documents\VMF_S_3D0000_packarsj.rvt

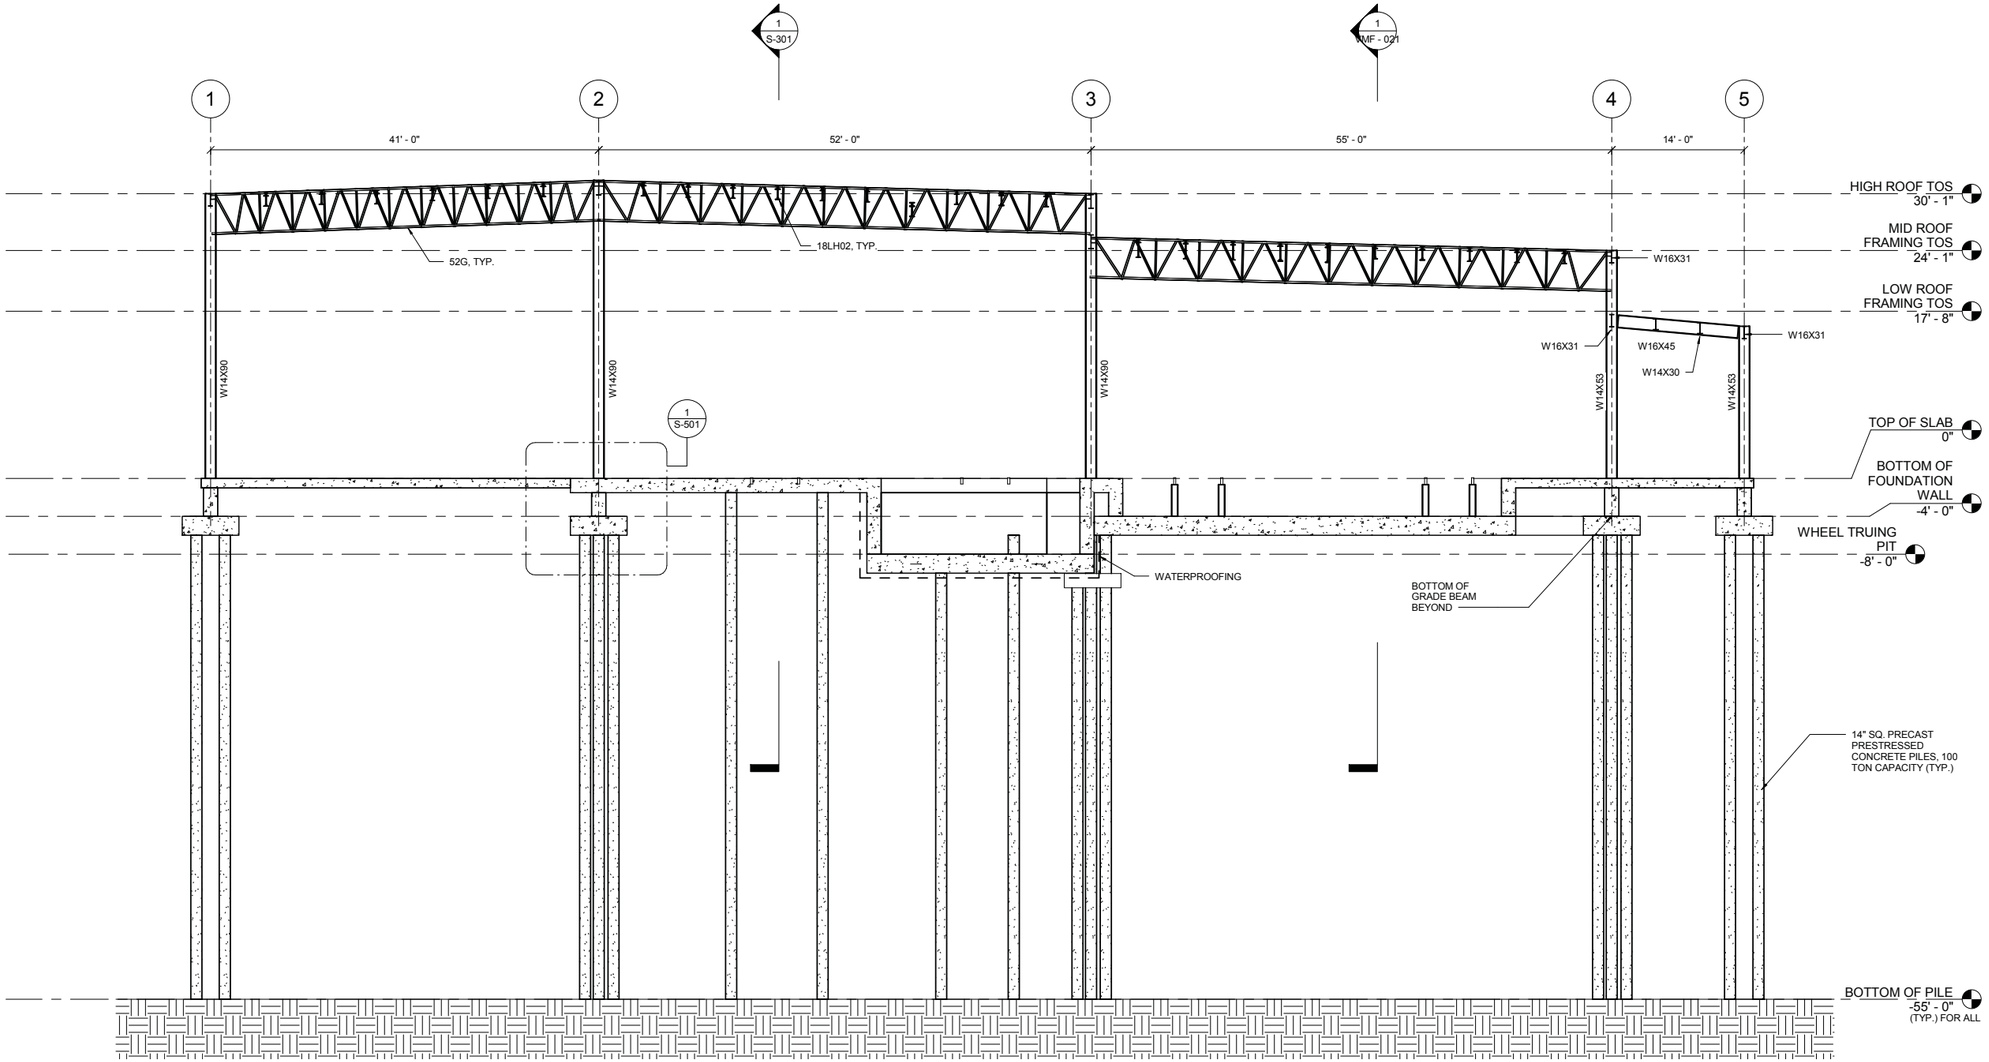

1 S-105 TRANSVERSE SECTION

1/8" = 1'-0"

0 4' 8' 16'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY
TRANSVERSE BUILDING SECTION


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-275.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	ZS	AD	ND	SHEET: VMF-022	

9/21/2017 1:58:51 PM
C:\Users\packars\Documents\VMF_S_3D0000_packars.rvt

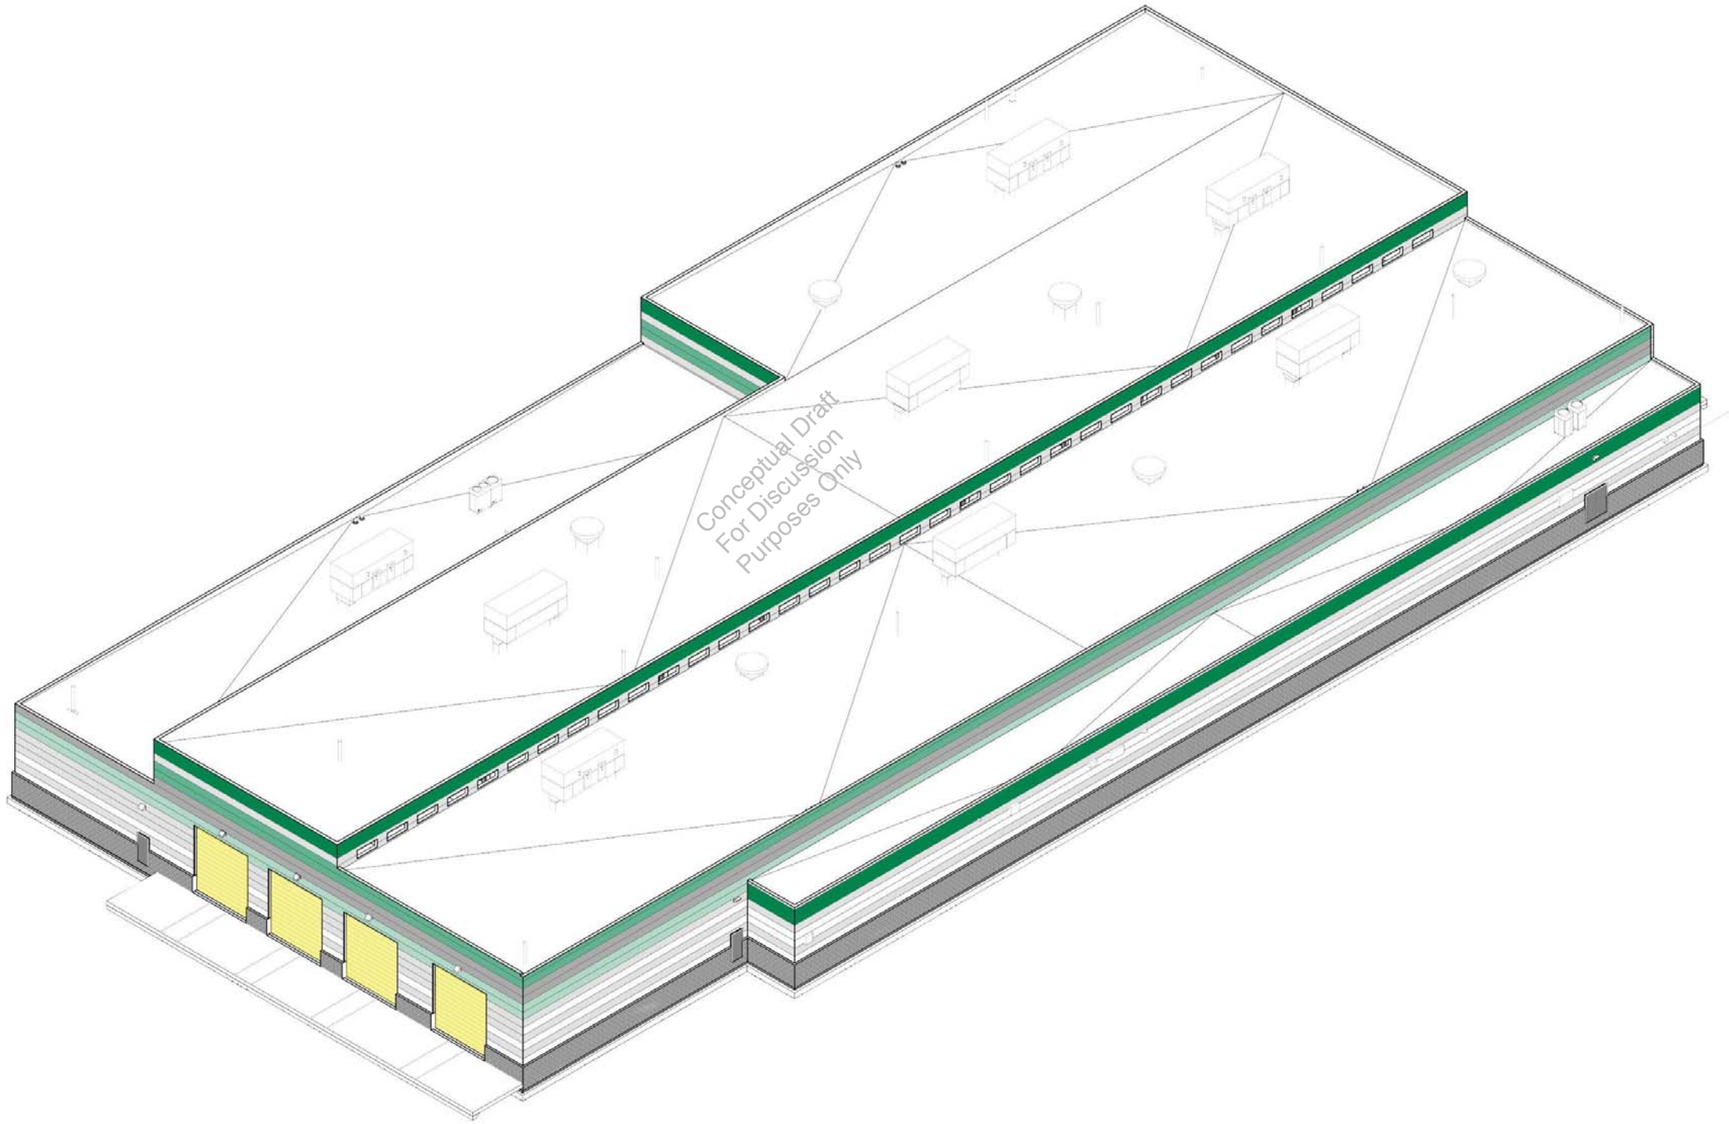

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY 3D REPRESENTATIONS AND ISOMETRICS

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-275.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE:	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	SP	SP	ND	SHEET: VMF-023	

6/28/2017 2:19:31 PM
C:\Users\packarsj\Documents\VMF_A_3D0000_packarsj.rvt

4.6 CIVIL AND GUIDEWAY

GLX Constructors has delivered a low cost design and construction solution for Civil and Guideway through a revised track and Community Path alignment that reduce work required to complete retaining walls, bridge spars, and track grades while avoiding conflicts with utilities and third parties. Our efficient design provides the MBTA greater certainty the Project will be completed on schedule

During the proposal process, we expended significant time and effort to optimize the design provided by the MBTA.

Our engineers focused on rail design to enhance our design accuracy. The proposed track center line alignments and top-of-rail profiles drive many heavy civil components of the Project, such as earthwork, grading, retaining walls, drainage, and cross-section development. Our efforts during the proposal phase will allow our team to accelerate the Project schedule.

> **Our team is composed of seasoned professionals to manage horizontal and vertical spatial constraints for the design of the track and all necessary civil components in support of the work.**

4.6.A APPROACH TO CIVIL AND GUIDEWAY COMPLIANCE

GLX Constructors has reviewed the Technical Provisions Section 10.1 and 10.2 and subsequent addenda to establish the project design criteria, which we used to cross check the provided Definition Plans and verify their compliance. The Technical Provisions served as the starting point for our proposed design enhancements and Alternative Technical Concepts (ATC).

During our evaluation, we identified several opportunities for optimization within the horizontal and vertical alignments and the special trackwork. The following is a summary of our findings.

Horizontal Track Alignment Revisions. We have revised the Project Definition Plan's horizontal alignments at many locations. All revisions generate cost savings, contributing to the MBTA's cost certainty goals without sacrificing quality or performance. Some of our revisions are Project improvements, noted below.

Horizontal Track Alignment Improvements	Technical Drawing
Revised the Medford Branch (MB) and New Hampshire alignments to eliminate impacts to the Walnut Street west abutment.	Sheets C-011 to C-012, C-035 to C-036
The MB north approach alignment to the East Somerville Station has been revised to reduce the Washington Street Bridge width.	Sheets C-009 to C-011
The MB alignments at the Gilman Station were revised to improve platform geometry by allowing it to be completely tangent. This allows for room for the required south elevator and stairs on the concourse, while eliminating ROW impacts just north of the Medford Street bridge.	Sheets C-012 to C-014, C-036 to C-038
The MB alignment at the Magoun Station was revised to improve platform geometry. It is now completely tangent and the platform edges parallel. This allows for room for the south elevator and the stairs on the station concourse. The MB-WB alignment centerline is only 6 feet from the ROW corner at Sta.312+50 in the Definition Plans. In this case, the ballast shoulder and emergency walkway would have been on the neighboring property. The revised alignment has been shifted to the east to allow room for the ballast shoulder and emergency walkway.	Sheets C-017 to C-018
The West Bound-MB north approach alignment to the Ball Square Station was revised to eliminate ROW impacts. The Definition Plans' alignment was only 5 feet from the ROW from Sta. 336+00 to Sta. 338+00. The ballast shoulder and emergency walkway would be on the neighboring property. The revised alignment has been shifted to the east to allow room for the ballast shoulder and emergency walkway.	Sheet C-020
The MB north approach alignment to the College Ave. Station was revised to reduce the height of the east retaining wall along Boston Ave.	Sheets C-023 to C-024
Both the east- and west-bound Union Square Branch alignments were revised at the eastern approach to the Union Square Station. This allows the platform to be tangent, instead of the curved platform as shown in the Definition Plans. Technical Provision Section 10.2.3.2 (c) (ii) (A) requires the horizontal alignments to be tangent through the entire platform.	Sheets C-030 to C-031
The VMF loop track's horizontal alignment was revised to improve the grading for the Third Avenue VMF entrance. This allows for a 5-foot raise of the VMF and Car Storage Yard track profiles that will substantially reduce the proposed grading excavation.	Sheet C-051

Figure 4.6-1. Horizontal Track Alignment Improvements. *The horizontal improvements that GLX Constructors have made will reduce Project costs and shorten schedule duration.*

Vertical Track Alignment Revisions. We have revised the Definition Plan's vertical alignments as noted below.

Vertical Track Alignment Improvements	Technical Drawing
The New Hampshire profile has been modified to minimize track undercutting, earth excavation, retaining wall heights, and other drainage related items. These profile revisions still allow for a minimum of 17.75' of vertical clearance under bridges to meet Technical Provision Section 10.1.3.5 (d) (i).	Sheets C-033 to C-049
The MB profile has been raised in various areas north of Washington Street to minimize excavation for the roadbed and retaining wall height.	Sheets C-010 to C-024
The MB and EB Union Square profiles have been lowered at the south half of the viaduct. The viaduct piers and columns constructed under an advanced contract will not be impacted by the lowered profiles. The revised profile will still meet the required 16.5-foot street vertical clearance for the bus loop driveway, as required by Section 8.7.3.9. The revised profile meets the 12.5-foot vertical clearance for the bus loop driveway, as required by Section 7.2.3.6 (a) (i).	Sheets C-003 to C-007, C-032

> **We have revised the horizontal and vertical alignments to capture cost savings and shorten project schedule.**

Vertical Track Alignment Improvements	Technical Drawing
The top of rail profiles were raised for the yard lead tracks, car storage tracks, and the VMF track. This 5-foot raise above the Definition Plans yard profiles decreases project earth excavation and retaining walls for the yard leads and car storage area. Large amounts of excavation from other project areas can also be used as fill within the VMF to meet the 5-foot raise and improve the balance of earthwork throughout the Project instead of trucking soil offsite.	Sheets C-053 to C-055

Figure 4.6-2. Vertical Track Alignment Improvements. *The vertical improvements that GLX Constructors have made will reduce Project costs and shorten schedule duration.*

Special Trackwork Revisions

We propose revising the track alignment with standard diamond crossovers.

Special Trackwork Improvements	Technical Drawing
The custom diamond crossover for the Union Square Station approach will be replaced with a standard #8 diamond crossover. The US-EB speed must be 15 mph, as the alignment travels through the diverging route of the custom #8 turnout of the diamond crossover. The standard diamond crossover will allow for a speed of 20 mph and is a project operational improvement.	Sheets C-030 to C-031
The Yard Lead 2 and Yard Lead 3 custom diamond crossover at the Brick Bottom Interlocking will be replaced with a standard #6 diamond crossover.	Sheets C-050, C-052

Figure 4.6-3. Special Trackwork Improvements. *Identified trackwork improvements will lead to cost certainty and operational efficiency.*

Track Construction Staging

We have developed track staging plans for the Washington Street Bridge Construction. Three stages have allowed for both mainline New Hampshire tracks and Yard Lead 10 to be in service at all times, except for a few weekend single-track operations.

By shifting the New Hampshire Line Tracks to allow for the new MB construction, we are proposing three stages. Each stage is roughly one-third of the New Hampshire Line length and will involve some relaying of the exiting track material. We anticipate very little impact to the commuter operations during this shifting work.

The MB Construction will have conventional construction staging after the New Hampshire Tracks are shifted to the east. Following, the MB construction will have little impact to train operations.

The Union Square Branch construction will also have conventional staging. The existing Fitchburg tracks will be relocated out of the Union Square Branch by an advanced contract. The Union Square construction will have little impact to train operations.

Features, Rationales, and Limitations of Alignment Design Elements

GLX Constructors has made significant improvement to of the features and rationale of the alignment design elements.

Design Speed. The design speeds are the same as the provided by the Definition Plans.

Transitions between the Various Track Bedding Types. Using ballasted deck bridges, the transitions will be eased between fill and structure. To prevent differential settlement, we will use approach slabs at the Harvard Street Bridge on the New Hampshire Line and at the Medford Street Bridge on the Union Square Branch.

Clearance Envelope. Our design complies with the minimum clearance envelopes for the Commuter Line and Light Rail Branches, as specified in the Technical Provisions. The only exception is where the Definition Plans deviate from clearance at Sta. 10+75 (Horizontal clearance of 6.25 feet). This exception is required for the Fitchburg Line work, which is not part of the Green Line Extension Contract. See Sheet C-028.

Line of Sight. Proper lines of sight safely provide greater reaction times for the vehicle operators. The Project will be designed to allow for maximum lines of sight. Proposed Green Line signals will be placed free of obstruction and clearly in the operator's line of sight per the Project's Technical Provisions, Section 11.

Approaching Stations. Our team will realign the track approaches to the East Somerville, Gilman, Magoun, Ball Square, College Avenue, and Union Square Stations. These changes improve the platform geometry, allow for the proposed elevators stairs to fit on the approach concourses, and eliminate ROW issues. Our designs speeds are the same as the Definition Plans at the station approaches.

Structural Crossings. Our design meets all vertical clearances at all of the grade-separated crossings along the Project alignment.

Special Track Work. GLX Constructors has used the same turnout sizes as the Definition Plans. The minimum mainline turnouts are to be #8 per Technical Provision 10.2.3.3 (k) (iii). A #10 left-hand mainline crossover was used on the Union Square Branch in the Definition Plans.

Definition Plans called for #6 Crossovers at the East Somerville Interlocking and a #6 turnout for the US-EB track connection to the Yard Lead 4. These are smaller than standard sizes on the mainline tracks because of constricted geometry. GLX Constructors will use the same turnouts at these locations as the Definition Plans.

The mainline crossovers at Sta. MB-EB 210+ and Sta. MB-EB 319+00 can be modified #6 hand-throw electric lock per Technical Provision 10.2.3.3 (k) (vii).

Yard Lead crossovers are #6 turnouts per Definition Plans and meet MBTA track standards. These are non-revenue tracks. See Sheets C-050 and C-052. The Yard Turnouts are a minimum 150-foot curve radius, Fully Guarded per Technical Provision 10.2.3.3 (n) (iii) the same as the Definition plans.

There is no new special trackwork on the New Hampshire Line along the Project.

Geometric Horizontal and Vertical Alignment Design Brief

GLX Constructors has implemented a number of changes in both horizontal and vertical alignment that will result in construction or operational cost savings and overall Project improvements. Each modification was developed in accordance with the Technical Provisions.

Conducting a thorough proposal review of the geometric alignments, we identified new and exciting design exceptions. Improving on existing geometry, 12 design exceptions detailed within Appendix 1 – Design Criteria Exceptions – Track, prepared by AECOM/HNTB, Dated 11-21-2014, were carried over, and 21 additional design exceptions are required because of existing structures, geography, and grading plans.

“To mitigate the impact to abutters and many important businesses around the Green Line, we will employ a philosophy of avoid, minimize, or mitigate.

The 12 exceptions carried over apply to the light rail system and include five locations along Union Square branch, where minimum horizontal or vertical tangent track lengths cannot be met because of profile grading and/or Right of Way (ROW) constraints. Six of the remaining seven exceptions reference Volume 2 Technical Provisions, Section 10.2.3.2.c.iii.B, and exceed the maximum unbalance of 0.50 inches, two of which are designated as OPEN within AECOM/HNTB Attachment A (#68 and #69). These are no longer relevant because our improved design reduces the unbalance at these curves below the maximum of 0.50 inches.

The additional 21 exceptions identified by GLX Constructors include similar scenarios where maximum vertical or horizontal tangent track cannot be met, curve sections of track are within the minimum 45-foot tangent section of track from platform edge, or curve unbalance super elevation exceeds the maximum of 0.50 inches.

Of the additional 21 exceptions, several exceptions are required based on existing/provided alignment geometry that was not identified in the AECOM/HNTB Attachment A, dated 11-21-2014. These exceptions are in relation to minimum track spacing, one located within the MB Viaduct and the other exception required for the commuter rail, where it is required to blend into existing track territory along New Hampshire from Station 87+17 to Station 89+16. Two other track spacing design exceptions are required because of existing site constraints and interference with the ROW, which prohibits additional centerline spacing with incremental inches required by super elevation and degree of curvature.

We have compiled an extensive list of exceptions that might possibly be needed during final design and for brevity have included three of them below as an example.

COMMUTER AND LIGHT RAIL DESIGN EXCEPTIONS			
Element	**Description**	**Ref. Sect**	**Ref. Doc.**
Light Rail	The tangent preceding MAF turnout 10 (PS SW – 25+23.54) is 8.15 feet due to alignment	1.6.2.1.6	GLX Design Criteria Manual
Light Rail	Curve US-WB 2 – Required speed of 25 MPH results in an unbalance superelevation of greater than the maximum allowable 0.5 inches. Superelevation cannot be increased without impact to #10 turnout east of curve or running off superelevation on tangent. Proposed unbalance superelevation for this curve shall be 0.60 inches.	1.6.2.1.4.3B	GLX Design Criteria Manual
Light Rail	The tangent preceding MAF turnout I3 (PC Sta= 27+81) is 1.7 feet due to alignment constraints	1.6.2.1.6	GLX Design Criteria Manual

Figure 4.6-4. Commuter and Light Rail Design Exceptions. *An example of the commuter and light rail design exceptions.*

For features of alignment segments that confirm compliance with the geometric criteria of the Volume 2 Technical Provisions, see Section 4.6.A.

Design Approach and Criteria of the Wayside Elements

Coordination and integration are two key measures in the wayside design approach. In a tight corridor, such as the Green Line, every decision to place a structure or element along the ROW will have an impact on other disciplines. For example, the location of the OCS poles will impact the placement of signals, since the location of OCS can cause sight line issues with the LRV operator seeing a wayside train control signal.

The OCS pole layout will be closely coordinated with our Civil Team; to avoid clashes with drainage and underground structures during construction. There will be a hierarchy of precedence for wayside items along the ROW; we will build items such as walls, bridges, and other large structures first because they take the highest priority of location.

Utilities will be next. Items like culverts, drainage pipe, and pump stations are driven by the topology of the ROW and have some adjustability, but they must be designed early and cannot be revised once the design is complete. The system elements, OCS poles, ductbanks, troughs, CIH, and signals have the most flexibility in terms of their location. Once all civil and structural items have been preliminarily located, the systems group will analyze the remaining property and design the systems around available property.

With close Design-Build coordination conflicts will be identified early, formally tracked, and resolved to provide a fully coordinated and integrated light rail corridor.

Conduit Provisions for System Installation. Conduit provisions of systems along the ROW will be a system-wide trough for the installation of

communication and train control cables. Junction boxes will be installed to break the cables out of the trough and route the wayside devices. There will be spare capacity built into all conduit installations per the Technical Provisions. Aerial cabling will also be used along the corridor to minimize impacts to sub-surface work. For example, to maintain two separate paths for the communications fiber path, one run will be in the trough and a second will be aerial along the OCS poles. Conduit provisioning along the corridor will allow no more than 40 percent fill for the conduit, and it will be fully compliant with the Technical Provisions, Section 7.4.

Civil Infrastructure Installed in Support of the Signaling and Communications Equipment and Electrification

To maximize construction and minimize impacts on schedule, our Civil Infrastructure Team will install conduits and foundations for the signaling, power, and communications equipment along the ROW. The coordination between Civil Infrastructure and System Teams will limit excavation during the early stages of design on the Green Line Extension. We will install the infrastructure for systems elements to avoid subsurface work after final grade has been established or sub-ballasts have been placed. The intent is to dig once, and then work vertically from the ground.

Community Path Continuous Plan and Profile Drawings. The proposed community path will create a pedestrian and cyclist path that is a continuation of the existing path that terminates just south of the Lowell Street Bridge. The community path will provide a conduit for users between the existing path and the sidewalk at Washington Street, Somerville. The design will be in accordance with the FHA, AASHTO, and MUTCD guidelines pertaining to bicycle facilities and trails. The community path is designed to be ADA/MAAB accessible with maximum longitudinal grades no greater than 5 percent, and cross slope grading less than 2 percent, with a minimum grade of 0.5 percent while maximizing pedestrian and cycle comfort.

The community path's 10-foot width with 1-foot-wide shoulders will enhance the cyclist experience and will prevent cyclists and pedestrians from feeling constrained along the path. Grading the community path is partially dictated by meeting the existing grades at the roadway bridge and sidewalk crossings at Central Street, Sycamore Street, and School Street, and crossing beneath Medford Street and Walnut Street in underpass structures.

We will achieve the community path's positive drainage by pitching flow across the impervious travel surface toward the pervious shoulder and collecting runoff in subsurface perforated pipes and inlet structures that will combine with track drainage. The grading design requirement also allows for shedding drainage flow efficiently from the community path's travel surface and eliminating areas of ponding. Where necessary, the community path will be elevated above the proposed track and wayside elements by viaduct structures.

We will provide lighting at key locations, such as connection points at the existing roadway bridges and at underpass structures, at illumination levels to provide a safe environment for all users. For user safety, emergency call boxes will be provided at a maximum spacing of 1,000 feet with at least one call box located strategically between all path access points and at all underpasses. Other safety features include removable bollards with locks at all vehicle access points, which prohibits unauthorized vehicles from accessing the community path and 1-foot-wide shoulders with either guard rail or railings with a rub rail to keep cyclists and emergency responder vehicles from veering too close to the track-side edge of the path.

The GLX Constructors Civil Infrastructure and Structural Guideway Team coordination efforts will be critical to every discipline providing wayside elements. GLX Constructors has been organized as a fully integrated design build team in order to share critical design information. Our guideway design provides the operational flexibility afforded by the constrained corridor while maintaining rider comfort and convenience. Safety is paramount to us and to the MBTA, so systems maintenance activities to support rider safety will be well-thought throughout and coordinated from design to revenue operations.

While the guideway connects to all communities of Boston, the community path unites the local surrounding communities. The path will create a direct route between the Magoun Square and the Washington Street/East Somerville areas for commuters and recreational users. The community path will be a safe and comfortable route in a congested urban setting. It will provide another means of transit and access for residents and visitors to connect to existing local businesses and other community amenities, such as the Somerville YMCA, City Offices, and the High School – all in close proximity to the School Street connection or the Hoyt-Sullivan Playground.

"Wayside element coordination has already begun and will continue through construction. These elements include stations; VMF yard and building; TPSS sites and buildings; bridges and viaducts; utilities, including OCS and signal structures; community path; ROW access; and maintenance road requirements.

ITP Request	RFP		
	Drawing Number	Drawing Title	Reference Section or Drawing
A5.2.6.B.1	C-001 to C-057	Titles included on the Attached Drawings	
A5.2.6.B.2	C-003 to C-024; C-026 to C-032; C-033 to C-049, C-053 to C-055		
A5.2.6.B.3	C-001 to C-002; C-025		4.1(SYS-005 and SYS-006)
A5.2.6.B.4	C-001 to C-002; C-025		
A5.2.6.C.1	C-001 to C-057		
A5.2.6.C.2	C-003 to C-024; C-026 to C-032; C-033 to C-049, C-053 to C-055		

Technical Solutions Drawing Matrix.

APPENDIX 1

Design Criteria Exceptions – Track

COMMUTER AND LIGHT RAIL DESIGN EXCEPTIONS

Prepared By: STV Inc. | Date: 9/25/2017

Element	Item #	Description	Reference Section(s)	Reference Documents	Status	Date	Last Name (Print Initials)
Existing AECOM/HNTB							
Light Rail	27	The crossovers East of College Ave and Union Square Stations contain non-standard crossover configurations utilizing mainline moves through the diverging side of the crossover. UPDATE 1/27/14: union square issue closed.	N/A	GLX Design Criteria Manual	OPEN	8/6/13	E. DiVirgilio (AECOM/HNTB)
Light Rail	53	The tangent preceding MAF turnout 10 (PS SW—25+23.54) is 8.15 feet due to alignment	1.6.2.1.6	GLX Design Criteria Manual	OPEN	10/11/13	E. DiVirgilio (AECOM/HNTB)
Commuter Rail	65	The 4 foot high interlock fence between the commuter rail and light rail tracks was placed at 8.5 feet from the commuter rail track centerline in the ACD design plans. This dimension does not allow for an increase in clearance due to curvature and superelevation, as required by the MBTA CRDSM. Please clarify the clearance requirement for intertrack fence	6.C.2	Commuter Rail Design Standards Manual (CRDSM)	OPEN	12/16/13	E. DiVirgilio (AECOM/HNTB)
Light Rail	68	Curve US-WB 2 - Required speed of 25 MPH results in an unbalance superelevation of greater than the maximum allowable 0.5 inches. Superelevation cannot be increased without impact to No. 10 turnout east of curve or running off superelevation on tangent Proposed unbalance superelevation for this curve shall be 0.60 inches.	1.6.2.1.4.3B	GLX Design Criteria Manual	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Light Rail	69	Curve US-WB 3 - Required speed of35 MPH results in an unbalance superelevation of greater than the maximum allowable 0.5 inches. This was done to comply with an MBTA comment requesting spirals be made longer than the minimum. Proposed unbalance superelevation for this curve shall be 0.72 inches.	1.6.2.1.4.3B	GLX Design Criteria Manual	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Light Rail	76	18” minimum ballast shoulders are required by the design criteria. 12” ballast shoulders on the high side of superelevated double track sections are required on the viaduct due to 11.5 track centers. See IGMP-04 sheet 000-K-1000 for additional information.	1.6.2.2.3.5	GLX Design Criteria Manual	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Light Rail	80	The tangent preceding MAF turnout l3 (PC Sta= 27+81) is 1.7 feet due to alignment constraints	1.6.2.1.6	GLX Design Criteria Manual	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Commuter Rail	81	YARD 10 horizontal curves PAR-02, PAR-07, and YL-105-01 are less than 100 ft. in length. These are yard curves and the criteria is intended for mainline curves. Curve lengths less than 100 feet are an existing condition within the yard. The track layout has been approved by Pan-AM.	3.C.3	Commuter Rail Design Standards Manual (CRDSM)	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Commuter Rail	82	YARD 10 horizontal tangent lengths between curves PAR-01/02 and also at the connection existing track east of Cobble Hill cad are less than the design criteria minimum of 40 ft. The short tangent lengths are an existing condition. The track layout has been approved by Pan-AM	1.C.1.B	Commuter Rail Design Standards Manual (CRDSM)	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Commuter Rail	83	YARD 10 grades are greater than the maximum allowable storage track grade of 0.25%o. This is an existing condition within the yard.	3.C.5.B	Commuter Rail Design Standards Manual (CRDSM)	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Light Rail	84	The concrete curb supporting OCS poles on the viaduct structure adjacent to the outside of curve US-EB 1 provides 6 feet of horizontal clearance. The minimum allowable clearance is 6.26 ft. accounting for end overhang. The clearance provided is essentially the minimum less 3 inches of running clearance.	DWG 125	MBTA MOW Standard Plans	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Light Rail	85	The minimum allowable clearance between track centerline and OCS poles is 6’-6”. The minimum designed clearance to OCS poles within the LRT maintenance yard is 6’-2”, where track centers are spaced at 13’-4”. This is necessary to provide walkways without OCS poles where track centers are spaced at 18’-0”.	1.6.2.1.7.3	GLX Design Criteria Manual	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)

COMMUTER AND LIGHT RAIL DESIGN EXCEPTIONS

Prepared By: STV Inc. | Date: 9/25/2017

Element	Item #	Description	Reference Section(s)	Reference Documents	Status	Date	Last Name (Print Initials)
Light Rail	86	The distance from track centerline to edge of all curved station platforms are designed to be a constant horizontal offset of 4'-9". The curved platforms at Lechmere, Union, and Ball Square (future extension) Stations are adjacent to curves that have vehicle inswing and outswings of less than 2", which means the vehicle will not strike the low-level platform. Maintaining a uniform offset will simplify fabrication and construction of the station platforms.	1.6.2.1.7.3	GLX Design Criteria Manual	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Light Rail	88	The future platform is adjacent to the WB track at Ball Square Station platform is in a horizontal spiral due to corridor right of way constraints.	1.6.2.1.4.2	GLX Design Criteria Manual	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Light Rail	89	Site constraints within IGMP-04 do not allow space for the LRT maintenance walkway (defined as 30 inches beyond the clearance envelope) on both sides of the track bed at the locations noted in the attached plan.	1.6.2.1.7.3	GLX Design Criteria Manual	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Light Rail	91	The design criteria states that derails are required on all yard leads to prevent vehicles from inadvertently entering the mainline. Derails are not proposed on Yard Leads 1, 2, 4, and 5 because the prevailing grade of these tracks is down and away from the mainline and therefore the project team considers the derails unnecessary.	1.6.2.2.10	GLX Design Criteria Manual	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Light Rail	92	The design criteria states that derails are required on all tail tracks. The MBTA does not currently require derails on tail tracks.	1.6.2.2.10	GLX Design Criteria Manual	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
Light Rail	92	The wall mounted signal at Sta. US-EB 16+62 is located 5'-9" from track centerline. The minimum distance per the design criteria is 6'-6". The wall location is set to maintain continuity of the noise barrier on the US-WB viaduct. The track cannot be shifted away from the signal without impacting adjacent property and violating emergency egress requirements. The signal clears the dynamic envelope of the train with 3 inches of running clearance.	1.6.2.1.7.3	GLX Design Criteria Manual	OPEN	11/21/14	E. DiVirgilio (AECOM/HNTB)
NEW / FROM STV PLANSET							
Light Rail	STV-1	Lechmere Station platform is in a horizontal curve and does not meet the requirements for tangent length beyond ends of platform due to site constraints. Horizontal Curves: MB-EB 1, MB-EB 2, MB-WB 1, MB-WB 2. **(#16 CLOSED - 10/11/13) Change to Alignment 7/20/17**	10.2.3.2.c.ii.B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-2	Lechmere Station platform does not meet the requirements for Vertical tangent length beyond end of platform MB-EB/WB, east of the station. (PVI=186+85)	10.2.3.2.d.iii	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-3	Curve MB-EB 2 and MB-WB 2 - MBTA requested speed increase to 25 MPH results in an unbalance superelevation of greater than the maximum allowable 0.5 inches. Maximum unbalance superelevation for this curve shall be **1.18 inches (new)**. **(#55 CLOSED - 10/11/13) Change to Max Unbalance 7/20/17**	10.2.3.2.c.iii.B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-4	The length of the MB-EB & WB vertical curve (PVI=Sta198+25) does not meet the length required for combined horizontal and vertical curves. @100A, Min LVC=222.5 Ft, x1.5 = 333.75 Ft. Curve design is 300 Ft.	10.2.3.2.d.iv.D	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-5	Curve MB-EB 4 - unbalance superelevation of 0.6 inches is necessary to shorten the spiral length to prevent a conflict with the US-EB turnout, Curve MB-WB 4 is 1.5 inces. This results in an unbalance superelevation of greater than the maximum allowable 0.5 inches. Maximum unbalance superelevation for this curve **MB-EB 4 is 0.59 inches (new), and curve MB-WB 4 shall be 0.55 inches (new). (#56 CLOSED 10/11/13) Change to Max Unbalance 7/20/17**	10.2.3.2.c.iii.B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-6	The length of the MB-EB & WB vertical curve (PVI=Sta210+35.61) does not meet the minimum length or required length for combined horizontal and vertical curves. @100A, Min LVC=393.5 Ft, x1.5 = 590.25 Ft. LVC design is 300 Ft.	10.2.3.2.d.iv	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE

COMMUTER AND LIGHT RAIL DESIGN EXCEPTIONS


Prepared By: STV Inc. | Date: 9/25/2017

Element	Item #	Description	Reference Section(s)	Reference Documents	Status	Date	Last Name (Print Initials)
Light Rail	STV-7	The length of the MB-EB & WB vertical curve (PVI=Sta221+51.33) does not meet the minimum length for vertical curves. @100A, Min LVC=326.5 Ft. LVC design is 230 Ft.	10.2.3.2.d.iv	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-8	East Somerville Station platform does not meet the requirements for tangent length beyond end of platform MB-EB, east of the station due to corridor right of way constraints and MB-WB, West of the station.	10.2.3.2.c.ii.B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-9	Curve MB-EB 11 has an unbalance superelevation of greater than the maximum allowable 0.5 inches. Maximum unbalance superelevation for this curve shall be 0.51 inches (new).	10.2.3.2.c.iii.B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-10	The length of tangent track between curves MB-WB 11 and MB-WB 12 does not meet the minimum length requried for tangent track between curves. Min. Tangent length between curve sections shall be 60 Ft. Minimum tangent between MB-WB 11 and MB-WB 12 is 51.13 Ft.	10.2.3.2.c.ii.A	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-11	Gilman Square Station platform does not meet the requirements for tangent length beyond end of platform MB-WB, east of the station due to corridor right of way constraints.	10.2.3.2.c.ii.B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-12	Gilman Square Station platform does not meet the requirements for Vertical tangent length beyond end of platform MB-EB/WB, east of the station. (PVI=270+75)	10.2.3.2.d.iii	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-13	Magoun Square Station platform does not meet the requirements for tangent length beyond end of platform MB-EB and MB-WB, east of the station. MB-EB to the west.	10.2.3.2.c.ii.B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-14	Magoun Square Station platform does not meet the requirements for Vertical tangent length beyond end of platform MB-EB/WB, east of the station. (PVI=305+39.91)	10.2.3.2.d.iii	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-15	Ball Square Station platform does not meet the requirements for tangent length beyond end of platform MB-WB, West of the station.	10.2.3.2.c.ii.B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-16	College Ave. Station platform does not meet the requirements for tangent length beyond end of platform MB-EB and MB-WB, east of the station.	10.2.3.2.c.ii.B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-17	The Vertical tangent to the west of Crossover No. 8 (MB-EB PS Sta 362+99.85) is 5.15 feet due to alignment constraints	10.2.3.2.e	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-18	The Horizontal tangent preceding MOD US-WB turnout 10 **(MB-WB PS Sta 207+07.16/ US-WB PS Sta 0+00)** is 23 feet due to alignment constraints. Tangent length preceding the switch of less than the 30 foot minimum, but greater than the absolute minimum of 12 feet, due to alignment **(#22/23 CLOSED - 10/11/13) Change to Alignment 7/20/17**	10.2.3.2.e	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-19	The Vertical tangent preceding MOD US-WB No. 10 Turnout **(MB-WB PS Sta 207+07.16/ US-WB PS Sta 0+00)** is 23 feet due to alignment constraints. Tangent length preceding the switch of less than the 30 foot minimum, but greater than the absolute minimum of 12 feet, due to alignment **(#22/23 CLOSED - 10/11/13) Change to Alignment 7/20/17**	10.2.3.2.e	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-20	MOD US-WB No. 10 Turnout (MB-WB PS Sta 207+07.16/ US-WB PS Sta 0+00) is located in the following vertical curve US-WB PVI 1+63.89. Turnout extends into the vertical curve	10.2.3.2.e	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-21	Curve US-WB I - MBTA requested speed increase to 15 MPH results in an unbalance superelevation of greater than the maximum allowable 0.5 inches. Maximum unbalance superelevation for this curve shall be **1.53 inches (new)**. **(#62 CLOSED - 10/11/13) Change to Max Unbalance 7/20/17**	10.2.3.2.c.iii.B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE

COMMUTER AND LIGHT RAIL DESIGN EXCEPTIONS

Prepared By: STV Inc. | Date: 9/25/2017


Element	Item #	Description	Reference Section(s)	Reference Documents	Status	Date	Last Name (Print Initials)
Light Rail	STV-22	Curve US-WB 4 - MBTA requested speed increase to 35 MPH results in an unbalance superelevation of greater than the maximum allowable 0.5 inches. Maximum unbalance superelevation for this curve shall be **0.94 inches (new). (#63 CLOSED - 10/11/13) Change to Max Unbalance 7/20/17**	10.2.3.2.c.iii.B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-23	Curve US-WB 2 - Required speed of 25 MPH results in an unbalance superelevation of greater than the maximum allowable 0.5 inches. Superelevation cannot be increased without impact to No. 10 turnout east of curve or running off superelevation on tangent Proposed unbalance superelevation for this curve shall be **0.35 inches (new)**. **(#68 TO BE CLOSED - OPEN AS OF 11/21/14) Change to Alignment 7/20/17**	1.6.2.1.4.3B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-24	Curve US-WB 3 - Required speed of35 MPH results in an unbalance superelevation of greater than the maximum allowable 0.5 inches. This was done to comply with an MBTA comment requesting spirals be made longer than the minimum. Proposed unbalance superelevation for this curve shall be **0.47 inches (new). (#69 TO BE CLOSED - OPEN AS OF 11/21/14) Change to Alignment 7/20/17**	1.6.2.1.4.3B	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-25	Union Square Branch EB #6 MOD Turnout (Sta 12+62.59) has a vertical tangent length preceding the switch of less than the 30 foot minimum, but greater than the absolute minimum of 12 feet, due to alignment **(#23 CLOSED - 10/11/13) Change to Alignment 7/20/17**	10.2.3.2.e	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-26	The tangent lengths preceding the points of switch of the No. 8 diamond crossover east of Union Square Station are less than the minimum of 30 ft. This is necessary to allow the adjacent curves to have centerline radii of greater than 1,000 ft. **(#71 CLOSED - 10/11/13) Change to Alignment 7/20/17**	10.2.3.2.e	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-27	The vertical tangent between the vertical curve (PVI 35+38.94) and the No. 8 diamond crossover east of Union Square Station is less than the minimum of 30 ft. The proposed tangent length to the east is 5.34 Ft. This is necessary to create space for the preferred interlocking configuration. **(#72 CLOSED - 10/11/13) Change to Alignment 7/20/17**	10.2.3.2.e	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-28	Track Spacing between alignments MB-WB and MB-EB is less than the miminum spacing at curve locations 0,0; 3,3; 4,4; 5,5; 6,6. These curves are located within the viaduct.	10.2.3.2.e.v	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-29	Track Spacing between alignments MB-WB and MB-EB is less than the miminum spacing at curve locations MB-EB 7, MB-WB 15A and MB-EB 14A, MB-EB 16, and MB-EB 17.	10.2.3.2.e.v	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-30	Vehicle Maintenance track curve numbers VMF-1, VMF-2, and VMF-3 do not meet the minimum circular curve length due to alignment constraints	10.2.3.2.c.iii.A	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Light Rail	STV-31	Vehicle Maintenance lead track vertical profile does not meet grade requirements defined in Yard Track/Yard Storage and Pocket Track due to site grading plan.	10.2.3.2.d.ii	GLX Vol. 2 Technical Provisions	OPEN	7/20/17	T.MOORE
Commuter Rail	STV-32	Track Spacing between NH-T2 and NH-T1 is less than the minimum of 13 ft, from Sta 87+17 to Sta 89+16, and Sta 135+17 to Sta 137+57. Station 87+17 to Station 89+16 is located in existing track territory.	10.1.3.5.b.i	GLX Vol. 2 Technical Provisions/ Commuter Rail Design Standards Manual (CRDSM)	OPEN	7/20/17	T.MOORE
Commuter Rail	STV-33	Track Spacing between Curves NH-T2 10 and NH-T1 10 does not allow for additional track spacing of 2 Inches per degree of curvature due to clearances at structures	10.1.3.5.b.i/ 6.D.2	GLX Vol. 2 Technical Provisions/ Commuter Rail Design Standards Manual (CRDSM)	OPEN	7/20/17	T.MOORE

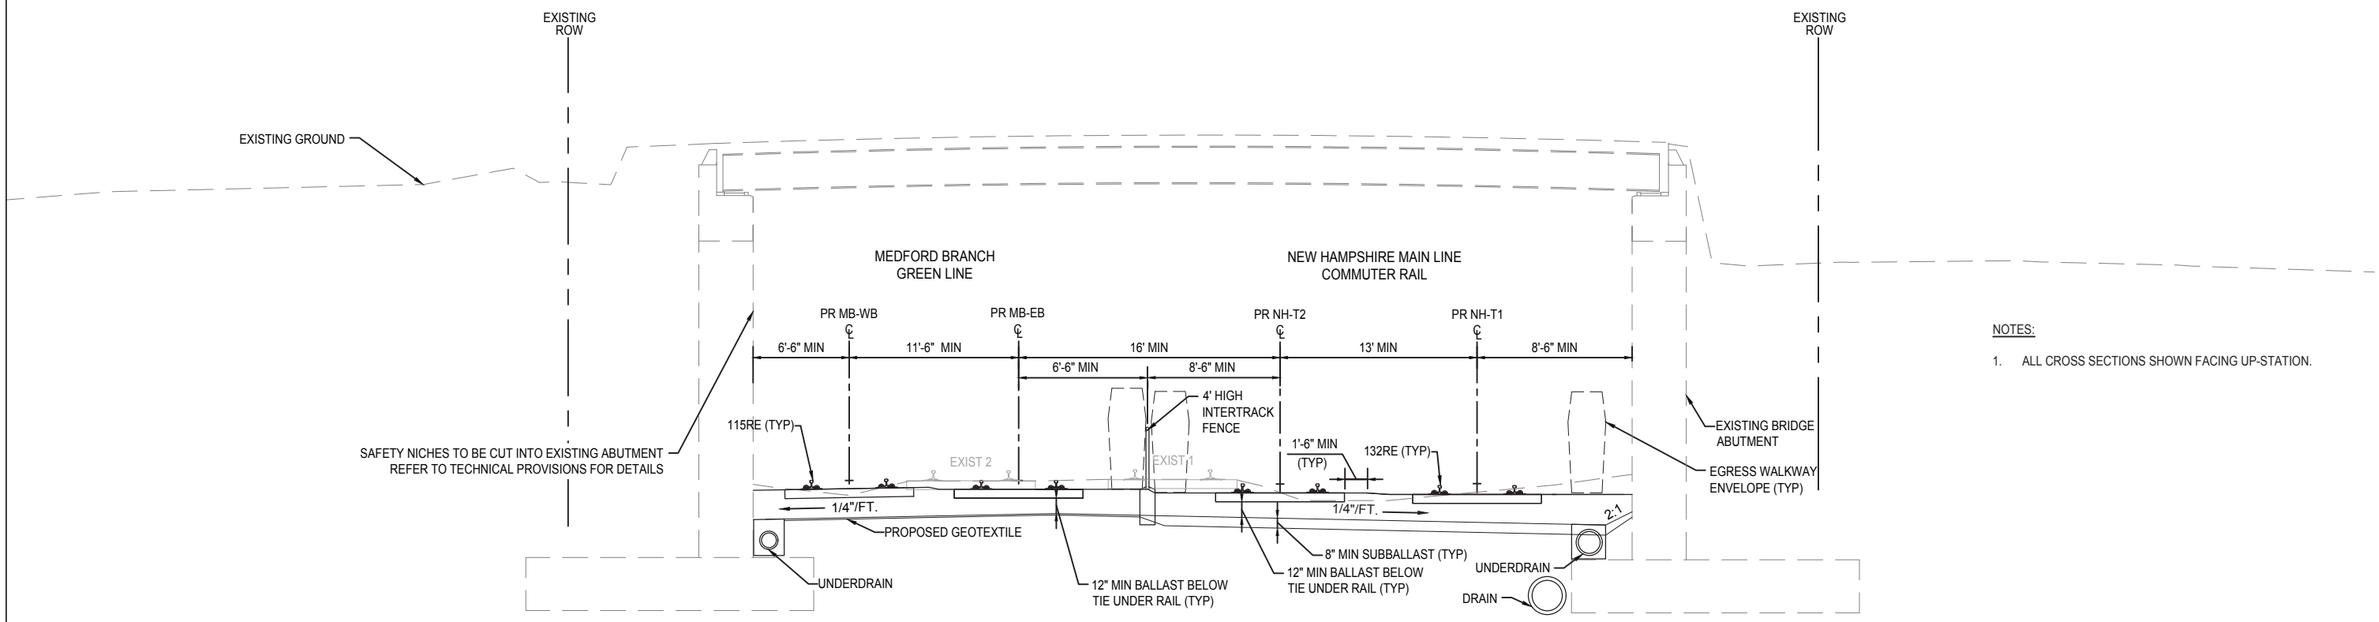

CEDAR STREET OVERHEAD BRIDGE SECTION
MB-EB 321+00

NOTES:

1. ALL CROSS SECTIONS SHOWN FACING UP-STATION.

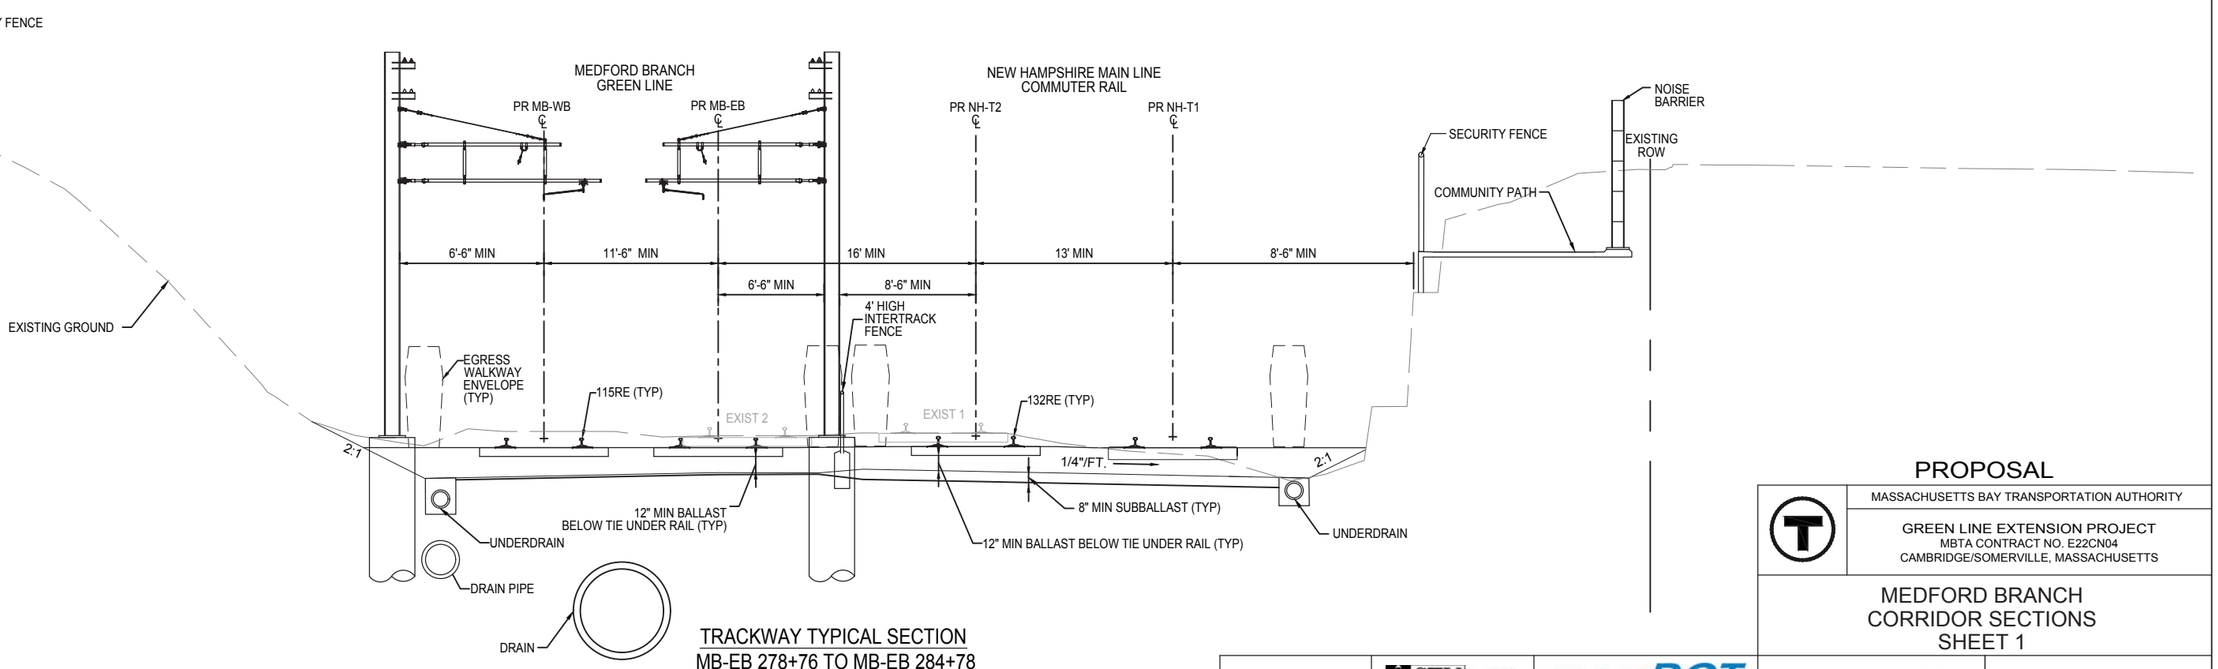

TRACKWAY TYPICAL SECTION
MB-EB 278+76 TO MB-EB 284+78

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


MEDFORD BRANCH
CORRIDOR SECTIONS
SHEET 1

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-276

SCALE: NO SCALE	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-001	


PLOTTED: 09/21/17 1:36PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CR_TRACK_RAIL\000-K-1001-1002.DWG [K-1001] 09/21/17 10:07AM

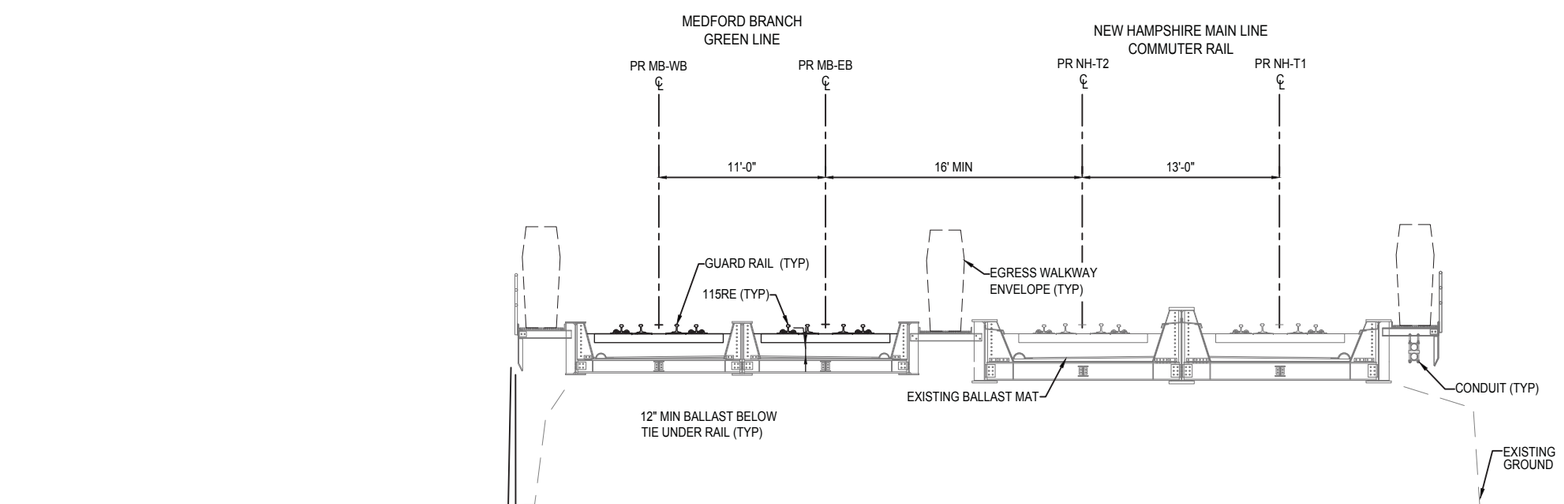

HARVARD STREET RAIL BRIDGE SECTION
REFER TO CONTRACT E22CN01 FOR BRIDGE DETAILS

NOTES:

1. ALL CROSS SECTIONS SHOWN FACING UP-STATION.
2. INTERTRACK FENCE SHALL TERMINATE AT HARVARD STREET BRIDGE STRUCTURE.
3. DESIGN-BUILDER SHALL DESIGN AND CONSTRUCT RETAINING WALL. RETAINING WALL IS PROVIDED FOR REFERENCE.

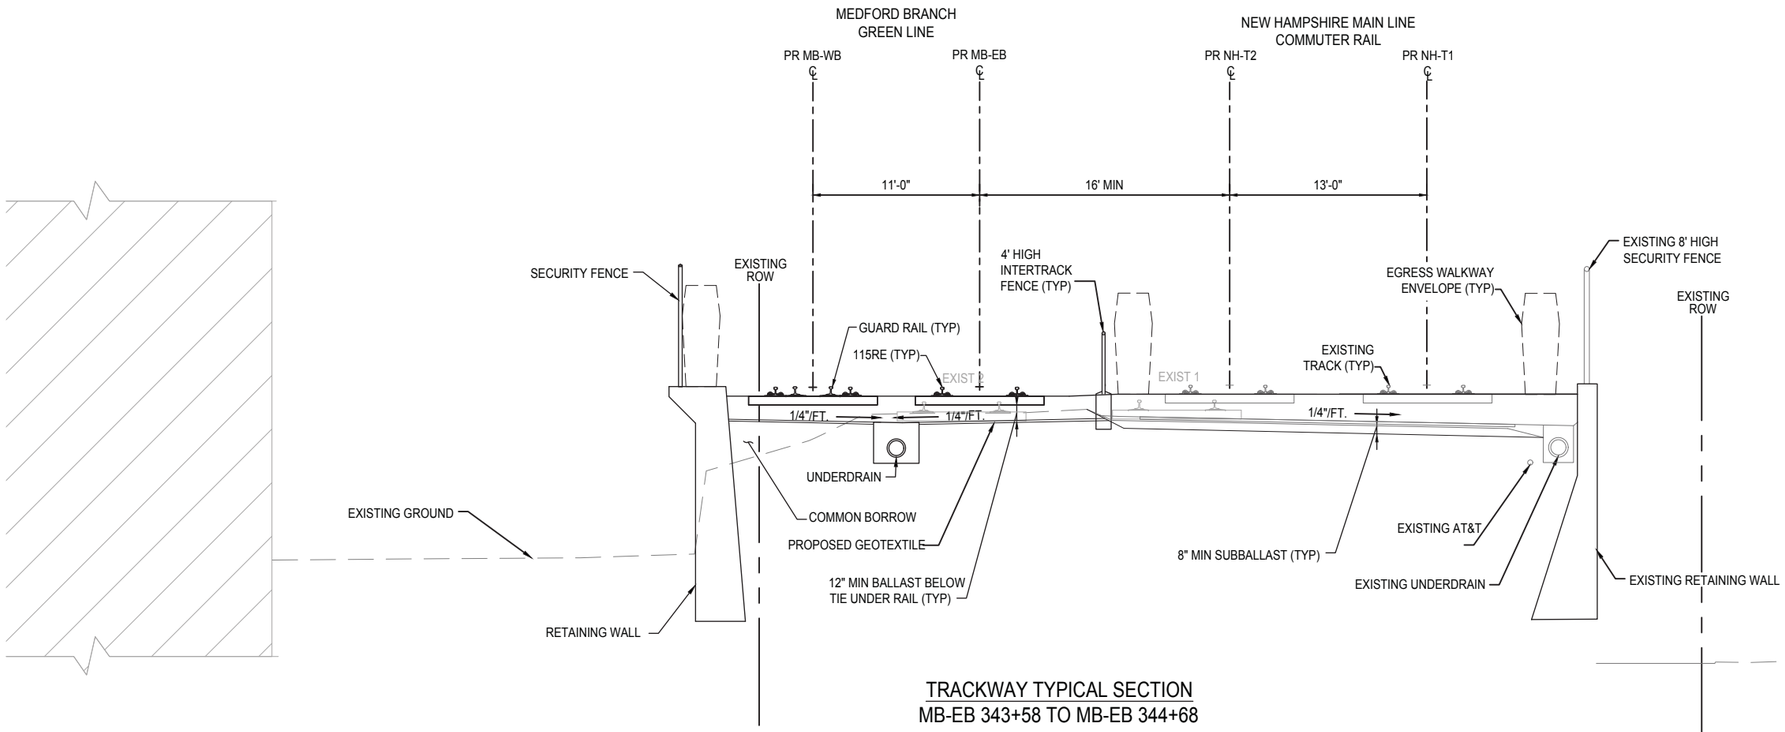

TRACKWAY TYPICAL SECTION
MB-EB 343+58 TO MB-EB 344+68

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH
CORRIDOR SECTIONS
SHEET 2


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: NO SCALE	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-002	

PLOTTED: 09/21/17 5:30AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0002820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-1001-1002.DWG [K-1002] 09/20/17 7:41PM

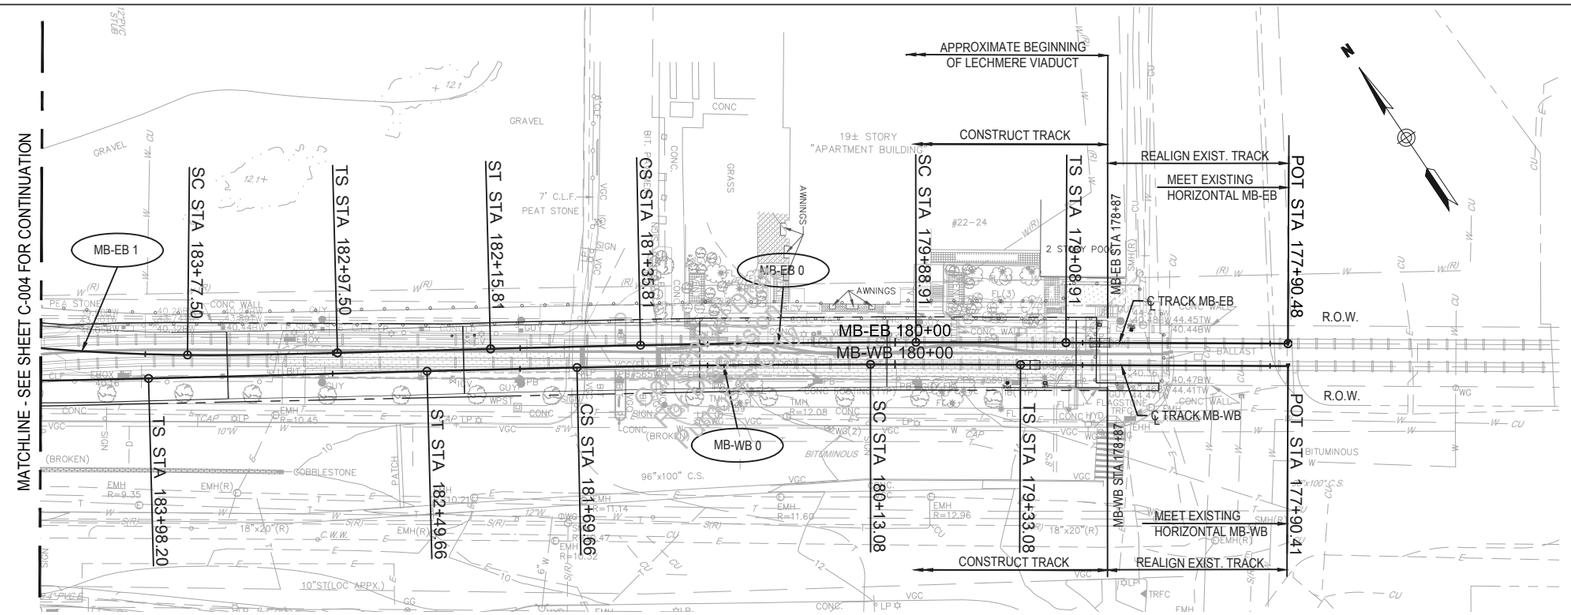

CURVE NO.	MB-EB 0	MB-WB 0	MB-EB 1
R	7443.94 FT	7701.29 FT	1100.00 FT
Lc	146.90 FT	156.58 FT	268.27 FT
Ls1	80.00 FT	80.00 FT	80.00 FT
Ls2	80.00 FT	80.00 FT	80.00 FT
Ea	0.25 IN	0.25 IN	2.00 IN
Eu	0.09 IN	0.08 IN	0.28 IN
V	25 MPH	25 MPH	25 MPH

SYMBOL	DESCRIPTION
	EXISTING GROUND
	EXISTING RAILROAD TRACK
	EXISTING RAILROAD RIGHT-OF-WAY LINE
	PROPOSED CENTERLINE OF TRACK (NEW CONSTRUCTION/LINE AND SURFACE EXISTING)/PROPOSED TOP OF RAIL
	CENTERLINE OF TRACK CONSTRUCTED IN A PREVIOUS PHASE
	PROPOSED TURNOUT (RIGHT-HAND SHOWN)
	SINGLE CROSSOVER (LEFT-HAND SHOWN)
	DOUBLE CROSSOVER
	PROPOSED HIGHWAY/ RAILROAD GRADE CROSSING
℄	CENTERLINE
	POINT OF SWITCH - DENOTES SWITCH MACHINE LOCATION
	POINT OF SWITCH - DENOTES ELECTRIC LOCK LOCATION
	POINT OF SWITCH - DENOTES HAND THROW LOCATION
	POINT OF CURVE/SPIRAL
Ea	ACTUAL SUPERELEVATION
Eu	UNBALANCED SUPERELEVATION
V	DESIGN SPEED IN MPH
TO	TURNOUT
XO	CROSSOVER
MB-EB 1	CURVE NUMBER
MP 1	MILE POST
SIH	SIGNAL INSTRUMENT HOUSE (COMMUTER RAIL)
CIH	CONTROL INSTRUMENT HOUSE (LIGHT RAIL)
EQ	TRACK ALIGNMENT STATION EQUATION
	POINT OF INTERSECTION

ABBREVIATIONS

MB - MEDFORD BRANCH
US - UNION SQUARE BRANCH
NH - NEW HAMPSHIRE
YL - YARD LEAD
ST - STORAGE TRACK
MAF - MAINTENANCE TRACK
PT - POINT OF TANGENT
LVC - LENGTH OF VERTICAL CURVE
PVC - POINT OF VERTICAL CURVE
PVI - POINT OF VERTICAL INTERSECTION
PVT - POINT OF VERTICAL TANGENT
EGL - EXISTING GRADE LINE
TS - TANGENT SPIRAL
SC - SPIRAL CURVE
CS - CURVE SPIRAL
ST - SPIRAL TANGENT
R - RADIUS
Lc - LENGTH OF CURVE
Ls - LENGTH OF SPIRAL
MOD - MODIFIED
P - PIPE
MH - MANHOLE
BG - BOTTOM OF GIRDER
MSE - MECHANICALLY STABILIZED EMBANKMENT
MW - MEDFORD WEST RETAINING WALLT
ME - MEDFORD EAST RETAINING WALL
UN - UNION SQUARE NORTH WALL
MCW - MEDFORD CRIB WALL

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH CORRIDOR PLAN AND PROFILE STA MB-EB 176+50 TO STA MB-EB 184+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	PEB	SHEET: C-003	

PLOTTED: 09/21/17 5:35AM BY:BRYANTPJ
DRAWING: E:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CR_TRACK_RAIL\000-HC-2001-2008.DWG [C-003] 09/20/17 9:47PM

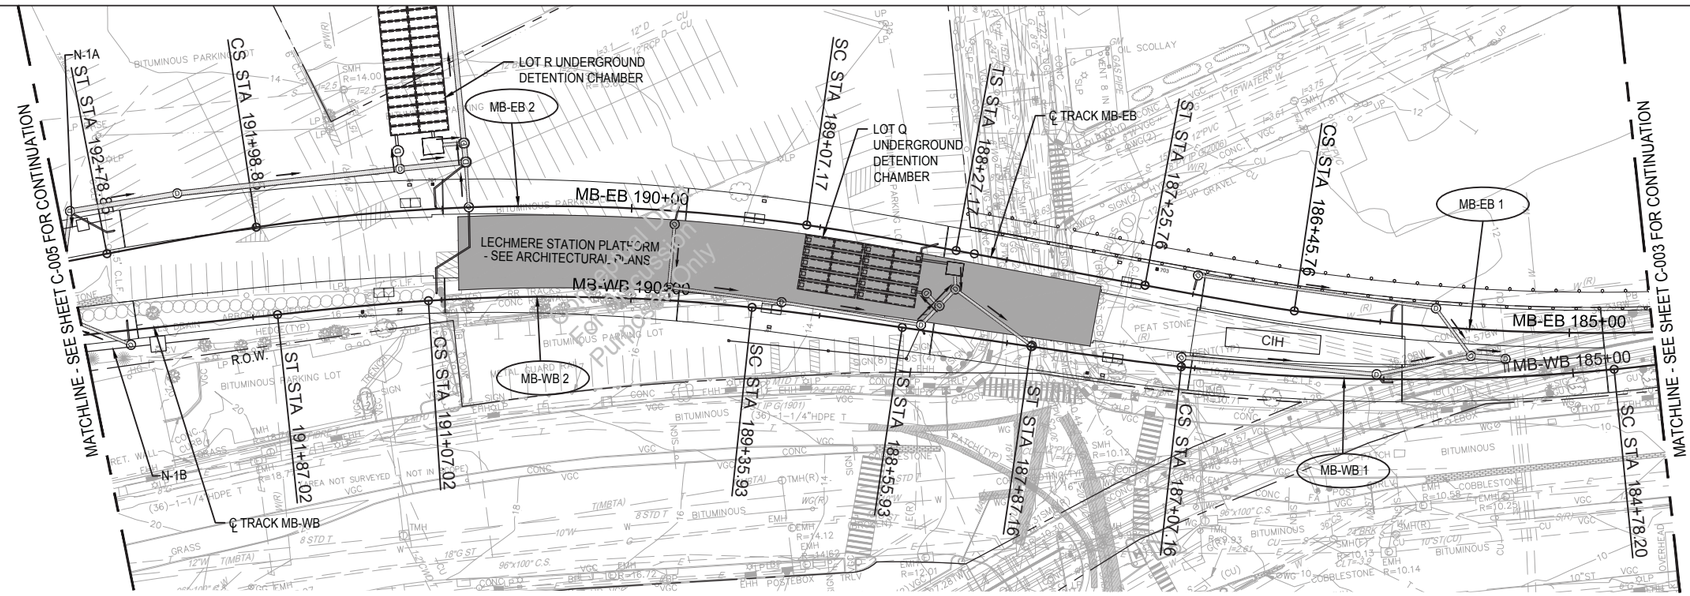

PLAN

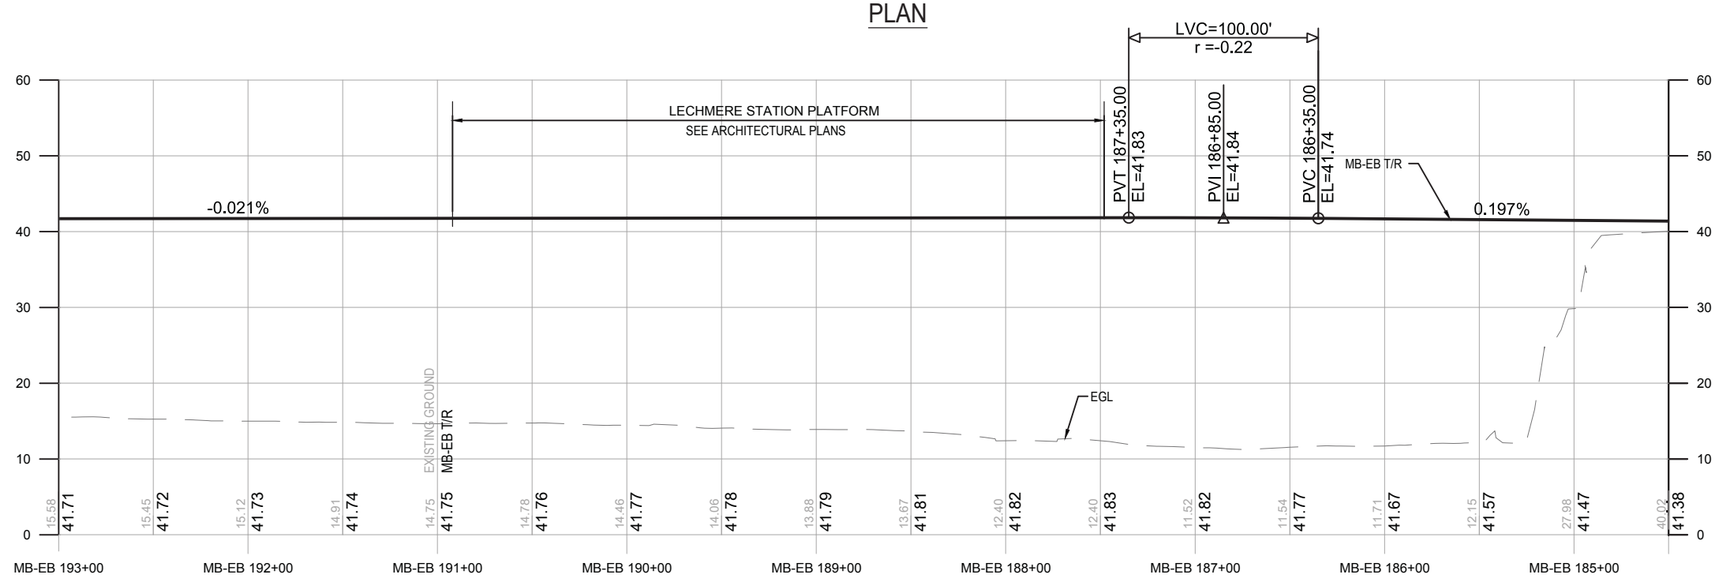

PROFILE

CURVE NO.	MB-EB 1	MB-EB 2	MB-WB 1	MB-WB 2
R	1100.00 FT	1000.00 FT	1100.00 FT	1000.00 FT
Lc	268.27 FT	291.68 FT	228.96 FT	171.09 FT
Ls1	80.00 FT	80.00 FT	80.00 FT	80.00 FT
Ls2	80.00 FT	80.00 FT	80.00 FT	80.00 FT
Ea	2.00 IN	1.50 IN	2.00 IN	1.50 IN
Eu	0.28 IN	1.01 IN	0.28 IN	1.01 IN
V	25 MPH	25 MPH	25 MPH	25 MPH

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH CORRIDOR PLAN AND PROFILE STA MB-EB 184+50 TO STA MB-EB 193+00


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	PEB	SHEET: C-004	

PLOTTED: 09/21/17 1:42PM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\G062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2001-2008.DWG [C-004] 09/21/17 12:57PM

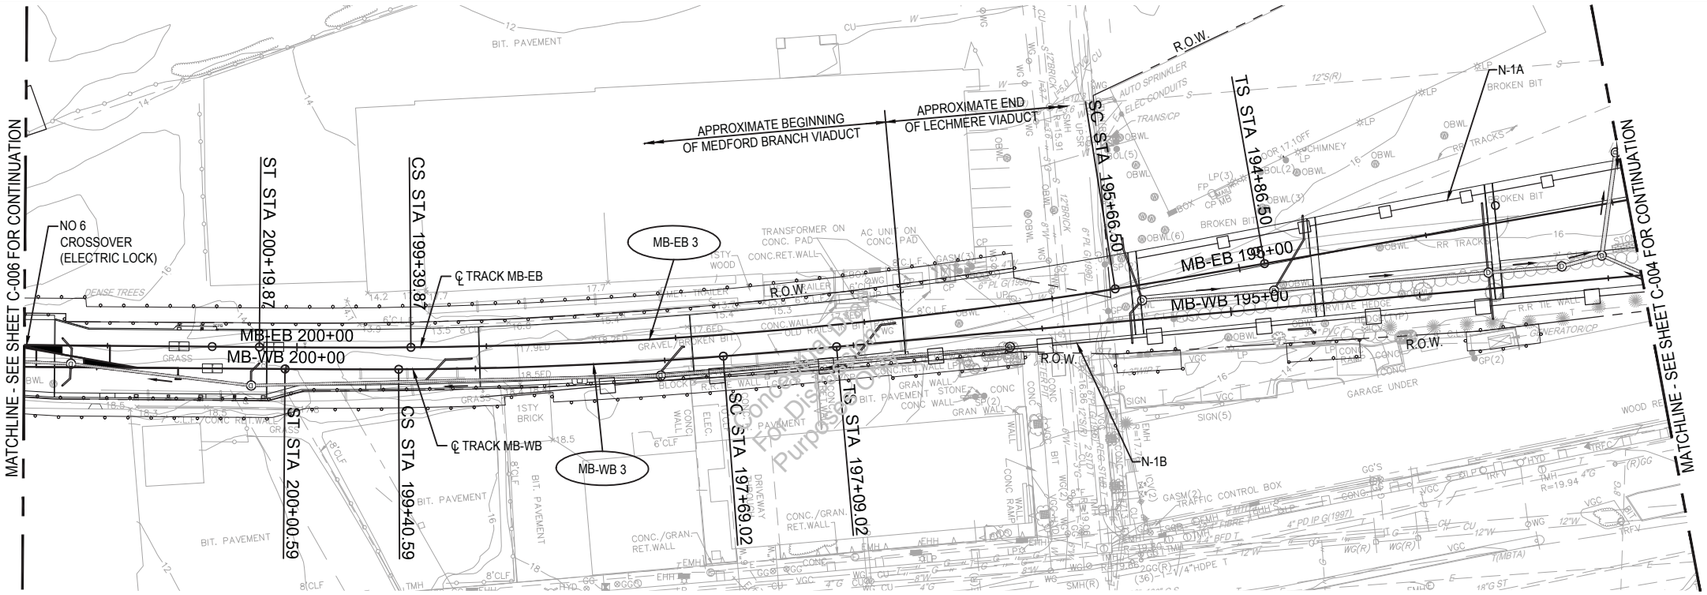

PLAN

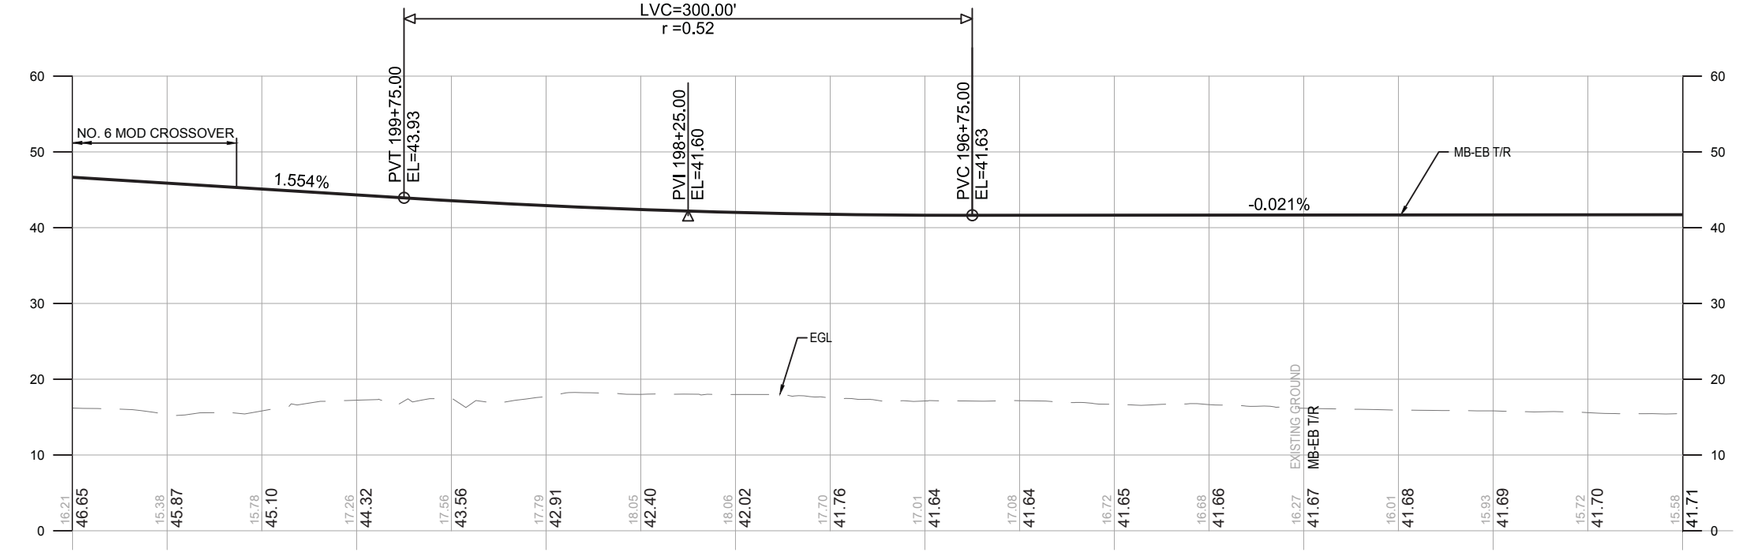

PROFILE

CURVE NO.	MB-EB 3	MB-WB 3
R	2500.00 FT	2400.00 FT
Lc	373.37 FT	171.57 FT
Ls1	80.00 FT	60.00 FT
Ls2	80.00 FT	60.00 FT
Ea	1.00 IN	1.00 IN
Eu	0.44 IN	0.50 IN
V	30 MPH	30 MPH

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 193+00 TO STA MB-EB 201+50

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


GV20170258-276

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-005	

For Discussion Purposes Only

PLOTTED: 09/22/17 7:25AM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\Q062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAL\000-K-2001-2008.DWG [C-005] 09/21/17 8:36PM

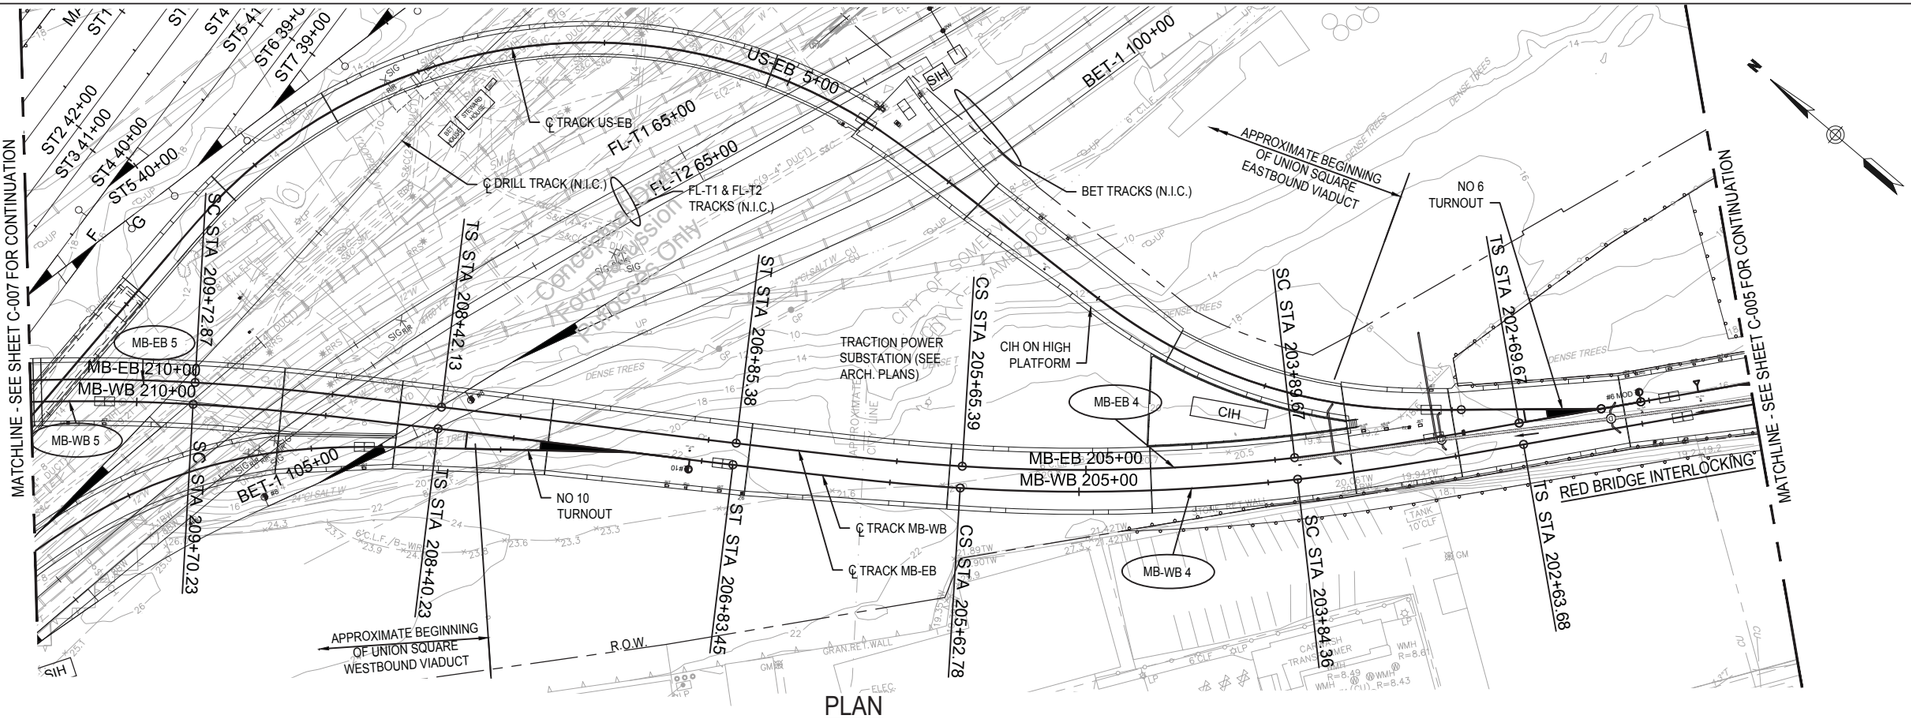

PLAN

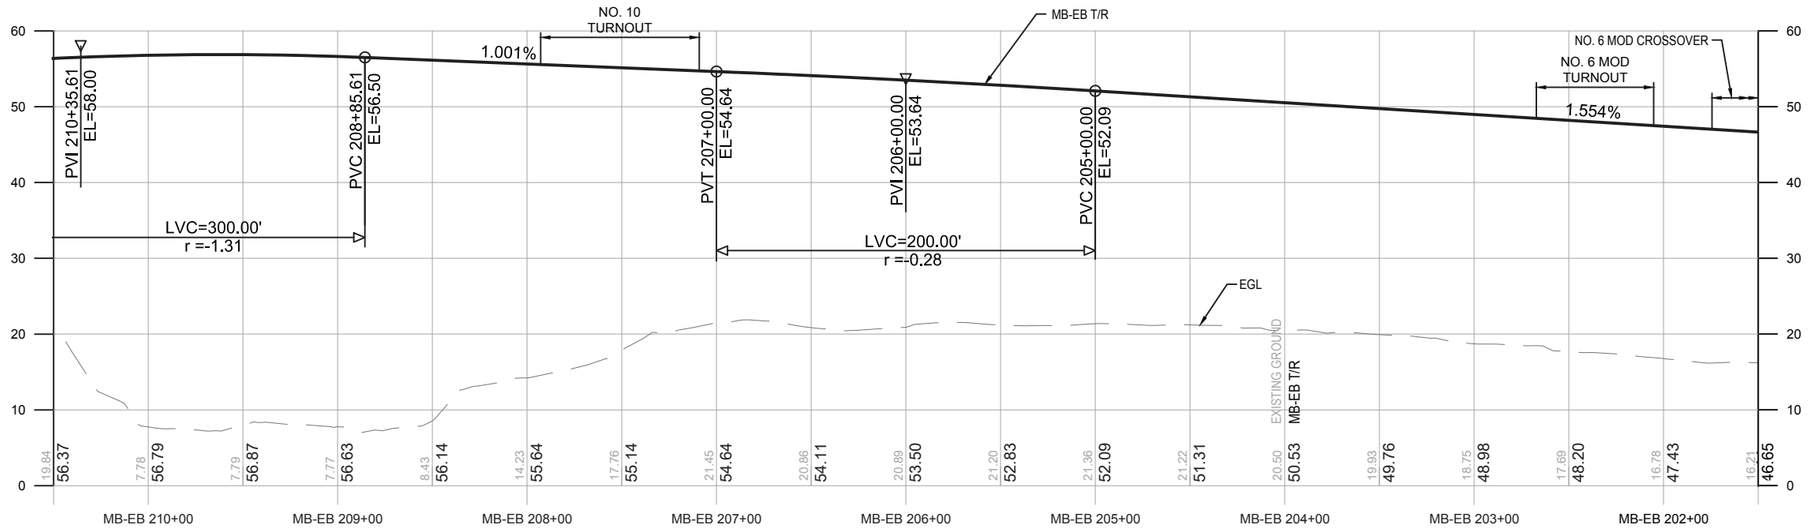

PROFILE

CURVE NO.	MB-EB 4	MB-WB 4	MB-EB 5	MB-WB 5
R	1005.00 FT	1016.50 FT	1016.50 FT	1005.00 FT
Lc	175.71 FT	178.42 FT	194.16 FT	191.23 FT
Ls1	120.00 FT	120.68 FT	130.74 FT	130.00 FT
Ls2	120.00 FT	120.68 FT	130.74 FT	130.00 FT
Ea	3.00 IN	3.00 IN	3.25 IN	3.25 IN
Eu	0.59 IN	0.55 IN	0.30 IN	0.34 IN
V	30 MPH	30 MPH	30 MPH	30 MPH

NOTES:

1. REFER TO SHEETS C-026 TO C-032 FOR UNION SQUARE BRANCH ALIGNMENT AND PROFILE.
2. REFER TO SHEET C-056 FOR DRAINAGE FROM STA 203+85 TO STA 213+85 .

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 201+50 TO STA MB-EB 210+50


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	PEB	SHEET: C-006	

PLOTTED: 09/22/17 9:01AM BY:BRYANTPJ
DRAWING: E:\PROPOSALS\2017\Q062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-#C-2001-2008.DWG [C-006] 09/22/17 8:41AM

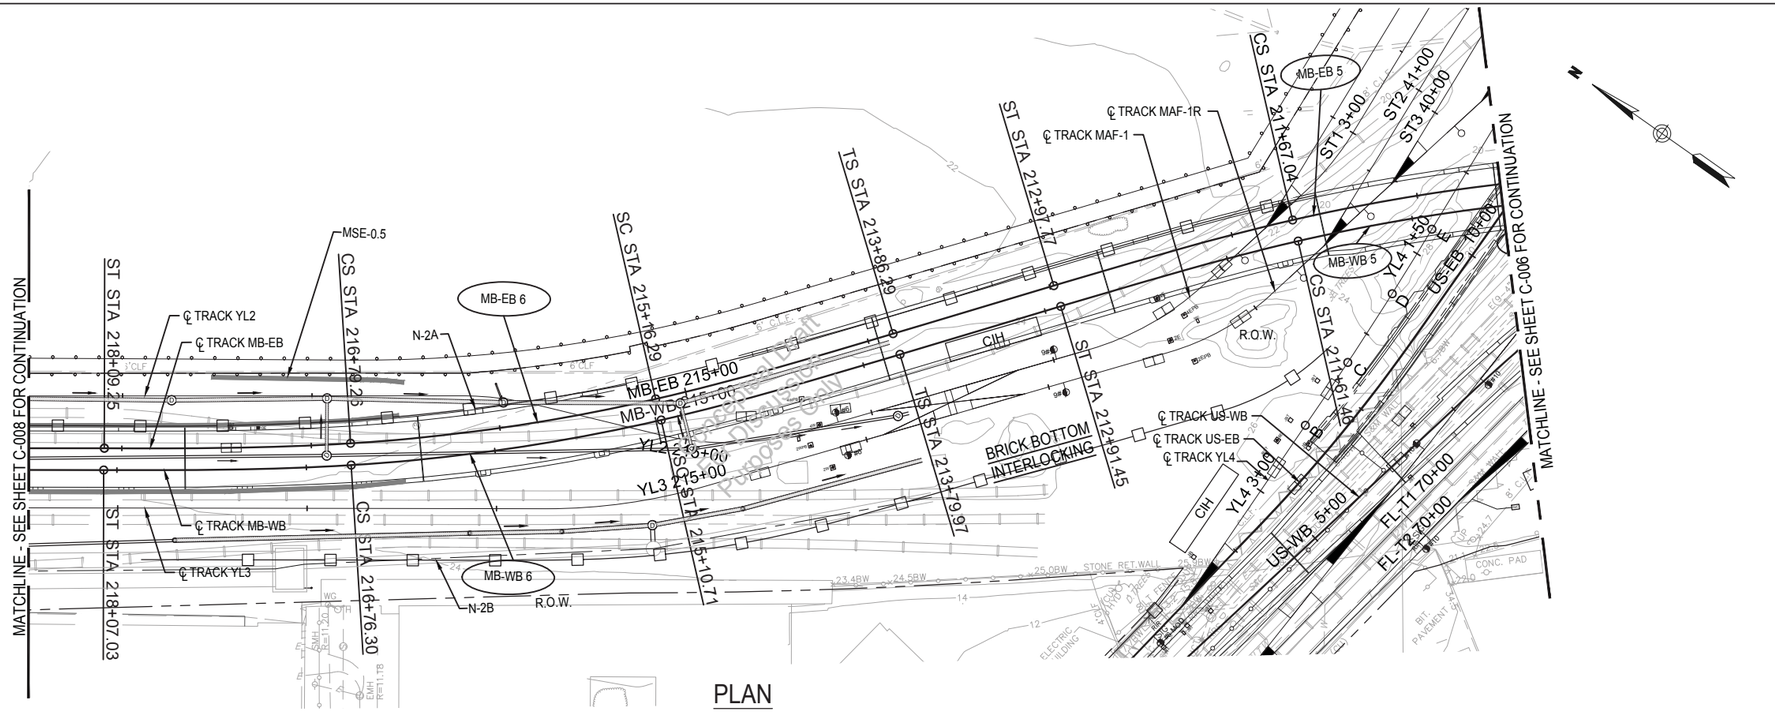

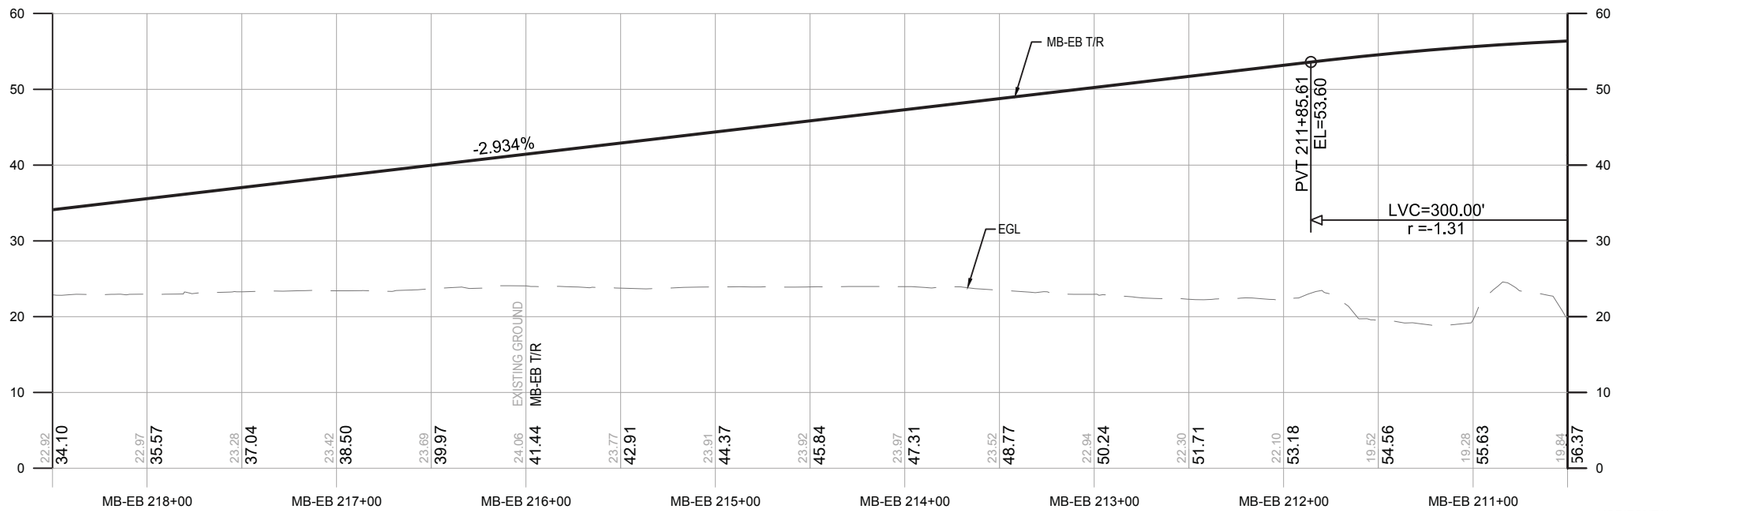

PROFILE

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

CURVE NO.	MB-EB 5	MB-WB 5	MB-EB 6	MB-WB 6
R	1016.50 FT	1005.00 FT	1005.00 FT	1016.50 FT
Lc	194.16 FT	191.23 FT	162.97 FT	165.58 FT
Ls1	130.74 FT	130.00 FT	130.00 FT	130.74 FT
Ls2	130.74 FT	130.00 FT	130.00 FT	130.74 FT
Ea	3.25 IN	3.25 IN	3.25 IN	3.25 IN
Eu	0.30 IN	0.34 IN	0.34 IN	0.30 IN
V	30 MPH	30 MPH	30 MPH	30 MPH

NOTES:

1. REFER TO SHEETS C-026 TO C-032 FOR UNION SQUARE BRANCH ALIGNMENT AND PROFILE.
2. REFER TO SHEETS C-050 TO C-055 FOR YARD LEAD ALIGNMENT AND PROFILE.
3. REFER TO SHEET C-056 FOR DRAINAGE FROM STA 203+80 TO STA 213+85.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 210+50 TO STA MB-EB 218+50

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-276


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-007	

Preliminary Draft Purposes Only

PLOTTED: 09/22/17 7:33AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\J062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_GX_TRACK_RAIL\000-#C-2001-2008.DWG [C-007] 09/21/17 8:36PM

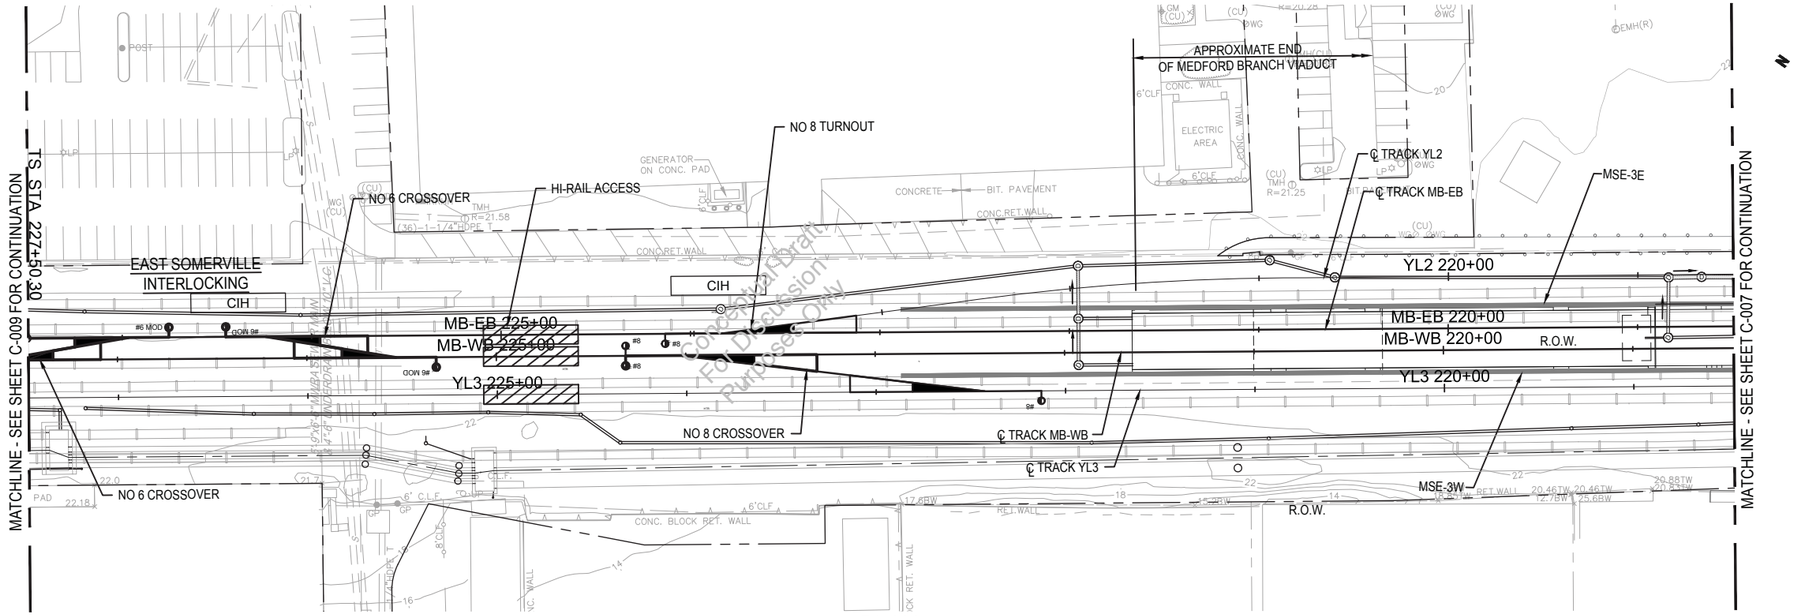

PLAN

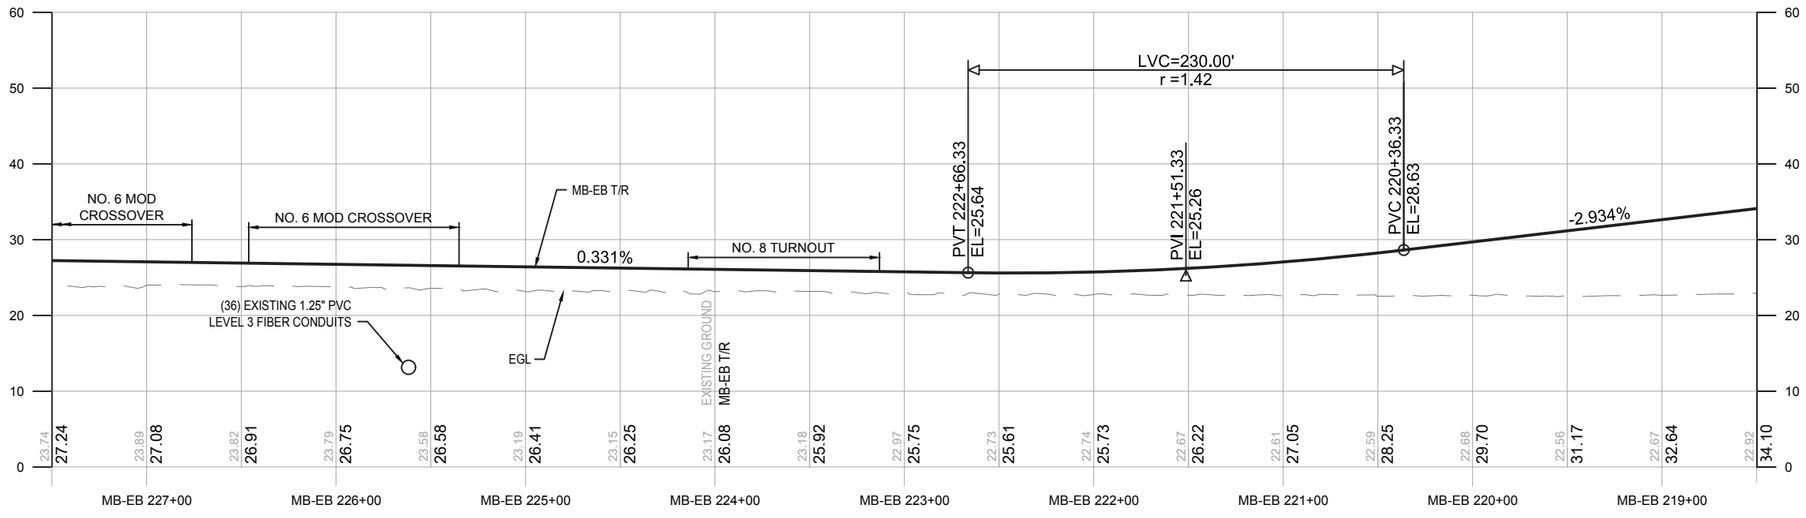

PROFILE

NOTES:

1. REFER TO SHEETS C-050 TO C-055 FOR YARD LEAD ALIGNMENT AND PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH CORRIDOR PLAN AND PROFILE STA MB-EB 218+50 TO STA MB-EB 227+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


GV20170258-276

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-008	

PLOTTED: 09/21/17 5:58AM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2001-2008.DWG [C-008] 09/20/17 9:47PM

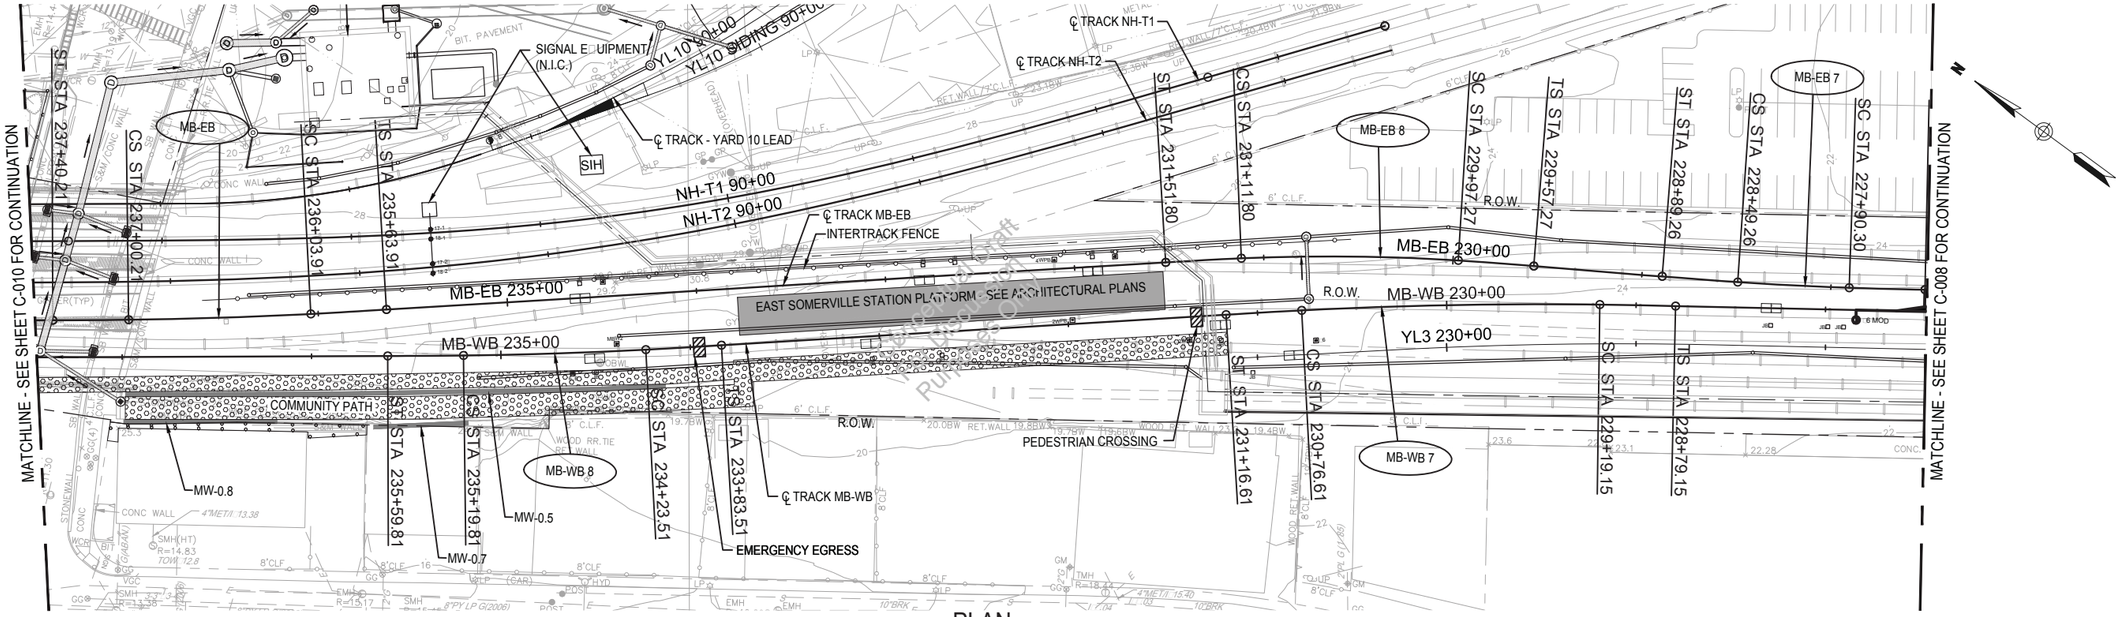

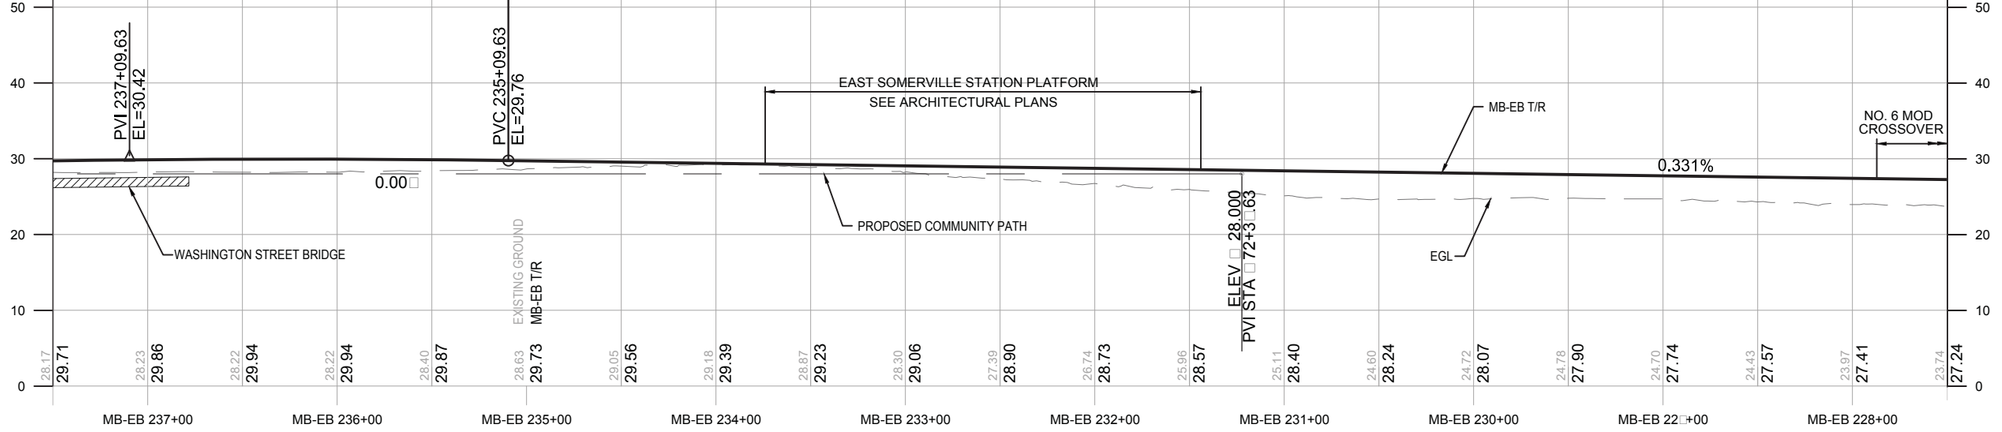

PROFILE

CURVE NO.	MB-EB 7	MB-EB 8	MB-WB 7	MB-WB 8	MB-EB 9
R	1700.00 FT	1100.00 FT	2400.00 FT	2400.00 FT	2400.00 FT
Lc	58.96 FT	114.54 FT	157.46 FT	96.30 FT	96.30 FT
Ls1	40.00 FT	40.00 FT	40.00 FT	40.00 FT	40.00 FT
Ls2	40.00 FT	40.00 FT	40.00 FT	40.00 FT	40.00 FT
Ea	1.00 IN	1.00 IN	1.00 IN	1.25 IN	1.25 IN
Eu	0.43 IN	0.46 IN	0.49 IN	0.22 IN	0.22 IN
V	25 MPH	20 MPH	25 MPH	30 MPH	30 MPH

NOTES:

1. REFER TO SHEETS C-033 TO C-04□ FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. REFER TO SHEETS C-050 TO C-055 FOR YARD LEAD ALIGNMENT AND PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH CORRIDOR PLAN AND PROFILE STA MB-EB 227+50 TO STA MB-EB 237+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-00□	

PLOTTED: 09/21/17 6:33PM BY:BRYANTPJ
DRAWING: E:\PROPOSALS\2017\Q062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_GX_TRACK_RAIL\000-#C-2001-2008.DWG [C-009] 09/21/17 4:33PM

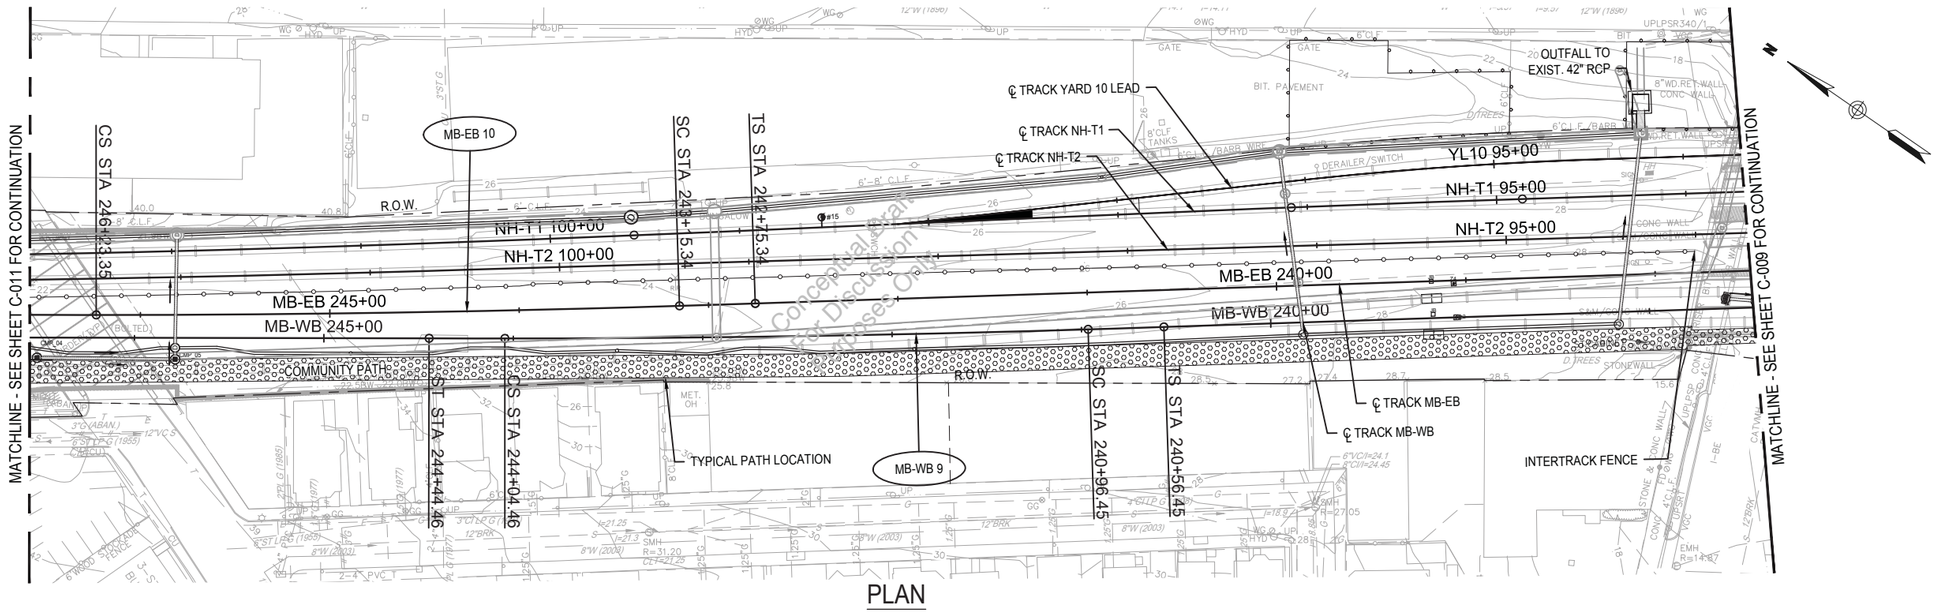

CURVE NO.	MB-WB 9	MB-EB 10
R	10000.00 FT	10000.00 FT
Lc	308.01 FT	308.01 FT
Ls1	40.00 FT	40.00 FT
Ls2	40.00 FT	40.00 FT
Ea	1.00 IN	1.00 IN
Eu	0.00 IN	0.00 IN
V	50 MPH	50 MPH

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 237+50 TO STA MB-EB 246+50


GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-010	

PLOTTED: 09/21/17 6:40PM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2001-2008.DWG [C-010] 09/21/17 4:33PM

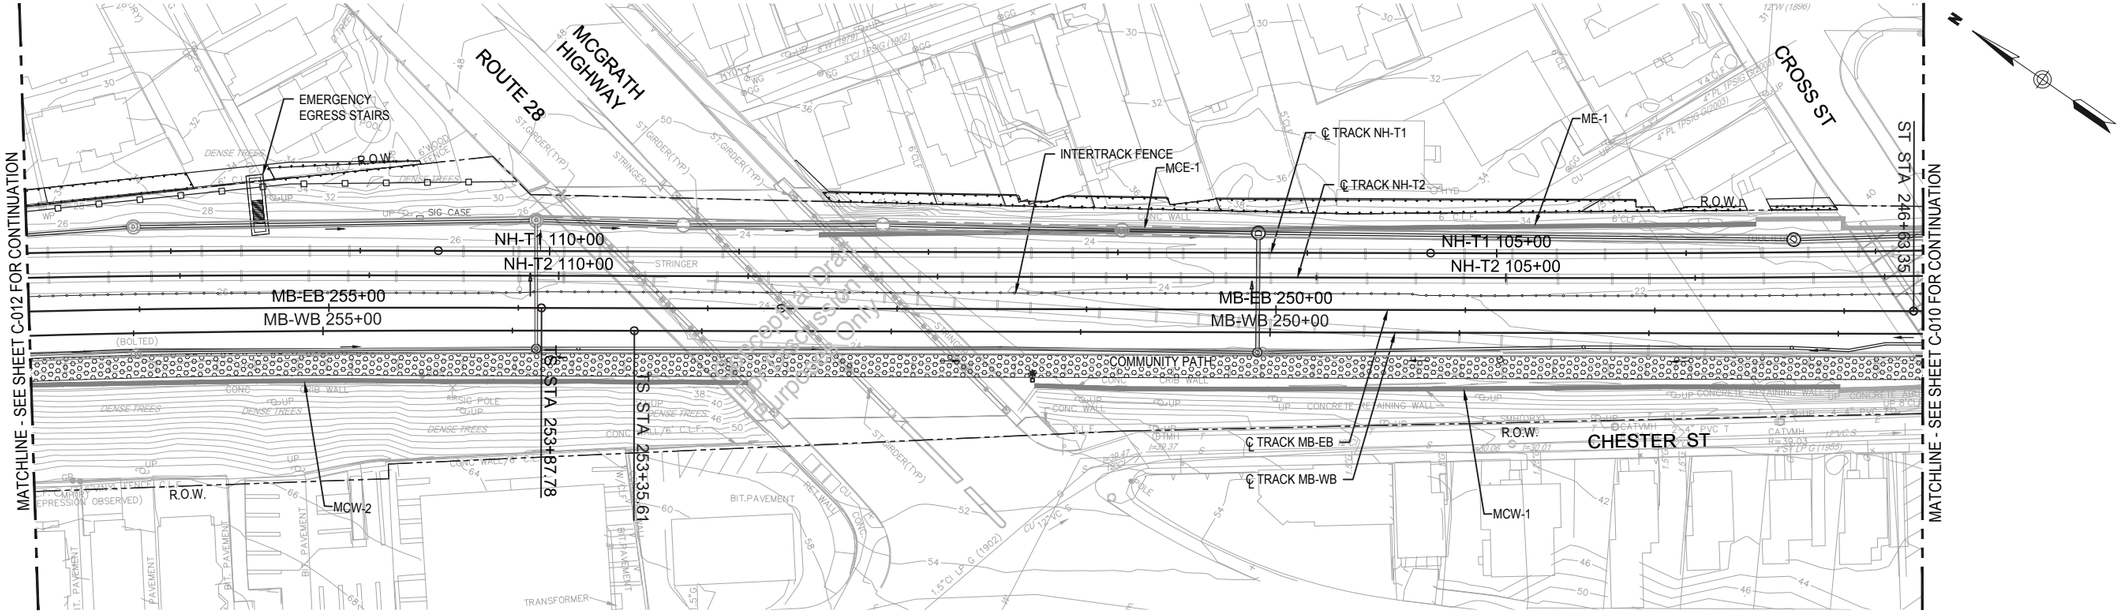

PLAN

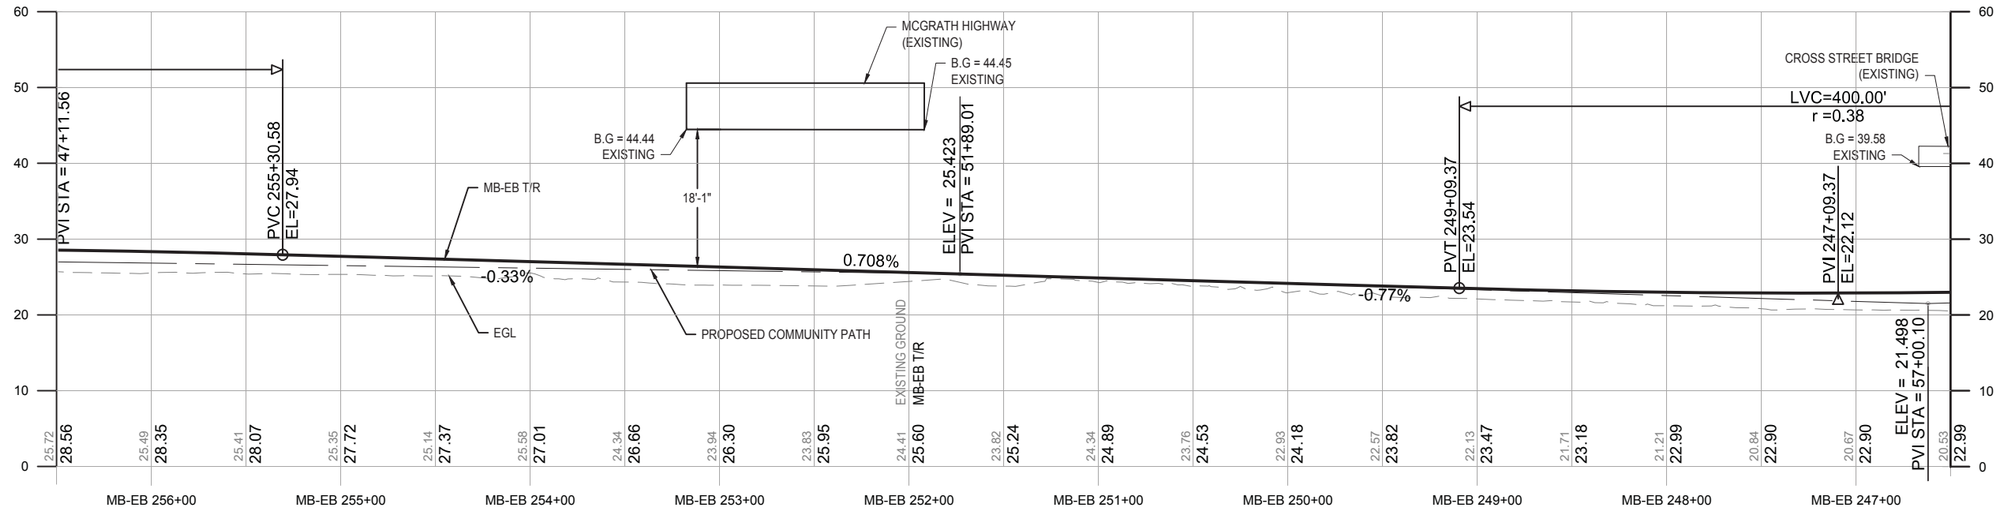

PROFILE

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH CORRIDOR PLAN AND PROFILE STA MB-EB 246+50 TO STA MB-EB 256+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-011	

PLOTTED: 09/22/17 1:49PM BY:RENEKC
DRAWING: L:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2009-2022.DWG [C-011] 09/22/17 1:37PM

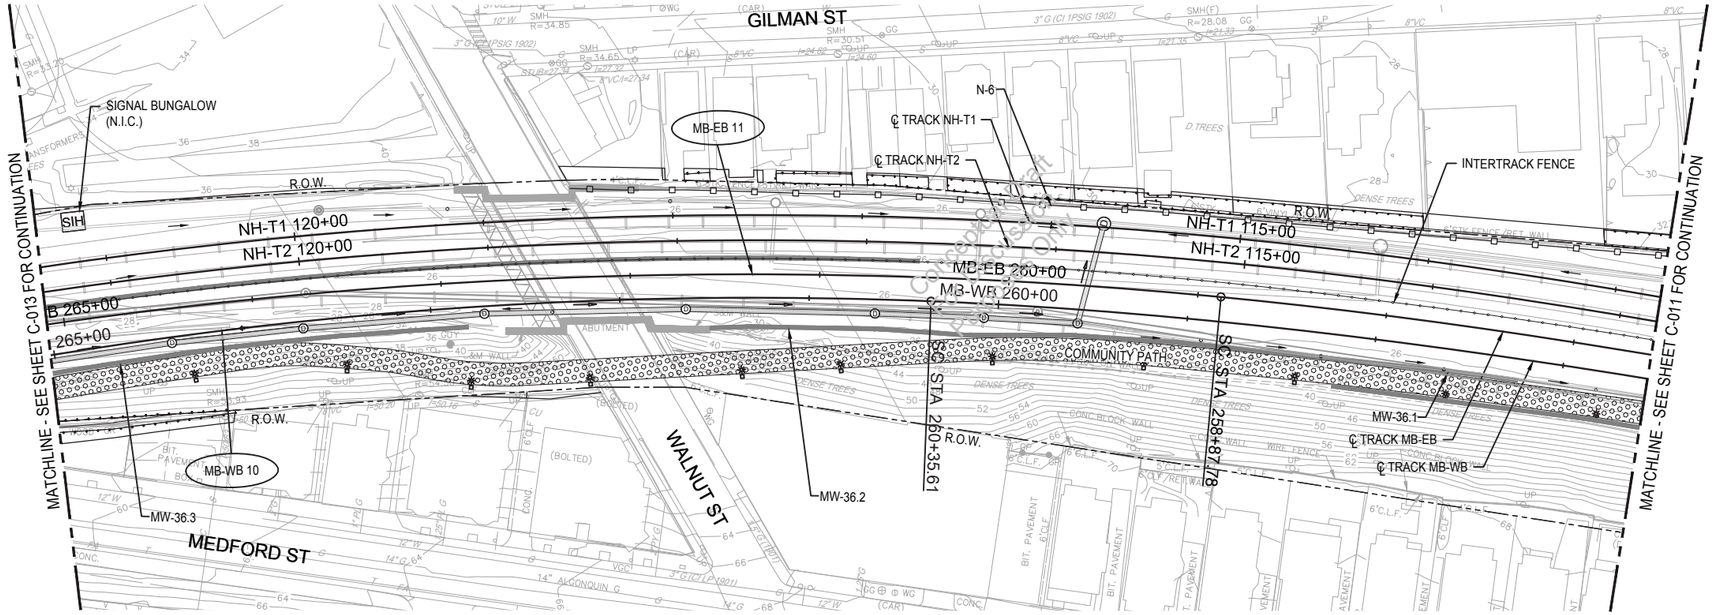

PLAN

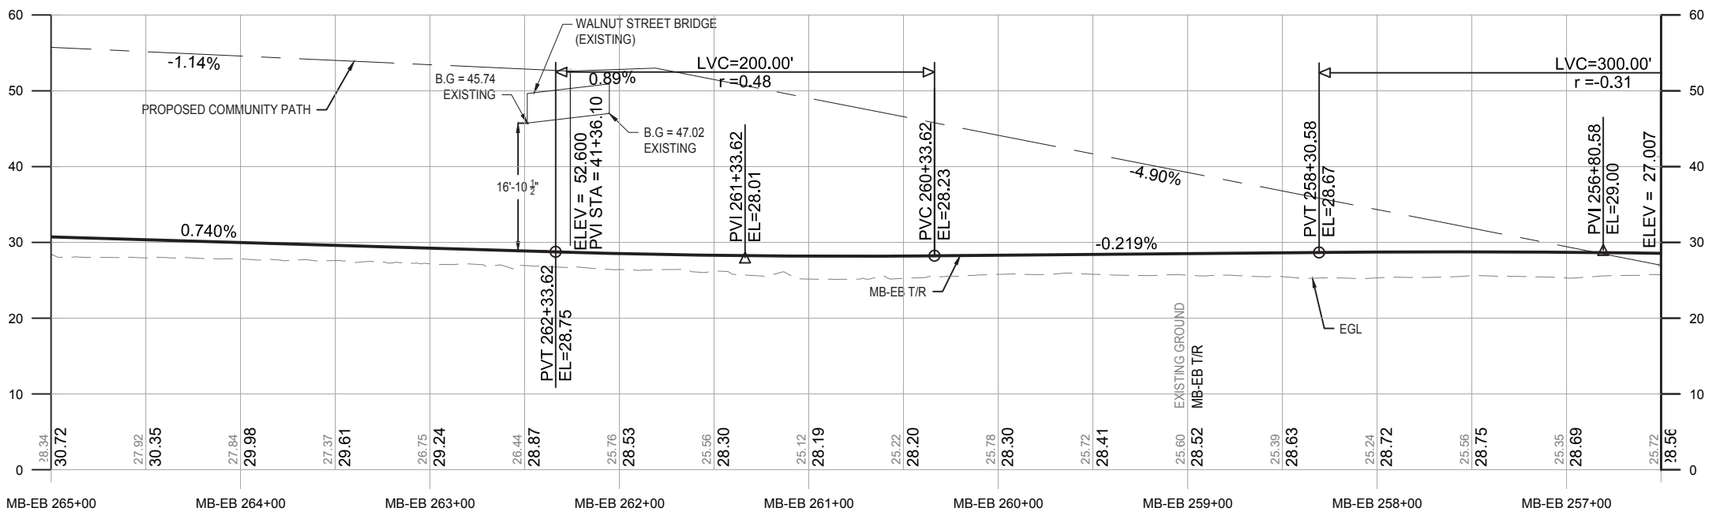

PROFILE

CURVE NO.	MB-WB 10	MB-EB 11
R	2300.00 FT	2600.00 FT
Lc	532.41 FT	739.49 FT
Ls1	700.00 FT	500.00 FT
Ls2	150.00 FT	200.00 FT
Ea	3.25 IN	3.50 IN
Eu	0.28 IN	0.36 IN
V	45 MPH	50 MPH

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 256+50 TO STA MB-EB 265+00

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


GV20170258-276

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


SCALE: AS NOTED | DRAWN BY: CRR | DESIGN BY: PJB | CHECK BY: JEB | PLAN NO. . | ISSUE

DATE: SEPT. 28, 2017 | SHEET: C-012

PLOTTED: 09/22/17 2:10PM BY:RENEKC
DRAWING: I:\PROPOSALS\2017\0062820 GLX C-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2009-2022.DWG [C-012] 09/22/17 1:37PM

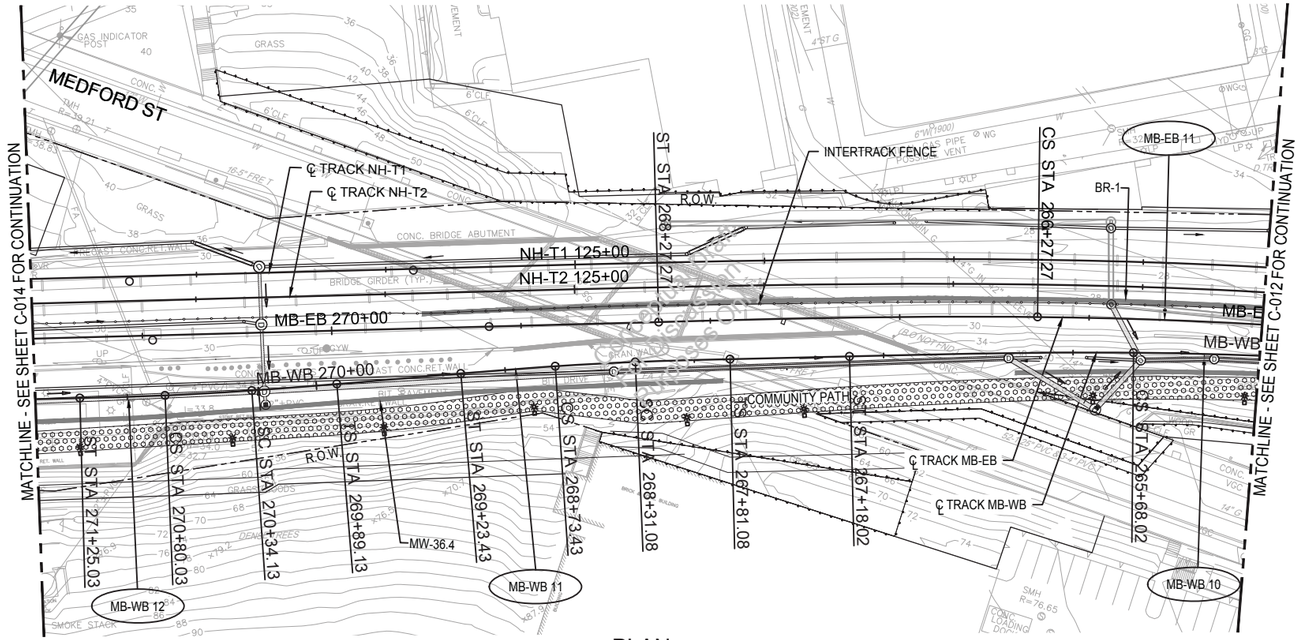

PLAN

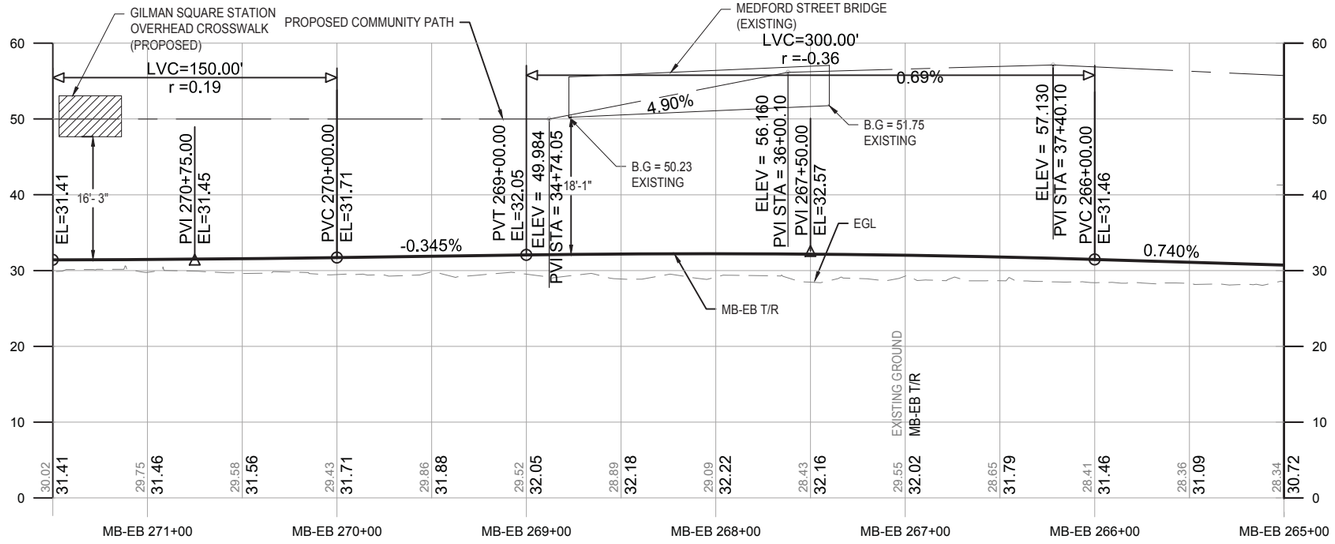

PROFILE

CURVE NO.	MB-WB 10	MB-WB 11	MB-WB 12	MB-EB 11
R	2300.00 FT	1550.00 FT	1600.00 FT	2600.00 FT
Lc	532.41 FT	42.35 FT	45.90 FT	739.49 FT
Ls1	700.00 FT	50.00 FT	45.00 FT	500.00 FT
Ls2	150.00 FT	50.00 FT	45.00 FT	200.00 FT
Ea	3.25 IN	1.00 IN	1.00 IN	3.50 IN
Eu	0.28 IN	0.12 IN	0.57 IN	0.36 IN
s	45 MPH	25 MPH	25 MPH	50 MPH

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. CURVE MB-EB 12 DOES NOT EXIST.
3. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 265+00 TO STA MB-EB 271+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-013	

PLOTTED: 09/22/17 2:40PM BY:RENEKC
DRAWING: I:\PROPOSALS\2017\00082820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_FAIL\000-K-2009-2022.DWG [C-013] 09/22/17 2:39PM

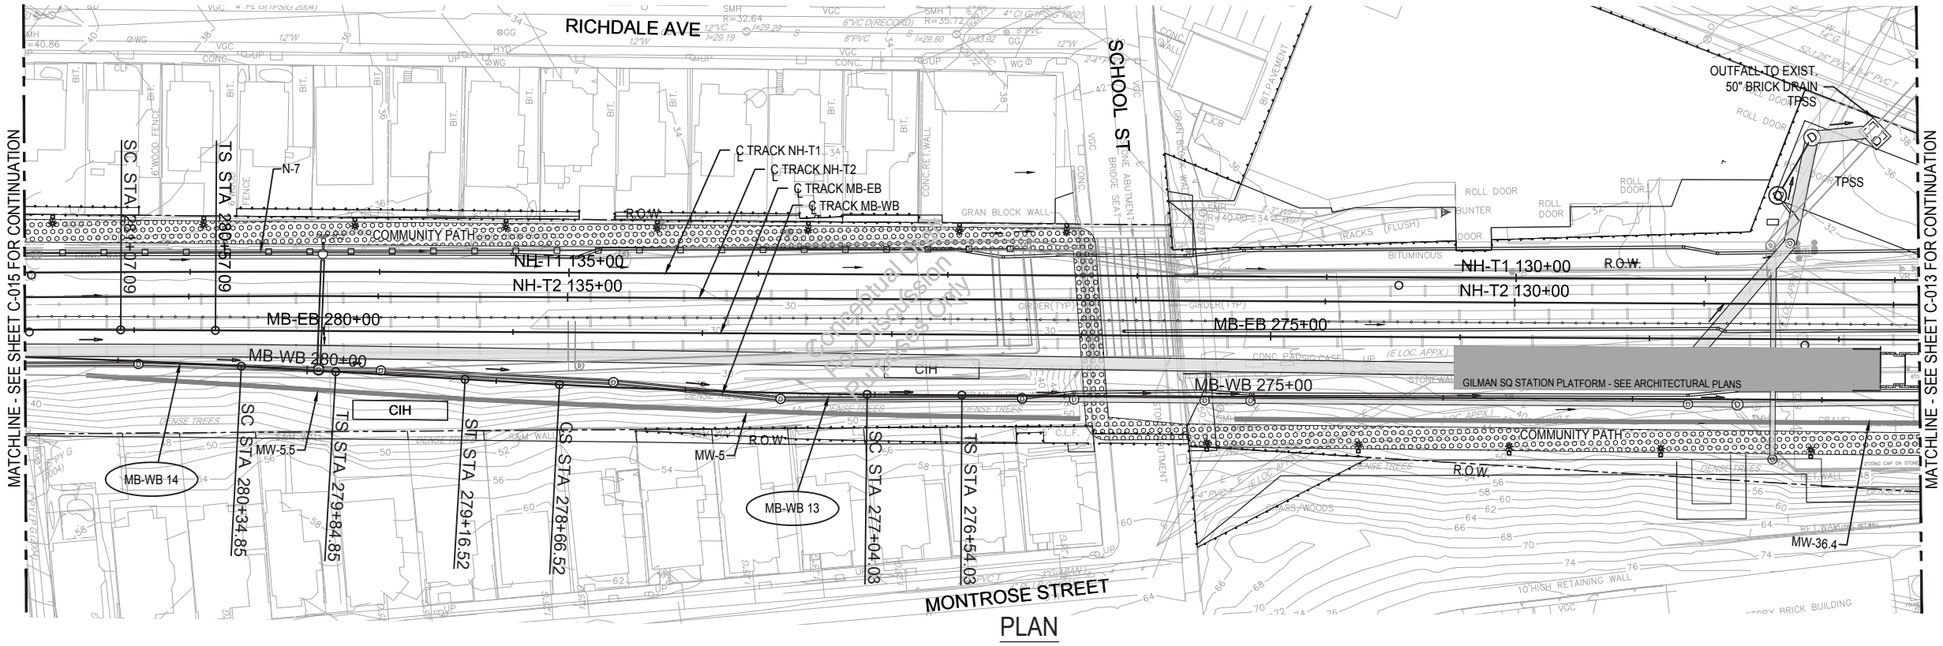

PLAN

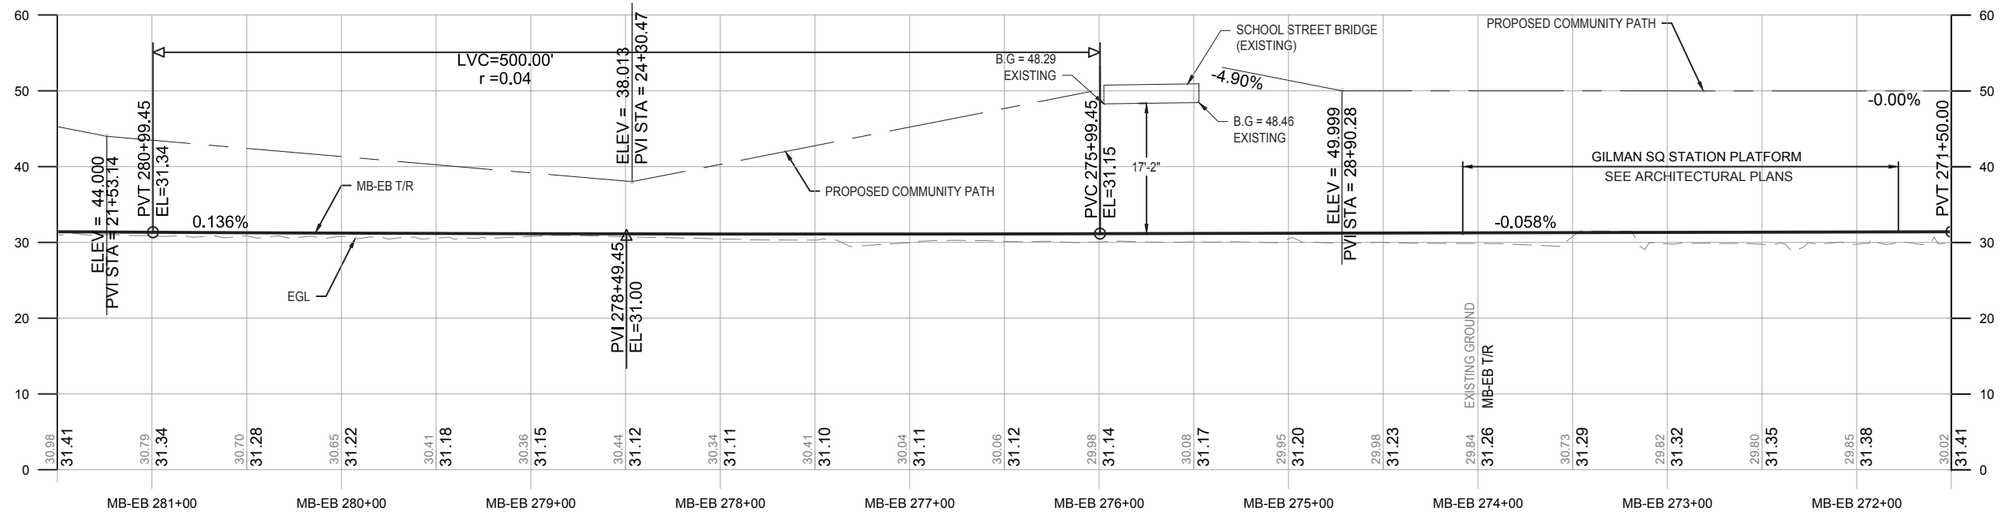

PROFILE

CURVE NO.	MB-WB 13	MB-WB 14
R	4000.00 FT	5000.00 FT
Lc	162.49 FT	265.74 FT
Ls1	50.00 FT	50.00 FT
Ls2	50.00 FT	50.00 FT
Ea	1.00 IN	1.00 IN
Eu	0.23 IN	0.28 IN
V	35 MPH	40 MPH

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 271+50 TO STA MB-EB 281+50

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-014	

PLOTTED: 09/22/17 2:34PM BY:RENEKC
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2009-2022.DWG [C-014] 09/22/17 1:37PM

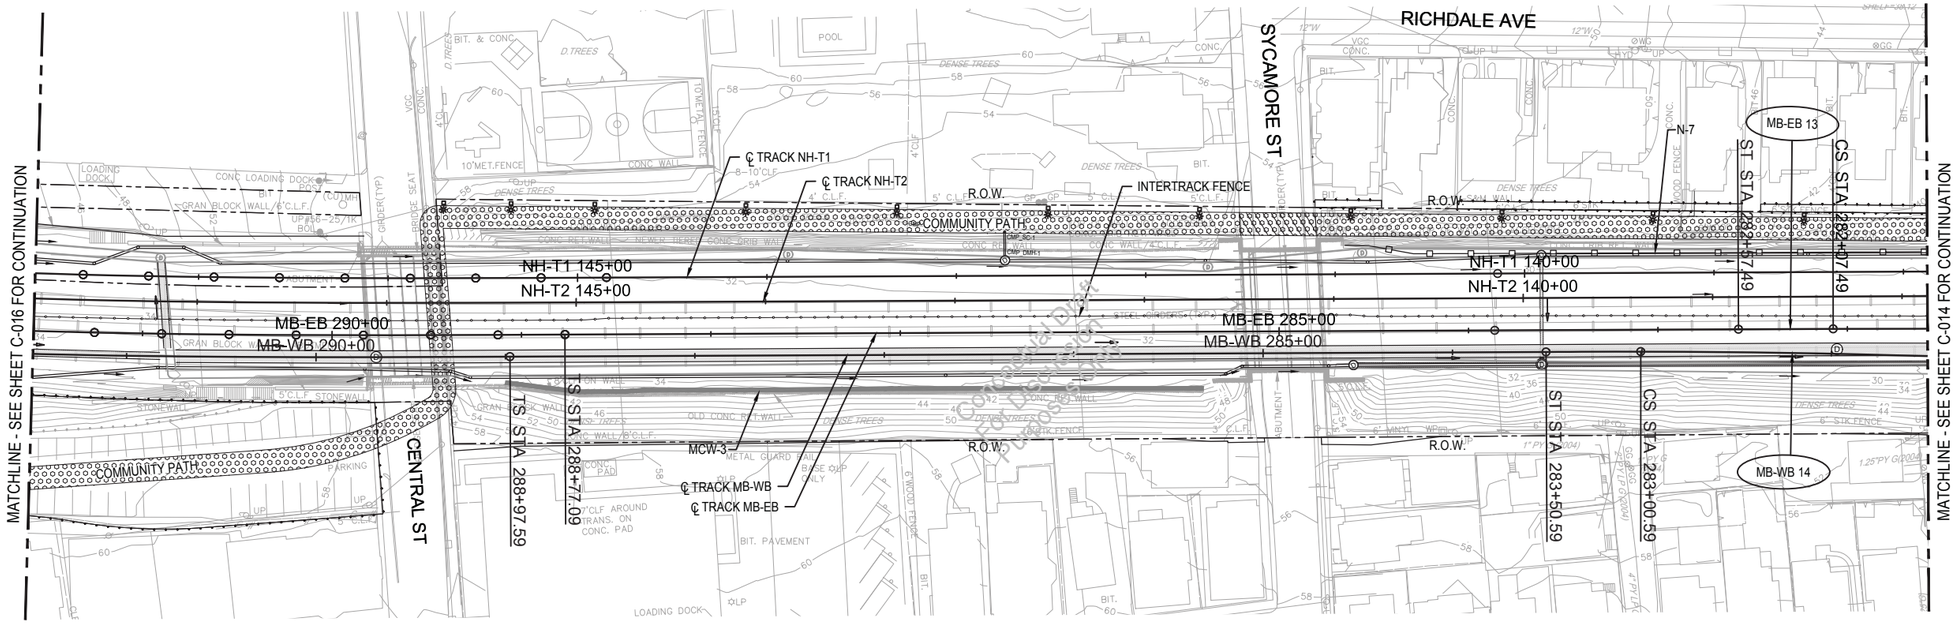

PLAN

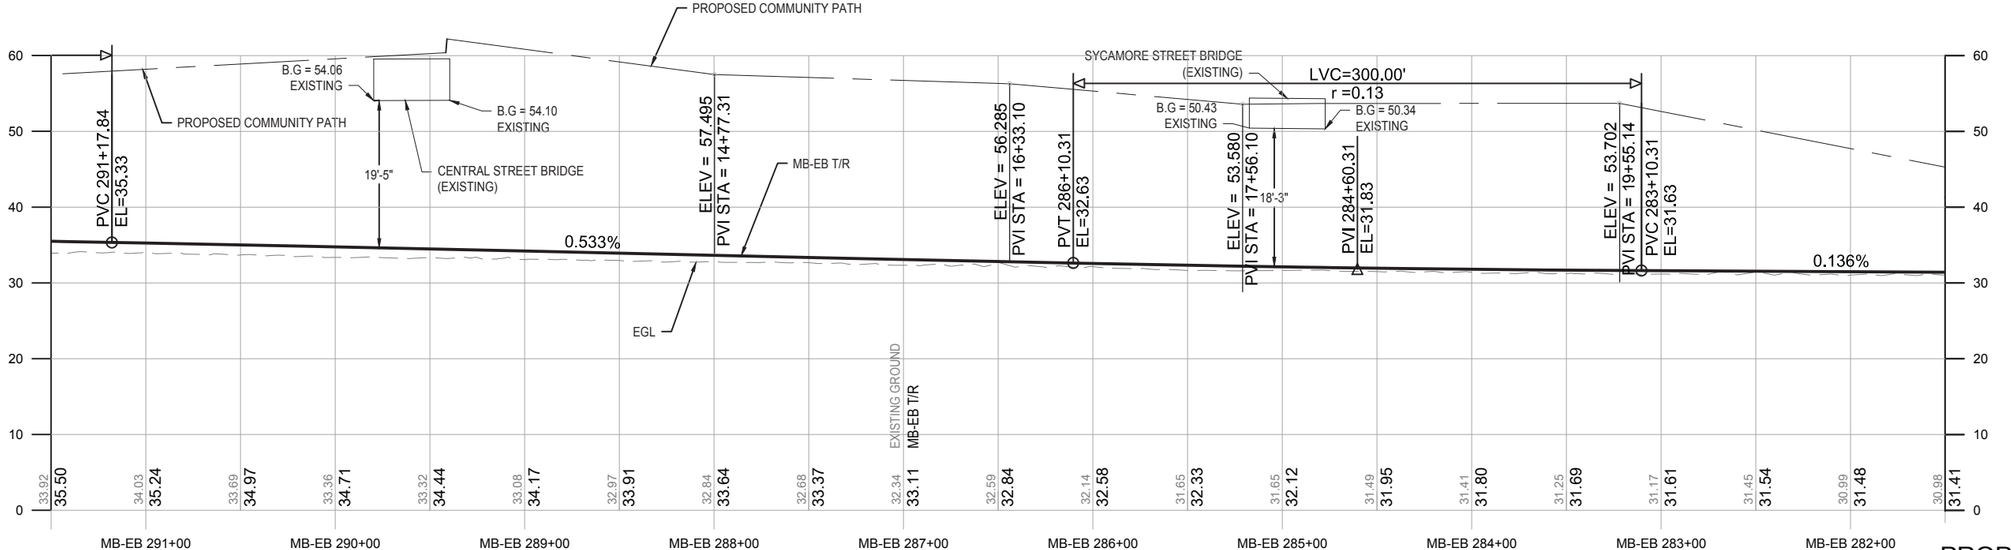

PROFILE

CURVE NO.	MB-EB 13	MB-WB 14
R	15000.00 FT	5000.00 FT
Lc	100.39 FT	265.74 FT
Ls1	50.00 FT	50.00 FT
Ls2	50.00 FT	50.00 FT
Ea	0.50 IN	1.00 IN
Eu	0.17 IN	0.28 IN
V	50 MPH	40 MPH

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 281+50 TO STA MB-EB 291+50

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-015	

PLOTTED: 09/22/17 2:19PM BY:RENEKC
DRAWING: E:\PROPOSALS\2017\G0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_GX_TRACK_RAIL\00D-K-2009-2022.DWG [C-015] 09/22/17 1:37PM

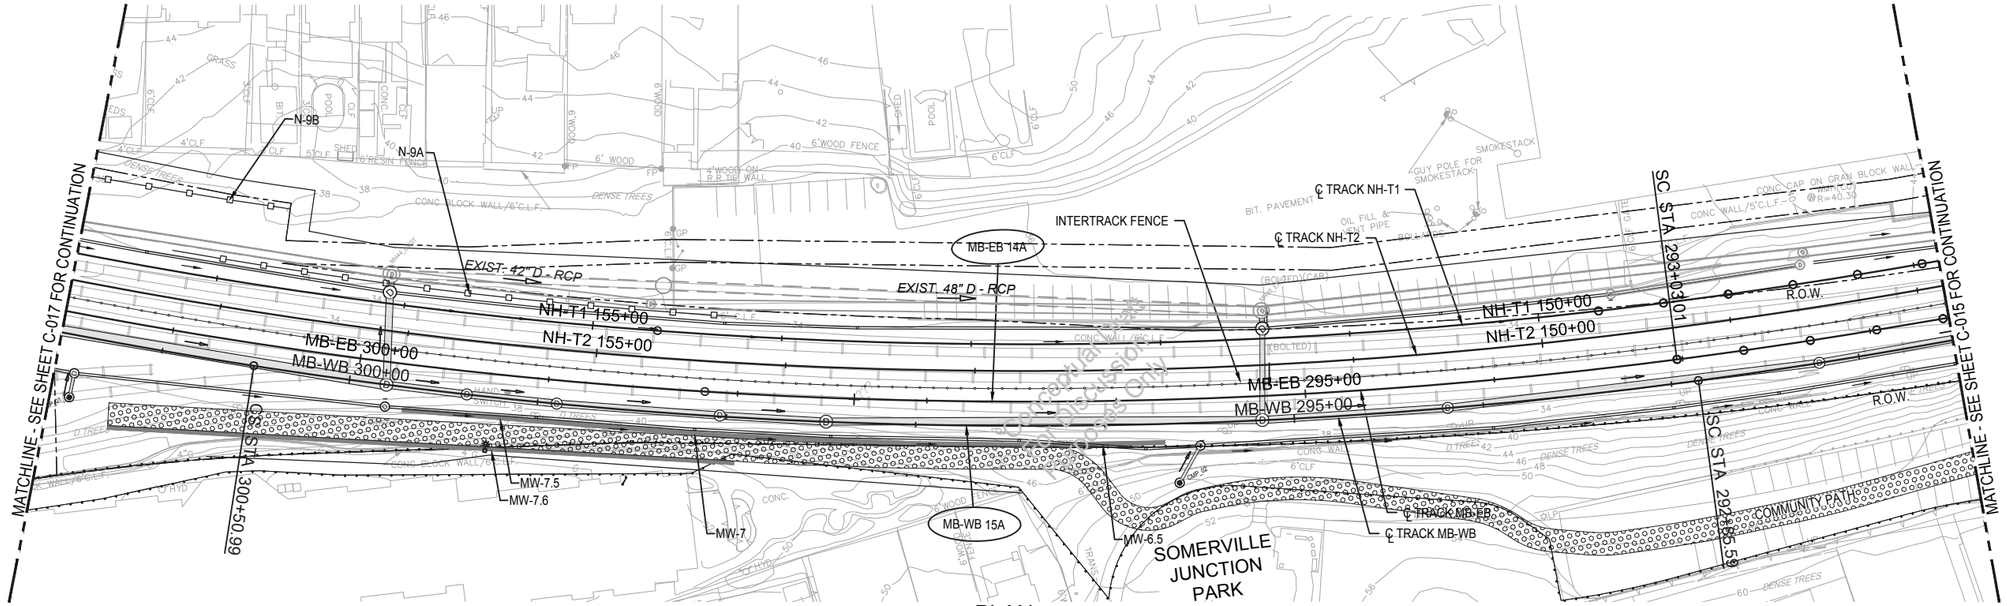

PLAN

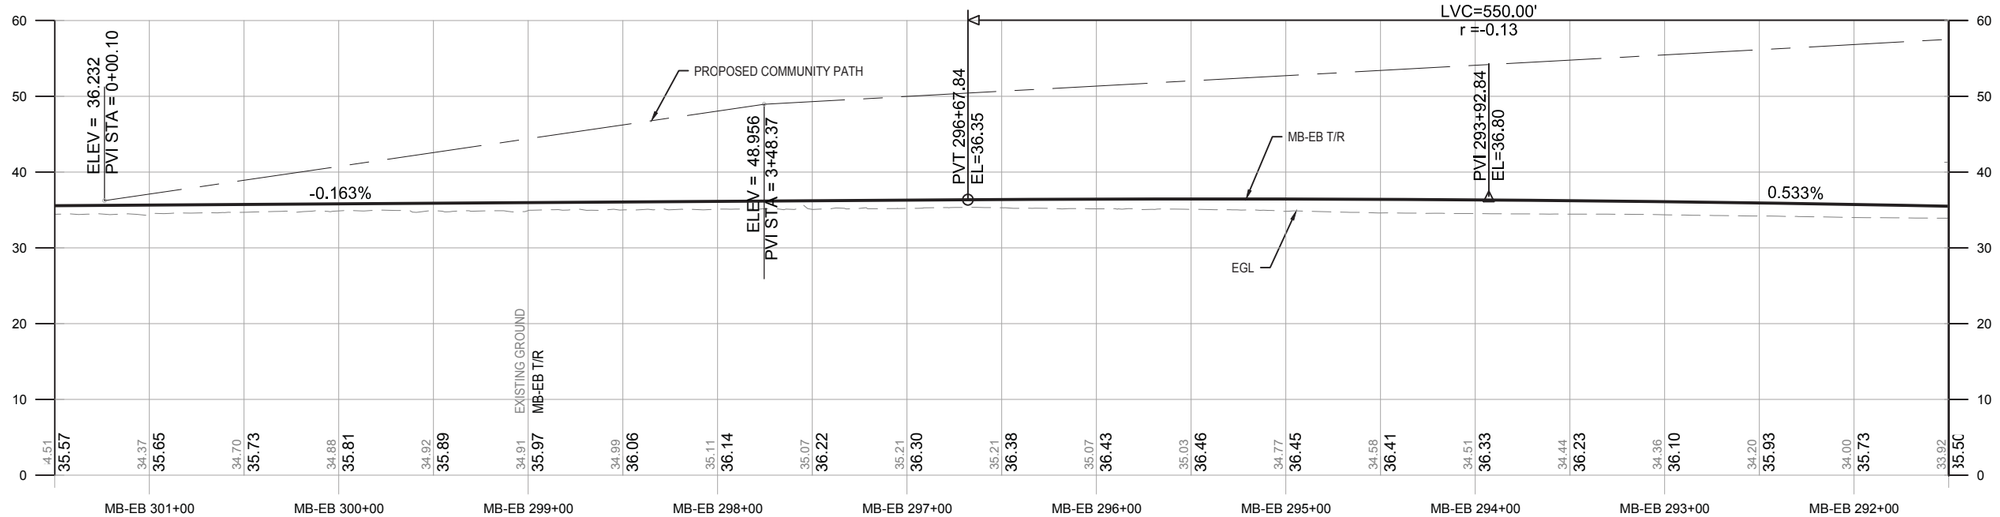

PROFILE

CURVE NO.	MB-EB 14A	MB-WB 15A
R	2690.00 FT	2644.92 FT
Lc	1041.25 FT	765.39 FT
Ls1	425.92 FT	388.00 FT
Ls2	110.00 FT	131.00 FT
Ea	2.00 IN	2.25 IN
Eu	0.39 IN	0.18 IN
V	40 MPH	40 MPH

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 291+50 TO STA MB-EB 301+50

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-016	

PLOTTED: 09/22/17 2:07PM BY:RENEKC
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-4-2009-2022.DWG [C-016] 09/22/17 1:37PM

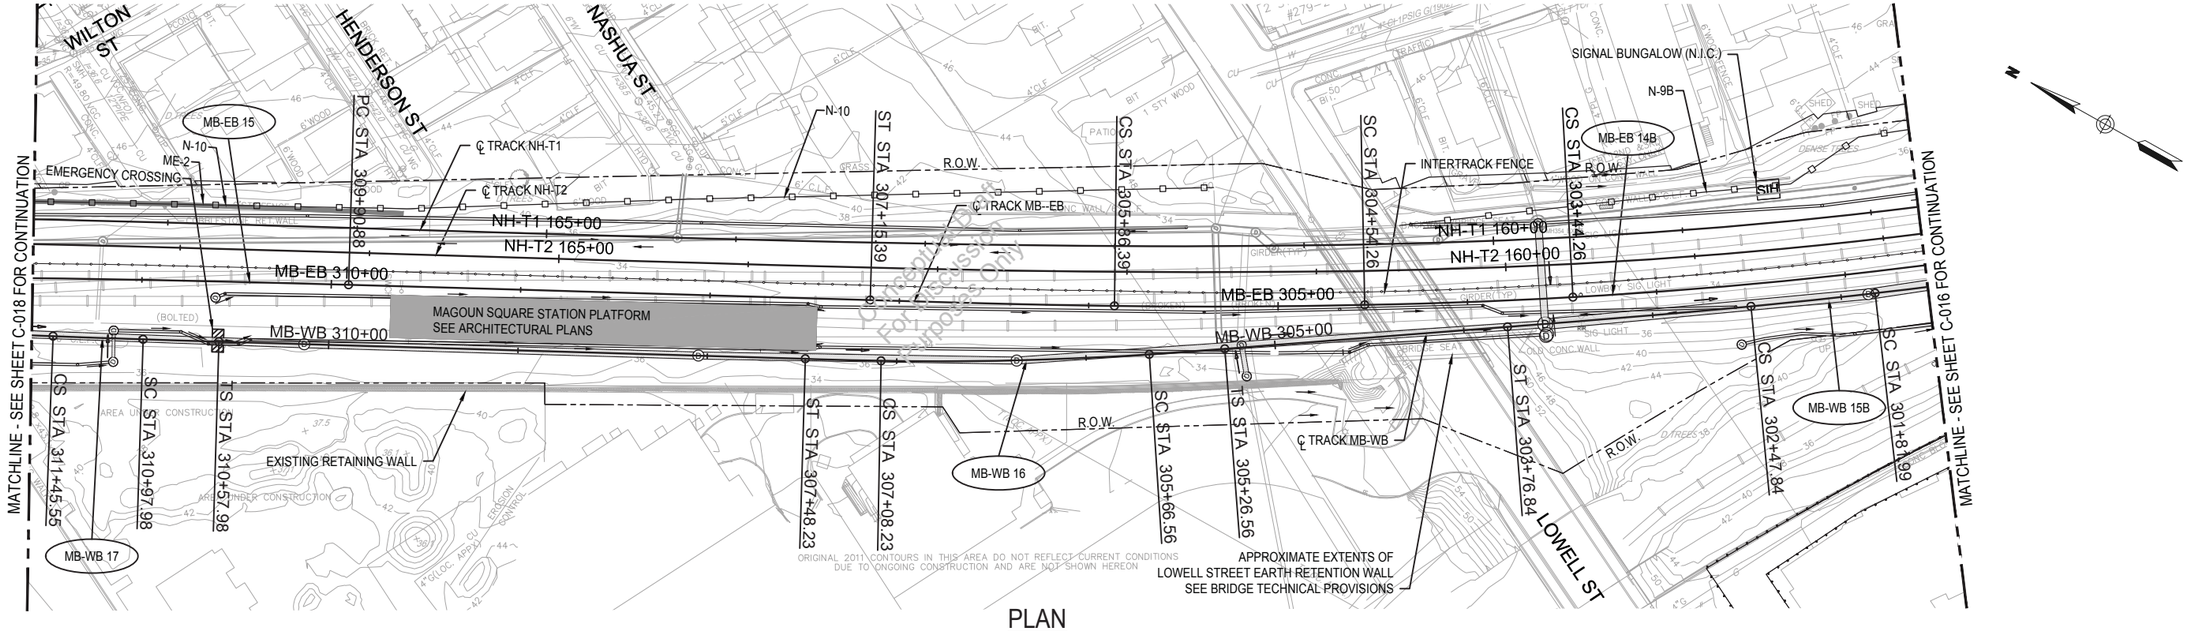

PLAN

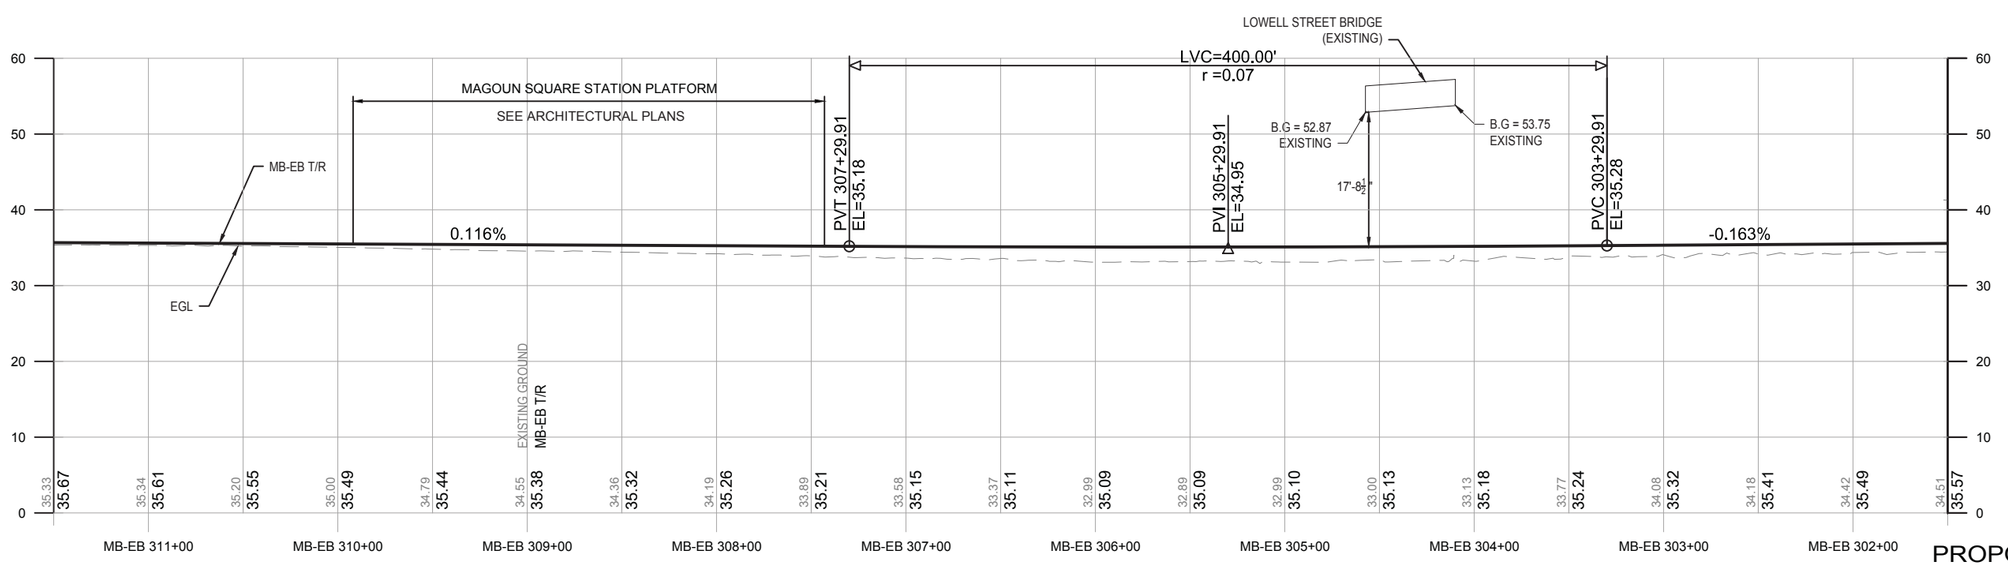

PROFILE

CURVE NO.	MB-EB 14B	MB-EB 15	MB-WB 15B	MB-WB 16	MB-WB 17
R	3900.00 FT	10000.00 FT	3444.88 FT	1700.00 FT	8000.00 FT
Lc	132.13 FT	401.85 FT	65.85 FT	141.68 FT	47.57 FT
Ls1	110.00 FT	0.00 FT	131.00 FT	40.00 FT	40.00 FT
Ls2	129.00 FT	0.00 FT	129.00 FT	40.00 FT	40.00 FT
Ea	1.50 IN	0.00 IN	1.75 IN	1.00 IN	1.00 IN
Eu	0.15 IN	0.49 IN	0.11 IN	0.47 IN	0.25 IN
V	40 MPH	35 MPH	40 MPH	25 MPH	30 MPH

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 301+50 TO STA MB-EB 311+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-017	

PLOTTED: 09/22/17 1:53PM BY:RENEKC
DRAWING: I:\PROPOSALS\2017\0082820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2009-2022.DWG [C-017] 09/22/17 1:37PM

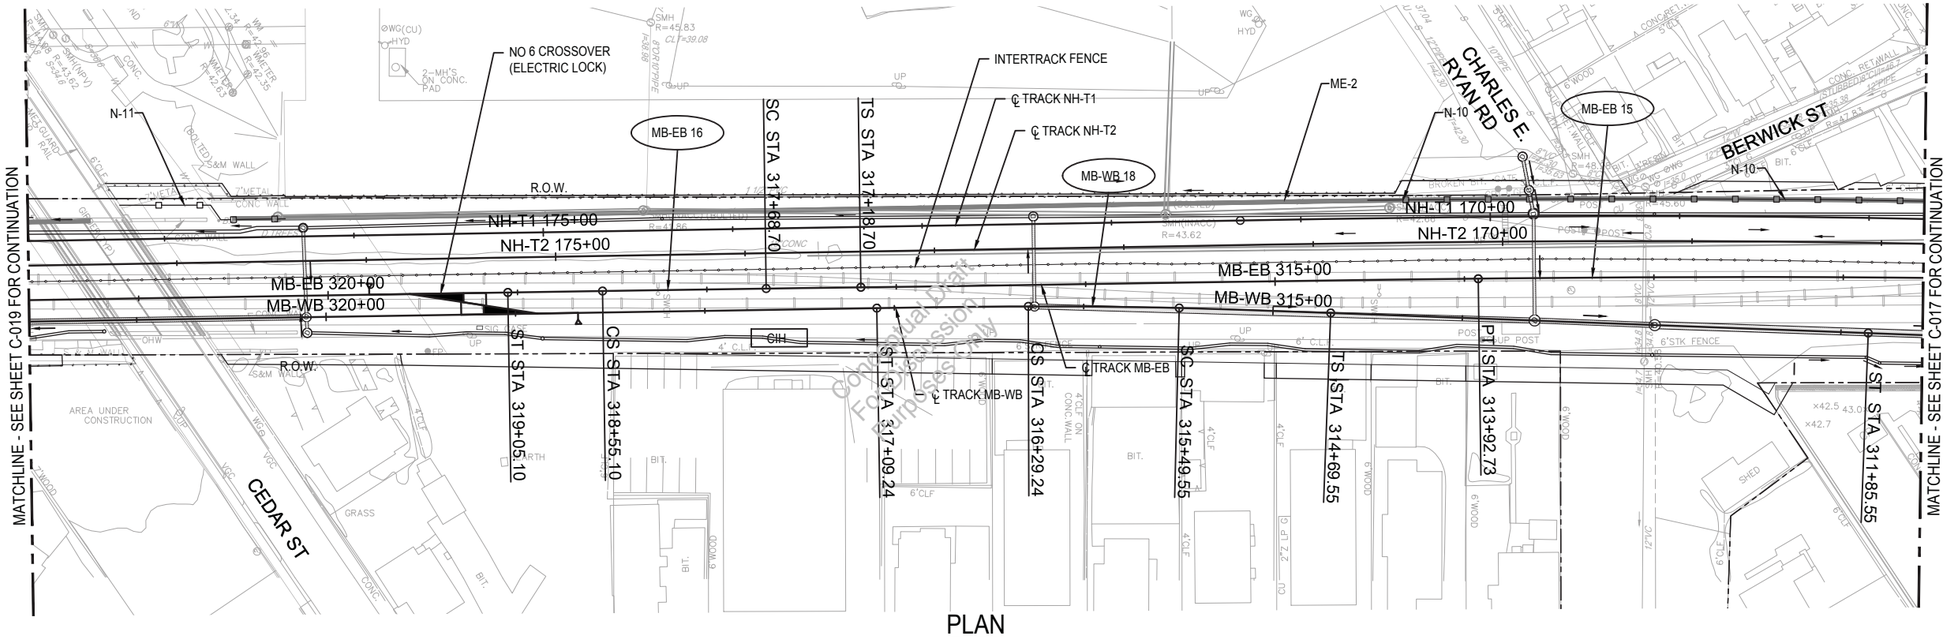

PLAN

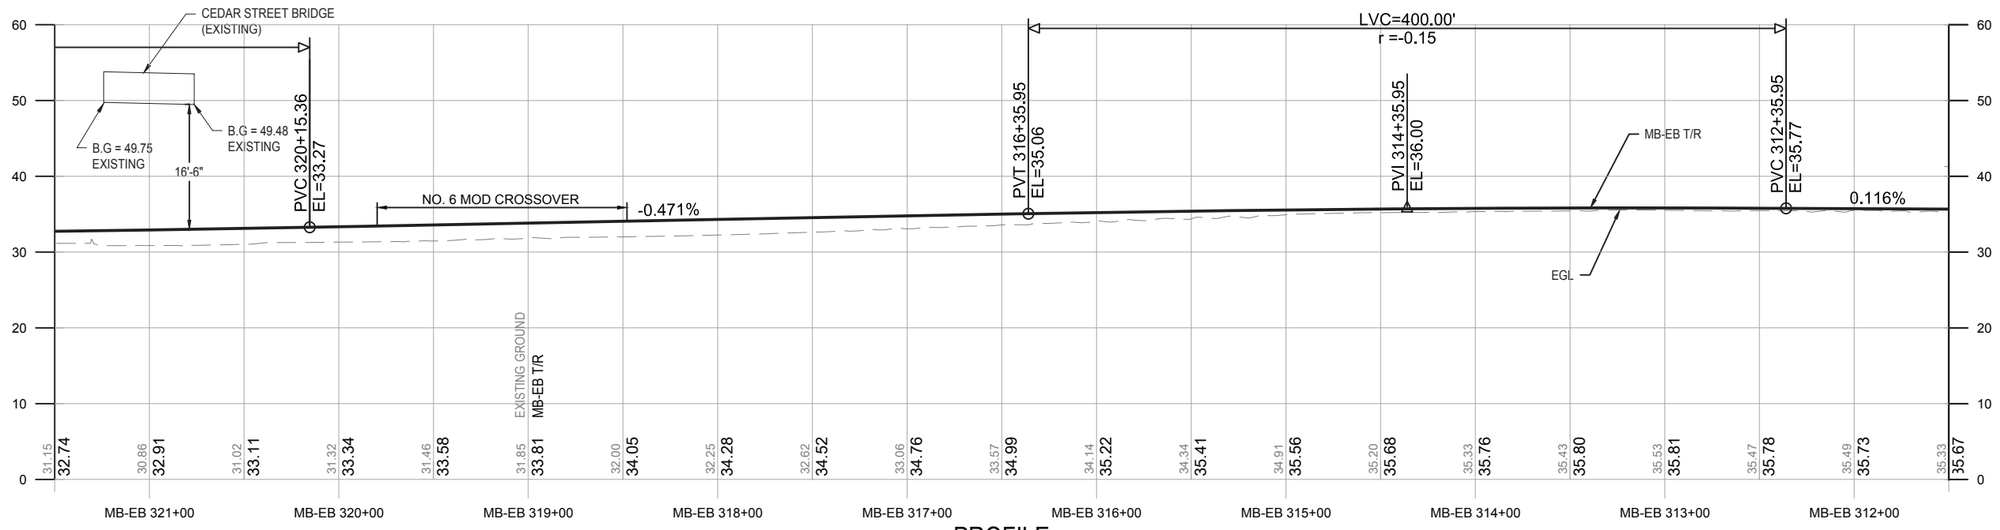

PROFILE

CURVE NO.	MB-EB 15	MB-EB 16	MB-WB 18
R	10000.00 FT	65000.00 FT	3000.00 FT
Lc	401.85 FT	86.40 FT	79.69 FT
Ls1	0.00 FT	50.00 FT	80.00 FT
Ls2	0.00 FT	50.00 FT	80.00 FT
Ea	0.00 IN	0.00 IN	1.75 IN
Eu	0.49 IN	0.15 IN	0.39 IN
V	35 MPH	50 MPH	40 MPH

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 311+50 TO STA MB-EB 321+50


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GLX CONSTRUCTORS


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-018	

PLOTTED: 09/21/17 12:18AM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\0002820 GLX D-B\STV 2017 RFP DESIGN\00_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-H-2009-2022.DWG [C-018] 09/20/17 10:08PM

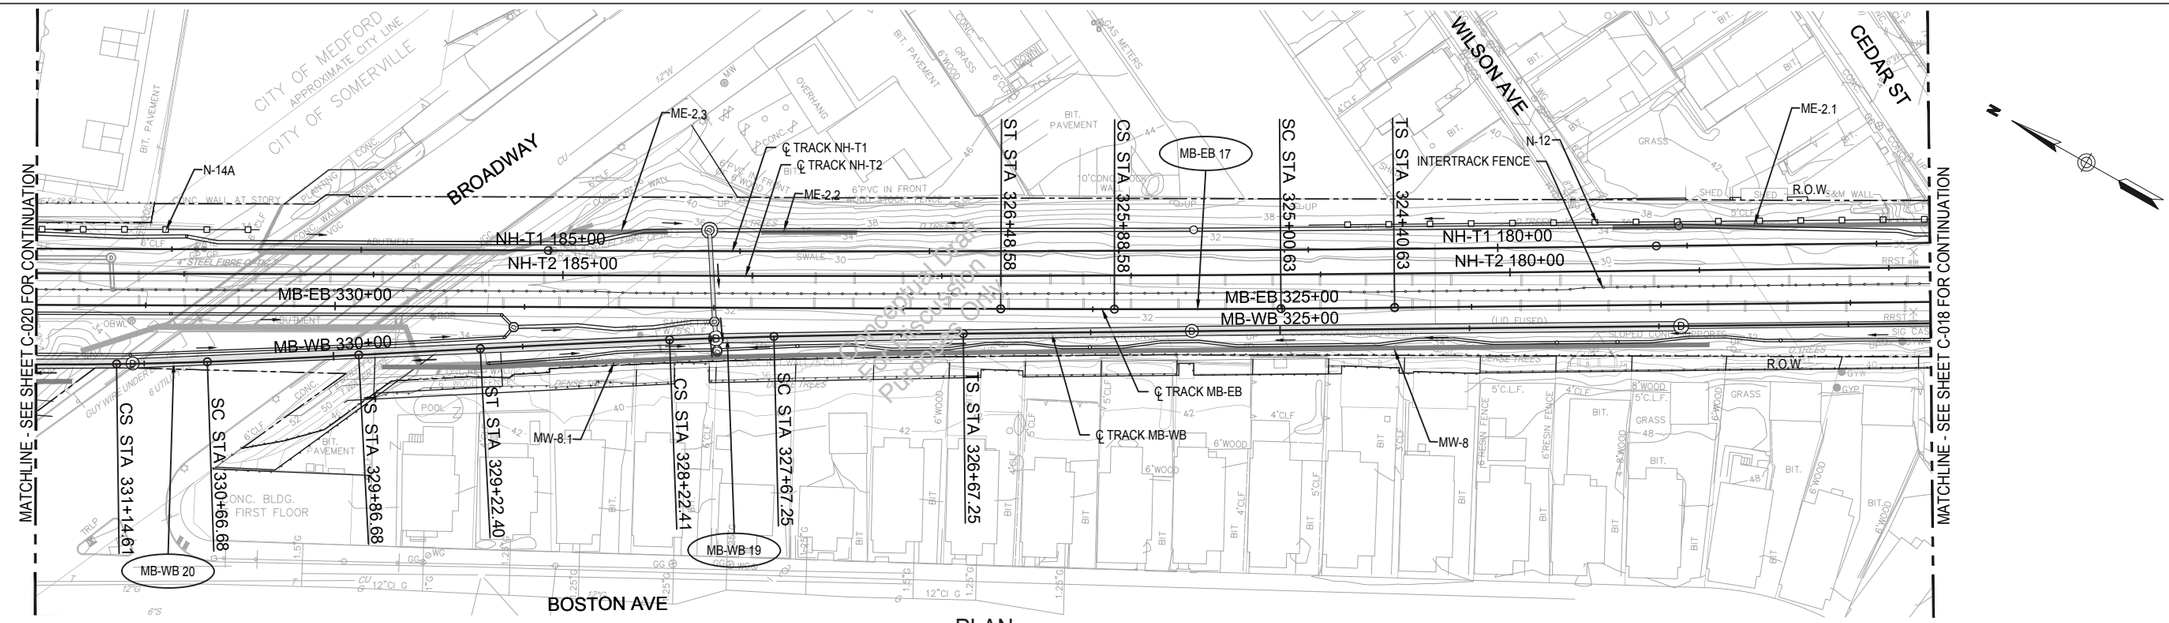

PLAN

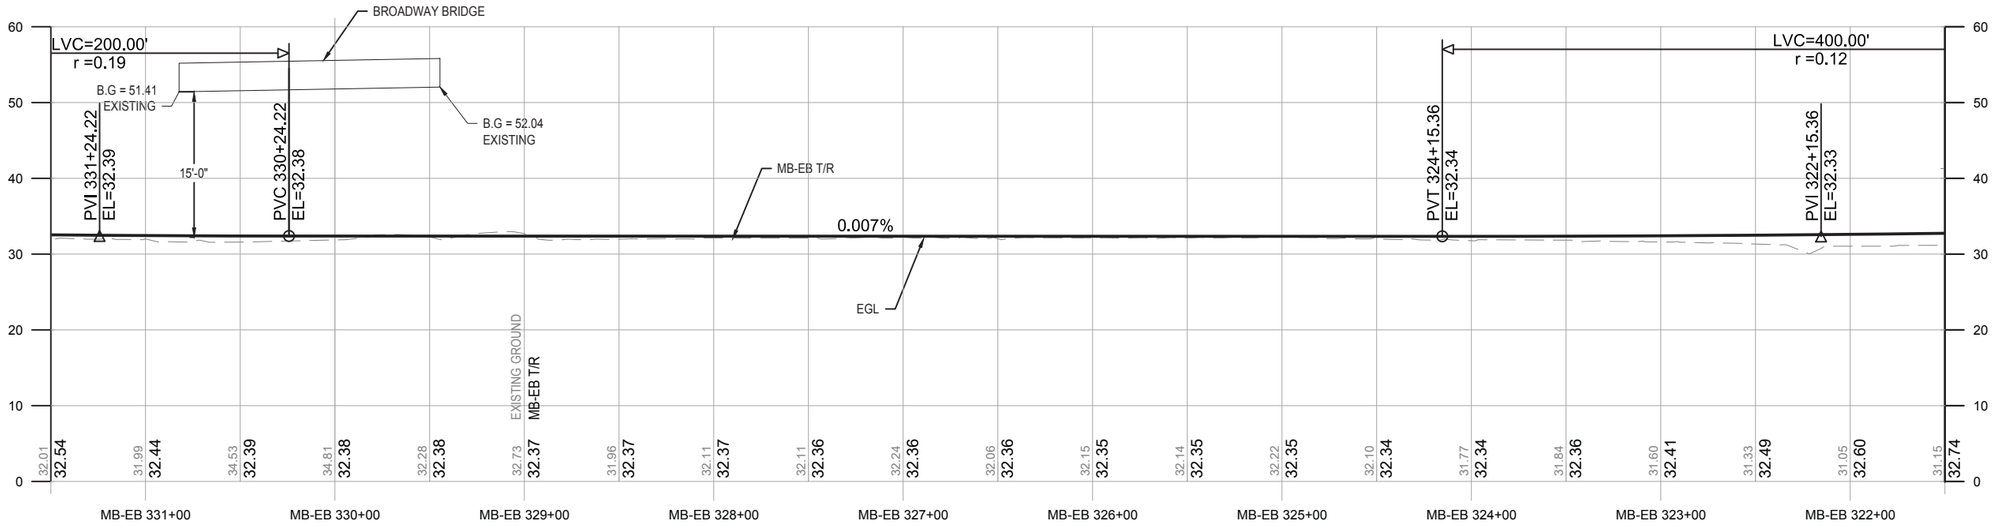

PROFILE

CURVE NO.	MB-EB 17	MB-WB 19	MB-WB 20
R	10000.00 FT	3800.00 FT	2300.00 FT
Lc	87.95 FT	55.15 FT	47.93 FT
Ls1	60.00 FT	100.00 FT	80.00 FT
Ls2	60.00 FT	100.00 FT	80.00 FT
Ea	0.75 IN	1.75 IN	1.75 IN
Eu	0.25 IN	0.39 IN	0.39 IN
V	50 MPH	45 MPH	35 MPH

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 321+50 TO STA MB-EB 331+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-019	

PLOTTED: 09/21/17 12:28AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_GX_TRACK_RAIL\000-RC-2009-2022.DWG [C-019] 09/20/17 10:08PM

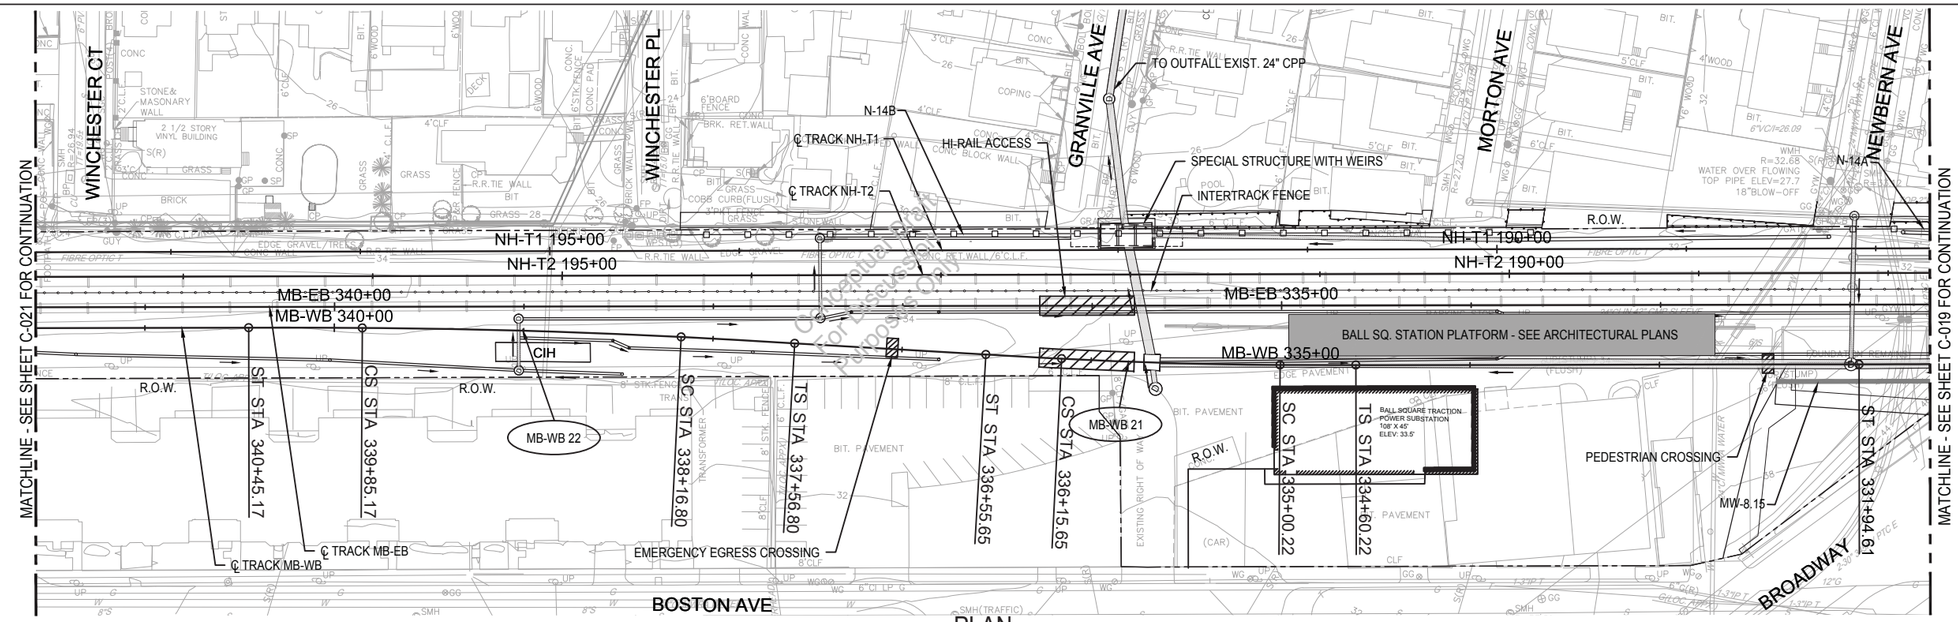

PLAN

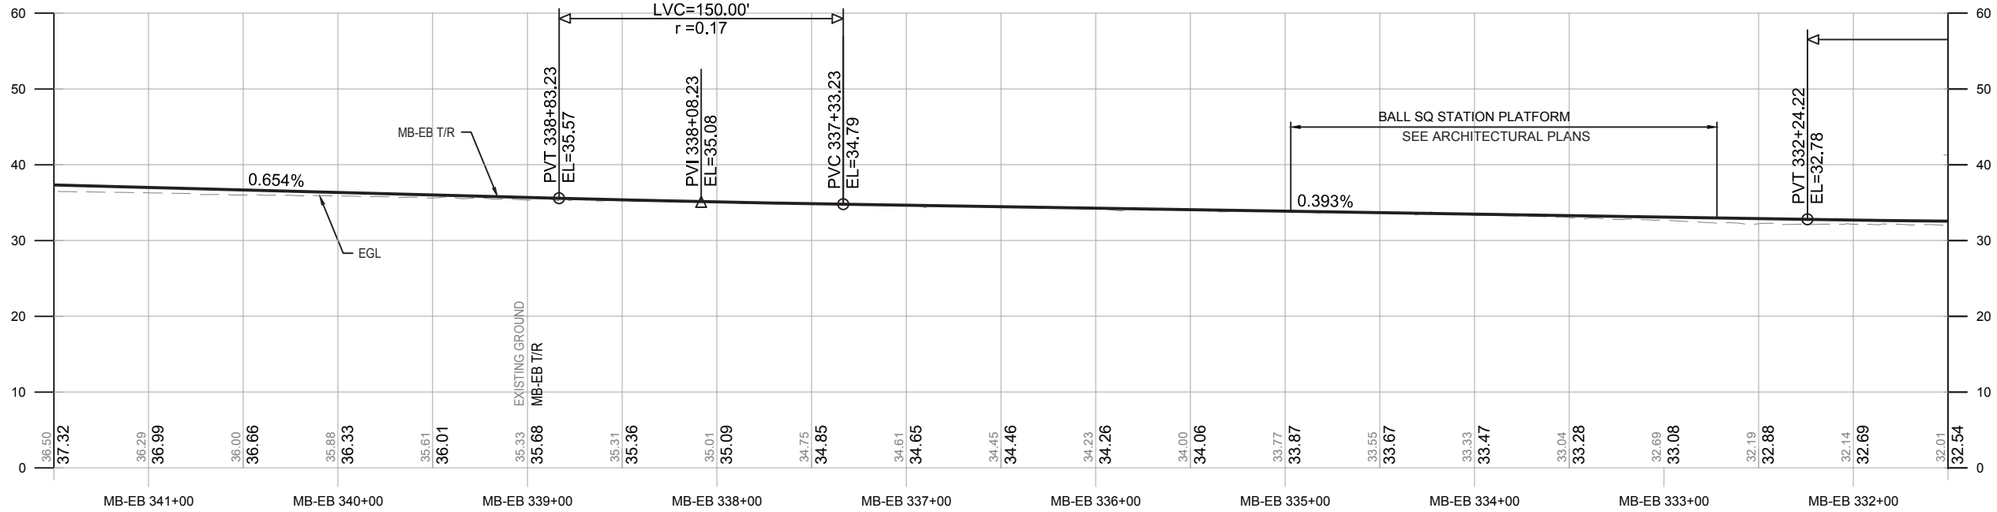

PROFILE

CURVE NO.	MB-WB 21	MB-WB 22
R	2600.00 FT	3820.00 FT
Lc	115.44 FT	168.37 FT
Ls1	40.00 FT	60.00 FT
Ls2	40.00 FT	60.00 FT
Ea	1.00 IN	1.50 IN
Eu	0.42 IN	0.18 IN
V	30 MPH	40 MPH

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 331+50 TO STA MB-EB 341+50

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-020	

PLOTTED: 09/22/17 7:47AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CR_TRACK_RAIL\000-K-2009-2022.DWG [C-020] 09/21/17 8:37PM

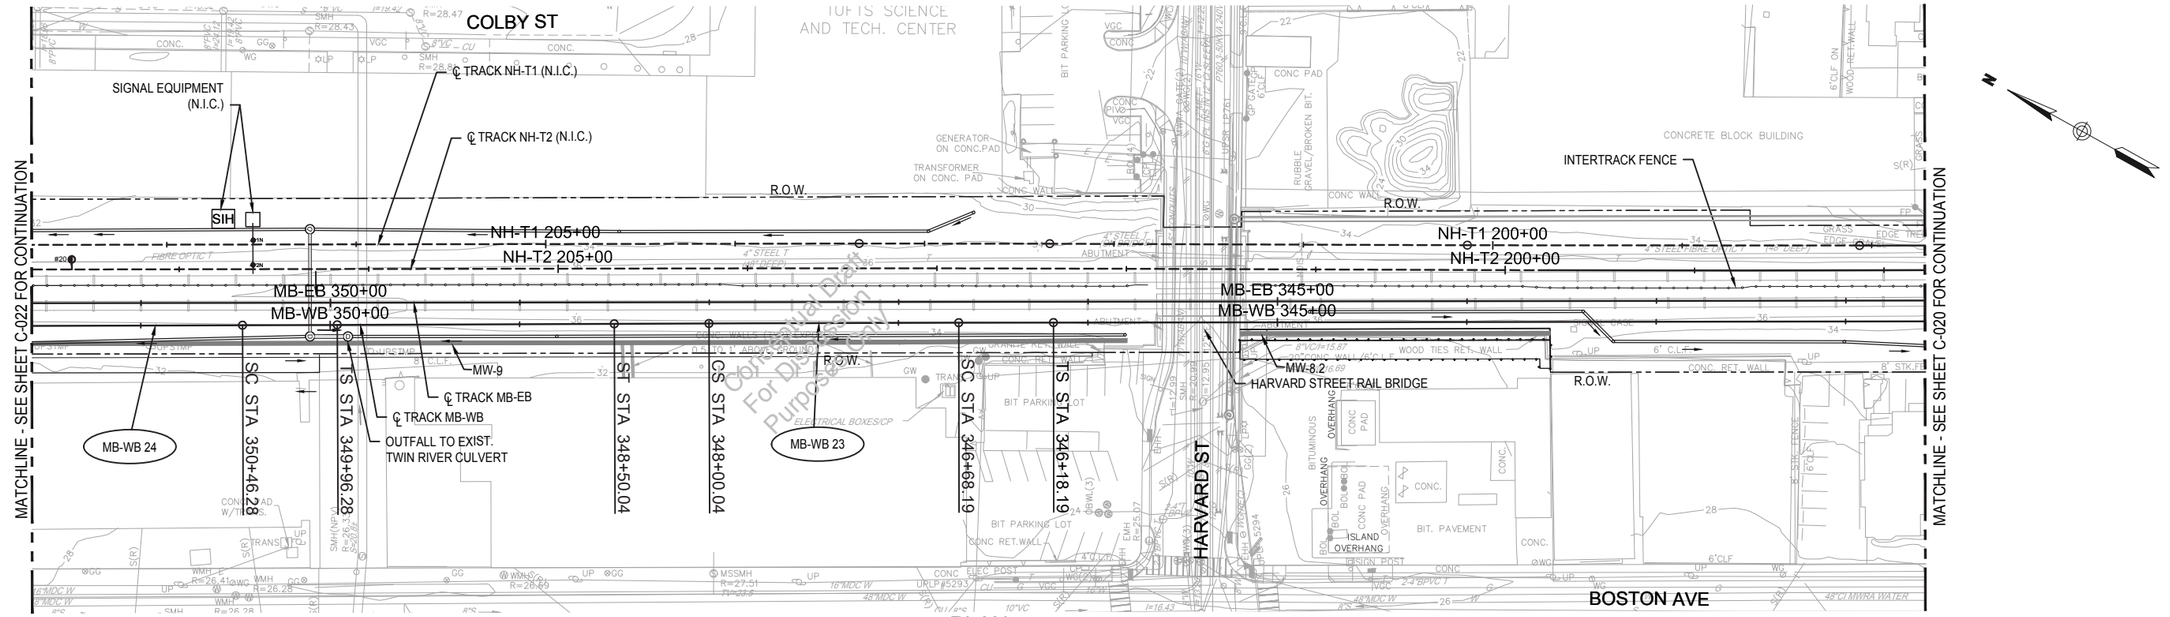

PLAN

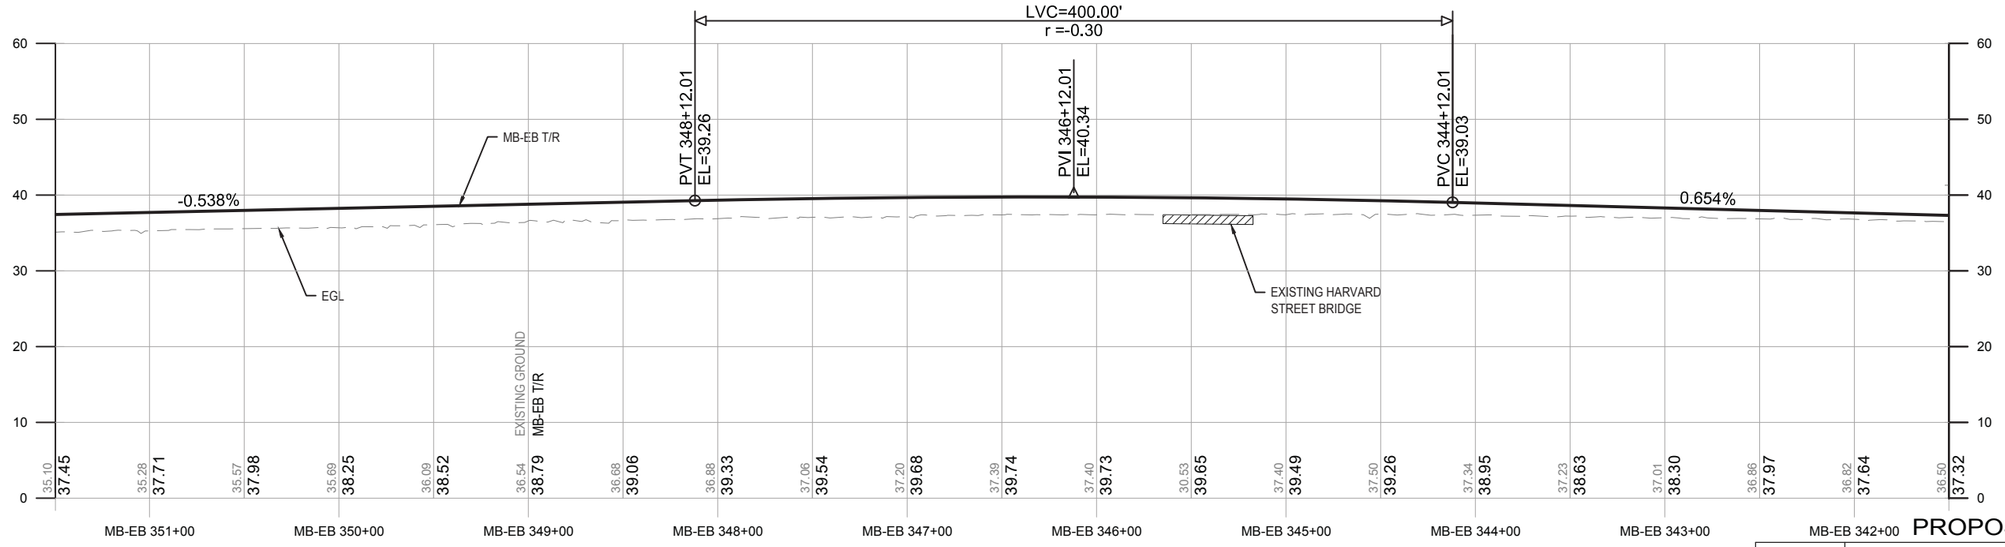

PROFILE

CURVE NO.	MB-WB 22	MB-WB 23	MB-WB 24
R	3820.00 FT	68754.94 FT	68754.94 FT
Lc	168.37 FT	131.84 FT	131.84 FT
Ls1	60.00 FT	50.00 FT	50.00 FT
Ls2	60.00 FT	50.00 FT	50.00 FT
Ea	1.50 IN	0.00 IN	0.00 IN
Eu	0.18 IN	0.15 IN	0.15 IN
V	40 MPH	50 MPH	50 MPH

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 341+50 TO STA MB-EB 351+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-021	

PLOTTED: 09/22/17 8:03AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2009-2022.DWG [C-021] 09/21/17 8:37PM

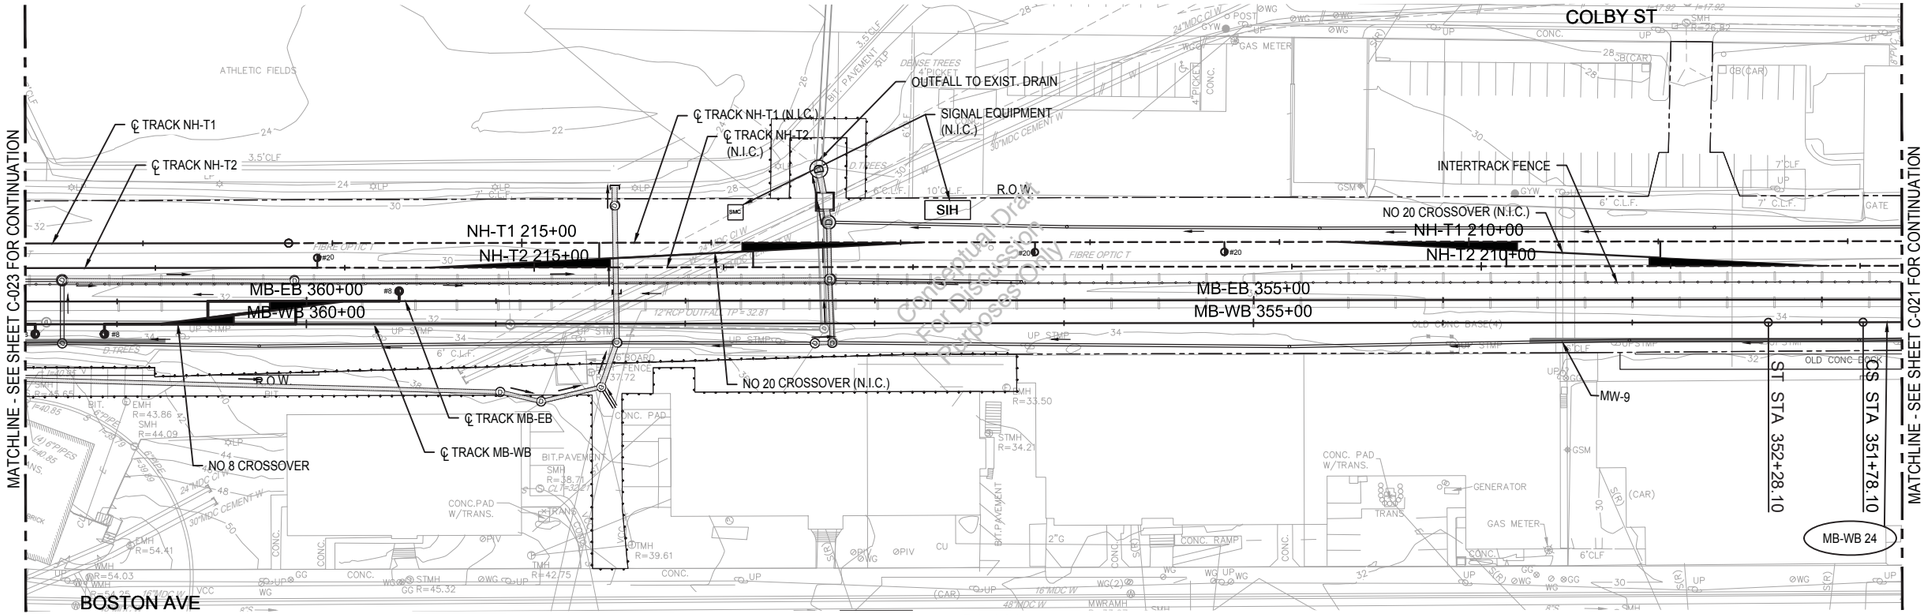

PLAN

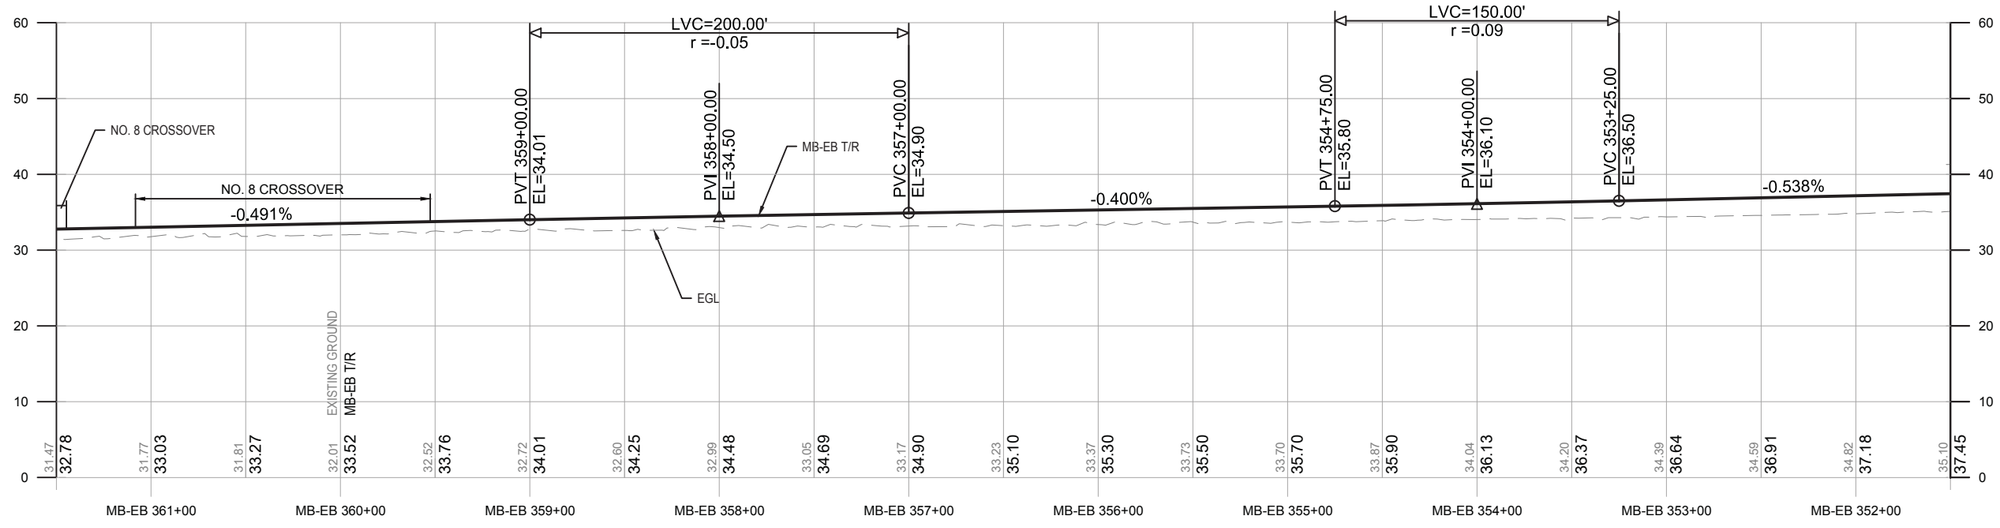

PROFILE

CURVE NO.	MB-WB 24
R	68754.94 FT
Lc	131.84 FT
Ls1	50.00 FT
Ls2	50.00 FT
Ea	0.00 IN
Eu	0.15 IN
V	50 MPH

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 351+50 TO STA MB-EB 361+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-022	

PLOTTED: 09/22/17 8:14AM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\00628200 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2009-2022.DWG [C-022] 09/21/17 9:37PM

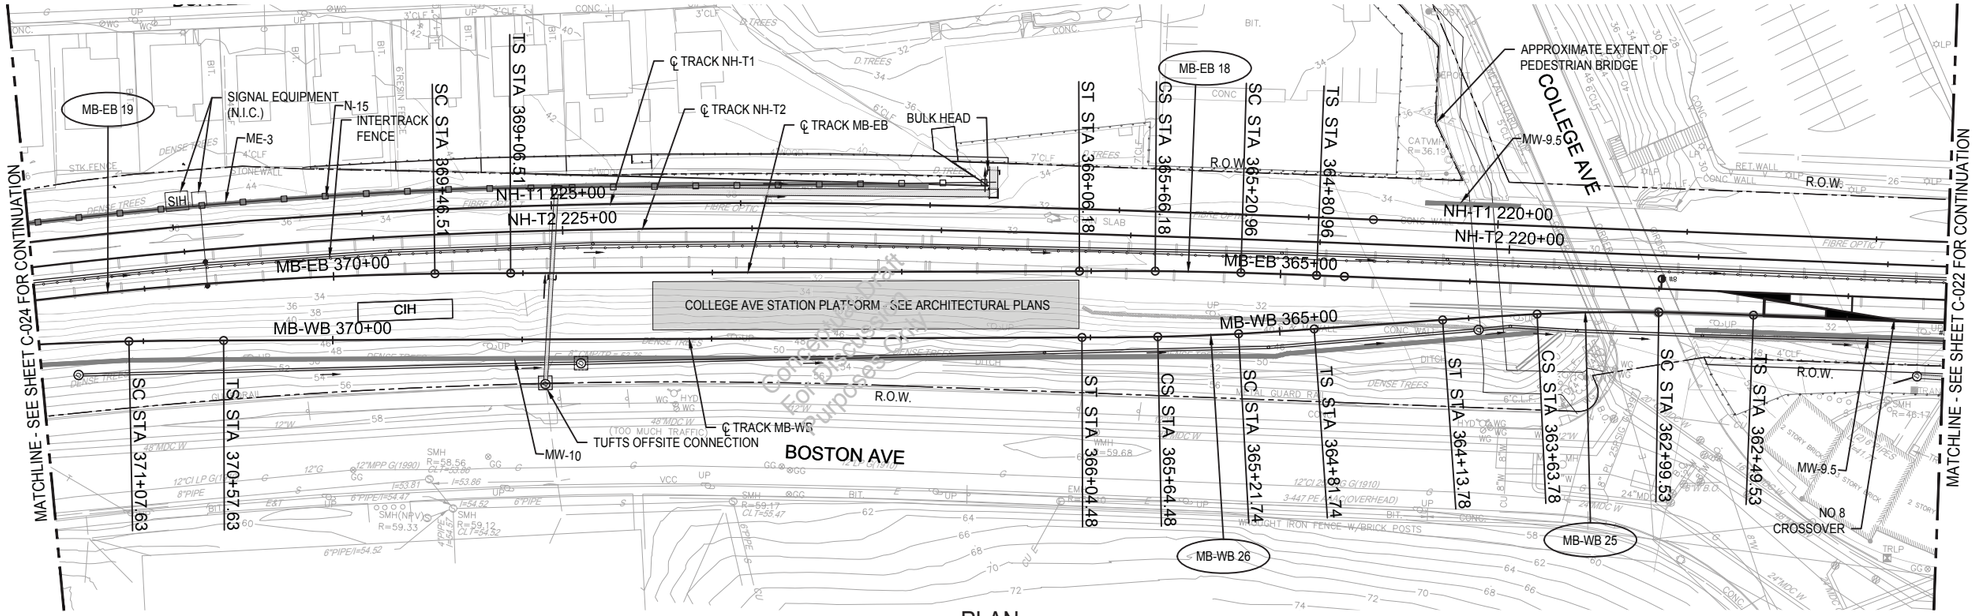

PLAN

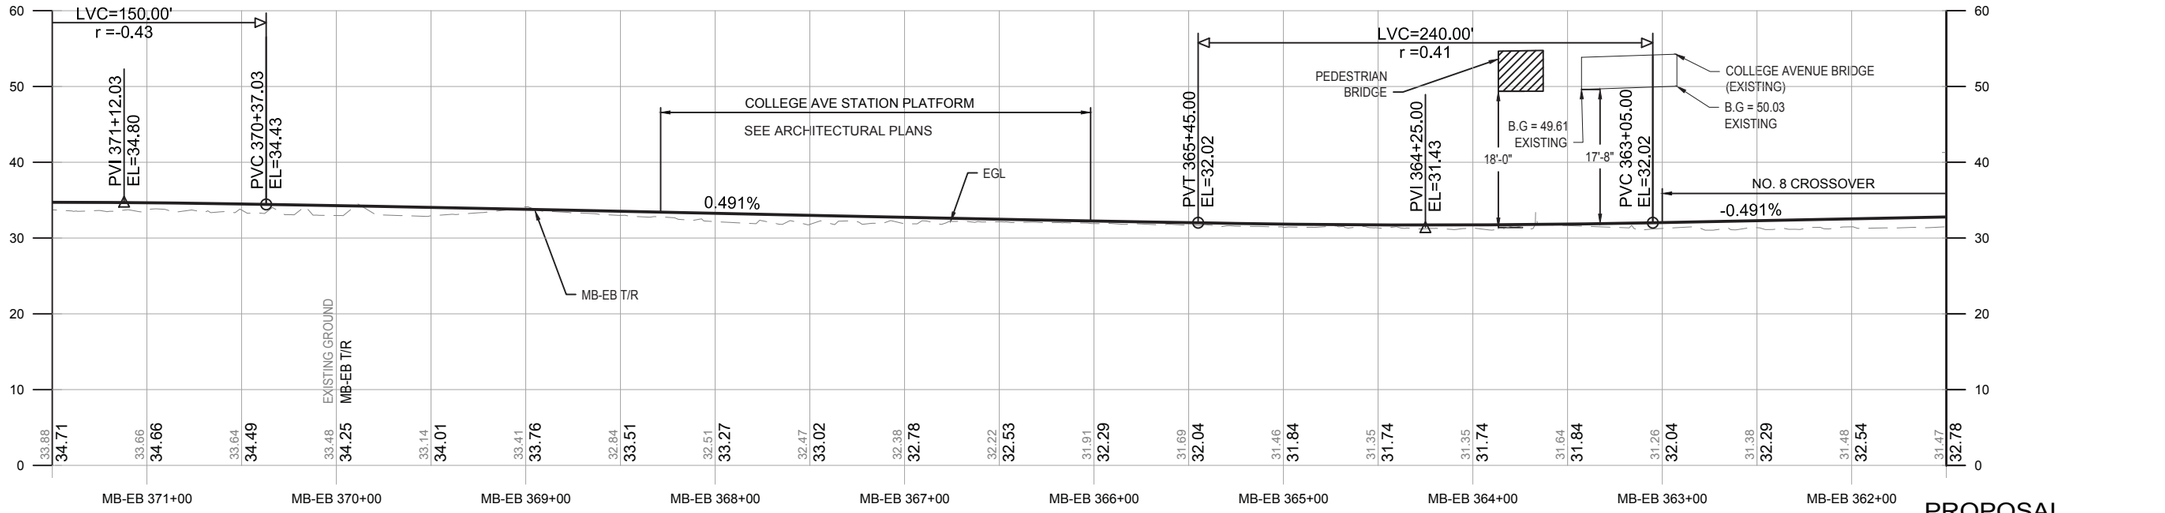

PROFILE

CURVE NO.	MB-EB 18	MB-EB 19	MB-WB 25	MB-WB 26
R	2000.00 FT	2000.00 FT	1050.00 FT	1250.00 FT
Lc	45.22 FT	292.96 FT	64.25 FT	42.74 FT
Ls1	40.00 FT	40.00 FT	50.00 FT	40.00 FT
Ls2	40.00 FT	40.00 FT	50.00 FT	40.00 FT
Ea	1.00 IN	1.25 IN	2.00 IN	1.00 IN
Eu	0.25 IN	0.34 IN	0.39 IN	0.50 IN
V	25 MPH	25 MPH	25 MPH	20 MPH

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH CORRIDOR PLAN AND PROFILE STA MB-EB 361+50 TO STA MB-EB 371+50

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


GV20170258-276

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


SCALE: AS NOTED | DRAWN BY: CRR | DESIGN BY: PJB | CHECK BY: JEB | PLAN NO. . | ISSUE

DATE: SEPT. 28, 2017 | SHEET: C-023

PLOTTED: 09/21/17 1:06AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\Q062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAL\000-K-2009-2022.DWG [C-023] 09/20/17 10:08PM

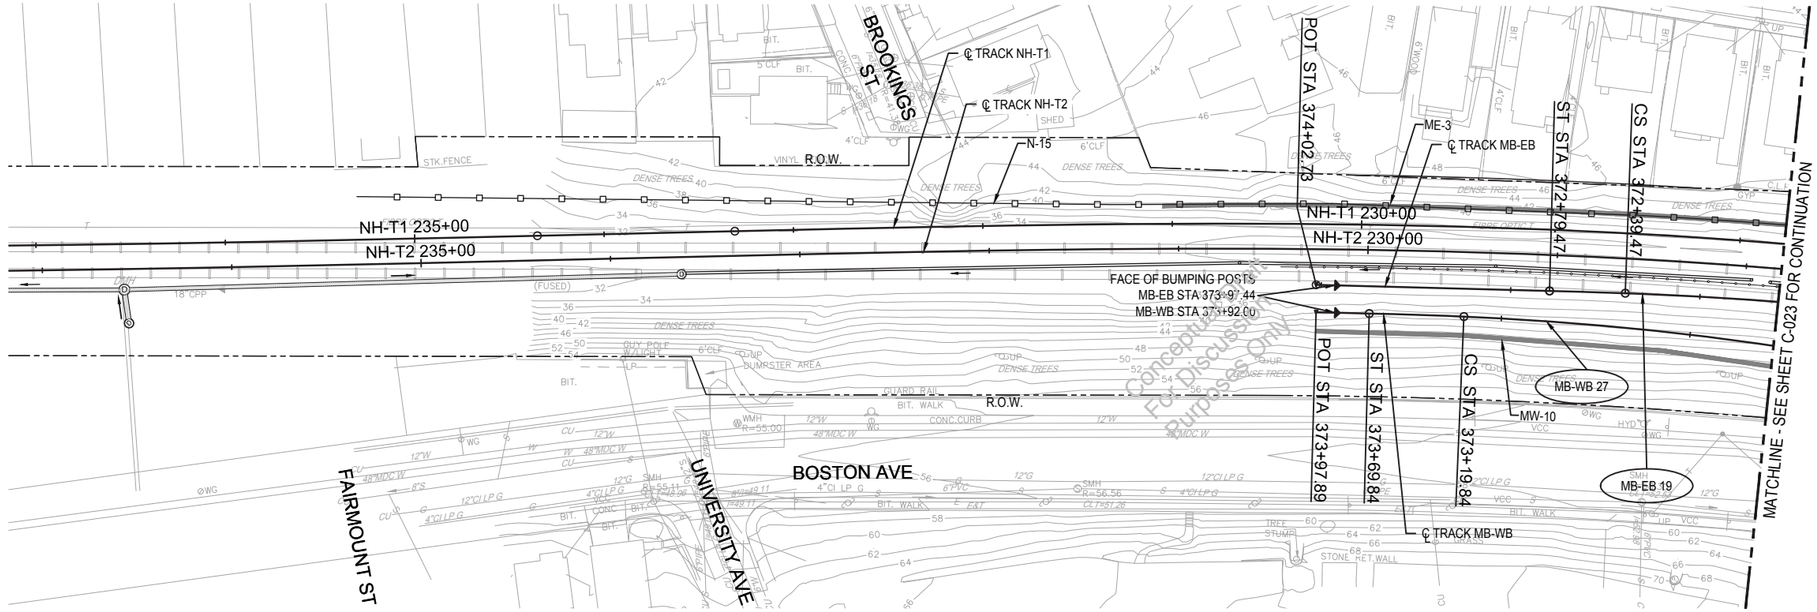

PLAN

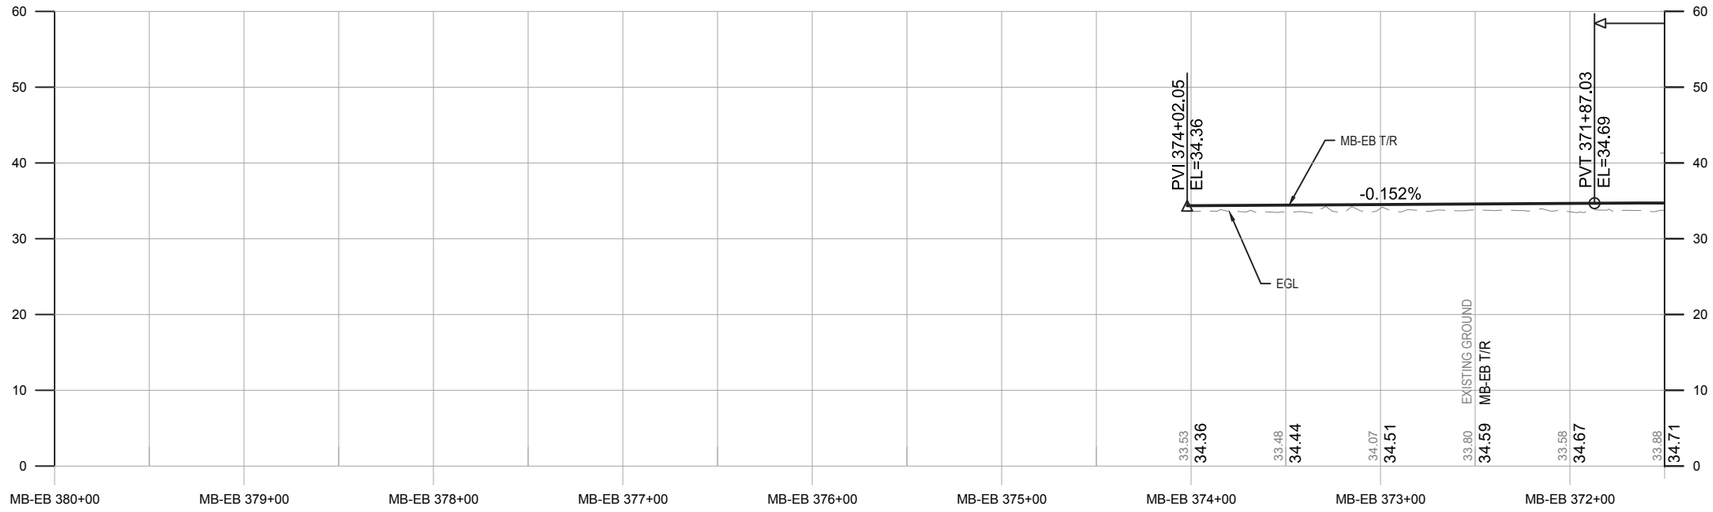

PROFILE

CURVE NO.	MB-EB 19	MB-WB 27
R	2000.00 FT	1575.00 FT
Lc	292.96 FT	212.21 FT
Ls1	40.00 FT	50.00 FT
Ls2	40.00 FT	50.00 FT
Ea	1.25 IN	0.75 IN
Eu	0.34 IN	0.32 IN
V	25 MPH	20 MPH

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

NOTES:

1. REFER TO SHEETS C-033 TO C-049 FOR NEW HAMPSHIRE MAINLINE ALIGNMENT AND PROFILE.
2. THE MB-WB T/R TRACK PROFILE TO BE THE SAME AS MB-EB T/R TRACK PROFILE.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MEDFORD BRANCH
CORRIDOR PLAN AND PROFILE
STA MB-EB 371+50 TO STA MB-EB 380+00


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-024	


PLOTTED: 09/21/17 1:14AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\C0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_GX_TRACK_RAIL\00D-KC-2009-2022.DWG [C-024] 09/20/17 10:08PM

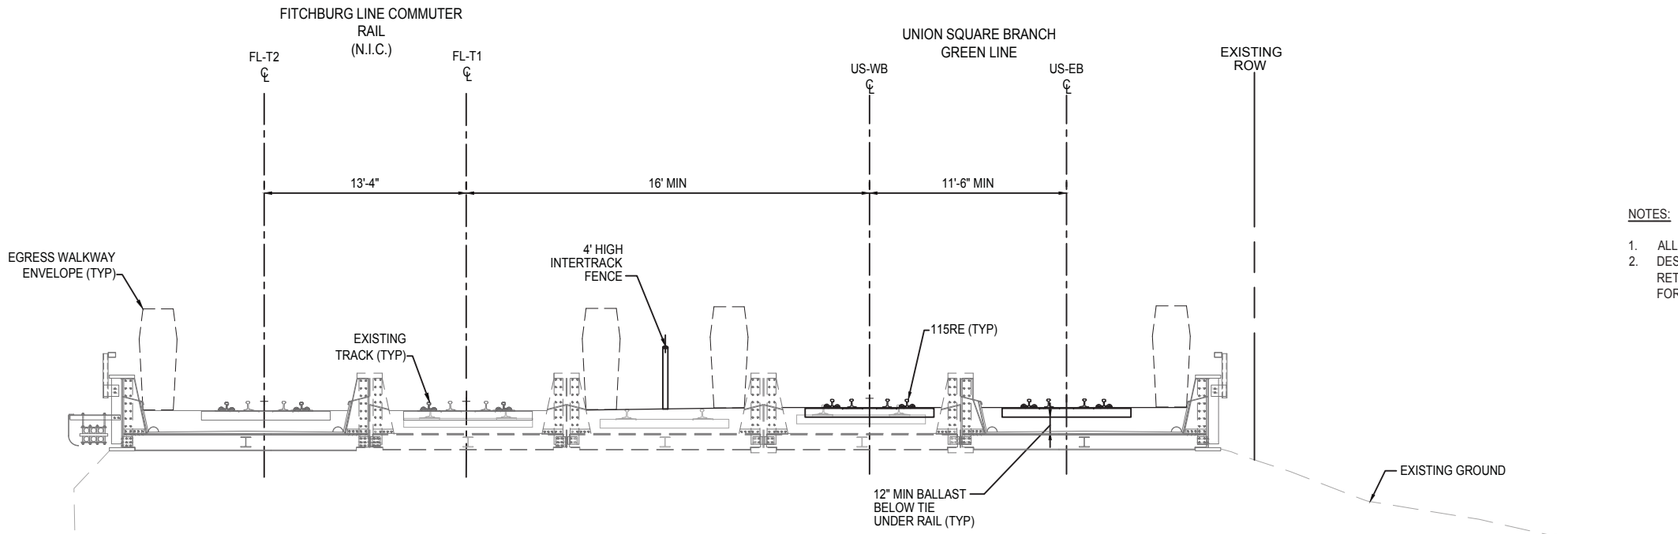

MEDFORD STREET RAIL BRIDGE TYPICAL SECTION
REFER TO CONTRACT E22CN01 FOR BRIDGE DETAILS

NOTES:

1. ALL CROSS SECTIONS SHOWN FACING UP-STATION.
2. DESIGN-BUILDER SHALL DESIGN AND CONSTRUCT RETAINING WALL. RETAINING WALL IS PROVIDED FOR REFERENCE.

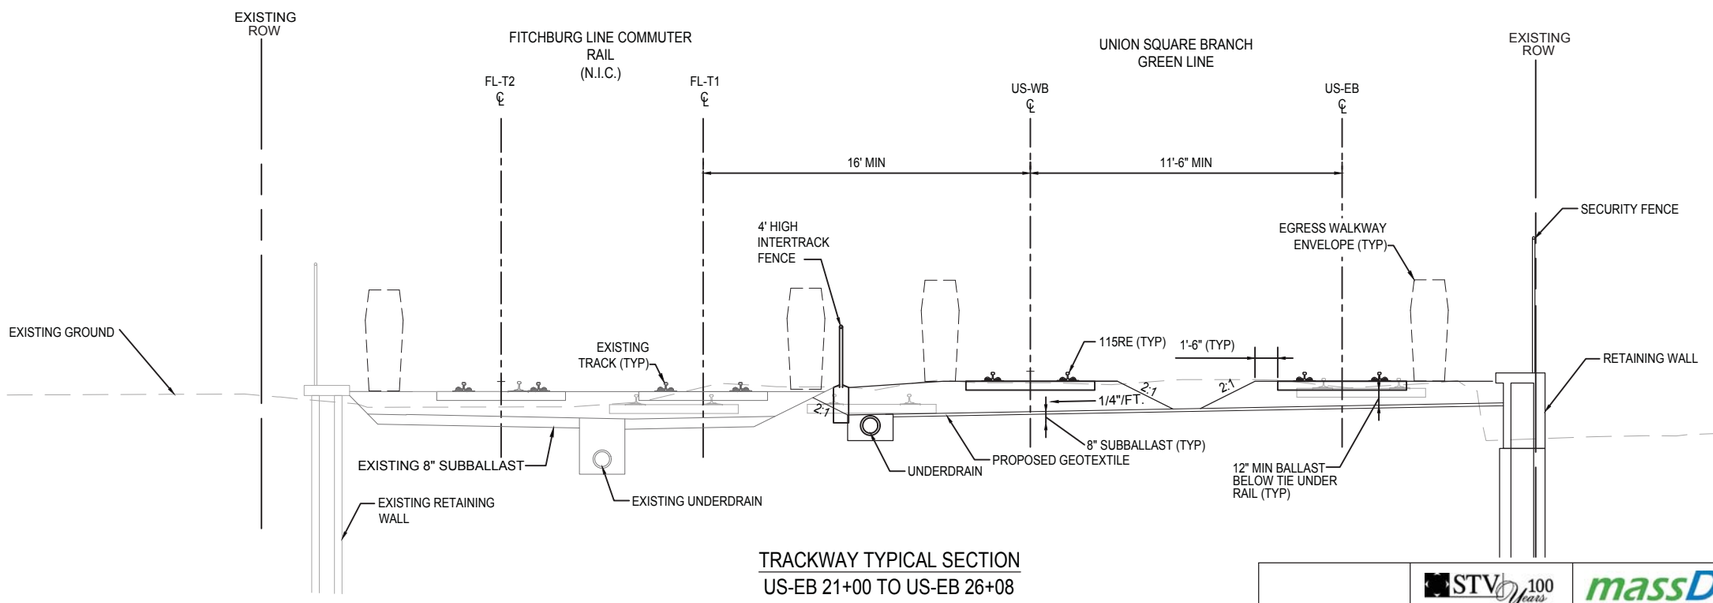

TRACKWAY TYPICAL SECTION
US-EB 21+00 TO US-EB 26+08

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


UNION SQUARE BRANCH
CORRIDOR SECTIONS
SHEET 1

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: NO SCALE	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-025	

PLOTTED: 09/21/17 2:16PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0082820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-4-2050.DWG [C-025] 09/20/17 10:09PM

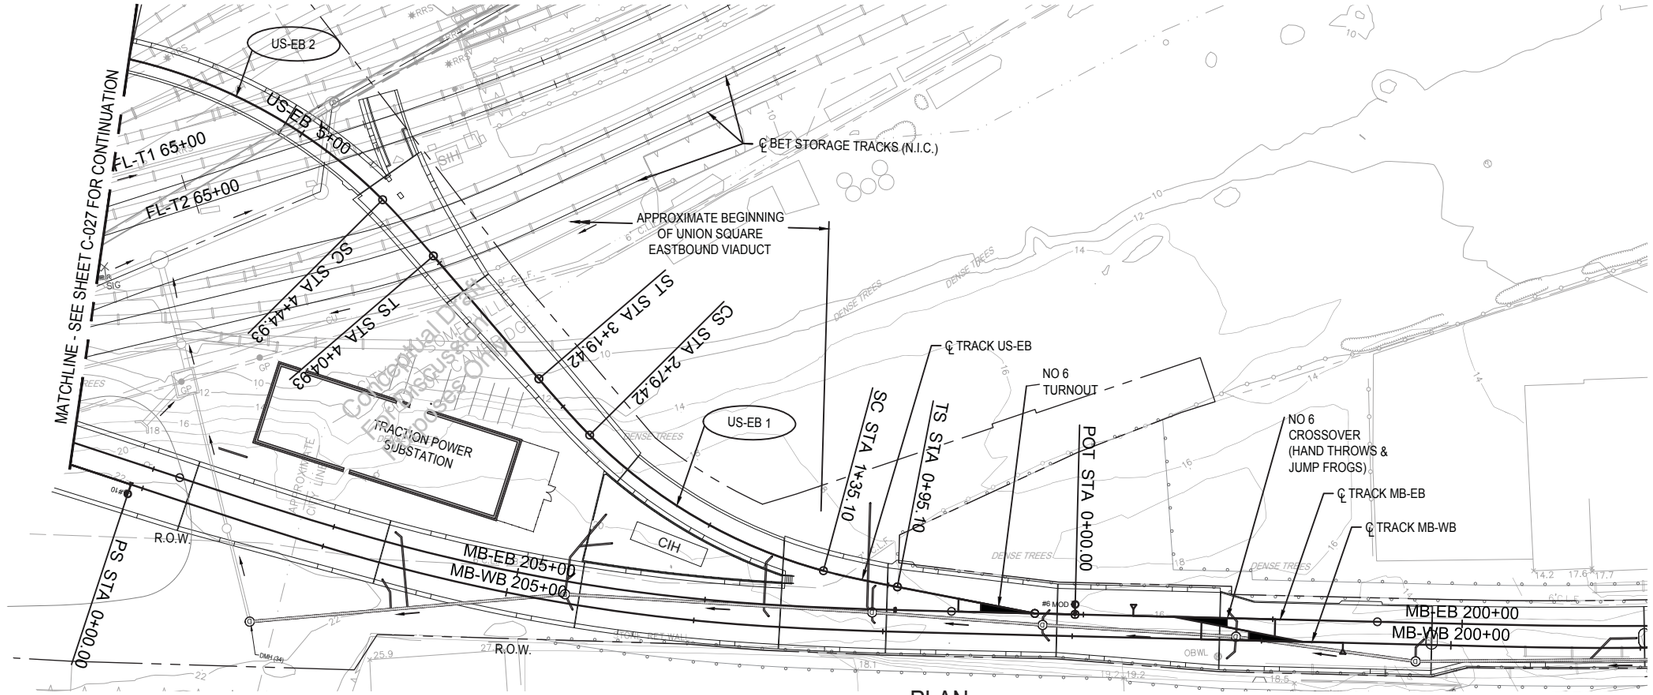

PLAN

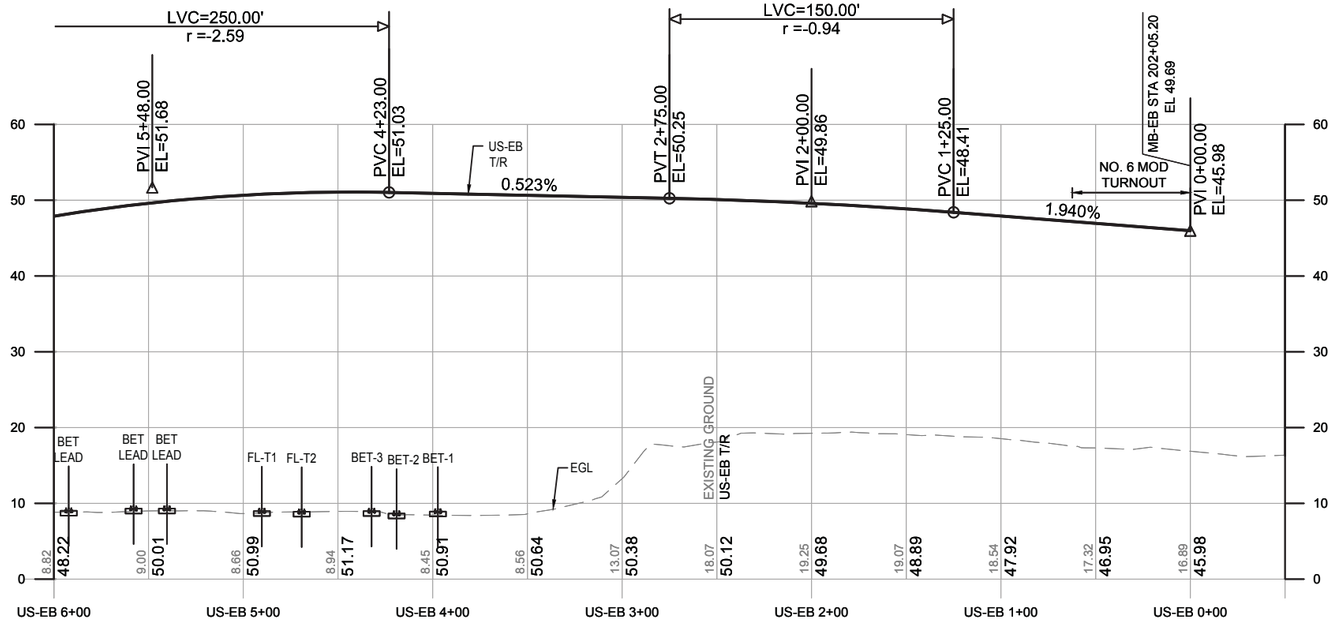

PROFILE

CURVE NO.	US-EB 1	US-EB 2
R	275.00 FT	275.00 FT
Lc	144.32 FT	380.64 FT
Ls1	40.00 FT	40.00 FT
Ls2	40.00 FT	40.00 FT
Ea	1.00 IN	1.00 IN
Eu	0.46 IN	0.46 IN
V	10 MPH	10 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. REFER TO SHEETS C-050 TO C-055 FOR YARD LEAD ALIGNMENT AND PROFILE.
3. REFER TO SHEET C-056 FOR DRAINAGE FROM STA 0+00 TO STA 6+00.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

UNION SQUARE BRANCH
CORRIDOR PLAN AND PROFILE
STA US-EB 0+00 TO STA US-EB 6+00


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-026	

PLOTTED: 09/21/17 1:21AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2061-2066.DWG [C-026] 09/20/17 10:23PM

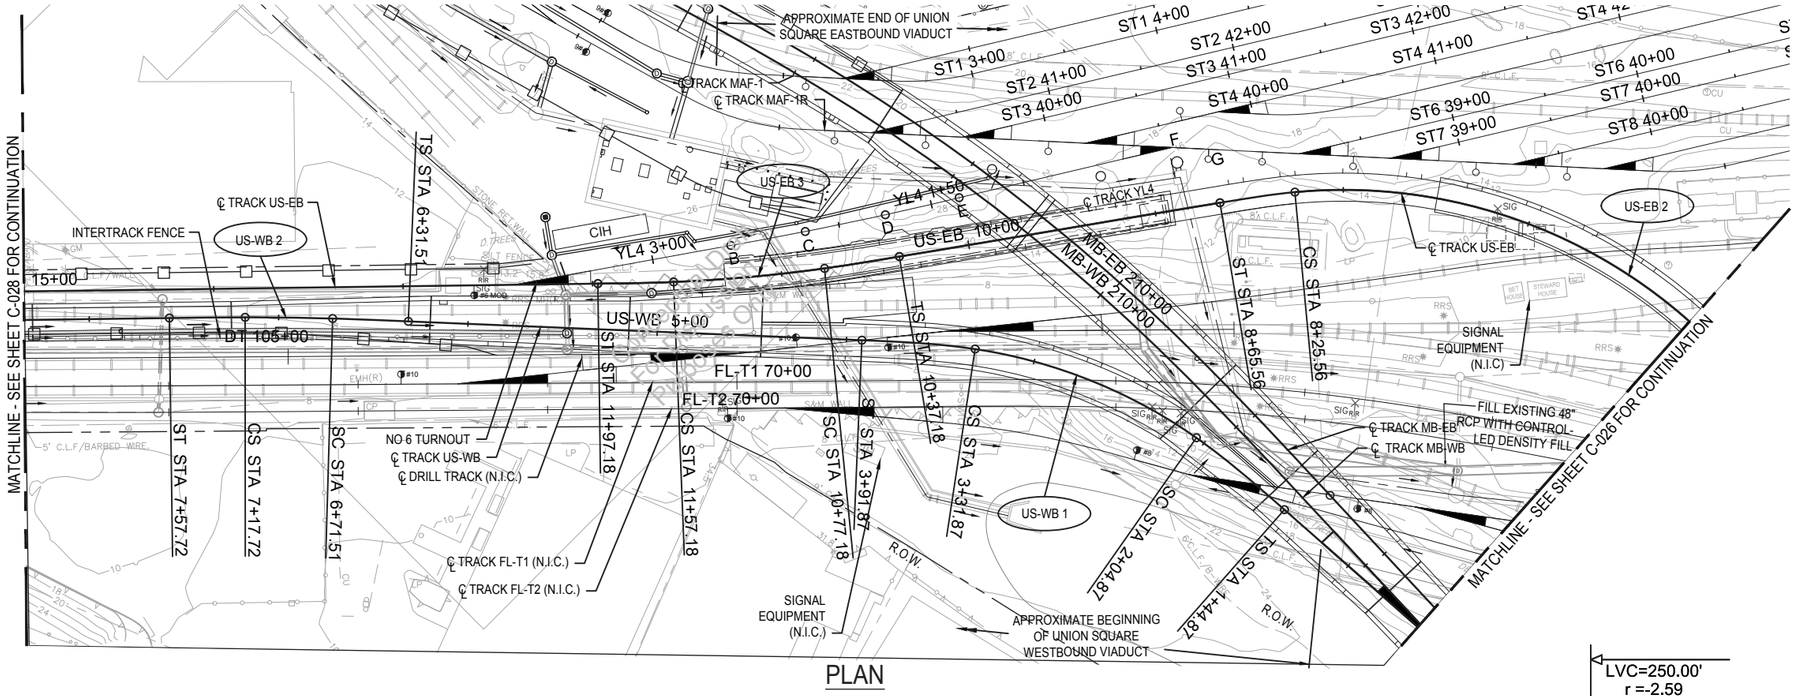

PLAN

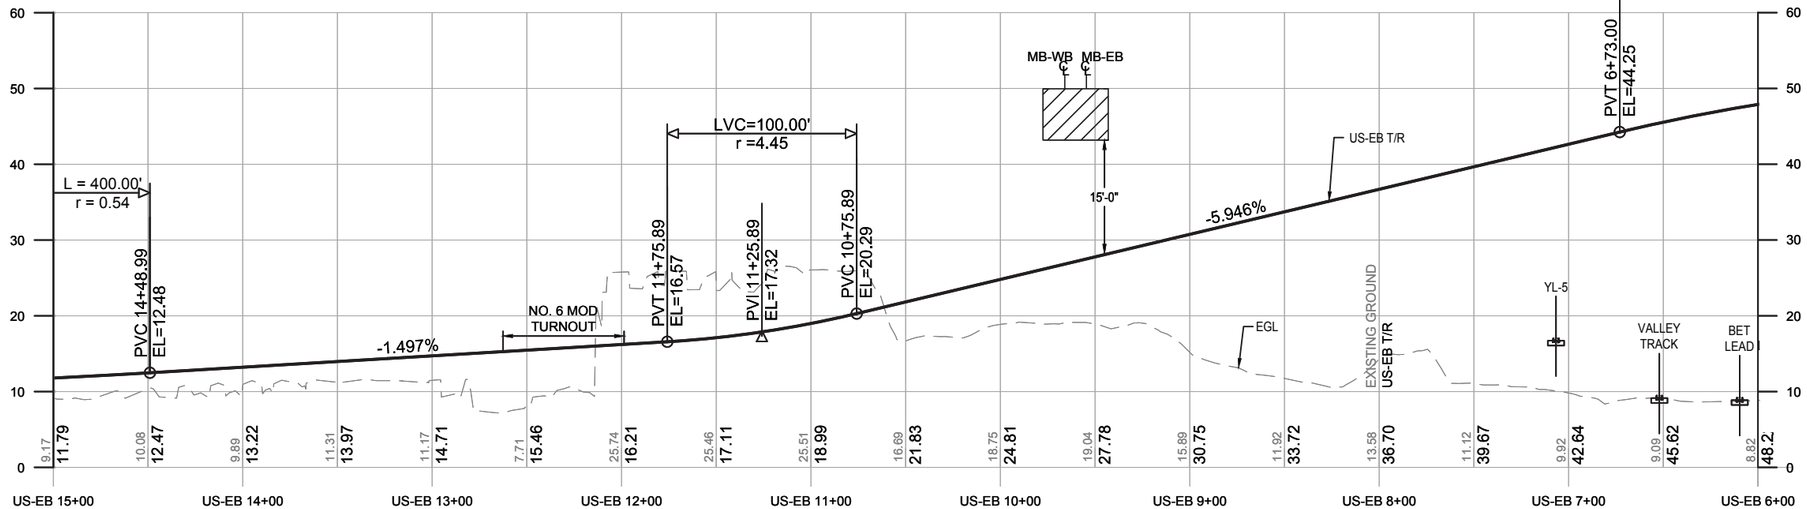

PROFILE

CURVE NO.	US-EB 2	US-EB 3	US-WB 1	US-WB 2
R	275.00 FT	787.59 FT	275.00 FT	1567.17 FT
Lc	380.64 FT	80.00 FT	127.00 FT	46.21 FT
Ls1	40.00 FT	40.00 FT	60.00 FT	40.00 FT
Ls2	40.00 FT	40.00 FT	60.00 FT	40.00 FT
Ea	1.00 IN	0.50 IN	1.75 IN	1.25 IN
Eu	0.46 IN	0.01 IN	1.53 IN	0.35 IN
V	10 MPH	10 MPH	15 MPH	25 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. REFER TO SHEETS C-050 TO C-055 FOR YARD LEAD ALIGNMENT AND PROFILE.
3. REFER TO SHEET C-056 FOR DRAINAGE FROM STA 6+00 TO STA 15+00.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

UNION SQUARE BRANCH
CORRIDOR PLAN AND PROFILE
STA US-EB 6+00 TO STA US-EB 15+00


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-027	

PLOTTED: 09/21/17 1:28AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\Q062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2051-2066.DWG [C-027] 09/20/17 10:23PM

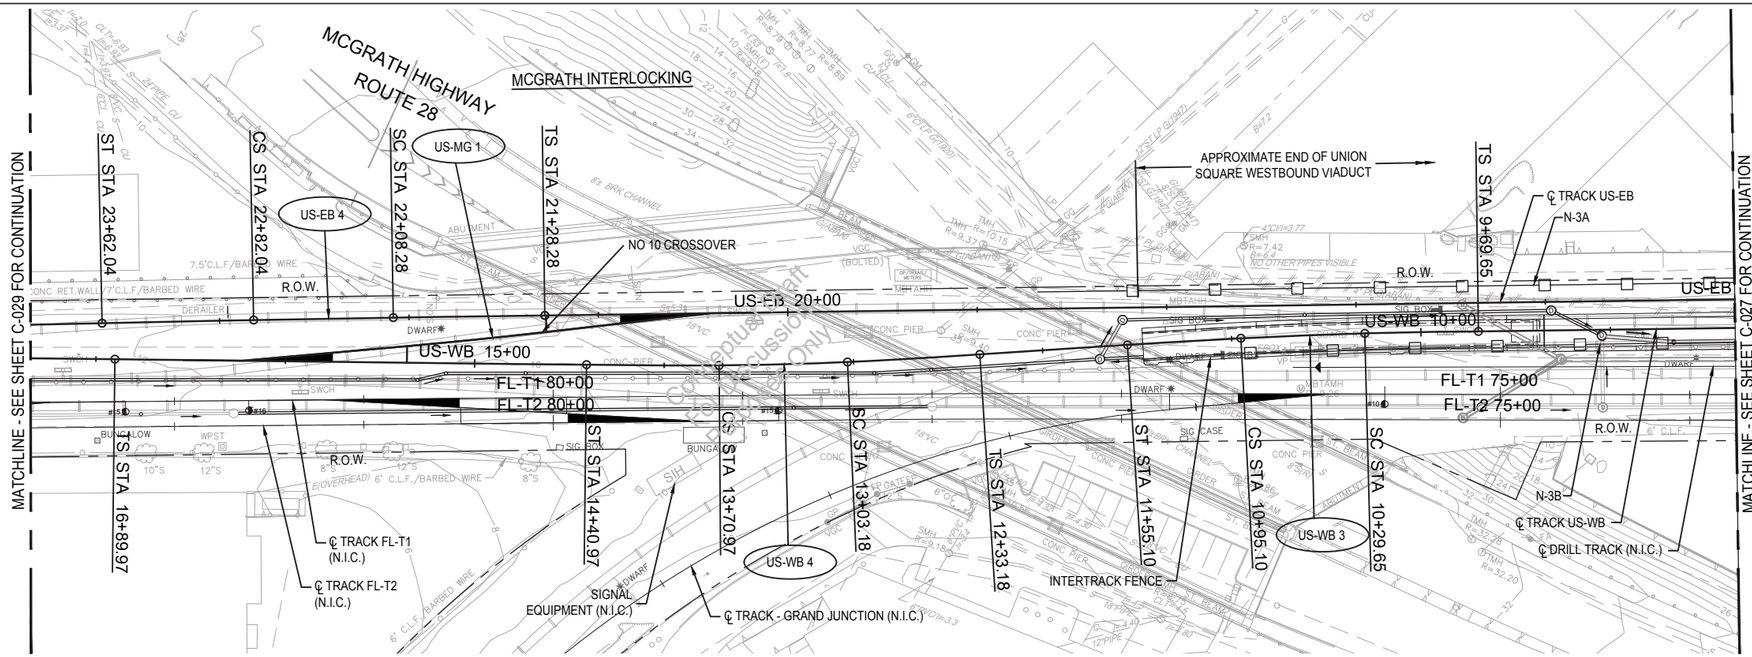

PLAN

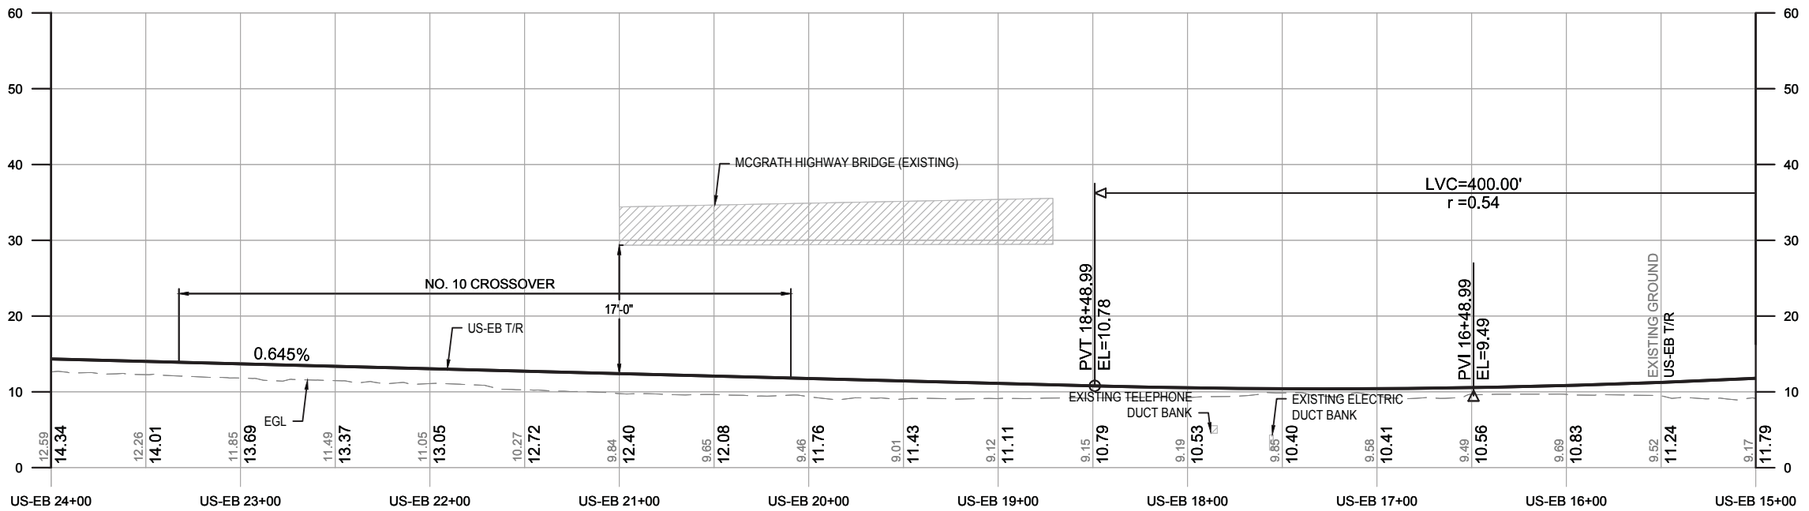

PROFILE

CURVE NO.	US-EB 4	US-WB 3	US-WB 4	US-MG 1
R	20000.00 FT	2500.00 FT	1829.82 FT	3800.00 FT
Lc	73.76 FT	65.46 FT	67.78 FT	70.00 FT
Ls1	80.00 FT	60.00 FT	70.00 FT	-
Ls2	80.00 FT	60.00 FT	70.00 FT	-
Ea	0.00 IN	1.50 IN	1.75 IN	0.00 IN
Eu	0.18 IN	0.47 IN	0.94 IN	0.24 IN
V	30 MPH	35 MPH	35 MPH	15 MPH

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


UNION SQUARE BRANCH
CORRIDOR PLAN AND PROFILE
STA US-EB 15+00 TO STA US-EB 24+00

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-028	

PLOTTED: 09/21/17 1:36AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\Q062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2061-2066.DWG [C-028] 09/20/17 10:23PM

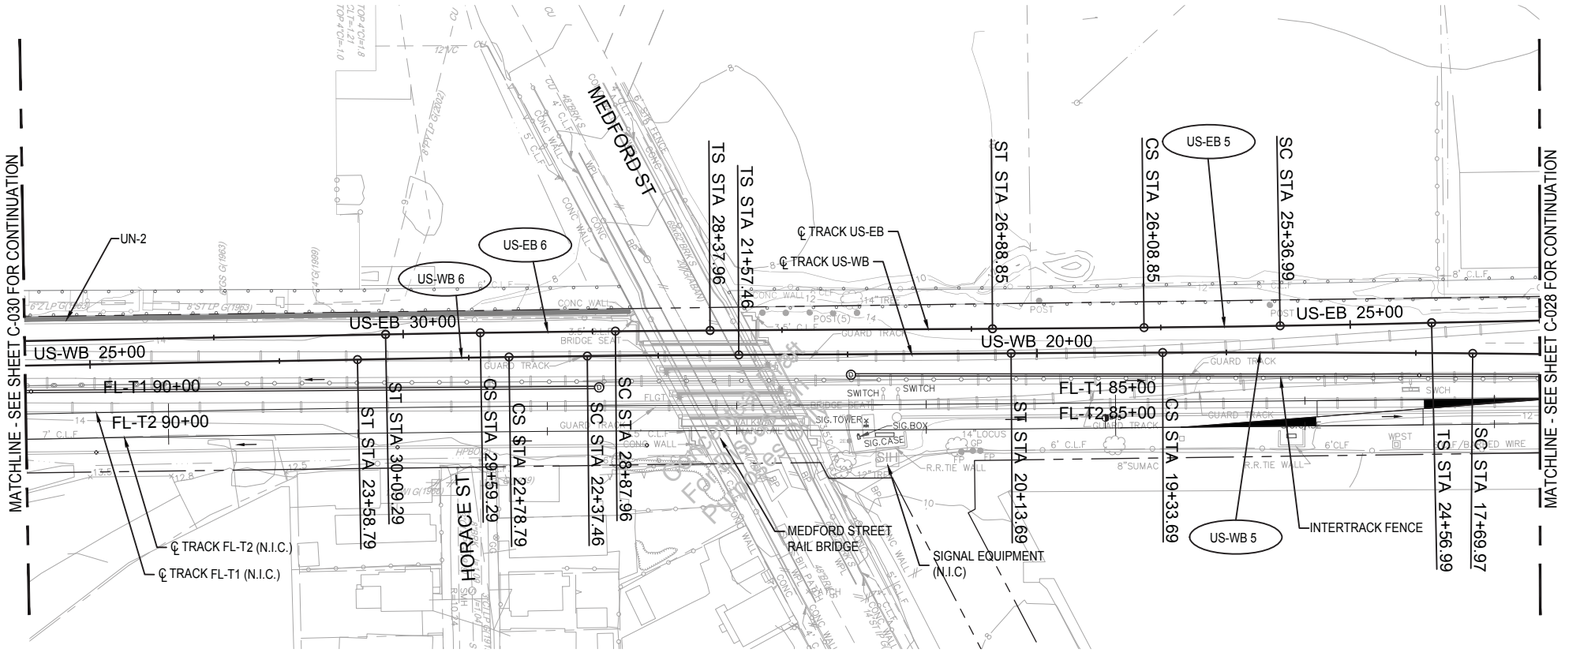

PLAN

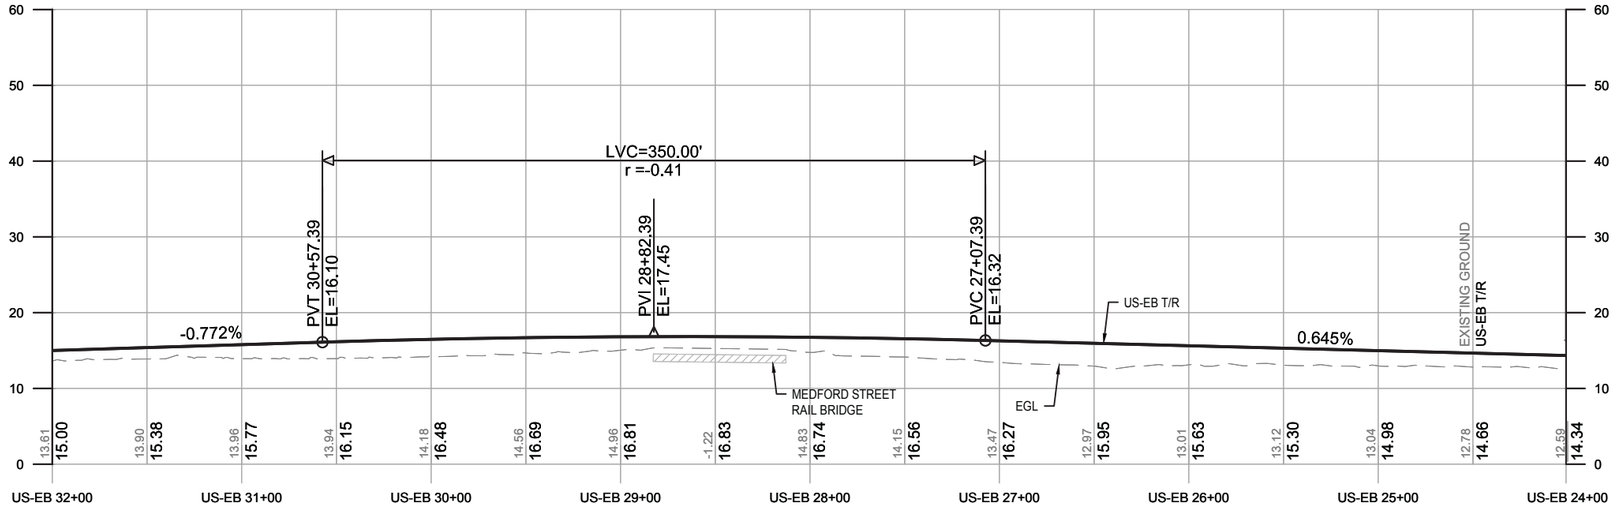

PROFILE

CURVE NO.	US-EB 5	US-EB 6	US-WB 5	US-WB 6
R	10000.00 FT	10000.00 FT	13833.65 FT	10000.00 FT
Lc	71.86 FT	71.33 FT	163.72 FT	41.33 FT
Ls1	80.00 FT	50.00 FT	80.00 FT	80.00 FT
Ls2	80.00 FT	50.00 FT	80.00 FT	80.00 FT
Ea	0.75 IN	0.75 IN	0.50 IN	0.75 IN
Eu	0.25 IN	0.25 IN	0.22 IN	0.25 IN
V	50 MPH	50 MPH	50 MPH	50 MPH

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

UNION SQUARE BRANCH
CORRIDOR PLAN AND PROFILE
STA US-EB 24+00 TO STA US-EB 32+00


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-029	

PLOTTED: 09/21/17 1:43AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\Q062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2061-2066.DWG [C-029] 09/20/17 10:23PM

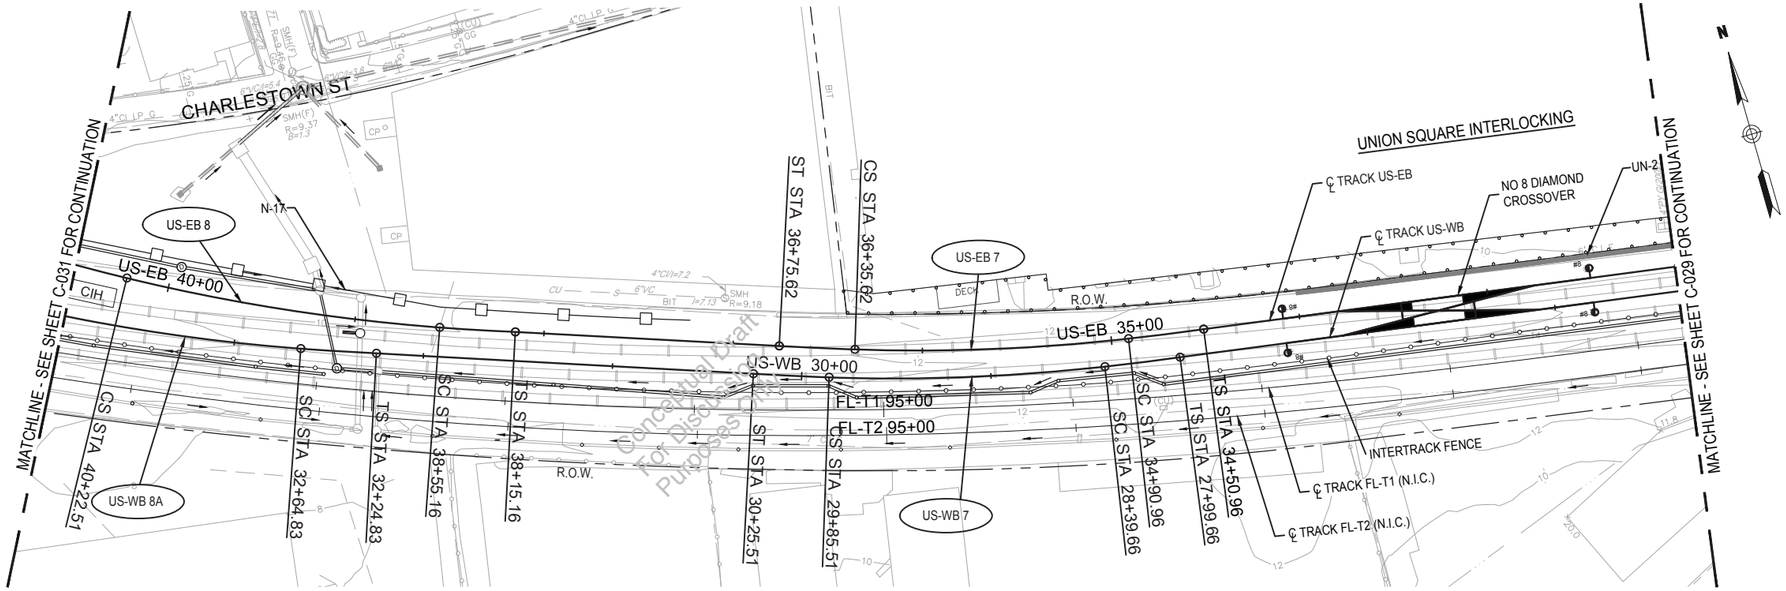

PLAN

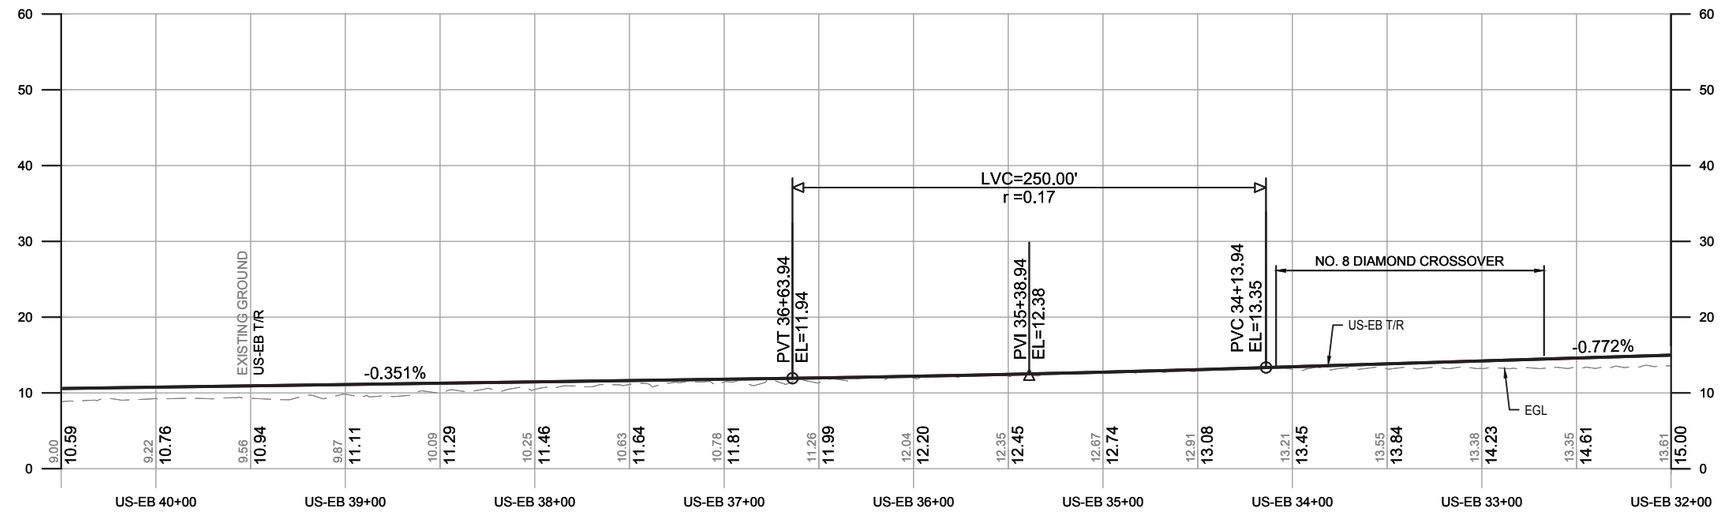

PROFILE

CURVE NO.	US-EB 7	US-EB 8	US-WB 7	US-WB 8A
R	1000.00 FT	1000.00 FT	1000.00 FT	1000.00 FT
Lc	144.67 FT	167.35 FT	145.85 FT	166.16 FT
Ls1	40.00 FT	40.00 FT	40.00 FT	40.00 FT
Ls2	40.00 FT	40.00 FT	40.00 FT	40.00 FT
Ea	1.25 IN	1.25 IN	1.25 IN	1.25 IN
Eu	0.35 IN	0.35 IN	0.35 IN	0.35 IN
V	20 MPH	20 MPH	20 MPH	20 MPH

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

UNION SQUARE BRANCH
CORRIDOR PLAN AND PROFILE
STA US-EB 32+00 TO STA US-EB 40+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-030	

PLOTTED: 09/21/17 2:39PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2061-2066.DWG [C-030] 09/21/17 12:22PM

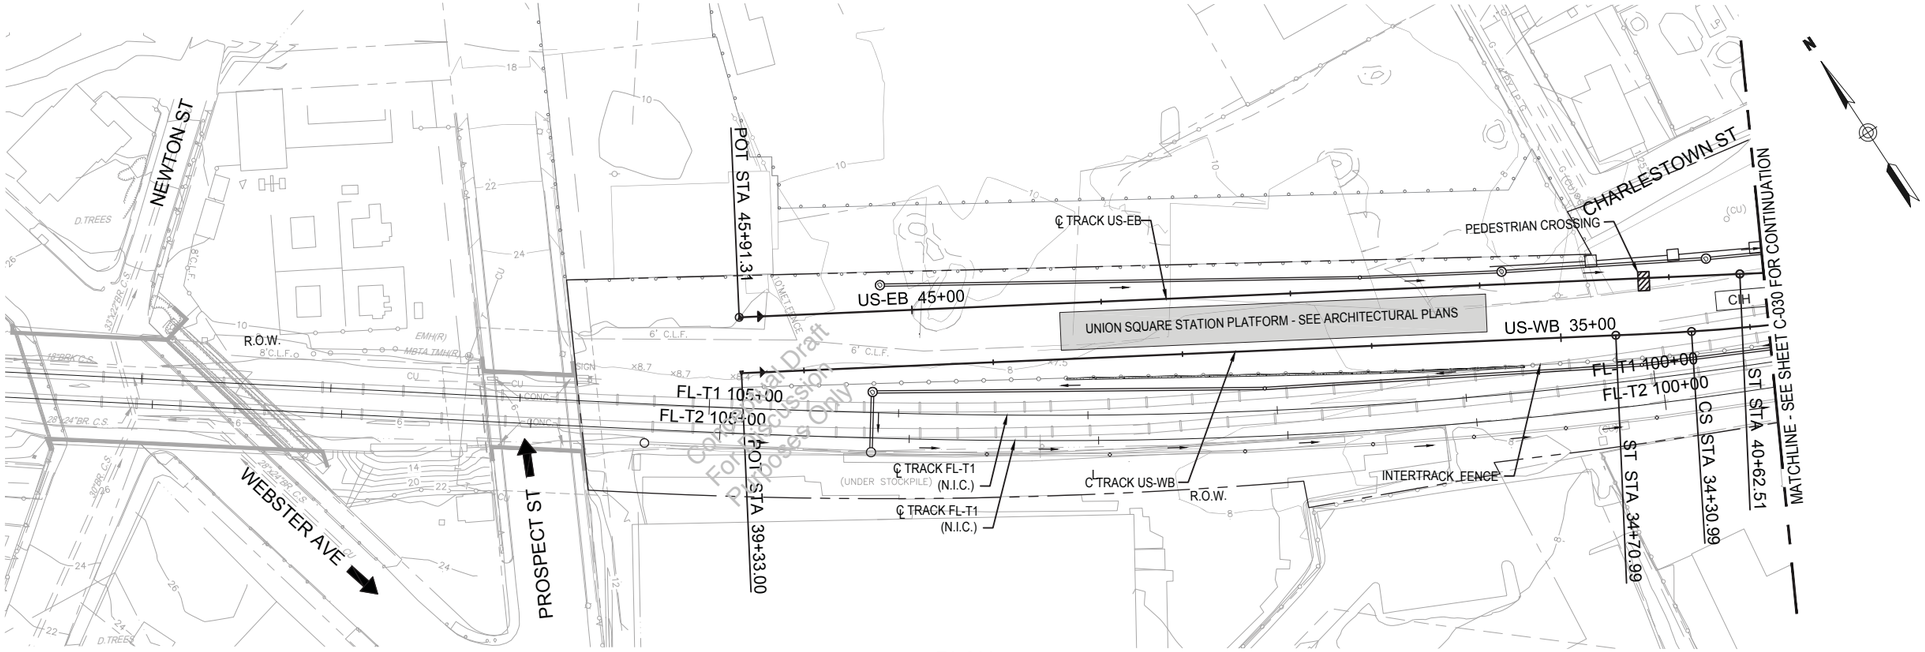

PLAN

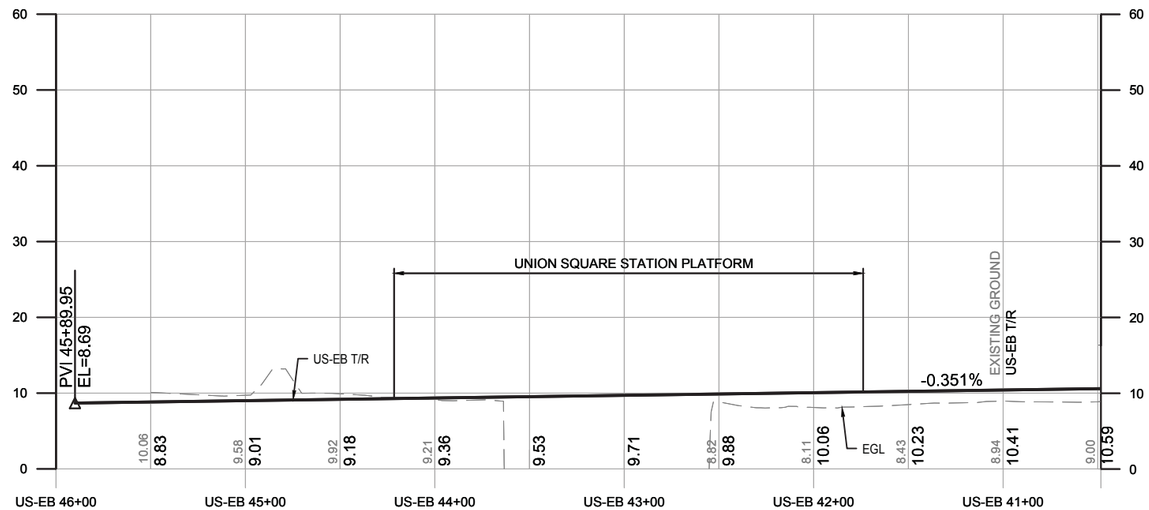

PROFILE

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


UNION SQUARE BRANCH CORRIDOR PLAN AND PROFILE STA US-EB 40+50 TO STA US-EB 46+00

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-031	

PLOTTED: 09/21/17 1:58AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0082820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2061-2066.DWG [C-031] 09/20/17 10:23PM

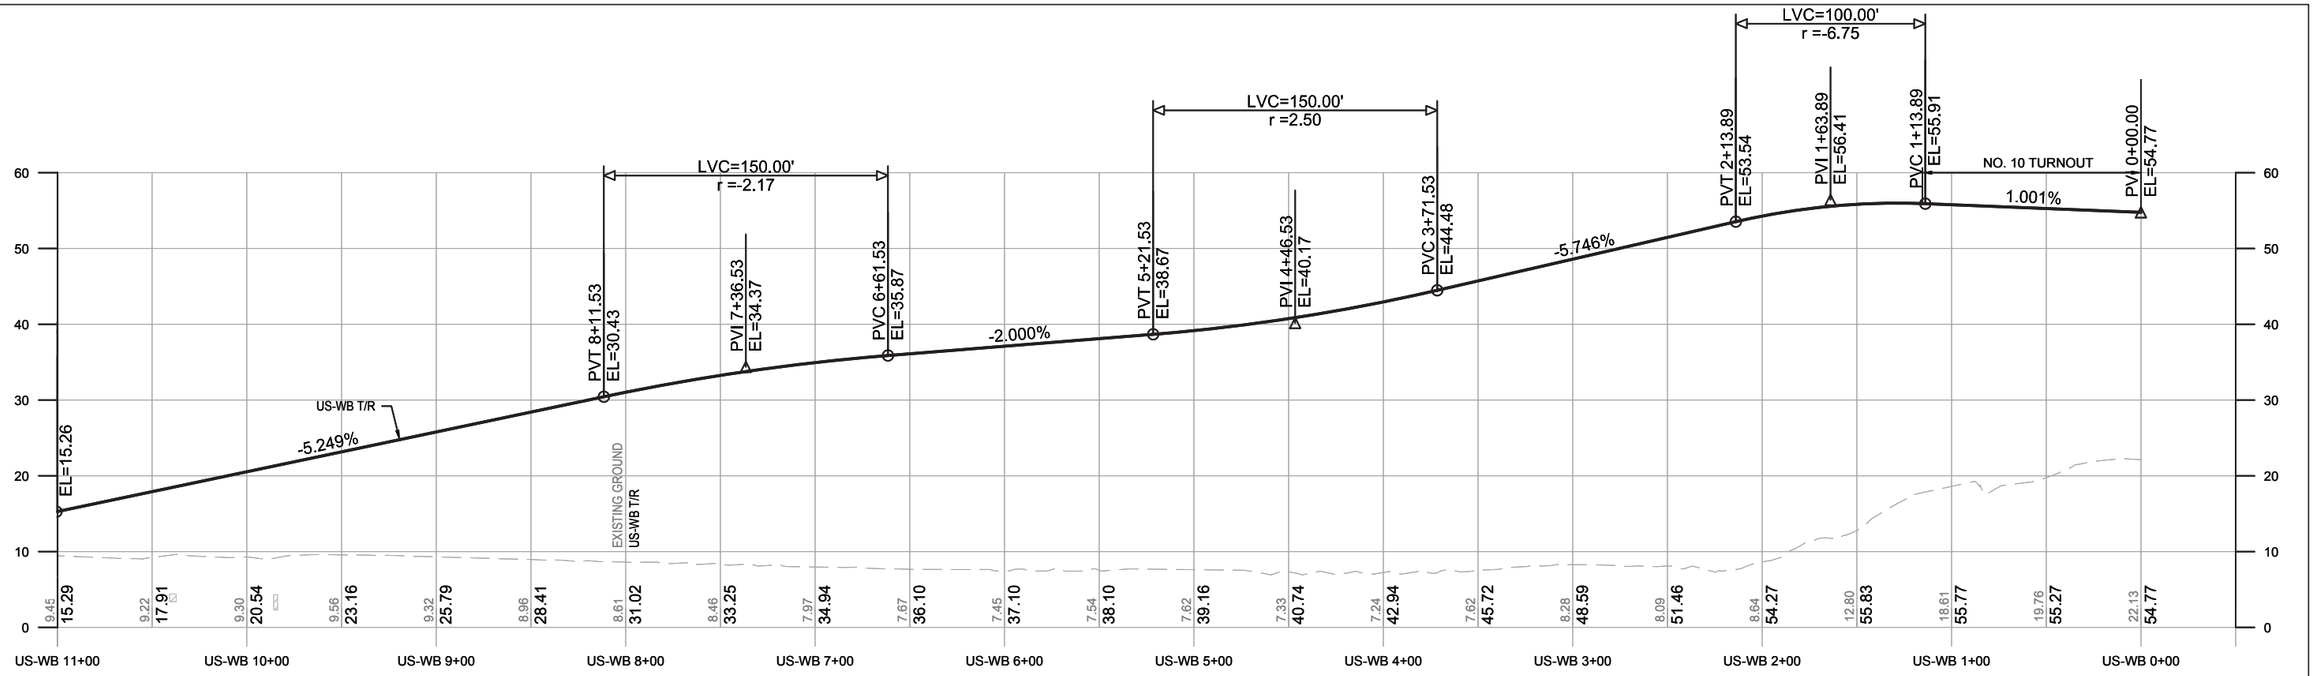

PROFILE

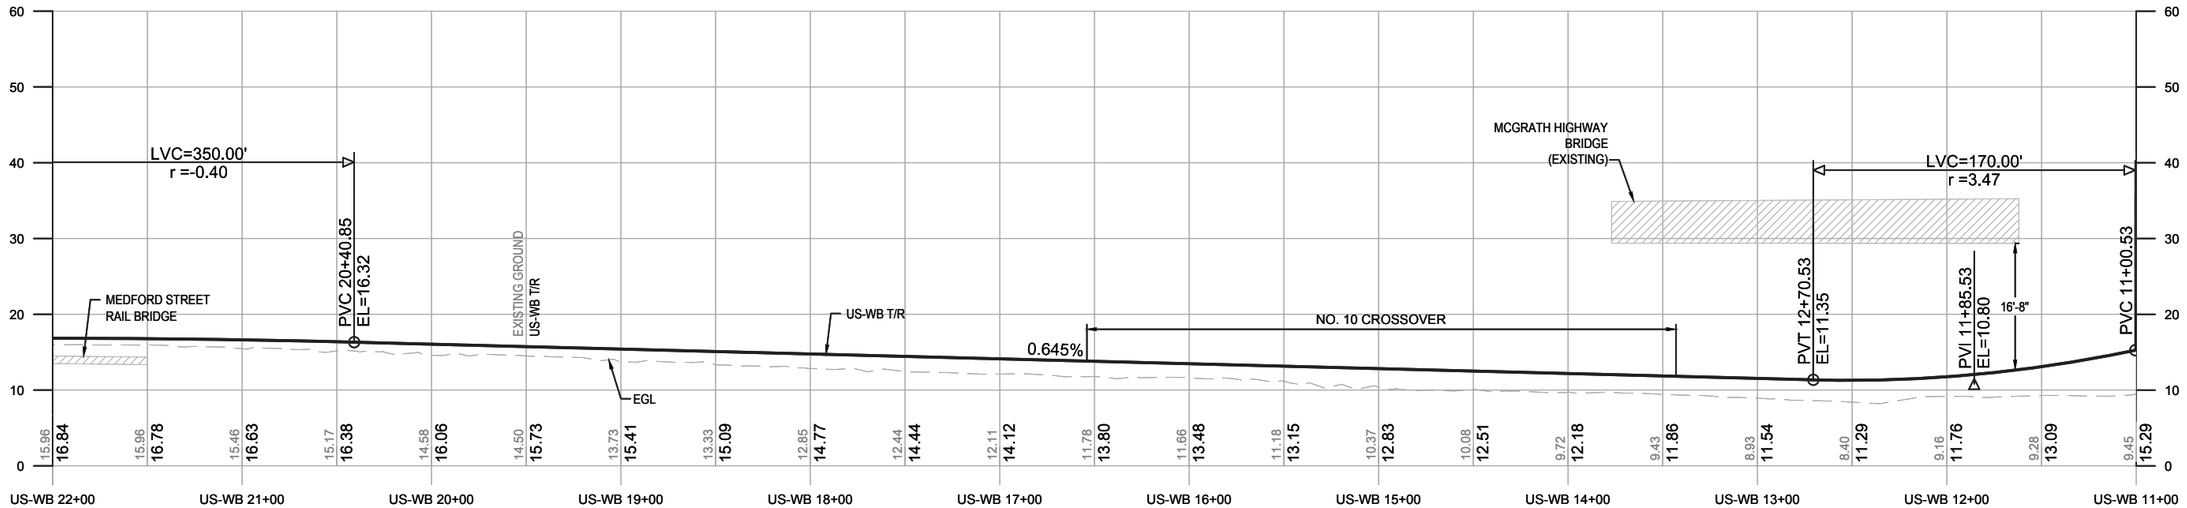

PROFILE

NOTE:
1. THE US-WB T/R TRACK PROFILE TO BE THE SAME AS US-EB T/R TRACK PROFILE FROM US-WB 22+00.00 TO US-WB 39+33.00

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

UNION SQUARE BRANCH TRACK PROFILE STA US-WB 0+00 TO STA US-WB 22+00


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-032	

PLOTTED: 09/21/17 1:58AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\GV62820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2067.DWG [C-032] 09/20/17 10:09PM

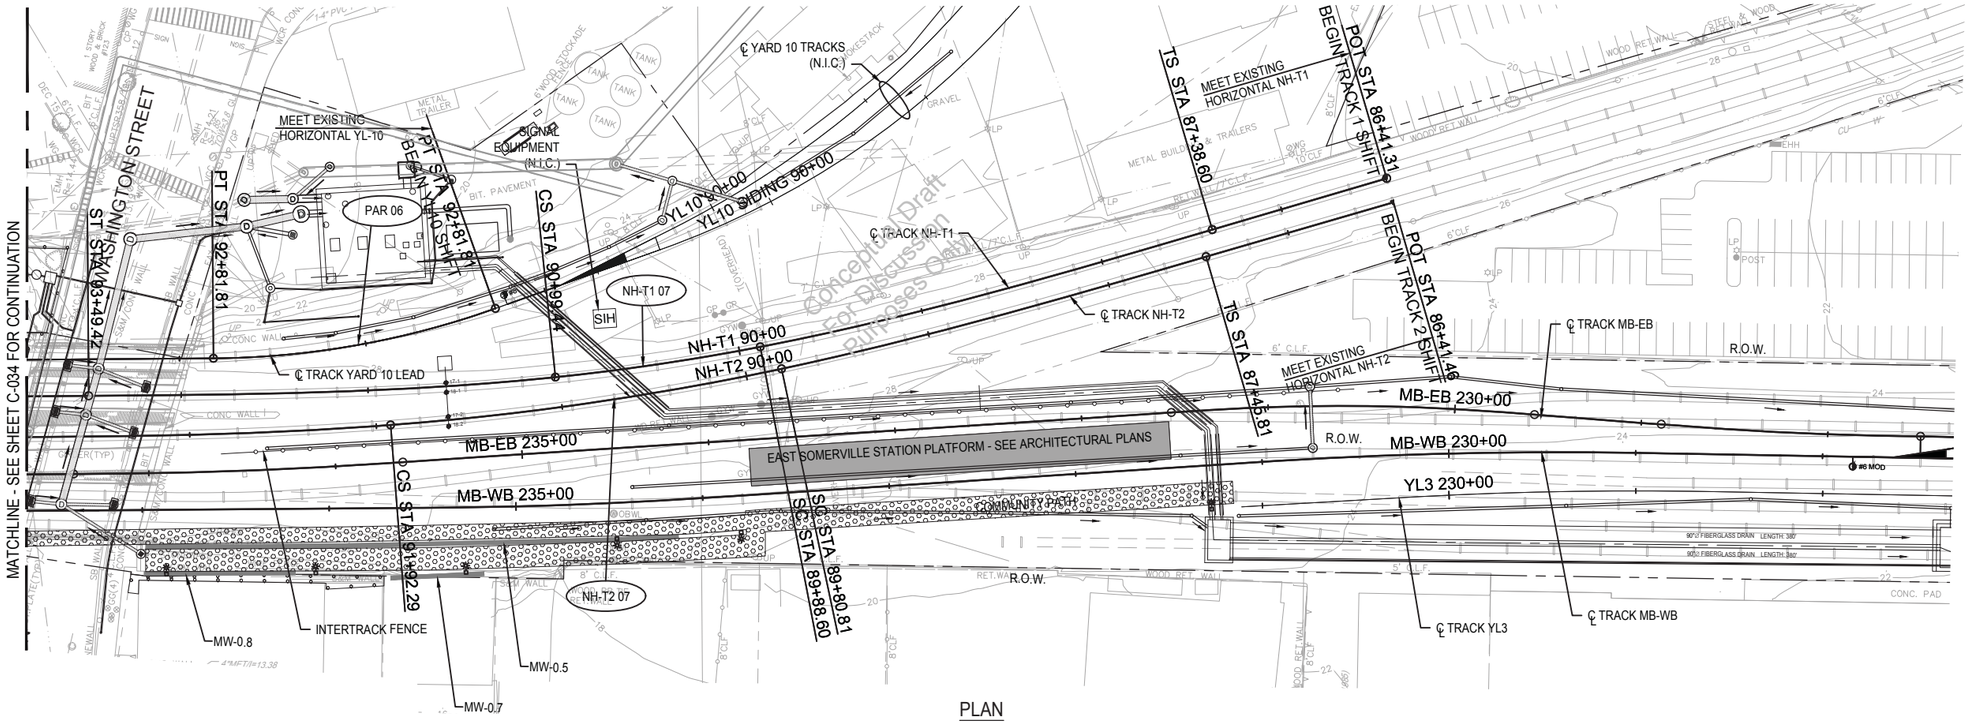

PLAN

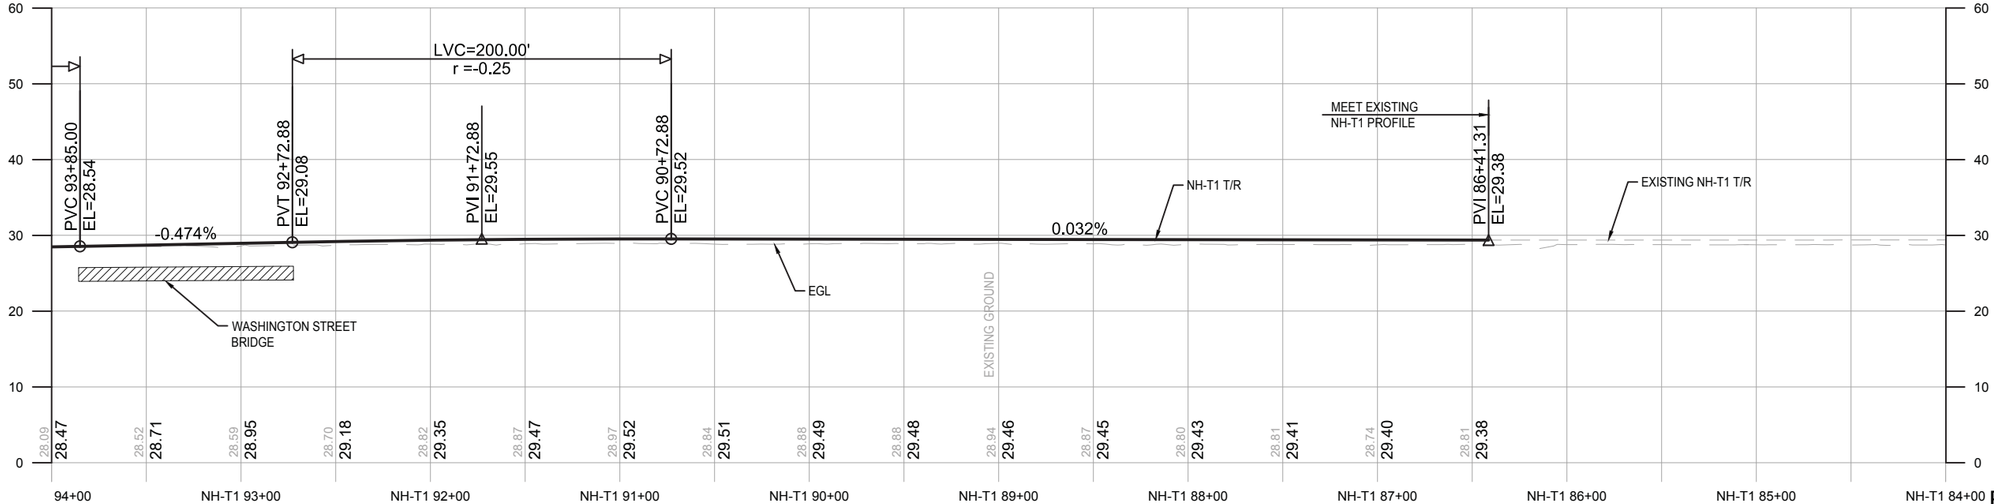

PROFILE

PROPOSAL

CURVE NO.	NH-T1 07	NH-T2 07	PAR 06
Dc	4°25'0.00"	3°35'0.00"	12°30'0.00"
Lc (CHORDED)	110.81 FT	211.44 FT	153.54 FT
Ls1	250.00 FT	235.00 FT	0.00 FT
Ls2	250.00 FT	235.00 FT	0.00 FT
Ea	2.00 IN	2.00 IN	0.00 IN
Eu	1.79 IN	1.07 IN	1.97 IN
V	35 MPH	35 MPH	15 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. YARD 10 LEAD PROFILE SHALL BE COORDINATED WITH KEOLIS.
3. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 84+00 TO STA NH-T1 94+00


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-033	

PLOTTED: 09/22/17 8:52AM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2107-2114.DWG [C-033] 09/21/17 4:46PM

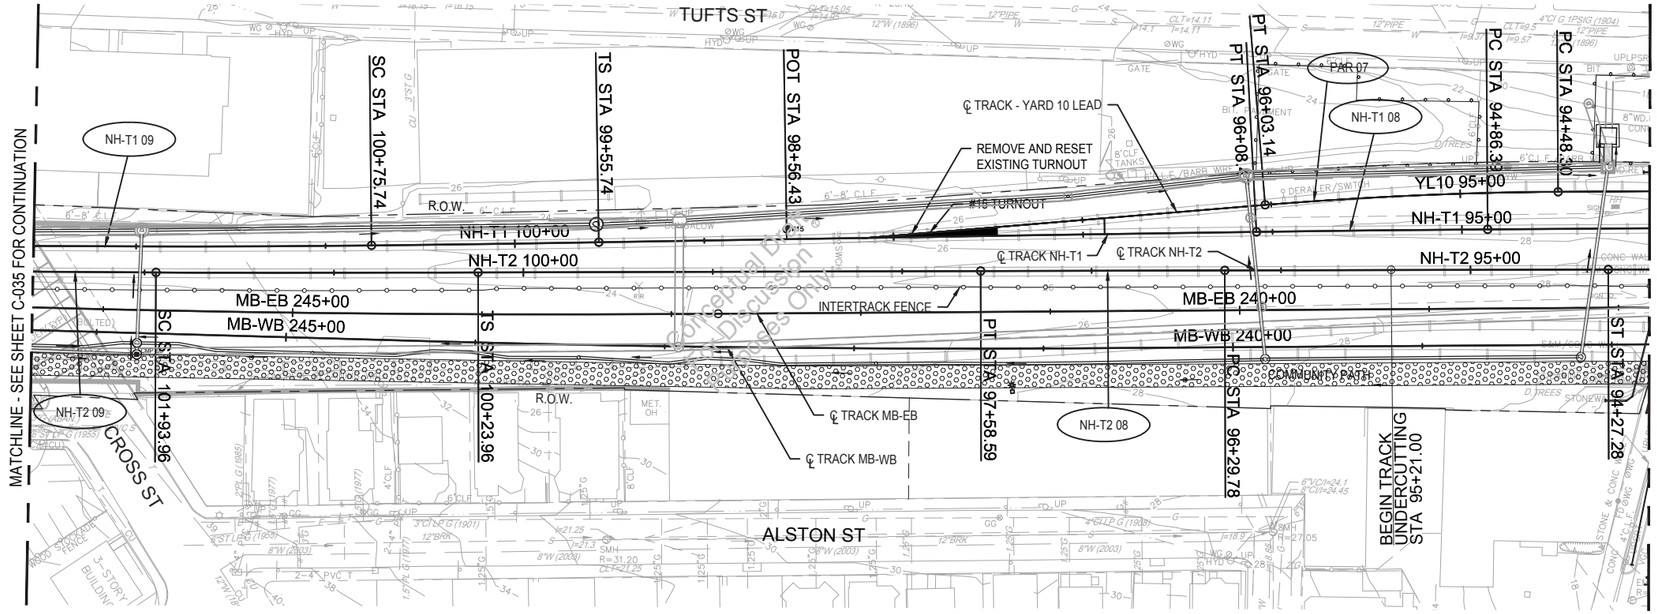

PLAN

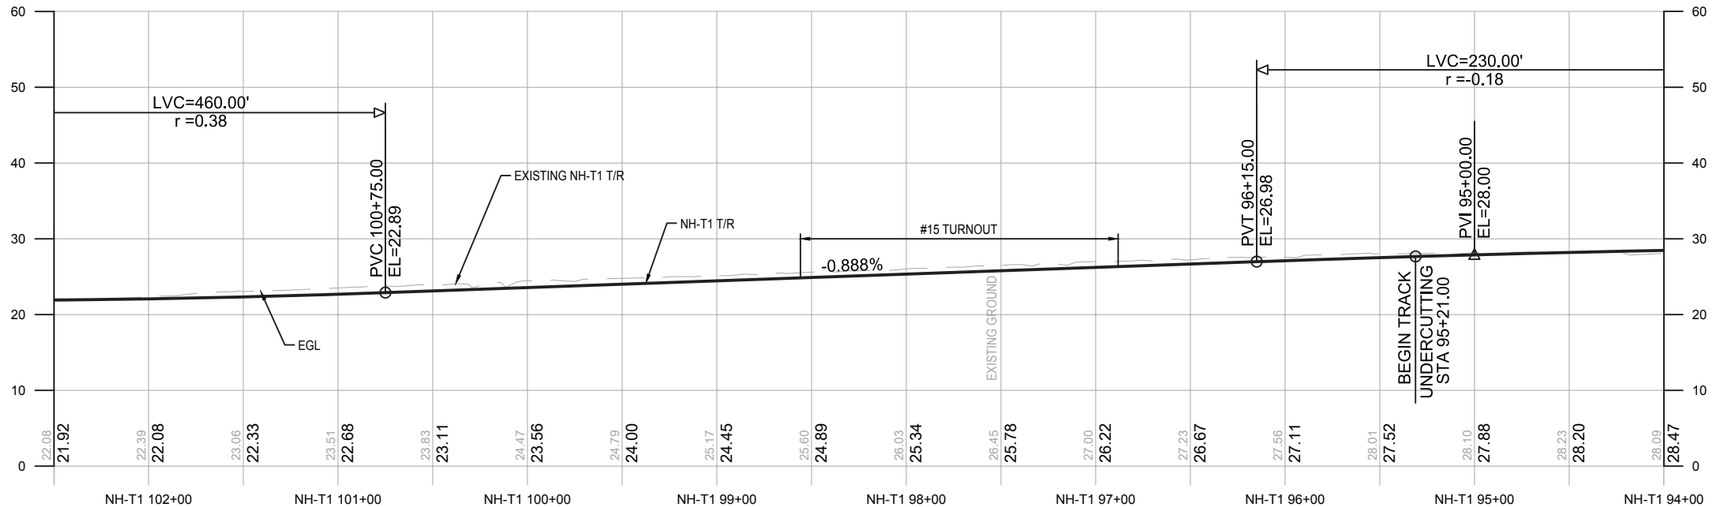

PROFILE

CURVE NO.	NH-T1 08	NH-T2 08	NH-T1 09	NH-T2 09	PAR 07
Dc	0°25'0.00"	0°0'30.00"	0°32'45.00"	0°29'57.91"	2°47'48.44"
Lc (CHORDED)	122.08 FT	128.81 FT	339.14 FT	181.78 FT	154.84 FT
Ls1	0.00 FT	0.00 FT	120.00 FT	170.00 FT	0.00 FT
Ls2	0.00 FT	0.00 FT	120.00 FT	170.00 FT	0.00 FT
Ea	0.00 IN	0.00 IN	1.25 IN	1.00 IN	0.00 IN
Eu	0.36 IN	0.01 IN	0.62 IN	0.71 IN	0.44 IN
V	35 MPH	35 MPH	70 MPH	70 MPH	15 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. YARD 10 LEAD PROFILE SHALL BE COORDINATED WITH KEOLIS.
3. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 94+00 TO STA NH-T1 102+50

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-034	

PLOTTED: 09/22/17 9:14AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2107-2114.DWG [C-034] 09/21/17 4:48PM

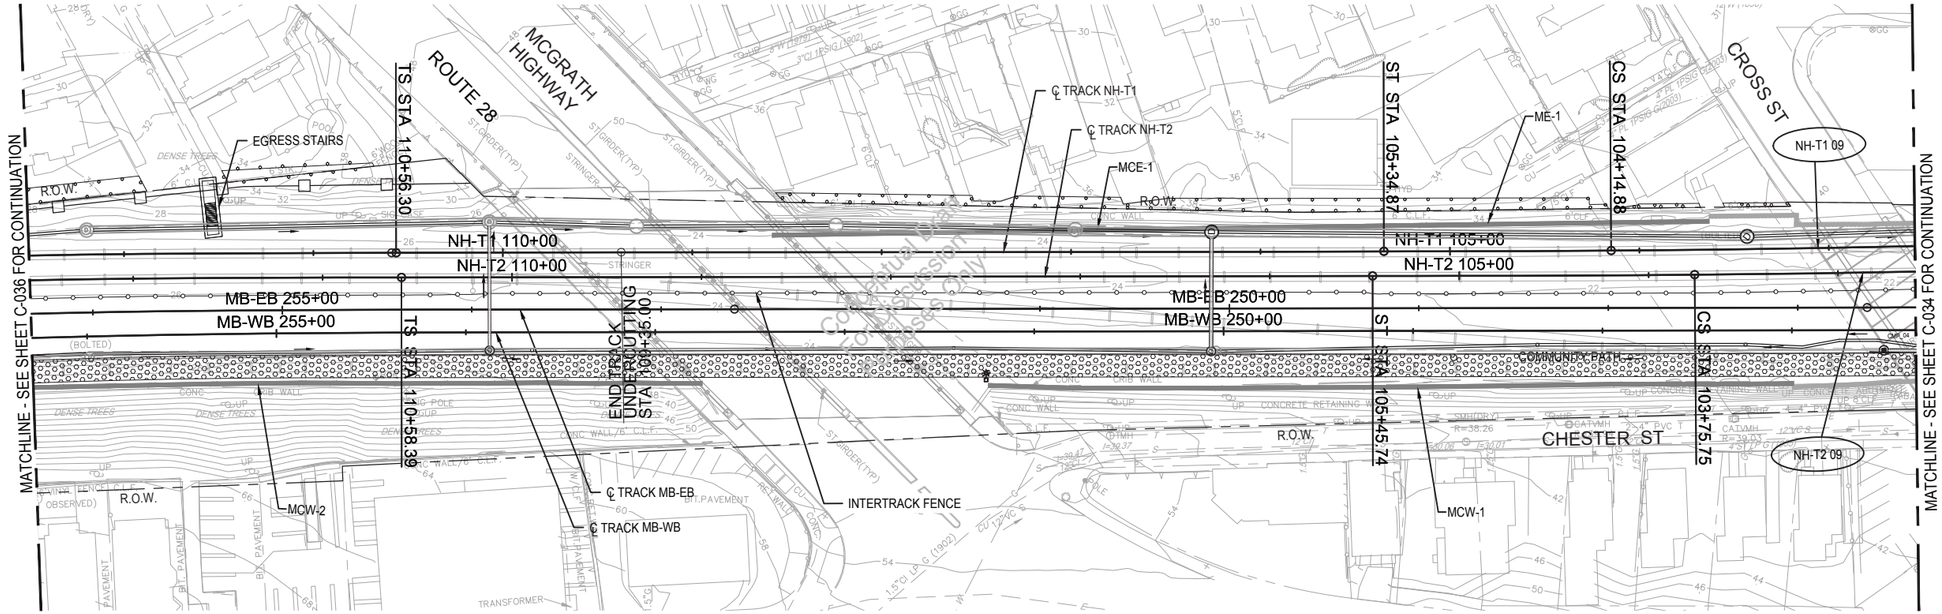

PLAN

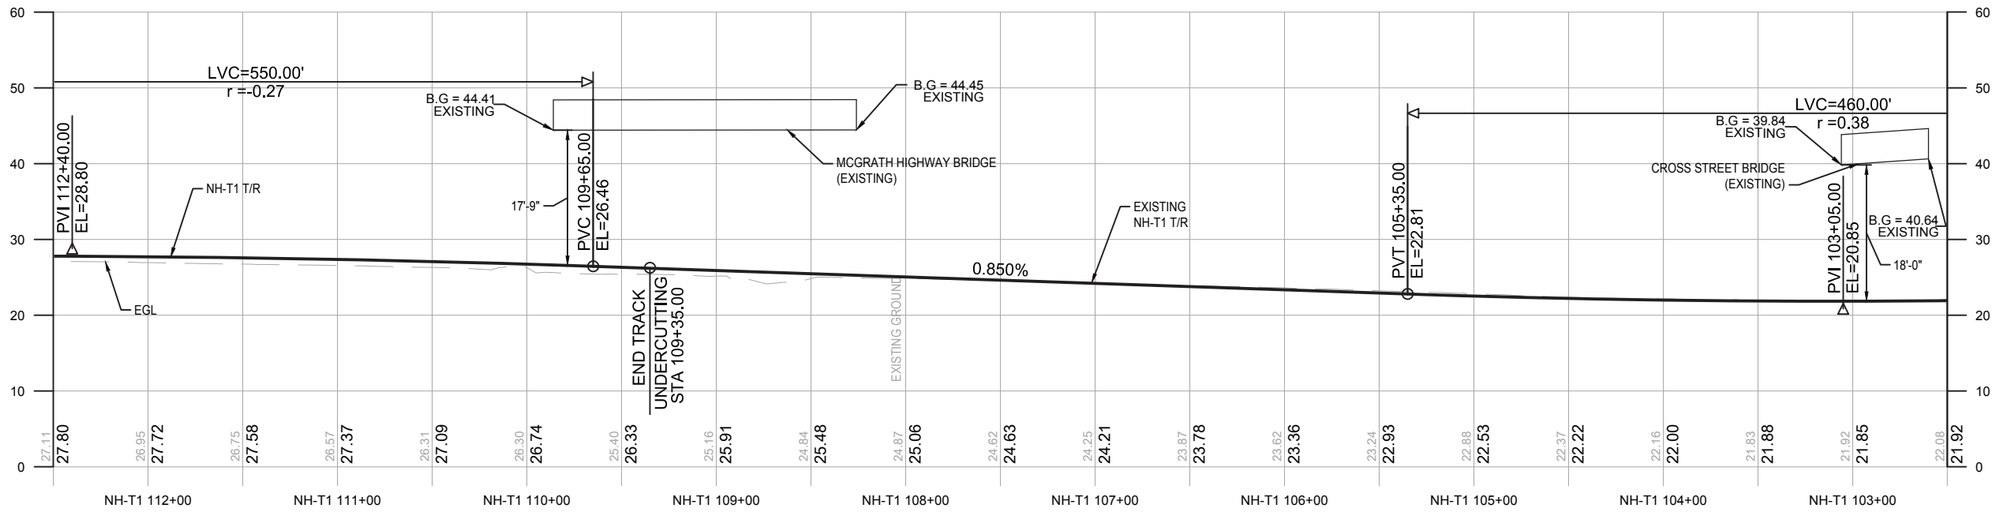

PROFILE

CURVE NO.	NH-T1 09	NH-T2 09
Dc	0°32'45.00"	0°29'57.91"
Lc (CHORDED)	339.14 FT	181.78 FT
Ls1	120.00 FT	170.00 FT
Ls2	120.00 FT	170.00 FT
Ea	1.25 IN	1.00 IN
Eu	0.62 IN	0.71 IN
V	70 MPH	70 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE
CORRIDOR PLAN AND PROFILE
STA NH-T1 102+50 TO STA NH-T1 112+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-035	

PLOTTED: 09/22/17 9:25AM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\0002820 GLX D-B\STV 2017 RFP DESIGN\00_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2107-2114.DWG [C-035] 09/21/17 4:46PM

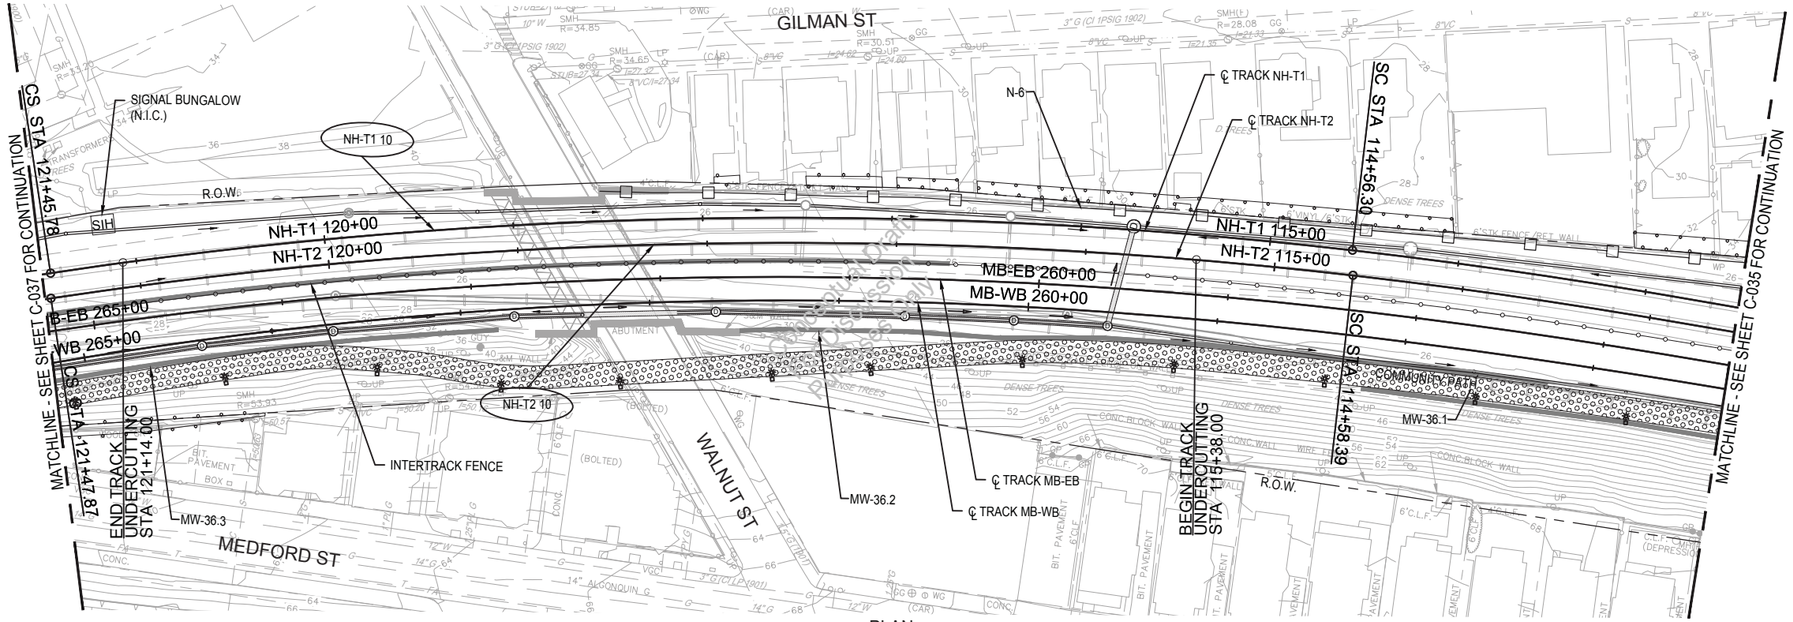

PLAN

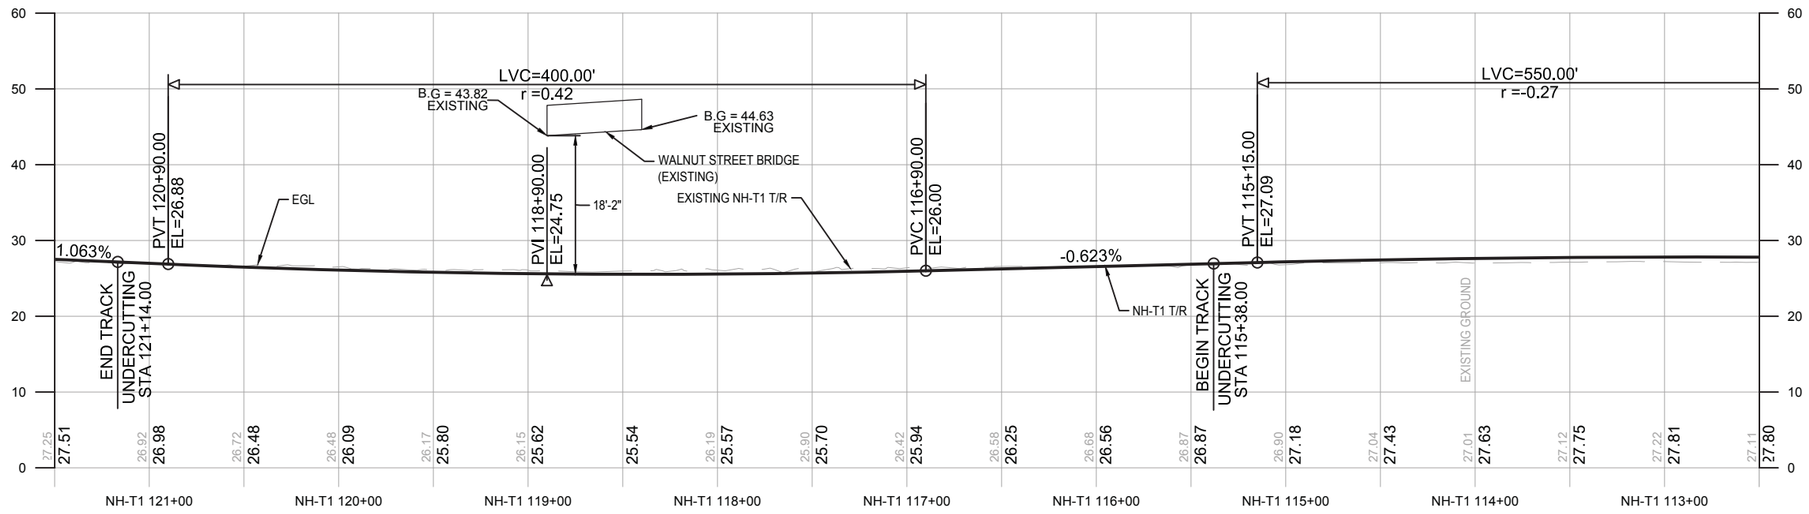

PROFILE

CURVE NO.	NH-T1 10	NH-T2 10
Dc	2°12'13.80"	2°12'13.80"
Lc (CHORDED)	689.49 FT	689.49 FT
Ls1	400.00 FT	400.00 FT
Ls2	400.00 FT	400.00 FT
Ea	3.75 IN	3.75 IN
Eu	2.35 IN	2.38 IN
V	65 MPH	65 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 112+50 TO STA NH-T1 121+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-036	

PLOTTED: 09/22/17 3:04PM BY:RENEKC
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_GC_TRACK_RAIL\000-K-2107-2114.DWG [C-036] 09/22/17 1:34PM

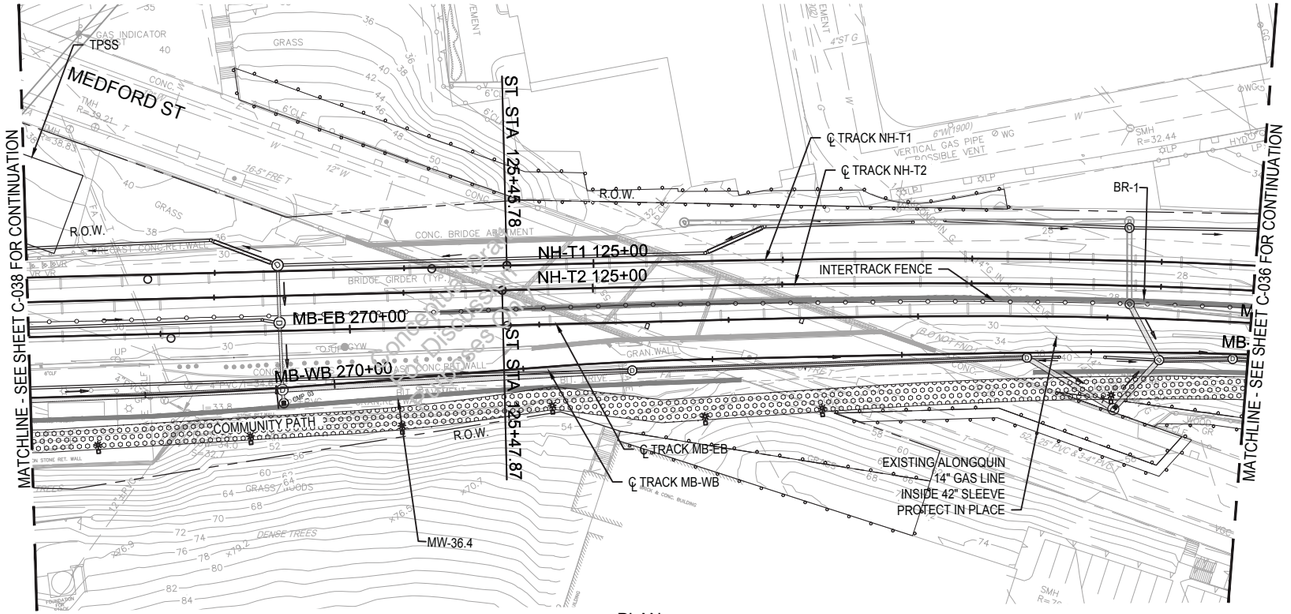

PLAN

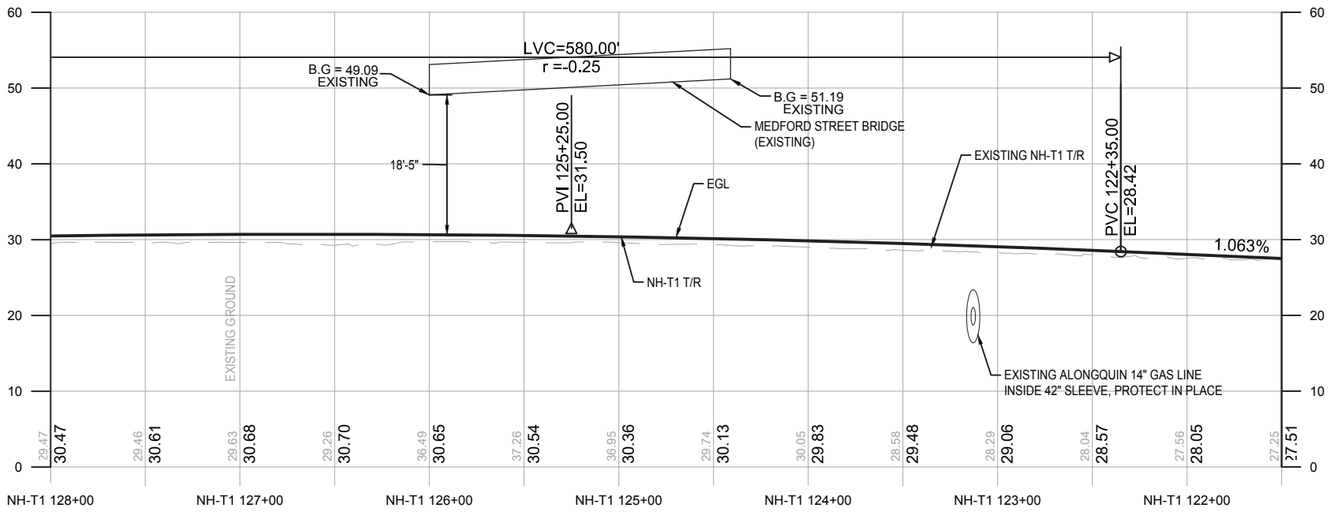

PROFILE

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 121+50 TO STA NH-T1 128+00


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-037	

PLOTTED: 09/22/17 2:45PM BY:RENNEKC
DRAWING: L:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_GX_TRACK_RAIL\000-HC-2107-2114.DWG [C-037] 09/22/17 1:34PM

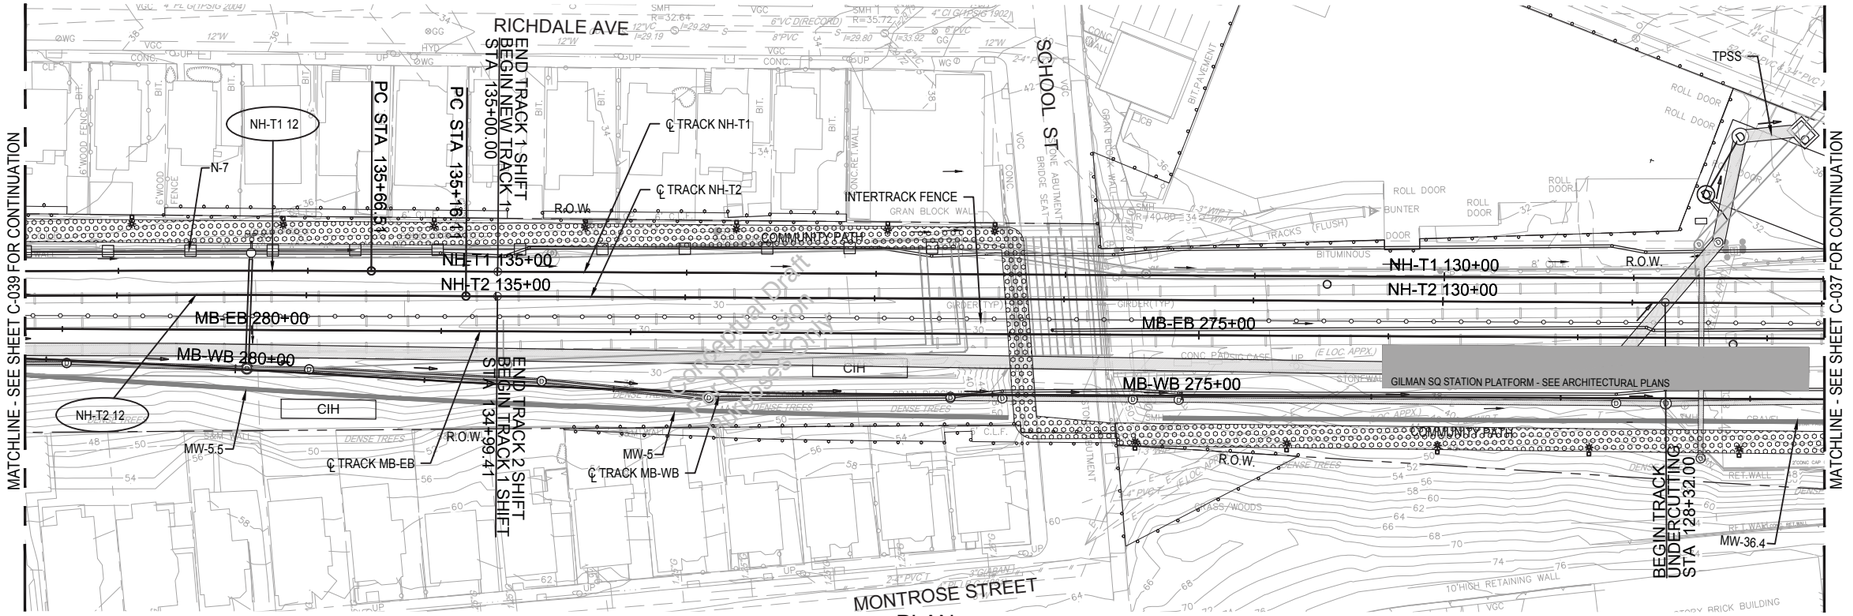

PLAN

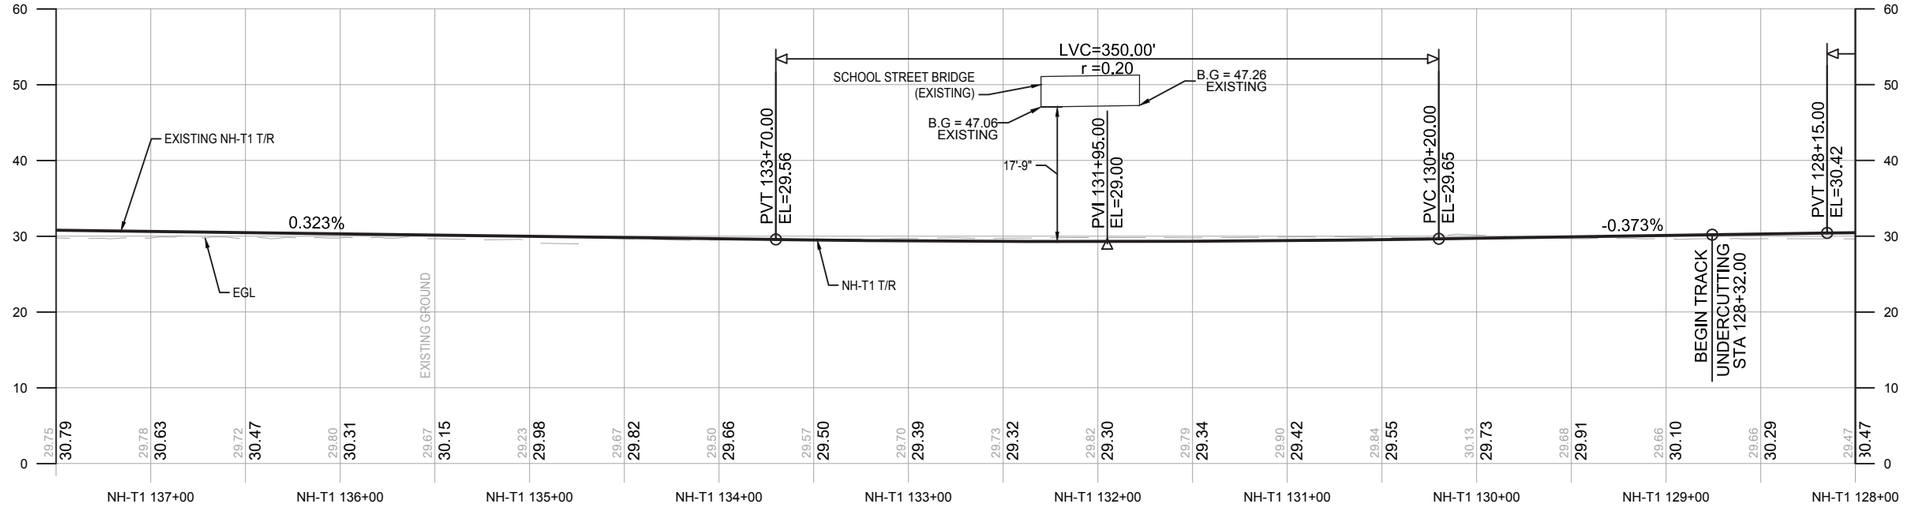

PROFILE

CURVE NO.	NH-T1 12	NH-T2 12
Dc	0°18'00.00"	0°11'51.26"
Lc (CHORDED)	230.40 FT	349.85 FT
Ls1	0.00 FT	0.00 FT
Ls2	0.00 FT	0.00 FT
Ea	0.00 IN	0.00 IN
Eu	1.34 IN	0.89 IN
V	80 MPH	80 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE
CORRIDOR PLAN AND PROFILE
STA NH-T1 128+00 TO STA NH-T1 137+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-038	

PLOTTED: 09/22/17 2:52PM BY:RENNEKC
DRAWING: L:\PROPOSALS\2017\G062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2107-2114.DWG [C-038] 09/22/17 1:34PM

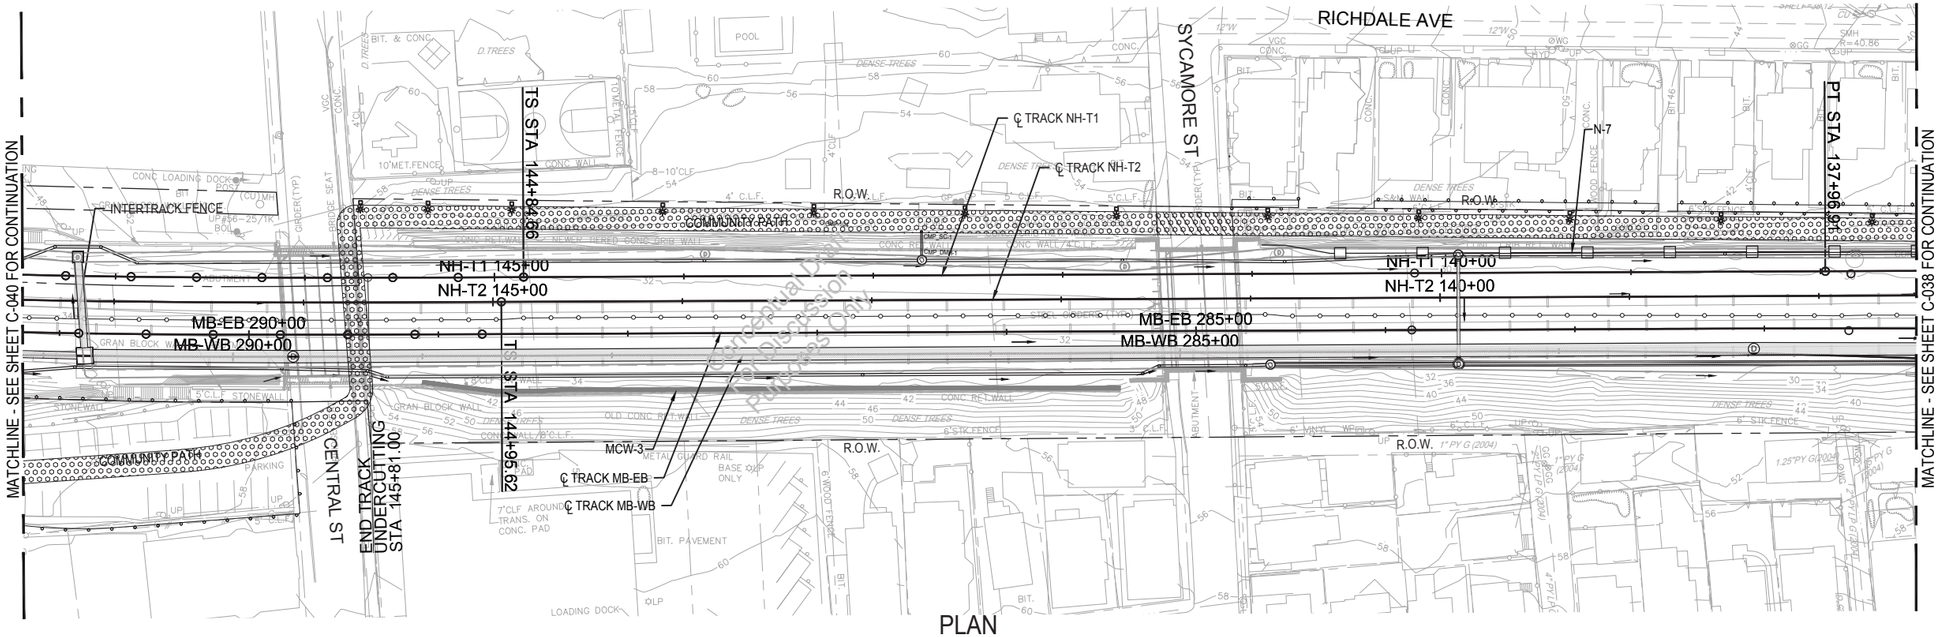

PLAN

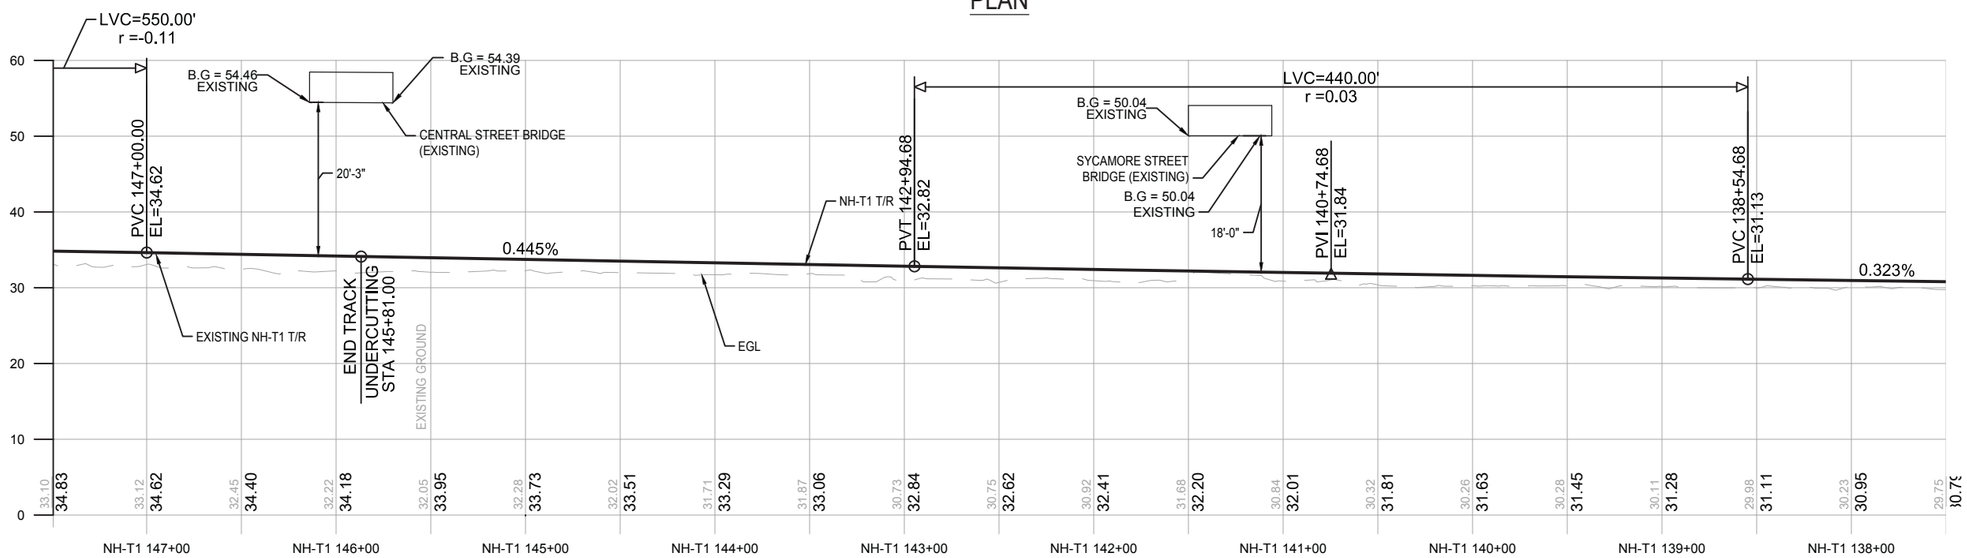

PROFILE

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 137+50 TO STA NH-T1 147+50

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-039	

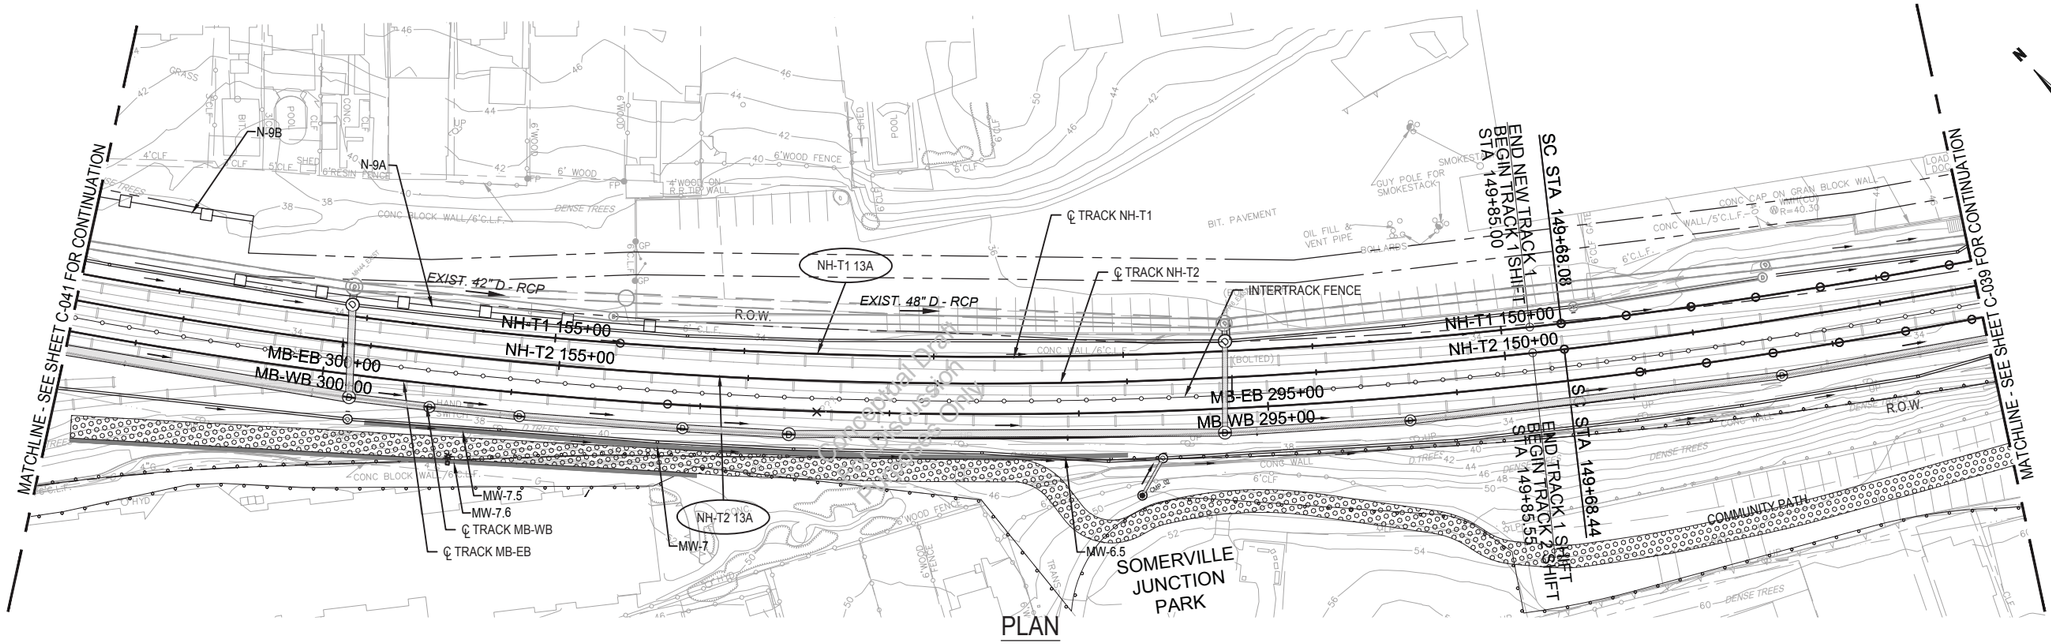

CURVE NO.	NH-T1 13A	NH-T1 13B	NH-T2 13A	NH-T2 13B
Dc	2°10'58.20"	1°01'23.30"	2°11'13.2"	1°01'10.2"
Lc (CHORDED)	997.21 FT	108.16 FT	1000.86 FT	83.19 FT
Ls1	483.42 FT	125.50 FT	472.82 FT	151.13 FT
Ls2	125.50 FT	278.07 FT	151.13 FT	245.97 FT
Ea	4.00 IN	2.75 IN	4.00 IN	2.75 IN
Eu	2.51 IN	2.23 IN	2.51 IN	2.23 IN
V	65 MPH	65 MPH	65 MPH	65 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE..
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 147+50 TO STA NH-T1 157+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-040	

PLOTTED: 09/22/17 2:33PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\G062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAL\000-K-2107-2114.DWG [C-040] 09/22/17 1:34PM

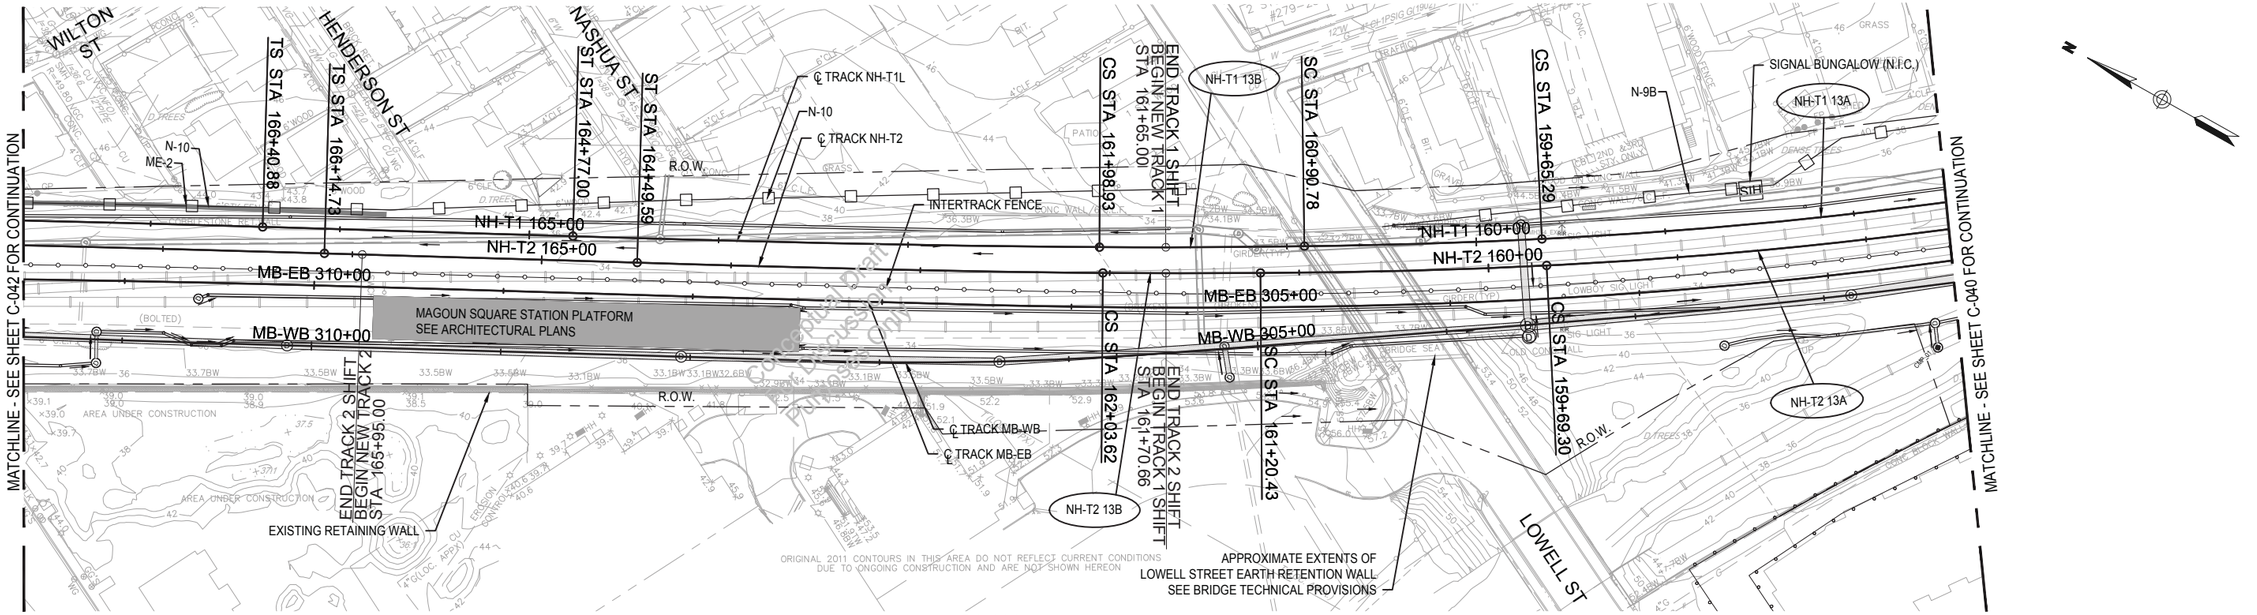

PLAN

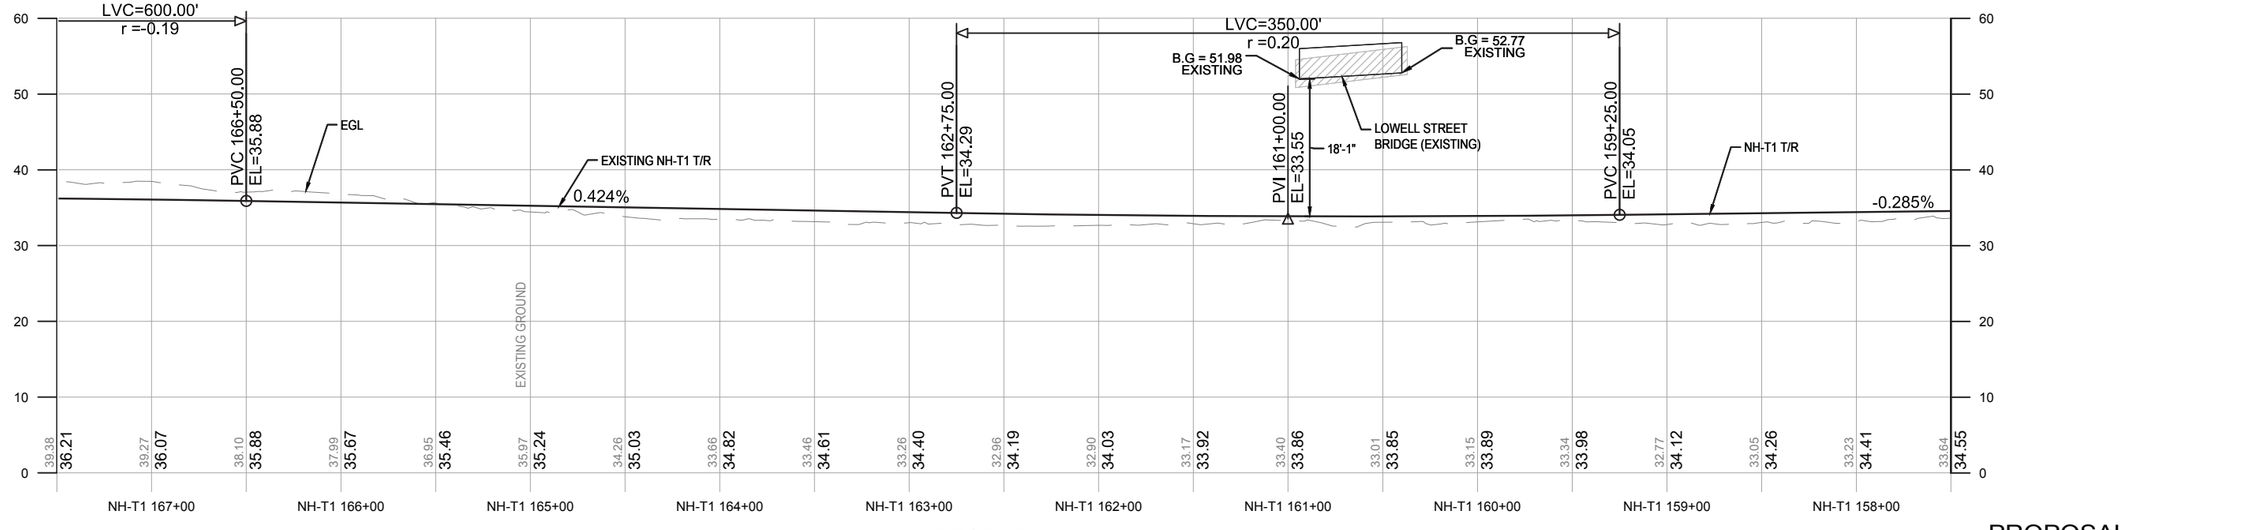

PROFILE

CURVE NO.	NH-T1 13A	NH-T1 13B	NH-T2 13A	NH-T2 13B
Dc	2°10'58.20"	1°01'23.30"	2°11'13.2"	1°01'10.2"
Lc (CHORDED)	997.21 FT	108.16 FT	1000.86 FT	83.19 FT
Ls1	483.42 FT	125.50 FT	472.82 FT	151.13 FT
Ls2	125.50 FT	278.07 FT	151.13 FT	245.97 FT
Ea	4.00 IN	2.75 IN	4.00 IN	2.75 IN
Eu	2.51 IN	2.23 IN	2.51 IN	2.23 IN
V	65 MPH	65 MPH	65 MPH	65 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE
CORRIDOR PLAN AND PROFILE
STA NH-T1 157+50 TO STA NH-T1 167+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-041	

PLOTTED: 09/22/17 2:28PM BY:BRYANTPJ
DRAWING: E:\PROPOSALS\2017\C0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_GK_TRACK_RAIL\00D-RC-2115-2123.DWG [C-041] 09/22/17 12:53PM

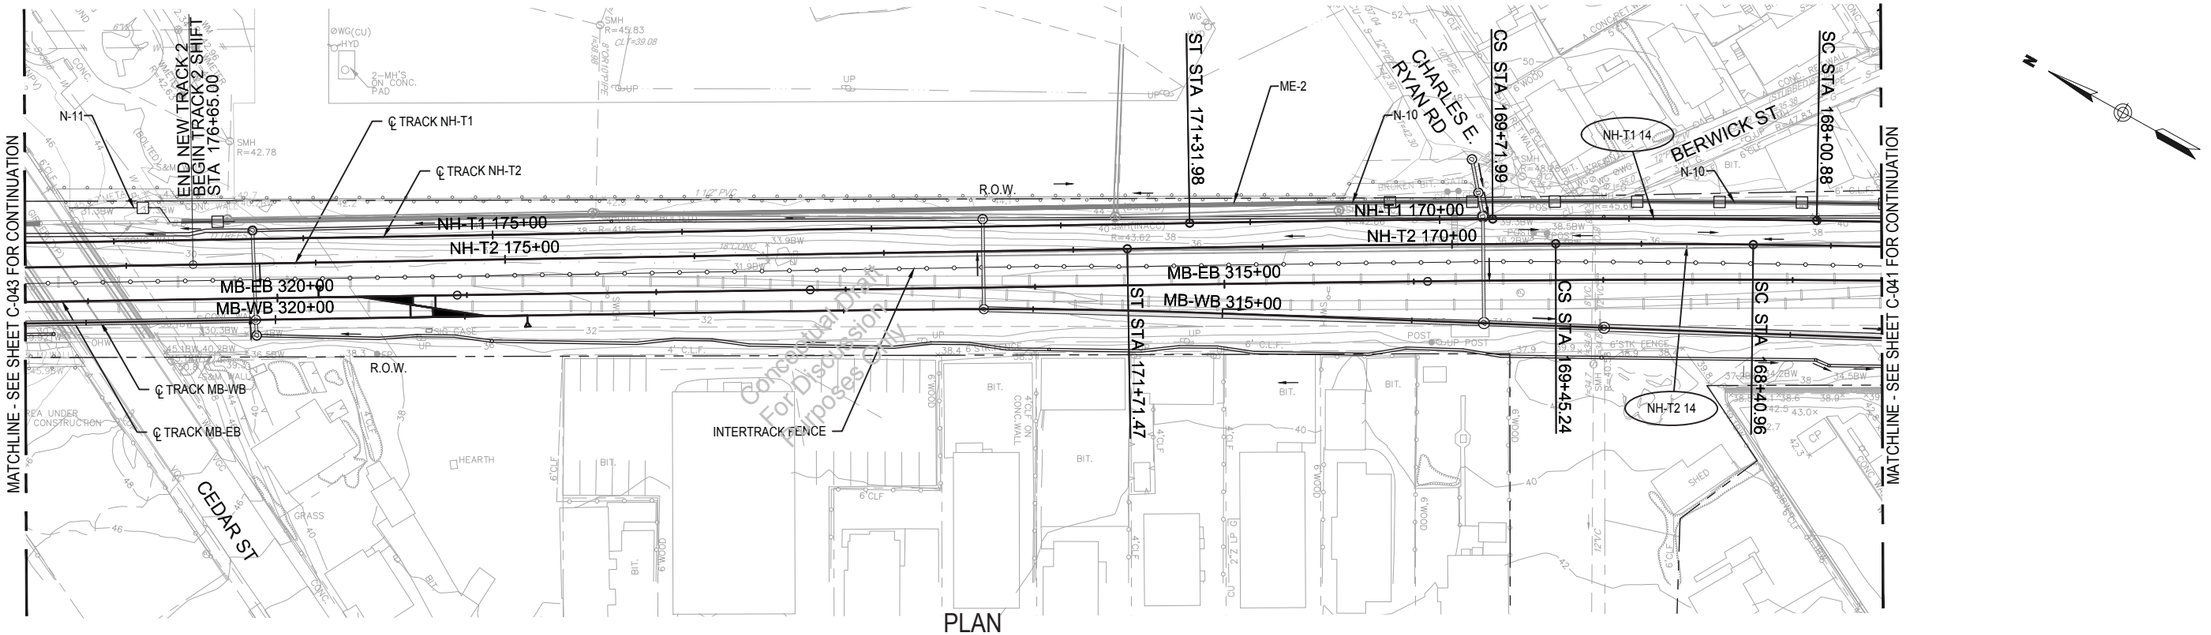

PLAN

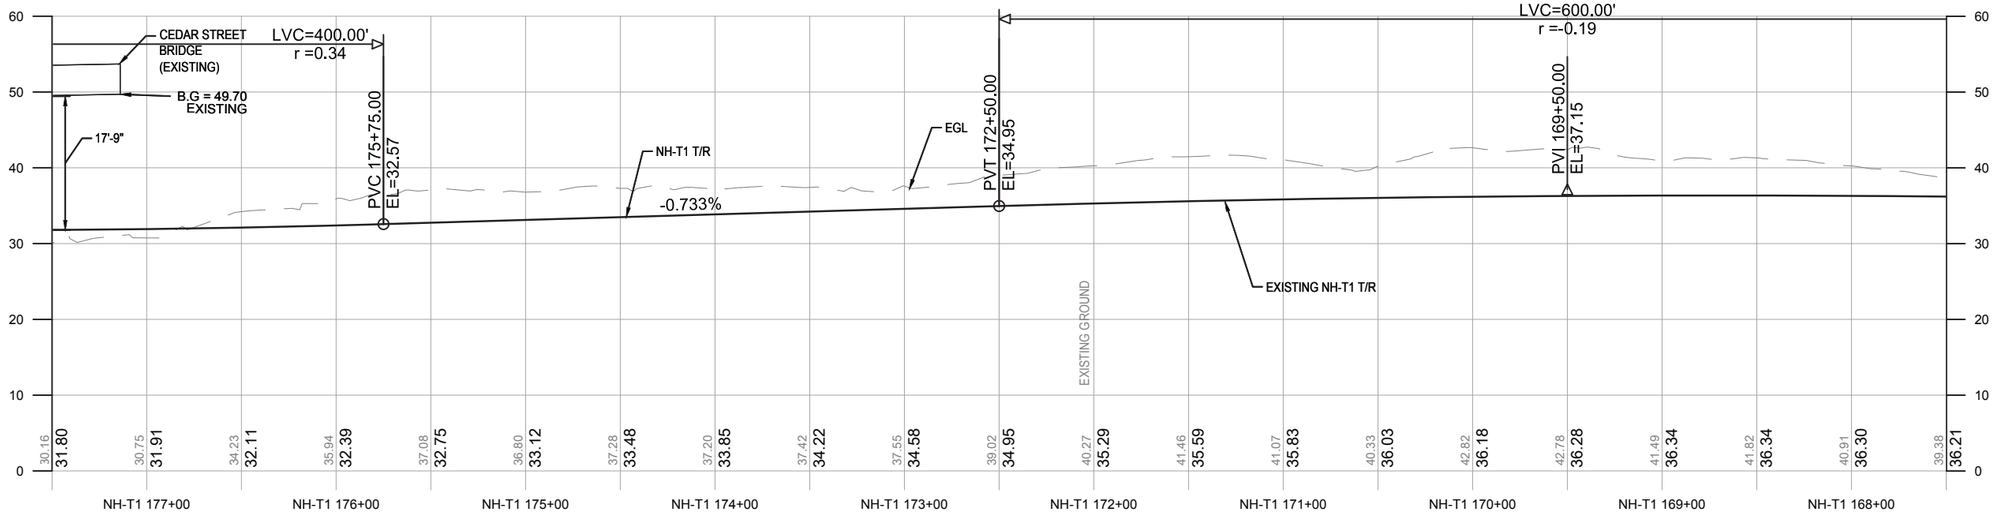

PROFILE

CURVE NO.	NH-T1 14	NH-T2 14
Dc	0°45'0.00"	0°45'04.7"
Lc (CHORDED)	171.11 FT	104.29 FT
Ls1	160.00 FT	226.23 FT
Ls2	160.00 FT	226.23 FT
Ea	1.75 IN	1.75 IN
Eu	1.61 IN	1.62 IN
V	80 MPH	80 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 167+50 TO STA NH-T1 177+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-042	

PLOTTED: 09/21/17 3:29AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_GX_TRACK_RAIL\000-RC-2115-2123.DWG [C-042] 09/20/17 8:38PM

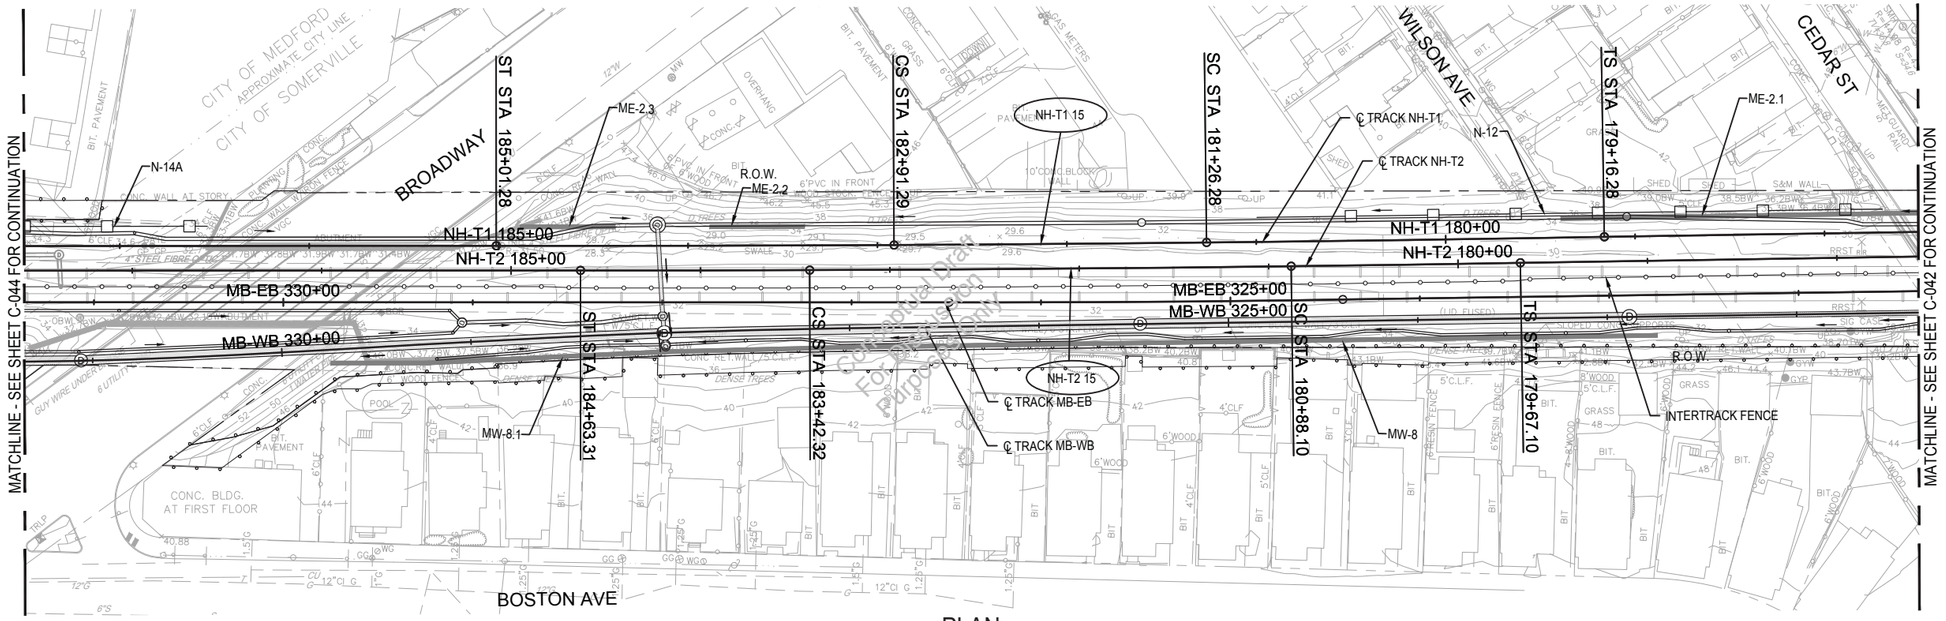

PLAN

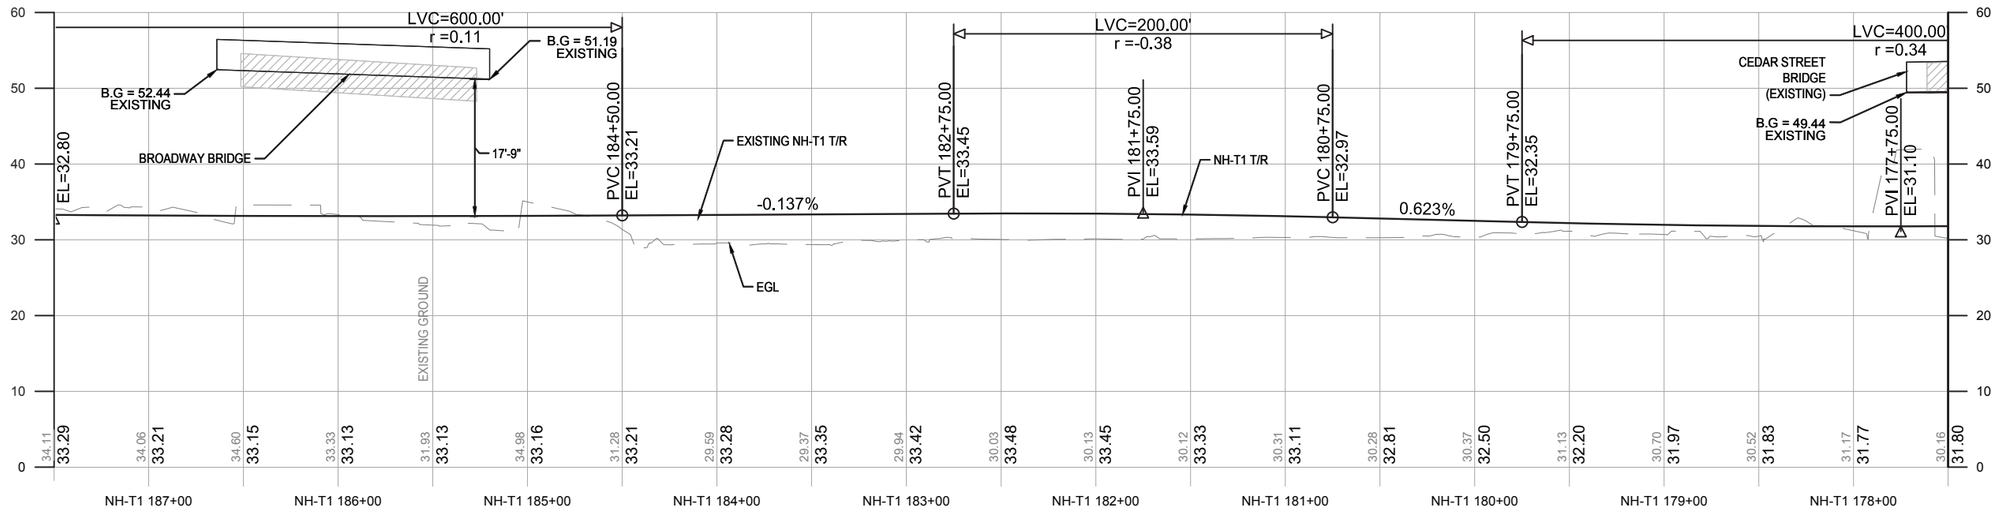

PROFILE

CURVE NO.	NH-T1 15	NH-T2 15
Dc	0°14'0.00"	0°13'59.55"
Lc (CHORDED)	165.02 FT	254.21 FT
Ls1	210.00 FT	121.00 FT
Ls2	210.00 FT	121.00 FT
Ea	1.00 IN	1.00 IN
Eu	0.05 IN	0.04 IN
V	80 MPH	80 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 177+50 TO STA NH-T1 187+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-043	

PLOTTED: 09/22/17 2:13PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_GK_TRACK_RAIL\000-K-2115-2123.DWG [C-043] 09/22/17 12:53PM

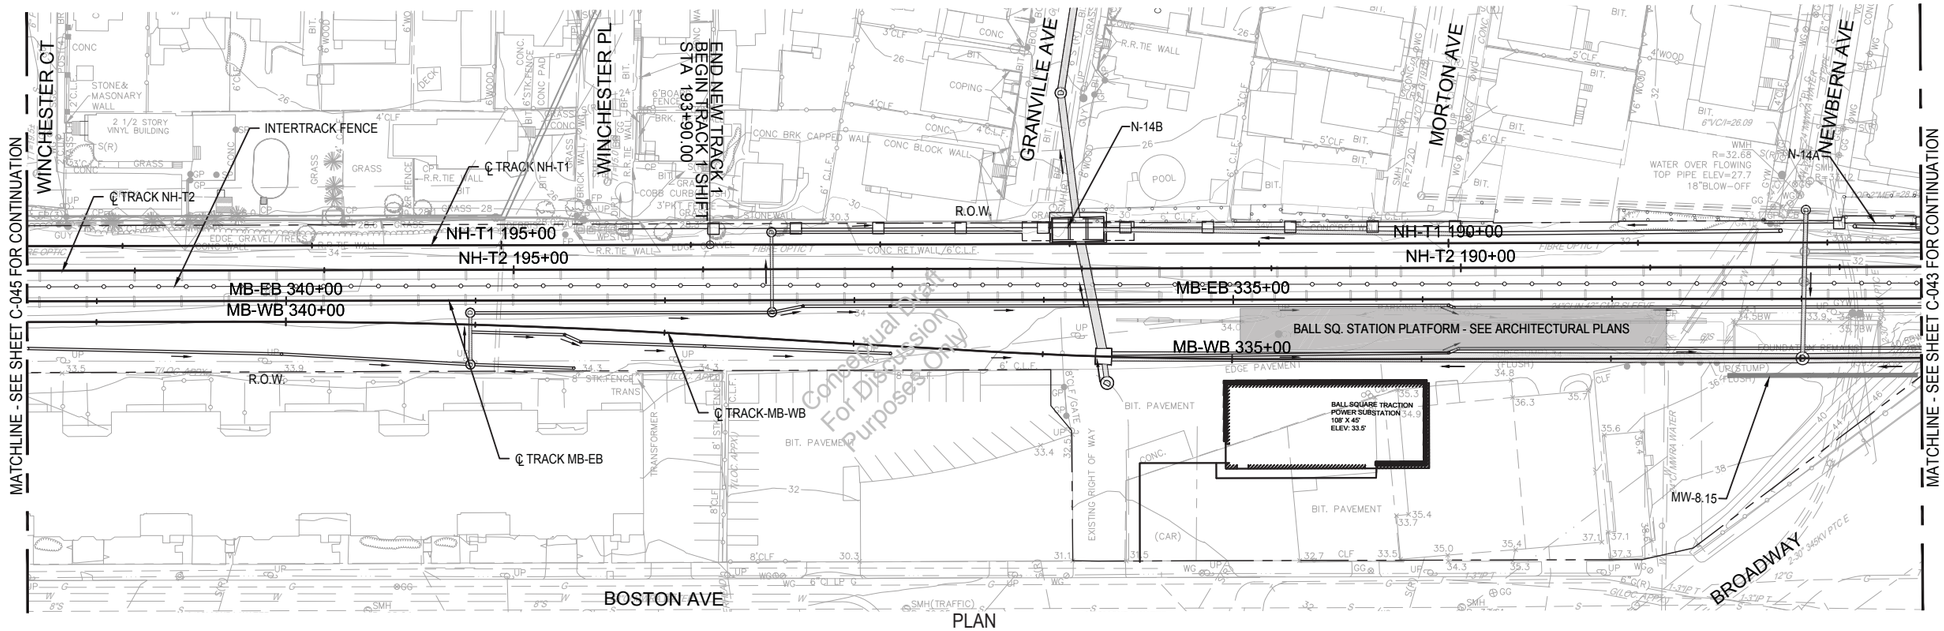

PLAN

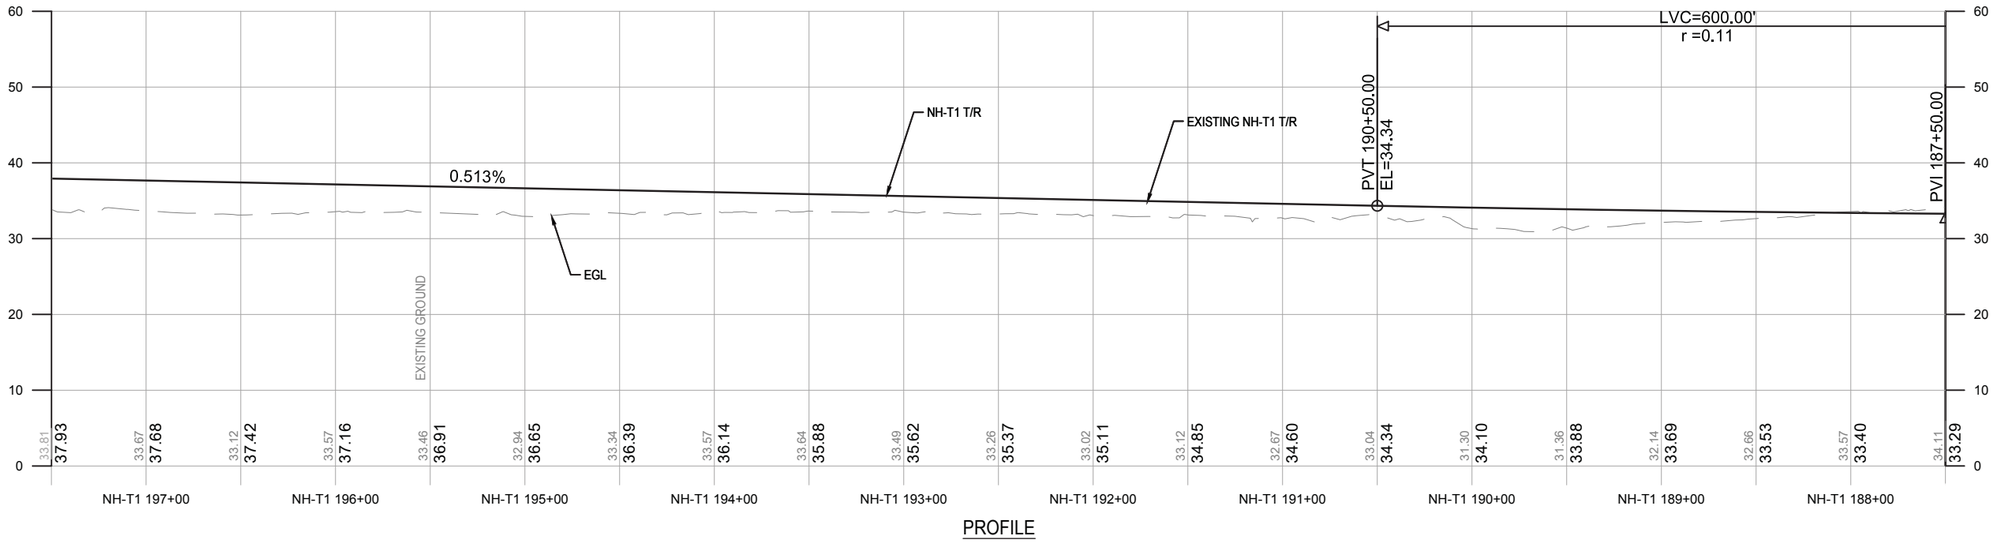

PROFILE

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 187+50 TO STA NH-T1 197+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-044	

PLOTTED: 09/21/17 3:48AM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\0082820 GLX D-B\STV 2017 RFP DESIGN\00_CAD MODELS AND SHEETS\04_CR_TRACK_RAIL\000-H-2115-2123.DWG [C-044] 09/20/17 9:39PM

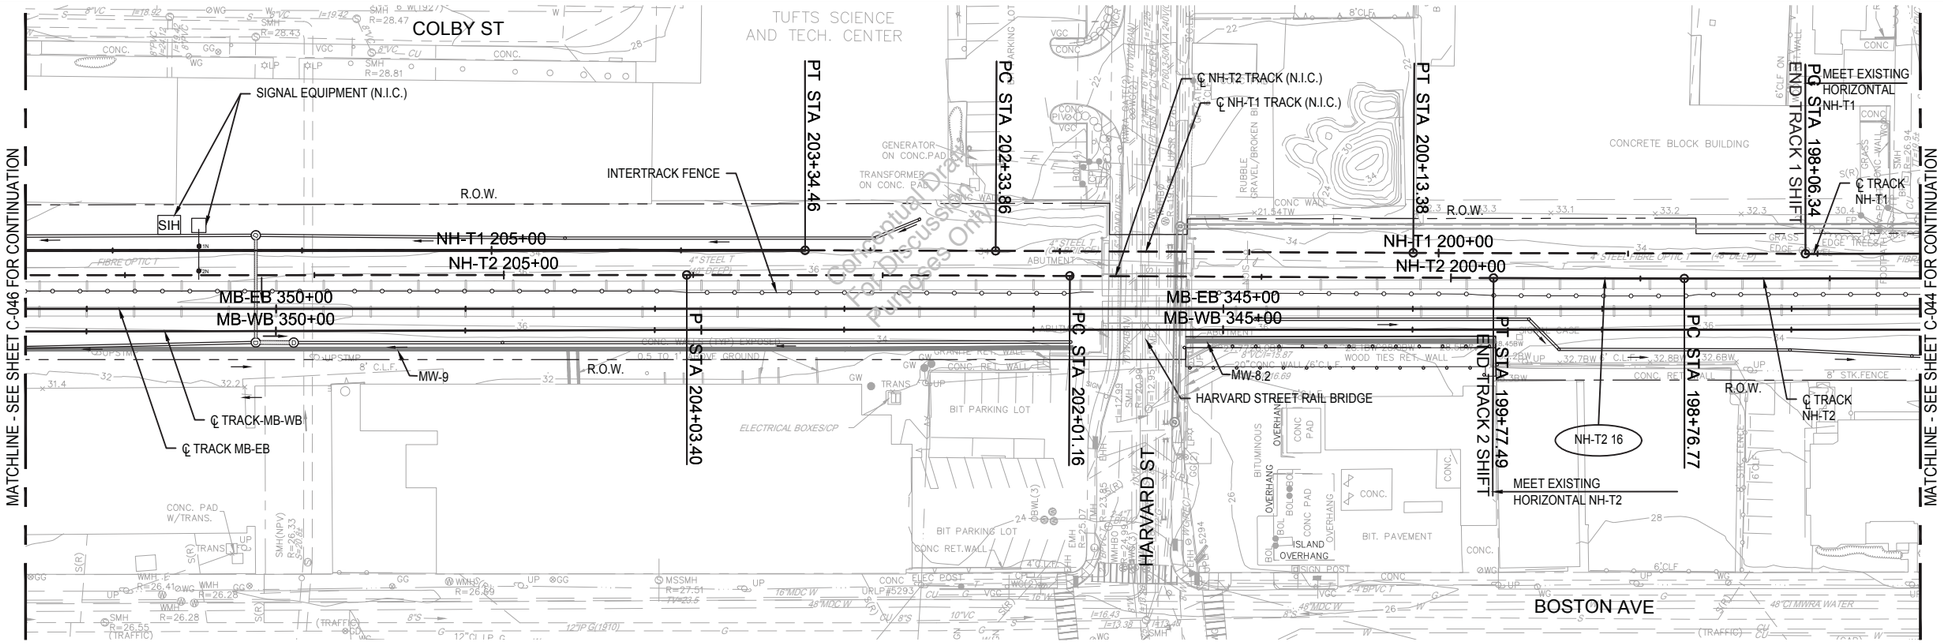

PLAN

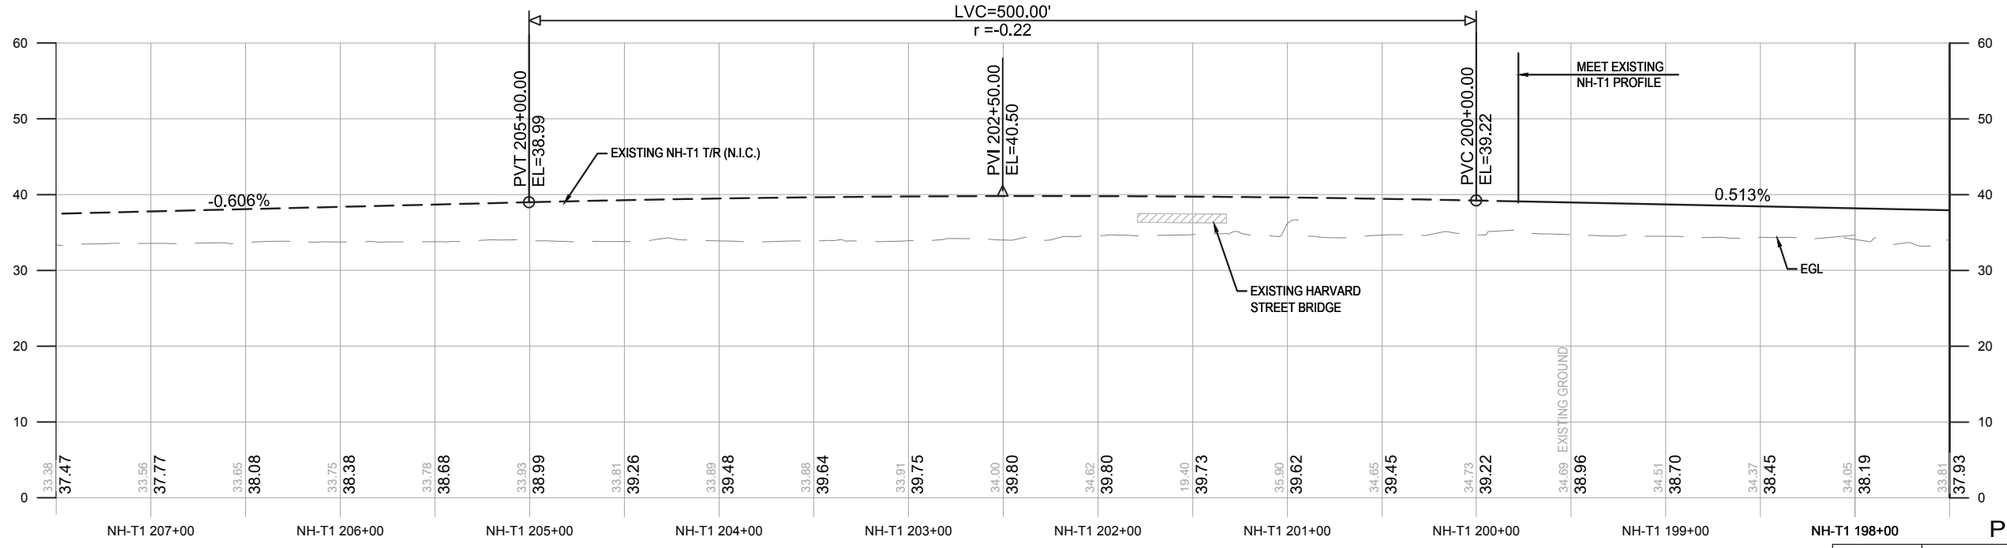

PROFILE

CURVE NO.	NH-T2 16
Dc	0°19'05.92"
Lc (CHORDED)	100.72 FT
Ls1	0.00 FT
Ls2	0.00 FT
Ea	0.00 IN
Eu	1.43 IN
V	80 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 197+50 TO STA NH-T1 207+50

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-045	

Conceptual For Discussion Purposes Only

PLOTTED: 09/22/17 1:48PM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\0082820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2115-2123.DWG [C-045] 09/22/17 12:53PM

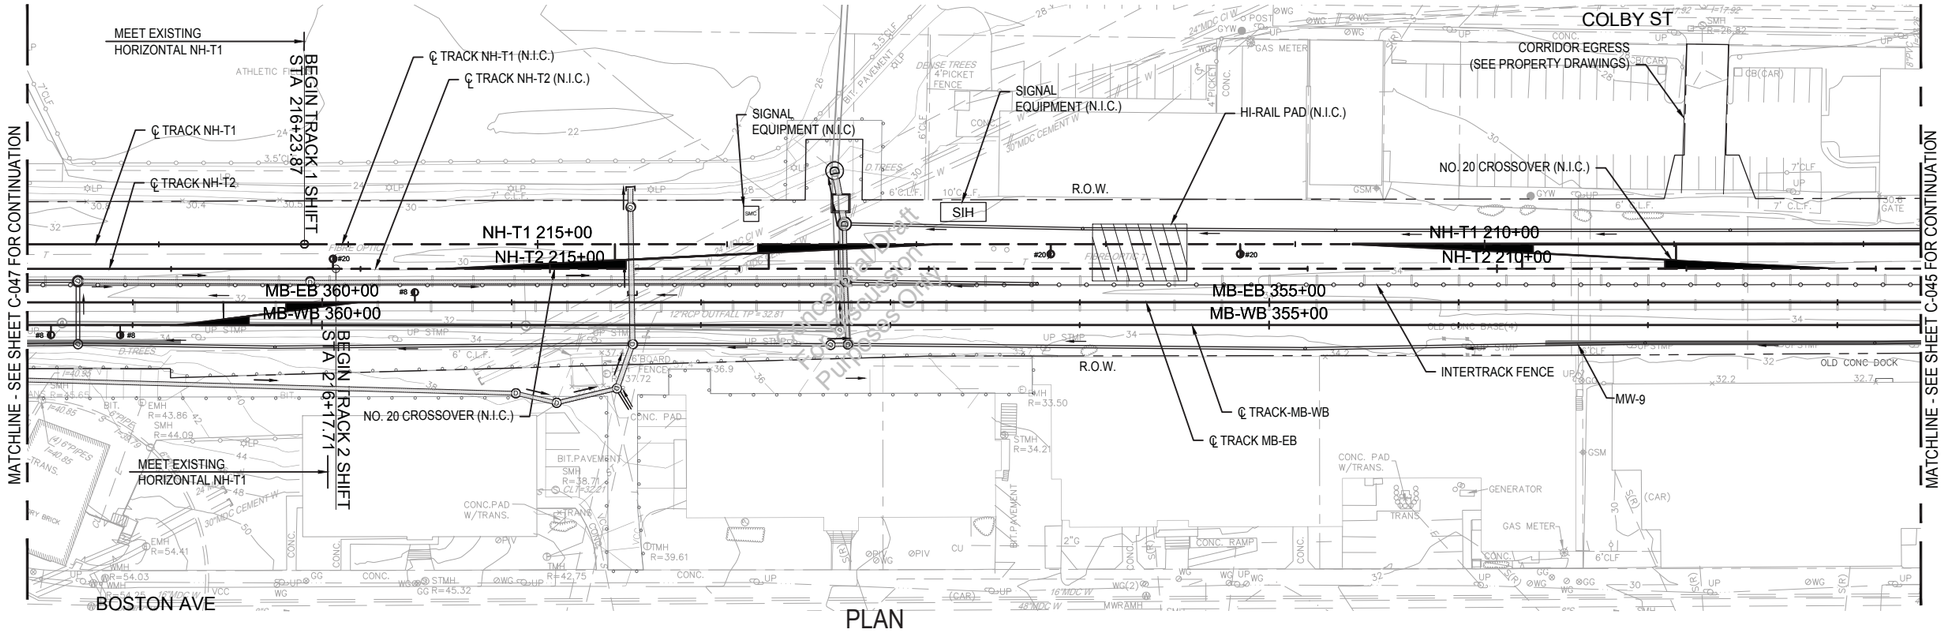

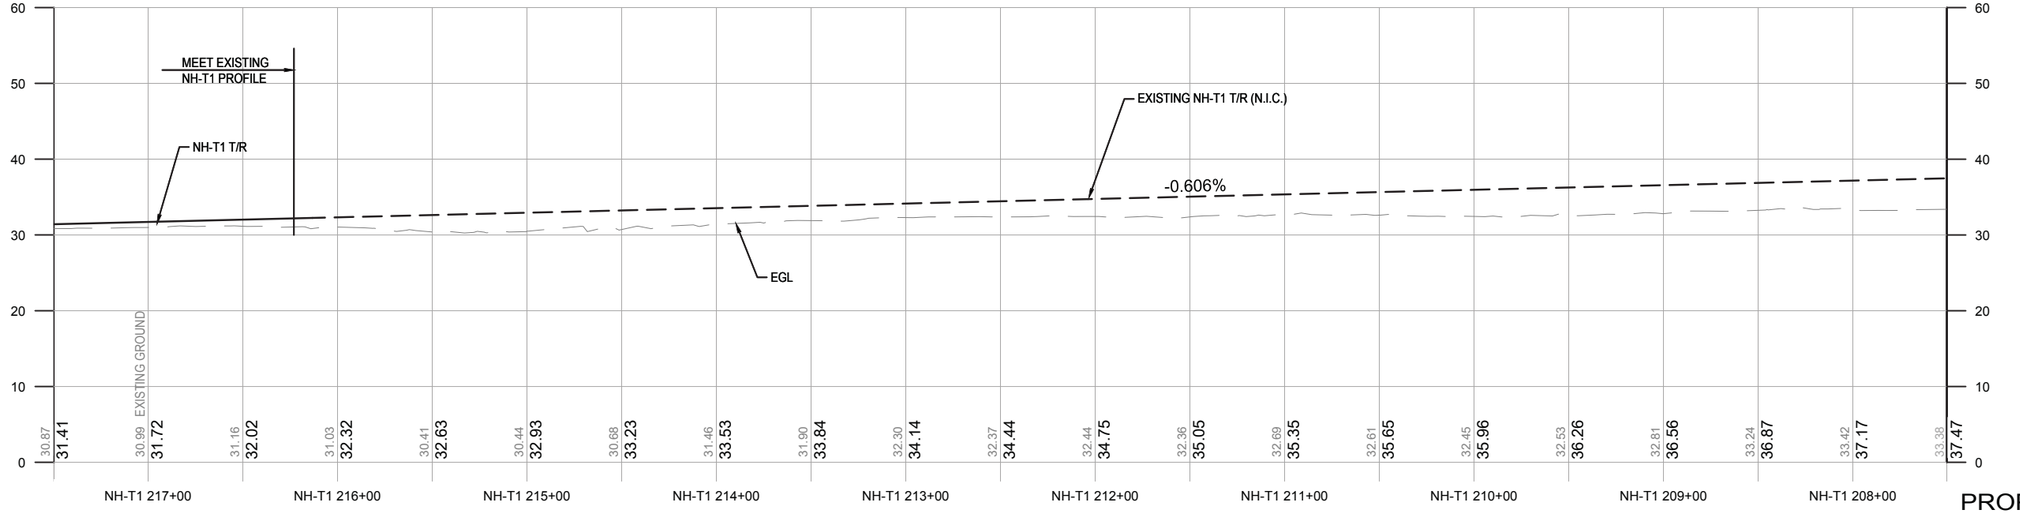

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 207+50 TO STA NH-T1 217+50

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-046	

PLOTTED: 09/21/17 4:04AM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\00_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2115-2123.DWG [C-046] 09/20/17 9:38PM

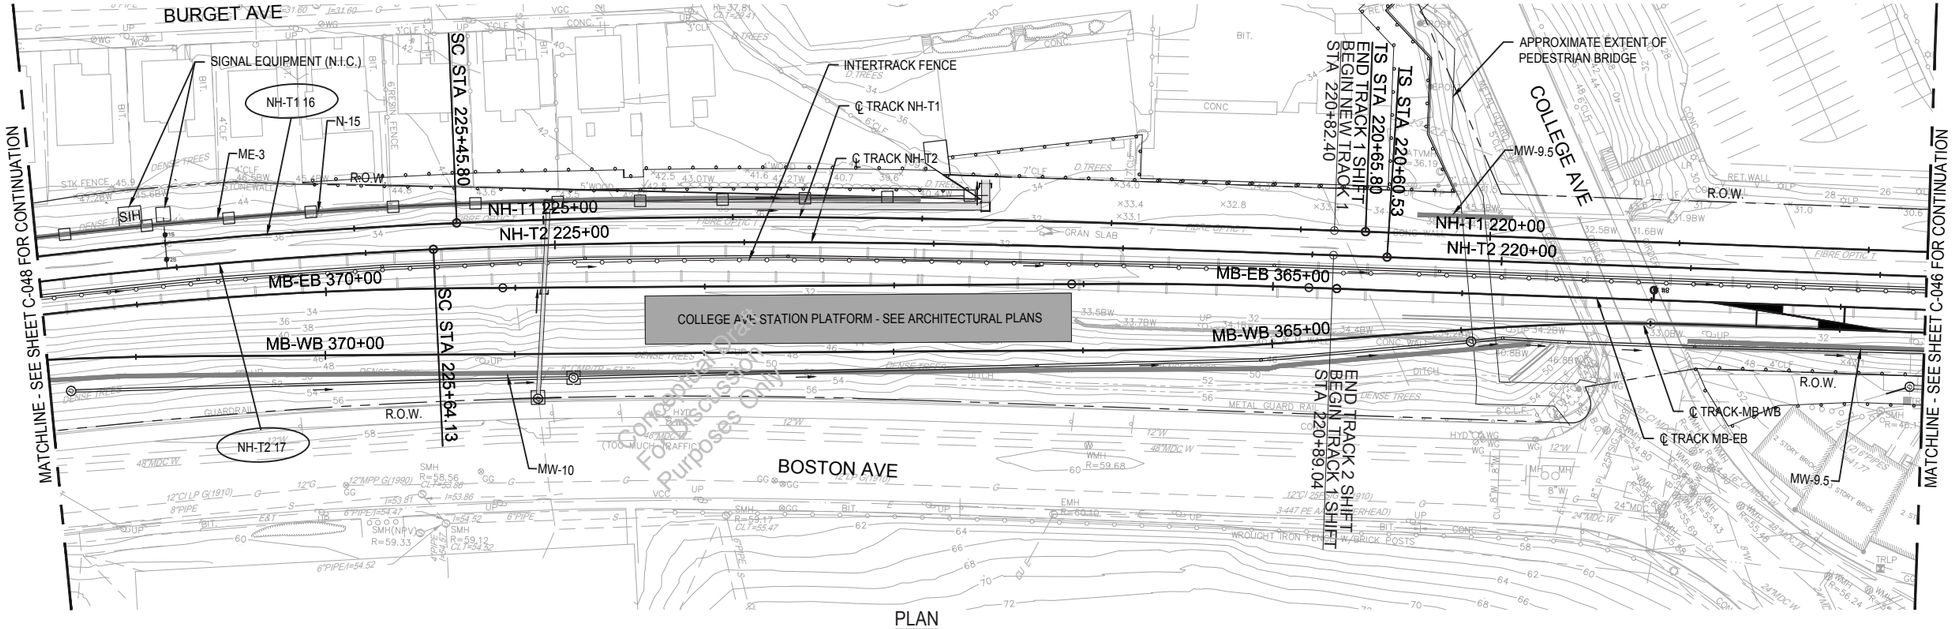

PLAN

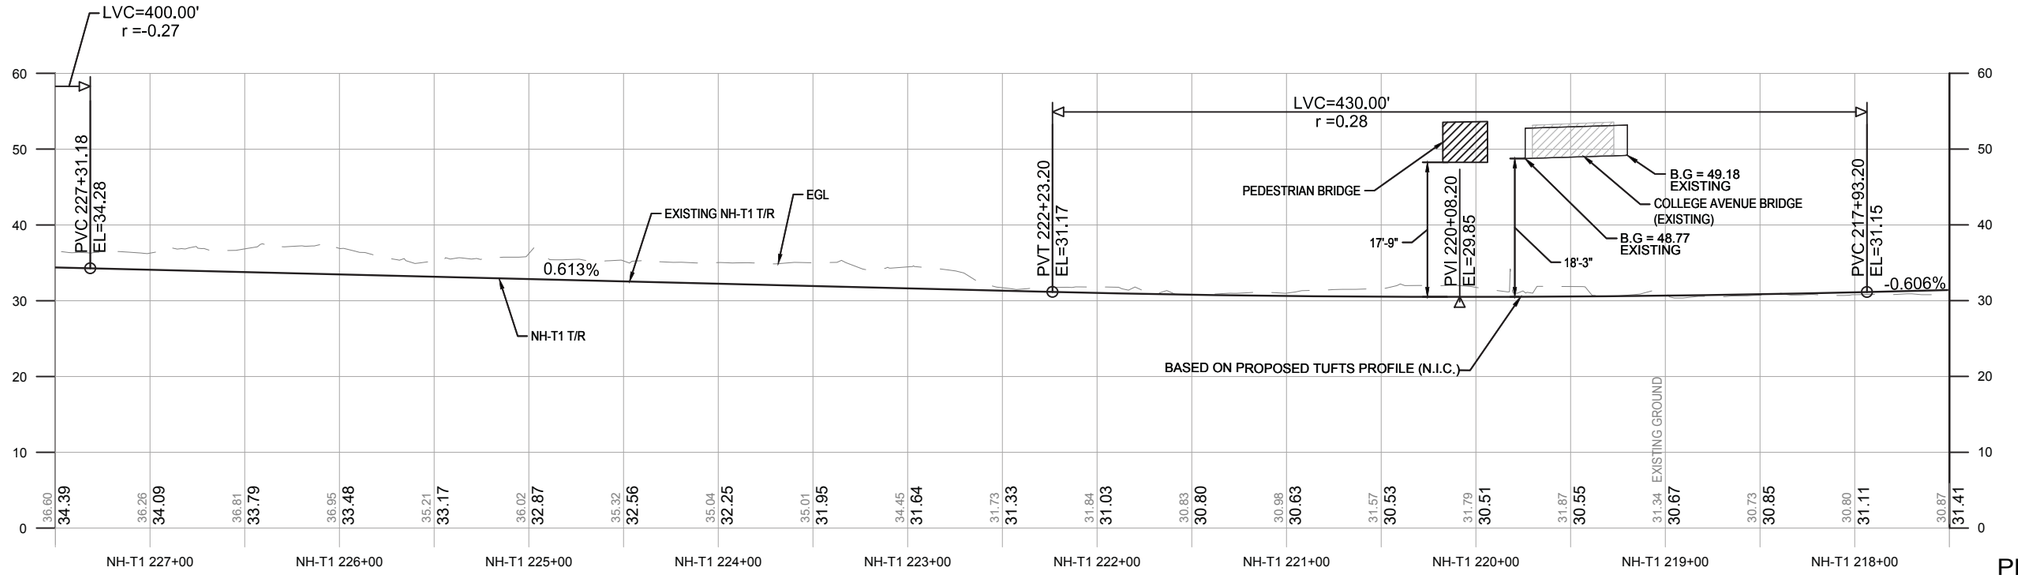

PROFILE

CURVE NO.	NH-T1 16	NH-T2 17
Dc	1°53'05.49"	1°53'35.38"
Lc (CHORDED)	305.15 FT	278.10 FT
Ls1	480.00 FT	503.60 FT
Ls2	480.00 FT	503.60 FT
Ea	4.00 IN	4.00 IN
Eu	2.47 IN	2.49 IN
V	70 MPH	70 MPH

NOTES:

1. REFER TO SHEETS C-003 TO C-024 FOR MEDFORD BRANCH ALIGNMENT AND PROFILE.
2. THE NH-T2 T/R TRACK PROFILE TO BE THE SAME AS NH-T1 T/R TRACK PROFILE.

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 217+50 TO STA NH-T1 227+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-047	

PLOTTED: 09/22/17 1:59PM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_GX_TRACK_RAIL\000-HC-2115-2123.DWG [C-047] 09/22/17 12:53PM

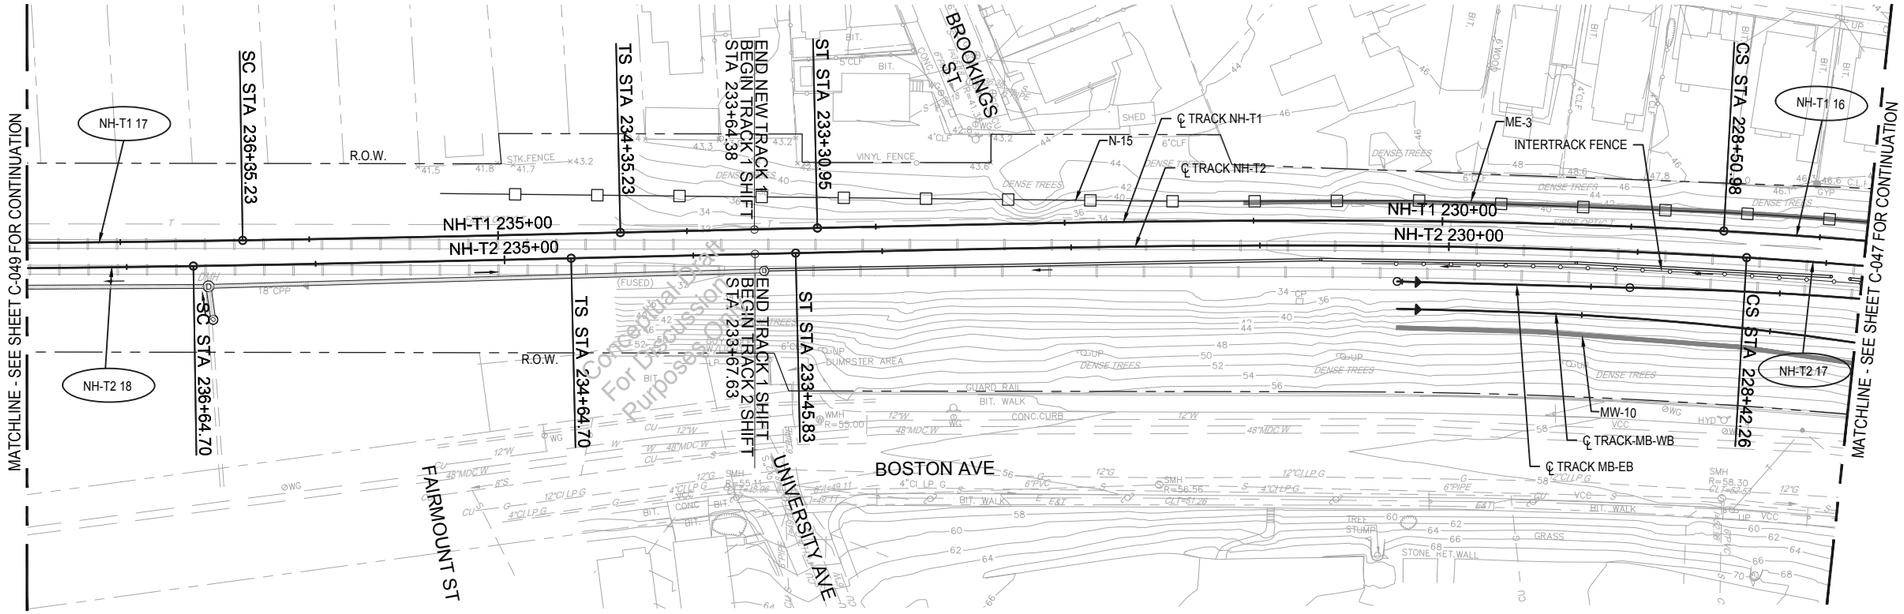

PLAN

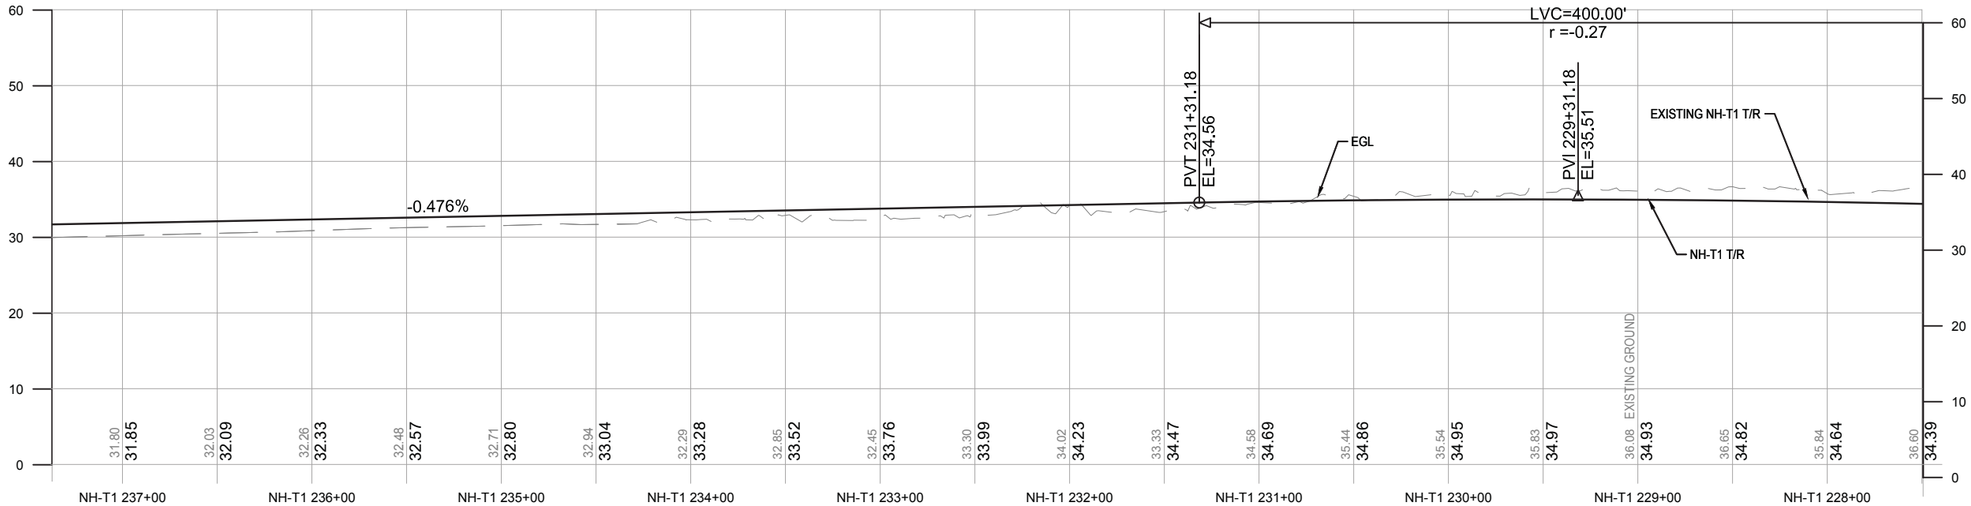

PROFILE

CURVE NO.	NH-T1 16	NH-T2 17	NH-T1 17	NH-T2 18
Dc	1°53'05.49"	1°53'35.38"	0°24'34.7"	0°24'34.7"
Lc (CHORDED)	305.15 FT	278.10 FT	140.16 FT	140.77 FT
Ls1	480.00 FT	503.60 FT	200.00 FT	200.00 FT
Ls2	480.00 FT	503.60 FT	200.00 FT	200.00 FT
Ea	4.00 IN	4.00 IN	1.00 IN	1.00 IN
Eu	2.47 IN	2.49 IN	0.41 IN	0.41 IN
V	70 MPH	70 MPH	70 MPH	70 MPH

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE
CORRIDOR PLAN AND PROFILE
STA NH-T1 227+50 TO STA NH-T1 237+50


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-048	

PLOTTED: 09/21/17 4:21AM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\0082820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2115-2123.DWG [C-048] 09/20/17 9:39PM

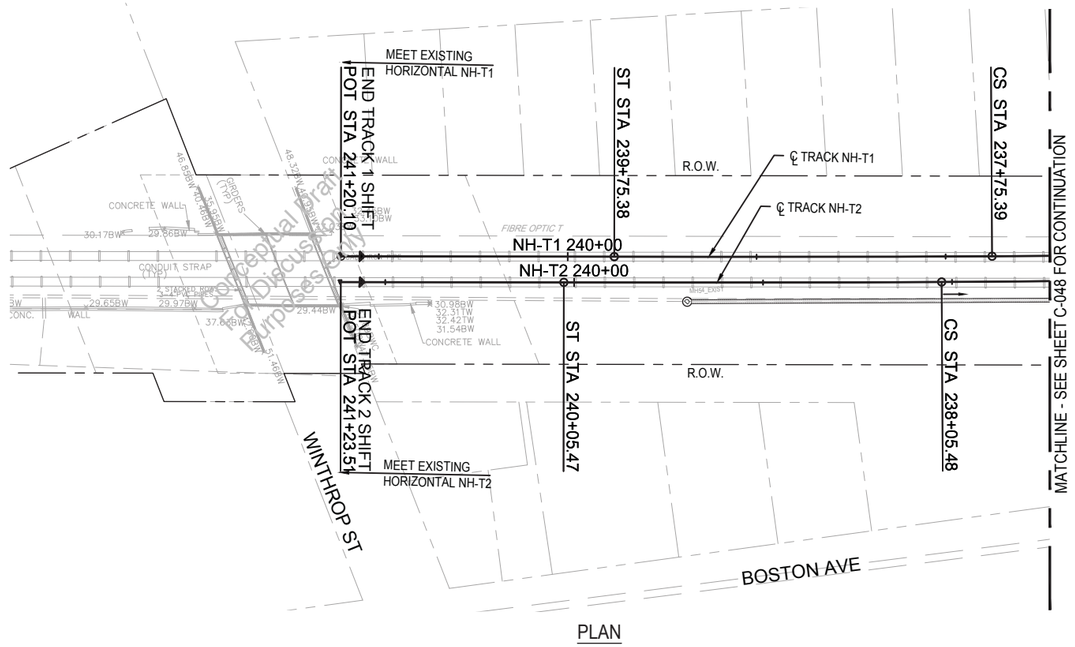

PLAN

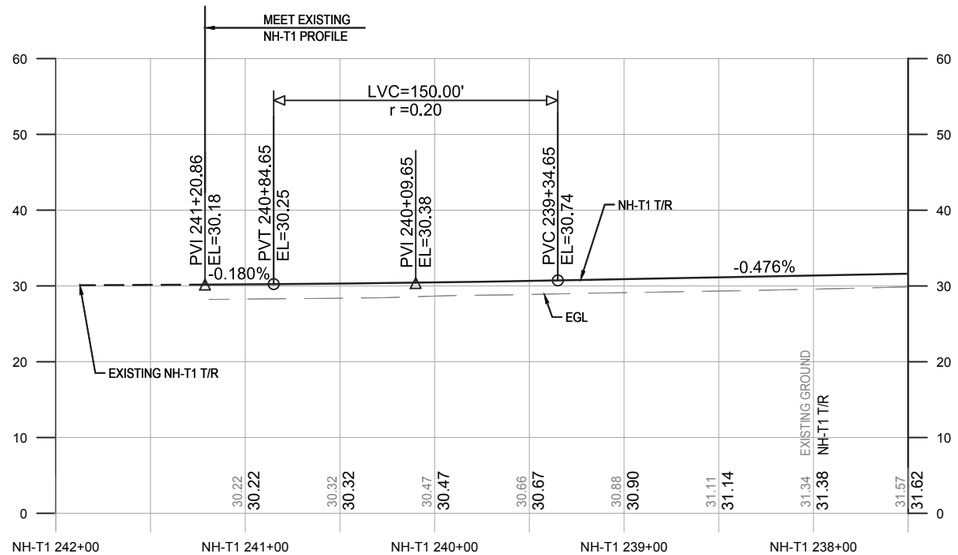

PROFILE

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

NEW HAMPSHIRE MAINLINE CORRIDOR PLAN AND PROFILE STA NH-T1 237+50 TO STA NH-T1 241+20.86


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-049	

PLOTTED: 09/21/17 4:30AM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\00_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-K-2115-2123.DWG [C-049] 09/20/17 9:38PM

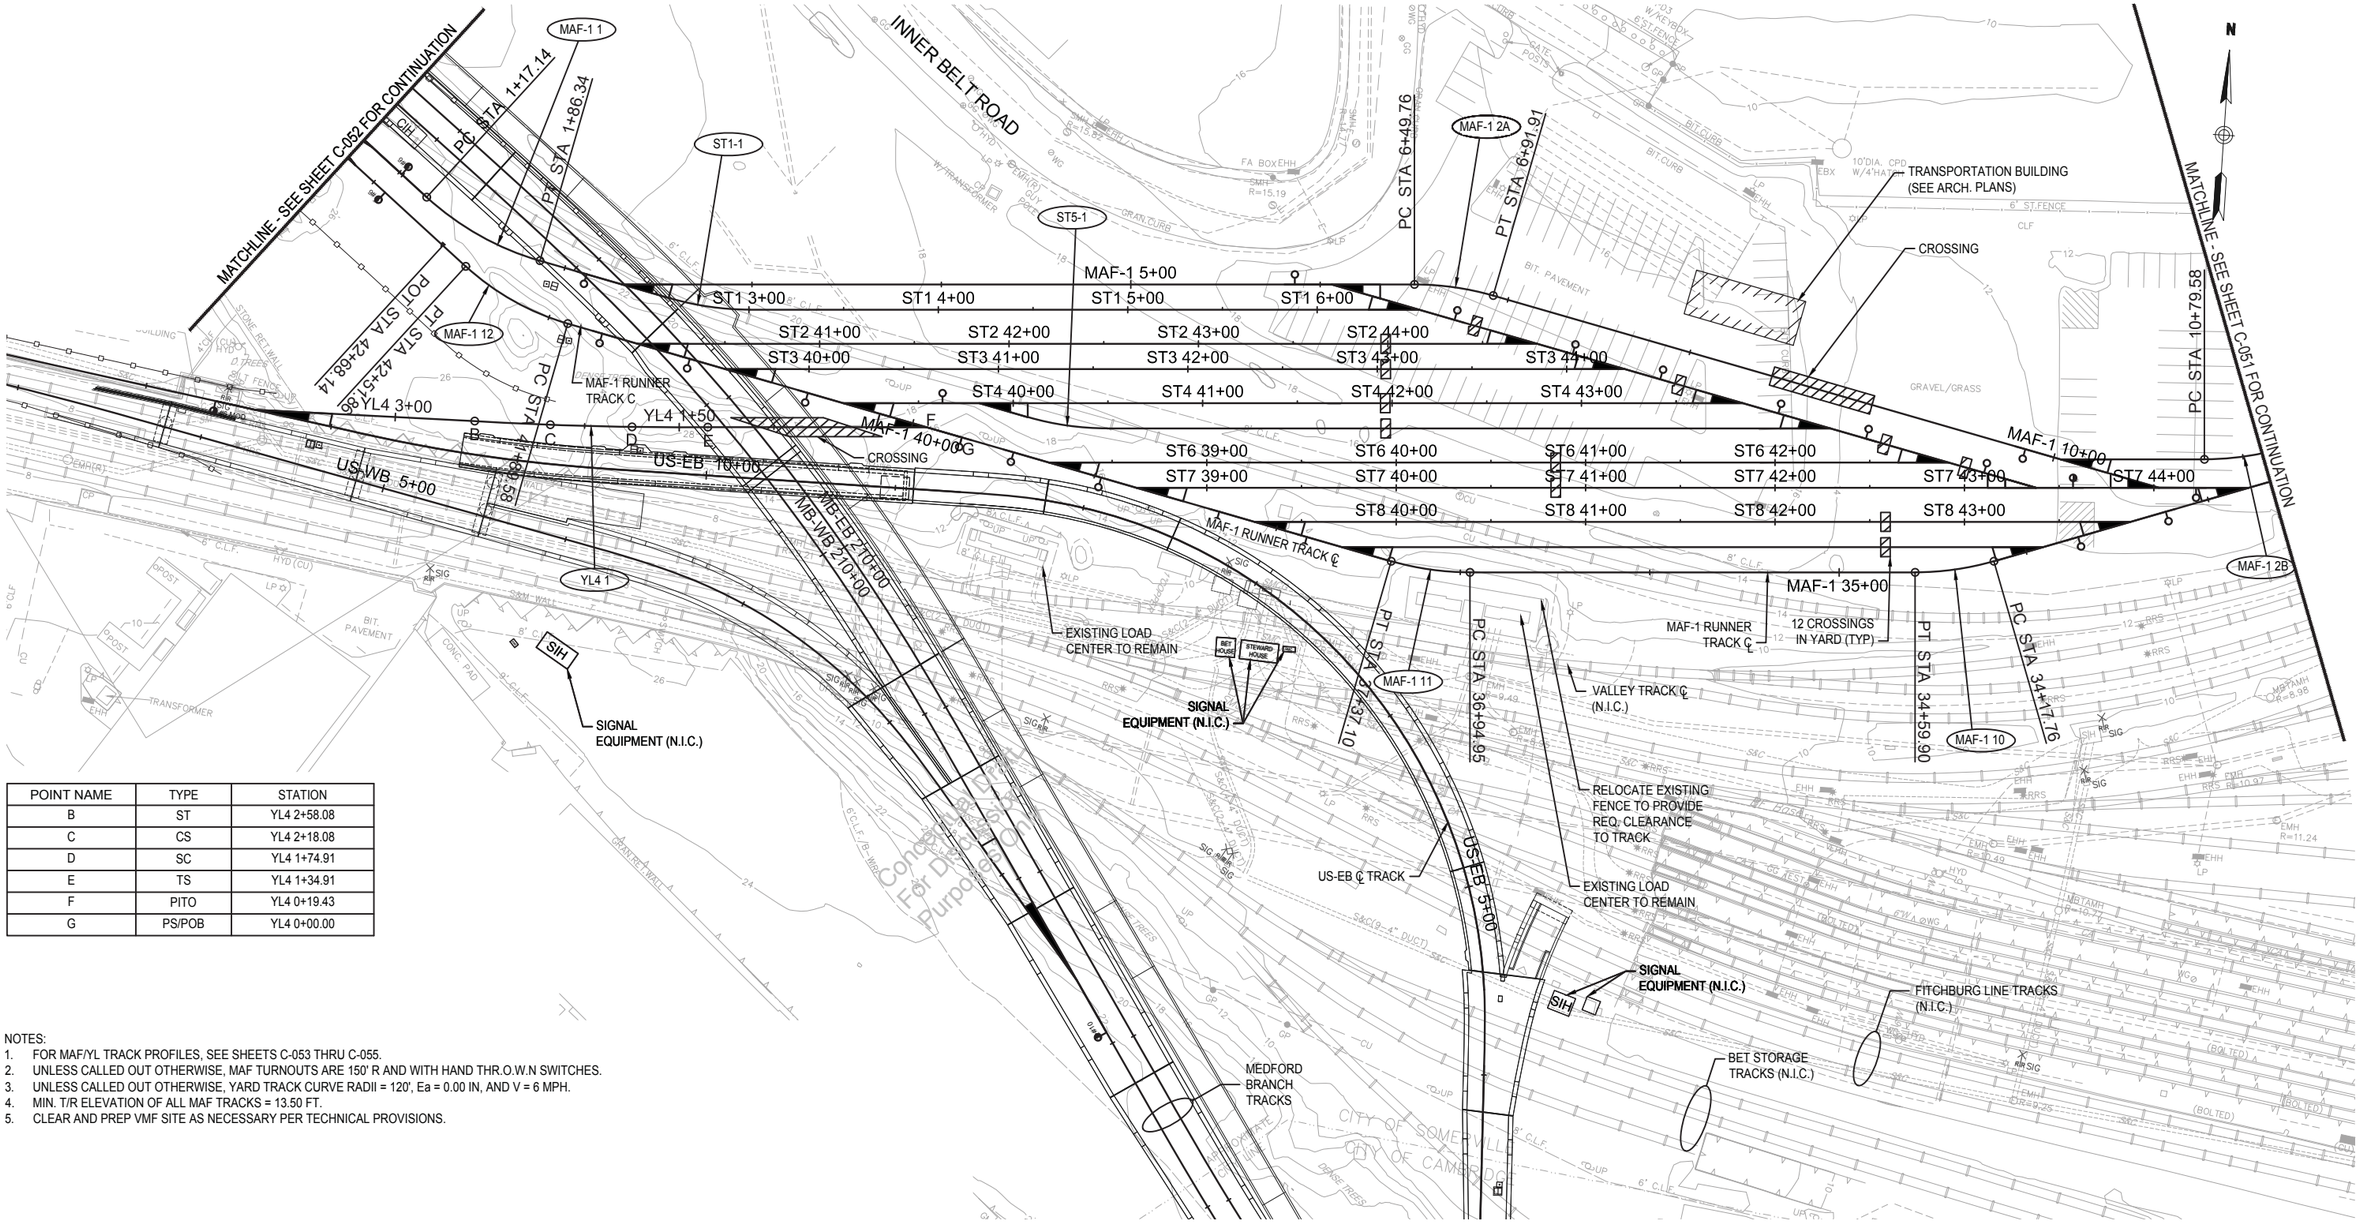

POINT NAME	TYPE	STATION
B	ST	YL4 2+58.08
C	CS	YL4 2+18.08
D	SC	YL4 1+74.91
E	TS	YL4 1+34.91
F	PITO	YL4 0+19.43
G	PS/POB	YL4 0+00.00

NOTES:
1. FOR MAF/YL TRACK PROFILES, SEE SHEETS C-053 THRU C-055.
2. UNLESS CALLED OUT OTHERWISE, MAF TURNOUTS ARE 150' R AND WITH HAND THR.O.W.N SWITCHES.
3. UNLESS CALLED OUT OTHERWISE, YARD TRACK CURVE RADII = 120', Ea = 0.00 IN, AND V = 6 MPH.
4. MIN. T/R ELEVATION OF ALL MAF TRACKS = 13.50 FT.
5. CLEAR AND PREP VMF SITE AS NECESSARY PER TECHNICAL PROVISIONS.

PLAN

CURVE NO.	YL4 1	MAF-1 1	MAF-1 2A	MAF-1 2B	MAF-1 10	MAF-1 11	MAF-1 12	ST1-1	ST5-1
R	1600.00 FT	150 FT	150 FT	150 FT	150 FT	150 FT	150 FT	150 FT	150 FT
Lc	43.18 FT	69.2 FT	42.15 FT	42.15 FT	42.15 FT	42.15 FT	69.2 FT	42.15 FT	42.15 FT
Ls1	40.00 FT	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT
Ls2	40.00 FT	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT	O FT	0 FT
Ea	.00 IN	0 IN	0 IN	0 IN	0 IN	0 IN	0 IN	O IN	0 IN
Eu	0.25 IN	0.96 IN	0.96 IN	.96 IN	0.96 IN	0.96 IN	0.96 IN	.96 IN	0.96 IN
V	10 MPH	6 MPH	6 MPH	6 MPH	6 MPH	6 MPH	6 MPH	6 MPH	6 MPH

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE & STORAGE FACILITY
YARD LEAD TRACK PLAN
SHEET 1


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE:	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-050	

PLOTTED: 09/21/17 2:02PM BY:BRYANTPJ
DRAWING: L:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\MAF-K-2001_RE-DEF.DWG [C-050] 09/20/17 8:23PM

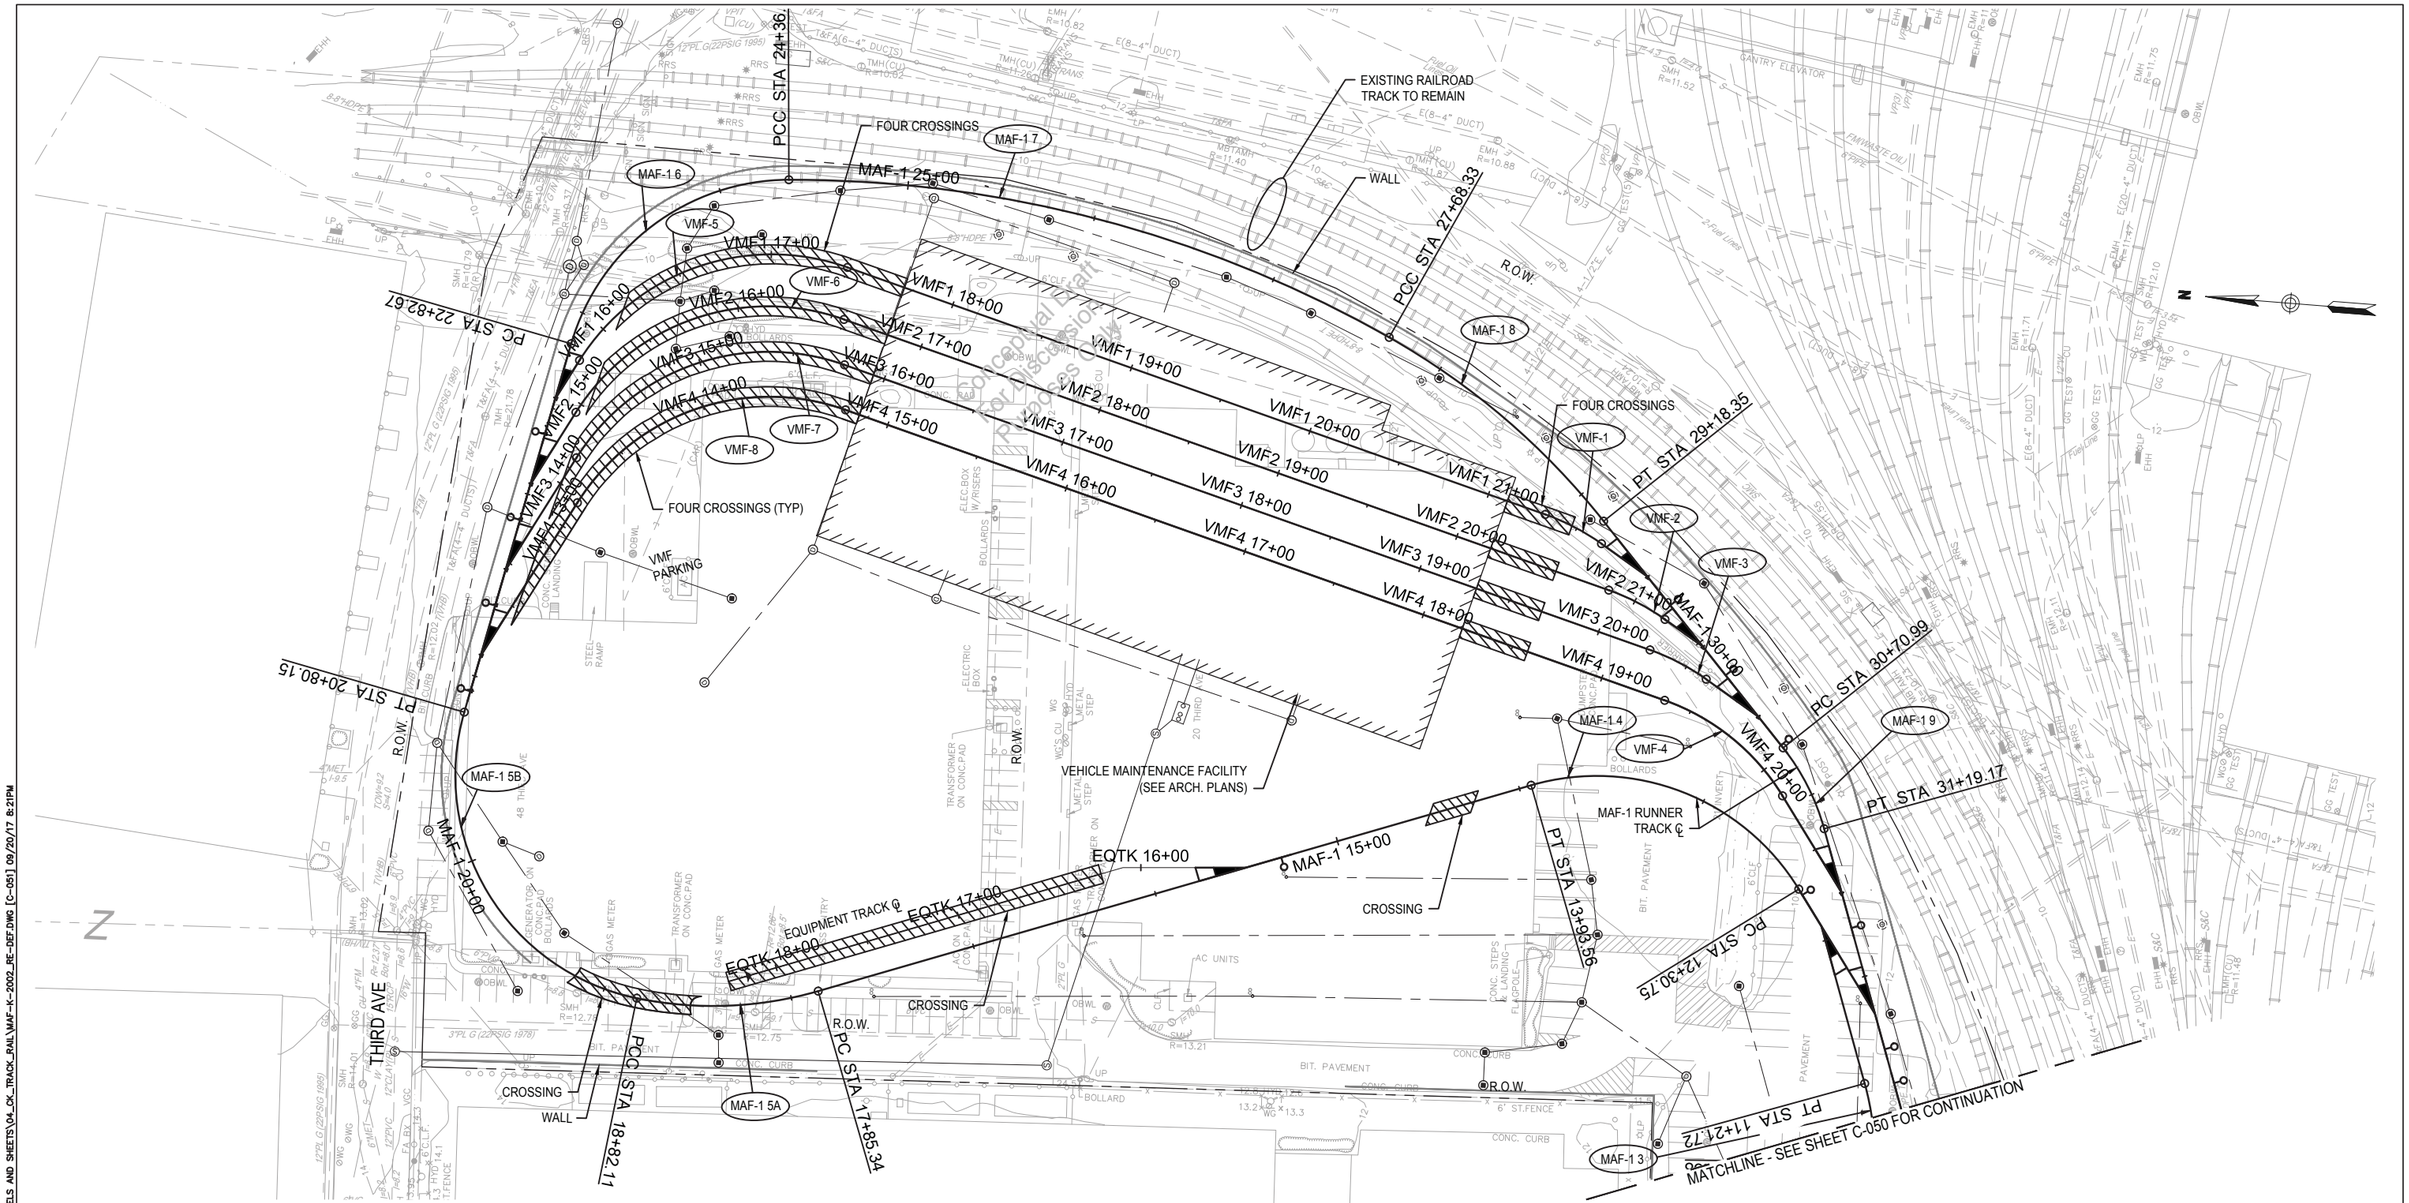

CURVE NO.	MAF-1 3	MAF-1 4	MAF-1 5A	MAF-1 5B	MAF-1 6	MAF-1 7	MAF-1 8	MAF-1 9
R	150 FT	125 FT	200 FT	120 FT	120 FT	638.74 FT	390 FT	120 FT
Lc	42.15 FT	162.81 FT	96.77 FT	198.04 FT	154.3 FT	331.36 FT	150.02 FT	48.19 FT
Ls1	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT
Ls2	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT
Ea	0 IN	0 IN	0 IN	0 IN	0 IN	0 IN	0 IN	0 IN
Eu	0.96 IN	1.16 IN	0.72 IN	1.2 IN	1.2 IN	0.23 IN	0.37 IN	1.2 IN
V	6 MPH	6 MPH	6 MPH	6 MPH	6 MPH	6 MPH	6 MPH	6 MPH

CURVE NO.	VMF-1	VMF-2	VMF-3	VMF-4	VMF-5	VMF-6	VMF-7	VMF-8
R	120 FT	120 FT	120 FT	120 FT	120 FT	120 FT	120 FT	120 FT
Lc	33.56 FT	33.56 FT	33.56 FT	81.69 FT	158.66 FT	161.71 FT	161.71 FT	161.78 FT
Ls1	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT
Ls2	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT	0 FT
Ea	0 IN	0 IN	0 IN	0 IN	0 IN	0 IN	0 IN	0 IN
Eu	1.2 IN	1.2 IN	1.2 IN	1.2 IN	1.2 IN	1.2 IN	1.2 IN	1.2 IN
V	6 MPH	6 MPH	6 MPH	6 MPH	6 MPH	6 MPH	6 MPH	6 MPH

PLAN

NOTES:
1. FOR MAF/YL TRACK PROFILES, SEE SHEETS C-053 THRU C-055.
2. UNLESS CALLED OUT OTHERWISE, MAF TURNOUTS ARE 150' R AND WITH HAND THROWN SWITCHES.
3. UNLESS CALLED OUT OTHERWISE, YARD TRACK CURVE RADII = 120', Ea = 0.00 IN, AND V = 6 MPH.
4. MIN. T/R ELEVATION FOR ALL TRACKS = 13.50 FT.
5. CLEAR AND PREP VMF SITE AS NECESSARY PER TECHNICAL PROVISIONS.

40 0 40 80
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE & STORAGE FACILITY
YARD LEAD TRACK PLAN
SHEET 2

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-276


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-051	

4-197

PLOTTED: 09/20/17 10:29PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0082820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\MAF-K-2002_RE-DEF.DWG [C-051] 09/20/17 8:21PM

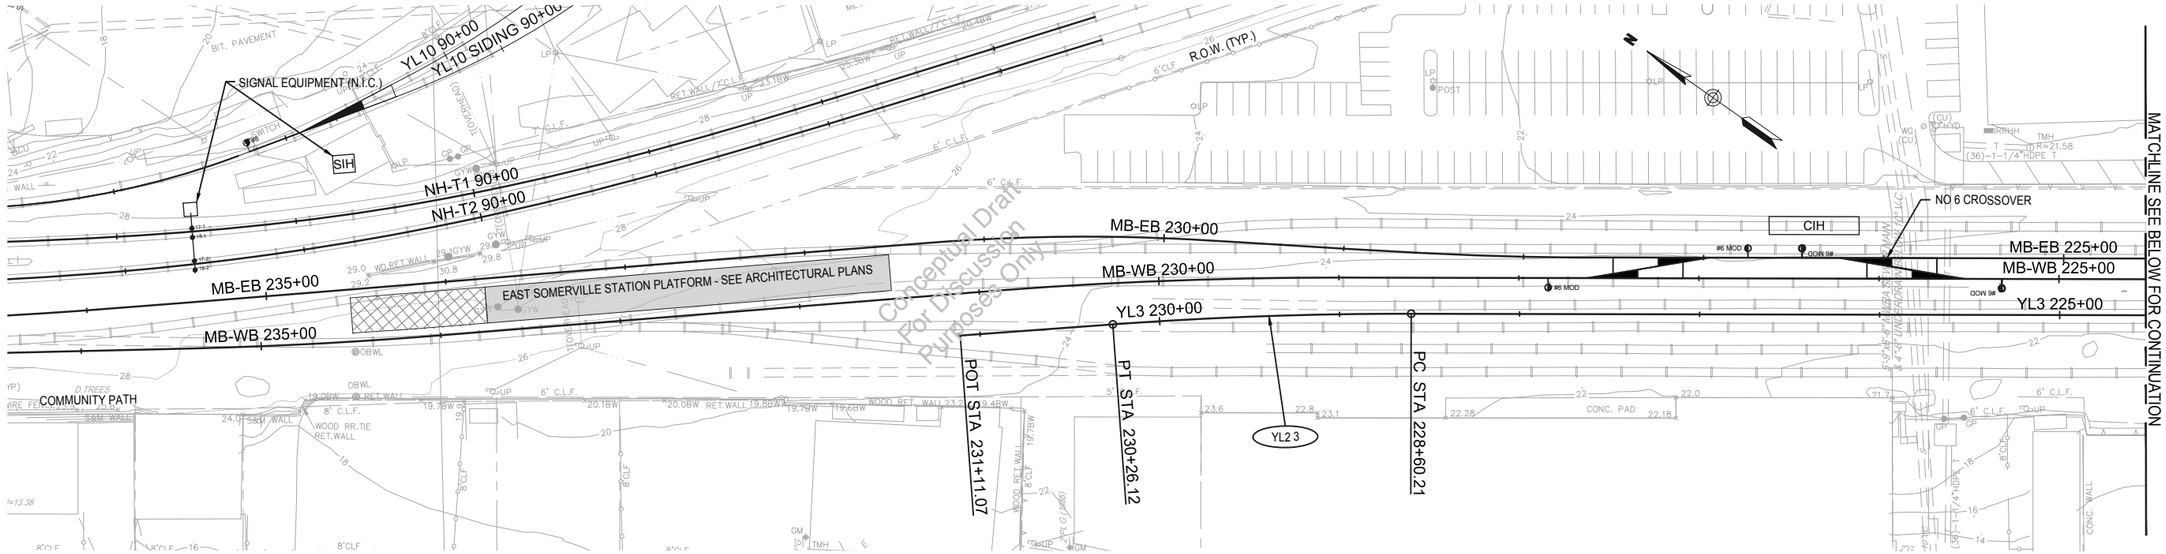

PLAN

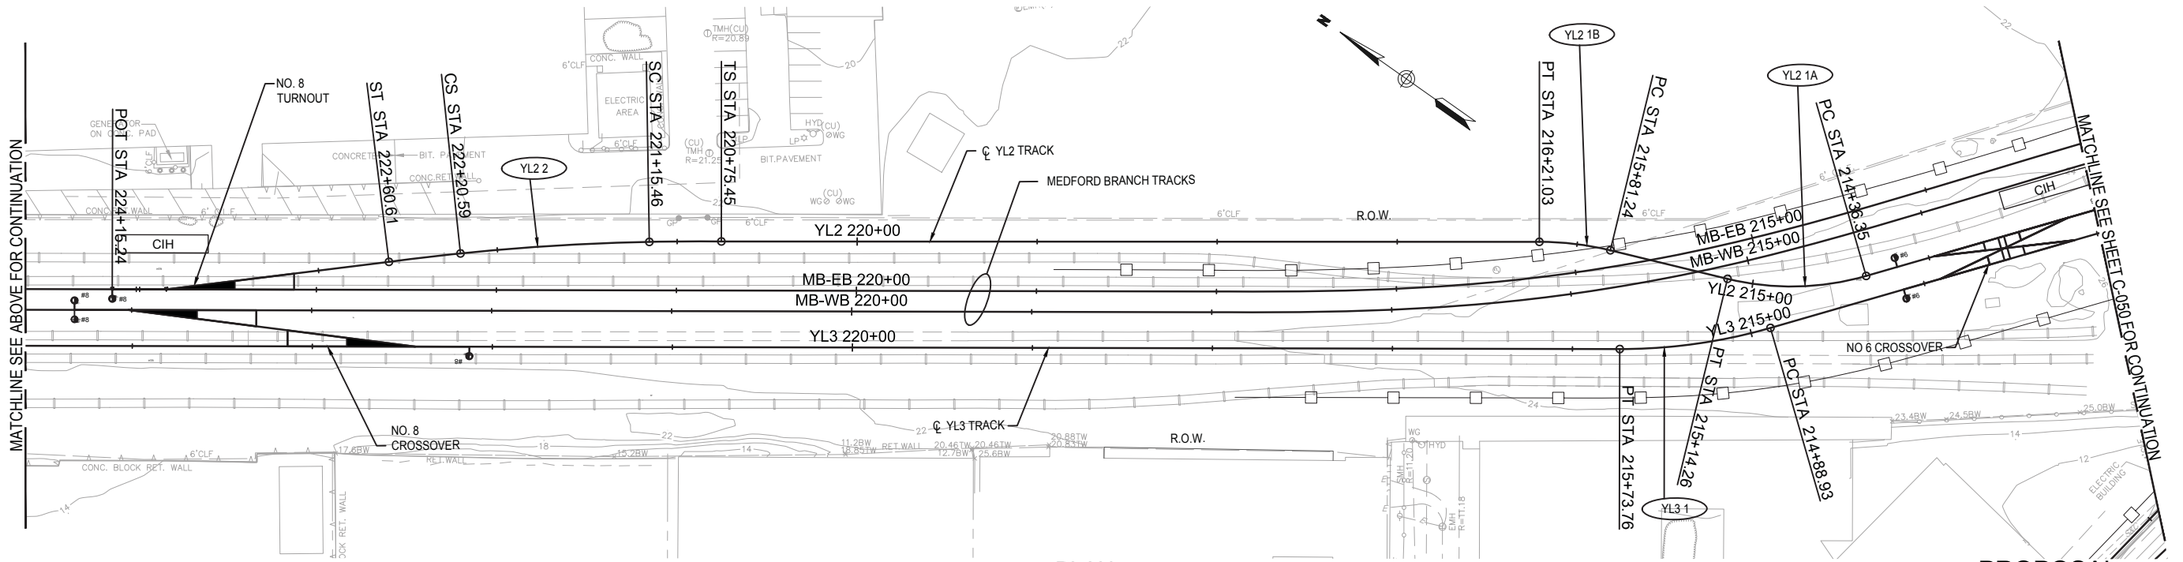

PLAN

NOTES:
1. FOR MAF/YL TRACK PROFILES, SEE SHEETS C-053 THRU C-055.
2. UNLESS CALLED OUT OTHERWISE, MAF TURNOUTS ARE 150' R AND WITH HAND THROWN SWITCHES.
3. UNLESS CALLED OUT OTHERWISE, YARD TRACK CURVE RADII = 120', Ea = 0.00 IN, AND V = 6 MPH.

CURVE NO.	YL2 1A	YL2 1B	YL2 2	YL3 1	YL2 3
R	140 FT	167 FT	1178 FT	300 FT	2213.39 FT
Lc	49.47 FT	39.79 FT	105.14 FT	84.82 FT	101.16 FT
Ls1	0 FT	0 FT	40.01 FT	0 FT	65 FT
Ls2	0 FT	0 FT	40.01 FT	0 FT	65 FT
Ea	0 IN	0 IN	1 IN	1 IN	0.5 IN
Eu	1.03 IN	0.86 IN	0.36 IN	0.34 IN	0.22 IN
V	6 MPH	6 MPH	20 MPH	10 MPH	20 MPH

40 0 40 80
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE & STORAGE FACILITY
YARD LEAD TRACK PLAN
SHEET 3


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-052	

PLOTTED: 09/20/17 10:31PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017_0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\MAF-K-2003.DWG [C-052] 09/20/17 8:24PM

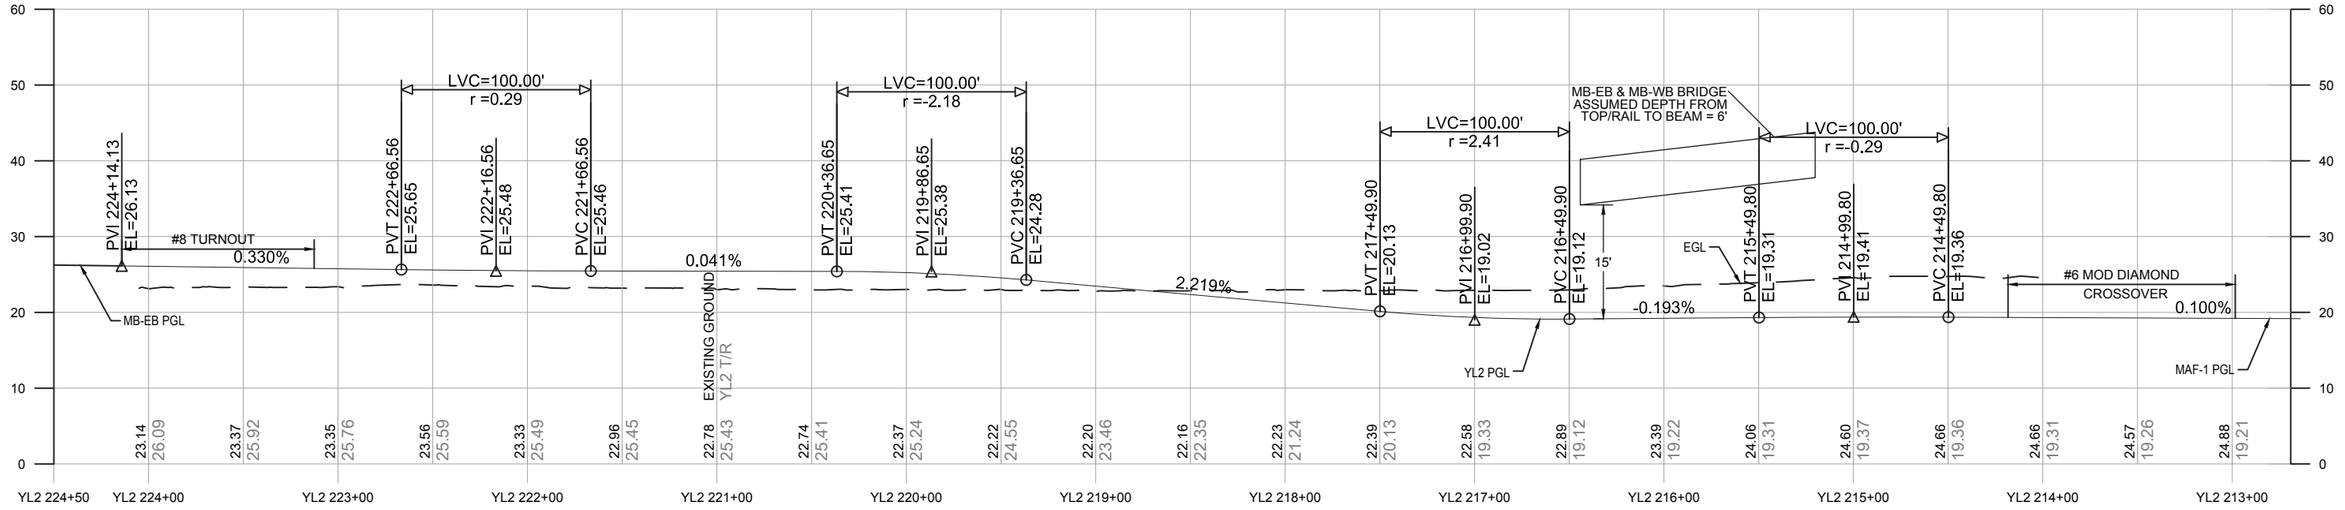

YARD LEAD 2
PROFILE

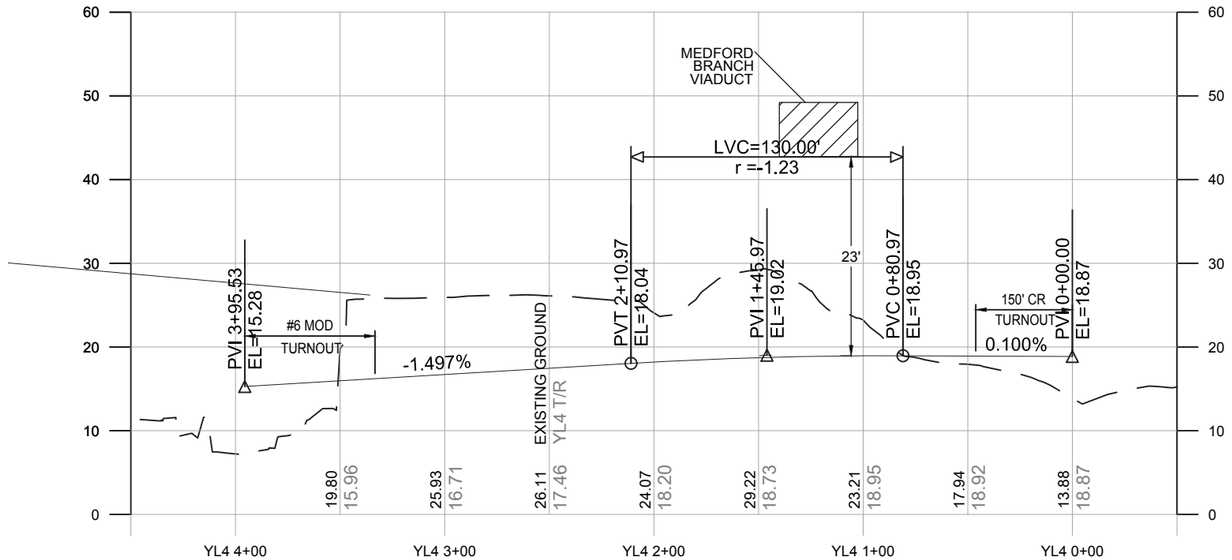

YARD LEAD 4
PROFILE

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


VEHICLE MAINTENANCE & STORAGE FACILITY
MAF TRACK PROFILE
SHEET 1

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-276

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-053	

PLOTTED: 09/20/17 10:31PM BY:BRYANTPJ
DRAWING: E:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_GX_TRACK_RAIL\MAF-XX-3001.DWG [C-053] 09/20/17 8:29PM

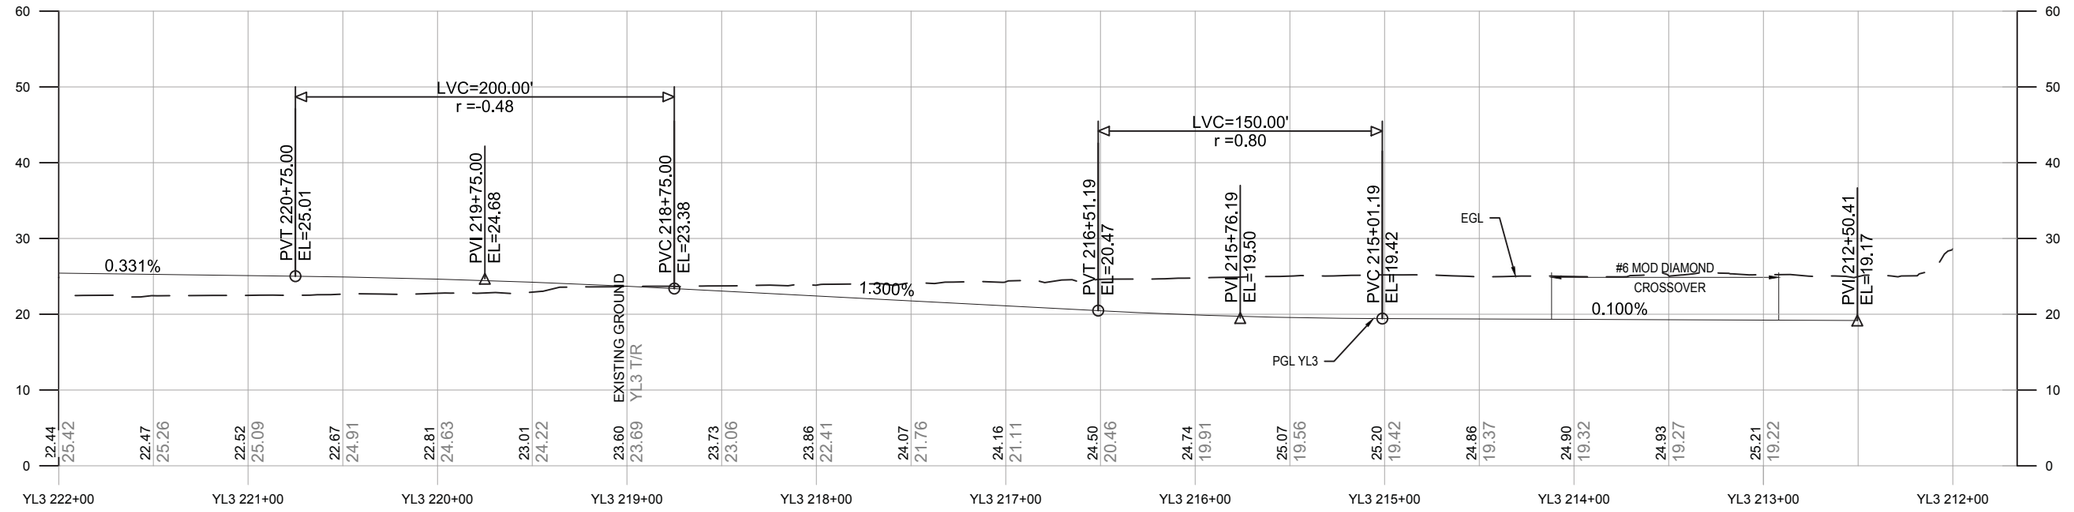

YARD LEAD 3
PROFILE

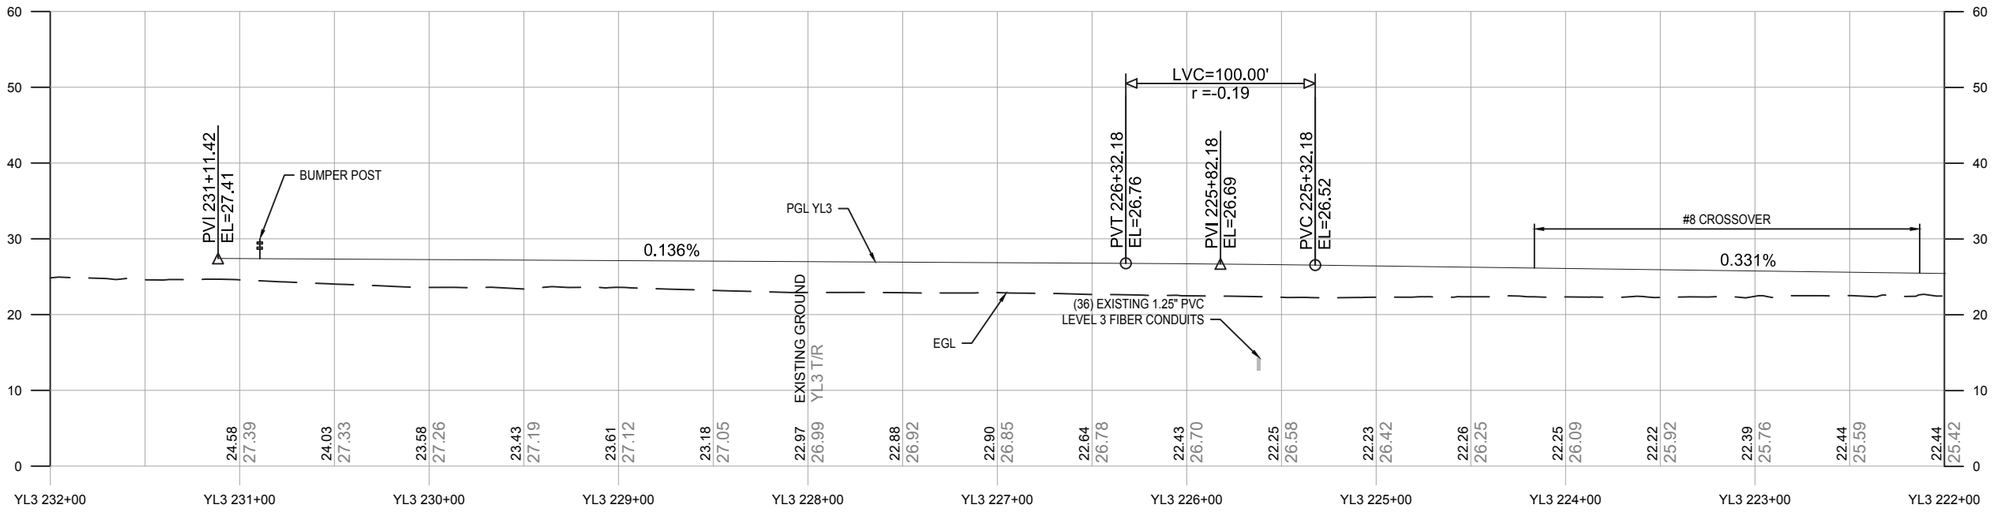

YARD LEAD 3
PROFILE

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE & STORAGE FACILITY
MAF TRACK PROFILE
SHEET 2


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-054	

PLOTTED: 09/20/17 10:31PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\00_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\MAF-H-3002.DWG [C-054] 09/20/17 8:29PM

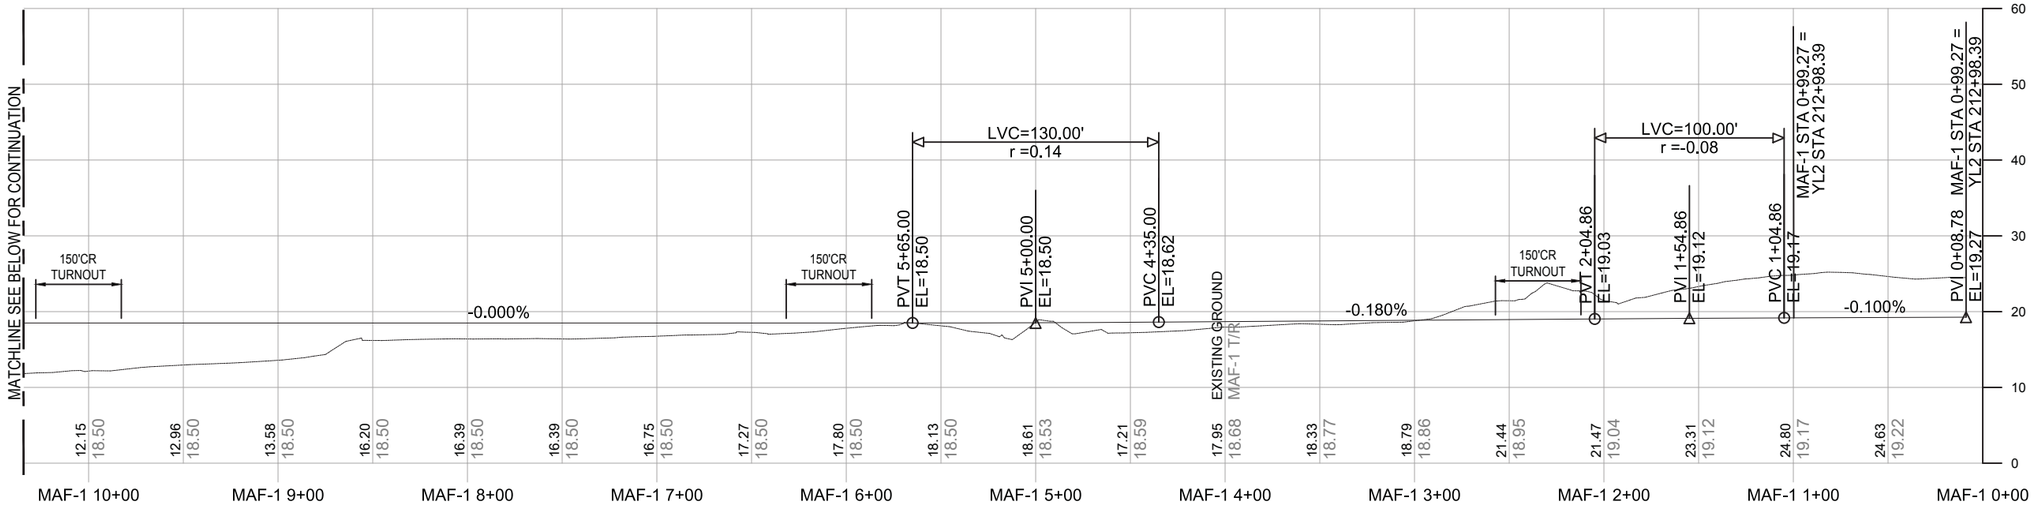

YARD TRACKS - MAF-1
PROFILE

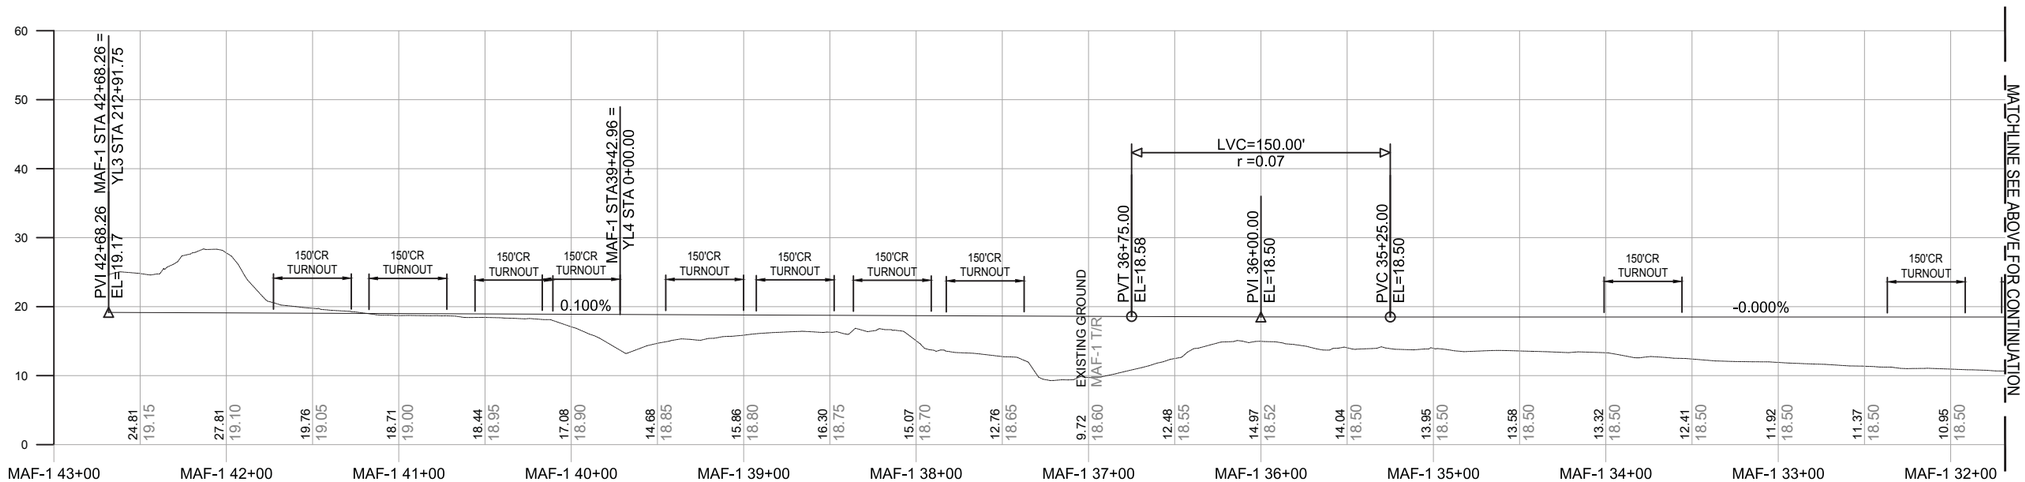

YARD TRACKS - MAF-1
PROFILE

HORIZONTAL
40 0 40 80
10 0 10 20
VERTICAL
SCALE IN FEET

NOTES:
1. ELEVATION OF MAF-1 FROM BREAKLINE MAF-1 10+00 TO BREAKLINE MAF-1 32+00 IS TO STAY AT 18.50FT AT GRADE 0.00%.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE & STORAGE FACILITY
MAF-1 TRACK PROFILE
SHEET 3


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-276


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	KLN	PJB	JEB	SHEET: C-055	

4-201

PLOTTED: 09/20/17 10:31PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\MAF-K-3003.DWG [C-055] 09/20/17 8:25PM

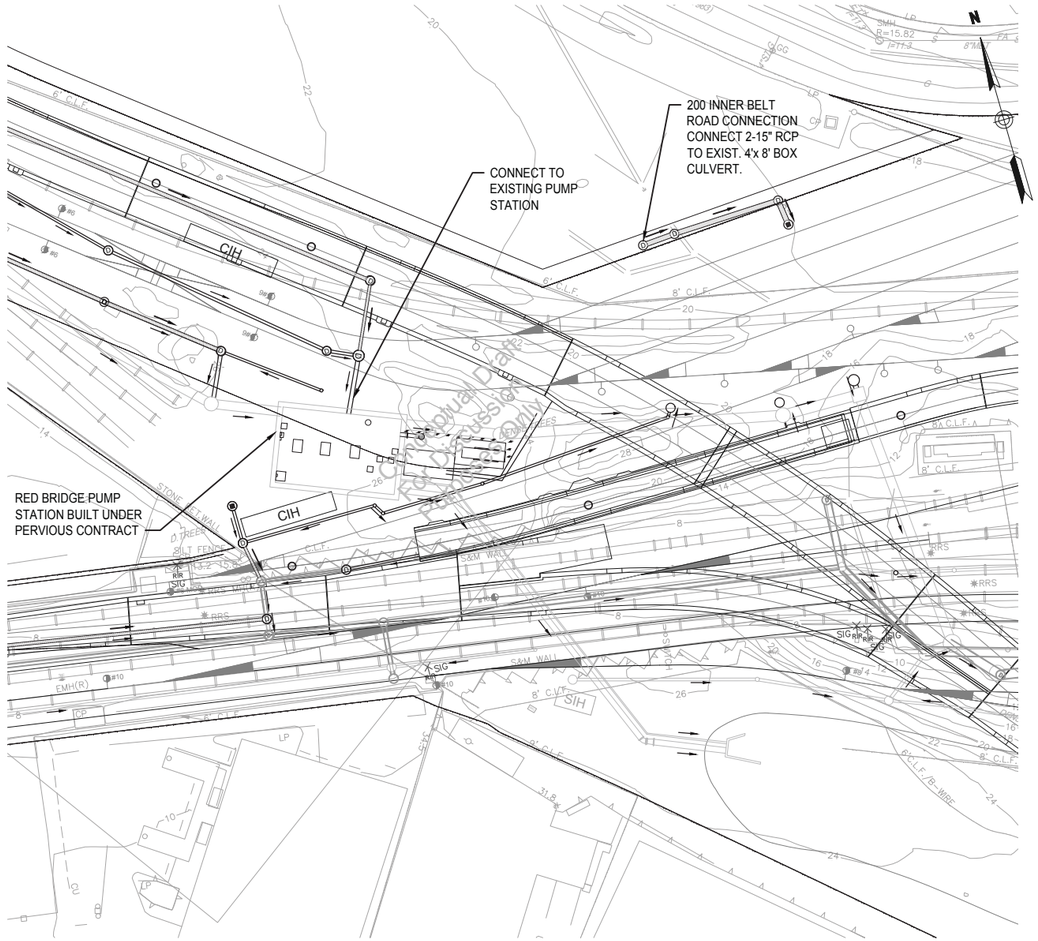

PLAN

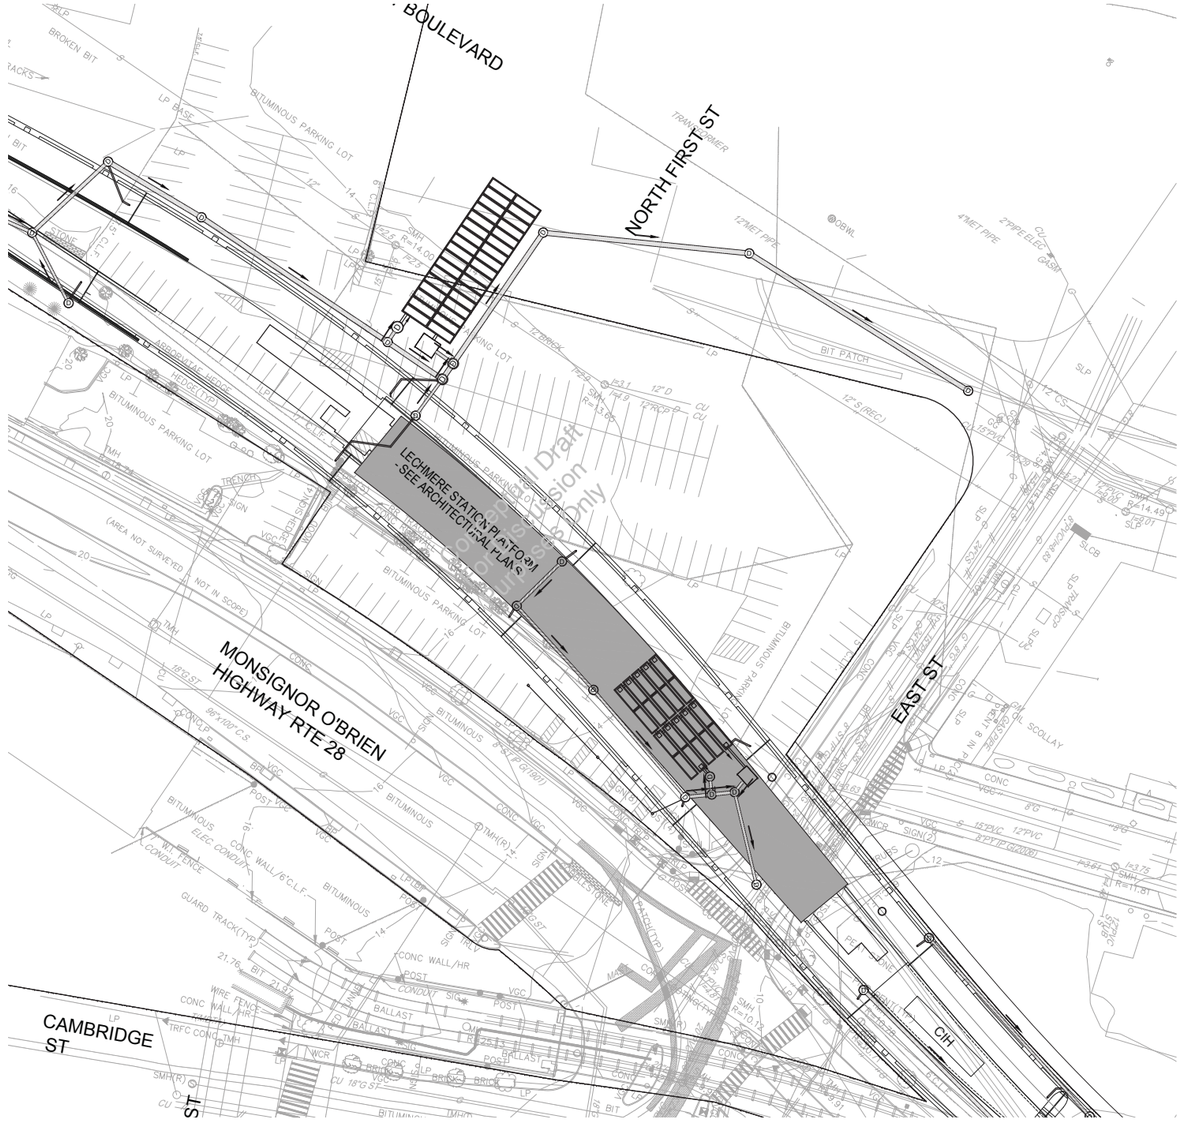

PLAN

40 0 40 80
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

STORM SEWER SYSTEM CORRIDOR PLAN


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-056	

PLOTTED: 09/21/17 2:52PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\000-STRM-001.DWG [C-056] 09/21/17 2:17PM

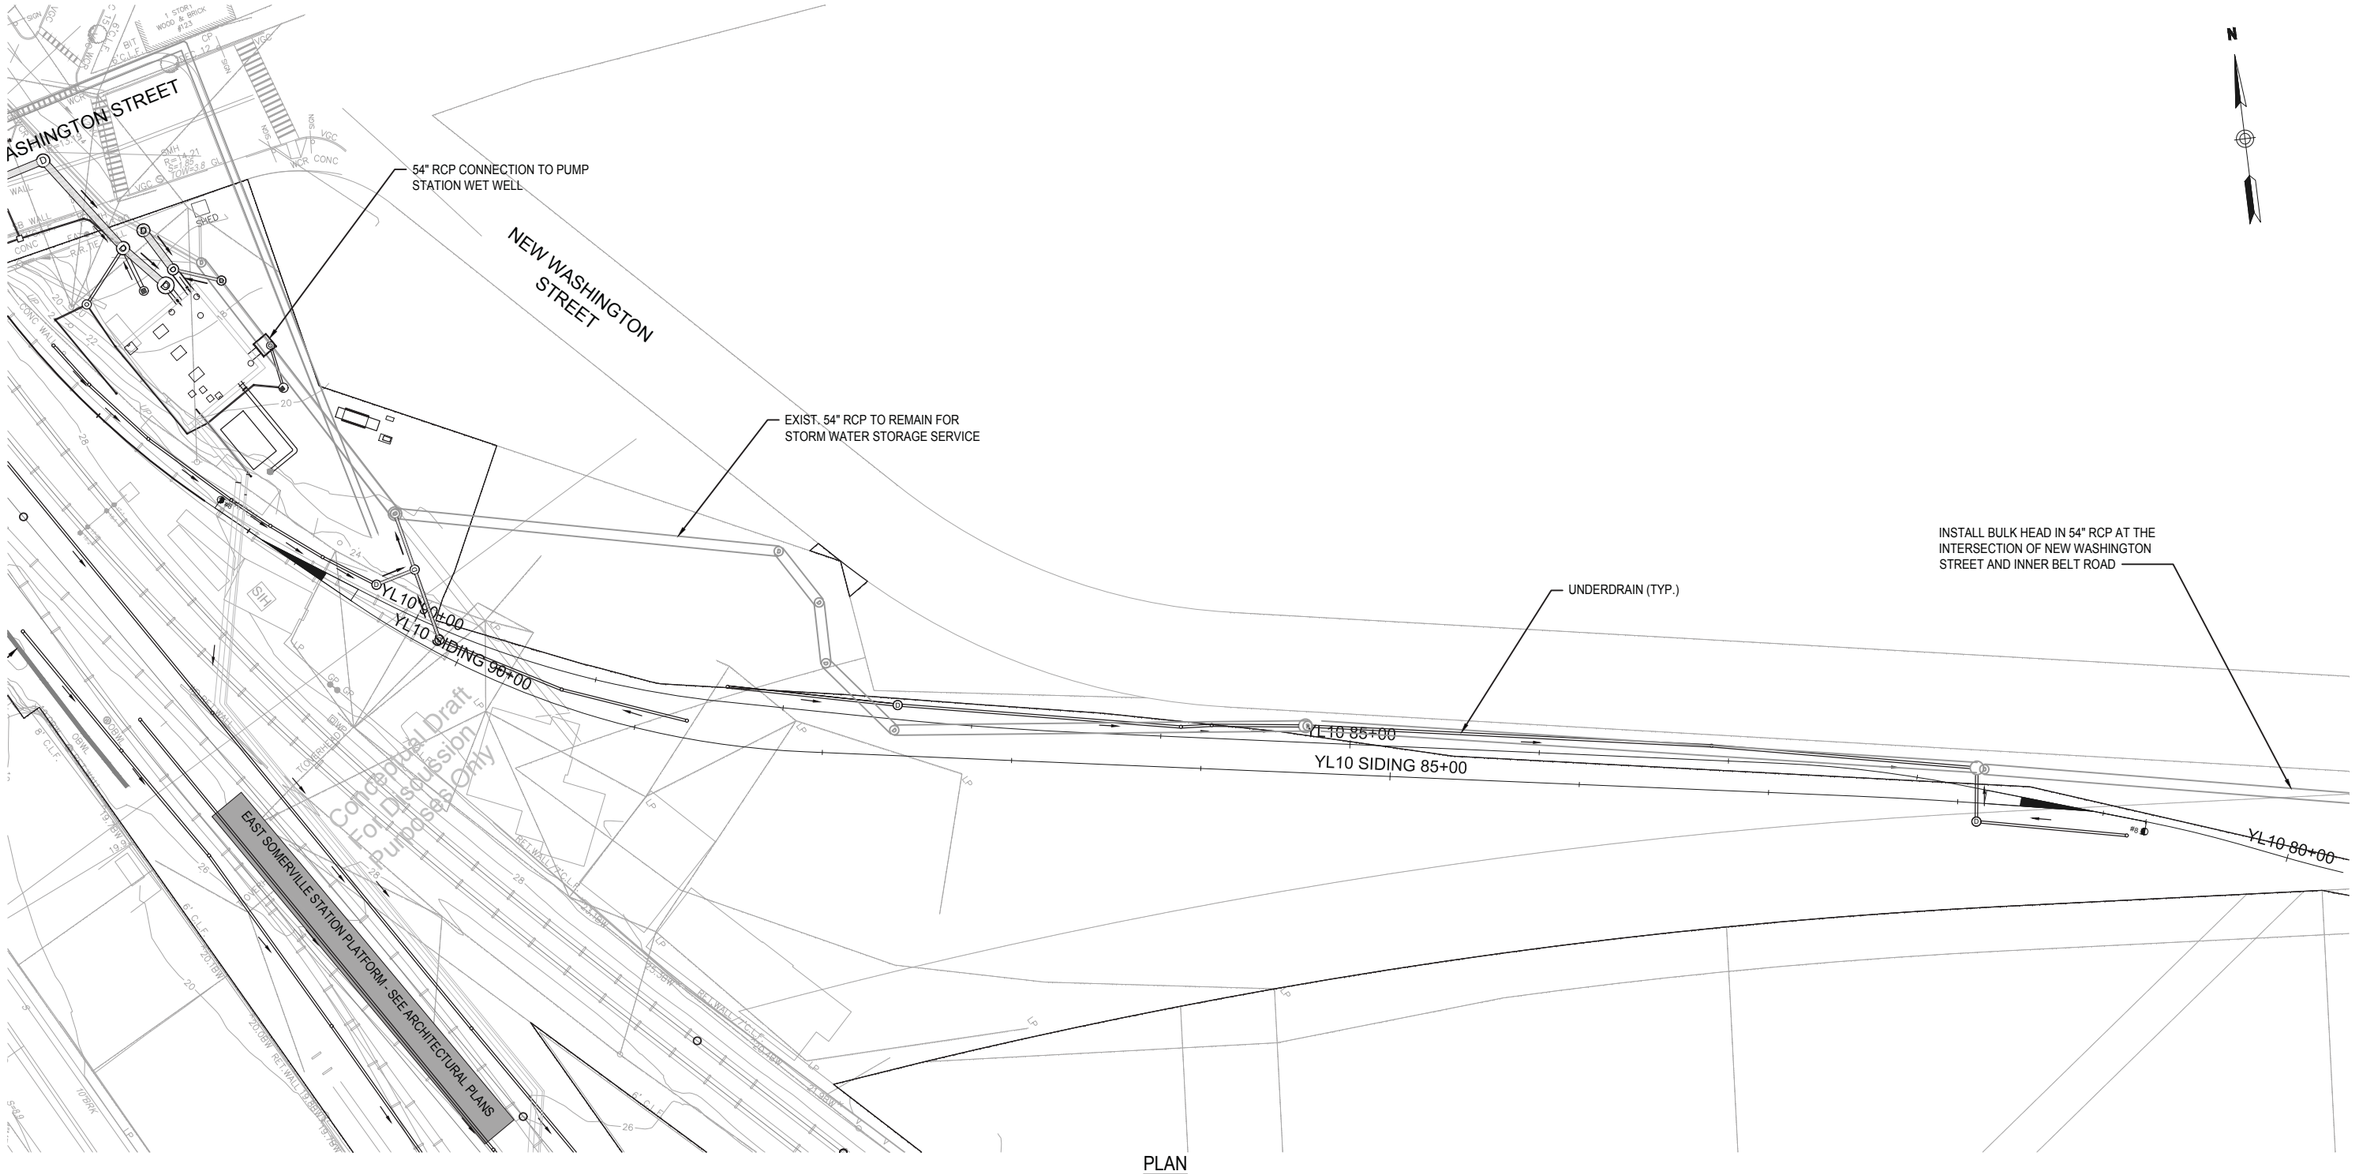

PLAN

40 0 40 80
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

STORM SEWER SYSTEM
CORRIDOR PLAN
YARD LEAD 10

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-276

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	CRR	PJB	JEB	SHEET: C-057	

PLOTTED: 09/21/17 2:12PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_OK_TRACK_RAIL\000-STRM-001.DWG [C-057] 09/20/17 8:27PM

4.7 DRAINAGE AND STORMWATER MANAGEMENT

Integrating rail construction with the MBTA's existing drainage facilities through the Project will require considerable effort to maintain the existing, positive drainage and improve potential flood areas as necessary. GLX Constructors' design solution will continue the MBTA's efforts to mitigate flood issues via intentional pump station design, larger drainage lines, and overall improved drainage systems. Our intent is to support the MBTA's sustainability goals, reduce the need for costly excavation, and address the long-standing flood issues that have burdened the alignment and the surrounding areas in the past.

"Water quality and quantity are two important aspects of the Green Line Extension DB Project. There is a substantial history of flooding in locations within and adjacent to the limits of work, resulting in disruption of commuter rail services. Effective stormwater management is critical to the Project to prevent flooding and to meet the water quality criteria of the regulatory authority.

An extensive network of drainage systems exists within the Project corridor. These systems are owned and operated by several entities, including the various municipalities, MassDOT, Massachusetts Water Resources Authority (MWRA), and Boston Water and Sewer Commission (BWSC). Project improvements will need to connect to these boundary conditions and identify acceptable discharge locations. Considering the various site constraints is the key to success.

The corridor drainage and, where possible, stormwater from adjacent offsite areas will be directed into the track's underdrain system and redirected. Larger carrier pipes will carry overflow downstream to an outfall location. GLX Constructors will design around community path and convey flows to the collection system. Constructing each of the seven stations includes platforms and associated structures that will potentially impact the existing drainage conditions. We will evaluate these impacts to determine if detention is needed to meet regulatory agency requirements.

4.7.A APPROACH TO ENSURING THE DESIGN CONFORMS TO STORMWATER MANAGEMENT REQUIREMENTS

Our work will be in strict compliance with Technical Provisions, including Massachusetts Department of Environmental Protection's (MassDEP) stormwater management standards and other applicable standards for a redevelopment project. Measures to control water quality, flow rates, and volumes will be implemented. Specific requirements established by the United States Environmental Protection Agency (USEPA) for Total Maximum Daily Load (TMDL) for phosphorus discharging to the Charles River will be considered for the design of discharge to North Point Development, as established by the City of Cambridge.

We will provide temporary stormwater management systems as necessary, during construction of the Project. We will relocate or abandon existing utilities in conflict with storm management systems. Where existing trunk lines are used, the pipes will be relined or rehabilitated to prevent contaminated groundwater from entering into the conveyance system.

Approach to Stormwater Management Plans

Our Stormwater Management Plans will include best management practices (BMPs) to address water quality and groundwater recharge. This includes hydrodynamic separators for Total Suspended Solids (TSS) and oil removal, infiltration trenches, and detention systems to capture the first inch of runoff from large roof areas to address water quality and groundwater recharge. See Figure 4.7-1.

The USEPA has established a TMDL for phosphorus discharging into Charles River. We will accomplish the TMDL by treating the first half-inch of runoff from impervious areas for phosphorus. According to the *Final Nutrient TMDL Development for the Lower Charles River Basin, Massachusetts* treating the first half-inch of runoff by infiltration will eliminate approximately 65 percent of phosphorus, meeting TMDL requirements.

Areas located within the viaduct dripline, above grade viaduct drainage and building roof, are considered clean, and no treatment is required for phosphorus removal in these areas. To meet requirements, we will use infiltration trenches or filter units to treat the remaining impervious areas before discharging to the Divco Development drainage system.

Detentions systems will be sized to store and control runoff rates to meet allowable peak development rates and volumes due to the increase in impervious area per cities of Medford, Somerville, and Cambridge requirements at outfalls. Because of the increase in impervious areas in these cities, design requirements for the increase in flow at the outfalls have to be met.

GLX Constructors will manage contaminated groundwater resulting from dewatering operations associated with stormwater pipe installation. We will provide a stormwater management plan that prevents contaminated materials from entering existing and proposed drainage systems.

Design Standards and Criteria for Drainage Elements

GLX Constructors will coordinate with pertinent authorities to make certain that all official requirements and permits are cleared in advance. We will also fully evaluate all requirements to ensure compliance with existing permits, regulatory requirements, and agency guidelines.

Quantity. Stormwater quantity control criteria protects downstream properties due to upstream development. The municipalities have defined the



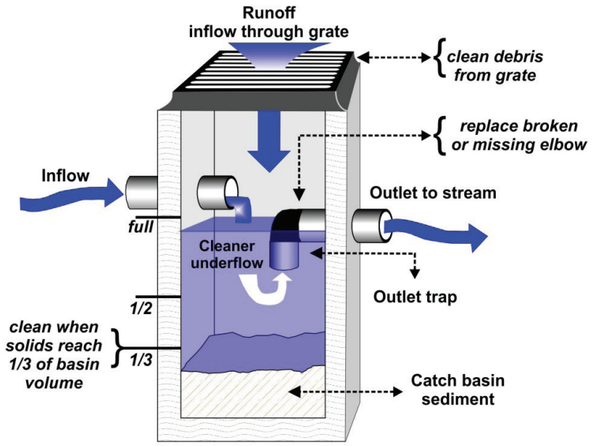


Figure 4.7-1. Hydrodynamic Separator. *The separators will be used for Total Suspended Solids (TSS) and oil removal in order to address water quality and groundwater recharge.*



GLX Constructors' Lead Designer, STV, has completed stormwater control projects across the country, including projects for the MBTA such as the Bound Brook Flood Plain Analysis, which verified that an MBTA-proposed bridge structure in Scituate, Massachusetts, would not negatively affect flooding in the area.

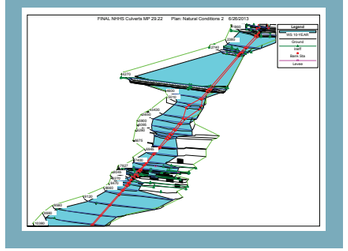

outfall peak flow rate and volume control criteria to make certain pre-development flow targets are met. Typically, criteria is met by providing detention prior to outfall. The hydrograph in Figure 4.7-2 illustrates the process by which we have reduced water runoff by incorporating detention into our design.

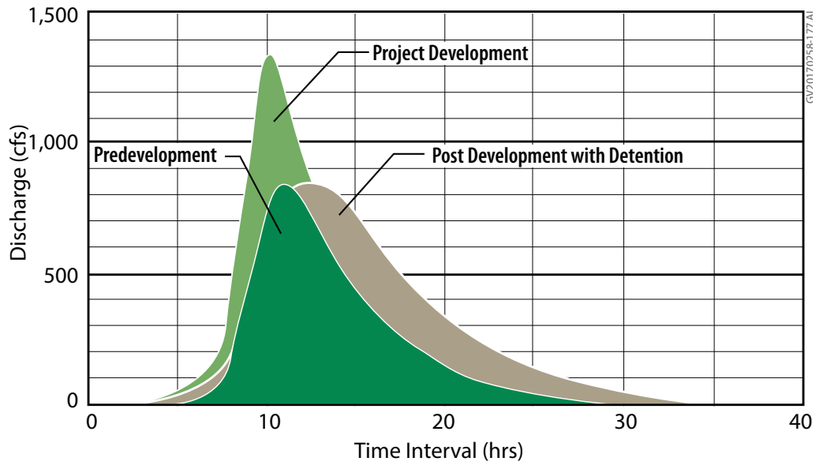


Figure 4.7-2. Project-Wide Stormwater Runoff Hydrograph. *By developing and implementing detentions, we will reduce stormwater discharge, reducing the potential for flooding along the alignment.*

Quality. Stormwater quality control protects bodies of water from potential water quality degradation that may result from development and urbanization. MassDEP Stormwater Management Standards regulate water quality treatment levels and remove a percentage of TSS from runoff before it discharges to a receiving body of water. The stormwater management criterion stipulates that 80 percent of the average annual post-construction load of TSS will be removed. We will achieve this by using structural and non-structural BMPs.

TMDL requirements for the lower Charles River watershed stipulate stormwater management systems be designed to reduce the stormwater phosphorous baseline load by at least 65 percent. For determining the size of infiltration trenches, above-grade viaducts and building roofs are excluded from the calculation of impervious areas. For typical commercial and high-density residential areas, storing approximately a half inch of runoff from the impervious portions of the areas would capture the required amount.

Erosion Control. We will implement erosion control measures during construction to avoid water quality deterioration. Such measures include silt sacks and sedimentation control devices, such as silt bags for catch basins.

Water Balance. Balancing the infiltration, runoff, and evapotranspiration that exists in natural settings, coupled with the imbalance that results from introducing impervious surfaces during urbanization, are key factors in protecting groundwater and resource areas. Managing the water balance will require incorporating infrastructure that matches the pre-development proportions of infiltration and runoff. We will propose low-impact developments, such as infiltration trenches, to achieve the goal to enhance water quality.

Storm Runoff Management

Water resources computer models are an important tool in evaluating the difference in pre-development and post-development conditions, both uncontrolled and with stormwater management controls in place. The primary hydrology and hydraulic components of the model will use USEPA's Stormwater Management Model (SWMM) to generate the runoff and route the flow through collection systems. This approach builds upon the previous modeling conducted for the Project and further develops the model using software PCSWMM 2D, an advanced graphic interface of the USEPA SWMM. We will use PCSWMM to analyze the hydraulic grade line (HGL) with respect to top of tie at any location during the peak flow from a 50-year rainfall, reported in a Stormwater Report. See Figure 4.7-3 for a demonstration of a typical graphical representation of the data.

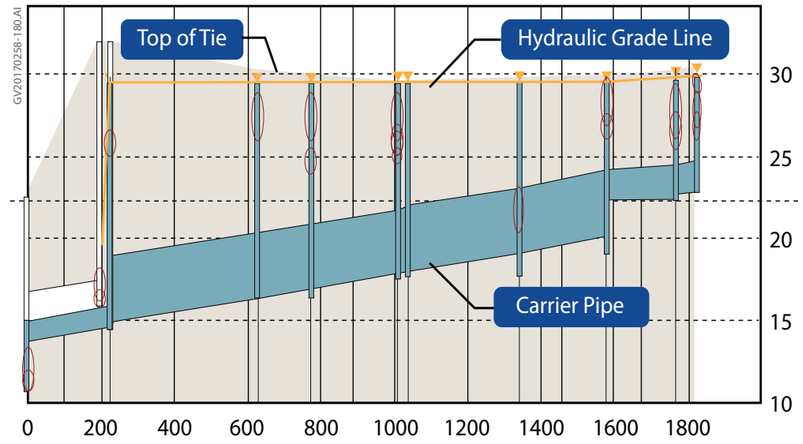


Figure 4.7-3. Hydraulic Grade Line Profile. *The 50-year stormwater hydraulic grade line does not exceed the top of tie elevation.*

We will incorporate accepted temporary stormwater detention practices during construction. We will comply with all federal, state, and local permit requirements during construction, with heightened attention focused on the City of Cambridge requirements for the Cambridge Department of Public Works, and cities of Somerville and Medford Stormwater Management Policy/Program.

Description of Key Drainage Issues

We will consider the drainage issues in the five separate areas and sub-areas within the corridor. Figure 4.7-4 defines the sub-watershed areas and lists their specific characteristics.

These areas will be analyzed for the design criteria in the Technical Provisions.

Millers River Drainage area is partially constructed and will be incorporated into the design of the rest of the system. The remaining work includes:

- Installing pumps
- Activating the pump at the Washington Street pump station (WSPS)
- Activating the pump at the Red Bridge pump station (RBPS)

College Avenue Area (North of Harvard Street to Winthrop Street)	Ball Square –Gilman Square Station – Washington Street Area (North of Washington Street to Harvard Street)	Union Square Branch Area (West of Medford Street to Prospect Street)	Lechmere/North Point Development Area (North of Edwin H. Land Boulevard to Red Bridge area.)	Millers River Drainage Area (South of Washington Street to Miller's River Outfall)
Watershed Area: ~45 Acres	**Watershed Area:** ~206 Acres	**Watershed Area:** ~18 Acres	**Watershed Area:** ~5 Acres	**Watershed Area:** ~40 Acres
Outfall: Winthrop Street Tufts University Athletic Fields, Two Penny Brook Culvert	**Outfall:** Granville Avenue (Ball Square). Medford Street (Gilman Square Station) & Washington Street	**Outfall:** Charlestown Street	**Outfall:** North Point Street (Lot Q), East Street (Lot R), Millers River & Lechmere Canal Outfall (viaduct)	**Outfall:** Millers River Outfall
Jurisdiction: City of Medford	**Jurisdiction:** City of Medford (Ball Square) & City of Somerville (Gilman & Washington Street Area)	**Jurisdiction:** City of Somerville	**Jurisdiction:** City of Cambridge	**Jurisdiction:** City of Somerville & City of Cambridge

Figure 4.7-4. Watershed Characteristics. *Each of these five watershed areas have drainage issues that GLX Constructors will consider in our design.*

Work will be completed to convey stormwater flows from Washington Street area to Red Bridge area.

The Washington Street roadway underpass is prone to chronic flooding. WSPS will convey flows from the Washington Street area to the Red Bridge area. We will provide a high-water control signal from a sensor at the outlet control structure of the WSPS, which will transmit to the RBPS control panel to control high flows to the detention basin. The Washington Street underpass' low area will be designed so the maximum 100-year flood elevation does not exceed 12 inches above the roadway surface at the low point along the gutter. We will design and construct a temporary drainage system to address flooding problems during reconstruction.

Some of the existing New Hampshire Mainline drainage, extending both north and south of Washington Street on east side of the track, may need to be relocated because of the proposed retaining wall location, but certain portions can be reused. When existing pipes are reused, they will be rehabilitated using lining methods or others identified by a Licensed Site Professional (LSP).

We will adhere to recommendations from the LSP to prevent contaminated groundwater, soils, and vapors from entering the drainage system. The minimum extent of rehabilitation will be as specified in the Technical Provisions. We will operate and maintain a temporary treatment facility that will treat contaminated water from dewatering pipe trenches, excavated during the Washington Street construction, affected by the contaminated site at 50 Tufts Street.

The 66-inch drain was relocated from the east side of the corridor to under the west-bound track. This supports a better construction sequence, allowing the maintenance of New Hampshire mainline tracks to remain active at all times.

Red Bridge Area is prone to chronic flooding. The low point is the Fitchburg Mainline tracks, between the RBPS and an offline detention basin. Directing peak flows to the detention basin at RBPS, which is already in place, alleviates flooding. We will complete the design and construction of RBPS so the 48" Fitchburg Main Drain (FMD) HGL does not cause surface flooding within the track.

The proposed VMF site is located in an area prone to flooding. Currently, the site contains extensive impervious surface treatments. In response, our design raises the VMF by approximately five feet and the impervious areas will be reduced, thereby eliminating flooding issues onsite and creating more area for stormwater management. These flooding concerns will be coordinated with the project-wide model. The drainage in the VMF is routed to two existing discharge points. The southern section discharges to RBPS, and the northern section discharges into an existing system along the tracks near the west edge of the commuter rail facility. As part of our VMF design, we will provide detention systems for the VMF so the proposed stormwater runoff volume and rate does not increase the existing runoff and rate for all design storms. We will further evaluate water quality improvements, including deep sump catch basins, oil water separators, grit removal, and detentions systems, during final design development after consulting with the MBTA and the City of Somerville. Figure 4.7-5 shows the type of deep sump catch basin used to catch surface water drainage or runoffs.

The drainage from 200 Innerbelt Road, in the Millers River area, is adjacent to the MBTA's ROW and tied into the MBTA's drainage system. We will evaluate the capacity of the MBTA's system to handle stormwater flows from this offsite property and test for water quality and potential contamination. We will obtain the necessary license agreements to make certain currently-existing discharge is accepted by the MBTA.

There is an existing 54-inch drain that diverges away from the track corridor along New Washington Street. This pipe will act as a supplemental wet well storage in the final design. To prevent contributing stormwater flows from the MBTA's property, to divert flows away from Old Stone Culvert and thereby prevent flooding, a bulkhead will be located at a point between the WSPS and the intersection of New Washington Street and Inner Belt Road.

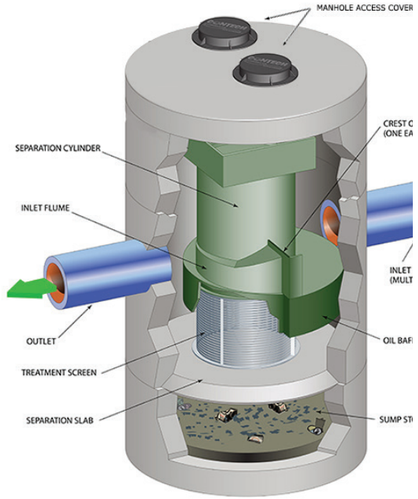


Figure. 4.7-5. Deep Sump Catch Basin. *The basins that catch surface water drainage or runoff will be used to evaluate water quality improvements.*

Description of Drainage System and Appurtenances Involved

The primary collection system in the track area is the underdrain system, and the key component within this system is the ballast storage. The ballast infiltrates the flows collected in the track bed. The perforated pipe in the ballast collects excess flows in the track, and conveys the flows to carrier pipes or trunk lines, and ultimately to the approved municipal outlets.

Detention and infiltration systems store peak runoff and prevent any increase in peak flows to municipal stormwater drainage systems, improving water quality prior to discharge at outfall locations. Hydrodynamic separators will be installed to treat pavement runoff. Low impact development (LID) practices, such as rain gardens and bio retention areas, will be implemented, where feasible to maintain natural hydrology and treat impervious areas. Infiltration facilities and LIDs are typically designed to manage more frequent and lower magnitude rainfall events.

The trunk lines dually act as carrier pipes and storage conduits to attenuate peak flows. We will also attenuate peak flows by using outlet control structures such as weirs and orifices. All outfall locations will be analyzed for the pre- and post-development peak flows, and they will be controlled to meet the requirement of the authority having jurisdiction. Figure 4.7-6 shows a comparison of the outfall node at Medford Street. This will be further revised to capture design changes and decreases in impervious areas.

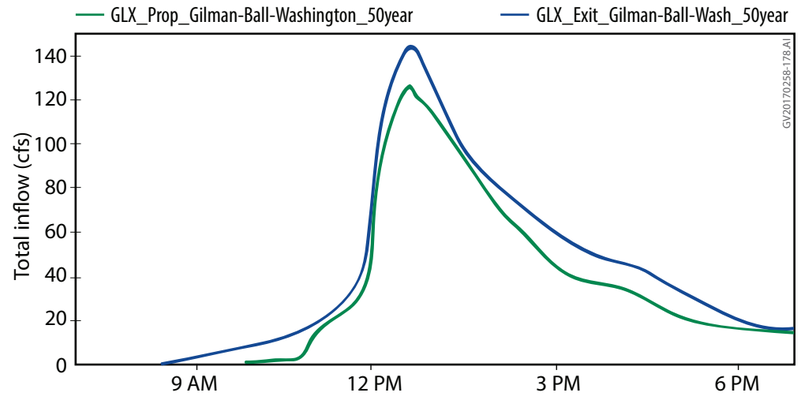


Figure 4.7-6. Outfall at Medford Street. *Outfall nodes will be designed such that existing inflow is less than the proposed conditions*

Within the Ball Square system, a storage conduit is proposed that empties into the existing system at Granville Avenue. Alternative approaches may be considered where the difference in grades requires uplift of the stormwater to a downstream conveyance system at higher elevation.

GLX Constructors proposes enhancing the existing ROW drainage for adequate rainwater runoff and flooding prevention. Specific improvements are proposed for track drainage, new stations, and the community path. We will comply with all stormwater standards, and we will optimize where possible.

We will coordinate with municipalities to demonstrate that the proposed drainage improvements meet the design criteria established for the Project. Any variations will be thoroughly discussed and documented during weekly TWG meetings, included in the Design Submittal, and submitted to the MBTA for acceptance prior to final design development.

ITP Request	RFP		
	Drawing Number	Drawing Title	Reference Section or Drawing
A5.2.7.B			4.6 (C-003 to C-024; C-026 to C-031; C-033 to C049; C-056 to C-057) For a description of Major and Minor Overland Flows see the narrative of Section 4.7.

Technical Solutions Drawing Matrix.

4.8 ENVIRONMENTAL MANAGEMENT STRATEGY

Employing sustainable design and construction best practices, GLX Constructors has completed extensive due diligence and has identified potential environmental issues and corresponding mitigations to prevent schedule creep, unforeseen costs, and further environmental issues, such as noise pollution, hazardous materials, and unwanted dust residues. Environmental awareness and sensitivity is key to helping the MBTA achieve its overall sustainability goals, and GLX Constructors' solution will reduce costs and extinguish the MBTA's exposure to long-term liability associated with environmental neglect.

GLX Constructors is committed to conserving the Boston area's natural and cultural resources by making certain the Green Line Extension DB Project is designed, constructed, commissioned, and operated in full compliance with applicable environmental and permitting requirements. Our goal is zero environmental violations. To obtain our goal, we will employ a detailed Environmental Management Strategy that identifies the potential environmental impacts, develops best management practices (BMPs) for each impact, and assigns responsibility and timetables for the management and control of impacts, particularly handling stormwater, process waters, and contaminated materials.

4.8.A ROLES, RESPONSIBILITIES, AUTHORITY, AND REPORTING STRUCTURE WITHIN THE ENVIRONMENTAL TEAM

To develop an effective Environmental Management Strategy, we will establish a direct working relationship between our Management Team, Design Team, and Construction Execution Team. As illustrated in Figure 4.8-1, the PE Environmental will be supplemented by two local consultants: TRC Environmental Corporation (TRC) and Tetra Tech, Inc. (Tetra Tech). To communicate thoroughly, GLX Constructors' Environmental Team will have frequent meetings both internally and with our Management Team.

TRC will be responsible for compliance and management of hazardous materials during the Project.

Tetra Tech will lead the stormwater permitting, planning, and compliance efforts.

4.8.B SUMMARY OF ENVIRONMENTAL PROTECTION AND CONTINGENCY PLANS

GLX Constructors will develop a Spill Response Plan to be fully prepared in the event of an accidental oil and/or hazardous materials (OHM) spill, and a Stormwater Pollution Prevention Plan (SWPPP), to identify and protect against conditions that occur during construction. The SWPPP will be developed under the National Pollution Discharge Elimination System (NPDES) program, administered by the Environmental Protection Agency (EPA). It will include BMPs for controlling erosion, treating and discharging stormwater from the site, and preventing pollution.

We have identified the locations and regulatory status under the MCP of all known Release Tracking Numbers (RTNs) within the Project corridor and will coordinate with the MBTA's LSP on the closure of these RTNs.

GLX Constructors will establish an Equipment Maintenance Program, which will be used to prevent OHM spills. This Equipment Maintenance Program will make certain that we are prepared to handle any accidental OHM spills resulting from refueling or normal equipment maintenance such as fluid change, hydraulic hose breaks, etc.

4.8.C APPROACH FOR COMPLIANCE WITH REQUIREMENTS OF THE ENVIRONMENTAL COMMITMENTS AND AGREEMENTS

We will develop a database of all of the key commitments and constraints resulting from the various permits, approvals, and submittals required by regulatory agencies. Upon selection, we will meet with MassDOT Environmental Staff and the Owner's Representative team to review all of the requirements and gain an understanding of the background behind the requirements, the history of discussions with regulatory agencies, and other intangible yet critical information that contributes to various requirements. Based on this collaboration, we will annotate and complete our database which will serve as a basis for evaluating the final design.

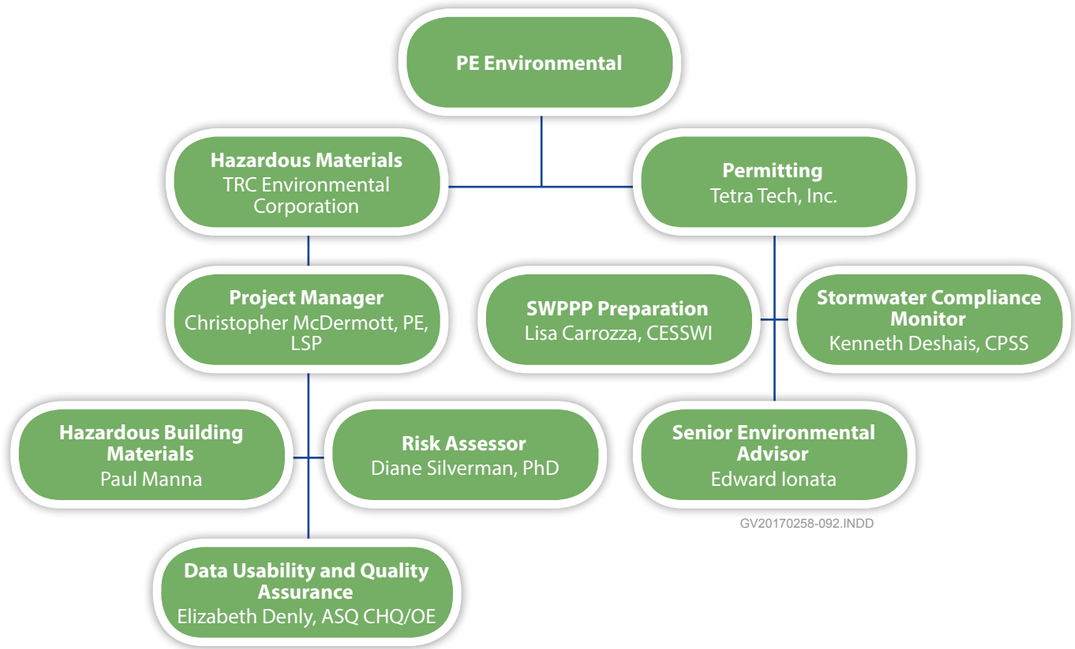


Figure 4.8-1. GLX Constructors' Environmental Team Structure. *We have identified local experts that will be engaged in performing tasks associated with environmental matters.*

GV20170258-120.INDD

“TRC has vast experience working on active railroads and will formulate sampling plans accordingly. For Amtrak, TRC performed a detailed site investigation and collected samples during geotechnical and environmental sub surface investigations. The environmental borings were conducted adjacent to Amtrak’s high speed track while maintaining passenger and freight service throughout the entire process.

GLX Constructors will work directly with construction field crews to maintain BMPs throughout construction.

4.8.D APPROACH TO ENVIRONMENTAL MONITORING, INSPECTION, AND REPORTING

We will prepare and implement soil and groundwater characterization sampling plans and coordinate with approved disposal facilities for properly disposing all excavated material that cannot be reused on-site. GLX Constructors’ team member, TRC, has conducted numerous sampling events in areas with various levels of contamination, and have established relationships and knowledge of local soil transporters and disposal facilities.

We will prepare the soil and groundwater sampling plans in accordance with the MBTA’s rules and regulations. The soil and groundwater characterization sampling plans will utilize the construction schedule and proposed excavation locations to identify sampling points along the corridor that best represent the current conditions in the proposed excavation or dewatering areas.

We will analyze laboratory results from the soil and groundwater characterization sampling events to determine which materials will be suitable for reuse on-site and which disposal facility can best accept non-usable excavated material. In the event that contamination is discovered above regulatory standards, our LSP will comply with all laws under the MCP and implement all necessary reporting.



Field engineers overseeing subcontractors drilling environmental borings and taking soil samples along a railroad Right of Way.

After soil and groundwater sampling plans have been implemented, we will prepare all necessary permits needed to properly disposal of excess soil and other wastes produced during the Project. We will also advise the Health and Safety Team about proper personal protective equipment for the expected conditions throughout the Project corridor. To ensure our processes remain compliant with MassDEP requirements during construction, our LSP or a qualified GLX Constructors’ representative will be present on-site during all excavations and loading of hazardous materials.

We will also regularly inspect the construction site for compliance with our SWPPP, direct the construction organization on maintaining management practices, and regularly update the SWPPP in relation to ongoing construction means and methods.

4.8.E APPROACH TO THE HANDLING AND MANAGEMENT OF WASTE AND CONTAMINATED MATERIALS

GLX Constructors will analyze soils and groundwater throughout the Project corridor to determine proper management practices.

Our team has already performed hazardous materials due diligence for the Project and has created an online Hazardous Materials Interactive Map, Figure 4.8-2 on the following page, which displays all previously sampled soil and groundwater along and adjacent to the Project corridor. We will continue to use this map to organize collected data and hazardous materials disposal throughout construction. To organize any excess soils into disposal categories, we will tabulate the data collected during the soil and groundwater-sampling events and compare it against regulatory standards and disposal requirements. We will also use the interactive map to identify and track where excavated soils were relocated or disposed of off-site.

To prevent the potential spread of contamination, our LSP will make certain that all equipment and personnel in contact with hazardous materials are properly decontaminated prior to exiting the Project corridor.

4.8.F APPROACH TO EXCAVATED SOIL MANAGEMENT

GLX Constructors will prepare design specifications that will be both cost efficient and environmentally compliant. We have incorporated the proposed excavation areas into the Hazardous Materials Interactive Map to aid in predicting soil conditions in those areas based on previously sampled data. After the soil sampling plan has been implemented, our team will be able to determine which soils can be reused on-site and which must be taken off-site for disposal. We will incorporate suitable excavated material from required cut areas to required fill areas within the Project limits. We will use the results of our sampling as an aid to determine which soils should be reused as backfill.

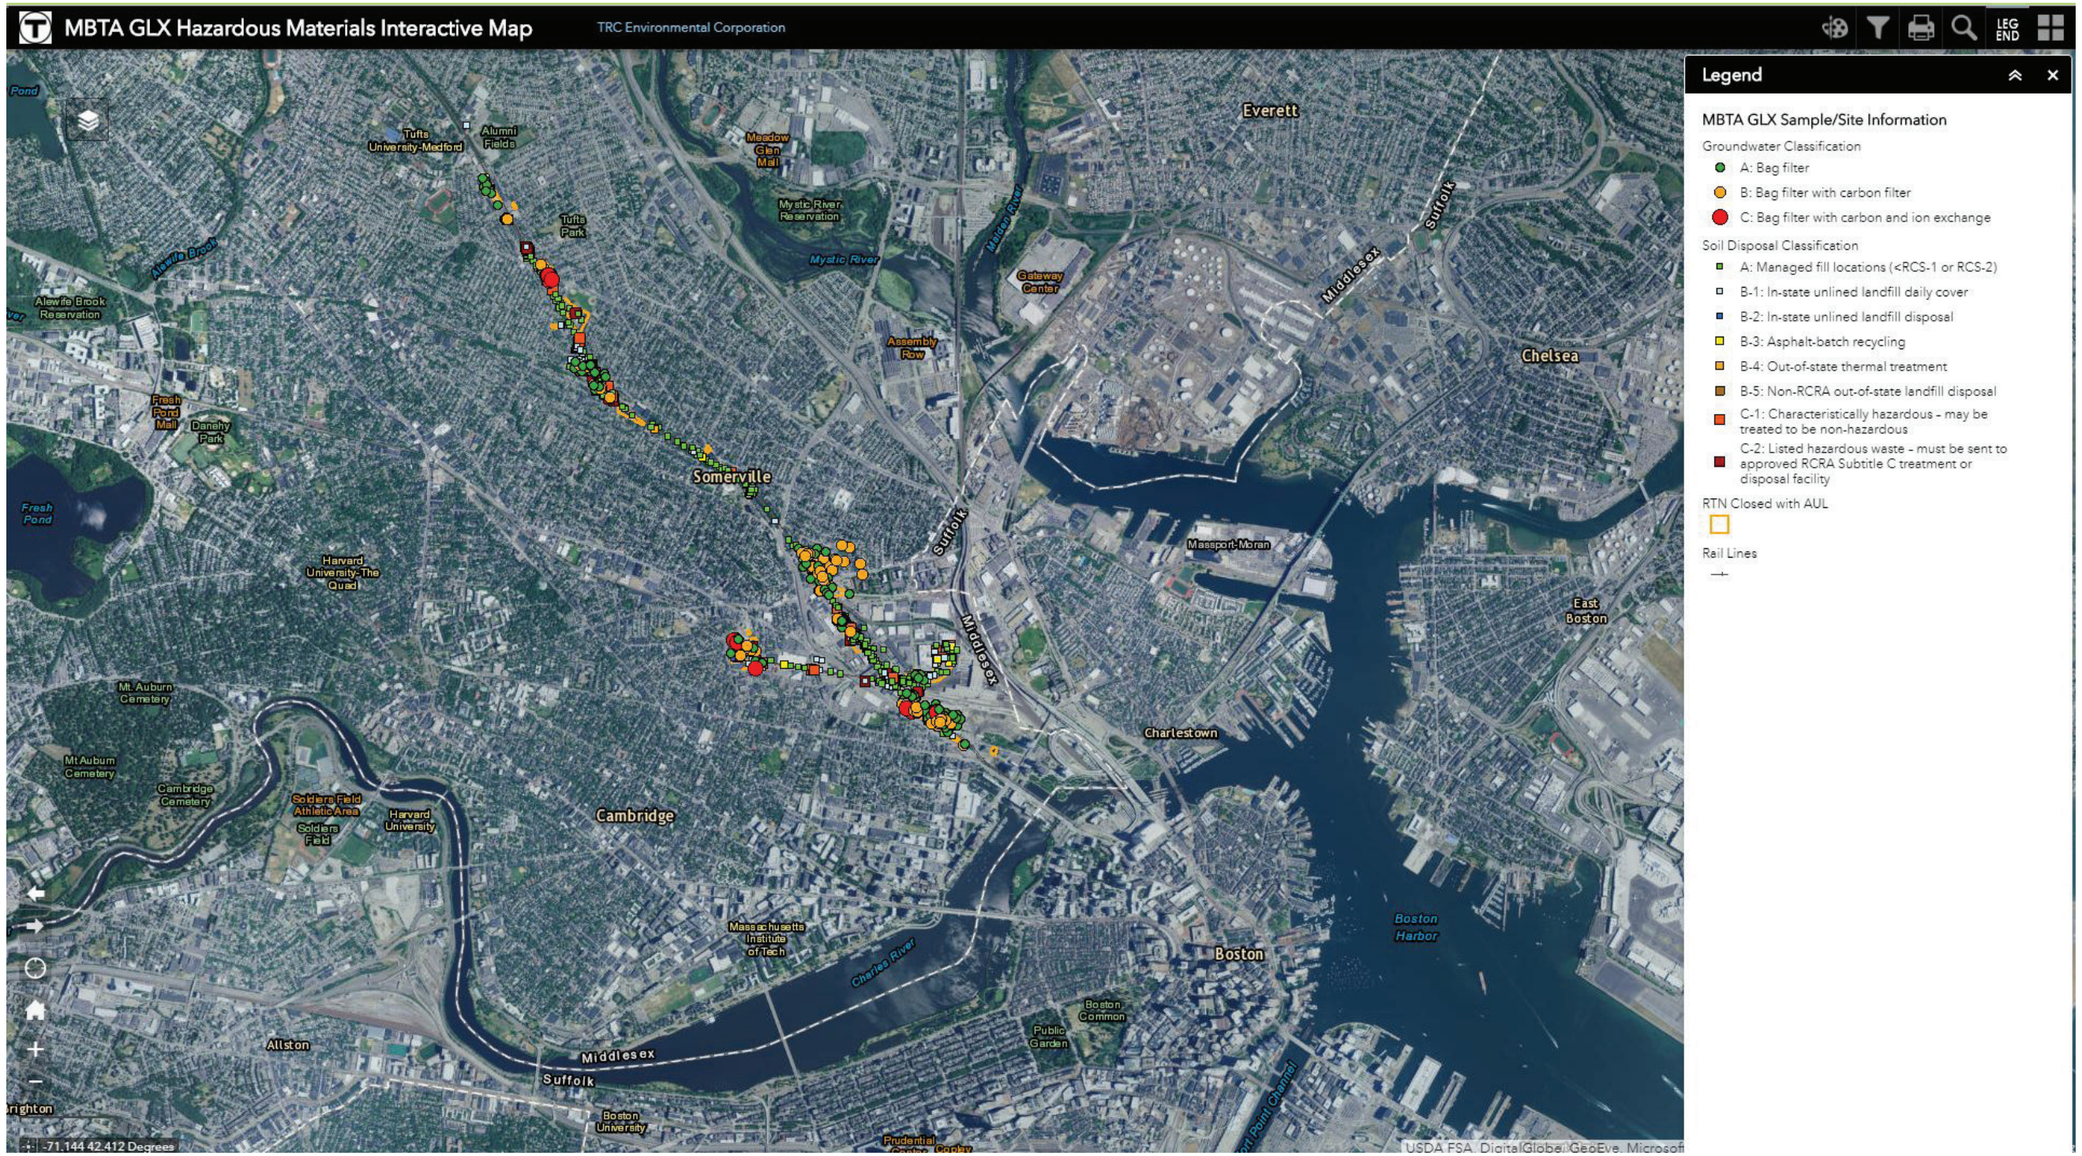


Figure 4.8-2. Hazardous Materials Interactive Map. *GLX Constructors performed extensive hazardous materials due diligence during the proposal phase. As lead of our Environmental TWG, TRC was tasked to identify all recorded soil and groundwater contamination along the entire project corridor. They then developed an interactive web mapping tool of all data points to show probable soil conditions linked to associated disposal categories across the entire Project corridor. This information was then incorporated into our design to maximize use of excavated contaminated material on-site versus off-site; thereby, reducing both costs and risks of unnecessary transport of material for off-site disposal.*

GLX Constructors' team member, TRC, was tasked with assessing and remediating hazardous materials at the WRTA New Vehicle Storage and Maintenance Facility Project, which was constructed over a former manufactured gas plant site in Worcester, Massachusetts. During initial sampling, TRC identified asbestos-containing materials and worked directly with the MassDEP to obtain approval for on-site capping of asbestos wastes, which saved WRTA more than $40,000,000 in potential off-site disposal costs. Our team will endeavor to provide similar cost savings to the Green Line Extension DB Project.

4.8.G APPROACH TO MINIMIZING NOISE AND VIBRATION IMPACTS

If there are locations where we exceed maximum parameters, we will install temporary noise barriers during construction as appropriate, such as excavated materials piles, temporary enclosures, or temporary barriers.

GLX Constructors will prepare and submit a project-specific Noise Control Plan prior to construction activities. To comply with federal and state guidelines and limits, the Noise Control Plan will outline methods to minimize noise and vibration, which will lessen impacts to potentially affected receptors along the alignment. At a minimum, the Noise Control Plan will require:

- Using specially quieted equipment with enclosed engines, high-performance mufflers, or both
- Construction equipment noise certification testing
- Ambient adjusting, or manually adjusted backup alarms set to 5 dBA over background noise levels
- A program for the minimization of truck and equipment idling
- Acoustic shields for jackhammers, chain saws, pavement breakers, and other exceptionally loud equipment
- An approach for responding to community complaints
- A protocol for reporting noise monitoring results, noise reduction initiatives, and responses to the community

Wherever possible, GLX Constructors will select equipment and techniques that generate the least overall noise including:

- Sound insulated compressors, generators, and power-driven equipment to limit excess noise during construction
- Mufflers and silencers where applicable
- Electric equipment in lieu of gasoline-powered equipment where feasible
- Well-maintained equipment, operated at normal manufacturer's operating specifications

We will construct the Project in a manner that minimizes noise and vibration, including but not limited to the following best practices:

- Structure work flow to minimize the need for vehicles to back up
- Turn off idling equipment when not in use
- Avoid revving engines
- Minimize material drop height to the extent possible to avoid excess noise from soil, rock, and debris impacting truck beds
- Provide sound deadening material as liner for all dump trucks, hoppers, and storage bins

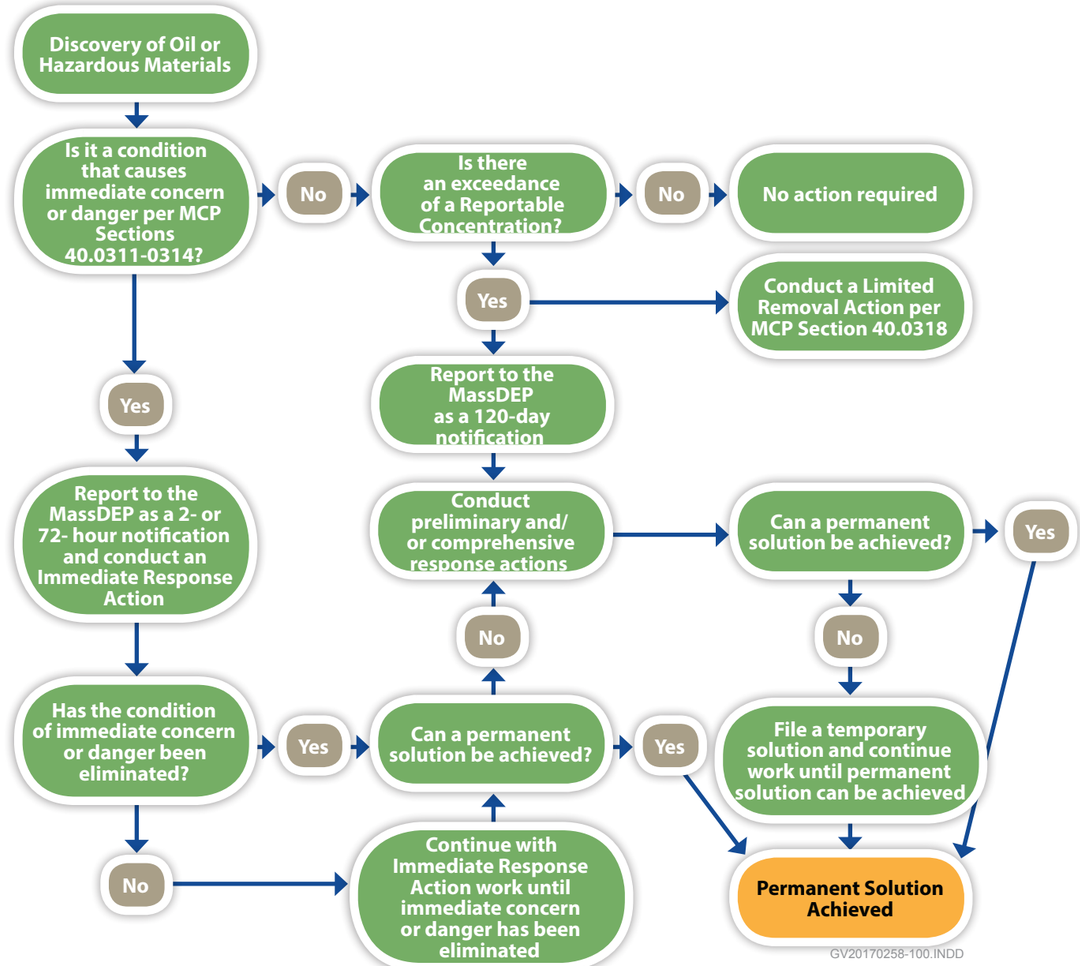


Figure 4.8-3. MassDEP Compliance Flow Chart. *The process that GLX Constructors will undertake to properly comply with MassDEP Plans in the case of oil or hazardous materials discovery.*

- Maximize source-receptor distances wherever possible
- Locate stationary equipment away from noise-sensitive sites

We will conduct equipment noise certification testing to verify noise levels from equipment used on-site and identify loud equipment that may require additional pathway attenuation.

In the event of a complaint regarding noise or vibration, we will submit a Noise and Vibration Complaint Report within seven days to document the equipment or activity used at the time of the complaint, monitoring results and subsequent actions taken to control noise or vibration.

GLX Constructors team member, TRC, has worked on contaminated urban construction projects with close abutting residential properties, including the Kiley Barrel Site. TRC worked closely with the City of Somerville and the abutting residents to ensure the community was involved and not impacted with any airborne contamination throughout the construction process. This relevant experience will be incorporated into our approach on the Green Line Extension DB Project.

4.8.H APPROACH TO MINIMIZING THE GENERATION AND DISPERSION OF AIRBORNE PARTICULATE MATTER AND MITIGATION OF POTENTIAL IMPACTS

GLX Constructors will use perimeter dust monitoring equipment to make certain that dust produced during construction does not leave the project corridor. In contaminated areas, we will perform site and perimeter air sampling to make sure that any dust produced in the contaminated areas does not adversely affect personnel and abutters.

GLX Constructors will evaluate all existing structures to be demolished for asbestos, lead, mercury, PCBs, etc. prior to construction to determine if any additional personal protective equipment will be needed. Our team member, TRC, has experience working with MassDOT on numerous on-call contracts for Industrial Hygiene Services, which have included indoor air quality monitoring as well as asbestos and lead abatement during demolition activities.

4.8.I APPROACH TO TARGETING FOR SALVAGE/RECYCLING

GLX Constructors will develop and implement a Construction and Demolition Waste Management Plan. The plan will include waste identification, anticipated percentage breakdown of materials, and a Waste Reduction Work Plan. Details of our approach include:

Waste Identification. We will indicate anticipated types and quantities/percentages by weight or volume of demolition, site-clearing, and construction waste generated by the work. It is our goal to target end-of-Project rates for salvage/recycling of at least 90 percent by weight of total nonhazardous solid construction and demolition waste and at least 80 percent of all hazardous or contaminated waste material that is able to be recycled. We will practice efficient waste management in using materials and use all reasonable means to divert construction and demolition waste from landfills and incinerators.

Waste Reduction Work Plan. This plan will list each type of waste and whether it will be salvaged, recycled, or disposed of in a landfill or incinerator. The types of waste will include wood, paper and cardboard, concrete, metals, and mixed construction and demolition waste. The plan will include points of waste generation, total quantity of each type of waste, quantity for each means of recovery, and handling and transportation procedures.

Construction and Demolition Waste Management Plan. This plan will provide details of how to separate recyclable waste from other waste materials, trash, and waste. It will also incorporate services of local solid waste handlers to make certain construction waste is separated, handled, and disposed.

Hazardous Waste Management Plan. We will identify how hazardous waste will be recycled or disposed of via proper handling procedures.

Structural steel from the existing Lechmere Viaduct is a Historic Element. GLX Constructors will salvage structural steel sections in accordance with Section 106. In addition, at the Holman's Building, 350 Medford Street, GLX Constructors will salvage the lions' heads per agreement with the City of Somerville.

GLX Constructors will salvage all Lechmere yard, viaduct, and lead track rail; all switch machines and signals; and all fare gates. All salvaged items will be delivered to the MBTA Railroad Operations material yard in Charlestown, Massachusetts, unless otherwise directed by the MBTA. The items to salvage include:

- OCS poles
- Trolley wire splices, 2/0
- Special track work including 4 RH point/mate turnouts
- Switch boxes with power craft switches
- Switches in chamber under the viaduct at Lechmere Station
- Balance weights
- Greaser equipment

We may reuse track materials that meet the requirements of the Contract Documents. We will coordinate with the MBTA to identify material that is salvageable. All material identified by the MBTA as salvageable will be delivered to the MBTA rail shop at 21 Arlington Avenue. All material determined to be non-salvageable by the MBTA, such as railroad ties, track bolts, nuts, washers, spikes, anchors, and lags, will become the property of GLX Constructors, and it will be disposed of off-site.

We will use soil recycling facilities as a means of soil disposal as appropriate. Such facilities include asphalt batch plants, where lightly contaminated soils are combined with asphalt binder to produce paving, and thermal processing facilities, where contaminants are removed from soil or rendered inert, creating a marketable product.

We will use the results from a soil characterization sampling and screen soils during construction to maximize our ability to salvage and recycle all acceptable hazardous and non-hazardous soils.

4.8.J APPROACH TO DIVERTING LANDSCAPING WASTE FROM LANDFILLS AND INCINERATORS

We will develop and implement a Construction and Demolition Waste Management Plan. As part of the plan, a minimum of 50 percent of all non-hazardous soil will be reused and where appropriate for planting. Any soil proposed for on-site reuse will meet the Contract requirements. In addition, GLX Constructors will achieve end-of-Project rates for reusing/composting at

least 90 percent by weight of total nonhazardous landscaping waste. We will incorporate the following procedures in the Construction and Demolition Waste Management Plan:

- Strip topsoil from required excavation and stockpile for future use to landscape within the Project limits.
- Process all clearing and grubbing waste into mulch. Mulch can be incorporated into the work, made commercially available to outside consumers, or composted for the amending of soils.
- If possible, soils may be amended and retested to meet the requirements. Soils not meeting these standards will not be allowed in planting areas.

4.8.K APPROACH TO TRAINING WORKERS, SUBCONTRACTORS, AND SUPPLIERS ON PROPER WASTE MANAGEMENT PROCEDURES

GLX Constructors will train workers, subcontractors, and suppliers on proper waste management procedures as appropriate for the work by:

- Incorporating its salvage and recycling commitments, along with the Construction and Demolition Waste Management Plan, into all subcontracts for work. See Section 4.8.I for more information.
- Incorporating our Construction and Demolition Waste Management Plan into the overall Training Plan for new employees. See Section 4.8.I.

4.8.L APPROACH TO MEETING RECOMMENDED CONTROL MEASURES FOR CONSTRUCTION INDOOR AIR QUALITY

Prior to construction, GLX Constructors will analyze historic data and conduct sampling in indoor areas during construction. We will use this information to determine what measures must be best implemented according to Sheet Metal and Air Conditioning National Contractors Association IAQ Guidelines for Occupied Buildings Under Construction, ANSI/SMACNA 008-2008 (Chapter 3). If we encounter contaminated air, we will advise the Health and Safety Team of the appropriate personal protective equipment needed during construction and will continue to test during construction to ensure that the practices are performing.

4.8.M APPROACH TO PROVIDING ACCEPTABLE INDOOR AIR QUALITY IN ALL NEW BUILDINGS

GLX Constructors will analyze historic releases, current use limitations, and conduct sampling in the areas of proposed structures to determine any potential need for indoor air quality measures.

TRC has worked on many contaminated sites that were redeveloped to protect human health and the environment, including schools and passive/active recreational parks that now safely host children and has the requisite knowledge and experience to ensure the appropriate level of air quality is attained.

4.8.N APPROACH TO USING/RE-USING PRE-PURCHASED EQUIPMENT AND MATERIALS

Pre-Purchased Equipment

GLX Constructors will have a joint inspection with our Testing and Inspection Agency's engineering and technical personnel to determine the condition and usability of the MBTA's pre-purchased power equipment for the Project. From these inspections, we will generate, grade in various inspection categories, and file the inspection reports and photos.

We will then study and evaluate the existing power equipment's original submittals, approvals, and factory acceptance tests and their results. We will also study and evaluate the FTA's safety certification plan and check-offs of the plan lines pertaining to the existing power equipment up to the point when the contract was terminated. After reviewing these documents, we will generate a report with the results of the evaluation, which will be filed accordingly.

We will then study and evaluate the power equipment reports and photos gathered from the aforementioned tasks to determine a go/no-go for each piece of power equipment. New power equipment pieces will fill any voids. The power equipment will then be integrated with the new power equipment as one, overall functioning and operational power system.

Pre-Purchased Materials

Washington Street Bridge. Our design at the Washington Street Bridge will be similar to the structure from the RIDS Plans. As described in Section 4.2.B, our design proposes a through girder structure. The through girders will be set on a closer spacing than in the previous design, which will generate slightly shorter floor beams. The proposed design will reuse the previously purchased plate that is available for the selected DB entity.

Viaduct. Our design will incorporate the pier structures constructed to date. Span configurations for the proposed viaduct will be compatible with the original design allowing for the pier reuse.

Similar to Washington Street Bridge, our viaduct superstructure design is based on reusing as much of the pre-purchased plate as possible. Our design uses steel welded 'I' girders in the spans that the GMP plans had called for tub girders. However, the plate purchased for the tubs can still be used. We will maintain the top flange, web, and bottom flange thicknesses, and the depth of the section will be similar, allowing reuse of the plate.

On the GMP viaduct design, where single-track viaduct structure was employed, a single tub was used in combination with a large concrete counterweight. This configuration is not workable because the counterweight, being several times stiffer than the tub, becomes the primary support system. Our design involves

replacing both the single tub and counterweight with three welded 'I' shaped girders.

The girders, having a wider support footprint than the single tub, eliminate the need for the counter weight. For this case, we will cut the bottom flange plate of the single tub into thirds; these three plates will form the bottom flanges of the proposed three girders.

4.8.O APPROACH TO PROVIDING BUILDING COMMISSIONING IN COORDINATION AND UNDER MBTA MANAGEMENT

The VMF building and station commissioning process is provided through the GLX Construction Execution Team and interfaces with the Quality Manager and Testing and Commissioning Manager. Cutler, our dedicated subcontractor responsible for construction of the VMF and Stations, will provide the dedicated Commissioning Agent (CA) to lead the commissioning process. The CA will report through the Quality Manager and direct the Design Discipline Leads and Construction Superintendents during performance of the interim and final testing and commissioning of the buildings and station facilities in preparation for approval to occupy.

To provide documented confirmation that the facility fulfills the functional and performance requirements of the occupants and operators, the CA will establish and document the Owner's Project Requirements (OPR) and criteria for system function, performance, and maintainability and prepare a final testing and commissioning checklist for execution of the final facility commissioning. The MBTA's Project Requirements will form the basis from which we make our design, construction, acceptance, and operational decisions. These requirements include accessibility, acoustics, comfort, communications, energy efficiency, fire protection, life safety, flexibility health, hygiene, indoor environment, lighting, maintenance requirements, security, and structural safety.

During the construction phase, the CA will confirm and verify that systems and assemblies operate in a manner that will achieve the MBTA's Project Requirements and coordinate the training of Operating Personnel in the required care, adjustment, maintenance, and operation of the new facility equipment and systems. To facilitate the commissioning process, copies of approved submittals critical to the commissioning process are provided to the CA as they are received. The CA develops construction checklists for our team to implement and for documentation and verification of accepted construction.

Functional performance testing occurs as construction verification is completed. Where components require factory acceptance testing, the CA and/or QA personnel will travel to the manufacturing facility to witness the factory acceptance testing that occurs prior to shipment of the components to the construction site for installation. Functional testing of the system/building provides confirmation of the components' ability to work together as a system to achieve the MBTA's Project Requirements. For valid results, the individual components and systems must be verified as operating properly, including start-up and Testing, Adjusting, and Balancing (TAB). Test data records confirm outcomes of functional performance testing, including test data, observations, and measurements. Data may be recorded using photographs, forms, or other means appropriate.

Lighting commissioning. Will comprise up to four process phases: pre-design, design, construction, and occupancy and operations. The commissioning process will use IES recommendations as a guideline.

Pre-design phase. Our Design Team and the CA will work with the MBTA to develop the OPR document. This written document is used throughout the Project to detail the owners' expectations as to how the lighting and controls are intended to operate and includes expected illuminance levels.

Design phase. Completed design documents include details for all lighting controls and illuminance levels that meet the requirements of the OPR. The CA reviews these documents and identifies items to be included in the system manual.

Construction phase. After reviewing contractor submittals of systems under commission, the CA will develop a system manual for operating staff and confirm the training requirements the manufacturer must provide. Submittal review comments from the CA are submitted to the Engineer of Record for review and comment. The CA, along with the Engineer of Record, will verify that the correct equipment is installed and functioning in accordance with the construction documents.

Occupancy and Operations phase. After substantial completion, the CA will review the operation of the lighting system with the operations and maintenance staff and occupants and develop a plan to resolve any outstanding commissioning issues.

HVAC commissioning will be a living process over the entire duration of the Project. Commissioning of the mechanical system will start during the Design Phase with a mechanical design narrative that captures the design intent of a particular system, summarizes the system operation, and outlines the design criteria that will govern how that system is sized and operated. We will update the narratives as the design documents advance, and they will serve as a summary of each mechanical system.

Mechanical pre-functional checklists will be prepared during design to assist the contractor with installation, confirm all steps performed during start-up, and include verification checklists required to move on to functional testing. We will create functional testing documents to verify the equipment's performance. The objective of the functional testing is to measure the energy-efficient performance of each system as defined in the final design documents.

Once construction of a particular system is approaching completion, the pre-functional process will include Testing and Balancing (TAB) of the system, as shown on the design documents, and the recording measurements to be used by the controls contractor. These steps require bringing the TAB Contractor (TAB agency), Automatic Temperature Control (ATC) contractor, and Designer Engineer together during initial installations and Project start-up to ensure checklists are completed and information is available when needed. These meetings will also include project superintendents and construction managers to discuss submittal reviews, verify checklists completed, perform testing, and finally, verify all completed training.

To complete any seasonal testing of systems and components, and to sign-off on occupancy phase commissioning activities, the commissioning process of mechanical systems will continue into the early occupancy phase of the building.

The CA will hold consistent, regular commissioning meetings to maintain the progress of the Project and develop logs/reports, and checklists and issue progress reports.

4.8.P APPROACH FOR STORING COMPONENTS

For systems components, providing a secure and weather-protected storage is critical to adhere to the warranty period and meeting the anticipated life cycles. These items will be stored off the ground on pallets to protect from sudden flash flooding within the warehouse facility.

GLX Constructors will secure an adequately sized warehouse facility, which will store these electrical components and systems assemblies. This warehouse facility will be climate controlled to include correct temperature settings based on the manufacturer's recommended storage temperature range that will accommodate all system elements housed in the warehouse facility. Condensation buildup prevention is critically important, especially with electrical components and systems assemblies. In normal weather conditions, we will visually inspect our warehouse. Any anticipated, inclement severe weather conditions will be studied and processes in place will be evaluated. If additional mitigation measures are necessary, they will be initiated. Based on discussions with his team, the Project Manager, John West, will make the final decision.

Although poles and other structures will be stored outside, the specifications allow for protection against weather by paint and galvanization. The bottom layer of these structures will be stored on wood timbers above the ground. Visual inspections will occur weekly and the inspections will be documented. This includes the timber placement, the straightness of the poles/structures, and the condition of the paint and galvanized coatings.

4.8.Q PROVIDING MINIMALLY MANAGED LANDSCAPE

We will provide a minimally managed landscape through Permaculture gardening. This process begins by understanding the area's conditions, the soil type, sun or shade quantity, water availability, and the best type of plant community for a specific environment. Planting areas will be positioned to gather water appropriately.

We will select plants based on the ecological communities in which they grow in the wild. Native species are usually best adapted to any given area, though there are some hardy non-native species that are quite adaptable. When installing plants, we will amend the soil to the plant's needs. This is particularly important for tree and shrub plantings because roots will remain in the tree pit, and not expand into the existing soil, if the soil mixture is too rich.

If the plants are selected to be drought tolerant, durable, and are planted in healthy communities to establish themselves, the vegetation will be able to thrive and not rely on irrigation or fertilizer after the initial 90-day maintenance period.

4.8.R APPROACH TO CREATING AND/OR ENHANCING ACCEPTABLE WILDLIFE HABITATS

The landscape design proposed by our team includes native plants, which will flower throughout the growing season. In turn, these flowering plants will provide nectar for beneficial insects and subsequently produce seeds and berries for urban wildlife use. Non-deciduous plants will provide winter shelter for urban wildlife. We will limit clearing and trimming existing vegetation, except for the required clearance envelope or providing construction access.

4.8.S AN APPROACH FOR ACHIEVING LONG-TERM, ENVIRONMENTALLY SOUND PEST SUPPRESSION AND PREVENTION

GLX Constructors will address pest control both during construction and in the design of the permanent facilities. During construction, the SWPPP and local requirements will guide site conditions. We will avoid creating areas of untreated standing water that serve as breeding locations for insects. We will implement an integrated pest control program to control rodents in compliance with MBTA's rodent control program within the limits of construction and to avoid displacing rodents from the site to the surrounding areas. We will use a licensed pest control contractor to assess the existing rodent population and prepare a baiting program to eliminate rodent populations prior to construction on a location-by-location basis.

Perimeter baiting stations continuously control rodents for the duration of construction. The program will be supported by careful control of food wastes on the construction site including covered, rodent-proof refuse cans and regular removal of wastes.

Post-construction, our design controls pests by not creating areas of standing water to avoid insect breeding, constructing sealed building foundations to resist pest infestation, and avoiding unprotected horizontal ledges in structures to avoid creating bird-nesting areas.

4.8.T APPROACH TO PROVIDING TIME-OF-DAY LIGHTING NEEDS

GLX Constructors understands that effectively using lighting and power is of the utmost concern to the MBTA. Our proposed lighting system will use cost-effective, low-maintenance, user-friendly methods that will properly light the station during hours of operation and dial back lighting after hours or when not required.

We propose a small 4-to-8 circuit lighting control panel to control station and platform lighting, which will have fully programmable time settings for each circuit, and will operate in conjunction with an on-site photocell and occupancy sensors. These controls allow each station to be fully lit during peak hours and have the capability to reduce lighting levels when no occupants are detected.

All fixtures located on the platform and exposed to adjacent properties will be dark skies compliant, full cutoff fixtures that limit the intensity of light in the 80 to 90 degree region of the fixture. In addition, we will use shielding in the case we are concerned about light spill to adjacent properties.

4.8.U APPROACH TO PROVIDING ENERGY EFFICIENT LAMPS AT APPROPRIATE LOCATIONS

Our design incorporates lighting fixtures with LED sources in all locations in and around the stations.

Luminous efficacy is a measure of how well a light source produces visible light given the amount of power consumed. It is the ratio of luminous flux to power, measured in lumens per watt. In other words, the source uses the least amount of power to produce the most amount of light. The lighting source with the highest efficacy is an LED source. This source is also the most widely accepted by the lighting industry and has the most options with regard to fixture types available.

The dimming range of LEDs is broader than that of compact fluorescent and high-intensity discharge lamps. They can turn down to less than 1 percent of their full potential output, compared to 10 percent to 30 percent of measured light output for compact fluorescents and 30 to 60 percent of lamp power for high-intensity discharge lamps. In essence, LED sources use less power to provide more light and have much more controllability than both compact fluorescent and high intensity discharge sources.

4.8.V APPROACH TO PROVIDING WATER-EFFICIENT EQUIPMENT AND FIXTURES AT APPROPRIATE LOCATIONS

Sustainable and responsible design is rapidly becoming part of all engineering aspects. To this end, all new plumbing fixtures, where appropriate, will bear the Environmental Protection Agency's WaterSense Label. WaterSense-labeled products are certified to use at least 20 percent less water, save energy, and perform as well as or better than regular models.

During the proposal period, we thoroughly reviewed the applicable environmental approvals, permits, laws, and regulations. The key to our approach is instituting a strategy that is compliant with the requirements of the Technical Provisions. In teaming with our experienced, local subcontractors, Tetra Tech and TRC, GLX Constructors is prepared with the knowledge, resources, and experience to remain compliant and eliminate potential environmental issues before they occur.

ITP Request	RFP		
	Drawing Number	Drawing Title	Reference Section or Drawing
Drawings not required			

Technical Solutions Drawing Matrix.

4.9 UTILITIES

To reduce Project cost and provide greater schedule certainty, we have identified and created plans to avoid or adjust more than 150 utility conflicts, including electric, telecommunications, gas, water, and sanitary sewer. We are committed to developing positive working relationships with utility owners. We will be effective on day one due to our existing relationships with utilities established on the Longfellow Bridge and State Street Station Projects, communication methods, intensive interdisciplinary reviews, and careful utility coordination. Our efforts will limit design changes, uphold safety standards, and keep rework to a minimum.

Proper identification, coordination, protection, relocation, and construction of utilities will reduce Project risks while promoting a positive public perception of the Project. We will dedicate a team of design and construction experts whose sole purpose will be to identify utilities, coordinate with public and private utilities providers, accurately verify utility locations, design protections or relocations, and monitor and report progress on all utility activities. As shown in Figure 4.9-1 we have a vast amount of experience with utility construction and coordinating with utility companies. We will collaborate with the MBTA to make certain that excellent utility coordination optimizes the delivery of the Project.

4.9.A GLX CONSTRUCTORS' UTILITY INFRASTRUCTURE RELOCATION PLAN APPROACH

Utility Relocation Plans require close coordination with many third parties, including the utility owners and their customers. The key to this coordination is the early identification of all utilities within the Project limits by establishing a utility matrix that identifies the following:

- Utility type
- Location (vertically and horizontally)
- Diameter
- Material type
- Owner
- Facilities serviced
- Disposition

To meet the requirements of Volume 2 Technical Provisions, GLX Constructors' developed a Utility Matrix at the beginning of our proposal effort shown in Appendix 2. We have refined this information to identify utilities that influence the GLX Project. We have contacted a number of utility providers to confirm our concepts for protection, supports, and potential shut downs.

Identification of Existing Utility Infrastructure

To avoid potential conflicts, we will contact all utility owners within the Project limits to obtain every available record data, and confirm the MBTA provided prepared base mapping. This effort will include meetings with the utility providers' field personnel, who know where and how the utilities are constructed. This firsthand knowledge is critical in identifying access points, bends, or valves, which can expedite utility relocations or protect utilities in place.

Where utility record information is lacking or highly accurate locations are required, we will use subsurface utility location tools, including vacuum excavation, ground penetrating radar, and electromagnet locating. Because such technology will vastly increase the accuracy of utility locations, it reduces risk to both schedule and cost.

Recommended Utility Work

Through regular design coordination meetings, GLX Constructors' Utilities Technical Working Group (TWG) will be able to identify if the planned construction activities will conflict with existing utilities.

We will resolve utility conflicts with a four question approach:

- **Safety.** Can the utility safely remain in place?
- **Age and condition of the utility.** Is there a concern that the utility may already be structurally deficient?
- **Proposed construction operations.** How close will work take place to the utility?
- **Temporary works.** What other operations could affect the utility?

Our Utilities TWG will partner with the MBTA and the utility owner. We will document the review, coordination, decisions, and approval process on our Utility Matrix.



Figure 4.9-1. *The Construction of the Hingham Tunnel required coordination and relocation of numerous utilities including the 54" Town Brook Culvert. The project was successfully completed on time.*

Assumptions and Considerations

We will identify all utilities through close coordination with the utility owners and complete detailed investigations to determine their locations. We will engineer Utility Designs to protect utilities in place or relocate them out of conflict with the proposed works. We have considered and assume all Project and utility owners are listed in Figure 4.9-2.

Water	Cambridge Water
	Medford Water & Sewer
	Somerville DPW Water & Sewer
	MWRA
Sewer	Cambridge Drain & Sewer
	Somerville DPW Water & Sewer
	Medford Water & Sewer
	MBTA
Gas	Spectra Energy Algonquin
	National Grid Gas
	NSTAR Gas
	Eversource
Telecommunications	Phoenix Communications
	Zayo
	AT&T
	Comcast (Somerville, Medford, Cambridge)
	Level 3
	Lightower Fiber Networks
	Waveguide
	MCI Metro
	Crown Castle
	Poltel
	NSTAR Communications
	RCN
	Verizon (Medford, Somerville, Cambridge)
	Bell Canada
	Hibernia Networks
	XO Communications
Electric	National Grid
	Eversource

Figure 4.9-2. Green Line Extension Utility Owners. *GLX Constructors will work closely with the Utility Owners to protect or relocate impacted utilities.*

“We were very successful in avoiding utility issues during the construction of the Town Brook Culvert, installed through downtown Hingham, Massachusetts, which had active utilities dated 80 years old.

Approach to Communication and Coordination with Utility Companies

GLX Constructors has extensive experience in communicating and coordinating utility relocations with owners, including local experience with the Greenbush Line Rail Restoration DB Project. We will initiate regular coordination with each utility owner at the start of the Project. This coordination effort will be through a single point of contact, the Design Discipline Lead, Sean Barry, PE, who leads a team that has designed and coordinated utility relocations throughout the greater Boston area for more than 25 years. We will successfully coordinate with utility owners by providing appropriate attention to understand their needs. Partnering with all parties will foster Project-related pride and create positive results.

Understanding Utility Companies’ Operational Constraints. The Green Line Extension DB Project is critical to regional economic growth. Utility owners must maintain service to their existing customers. Successful coordination with utility owners will be accomplished through a detailed understanding of each utility owners’ operational constraints. Through regular utility coordination meetings, we will develop an understanding of each utility system’s constraints and confirm that these limitations are part of the decisions made on each utility.

Approach to Managing Service Interruptions to Utilities Companies’ Customers and Property Owners

We will make every effort to avoid interruptions; however, when interruptions are unavoidable we will plan and execute to minimize the interruption.

Options to minimize impacts include night work or off season work, where the demand on a utility is at its least. We will maintain positive public perception of the project by proactively communicating interruptions through email blasts, project website posting, announcements through community access channels, and publications in local newspapers. All public outreach will take place in accordance with the Technical Provisions, Section 2.9.3.

Approach to Early Identification and Mitigation of Impacts to Critical Utilities

We have already identified a number of critical utility issues throughout our proposal efforts, including the 48-inch MWRA Water Line at Medford Street, the sewer siphon at School Street, the Algonquin gas line at MB-EB Sta 266+50, and the two 12-inch gas lines in Washington Street to name a few. These issues are included in our Utility Matrix. As we continue our work, we expect to identify other critical utilities through careful coordination with utility owners.

Utility services can become critical if they provide service to critical public safety facilities, have equipment that requires long-lead time, or are not easily replaced or relocated because of system limitations. We have already initiated outreach with each utility owner, and started to develop plans with each for relocating and protecting each utility.

This effort will benefit the schedule at Notice to Proceed because we have already established relationships and understand the utility owners' needs.

Approach to Coordination with All Other Area Utility Infrastructure Relocations

Our goal is to minimize impact of utility work on the surrounding communities. Regular utility coordination meetings with utility companies and third parties will include review and discussion of other area utility infrastructure work.

This coordination effort is similar to those that we attend as part of our design and coordination efforts with the City of Cambridge. These meetings allow the Design and Construction Team to identify common elements that can be coordinated for the greater success of the Project and save schedule. Project-wide planning between GLX Constructors and all affected parties will avoid Project delays to successfully minimize impacts.

Approach to Supplying Utility Services to the Project

Each station, traction power substation, signal bungalow, the transportation building, and the vehicle maintenance facility will require water, sewer, drain, power, and telecommunication services. GLX Constructors has determined the scope of each of these services and the most efficient routing from the service provider to the appropriate service location at each facility.

As part of our utility outreach due diligence, we have verified that adequate system capacity exists to provide service to the various facilities. Where not available, we have identified needs for system upgrades to meet the Project needs. We will revisit these determinations throughout the Design Build process to make certain that each facility will provide adequate capacity.

Approach to Maintaining, Protecting, and Relocating Positive Train Control Fiber Optic Cable

We understand that the MBTA is upgrading to Positive Train Control and have selected the New Hampshire Branch of the MBTA Commuter Rail system as one of the first areas to employ this system. The system runs from the Winchester Signal Instrument House to the Commuter Rail Operating Control Center. The existing system consists of a 48-strand single mode fiber optic cable installed either on poles or within inner duct/conduit.

GLX Constructors understands that this system must remain operational. In addition, we understood that the PTC Fiber Optic is to remain operational and that any proposed relocation or replacement must be accomplished in accordance with the MBTA project specifications, which include a 30-day advanced notice and plans detailing the proposed work such as splice locations, inspection, and testing. So that the PTC cable is paramount in all design and construction considerations, the first step in its protections will be to accurately survey the locations of all poles, houses, cabinets, fiber, and ducts of the PTC system. This information will be accurately located and annotated as PTC CABLE – Do Not Disturb on the project-wide mapping to reflect its importance. Once located and accurately reflected on the project mapping and similar to other critical utilities, GLX Constructors will ensure that the system is protected and maintained during all design and construction reviews.

When construction activities require the PTC Cable to be relocated, our first consideration will be to place the PTC fiber into a secure and final location. It is our goal to make certain that relocation of any section of fiber only happens once, which should limit the impact to MBTA operation and costs to the Project.

4.9.B BENEFITS OF GLX CONSTRUCTORS' APPROACH TO UTILITIES FOR OWNERS AND USERS DURING THE CONSTRUCTION PERIOD

GLX Constructors has a proven record of identifying critical utilities, coordinating with affected utility companies, and designing for utility protection or relocation. These same skills were employed for the MBTA's Greenbush Line Rail Restoration DB Project with recognized success. We will use the same utility coordination that led utility management on the Greenbush Project. They will employ their lessons learned from working with various impacted utilities to develop a spirit of partnership with each utility owner, identify critical issues, and develop design solutions to solve each.

Additionally, GLX Constructors Team Member, Middlesex, routinely performs work for several local utilities, including major projects for Eversource, and will incorporate the knowledge gained of their requirements into the design, relocation, and negotiation processes.

Our team's combined working knowledge with the local utilities will have the following positive benefits for utility owners and users:

- Safely planned and executed utility work
- Advanced notice of planned interruptions
- Shorter construction disruptions
- Work that is completed correctly the first time
- Preservation of critical utility services.

4.9.C PERMANENT AND TEMPORARY RELOCATION/PROTECTION PLANS

Figure 4.9-3 is an example of one utility relocation plan that will continue to be coordinated with a local utility who was willing to work with us before NTP. Because most of our utility partners are interested in reviewing and talking to the team that has been awarded the Project, our ability to provide complete relocation and protection drawings for the entire Project is limited by where we are in the proposal process. Working with MWRA, we coordinated and planned ATC 36 which raised the community path to avoid this critical 48" water line. Our Utility Matrix has captured every potential issue that we have been able to identify from the MBTA's provided documents and includes proposed solutions, site conditions, and proposed works.

Through careful coordination with the many public and private utilities, the GLX Constructors' Utilities Team will be the face of the Green Line Extension DB Project for many of the project stakeholders. This team will lead the effort in identifying all utilities within the project limits and be responsible for identifying those critical utilities that could affect Project schedule. Our Team will maintain frequent and regular coordination with the effected utilities, serving as a conduit for information to keep the utilities appraised of the Project schedule, and keep their attention on the needs of the Project. We have an experienced DB utility coordination team that well lower Project costs while shortening the construction duration.

"To mitigate the impact to abutters and many important businesses around the Green Line, we will employ a philosophy of avoid, minimize, or mitigate.

ITP Request	RFP		
	Drawing Number	Drawing Title	Reference Section or Drawing
A5.2.9.C.1			Drawings are as described by Section 4.9.C
A5.2.9.C.2			Drawings are as described by Section 4.9.C
A5.2.9.C.3			Drawings are as described by Section 4.9.C

Technical Solutions Drawing Matrix.

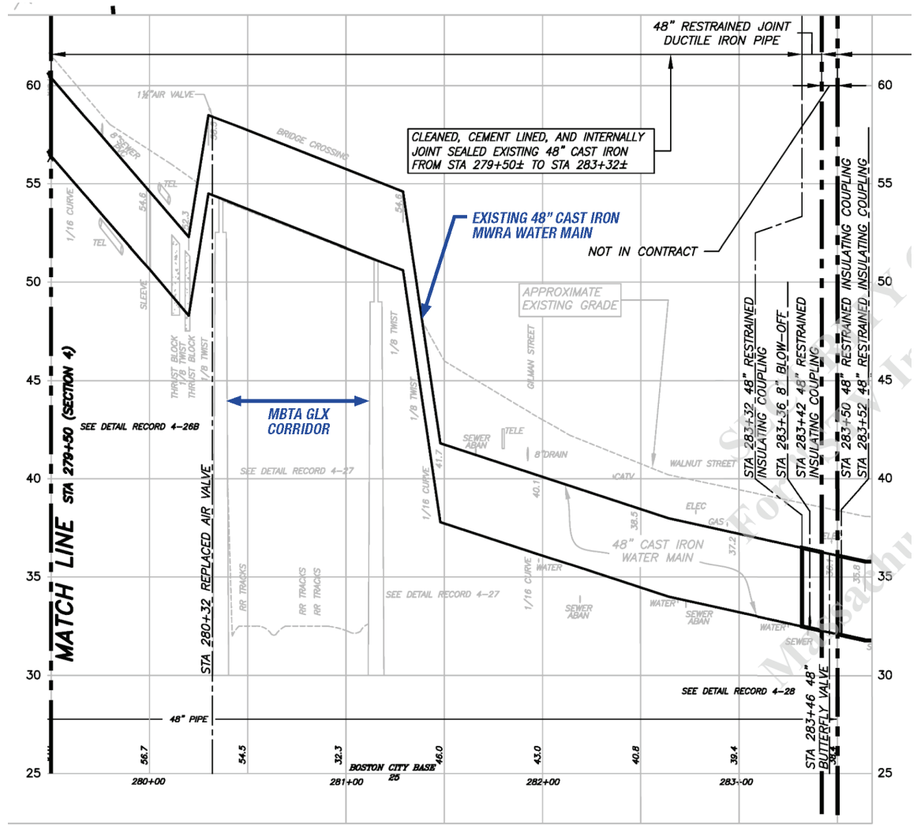


Figure 4.9-3. 48" Cast Iron Water Main at Walnut Bridge. *GLX Constructors approved ATC 36 which raises the community path and significantly reduces impact to the critical MWRA utility.*

APPENDIX 2

Utility Matrix

PRELIMINARY UTILITY MATRIX

SIZE AND MATERIALS	TYPE	STATION (MB-WB)			UTILITY CROSSES RR				UTILITY LOCATED PARALLEL AND BETWEEN RR					OVERHEAD	OWNER/ POTENTIAL OWNER	BRIDGE OR STREET	ON BRIDGE	DISPOSITION (TO BE REPLACED/ RELOCATED/ REMAIN/ ABANDONED ETC.)
		CROSSING	PARALLEL		MB-WB	MB-EB	NH-T2	NH-T1	MB-WB	MB-EB	NH-T2	NH-T1	YL-10					
			FROM	TO														
MEDFORD BRANCH																		
24"	SEWER	188+00														East Street		TO REMAIN
8"	WATER	188+00													CAMBRIDGE WATER DEPT			TO REMAIN
16"	WATER	188+00													CAMBRIDGE WATER DEPT	East Street		TO REMAIN
8" ST IP	GAS	188+00			X	X									EVERSOURCE	East Street		TO REMAIN
2-4" TELE	TELE	188+00														East Street		TO REMAIN
GAS ABANDONED	GAS	188+00			X	X									EVERSOURCE	East Street		TO REMAIN
UNKNOWN	ELEC	191+50			X	X								x	EVERSOURCE			UNKNOWN
WATER PIPE	WATER	192+00													MWRA/ CAMBRIDGE WATER DEPT			TO REMAIN
TELE	TELE	195+75			X	X									VERIZON	Water Street		TO REMAIN
8" PIPE	WATER	196+00													CAMBRIDGE DPW	Water Street		TO REMAIN
12" BRICK	SANITARY	196+00			X	X									CAMBRIDGE DPW	Water Street		TO REMAIN
3" GAS	GAS	196+00			X	X									EVERSOURCE	Water Street		TO REMAIN
GAS ABANDONED	GAS	196+00			X	X									EVERSOURCE	Water Street		TO REMAIN
UNKNOWN	TELE	196+25			X	X								X	VERIZON	Water Street		UNKNOWN - TO REMAIN
UNKNOWN	TELE	196+25			X	X								X	VERIZON	Water Street		UNKNOWN - TO REMAIN
UNKNOWN	ELEC	196+50												X	EVERSOURCE	Water Street		UNKNOWN - TO BE RELOCATED?
24" CI SALT W	WATER	208+00													CAMBRIDGE WATER DEPT			TO REMAIN
UNKNOWN	ELEC	208+25			X	X								X	EVERSOURCE			UNKNOWN - RELOCATE?
UNKNOWN	ELEC	208+50												X				UNKNOWN - RELOCATE?
MBTA Signal	ELEC	209+00																TO REMAIN
12" W ABANDONED	WATER	209+00			X	X									MBTA			ABANDONED
2- 4" DUCT	ELEC	209+50			X	X									MBTA			TO REMAIN
12" W ABANDONED	WATER	209+50			X	X									MBTA			ABANDONED
9-4" DUCT	ELEC	210+00			X	X									MBTA			TO BE RELOCATED
5'-9"X6'-6" SEWER MAIN	SANITARY	226+00													MWRA	JOY STREET		TO REMAIN
10" V.C	SANITARY	226+01													CAMBRIDGE			TO REMAIN
(36) -1-1/4" Level 3 T QL-B	TELE	225+50			X	X									LEVEL 3			TO REMAIN
UNKNOWN	ELEC	233+50				X	X	X						X	EVERSOURCE			MULTIPLE OVERHEAD LINES CROSSES AROUND 233+50 TO BE RELOCATED
68-1-1/4 PVC & 4- 4" PVC	TELE	237+25													VERIZON	WASHINGTON ST	X	TO REMAIN

PRELIMINARY UTILITY MATRIX

SIZE AND MATERIALS	TYPE	STATION (MB-WB)			UTILITY CROSSES RR				UTILITY LOCATED PARALLEL AND BETWEEN RR					OVERHEAD	OWNER/ POTENTIAL OWNER	BRIDGE OR STREET	ON BRIDGE	DISPOSITION (TO BE REPLACED/ RELOCATED/ REMAIN/ ABANDONED ETC.)
		CROSSING	PARALLEL		MB-WB	MB-EB	NH-T2	NH-T1	MB-WB	MB-EB	NH-T2	NH-T1	YL-10					
			FROM	TO														
10- 4" FIBER OPTIC	TELE	237+25													VERIZON	WASHINGTON ST	X	TO REMAIN
UNID-UTIL	ELEC	253+50													EVERSOURCE	McGrath HWAY	X	TO REMAIN
8" SANITARY	SANITARY	262+00														WALNUT ST	X	TO REMAIN
TELE	TELE	262+50													VERIZON	WATNUT ST	X	TO REMAIN
48" MDC	WATER	262+50													MWRA	WALNUT ST	X	TO REMAIN
14" Gas in 42" sleeve Transmission	GAS	266+50			X	X	X	X							SPECTRA ENERGY ALGONQUIN			VERTICAL GAS PIPE VENT ON BOTH ENDS NEAR ROW LINE - To be relocated to accommodate wall construction
12" W	WATER	268+00													SOMERVILLE DPW-WATER & SEWER	MEDFORD ST	X	new water line installed on opposite side of bridge, this may be abandoned
16-4" FRP TELECOME DUCTS (ZAYO)	TELE	268+00														MEDFORD ST UTILITY BRIDGE		To remain, bridge to be modified to provide underpass, protect
24-4" FRP TELECOME DUCTS (VERIZON)	TELE	268+00														MEDFORD ST UTILITY BRIDGE		To remain, bridge to be modified to provide underpass, protect
2-4" FRP FIRE ALARM DUCTS	ELEC	268+00														MEDFORD ST UTILITY BRIDGE		To remain, bridge to be modified to provide underpass, protect
TELE	TELE	269+00			X	X	X	X							VERIZON	MEDFORD ST	X	To remain, bridge to be modified to provide underpass, protect
(60) 4" T & FA	TELE	271+00			X	X	X	X							VERIZON			MBTA reported that this was abandoned
15" PVC	SANITARY	272+00				X	X	X							SOMERVILLE DPW-WATER & SEWER			To be relocated
ELEC	ELEC	272+28				X	X	X							Eversource			Already abandoned - To be relocated?
RELOCATED WATER LINE	WATER	275+00														SCHOOL ST UTILITY BRDIGE		IS THIS ACTIVE?
RELOCATED 6-5" PVC ELEC DUCT	ELEC	275+00														SCHOOL ST UTILITY BRDIGE		IS THIS ACTIVE?
12" CI	SANITARY	275+25			X	X	X	X							To be replaced	SCHOOL ST		TO BE RELOCATED BECAUSE OF UNDERPASS
10"	WATER	275+50													SOMERVILLE DPW-WATER & SEWER	SCHOOL ST	X	Limited replacement required by underpass
8 - 4" DUCT	TELE	275+50													VERIZON	SCHOOL ST	X	Limited replacement required by underpass
2-4" MBTA	ELEC	275+50													EVERSOURCE	SCHOOL ST	X	Limited replacement required by underpass
UNID-UTIL	ELEC	275+50													EVERSOURCE	SCHOOL ST	X	Limited replacement required by underpass
UNID-UTIL	ELEC	284+50												X	EVERSOURCE	SYCAMORE ST	X	TO REMAIN
ELEC	ELEC	289+50												X	EVERSOURCE	CENTRAL ST	X	TO REMAIN

PRELIMINARY UTILITY MATRIX

SIZE AND MATERIALS	TYPE	STATION (MB-WB)			UTILITY CROSSES RR				UTILITY LOCATED PARALLEL AND BETWEEN RR					OVERHEAD	OWNER/ POTENTIAL OWNER	BRIDGE OR STREET	ON BRIDGE	DISPOSITION (TO BE REPLACED/ RELOCATED/ REMAIN/ ABANDONED ETC.)
		CROSSING	PARALLEL		MB-WB	MB-EB	NH-T2	NH-T1	MB-WB	MB-EB	NH-T2	NH-T1	YL-10					
			FROM	TO														
UNID-UTIL	ELEC	304+50													EVERSOUCRE	LOWELL ST	X	Limited replacement required by abutment work
8" VC	SANITARY	313+00			X	X	X	X							SOMERVILLE DPW-WATER & SEWER			to be replaced with sewer siphon
UNKNOWN	ELEC	313+75						X						X	EVERSOURCE			Relocate if in conflict with proposed work.
UNID-UTIL	ELEC	321+00												X	EVERSOURCE	CEDAR ST	X	TO REMAIN
TEMPORARY ELEC	ELEC	329+50														BROADWAY UTILITY BRDIGE		To remain and be protected
TEMPORARY TELE	TELE	329+50														BROADWAY UTILITY BRDIGE		To remain and be protected
TEMPORARY 12" WATER LINE	WATER	329+50														BROADWAY UTILITY BRDIGE		To remain and be protected
12" W	WATER	330+00													SOMERVILLE DPW-WATER & SEWER	BRAODWAY	X	ABANDONED
ELEC	ELEC	330+00													EVERSOURCE	BROADWAY	X	ABANDONED
TELE ABANDONED	TELE	330+01													VERIZON	BROADWAY	X	ABANDONED
ELEC ABANDONED	ELEC	330+25													EVERSOURCE	BROADWAY	X	ABANDONED
ELEC	ELEC	330+50													EVERSOURCE	BROADWAY	X	ABANDONED
2-30" 345 KV PTC (RECORDS AVAILABLE)	ELEC	331+50			X	X	X	X							NATIONAL GRID			TO REMAIN AND BE PROTECTED, CHECK FOR DRAINAGE CONFLICT
24" CI IN 42" CMP SLEEVE	WATER	332+50			X	X	X	X							MWRA			TO BE RELCOATED ACCORDNG TO DOCUMENTS AS I RECALL THIS NEEDS TO BE VERIFIED
2" W	WATER	332+50				X	X	X							MBTA			to be relocated
FIBER OPTICS	TELE	335+00				X	X	X							VERIZON/MCI-VERIZON			RELOCATE
8" G	GAS	345+25													NATIONAL GRID/ EVERSOURCE	HARVARD ST		TO REMAIN
12" G	GAS	345+25													NATIONAL GRID/ EVERSOURCE	HARVARD ST		TO REMAIN
TELE	TELE	345+25													VERIZON	HARVARD ST		TO REMAIN
16" MDC	WATER	345+50													MWRA	HARVARD ST		TO REMAIN
10"	WATER	345+50													MWRA	HARVARD ST		TO REMAIN
10" ABANDONED	WATER	345+50													MWRA	HARVARD ST		TO REMAIN
TELE	TELE	345+50													VERIZON/MCI-VERIZON	HARVARD ST		TO REMAIN
ELEC	ELEC	345+50													NATIONAL GRID	HARVARD ST		TO REMAIN
ELEC	ELEC	345+50													NATIONAL GRID	HARVARD ST		TO REMAIN

GV20170258-288.pdf

PRELIMINARY UTILITY MATRIX

SIZE AND MATERIALS	TYPE	STATION (MB-WB)			UTILITY CROSSES RR				UTILITY LOCATED PARALLEL AND BETWEEN RR					OVERHEAD	OWNER/ POTENTIAL OWNER	BRIDGE OR STREET	ON BRIDGE	DISPOSITION (TO BE REPLACED/ RELOCATED/ REMAIN/ ABANDONED ETC.)
		CROSSING	PARALLEL		MB-WB	MB-EB	NH-T2	NH-T1	MB-WB	MB-EB	NH-T2	NH-T1	YL-10					
			FROM	TO														
12" MET	SANITARY	345+50													MBTA	HARVARD ST		TO REMAIN
4" FIBER OPTIC	TELE	357+00			X	X	X	X							AT&T			TEMPORARY LINE
24" MDC C/W ABANDONED	WATER	358+50			X	X	X	X							MWRA			DEMOLISH AND CAP
30" MDC C/W ABANDONED	WATER	358+50			X	X	X	X							MWRA			DEMOLISH AND CAP
48" MDC	WATER	363+50													MWRA	COLLEGE AVE	X	TO REMAIN
20" MDC	WATER	363+50													MWRA	COLLEGE AVE	X	TO REMAIN
8" PL 25 PSIG	GAS	363+50													NATIONAL GRID/ EVERSOURCE	COLLEGE AVE	X	TO REMAIN
ELEC	ELEC	363+50												X	NATIONAL GRID	COLLEGE AVE	X	RELOCATE
ELEC	ELEC	363+50													NATIONAL GRID	COLLEGE AVE	X	RELOCATE
GAS ABANDONED	GAS		187+00	188+00					X	X					EVERSOURCE			TO REMAIN
4-4" PVC	TELE		188+50	196+00											VERIZON			TO REMAIN
6" PL ABANDONED GAS (1996)	GAS		196+00	196+50											EVERSOURCE			TO REMAIN
UNKNOWN	ELEC		232+25	233+50		X	X	X						X	EVERSOURCE			RELOCATE - MULTIPLE OVERHEAD LINES CROSSES AROUND 233+50.
ELEC	ELEC		272+00	275+00					X	X					EVERSOURCE			RELOCATE
9-4" DUCT	ELEC		274+00	275+50														MAINTAIN AND PROTECT (PER REDEF DRAWING)
UNKNOWN	ELEC		280+50	291+00										X	EVERSOURCE			UNKNOWN - TO BE REMOVED?
UNKNOWN	ELEC		290+00	300+00										X	EVERSOURCE			UNKNOWN - TO BE REMOVED?
12" VC	SANITARY		312+00	314+50											MBTA			TO REMAIN
SEWER LINE	SANITARY		312+00	314+50			X	X							MBTA			TO REMAIN
18" PVC	COMBINED STORM /SEWER AS PER REDEF DRAWING		314+50	320+25											MBTA			NO PIPE VISIBLE AT 314+50 - TO BE REMOVED?
4" STEEL FIBER OPTIC	TELE		329+00	335+00							X	X			AT&T			MAINTAIN AND PROTECT
UNKNOWN	ELEC		330+00	343+00					X	X				X	NATIONAL GRID			UNKNOWN - RELOCATE?
4" FIBER OPTIC	TELE		335+00	357+00											AT&T			RELOCATE
4-1.5" FIBER OPTIC ABANDONED	TELE		335+00	357+00							X	X			AT&T			To remain
FIBER OPTICS	TELE		357+25	375+00							X	X			AT&T			RELOCATE

GV20170258-288.pdf

PRELIMINARY UTILITY MATRIX

SIZE AND MATERIALS	TYPE	STATION (MB-WB)			UTILITY CROSSES RR				UTILITY LOCATED PARALLEL AND BETWEEN RR					OVERHEAD	OWNER/ POTENTIAL OWNER	BRIDGE OR STREET	ON BRIDGE	DISPOSITION (TO BE REPLACED/ RELOCATED/ REMAIN/ ABANDONED ETC.)
		CROSSING	PARALLEL		MB-WB	MB-EB	NH-T2	NH-T1	MB-WB	MB-EB	NH-T2	NH-T1	YL-10					
			FROM	TO														
UNID-UTIL	ELEC				X	X	X	X						X	TUFTS			UNKNOWN - RELOCATE?
14" Gas	GAS														ALOGONQUIN	ATTACHED TO McGrath		MAINTAIN AND PROTECT
20" WATER	WATER															WASHINGTON ST	X	TO REMAIN
36" CI G QL- B (SEE RECORDS)	GAS															WASHINGTON ST		TO REMAIN
12-4"	ELEC															WASHINGTON ST	X	TO REMAIN
2- 6 5/8" E (SEE RECORDS)	ELEC															WASHINGTON ST	X	TO REMAIN
UNION SQUARE BRANCH																		
UNKNOWN	ELEC		27+50	44+00											UNKNOWN			UNKNOWN / TO REMAIN
UNKNOWN	ELEC	41+50												X	UNKNOWN			UNKNOWN / TO REMAIN
UNKNOWN	ELEC	22+00													EVERSOURCE	MEDFORD ST		TO REMAIN
45" X 30" BRK	SANITARY	22+00													MWRA	MEDFORD ST		TO REMAIN
14'	WATER	28+50													CAMBRIDGE WATER DEPT	MEDFORD ST		TO REMAIN
20"	WATER	28+50													CAMBRIDGE WATER DEPT	MEDFORD ST		TO REMAIN
10 "	WATER		28+50	28+50											CAMBRIDGE WATER DEPT	MEDFORD ST		TO REMAIN
69" X 62" BRK	SANITARY	22+00													MWRA	MEDFORD ST		TO REMAIN
4" ABANDONED	GAS	22+00													SPECTRA / EVERSOURCE	MEDFORD ST		TO REMAIN
14" ALGONQUIN D	GAS	22+00													SPECTRA / EVERSOURCE	MEDFORD ST		TO REMAIN
14" ST IP ABANDONED	GAS	22+00													SPECTRA / EVERSOURCE	MEDFORD ST		TO REMAIN
UNKNOWN	GAS		22+00	22+00											SPECTRA / EVERSOURCE	MEDFORD ST		TO REMAIN
T & FA	TELE	22+00													VERIZON	MEDFORD ST		TO REMAIN
4-4" DUCT	ELEC		20+00	23+50											UNKNOWN			TO BE REPLACED
6-4" DUCT	ELEC	19+00													UNKNOWN			TO BE REPLACED
4-4" DUCT	ELEC	19+00													UNKNOWN			TO BE REPLACED
6-4" DUCT	ELEC		13+00	17+50											UNKNOWN			TO BE REPLACED
6- 4" DUCT	ELEC	13+00													UNKNOWN			TO BE REPLACED
2-4" DUCT	ELEC	20+50													UNKNOWN			TO BE REPLACED
SM 1- 4" DUCT	ELEC														UNKNOWN			TO REMAIN
S&C 3 -4" DUCT	ELEC														UNKNOWN			TO BE REPLACED

GV20170258-288.pdf

PRELIMINARY UTILITY MATRIX

SIZE AND MATERIALS	TYPE	STATION (MB-WB)			UTILITY CROSSES RR				UTILITY LOCATED PARALLEL AND BETWEEN RR					OVERHEAD	OWNER/ POTENTIAL OWNER	BRIDGE OR STREET	ON BRIDGE	DISPOSITION (TO BE REPLACED/ RELOCATED/ REMAIN/ ABANDONED ETC.)
		CROSSING	PARALLEL		MB-WB	MB-EB	NH-T2	NH-T1	MB-WB	MB-EB	NH-T2	NH-T1	YL-10					
			FROM	TO														
S&H 4-4 " DUCT	ELEC		18+50	17+50											UNKNOWN			TO REMAIN
S&C 4-4" DUCT	ELEC	18+00													UNKNOWN			TO REMAIN
12" ABANDONED	WATER	19+50													CAMBRIDGE WATER DEPT	McGRATH HWY	X	TO BE REPLACED
UNKNOWN	WATER	19+50													CAMBRIDGE WATER DEPT	McGRATH HWY		TO BE REPLACED
8" BRK CHANNEL	SANITARY	19+50													CAMBRIDGE	McGRATH HWY		TO BE REPLACED
8"	SANITARY	19+50													CAMBRIDGE DPW	McGRATH HWY		TO BE REPLACED
UNKNOWN	ELEC	19+50													EVERSOURCE	McGRATH HWY		
UNKNOWN ABANDONED	TELE	19+50													VERIZON	McGRATH HWY		
6-4" DUCT	ELEC		17+50	13+00						X					UNKNOWN			TO REMAIN
6-4" DUCT	ELEC	12+50													UNKNOWN			TO BE REPLACED
S&C (2- 4" DUCT)	ELEC		12+50	7+00						X					UNKNOWN			ABANDONED, DEMOLISHED AND CAPPED
4" PL	GAS		15+00	17+50											SPECTRA / EVERSOURCE			TO REMAIN
4" PL ABANDONED	GAS	15+00													SPECTRA / EVERSOURCE			TO REMAIN
4-E" DUCT	ELEC		20+00	24+00											UNKNOWN			
GAS	GAS		-	10+50														
12" CLDI WATER IN 24" STEE	WATER		8+75	11+00														
8" ABANDONED	WATER		17+00	12+00											UNKNOWN			
24" CI SALT AND 6" STEAM A	SALT WATER														UNKNOWN			
12" ABANDONED	WATER		17+00	5+00 +											UNKNOWN			
12"	WATER	14+-00													UNKNOWN			
1" COPPER	WATER	7+50													UNKNOWN			
ABANDONED	WATER		12+00	10+00											UNKNOWN			
ABANDONED	WATER		8+00	5+50											UNKNOWN			



Response to the Request for Proposal

for the Green Line Extension Design Build Project

Submitted to

Massachusetts Department of Transportation and The Massachusetts Bay Transportation Authority

Part 5 – Key Personnel and Experience Qualitative Evaluation Criteria Information

GLX CONSTRUCTORS

TABLE OF CONTENTS

PART 5 →

Key Personnel and Experience
Form T
Key Personnel Résumés

5. KEY PERSONNEL AND EXPERIENCE

GLX Constructors team members and key personnel have experience working together on large, complex transportation projects and with the MBTA. Our team was specifically formed to bring the best personnel together to design and build the Green Line Extension DB Project.

GLX Constructors has assembled a team of top industry professionals for the key positions needed to design and build the Green Line Extension DB Project. Our dedicated key personnel will work together to manage all aspects of the Project in a quality, timely, and effective manner to deliver the Project to the MBTA and stakeholders.

“GLX Constructors brings a senior DB management team with an average of 38 years of relevant experience.

The majority of this team, including John West, Jamie Doyle, Clyde Joseph, Mark Pelletier, Aaron Neely, and Lloyd Lovell have been working on the pursuit of this project since shortly after submission of our Letter Of Interest, with several having been dedicated full time since shortlisting. They have developed the necessary project knowledge, synergy and inter-personal relationships necessary in all successful teams, and will undoubtedly provide the MBTA with an outstanding combination of dedication, professional knowledge, experience and the partnering approach needed to make this project a success for all.

Each of the identified resources have demonstrated experience and expertise in producing quality work on large DB and/or light rail transit projects both locally and nationally. In addition, many of our key personnel have individually and collectively delivered rail projects in dense urban environments including active rail and integration with new and existing systems.

Highlights of our proposed key personnel and why their experience will bring value to GLX Constructors follow.

John West, Project Manager



- Extensive DB experience in the transportation industry
- Active rail corridor experience
- Experience working with proposed DBE Compliance Lead, Lloyd Lovell
- Stakeholder coordination
- Start-up, commissioning, and systems integration
- Title VI Program implementation

Percentage of Time Dedicated to the Project: **100%**

Chris Poe, Project Safety and Security Manager



- DB experience
- Urban transit experience
- Track record in safety improvement during construction
- Expert in development of large, complex projects with multiple stakeholders

Percentage of Time Dedicated to the Project: **100%**

Jamie Doyle, Construction Manager



- DB experience
- Local knowledge
- Experience working with MBTA
- Experience working with proposed Design Manager, Mark Pelletier
- Urban transit experience
- Large complex project experience

Percentage of Time Dedicated to the Project: **100%**

Mark Pelletier, PE, Design Manager



- Experience working with MBTA
- Local knowledge
- Experience managing large design teams
- Extensive rail transit experience
- Systems integration
- Start-up, testing, and commissioning experience

Percentage of Time Dedicated to the Project: **100%**

GV20170258-145.INDD

Bob Horn, Project Controls Manager



- DB experience in the transportation industry
- Experience working with proposed Design Build Coordinator, Michael Hoitink
- Rail transit experience
- 36 years of project controls experience

Percentage of Time Dedicated to the Project: **100%**

Aaron Neeley, Systems Integration Manager and Testing and Commissioning Manager



- DB experience
- Testing, commissioning
- Systems integration
- Tie in to existing systems
- Heavy rail mass transit and LRT systems installation

Percentage of Time Dedicated to the Project: **100%**

Sandro Plutino, Quality Manager



- DB experience in the transportation industry
- Experience working with proposed Design Build Coordinator, Michael Hoitink
- Rail transit experience
- Heavy civil construction experience

Percentage of Time Dedicated to the Project: **100%**

Hannah Brockhaus, Title VI Program Lead



- Title IV Program compliance
- Public involvement and public outreach specialist
- Experience with MassDOT
- Coordinates project meetings and community briefings

Percentage of Time Dedicated to the Project: **100%**


Hannah Carmical, EEO Compliance Lead



- Experience managing compliance with:
  - EEO Affirmative Action reporting
  - OFCCP
  - FHWA regulations for Federally assisted projects
- DB project experience

Percentage of Time Dedicated to the Project: **100%**

Lloyd Lovell, DBE Compliance Lead



- Experience working with proposed Project Manager, John West
- Title VI program compliance
- Alternative delivery experience
- DBE program development and implementation
- Rail transit experience
- Community outreach

Percentage of Time Dedicated to the Project: **100%**


Clyde Joseph, Project Executive



- Extensive heavy civil engineering and construction experience
- Extensive project management experience
- Extensive DB experience
- Experience with rail construction – heavy and light rail
- Quality management and strong safety management experience
- Stakeholder coordination

Percentage of Time Dedicated to the Project: **100%**

Michael Hoitink, Design Build Coordinator



- DB experience in the rail/transit industry
- Systems integration
- Experience working with proposed Project Controls Manager, Bob Horn
- Start-up, testing, and commissioning
- Urban environment
- Stakeholder coordination

Percentage of Time Dedicated to the Project: **100%**

GV20170258-145.INDD

STATEMENT OF COMMITMENT

GLX Constructors commits that the individuals designated as key personnel shall be available onsite in Boston for the duration of their work assignments to the extent within GLX Constructors' control.

FORM T – KEY PERSONNEL INFORMATION AND RÉSUMÉS

Please see attached Form T – Key Personnel Information and Résumés for GLX Constructors' proposed Key Personnel.

Form T

Key Personnel Information

FORM T

KEY PERSONNEL INFORMATION

Name of Proposer: GLX Constructors

Position	Name	Years of Applicable Experience	Education/ Registration	Parent Firm Name	Percent of Time Dedicated to Project
Project Manager	John West	45 years	B.S., Construction Management, Colorado State University	Herzog	100%
Project Safety and Security Manager	David (Chris) Poe	29 years	B.S., Occupational Safety and Health, Columbia Southern University A.S., Electrical Design/CAD Electronics, Eastfield College	Fluor	100%
Construction Manager	Jamie Doyle	35 years	MSCE, Construction Engineering and Management, Stanford University B.S., Mechanical Engineering and Architecture (Double Major), Yale University	Middlesex	100%
Design Manager	Mark Pelletier	34 years	B.S., Civil Engineering, University of Massachusetts	STV Incorporated	100%
Project Controls Manager	Robert (Bob) Horn	36 years	B.S., Industrial Management, Colorado State University	Fluor	100%

Position	Name	Years of Applicable Experience	Education/ Registration	Parent Firm Name	Percent of Time Dedicated to Project
Systems Integration Manager	Aaron Neeley	24 years	Business Financial Management, Cincinnati State University Theology, Old Testament History, Cincinnati Bible College Construction Estimating/Management, Red Rocks Community College Business Management/Law, Indiana University East Management Certification, Collin College, Frisco, Texas	Balfour Beatty Infrastructure, Inc.	100%
Quality Manager	Sandro Plutino	42 years	B.S., Construction Engineering, Italian Technical Institute, Vittorio Bottego	Fluor	100%
Title VI Program Lead	Hannah Brockhaus	4 years	B.S., Urban and Regional Studies/ Landscape Studies, Cornell University	Howard Stein Hudson Associates	100%
EEO Compliance Lead	Hannah Carmical	8 years	B.A., Art History, College of Charleston	Fluor	100%
DBE Compliance Lead	Lloyd E. Lovell	20 years	B.S., Business Administration, University of Phoenix A.A.S., Science/Industrial Management, NCC NY	Herzog	100%

Position	Name	Years of Applicable Experience	Education/ Registration	Parent Firm Name	Percent of Time Dedicated to Project
Testing and Commissioning Manager	Aaron Neeley	24 years	Business Financial Management, Cincinnati State University Theology, Old Testament History, Cincinnati Bible College Construction Estimating/Management, Red Rocks Community College Business Management/Law, Indiana University East Management Certification, Collin College, Frisco, Texas	Balfour Beatty Infrastructure, Inc.	100%
***Project Executive**	Clyde L. Joseph, PE	37 years	B.S., Civil Engineering, University of Washington	Fluor	100%
***Design Build Coordinator**	Michael Hoitink	15 years	B.S., Civil Engineering, Clarkson University	Fluor	100%

* Additional Committed Key Personnel

Use additional sheets when needed.

Key Personnel Résumés

JOHN WEST

Project Manager



Valuable Experience:
- ✓ Design-Build
- ✓ Light Rail
- ✓ Active Rail Corridor
- ✓ Large Project

Years of Experience:	45
Education:	B.S., Construction Management, Colorado State University
Professional License/ Certification:	Registered Professional Mechanical Engineer, California

John has extensive experience in the heavy/civil and track construction industry. As a project manager, he has overseen all aspects of nearly $3 billion in construction and transit projects. He is currently closing out the $876 million Silicon Valley Berryessa Light Rail Extension project in Milpitas, California. This DB project entails 10 miles of double track. He also completed the $438 million RTD West Rail Line project in Denver, Colorado, providing our team with a wealth of alternative delivery knowledge and leadership. He worked in close cooperation with the owner, designers, stakeholders, and other project members to deliver this project 8 weeks ahead of schedule.

DESCRIPTION OF COMPARABLE PROJECTS

Massachusetts Bay Transportation Authority, Green Line Extension CM/GC Project, Boston, Massachusetts. John served as the proposed project manager on the initial Green Line Extension CM/GC project. He was responsible for leading the proposal effort including refinement of project scope, budget, and schedule. John was responsible for selecting the best project team emphasizing critical aspects of the project. He also prepared for the project by quantifying work, developing design and construction alternatives, supporting DBE outreach efforts, soliciting subcontractors, and identifying potential risks.

Santa Clara Valley Transportation Authority, Silicon Valley Berryessa Extension, Milpitas, California. John served as project manager responsible for all design and construction coordination with the designer, owner, and the Bay Area Rapid Transit (BART) on this complex $867 million, design-build project. His primary responsibility was overseeing the trackwork and utility disciplines. The scope consisted of constructing 10 miles of double track, demolition of existing track, third-party relocates, and two stations. He was also responsible for coordinating the overall budget of the discipline and organizing constructability and value engineering concepts to better the project and the final product for the client.

Regional Transportation District, West Rail Line, Denver, Colorado. John served as project manager responsible for coordinating the proposal

REFERENCES

Jim Starling, PE
Former Project Manager
Regional Transportation District
Jacobs, 401 B Street, Suite 920,
San Diego, California 92101
303.819.4281
jim.starling@jacobs.com

Rick Clarke
Former Executive Director
Regional Transportation District
One Gateway Plaza, MS99-17,
Los Angeles, California 90012-2952,
303.299.218
clarker@metro.net

estimate, negotiating contract terms and conditions, leading preconstruction efforts, and managing the $370 million, 12.1-mile, LRT project through final completion. The project corridor was through a heavy urban area requiring extensive utility relocation and road re-routing. He managed successful project delivery, completing the project ahead of schedule and within budget, while overseeing a project staff of more than 300 employees and 100 subcontractors, including trucking. Mentored numerous DBE firms throughout the project making them stronger firms to build future projects.

Dallas Area Rapid Transit, Dallas Urban Circulator Streetcar System, Dallas, Texas. John served as project manager for this streetcar project centered in a heavily urban area of downtown Dallas, Texas. He held overall responsibility for acquiring temporary right of entry access for project activities on public and privately held owner property. Oversaw the day-to-day coordination with, and notification to adjacent property owners and businesses regarding the disruption due to the work scheduled. Many of the underground utilities were unknown or not marked in the correct locations, making this project more challenging. Herzog built the fixed trackwork, traction-power substations, OCS, and signaling systems. The extension was designed and built to allow the operability of the modern streetcars. The extension was a feeder line improving transit integration between the streetcar and light-rail system in downtown.

E-470 Tollway, Segments 2 and 3 Structures Design-Build, Aurora and Commerce City, Colorado. John provided executive oversight for the construction of all long span bridges on segments 2 and 3 of the tollway with an initial value of $63 million. Through the course of 3 years, John worked to develop a budget that would fit within the owner's revised bonding constraints. Once the project was funded, his team constructed 16 bridges in less than 2 years through a process of industrializing crews in specialized functions.

Colorado DOT, US 50 @ Salt Creek Bridge, Pueblo, Colorado. This was a 2-year project consisting of construction of four precast concrete girder bridges on US 50 over Salt Creek and the Union Pacific Railroad, which also included numerous cast-in-place and precast retaining-walls, storm drainage, creek channelization, roadway construction, water lines, electrical improvements, and signalization. As Operations Manager, John coordinated construction workers, subcontractors, general contractors, and architects. Prepared contracts and bids, estimated costs, made schedules, and ensured the project stayed within budget.

TARCO, Inc., US Highway 36/96th Street Interchange CM/GC, Broomfield, Colorado. Construction included a park-n-ride facility, bus lanes ZIP shuttle transit bridges, retaining walls, storm drainage, storm water-detention reservoirs, roadway construction, cast-in-place concrete-guardrail, new vehicular bridges, pedestrian underpass, lighting, and signalization. John worked with designers on constructability reviews and prepared preliminary estimates for design alternates. As the EVP, John mentored and managed team members, while developing client relationships.

GV20170258-156.INDD

DAVID (CHRIS) POE

Project Safety and Security Manager



Valuable Experience:
- ✓ Design-Build
- ✓ Urban Transit
- ✓ Development of large complex projects

Years of Experience:	29
Education:	B.S., Occupational Safety and Health, Columbia Southern University A.S., Electrical Design/CAD Electronics, Eastfield College
Professional Licenses/ Certifications:	Certified Safety Professional – CSP Certified Healthcare Safety Professional Commercial Driver's License – A CDL Virginia Master Electrician American Society of Safety Engineers

Chris has more than 29 years of health, safety and environmental (HSE) experience. His project experience includes heavy industrial construction, light rail/tunneling, track maintenance, and corporate experience as a vice president of safety and risk. Industries supported include highway, light ail, tunneling, power generation, chemical, petrochemical, telecommunications, manufacturing, and commercial construction. Chris has developed a people based safety program achieving zero harm for craft and subcontractor employees. He has experience with mining and tunneling projects for some of the world's leading mining companies such as Phelps Dodge and Barrick Gold and also for many light rail and subways projects for clients such as Los Angeles MTA; Washington Metropolitan Area Transit Authority (WMATA), Washington, D.C.; Sun Coast Parkway, Tampa, Florida; DART, Dallas, Texas, and I-895, Richmond, Virginia.

DESCRIPTION OF COMPARABLE PROJECTS

Mona Electric Group, Various Projects and Locations, Safety Director.
As safety director clients include DOD, Baltimore MTA, WMATA, Capital One, DC Water Authority, Amazon, and various other private clients. Assignment activities include managing two field safety managers, implementing fire protection and safety programs, developing training, and delivering statistical analysis to the principal ownership. Developed and implemented safety metrics that incorporated leading/lagging indicators, communication, and people based safety. Develop, implement, and review fire protection and HSE programs for continuous company improvement. Evaluate loss analysis trends to forecast anticipated future results. Develop operating budgets for fleet, safety, and claims and establish company goals to measure impact on implemented safety and risk programs.

REFERENCES

Bob Hegburga
Director of Safety Management,
Construction Risk Solutions, LLC
11311 McCormick Ep 4 Rd # 450
Hunt Valley, MD 21031
301.385.6315
bhegburg@thecrsteam.com

Mark Porter
Project Safety Manager,
Jay Dee Contractors Inc.
38777 Schoolcraft Rd,
Livonia, MI 48150
210.823.2084
mporter@jaydee.us.com

Jordan Foster Construction/Four Hats Inc., Various Projects and Locations, Vice President of Safety and Risk Management. Clients included CSX Railroad, Amtrac, UTEP, Texas DOT, El Paso Air Port Authority, Customs and Boarder Protection, and Department of Homeland Security. Supervised 16 remotely located safety professionals and one claims administrative assistant within the Jordan Foster and Four Hats operating districts. Responsible for auditing all federal, state, and local documentation requirements insurance lines and CCIP program for the company including purchasing insurance, broker/carrier relations, closure/subrogation of claims and assessment of financial risk, auditing placement and removal of traffic control devices on a daily basis, establishing lane shifts as directed client, and providing all equipment and devices for client worker protection while working in roadways. Conducted ATTSA certified Flagger training. Designed, implemented, and rolled out new safety programs designed to minimize risk and eliminate exposure for railroad, high rise, highway, refinery, pipeline, highway, and commercial/residential construction projects. Developed, organized, and monitored safety department operating budgets.

Fluor Barrick Gold, Pascua-Lama Gold/Silver/Copper Mine Project, Chile, Argentina, Senior Safety Manager. Managed up to 28 staff members and was responsible for the implementation of the HSE program for 3,000 Fluor and contractor personnel located at the project site. Developed and implemented safety metrics that incorporated leading/lagging indicators, communication, and people based safety. Developed, implemented, and ensured delivery of project required OSHA, MSHA, and Chilean law required training. Conducted "Tap Root" incident analysis for all near miss and incidents occurring on the project. Performed process/job hazard analyses, fire protection surveys, and environmental impact and storm water assessments and performed analysis of regulations against project needs so that designs complied with HSE and environmental regulations.

Hensel Phelps Construction Co, Various Projects and Locations in the Mid-Atlantic District, Safety Director. Clients included Baltimore MTA, WMATA, the Department of Defense, the U.S. Department of State, Digital Reality, Marriott, National Security Agency, and the U.S. Army Corp of Engineers. Supervised eight safety professionals on large, complex city infrastructure and transit projects. Responsibilities included assessment, development, and execution of risk management and fire protection programs. Performed planning and annual goal setting related to risk management and incurred claims (work comp, auto, general liability, and builders risk coverage). Managed and directed the day-to-day activities of the risk management effort to achieve strategic goals. Supported risk reporting for craft personnel and project teams. Developed and delivered fire protection and safety training for various aspects of construction and insurance risks.

GV20170258-157.INDD

JAMIE DOYLE

Construction Manager



Valuable Experience:

- ✓ MBTA
- ✓ Light Rail
- ✓ Large Construction Site

Years of Experience:	35
Education:	MSCE, Construction Engineering and Management, Stanford University B.S., Mechanical Engineering and Architecture (Double Major), Yale University
Professional License/ Certification:	Massachusetts Board of Building – Licensed Construction Supervisor (CS-023550)

Jamie has 35 years of construction experience, the majority of which has been in transportation and infrastructure construction project management.

His previous experience was as the joint venture Project Manager for the Massachusetts Bay Transportation Authority (MBTA) – Greenbush Commuter Railroad Design-Build (DB) Project. In addition to having completed a DB project with the MBTA, he also worked previously with the GLX Constructors' designer, STV, and partner, Balfour Beatty. In particular, Jamie has worked directly with proposed Design Manager, Mark Pelletier, and GLX Constructors' Executive Committee member, Roger Wilson.

In addition to his extensive civil and structural construction experience, he has a strong background in building work and harmonizing architectural requirements with the construction process. His transportation and infrastructure project management experience includes working in environmentally sensitive construction sites and within urban communities under tight schedules.

DESCRIPTION OF COMPARABLE PROJECTS

MBTA – Greenbush Commuter Railroad DB Project, Braintree to Scituate, Massachusetts, Project Manager. Jamie was responsible for design and construction of the Greenbush section of the Old Colony Railroad Rehabilitation Project. He managed construction of 18 miles of track and signal, including two cut-and-cover tunnel sections, five railroad and eight highway bridges (including three river crossings), 24 grade crossings, a maintenance facility, and seven stations through extensive wetland and suburban environments. This $338 million project was completed on schedule.

REFERENCES

Paul Hadley
Director MBTA
100 Summer Street
Boston, Massachusetts 02116
617.512.5999
PHadley@MBTA.com

Joe Allegro, P.E.
(Former MassDOT Director of Construction) President and Principal of Allegro Construction Services
11 Chestnut Square
Jamaica Plain, Massachusetts 02130
617.504.1735
jjallegro@comcast.net

Massachusetts Highway Department – Central Artery I-93 North Station Tunnel, Boston, Massachusetts, Project Manager. Jamie estimated and site managed the construction of the CA/T North Station Tunnel and Charles River Bridge south approach (C15A2). The project included construction of 1,100 feet of cut-and-cover tunnel sections and a 10 lane bridge approach through Boston's urban environment. The work included utility relocations, 420,000 square feet of slurry wall, drilled caissons, underpinning 1,600 feet of existing elevated I-93, installation of temporary traffic decks, support of excavation, 520,000 cubic yards (CY) of excavation, and 150,000 CY of CIP concrete.

Massachusetts Department of Transportation, Drawbridge Replacement Bridge – Beach Road over Lagoon Pond, Oak Bluffs-Tisbury, Massachusetts, Project Manager. Jamie oversaw the construction of replacement bascule bridge, including in-water installation of cofferdams, 10,000 linear feet (LF) of driven pipe pile, 8,000 CY of CIP concrete and erection of six fixed-structural-steel spans and one bascule span. Scope included installation and commissioning of a bridge machinery system. His responsibilities included logistic coordination (barge and tug transport) for all crews, materials, and equipment to off shore project site. This $40 million project was completed on schedule.

Massachusetts Highway Department – Central Artery Tunnel North Point Park Infrastructure Project, Cambridge, Massachusetts. Jamie managed all construction work on the Charles River including 100,000 CY of excavation (80,000 CY contaminated); construction of 1,000 LF of water features (dredge, liners, and rip rap); five bridges over the Charles River water feature; and 2,500 LF of pile supported granite masonry which relieved platform seawall, utilities, and roadway and park improvements. This $33 million project was completed on schedule.

Massachusetts Highway Department – Logan Airport I-90 Egress Ramps, Boston, Massachusetts, Project Manager. Jamie estimated and completed site management for construction of egress ramps at Logan Airport. This project included construction of a 2,000 foot CIP concrete post/tensioned viaduct, installation of utilities, and driven pile foundations and roadwork. This $36 million project was completed on schedule.

General Electric – Hudson River Sediment Remediation Phase I, Fort Edward, New York, Project Manager. Jamie was responsible for the dredging of hazardous materials from the Hudson River and associated canals. The project included mobilizing and demobilizing 17 dredges, 27 hopper barges, and 24 tug and crew boats, installing 4 miles of shoreline protection, driving and removing 120,000 square feet of sheet pile wall, dredging 302,000 CY of hazardous materials, and capping 460,000 SY. This $97 million project was completed on schedule.

GV20170258-125.INDD

MARK W. PELLETIER, PE

Design Manager



Valuable Experience:

- ✓ Experience working with the MBTA
- ✓ Local knowledge
- ✓ Experience managing large design teams
- ✓ Extensive rail transit experience
- ✓ Systems integration
- ✓ Start-up, testing, and commissioning experience
- ✓ Coordination with design build teams

Years of Experience:	34
Education:	B.S., Civil Engineering; University of Massachusetts
Professional Licenses/ Certifications:	Professional Civil Engineer: MA #34750 Professional Structural Engineer: MA #37343

Mark has spent the better part of his 34-year career at STV helping improve service for MBTA customers, particularly along the Green Line. He has overseen the North Station Transportation Improvement, Green Line Light Rail Accessibility Program, and Copley Station Accessibility Improvements, all of which were complex, multidisciplinary efforts that helped make the nation's busiest light rail system better. Mark is well-versed in all facets of engineering, including feasibility studies, design, permitting, and construction staging, but his greatest skill is his ability to communicate client goals to stakeholders and design teams. This quality made him well-suited to serve as design manager for the Greenbush Line Rail Restoration Design-Build, a challenging, 5-year assignment requiring day-to-day oversight of 100 design professionals and 15 subconsultant firms. Mark's on-site leadership was integral to Greenbush's 2007 launch and helped win STV the 2010 Gold Award for professional design excellence from the American Council of Engineering Companies of Massachusetts. He will commit to the same level of dedication for the duration of the Project.

DESCRIPTION OF COMPARABLE PROJECTS

MBTA, Greenbush Line Rail Restoration Design Build, Braintree, Weymouth, Hingham, Cohasset, and Scituate, Massachusetts, Design Manager. Mark oversaw the $320 million complete design, including engineering services and management of all design consultants, for the reconstruction of the out-of-service railroad ROW. He led the design for the 18-mile ROW construction and oversaw the design for a five-legged roundabout, the rehabilitation of 10 railroad bridges, and eight highway bridges, including substructure and superstructure replacement, as well as seven stations and 28 grade crossings.

MassDOT, Longfellow Bridge Rehabilitation Design Build, Boston and Cambridge, Massachusetts, Principal-in-charge. Mark is overseeing the $255 million design build effort to rehabilitate the Longfellow Bridge, a 2,135-foot structure that carries Route 3 and the MBTA's Red Line over the Charles River. As the lead designer, STV provided multidisciplinary design

REFERENCES

Michael O'Dowd
Senior Project Manager
MassDOT Highway Division
10 Park Plaza
Boston, MA 02116
857.368.9292
michael.o'dowd@state.ma.us

James Eng
Deputy Administrator of Rail Programs
MassDOT Rail and Transit Division
10 Park Plaza
Suite 4150, Boston, MA 02116
857.368.8963
james.eng@state.ma.us

services for the bridge, as well as plans for trackwork, traction power, communications, and signals for the Red Line. When complete, the bridge will be AASHTO compliant and ADA compliant. The design phase is complete and the firm is providing construction support services for the contractor.

MassDOT, Fore River Bridge Replacement Design-Build, Quincy and Weymouth, Massachusetts, Project Manager/Principal-in-Charge. Mark was responsible for the alternatives analysis, permitting, achievement of 60% design, and preparation of bridging documents for design-build procurement for the $245-million vertical-lift bridge of Route 3A over the Fore River. He is currently overseeing construction-phase services and design peer reviews on behalf of MassDOT.

MBTA, Wellington Carhouse Expansion and Improvements, Medford, Massachusetts, Principal-in-Charge. Mark oversaw the design development and final design services for the MBTA's $80 million expansion of the Wellington Carhouse. The firm designed a 12,000-sf single-bay addition to the east side of the building, as well as upgrades to safety and security, and the MEP/fire protection systems.

WRTA, Bus Maintenance, Operations, and Storage Facility, Worcester, Massachusetts, Principal-in-Charge. Mark oversaw the design and construction of a two-story, 150,000 sf operations and maintenance facility for the Worcester Regional Transit Authority (WRTA). The firm provided architectural, structural, MEP, fire protection, industrial, traffic, and civil design services for the $75-million facility. STV also assisted WRTA and their owner's project manager with the RFQ preparation and selection process to secure a CMR for this project, in accordance with Massachusetts General Law Chapter 149A.

MBTA, Green Line Copley Station Accessibility Improvements, Boston, Massachusetts, Project Manager/Project Director. Mark directed the $20 million accessibility improvements and general renovation of historic underground Copley Station. The improvements included rehabilitation of historic head houses, raising station platforms by 8 inches to accommodate the MBTA's new low-floor vehicles, adding ADA-compliant elevators at station platforms, and installing CCTV systems.

GV20170258-148.INDD

ROBERT (BOB) M. HORN

Project Controls Manager



Valuable Experience:
- ✓ Design Build
- ✓ Rail Transit
- ✓ Project Controls

Years of Experience:	36
Education:	B.S., Industrial Management, Colorado State University
Professional License/ Certification:	Association for the Advancement of Cost Engineering International (AACEI)

Robert has more than 36 years of experience in project controls including 30 years specific to projects in infrastructure and telecommunications. His responsibilities have included all planning, scheduling, estimating, and cost control functions over a wide range of infrastructure, telecommunications, petrochemical, and oil and gas projects including, commuter light rail, public safety emergency communications (911), and wireless and wireline networks.

DESCRIPTION OF COMPARABLE PROJECTS

Denver Regional Transportation District, Eagle P3 Commuter Rail Line, Denver, Colorado, United States. Robert was responsible for all project controls functions inclusive of cost management, schedule, progress, and change management for Denver Transit Partners. This P3 project has a complex structure with multiple LLC joint ventures supporting the design-build, rolling stock vehicle procurement, and operation and maintenance of 40 miles of a commuter light rail system. The project schedule was resource and cost loaded to support client billing and progress on an earned value basis. The cost control system (Timberline) was resource loaded for use in evaluating earned value to manage the work and produce weekly and monthly reporting. Monthly schedule and cost reporting responsibility included the client, LLC Boards, and project management.

Minera Yanacocha SRL, Conga Earthworks Project, Cajamarca, Peru, Project Controls Cost Lead. Robert served as the Project Controls Cost Lead in the front-end/set-up phase for the Conga Earthworks Team (CET), a Fluor-led joint venture formed to perform the heavy civil works for the Conga mining project. Overall scope consisted of permanent and temporary access roads, retention dams, and multiple platforms for the construction of the processing plant. He developed the work breakdown structure (WBS) and cost coding structure to manage the cost of the project and support reporting requirements of the client. This SAP based coding structure was used to convert and load the estimate from HCSS estimating software into the cost control system (FDCost). The progress system (MileMarker℠) was used to

REFERENCES

Gary Atchison
Project Controls Manager
RTD
1670 Broadway, Ste. 2700
Denver, Colorado 80202
303.299.2315
gary.atchison@rtd-denver.com

Monte Menard
Project Controls Manager
HDR
1670 Broadway, Ste. 3400
Denver, Colorado 80202
303.764.1520
monte.menard@hdrinc.com

provide production reporting to the field based on the quantities moved, and in using this information, the forecast for each area would be updated in the cost system. He established the invoice billing format and process, set up weekly and monthly cost related reporting, and prepared the cost sections of the PEP and PPM.

London Underground Limited, London Underground Connect, London, England, Cost Control and Estimating Lead. Robert provided lead cost control and estimating responsibilities from the project tender phase through project execution and closeout on the London Underground Connect project, a 20-year joint venture contract with EPCM responsibility for upgrading the radio and transmission networks throughout the London subway system. He developed and coordinated the estimate, program, and commercial and risk assessment input during the project tender phase. After award, he implemented and managed the cost control system and reporting process. He prepared periodic project detail estimates and provided estimating support and reviews. Robert also performed statistical risk and contingency assessments and participated in financial and commercial evaluations.

Fluor, Telecommunications Support, Irvine/Aliso Viejo, California, United States, Principal Project Controls Specialist. Robert served as the Principal Project Controls Specialist supporting the telecom business line/unit as project controls manager, lead estimator, and in general support of project controls execution on various projects and proposals. As Project Controls Manager, he was responsible for establishing and maintaining the project controls baseline, processes, and reporting for the following:

- City of Los Angeles, Public Safety System project, telecom engineering consulting services
- City of Los Angeles, Emergency Operations Center, architectural design services
- Nortel, Bell Mobility Canada project, project management oversight
- AT&T Wireless Services, Fixed wireless base station build out for 1,300 sites in six markets
- WorldCom, outside plant services
- Qwest, A&E design at 10 central office sites

He also served as Lead Estimator responsible for proposal estimating, scheduling, and pricing model support. Proposals of significant award included the Level 3 Network Expansion program, EPCM responsibility for fiber optic infrastructure to various sites within the United States, and the United Kingdom Highways Agency NRTS project which was a 10-year joint venture contract with EPCM responsibility for an integrated smart highway communications system across the United Kingdom road network.

GV20170258-123.INDD

AARON Q. NEELEY

Systems Integration Manager and Testing Commissioning Manager



Valuable Experience:

- ✓ Design-Build
- ✓ Large Light Rail
- ✓ System and Testing

Years of Experience:	24
Education:	Business Financial Management, Cincinnati State University Construction Estimating/Management, Red Rocks Community College Business Management/Law, Indiana University East Management Certification, Collin College, Frisco, Texas
Professional Licenses/ Certifications:	IBEW member. Journeyman Line Tech Classification through IBEW Local 71 Columbus, Ohio IMSA Level I, Level II and Work Zone Safety Project Manager Training, 6-month program, with Aldridge Electric Leadership Training, Giant Leap Consulting 30-hour OSHA Certification OST Crane and Rigging certification Completed training in NFPA 70, Excavation Competent Person, Confined Space, Railroad Safety, First Aid CPR, Cable Splicing, Fiber Splicing.

Aaron has 24 years of experience focused on heavy rail mass transit and LRT systems installation and rehabilitation. He has experience in design and design verification, procurement, installation, testing, and integration of overhead catenary, overhead conductor bar, third rail traction power, traction power substations, automated train control (relay and microprocessor based), and communications/SCADA (fiber and copper networks). Aaron has served as systems integration manager on several design build LRT projects including the Regional Transportation District's 2.3-mile, double track Southeast Rail Extension project.

DESCRIPTION OF COMPARABLE PROJECTS

Denver RTD, Southeast Rail Extension, Denver, Colorado, System Integration Manager. Aaron served as Systems Integration Manager for this $138 million, 2.3-mile, double track, design-build, LRT extension that connects three existing lines in metropolitan Denver. This project is a combination of aerial direct fixation track and at-grade ballasted track. The project includes

REFERENCES

Stuart Johnson
Project Manager
Paragon Project Resources Inc.,
(Project Management for DART)
1901 Royal Lane, Suite 104
Dallas, Texas 75229
214.325.7078
sjohnson@dart.org

Leo Himmel, Jr.
Senior Project Manager
(Former DART Systems
Construction Manager)
Jacobs
1593 Springhill RD Suite 300,
Vienna, Virginia 22182
508.801.7265
lmhjr@hotmail.com

three aerial structures (including on bridge over Interstate-25); three at-grade stations; a parking structure; OCS, a traction power substation, communications and signal systems.

Los Angeles County Metropolitan Transportation Authority (Metro) Crenshaw, LAX Project, Los Angeles, California. This is a $1.3 billion, 8.5-mile, double track, design-build, light rail connecting to the existing Green Line and terminating underground beneath the Exposition Station on the Blue Line. Aaron provided systems integration oversight. The $120 million systems subcontract consist of overhead catenary (SCAT and conductor rail), traction power substations, automated train control, and communications/SCADA systems.

Metro Westside Phase I Purple Line, Los Angeles, California, System Construction Manager. Aaron was responsinble for the $1.3 billion, 3.9-mile design-build subway extension from Wilshire/ Western Station to the new Wilshire/La Cienega Station. The systems subcontract included, traction power substations, connections to third rail, automated train control, and communications/SCADA systems.

Sound Transit Seattle S440 South Link Extension, Seattle, Washington. This was a $169 million project ($15.4 million systems) design-build contract providing a 1.8-mile aerial guideway extension south from SEATAC International Airport. The systems subcontract included two new traction power substations, new OCS (SCAT), automated train control, and communications/SCADA. Aaron was assigned as Interim Project Manager for seven months until the Tucson project staff completed their work.

Dallas Area Rapid Transportation (DART) Blue Line Expansion, Dallas, Texas, System Construction Manager. The project was a $188 million ($21 million systems) 4.8-mile design-build expansion of DART's Blue Line from Garland to Rowlett. The new line is comprised of double LRT track incorporating four at grade road crossings; one interlocking, block signal indicators; approximately 4500 feet of aerial structures; and one new light rail station. Aaron served as the Systems Construction Manager with responsibility for the installation and testing of the automated train control, communications, OCS (SCAT), and traction power substation systems.

GV20170258-126.INDD

SANDRO PLUTINO

Quality Manager



Valuable Experience:

- ✓ Extensive DB
- ✓ Urban Transportation
- ✓ Experience Implementing Quality Programs for Large, Heavy Civil Construction Projects

Years of Experience:	42
Education:	B.S., Construction Engineering, Italian Technical Institute, Vittorio Bottego
Professional Licenses/ Certifications:	NICET IV – Highway Construction (#74648) NJDOT Certificate of Completion – Traffic Control for Streets and Highway Construction and Maintenance Operations ATSSA – Traffic Control Supervisor (#00174457) NJ Society of Asphalt Technologists – Asphalt Paving Technologist VDOT Pavement Marking VDOT HCC Field VDOT Asphalt Concrete Field VDOT Slurry Surfacing VDOT Surface Treatment VDOT Soil and Aggregate Compaction DCR – Erosion & Sediment Control LADOTD – Structural Concrete Inspector LADOTD – Cement Concrete Pavement Inspector ISO 9001/2008: BSI/Internal Quality System Auditor (#7524990-83787)

Sandro possesses 42 years of quality control, field engineering, and construction management experience on major public projects involving all aspects of heavy civil construction. His most recent experience as Quality Manager and Quality Assurance Manager on the 95 and 495 Express Lanes, both large scale urban P3 projects, demonstrates his extensive knowledge of roadway and structure's construction methods, project controls techniques, procedures and practices, materials use and performance, environmental, and safety responsibilities related to transportation facilities.

DESCRIPTION OF COMPARABLE PROJECTS

Purple Line, Bethesda, Maryland, 95 Express Lanes, Fairfax County, Northern Virginia, Quality Assurance Manager. The I-95 Express Lanes is a design-build project to modify existing High Occupancy Vehicle (HOV) lanes into new High-Occupancy Toll (HOT) lanes on a 23 mile segment of I 95, with an additional eight miles of new extension. As the quality manager, Sandro has the overall responsibility for the implementation and management of

REFERENCES

John Moore, PE
Construction Manager
CH2M
16363 Walker Lane, Suite 500,
Alexandria, Virginia 22310
703.269.8166
John.morse@CH2M.com

Garrett W. Moore, PE
Chief Engineer
Virginia Department of
Transportation
14975 Alliance Drive
Fairfax, Virginia 22030
804.786.4798
Garrett.moor@VDOT.virginia.gov

the quality process as defined in the project Quality Management System Plan (QMSP) for both quality control (QC) and quality assurance (QA). Sandro manages all quality functions on the project, internal and external audits, statistical summaries of testing results, implementation of training programs, development, and implementation of specific project procedures to assure that contract requirements are met. Sandro is also accountable for the monthly status report of construction quality, report of deficiencies, and non conformances, and promoting awareness of the program.

I-495 Express Lanes, Fairfax County, Northern Virginia, Quality Assurance Manager. This design-build project introduced new high-occupancy toll (HOT) lanes to 14-mile segment of Capital Beltway (I 495). As the QA manager, Sandro led the QA effort to insure that the minimum QC/QA requirements established by the Virginia Department of Transportation (VDOT) for design-build and Private Public Transportation Act (PPTA) projects were met. Sandro was additionally responsible for managing the QA inspection, testing, and controlling, maintaining the QMSP and VDOT materials notebook, preparing audit checklists and reports, weekly and monthly status reports of construction quality, deficiencies and non-conformances, as well as promoting awareness of the program.

Pocahontas Parkway, Richmond, Virginia, Quality Assurance Manager. Sandro was responsible for providing the overall quality assurance and compliance of construction activities related to the approved drawings, specifications, and other similarly related documents. Additional responsibilities included management of two independent materials testing agencies, review of materials test requirements, and his recommendation to accept or reject materials and constructed elements. Sandro was responsible from time of discovery to resolution, of all materials and finished elements incorporated in the project and identified as a deficiency by Non Conformance Reports (NCRs).

Routes 40 and 322, Section 3K, Egg Harbor Township, New Jersey, Resident Engineer. Sandro is responsible for this $7 million reconstruction and widening effort. As Resident engineer, he coordinated the extensive utilities relocation effort and the new utility installation work, with full authority to provide plan changes for unexpected utility conflicts, and for the resolution of field construction problems and design issues. The project encompassed wide-ranging coordination of utility companies to minimize impact to residents and businesses along Routes 40 and 322, Section K.

GV20170258-158.INDD

HANNAH BROCKHAUS

Title VI Program Lead



Valuable Experience:
- ✓ Local
- ✓ Title VI Compliance
- ✓ Public Involvement

Years of Experience: 4

Education: B.S., Urban and Regional Studies/Landscape Studies, Cornell University

Hannah is a Public Involvement Specialist with project experience including the Mount Auburn Street Corridor Study, Allston I-90 Interchange Improvement Project, and the Casey Arborway Project. She has worked in active transportation, affordable housing, and community development; and she is able to effectively communicate complex project details to the broader public. Hannah's work shepherding projects, from conceptual design through construction, ensure a public process that can move forward in a timely and efficient manner.

DESCRIPTION OF COMPARABLE PROJECTS

Massachusetts Department of Transportation, I-90 Toll Plaza Demolition and Roadway Reconstruction Project, Massachusetts. In providing meeting presentations for the project website of this high-profile project, Hannah ensures Title VI compliance as well as web accessibility. The stakeholder notification process ensures full notice to local community groups, including groups with limited to no English proficiency, across the state.

Department of Conservation and Recreation (DCR), Mount Auburn Street Corridor Study, Cambridge/Watertown, Massachusetts. The objectives of this study are to identify improvements to safety, comfort, and operations for all modes of transportation that use the roadways in the traffic study area. Currently serving as a public involvement specialist, Hannah works closely with DCR staff and the project team to coordinate public outreach and project messaging. She also develops materials for meetings and the project website, manages public input, and manages the stakeholder database. In addition, she leads the documentation of the outreach process, including creating detailed meeting minutes, and thus has managed Title VI compliance.

Massachusetts Department of Transportation, Allston I-90 Interchange Improvement Project, Allston, Massachusetts. This multimodal transportation project will vastly improve cycling and pedestrian conditions in Allston, recreate a rail transit link to downtown Boston, and reconnect Allston to itself and the Charles River while processing vehicles effectively, ensuring that highway traffic does not leak onto residential streets. Hannah works with

REFERENCES

Anne Fiesinger
Director of Public Outreach
Department of Conservation and Recreation
251 Causeway Street, 9th Floor
Boston, Massachusetts 02114
617.626.1312
anne.fiesinger@massmail.state.ma.us

Michael J. O'Dowd, PE
Design Project Manager
MassDOT
10 Park Plaza
Boston, Massachusetts 02116
857.368.9292
michael.o'dowd@state.ma.us

the design team to bring information to the community and coordinate input gathering as the project moves through the environmental phase. She has ensured all information presented during public and task force meetings is fully accessible, including PowerPoint presentations, draft roll plans, and draft construction staging diagrams.

Massachusetts Department of Transportation, North Washington Street Bridge Replacement Project, Boston, Massachusetts. The goal of the project is to replace the structurally deficient North Washington Street Bridge with a new structure that will create a bridge that is livable, walkable, green, and multi-modal. Hannah coordinates project meetings and community briefings, creates detailed meeting minutes, and manages the stakeholder database for the project. She also manages accessibility compliance for all presentations and minutes.

Massachusetts Department of Transportation, I-95 Add-A-Lane, Needham/Wellesley, Massachusetts. Hannah is providing public involvement support on this project, which will add an additional travel lane and shoulder to I-95 north and southbound, upgrade and create new interchanges for safer and more efficient movements on and off the highway, and provide new collector-distributor roads to minimize weaving movements. Hannah's work has included producing materials for the project website, such as graphics, briefings, and email blasts, in addition to producing detailed meeting minutes for public meetings. She has worked closely with MassDOT web services staff to ensure Title VI compliance for all information uploaded to the project website, including meeting presentations and construction detour maps.

Massachusetts Department of Transportation, Casey Arborway, Boston, Massachusetts. MassDOT gathered an interdisciplinary team of engineers, planners, and urban design professionals to determine how best to replace the structurally deficient Casey Overpass. Located in the Jamaica Plain neighborhood, the Casey Overpass carries Route 203, locally known as the Arborway, and a primary east-west connecting route in the area over Forest Hills, a commuter hub including major north-south roadway, bicycle, pedestrian, and transit connections. Hannah ensures Title VI compliance in all public outreach activities, including construction and traffic shift notices and meeting documentation. Standard practice includes providing Spanish translations of meeting notices, as well as fully accessible documents for the project website.

GV20170258-124.INDD

HANNAH CARMICAL

EEO Compliance Lead



Valuable Experience:
- ✓ EEO Compliance
- ✓ EEOC Training
- ✓ Managing Diversity

Years of Experience: 8
Education: B.A., Art History, College of Charleston
Professional License/ Certification: PHR SHRM-CP

Hannah has more than 8 years of professional experience in the Nuclear Power, Government, Commercial, and Infrastructure business lines. Most recently, Hannah served as the HR/EEO Compliance Officer for the New York State Thruway Authority's Tappan Zee Hudson River Crossing project for Fluor. Additionally, Hannah has worked as a human resources generalist for Fluor's Corporate Health, Safety and Environmental (HSE) division. Her responsibilities have included overseeing corporate and field HSE employees, both international and domestic, leading the coordination team under the Talent Acquisition Group (TAG), upholding overall work processes within the TAG coordination group with continued alignment within Fluor Human Resources (HR), developing and implementing desktop procedures, and practices pertaining to the vendor and client submittal process.

DESCRIPTION OF COMPARABLE PROJECTS

New York State Thruway Authority, Tappan Zee Hudson River Crossing Project, Tarrytown, New York, United States, Human Resources Manager.
As the human resources manager, responsible for providing EEO Compliance Support and guidance to the project for all members of the LLC, their staff and direct hire union craft. Responsible for development of project specific procedures and policies for implementation (Employee Work Rules, HR Section of Project Procedures Manual, HR Management Plan, Workforce Participation Plan). Work with project management to fulfill contractual and partnering agreements related to HR, including: EEOC and Affirmative Action reporting, OFCCP and FHWA compliance for Federally Assisted Projects, Davis-Bacon requirements, staffing management, employee relations and policy implementation and enforcement. Responsible for the onboarding of craft new hires (orientation, processing paperwork, E-Verify, SAC, MVR, training documents, certification management), administering new hire orientation for Fluor employees and development and implementation of project orientation for all project hires. Work with HSE to ensure proper compliance regarding safety practices and developing project specific vehicle and motor vehicle records policies to help mitigate risk. Partner with labor relations for union hires and dispute resolution. Understanding of Project Labor Agreement (PLA)

REFERENCES

Tracey Mitchell
Diversity Compliance Manager
NYS Thruway Authority
303 S. Broadway Tarrytown, NY
10591
914.524.5482
Tracey.Mitchell@newnybridge.com

John Kowalski
Commercial & Contracts Directors
NYS Thruway Authority
555 White Plains Road, Suite 400
Tarrytown, NY 10591
914.524.5440
John.Kowalski@newnybridge.com

and specific Collective Bargaining Agreements (CBA) for unions present on project. Partner with project controls and business services to track and properly forecast HR specific project budgets and ensure overall compliance by member employees.


Fluor, Human Resources, Greenville, South Carolina, United States, HR Generalist and ETWeb Administrator for corporate HSE. Responsible for tracking and retaining HSE employees, international and domestic, for all SBU's, performance assessment administration, coordinating assignments and relocations, processing LOA's, separations and terminations, general recruiting duties, maintenance of internal and external bench list and weekly placement activity report and the development and implementation of the corporate HSE internship program. Supported all projects regarding HSE staffing efforts and HR issues that pertained to HSE employees. Supported corporate HSE (20) and field HSE (500) employees on all HR issues, provided problem resolution, and timely feedback. Worked with business unit leads regarding staffing augmentation and management of HSE employees and resources; including managing PA supervisors and approvers, cost center and org unit alignment, compensation reviews, out of cycles, general benefits inquiries, annual salary and hierarchy reviews, training and development, and all other general HR administrative issues.

Fluor Government Group, LOGCAP IV Overview, Greenville, South Carolina, United States. Provided home office coordination support for the LOGCAP IV Project, taking on the recruiting coordinator lead role in the summer of 2010. Responsible for work load distribution for a team of three and overall guidance and oversight for a team of eight coordinators, HR technicians and specialists working in Greenville and Houston. Worked closely with recruiting, HR, the CONUS Replacement Center (CRC), and industrial security to manage incoming candidates for the LOGCAP IV Task Orders. Responsible for tracking candidate progress and providing metrics throughout the hire process. Project Assignment Tracking System (PATS) power user for recruiting. Responsible for working with information services to develop and implement improvements to PATS, including providing guidance on recruiting work process flow to allow for a more intuitive system. Prepared weekly reports from PATS, identifying candidates cleared for hire and insuring government compliance. Worked with quality to develop the LOGCAP IV HR process flow in reference to the coordination process. Provided guidance on the background investigation process, working with legal and functional HR to maintain compliance with Fluor policy and consistency with final determinations regarding background discrepancies.

GV20170258-128.INDD

LLOYD LOVELL

DBE Compliance Lead

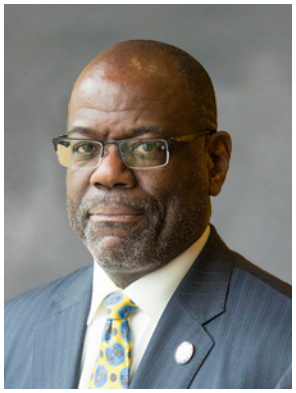

Valuable Experience:

- ✓ DBE Implementation
- ✓ Outreach Event
- ✓ DBE Plan Development

Years of Experience:	20
Education:	B.S., Business Administration, University of Phoenix A.A.S., Science/Industrial Management, NCC NY
Professional License/ Certification:	PHR SHRM-CP

Lloyd has 20 years of experience in designing, developing, implementing, and managing small, minority, women, and disadvantaged business enterprise programs (DBE) in the United States and the Caribbean. His experience includes administering contract compliance programs, small and local preference, vendor relations, and coordinating, supervising, and implementing comprehensive outreach and technical assistance programs that inform and prepare vendors for business opportunities. His clients include public and private sector businesses, Fortune 100 companies, local governmental agencies, housing authorities, as well as construction management and program management firms.

DESCRIPTION OF COMPARABLE PROJECTS

City of Kansas City, Kansas City, Missouri, Kansas City Downtown Streetcar CM@Risk. This starter project entailed the construction of 4 round trip miles of track for Kansas City. The project included major water and sewer relocations, 18 platform stops, traffic signal and street lighting, four TPSS substations, OCS system, and a new three-bay vehicle maintenance facility. Herzog was the Managing Partner of the joint venture for this $88 million project. The pre-construction phase lasted four months, in which multiple estimates and value engineering were performed. Lloyd was responsible for maximizing DBE and workforce participation throughout pre-construction and construction phases of the project. He coordinated technical and administrative support for DBE firms in accordance with 49 CFR Part 26 and monitored opportunities for additional DBE participation. Lloyd interfaced with KCMO City Staff, initiated, and reported on outreach activities. He provided updates on DBE participation percentages, identified additional opportunities as necessary, and monitored and managed all DBE subcontractors with regard to DBE and workforce compliance. Lloyd sees himself as an extension of every DBE Firm working on this project and stands ready to assist them with any DBE related or workforce goal questions, whether it be technical or administrative.

REFERENCES

Mr. Terry Nolan
General Manager
Highlands Ranch Metro District
62 W. Plaza Drive, Highlands Ranch
Colorado 80129
303.785.0320
tnolan@highlandsranch.org

Phillip Yelder
Director, Human Relations Department
City of Kansas City
4th Floor, City Hall, 414 East 12th Street
Kansas City, Missouri 64106
816.513.1801
hillip.yelder@kcmo.org

Regional Transportation District, Denver, Colorado, West Rail Line CM/GC. Under the direct supervision of the CM/GC project manager (John West), Lloyd directed, developed, and administered all aspects of the disadvantaged business enterprise program and oversaw all activities of the small and local business enterprise program. He maintained ongoing relationships between the Owner, external business organizations, and community organizations, advising them of opportunities to meet and exceed the 18 percent DBE goal by 6 to 24 percent and paying out $79 million to 90 local DBE firms. This was a $438 million CM/GC project that involved the construction of a 12.1-mile light rail extension with 12 stations and numerous bridge structures from Denver westward to Golden in Jefferson County.

Highlands Ranch Community Association, Highlands Ranch, Colorado, Community Manager. This was one of the largest master planned communities in the United States valued at $1.5 billion. It includes home ownership units, market rate rental, retail, commercial, office development, cultural centers, a town center, schools, RTD park-n-ride facilities, RTD bus shelters, libraries, parks and open-space trails, and recreation facilities. Lloyd served as Community Manager and was responsible for working with the Colorado Department of Transportation, the Denver Regional Council of Governments, the RTD board of directors and staff, the Douglas County School Board, the Master Developer (Mission Viejo Company, later Shea Homes), the Highlands Ranch Community Association board of directors, community residents, and groups, vendors, builders, and other stakeholders. He was responsible for managing the Highlands Ranch Community Association consisted of 20,000 units (47,000 residents) and four facilities. Additionally, Lloyd met with community residents, groups, vendors, and contractors to interpret, clarify, and discuss HRCA policies, goals, and objectives. Further, he was responsible for interfacing with HRCA finance, architectural, development, future facilities, vendor/contractor management groups, management information systems, and recreational advisory committees on all related development activities.

Ben & Jerry's Ice Cream, Caribbean, International. Responsible for all aspects of the design, development, implementation, and administration of disadvantaged business development programs, including vendor relations, community outreach, and using radio and newspapers to prepare vendor(s) for business opportunities in the distribution and marketing of Dreyer's/Edy's/Ben & Jerry's Ice Cream products throughout 21 Caribbean countries.

GV20170258-129.INDD

CLYDE L. JOSEPH, PE

Project Executive



Valuable Experience:
- ✓ Heavy Civil Project
- ✓ Railroad, Bridge, and Tunnel
- ✓ Project Management

Years of Experience:	37
Education:	B.S., Civil Engineering, University of Washington
Professional Licenses/ Certifications:	PE in Idaho (#5564 July 1987) PE in Tennessee (#19957 July 1988)

Clyde has more than 37 years of project engineering, project management, construction, and design management experience in heavy civil infrastructure projects, including railroad construction, tunnel construction, bridge and highway construction, and all types of utility construction. The majority of this time has been spent with railroad, bridge, and tunnel construction which will provide valuable experience and leadership to the Green Line Extension Project. He has a proven record of people management and mentorship, schedule and cost management, quality management, and strong safety management and results. The variety of his experience in all aspects of infrastructure projects will provide valuable capabilities to the management and execution of the Project.

Much of Clyde's experience has been in the proposal and procurement of heavy civil projects followed by management of those projects from start-up to completion. This management experience has included the design, estimating, construction, client approvals, public and local municipality outreach, contract modifications and negotiations, contract plans, and submittals and final acceptance documents.

DESCRIPTION OF COMPARABLE PROJECTS

Fluor, Infrastructure, Aliso Viejo, California, Senior Project Director. His current responsibilities include proposal preparation and review, estimate review, and executive management review for design build projects in excess of $1 billion in value.

Tutor Saliba/Tutor Perini Corp., Various Projects and Locations, Engineering Manager. As engineering manager on the SR99 Bored Tunnel Project in Seattle, Washington, responsible for project start-up, all engineering operations for the project, management of the designer on behalf of the design-build joint venture. Supervised a staff of 20 engineers and oversaw the design staff of 90 design professionals (50%). Served as operations manager/ lead senior estimator on successful proposals for construction of the Caldecott Tunnel 4th Bore, the New Irvington Water Tunnel, and the SR99 Bored Tunnel Alternative Project in Seattle, Washington. Support Senior Estimator on I

REFERENCES

Patrick McCormick
Construction Manager
Sound Transit Center
13427 NE 16th Street,
Bellevue, Washington 98005
206.903.7338
pat.mccormick@soundtransit.org

Matt Preedy
Deputy Director – Construction Management
Sound Transit Center
625 Union Station
Seattle, Washington 98104
206.398.5438
matt.preedy@soundtransit.org

215 Beltway Project, Warm Springs Cut and Cover Tunnels, JFK Runway reconstruction, I-5 Bridge Replacement over Lake Shasta, LAX Crossfield Taxi Way Construction, and the Transbay Terminal Support of Excavation Project.

American Civil Constructors, Various Projects and Locations, Vice President and Regional Manager. Vice President and Regional Manager VP/GM requiring transition from management change out, managing existing $65 million budget, staff reorganization, change in corporate organization, procurement of new works to support ongoing operations, and profit/loss responsibility.

P&L responsibility included the following:

- Locate, estimate, bid, and procure process of 145+ projects with hit ratio of one in 5. Procured over $60 million in new projects in 14-month time frame with anticipated margin of $11 million.
- Work concentration of 60 percent marine works and 40 percent inland foundations and structures.
- Geographical area covered Washington, Alaska, British Columbia, and Idaho.

Merco, Various Projects and Locations, Vice President and Chief Engineer. Mr. Joseph is responsible for all engineering and estimating functions of company. Estimated/bid on 60+ projects on yearly basis while managing or overseeing project execution.

Kern River PH1 Tunnel Rehabilitation Project, Bakersfield, California, Project Executive. Mr. Joseph is project executive on rehabilitation of 10 miles of water tunnel and reconstruction of Intake structure on 4 unit, 36 MW power plant.


- Project executive on drainage tunnel rehabilitation project under N/S railroad.
- Project executive on NJDOT Bridge at Hope Road including redesign of precast structure to cast in place concrete arch bridge to match adjacent historic concrete arch bridge. Initial precast design was not feasible to construct. Negotiated major change to the contract including outside design services.

Project executive on the New Jersey Transit Bergen Tunnel. This $67 million project required enlarging the existing tunnel and new concrete liner and major electrical installation.

GV20170258-067.INDD

MICHAEL L. HOITINK, PE

DB Coordinator

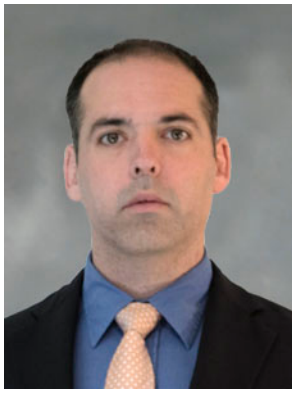

Valuable Experience:

- ✓ Design Build in the Rail/Transit Industry
- ✓ Systems Integration
- ✓ Stakeholder Coordination

Years of Experience: 15

Education: B.S., Civil Engineering, Clarkson University

Professional License/ Certification: Registered Professional Civil Engineer, Maryland

Michael has 15 years of experience in the management and design of transit, highway, drainage, and utility projects in locations across the country for various government and public agencies and institutions. His responsibilities have included design management, planning, geometric and project development, preparation of design documents including specifications, as well as coordination of diverse engineering disciplines, third parties, and offices. Since joining Fluor 4 years ago, Michael has served as the design-build coordinator and engineering manager for the design build of a new 36-mile commuter rail system in an urban area with heavy traffic congestion, two operating railroads, and more than 900 utilities requiring relocation. Currently, he is the engineering manager on the design build of a 22-mile freeway project for a state department of transportation.

DESCRIPTION OF COMPARABLE PROJECTS

Arizona Department of Transportation, Loop 202 South Mountain Freeway (Phoenix, Arizona). Michael serves as Engineering Manager for the Design Build of a 22-mile freeway that will complete the Loop 202 and Loop 101 freeway system, provide a direct link between the East Valley and West Valley, and an alternative to Interstate 10 through downtown Phoenix. He is responsible for managing the completion of the base scope design, as well as planning and implementation of the design services during construction scope. He serves as the primary point of contact for the client and any third parties to manage any design-related items. The project includes construction of a 15 foot wide multi-use trail along a portion of the existing alignment.

Regional Transportation District, Eagle P3 Commuter Rail Line (Denver, Colorado). Michael served as Engineering Manager and Design Build Coordinator for a new 36 mile system comprised of three separate commuter rail lines, 14 stations, 66 rail cars, and a 230,000-square-foot LEED certified maintenance facility. Project elements included installation and integration of infrastructure elements (roadway, track, stations, and structures), system elements (traction power, power supply, train control, signals,

REFERENCES

John Moore, PE
Construction Manager
CH2M
16363 Walker Lane, Suite 500,
Alexandria, Virginia 22310
703.269.8166
John.morse@CH2M.com

Garrett W. Moore, PE
Chief Engineer
Virginia Department of
Transportation
14975 Alliance Drive
Fairfax, Virginia 22030
804.786.4798
Garrett.moor@VDOT.virginia.gov

communications, and SCADA), and rolling stock. It is the first commuter rail system in the United States to have positive train control built into it from the ground up and not retrofitted.

Virginia Department of Transportation, 495 Express Lanes (Fairfax, Virginia). Michael served as Post Design Services Manager leading the engineering team responsible for budget forecasts, staffing estimates and scheduling, contract modifications, and providing engineering solutions to the field for the Design Build of high occupancy toll lanes along 14 miles of the Capital Beltway. He also served as the deputy design manager, lead signing engineer, and production center deputy manager. He coordinated and scheduled 60 design packages for area one that included three major arterial-to-interstate interchanges, 28 lane miles of new highway, and 22 bridges. Among his responsibilities were the ITS infrastructure and electronic tolling design on freeway and arterial routes, including detailed layout of ITS power distribution and communication network. He prepared Design Build engineering plans for traffic management, electronic tolling based on real-time traffic conditions, and ITS equipment power distribution. For 2 years, he led ITS subdisciplines in post design services and was responsible for quality management of ITS design changes during construction.

Virginia Department of Transportation, I 66 Spot Improvements (Northern Virginia). Michael served as Project Engineer responsible for supporting the widening of 2 miles of interstate highway, performing design calculations including super elevation, gore design, horizontal and vertical alignments, and cross section design.

Utility Distribution and Site Work Engineering Projects (Multiple Locations, United States). As project engineer, Michael was responsible for planning, design, and construction oversight on institutional campuses for varied projects, such as chilled water upgrades, campus-wide gas upgrade, parking garage expansion, master utility plans, and storm water management plans.

GV20170258-232.INDD



Response to the Request for Proposal

for the Green Line Extension Design Build Project

Submitted to

Massachusetts Department of Transportation and The Massachusetts Bay Transportation Authority

Part 7– Appendix A – Alternative Technical Concepts

GLX CONSTRUCTORS

TABLE OF CONTENTS

PART 7 →

ATC No. 12

ATC No.12 Preliminary Submission

ATC No.12 MBTA Acceptance of Preliminary Submission

ATC No.12 Formal Submission

ATC No.12 MBTA Acceptance of Formal Submission

ATC No. 35

ATC No.35 Preliminary Submission

ATC No.35 MBTA Acceptance of Preliminary Submission

ATC No.35 Formal Submission

ATC No.35 MBTA Request for Clarification

ATC No.35 Response for RFI 1

ATC No.35 MBTA Conditional Acceptance of Formal Submission

ATC No. 36

ATC No.36 Preliminary Submission

ATC No.36 MBTA Acceptance of Preliminary Submission

ATC No.36 Formal Submission

ATC No.36 MBTA Acceptance of Formal Submission

ATC No. 43

ATC No.43 Preliminary Submission

ATC No.43 MBTA Acceptance of Preliminary Submission

ATC No.43 Formal Submission

ATC No.43 MBTA Acceptance of Formal Submission

ATC No. 12

ATC No. 12

Preliminary Submission

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

PRELIMINARY

ALTERNATIVE TECHNICAL CONCEPTS

("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

GLX CONSTRUCTORS PRELIMINARY ATC FORM

ATC 12 – USE OF TWO OCS POLES ON VIADUCT

Sections A though E below must be completed to submit a Preliminary ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Preliminary ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. General Description

A general description (not to exceed two pages) of the Preliminary ATC, how the ATC will be used on the Project, the proposed location of the ATC, and any other pertinent information that would provide a clear understanding of the potential ATC;

The Contract Documents specify a single OCS Pole between the tracks on the new viaduct structure which result in a wider deck structure. By using two OCS Poles on the outside of the tracks on the viaduct structure, viaduct deck width will be reduced and result in decreased deep foundation dead loads.

B. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC and an explanation of the nature of the deviations from said requirements;

The tracked changes below, are our explanation of the changes that would be required for this ATC.

Volume 2, Technical Provisions, Section 11.2.3.4 Poles and Foundations "OCS poles shall be located between **or on the outside** of the tracks on the new viaduct structure~~**. except at junctions where they may be located at the sides of the track.**~~ On single track curves on the viaduct structure, the poles shall be located on the outside of the curve."

C. Benefits

Any potential benefits or implications of incorporating the Preliminary ATC into the Project, including in right-of-way acquisitions, rail operations, and routine or capital maintenance, and other Project risks;

A reduction in the new viaduct deck width will reduce the substructure foundation dead loads. This reduction will maximize the use of the early works substructure foundations (drilled shafts) to reduce cost. Removing the OCS Poles from between the tracks on the new viaduct structure will also eliminate obstructions in the access walkway.

D. Conceptual Drawings

Any conceptual drawings (if applicable) of the configuration of the potential ATC or other appropriate descriptive information that provides an understanding of the Preliminary ATC; and


Please refer to Figures ATC 12-1 "Typical Section – Design Concept", ATC 12-2 "Typical Section Alterative Technical Concept", ATC 12-3 " Deck Plan – Design Concept", and ATC 12-4 "Deck Plan – Alternative Technical Concept" below.

E. Cost Estimate and Schedule Impacts

An order of magnitude cost estimate and a preliminary analysis of schedule impacts associated with the Preliminary ATC.


This ATC will result in an estimated cost saving of $6 M. Our preliminary analysis indicates no impact to schedule milestones.

Figure ATC 12-1: Typical Section – Design Concept

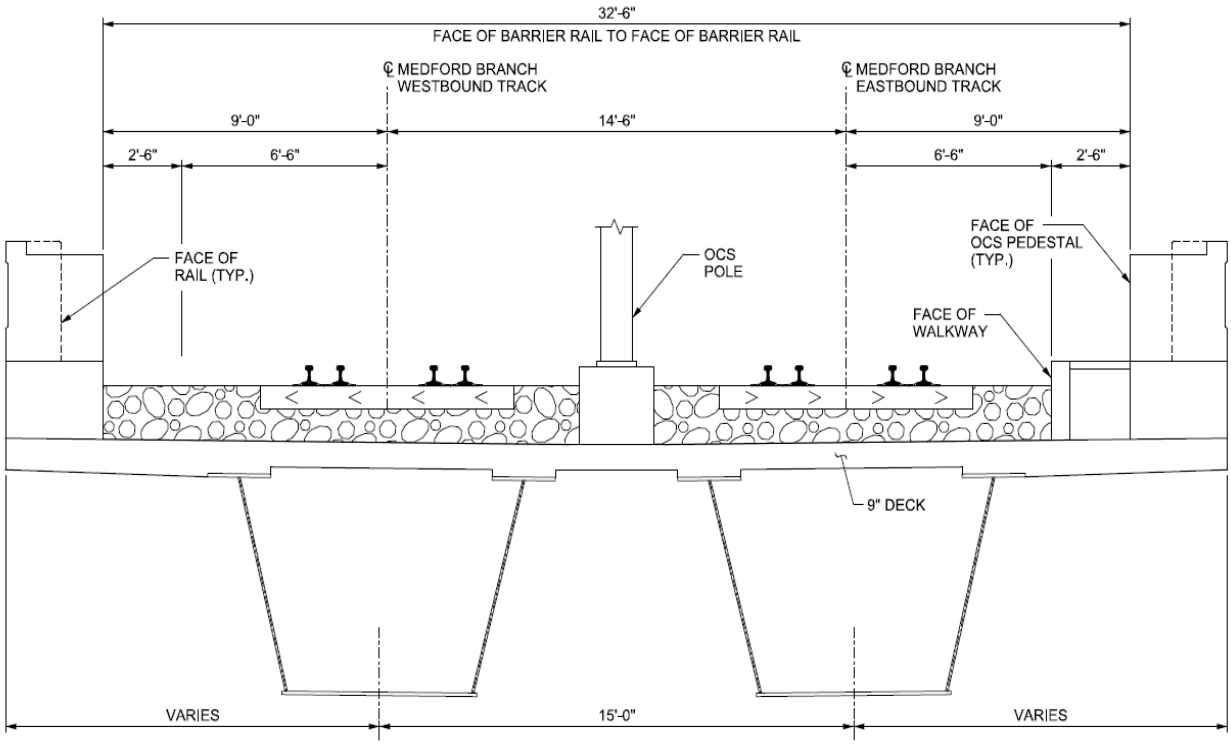


TYPICAL SECTION - DESIGN CONCEPT

Figure ATC 12-2: Typical Section - Alterative Technical Concept

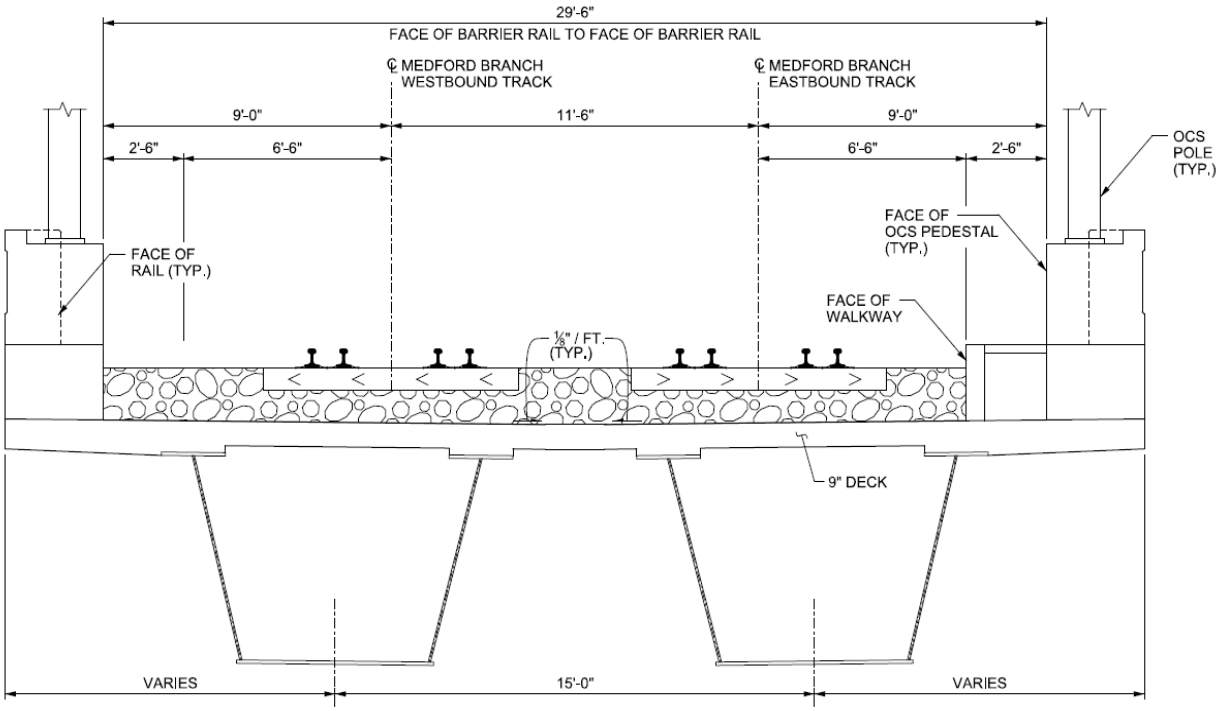


TYPICAL SECTION - ALTERNATIVE TECHNICAL CONCEPT

Figure ATC 12-3: Deck Plan – Design Concept

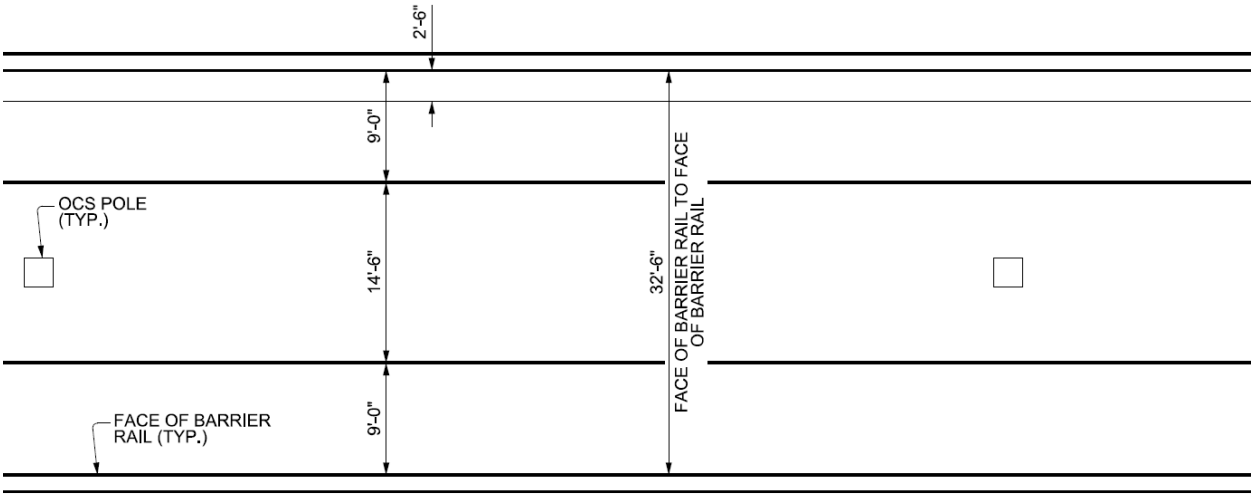

DECK PLAN - DESIGN CONCEPT

Figure ATC 12-4: Deck Plan – Alternative Technical Concept

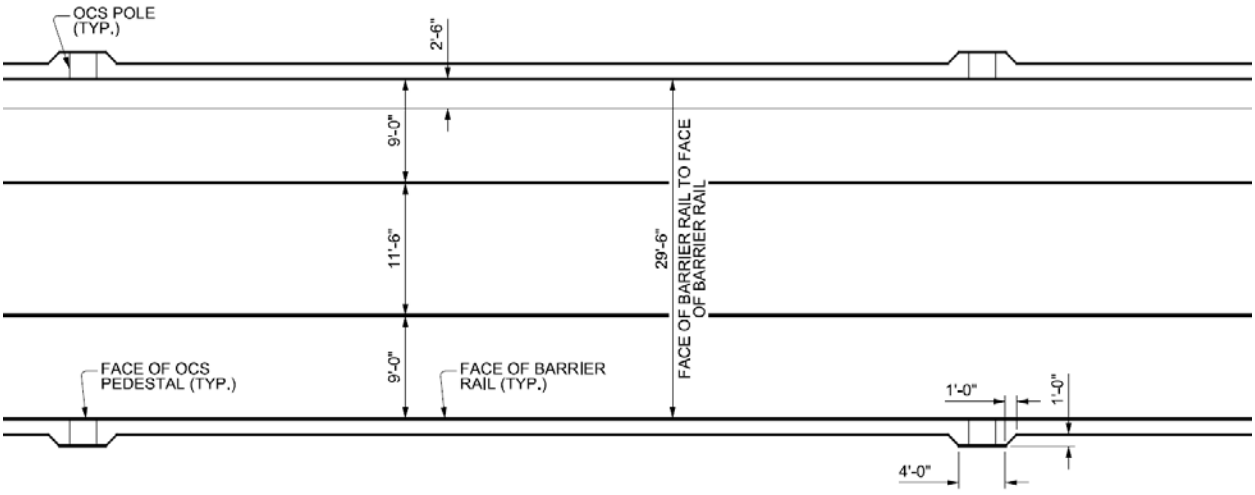

DECK PLAN - ALTERNATIVE TECHINCAL CONCEPT

ATC No. 12

MBTA Acceptance of Preliminary Submission

ATC Information:

Type of ATC:	Preliminary
Title:	GLX Constructors ATC 05 - Use of Two OCS Poles on Viaduct
Proposer Company:	GLX Constructors

Final Disposition:

Sent on behalf of Yvelisse Duvergé. The Preliminary ATC can be formally submitted for MBTA review as an ATC Submittal, subject to further refinement and submission of supporting information pursuant to Section 3.3.1 of the Instructions to Proposers.

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

PRELIMINARY

ALTERNATIVE TECHNICAL CONCEPTS

("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

GLX CONSTRUCTORS PRELIMINARY ATC FORM

ATC 12 – USE OF TWO OCS POLES ON VIADUCT

Sections A though E below must be completed to submit a Preliminary ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Preliminary ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. General Description

A general description (not to exceed two pages) of the Preliminary ATC, how the ATC will be used on the Project, the proposed location of the ATC, and any other pertinent information that would provide a clear understanding of the potential ATC;

The Contract Documents specify a single OCS Pole between the tracks on the new viaduct structure which result in a wider deck structure. By using two OCS Poles on the outside of the tracks on the viaduct structure, viaduct deck width will be reduced and result in decreased deep foundation dead loads.

B. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC and an explanation of the nature of the deviations from said requirements;

The tracked changes below, are our explanation of the changes that would be required for this ATC.

Volume 2, Technical Provisions, Section 11.2.3.4 Poles and Foundations "OCS poles shall be located between **or on the outside** of the tracks on the new viaduct structure~~**. except at junctions where they may be located at the sides of the track.**~~ On single track curves on the viaduct structure, the poles shall be located on the outside of the curve."

C. Benefits

Any potential benefits or implications of incorporating the Preliminary ATC into the Project, including in right-of-way acquisitions, rail operations, and routine or capital maintenance, and other Project risks;

A reduction in the new viaduct deck width will reduce the substructure foundation dead loads. This reduction will maximize the use of the early works substructure foundations (drilled shafts) to reduce cost. Removing the OCS Poles from between the tracks on the new viaduct structure will also eliminate obstructions in the access walkway.

D. Conceptual Drawings

Any conceptual drawings (if applicable) of the configuration of the potential ATC or other appropriate descriptive information that provides an understanding of the Preliminary ATC; and


Please refer to Figures ATC 12-1 "Typical Section – Design Concept", ATC 12-2 "Typical Section Alterative Technical Concept", ATC 12-3 " Deck Plan – Design Concept", and ATC 12-4 "Deck Plan – Alternative Technical Concept" below.

E. Cost Estimate and Schedule Impacts

An order of magnitude cost estimate and a preliminary analysis of schedule impacts associated with the Preliminary ATC.


This ATC will result in an estimated cost saving of $6 M. Our preliminary analysis indicates no impact to schedule milestones.

Figure ATC 12-1: Typical Section – Design Concept

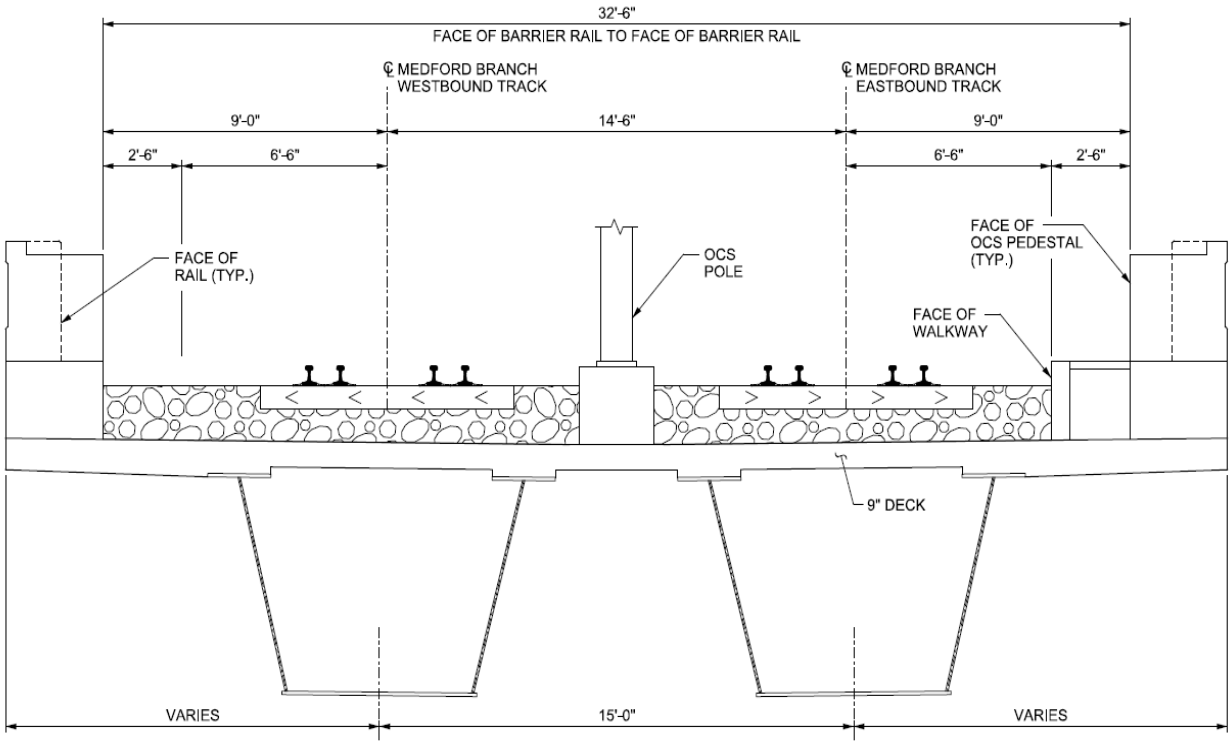


TYPICAL SECTION - DESIGN CONCEPT

Figure ATC 12-2: Typical Section - Alterative Technical Concept

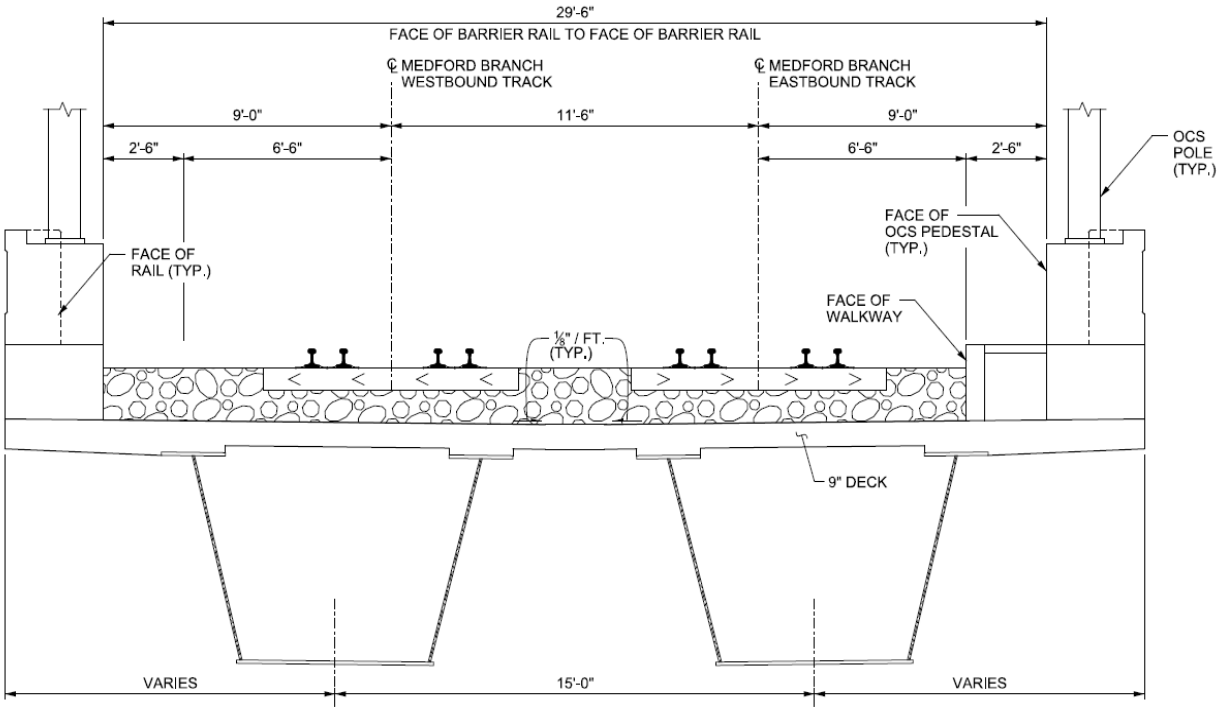


TYPICAL SECTION - ALTERNATIVE TECHNICAL CONCEPT

Figure ATC 12-3: Deck Plan – Design Concept

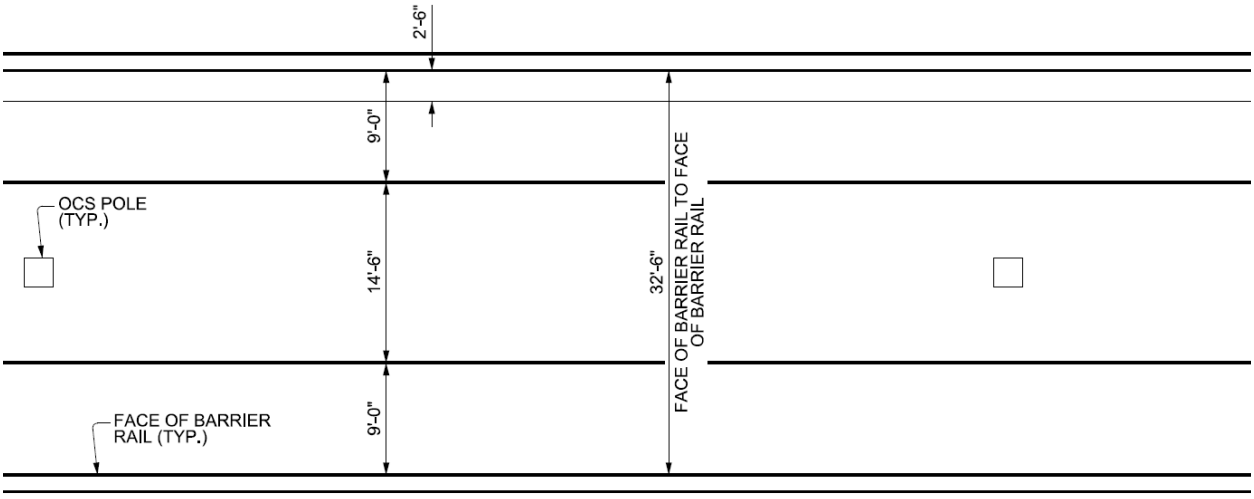

DECK PLAN - DESIGN CONCEPT

Figure ATC 12-4: Deck Plan – Alternative Technical Concept

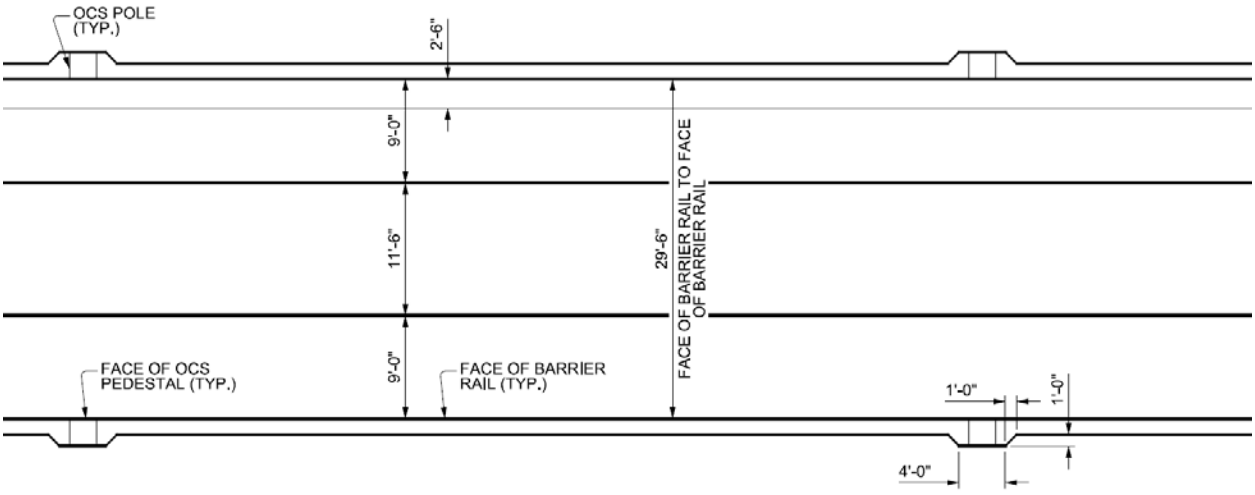

DECK PLAN - ALTERNATIVE TECHINCAL CONCEPT

ATC No. 12

Formal Submission

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

FORMAL

ALTERNATIVE TECHNICAL CONCEPTS ("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

JULY 11, 2017 (Final Round)

GLX CONSTRUCTORS FORMAL ATC FORM

USE OF TWO OCS POLES ON VIADUCT

Sections A though P below shall be completed to submit a Formal ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Formal ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. ATC Number

A sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.);

ATC 12

MBTA Preliminary ATC File Number: ATC-000011 – GLX Constructors ATC 05

B. Description and Conceptual Drawings

A description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information;

The Contract Documents specify a single OCS Pole between the tracks on the new viaduct structure which result in a wider deck structure. By using two OCS Poles on the outside of the tracks on the viaduct structure, viaduct deck width will be reduced and result in decreased deep foundation dead loads. Please refer to Figures ATC 12-1 "Typical Section – Design Concept", ATC 12-2 "Typical Section Alterative Technical Concept", ATC 12-3 " Deck Plan – Design Concept", and ATC 12-4 "Deck Plan – Alternative Technical Concept" below.

C. Locations and How Used

The locations where, and an explanation of how, the ATC will be used on the Project;

This ATC will be used on the viaduct structure to reduce deck structure.

D. Changes in Rail or Transit Operations

Any changes in rail or transit operations requirements associated with the ATC, including ease of operations;

No changes in operations are anticipated as a result of this ATC.

E. Changes in Routine or Capital Maintenance

Any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance;

This ATC will improve routine or capital maintenance access by removing the OCS Poles from between the tracks on the new viaduct structure will eliminating obstructions in the access walkway.

F. Changes in Anticipated Service Life

Any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC;

This ATC will result in no change to anticipated service life

G. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations;

Volume 2 Technical Provisions – Subsection 11.2.3.4 Poles and Foundations "OCS poles shall be located between the tracks on the new viaduct structure except at junctions where they may be located at the sides of the track. On single track curves on the viaduct structure, the poles shall be located on the outside of the curve."

H. Justification of Use

An analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed;

A reduction in the New Viaduct deck width will reduce the substructure foundation dead loads and the result will maximize the use of the early works substructure foundations (drilled shafts), which is a Cost Savings. Additionally, removing the OCS Poles from between the tracks on the new viaduct structure will eliminate obstructions in the access walkway.

I. Preliminary Analysis and Quantitative Discussion

A preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation;

No impacts on rail or transit operations are anticipated as a result of this ATC.

J. Impacts on Third Parties

A description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC. Proposers are advised that they may (i) be solely responsible for the cost and schedule impacts of the acquisition of any such Additional Properties, including the cost thereof and obtaining any necessary environmental approvals; (ii) not be entitled to any change order for time or money as a result of site conditions (i.e., hazardous materials, differing site conditions, geotechnical issues, or utilities) on such Additional Properties; and (iii) not be entitled to any change order for time or money as a result of any delay, inability, or cost associated with the acquisition of such Additional Properties;

No impacts to third parties are anticipated as a result of this ATC.

K. History of Use and References

A description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements;

The MBTA currently has this two pole design concept in active service as can be seen on the Green Line

between North Station and Science Park.

Joe Vassalo, MBTA, 617.222.1818, Jvassalo@MBTA.com

L. Additional Risks

A description of added risks to the MBTA or third parties associated with implementing the ATC;

No additional risks to the MBTA or to third parties are anticipated as a result of this ATC.

M. Additional Costs

An estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC;

Additional costs to the MBTA, DB Entity and third parties will not result from this ATC. One of the primary purposes of this ATC is cost reduction.

N. Estimated Price Adjustment

An estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented;

This ATC will result in an estimated savings of $1,800,000. The ATC pricing as shown in this proposal is an all inclusive price. All price deducts and/or adds have been considered, and the resulting price adjustment is offered as shown.

O. Schedule Adjustment

An estimate of the schedule adjustment, should the ATC be approved and implemented; and


This ATC does not require any schedule adjustment.

P. Analysis of Quality, Performance, and Reliability

An analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents.


This ATC will provide equal quality, performance and reliability than the specified pole locations on the viaduct. Removing the OCS Poles from between the tracks on the new viaduct structure will eliminate obstructions in the access walkway, increasing safety.

Figure ATC 12-1: Typical Section – Design Concept

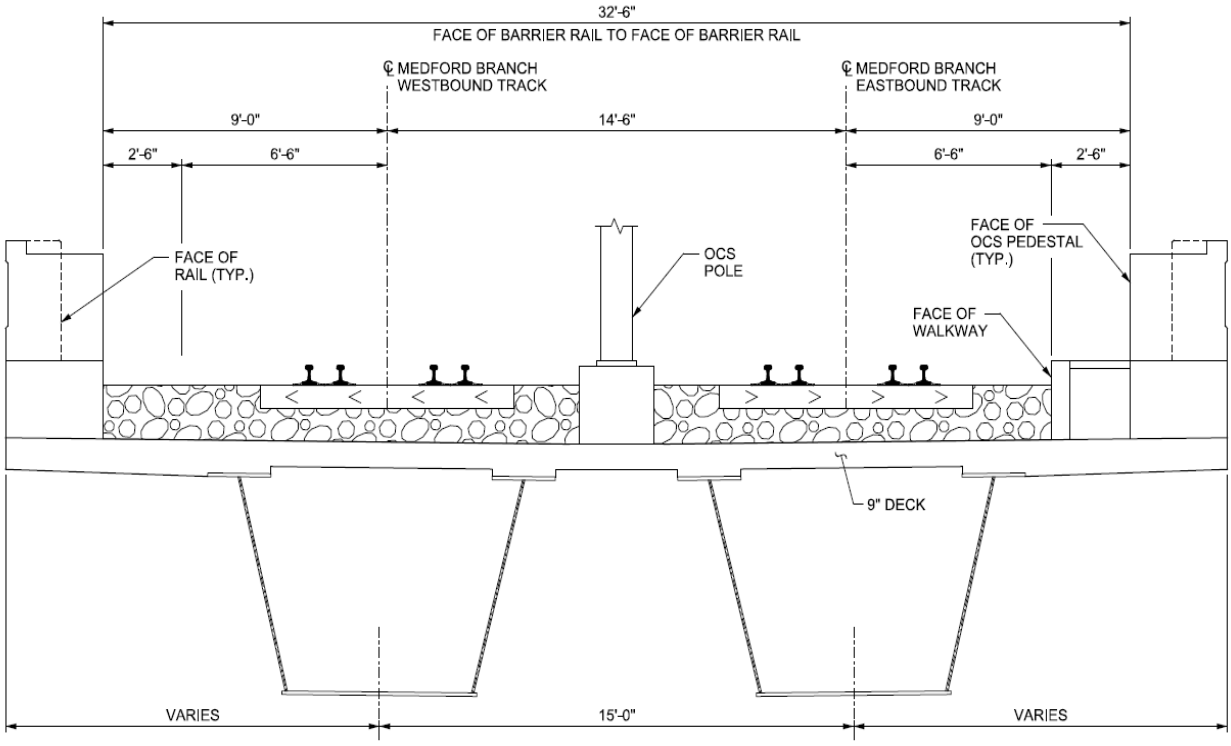


TYPICAL SECTION - DESIGN CONCEPT

Figure ATC 12-2: Typical Section - Alterative Technical Concept

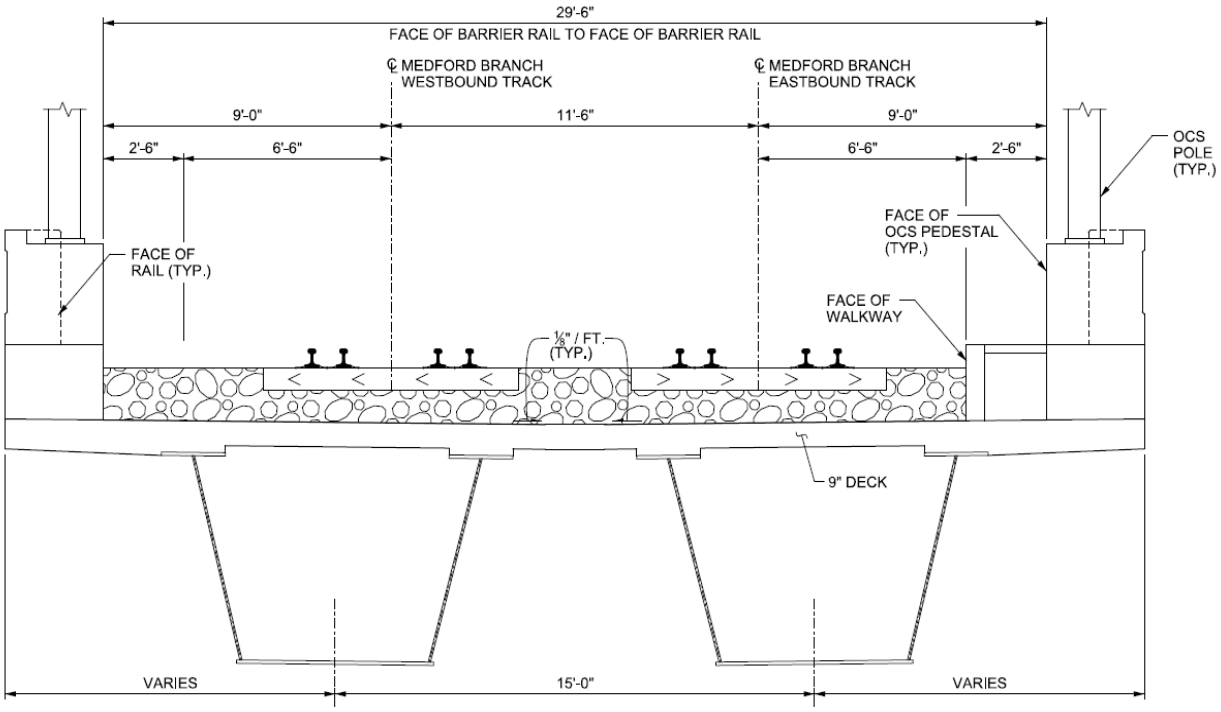


TYPICAL SECTION - ALTERNATIVE TECHNICAL CONCEPT

Figure ATC 12-3: Deck Plan – Design Concept

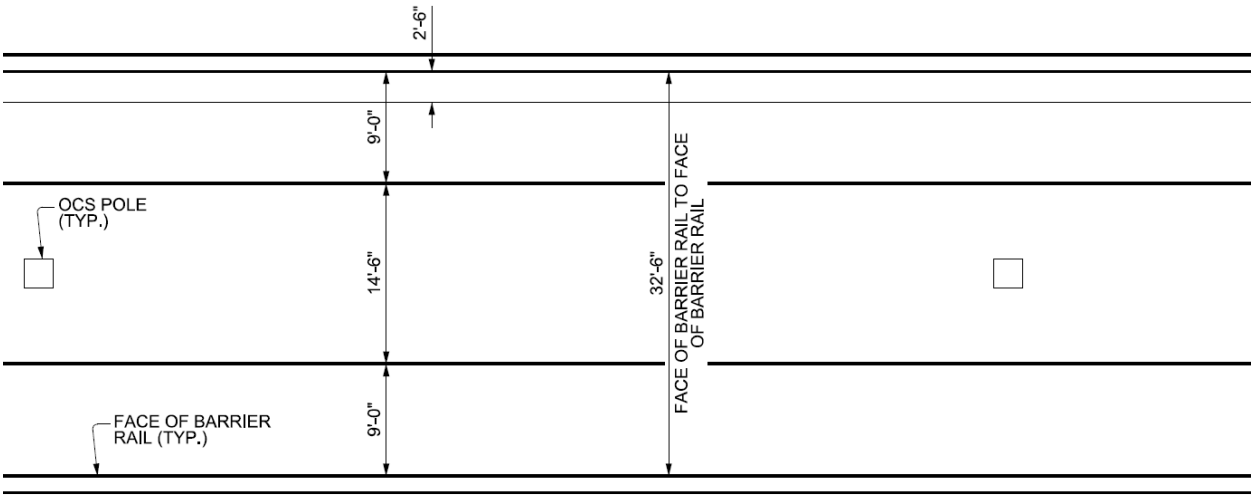

DECK PLAN - DESIGN CONCEPT

Figure ATC 12-4: Deck Plan – Alternative Technical Concept

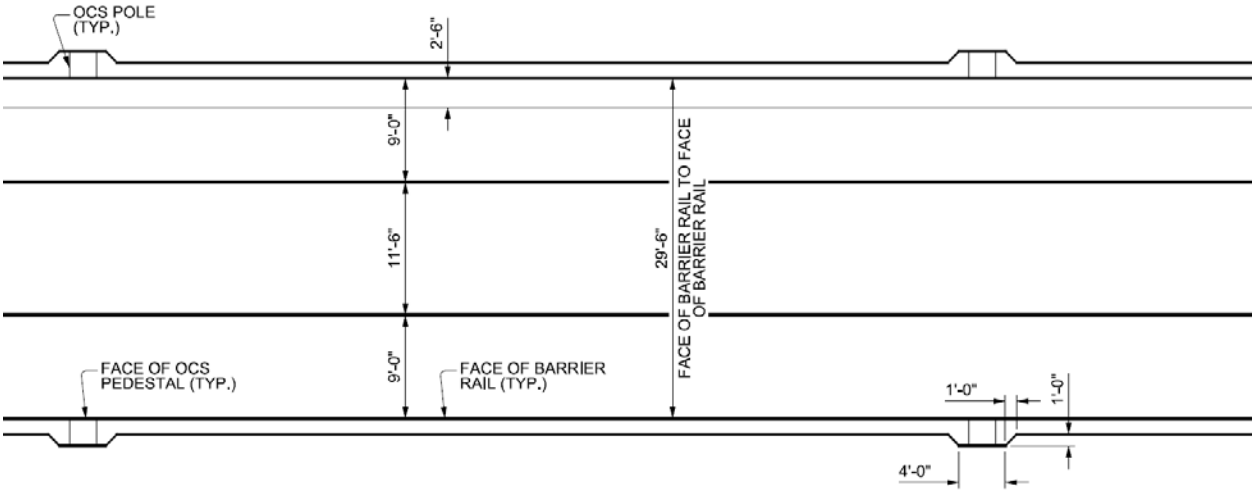

DECK PLAN - ALTERNATIVE TECHINCAL CONCEPT

ATC No. 12

MBTA Acceptance of Formal Submission

ATC Information:

Type of ATC:	Formal
Title:	GLX Constructors ATC 05 - Use of Two OCS Poles on Viaduct
Proposer Company:	GLX Constructors

Final Disposition:

Sent on behalf of Yvelisse Duvergé. The ATC Submittal is acceptable for inclusion in the Proposal

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

FORMAL

ALTERNATIVE TECHNICAL CONCEPTS ("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

JULY 11, 2017 (Final Round)

GLX CONSTRUCTORS FORMAL ATC FORM

USE OF TWO OCS POLES ON VIADUCT

Sections A though P below shall be completed to submit a Formal ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Formal ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. ATC Number

A sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.);

ATC 12

MBTA Preliminary ATC File Number: ATC-000011 – GLX Constructors ATC 05

B. Description and Conceptual Drawings

A description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information;

The Contract Documents specify a single OCS Pole between the tracks on the new viaduct structure which result in a wider deck structure. By using two OCS Poles on the outside of the tracks on the viaduct structure, viaduct deck width will be reduced and result in decreased deep foundation dead loads. Please refer to Figures ATC 12-1 "Typical Section – Design Concept", ATC 12-2 "Typical Section Alterative Technical Concept", ATC 12-3 " Deck Plan – Design Concept", and ATC 12-4 "Deck Plan – Alternative Technical Concept" below.

C. Locations and How Used

The locations where, and an explanation of how, the ATC will be used on the Project;

This ATC will be used on the viaduct structure to reduce deck structure.

D. Changes in Rail or Transit Operations

Any changes in rail or transit operations requirements associated with the ATC, including ease of operations;

No changes in operations are anticipated as a result of this ATC.

E. Changes in Routine or Capital Maintenance

Any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance;

This ATC will improve routine or capital maintenance access by removing the OCS Poles from between the tracks on the new viaduct structure will eliminating obstructions in the access walkway.

F. Changes in Anticipated Service Life

Any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC;

This ATC will result in no change to anticipated service life

G. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations;

Volume 2 Technical Provisions – Subsection 11.2.3.4 Poles and Foundations "OCS poles shall be located between the tracks on the new viaduct structure except at junctions where they may be located at the sides of the track. On single track curves on the viaduct structure, the poles shall be located on the outside of the curve."

H. Justification of Use

An analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed;

A reduction in the New Viaduct deck width will reduce the substructure foundation dead loads and the result will maximize the use of the early works substructure foundations (drilled shafts), which is a Cost Savings. Additionally, removing the OCS Poles from between the tracks on the new viaduct structure will eliminate obstructions in the access walkway.

I. Preliminary Analysis and Quantitative Discussion

A preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation;

No impacts on rail or transit operations are anticipated as a result of this ATC.

J. Impacts on Third Parties

A description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC. Proposers are advised that they may (i) be solely responsible for the cost and schedule impacts of the acquisition of any such Additional Properties, including the cost thereof and obtaining any necessary environmental approvals; (ii) not be entitled to any change order for time or money as a result of site conditions (i.e., hazardous materials, differing site conditions, geotechnical issues, or utilities) on such Additional Properties; and (iii) not be entitled to any change order for time or money as a result of any delay, inability, or cost associated with the acquisition of such Additional Properties;

No impacts to third parties are anticipated as a result of this ATC.

K. History of Use and References

A description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements;

The MBTA currently has this two pole design concept in active service as can be seen on the Green Line

between North Station and Science Park.

Joe Vassalo, MBTA, 617.222.1818, Jvassalo@MBTA.com

L. Additional Risks

A description of added risks to the MBTA or third parties associated with implementing the ATC;

No additional risks to the MBTA or to third parties are anticipated as a result of this ATC.

M. Additional Costs

An estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC;

Additional costs to the MBTA, DB Entity and third parties will not result from this ATC. One of the primary purposes of this ATC is cost reduction.

N. Estimated Price Adjustment

An estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented;

This ATC will result in an estimated savings of $1,800,000. The ATC pricing as shown in this proposal is an all inclusive price. All price deducts and/or adds have been considered, and the resulting price adjustment is offered as shown.

O. Schedule Adjustment

An estimate of the schedule adjustment, should the ATC be approved and implemented; and


This ATC does not require any schedule adjustment.

P. Analysis of Quality, Performance, and Reliability

An analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents.


This ATC will provide equal quality, performance and reliability than the specified pole locations on the viaduct. Removing the OCS Poles from between the tracks on the new viaduct structure will eliminate obstructions in the access walkway, increasing safety.

Figure ATC 12-1: Typical Section – Design Concept

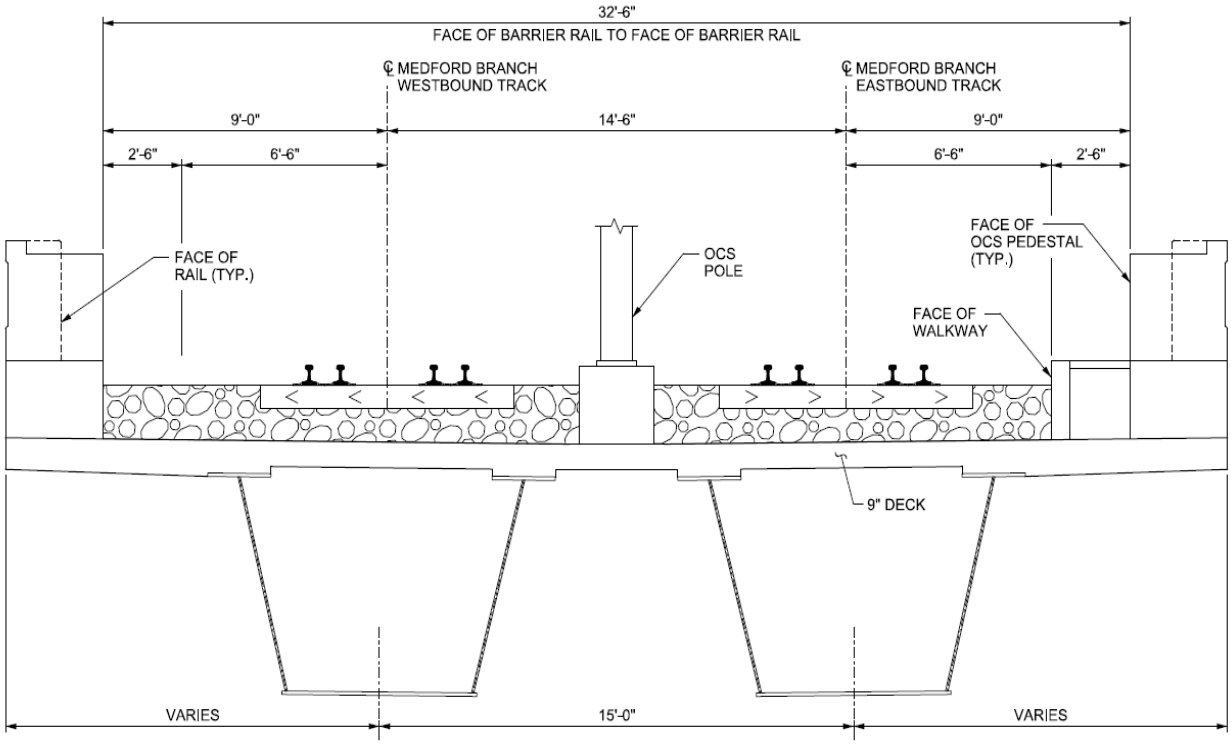


TYPICAL SECTION - DESIGN CONCEPT

Figure ATC 12-2: Typical Section - Alterative Technical Concept

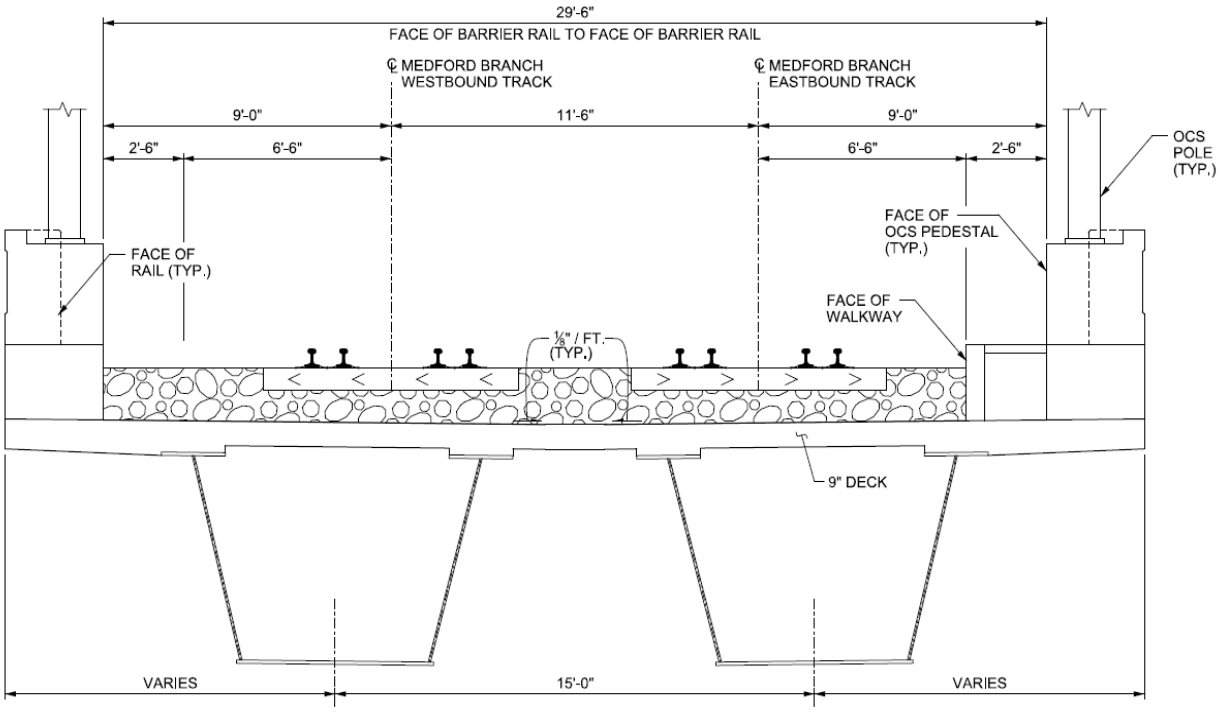


TYPICAL SECTION - ALTERNATIVE TECHNICAL CONCEPT

Figure ATC 12-3: Deck Plan – Design Concept

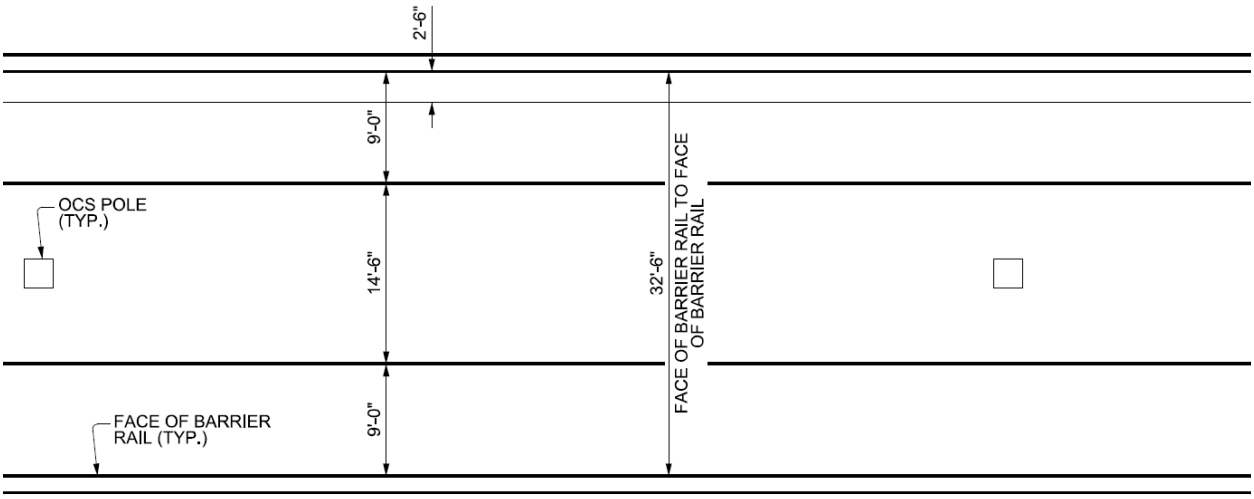

DECK PLAN - DESIGN CONCEPT

Figure ATC 12-4: Deck Plan – Alternative Technical Concept

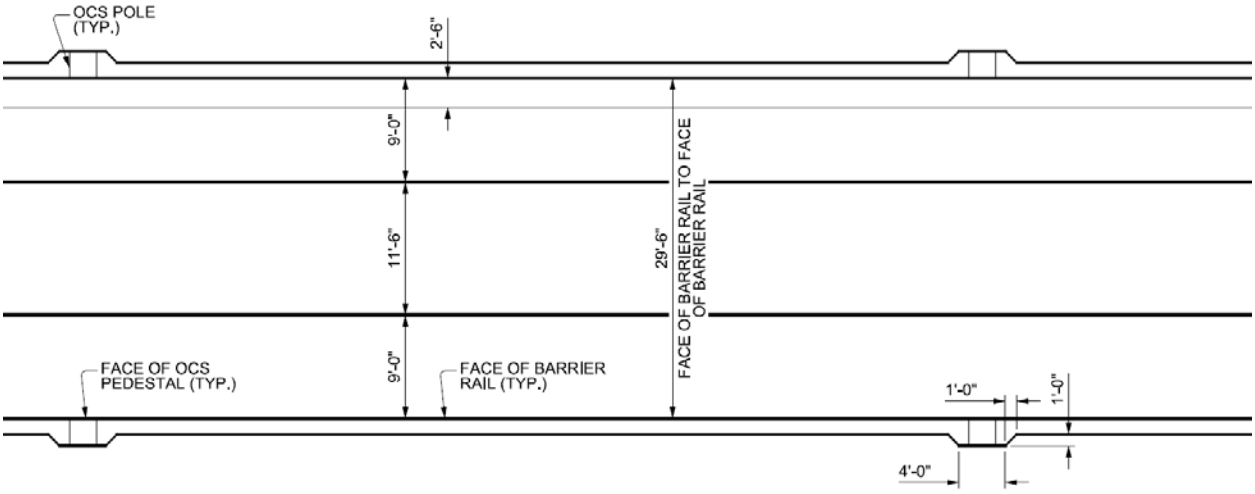

DECK PLAN - ALTERNATIVE TECHINCAL CONCEPT

ATC No. 35

ATC No. 35

Preliminary Submission

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

PRELIMINARY

ALTERNATIVE TECHNICAL CONCEPTS

("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

GLX CONSTRUCTORS PRELIMINARY ATC FORM

ATC 35 – VIADUCT OPTIMIZATION

Sections A though E below must be completed to submit a Preliminary ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Preliminary ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. General Description

A general description (not to exceed two pages) of the Preliminary ATC, how the ATC will be used on the Project, the proposed location of the ATC, and any other pertinent information that would provide a clear understanding of the potential ATC;

This ATC replaces three sections of elevated track with MSE walls as follows:

1.) Replace a section of elevated track from approximate Sta. MB-EB 196+00 to Sta. MB-EB 202+00 required on viaduct with an elevated section of track on MSE wall
2.) Replace a section of elevated track from approximate Sta. US-WB 7+75 to Sta. US-WB 11+50 required on viaduct with an elevated section of track on MSE wall
3.) Replace a section of elevated track from approximate Sta. MB-EB 214+00 to Sta. MB-EB 220+00 required on viaduct with an elevated section of track on MSE wall

B. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC and an explanation of the nature of the deviations from said requirements;

Volume 2, Technical Provisions, Section 1.2.1 General (a) and (b). Volume 2, Exhibit 2B, Project Definition plan sheets: UEV-S-2001, and UWV-S-2000. This ATC replaces sections of elevated concrete structure shown on the Project Definition plans with an MSE wall structure.

C. Benefits

Any potential benefits or implications of incorporating the Preliminary ATC into the Project, including in right-of-way acquisitions, rail operations, and routine or capital maintenance, and other Project risks;

This ATC will provide the following benefits:

- Reduced contaminated excavation and export off site while eliminating contaminated deep foundation spoils
- Mitigated deep foundation risks
- MSE wall will have lower maintenance cost
- Reduced noise and vibration during construction
- Reduced square footage of bridge deck
- Decrease in maintenance cost due to decrease in bridge deck area

D. Conceptual Drawings

Any conceptual drawings (if applicable) of the configuration of the potential ATC or other appropriate descriptive information that provides an understanding of the Preliminary ATC; and

Please reference Figures ATC-35-1 "Plan View of Proposed MSE Wall Sections" and ATC-35-2 "Profile Views of Proposed MSE Wall Sections"

E. Cost Estimate and Schedule Impacts

An order of magnitude cost estimate and a preliminary analysis of schedule impacts associated with the Preliminary ATC.

This ATC will result in an estimated cost savings of $10 M. Our preliminary analysis indicates no impact to schedule milestones.

Figure ATC-35-1: Plan View of Proposed MSE Wall Sections


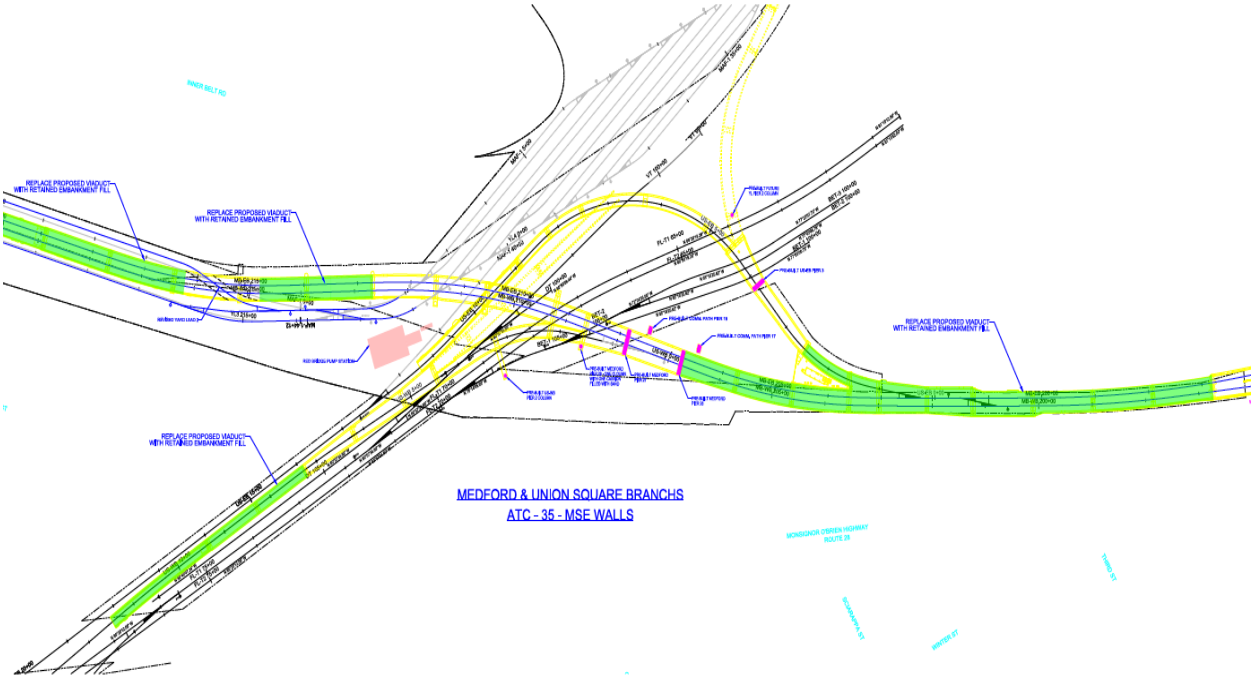


Figure ATC-35-2: Profile Views of Proposed MSE Wall Sections

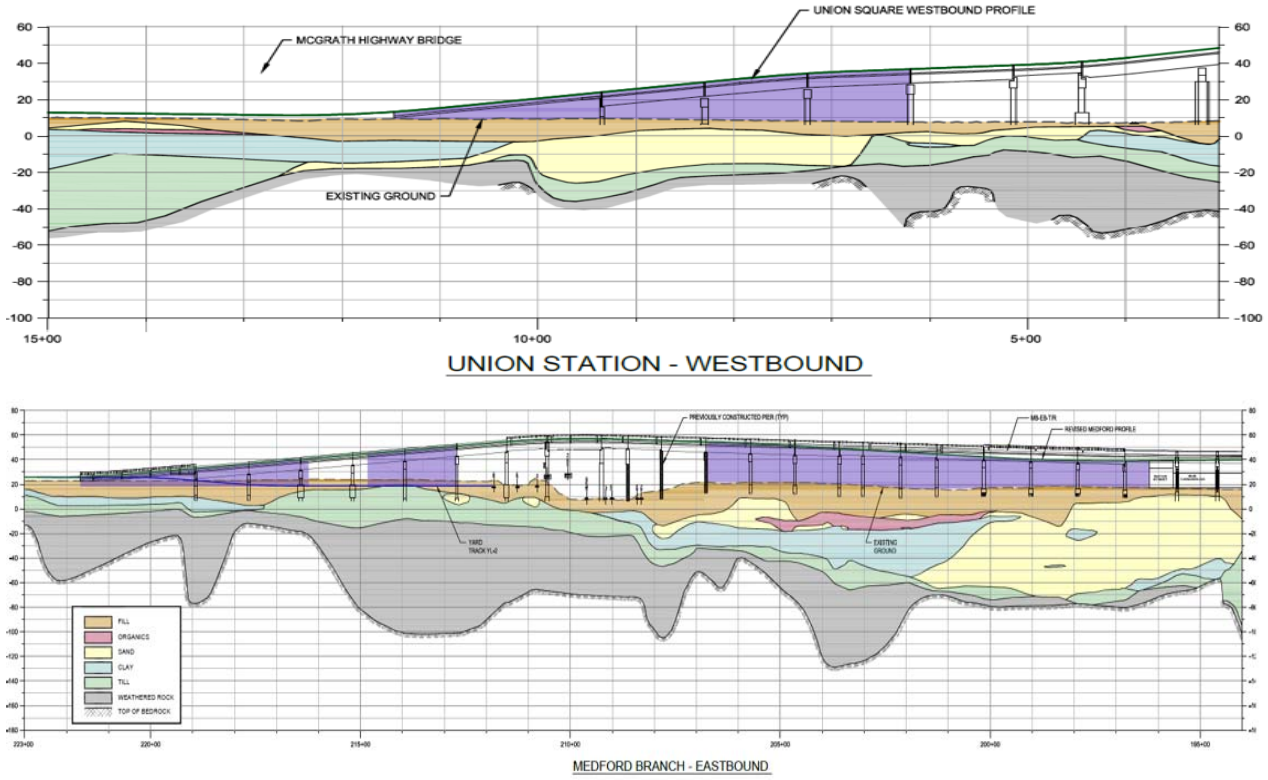

ATC No. 35

Acceptance of Preliminary Submission

ATC Information:

Type of ATC:	Preliminary
Title:	GLX Constructors ATC 07 - Viaduct Optimization
Proposer Company:	GLX Constructors

Final Disposition:

Sent on behalf of Yvelisse Duvergé. The Preliminary ATC can be formally submitted for MBTA review as an ATC Submittal, subject to further refinement and submission of supporting information pursuant to Section 3.3.1 of the Instructions to Proposers.

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

PRELIMINARY

ALTERNATIVE TECHNICAL CONCEPTS

("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

GLX CONSTRUCTORS PRELIMINARY ATC FORM

ATC 35 – VIADUCT OPTIMIZATION

Sections A though E below must be completed to submit a Preliminary ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Preliminary ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. General Description

A general description (not to exceed two pages) of the Preliminary ATC, how the ATC will be used on the Project, the proposed location of the ATC, and any other pertinent information that would provide a clear understanding of the potential ATC;

This ATC replaces three sections of elevated track with MSE walls as follows:

1.) Replace a section of elevated track from approximate Sta. MB-EB 196+00 to Sta. MB-EB 202+00 required on viaduct with an elevated section of track on MSE wall
2.) Replace a section of elevated track from approximate Sta. US-WB 7+75 to Sta. US-WB 11+50 required on viaduct with an elevated section of track on MSE wall
3.) Replace a section of elevated track from approximate Sta. MB-EB 214+00 to Sta. MB-EB 220+00 required on viaduct with an elevated section of track on MSE wall

B. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC and an explanation of the nature of the deviations from said requirements;

Volume 2, Technical Provisions, Section 1.2.1 General (a) and (b). Volume 2, Exhibit 2B, Project Definition plan sheets: UEV-S-2001, and UWV-S-2000. This ATC replaces sections of elevated concrete structure shown on the Project Definition plans with an MSE wall structure.

C. Benefits

Any potential benefits or implications of incorporating the Preliminary ATC into the Project, including in right-of-way acquisitions, rail operations, and routine or capital maintenance, and other Project risks;

This ATC will provide the following benefits:

- Reduced contaminated excavation and export off site while eliminating contaminated deep foundation spoils
- Mitigated deep foundation risks
- MSE wall will have lower maintenance cost
- Reduced noise and vibration during construction
- Reduced square footage of bridge deck
- Decrease in maintenance cost due to decrease in bridge deck area

D. Conceptual Drawings

Any conceptual drawings (if applicable) of the configuration of the potential ATC or other appropriate descriptive information that provides an understanding of the Preliminary ATC; and

Please reference Figures ATC-35-1 "Plan View of Proposed MSE Wall Sections" and ATC-35-2 "Profile Views of Proposed MSE Wall Sections"

E. Cost Estimate and Schedule Impacts

An order of magnitude cost estimate and a preliminary analysis of schedule impacts associated with the Preliminary ATC.

This ATC will result in an estimated cost savings of $10 M. Our preliminary analysis indicates no impact to schedule milestones.

Figure ATC-35-1: Plan View of Proposed MSE Wall Sections


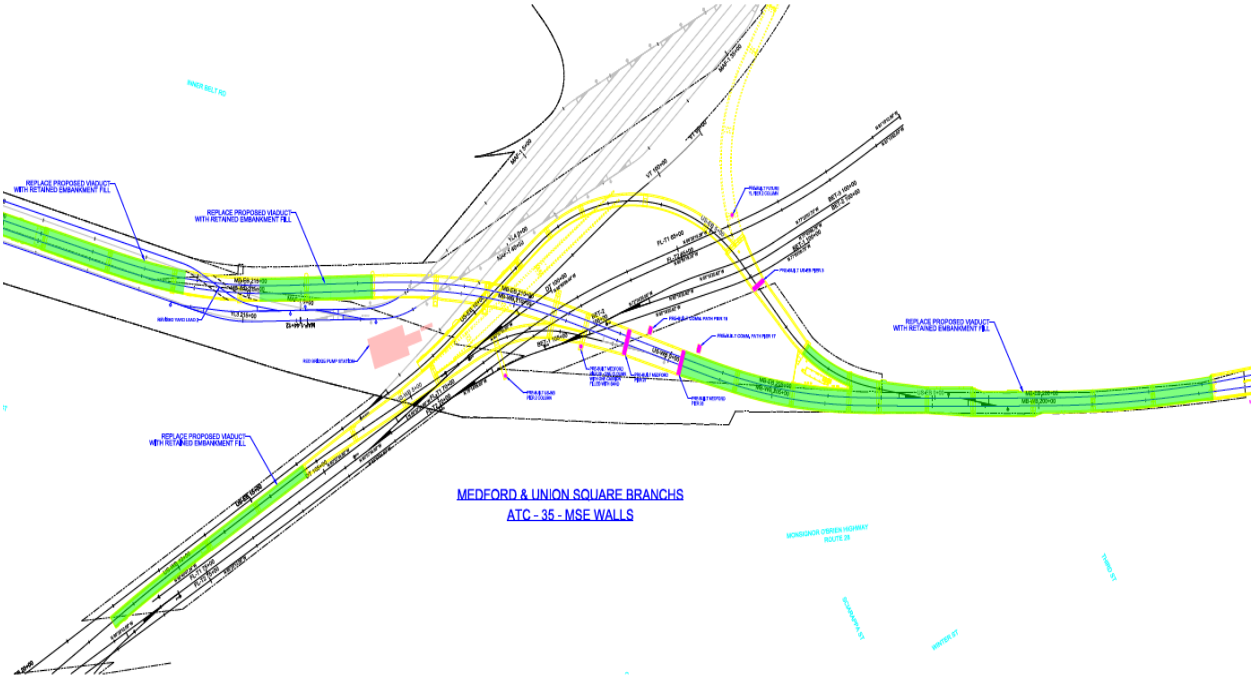


Figure ATC-35-2: Profile Views of Proposed MSE Wall Sections

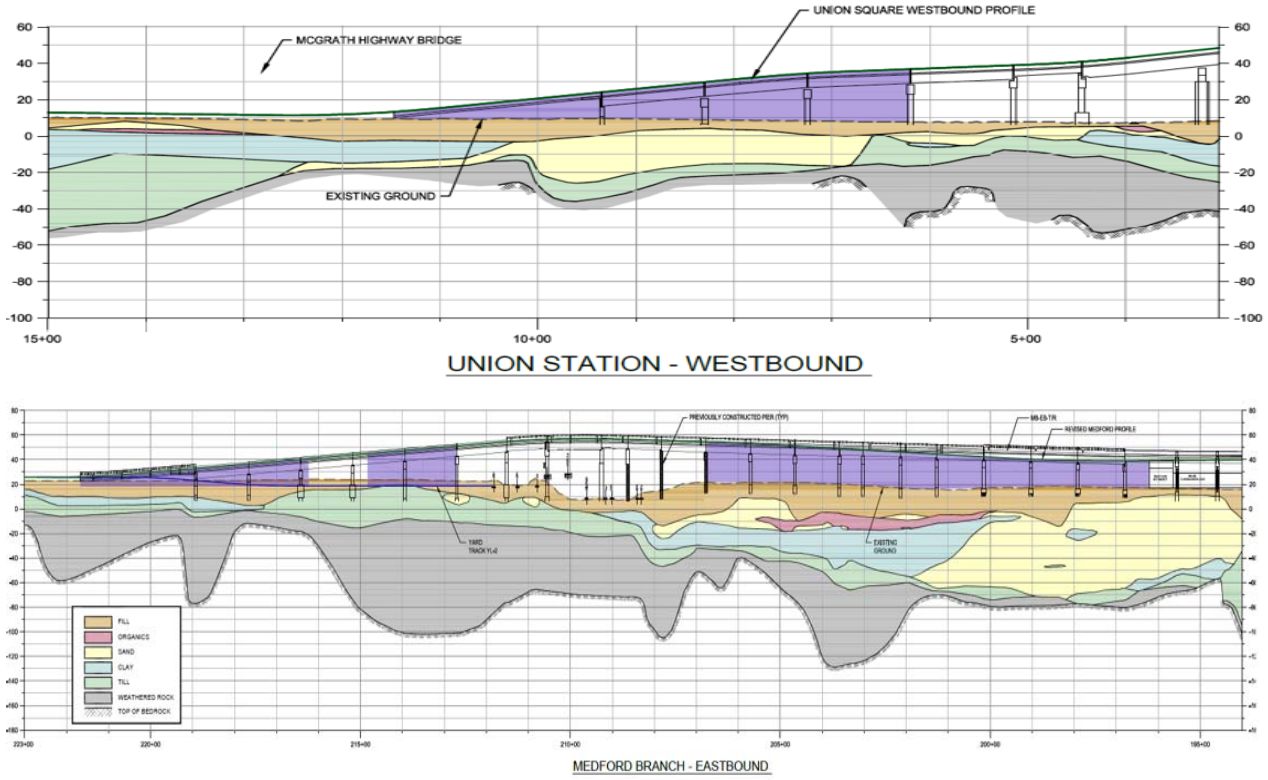

ATC No. 35

Formal Submission

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

FORMAL

ALTERNATIVE TECHNICAL CONCEPTS ("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

JULY 11, 2017 (Final Round)

GLX CONSTRUCTORS FORMAL ATC FORM

VIADUCT OPTIMIZATION

Sections A though P below shall be completed to submit a Formal ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Formal ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. ATC Number

A sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.);

ATC 35

MBTA Preliminary ATC File Number: ATC-000013 – GLX Constructors ATC 07

B. Description and Conceptual Drawings

A description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information;

This ATC replaces three sections of elevated track with MSE walls as follows:

1.) Replace a section of elevated track from approximate Sta. MB-EB 196+00 to Sta. MB-EB 202+00 required on viaduct with an elevated section of track on MSE wall
2.) Replace a section of elevated track from approximate Sta. US-WB 7+75 to Sta. US-WB 11+50 required on viaduct with an elevated section of track on MSE wall
3.) Replace a section of elevated track from approximate Sta. MB-EB 214+00 to Sta. MB-EB 220+00 required on viaduct with an elevated section of track on MSE wall

Please reference Figures ATC-35-1 "Plan View of Proposed MSE Wall Sections" , ATC-35-2 "Profile Views of Proposed MSE Wall Sections" and ATC-35-3 "MSE Wall At Viaduct"

C. Locations and How Used

The locations where, and an explanation of how, the ATC will be used on the Project;

This ATC will be used at approximate Sta. MB-EB 196+00 to Sta. MB-EB 202+00, US-WB 7+75 to Sta. US-WB 11+50, and Sta. MB-EB 214+00 to Sta. MB-EB 220+00 to replace sections of elevated track with MSE walls.

D. Changes in Rail or Transit Operations

Any changes in rail or transit operations requirements associated with the ATC, including ease of operations;

No changes in operations are anticipated as a result of this ATC.

E. Changes in Routine or Capital Maintenance

Any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance;

This ATC will include MSE walls that require less maintenance than an elevated structure and associated bridge deck area.

F. Changes in Anticipated Service Life

Any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC;

MSE wall sections will have a longer service life than the specified bridge sections. This is mainly due to alleviated corrosion or stray current issues associated with elevated bridge structures.

G. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations;

Volume 2, Technical Provisions, Section 1.2.1 General (a) and (b). Volume 2, Exhibit 2B, Project Definition plan sheets: UEV-S-2001, and UWV-S-2000. This ATC replaces sections of elevated concrete structure shown on the Project Definition plans with an MSE wall structure.

H. Justification of Use

An analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed;

This ATC will reduce contaminated excavation and export off site while eliminating contaminated deep foundation spoils. The deep foundations required for an elevated structures are eliminated, thus reducing the deep foundation risk associated with unforeseen conditions. MSE wall construction has lower noise and vibration than elevated structure construction. The reduction in bridge deck provides a significant cost savings to the project.

I. Preliminary Analysis and Quantitative Discussion

A preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation;

No impacts on rail or transit operations are anticipated as a result of this ATC.

J. Impacts on Third Parties

A description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC. Proposers are advised that they may (i) be solely responsible for the cost and schedule impacts of the acquisition of any such Additional Properties, including the cost thereof and obtaining any necessary environmental approvals; (ii) not be entitled to any change order for time or money as a result of site conditions (i.e., hazardous materials, differing site conditions, geotechnical issues, or utilities) on such Additional Properties; and (iii) not be entitled to any change order for time or money as a result of any delay, inability, or cost associated with the acquisition of such Additional Properties;

No impacts to third parties are anticipated as a result of this ATC.

K. History of Use and References

A description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements;

MSE Walls have been used successfully as a part of the Charlotte Area Transit System in Charlotte, North Carolina.

John Mrzygod, City of Charlotte Engineering and Property Management – Charlotte Area Transit System, 704.336.2245, jmrzygod@ci.charlotte.nc.us

L. Additional Risks

A description of added risks to the MBTA or third parties associated with implementing the ATC;

No additional risks to the MBTA or to third parties are anticipated as a result of this ATC.

M. Additional Costs

An estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC;

Additional costs to the MBTA, DB Entity and third parties will not result from this ATC. One of the primary purposes of this ATC is cost reduction.

N. Estimated Price Adjustment

An estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented;

This ATC will result in an estimated savings of $10,000,000. The ATC pricing as shown in this proposal is an all inclusive price. All price deducts and/or adds have been considered, and the resulting price adjustment is offered as shown.

O. Schedule Adjustment

An estimate of the schedule adjustment, should the ATC be approved and implemented; and

This ATC does not require any schedule adjustment.

P. Analysis of Quality, Performance, and Reliability

An analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents.

This ATC will provide an equal quality, performance, and reliability than the specified elevated track section. This ATC would increase the service life while reducing maintenance costs associated with

maintaining corrosion resistance.

Figure ATC-35-1: Plan View of Proposed MSE Wall Sections



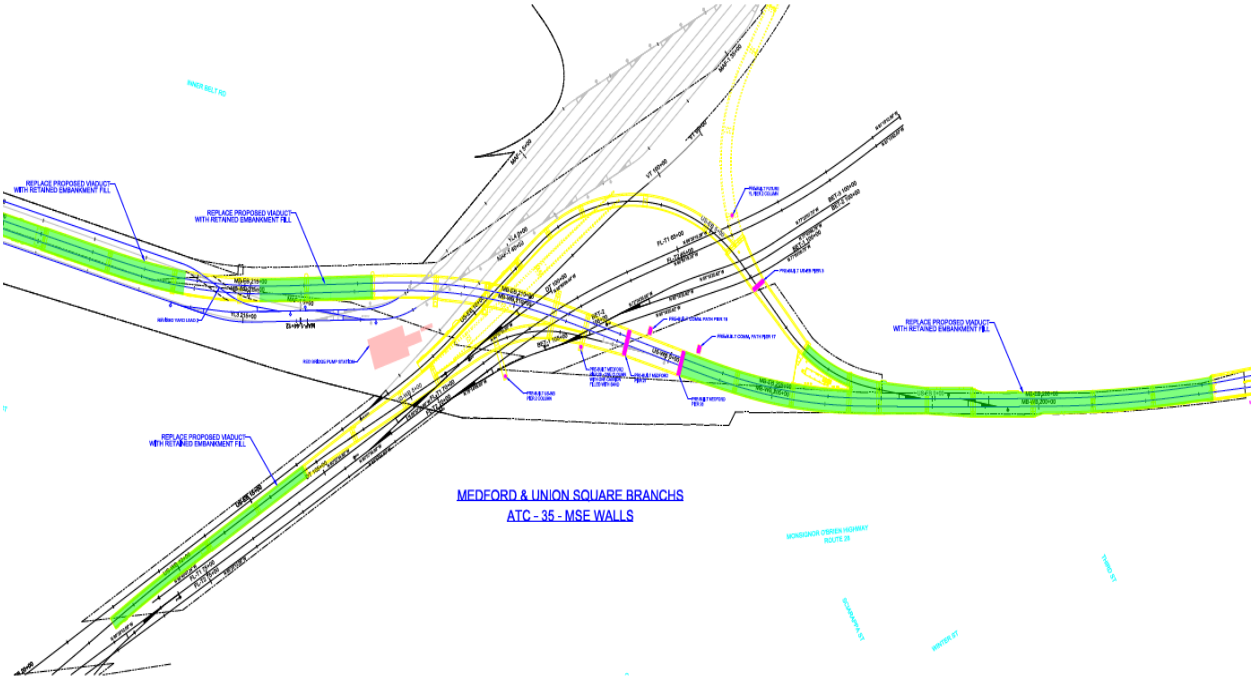


Figure ATC-35-2: Profile Views of Proposed MSE Wall Sections

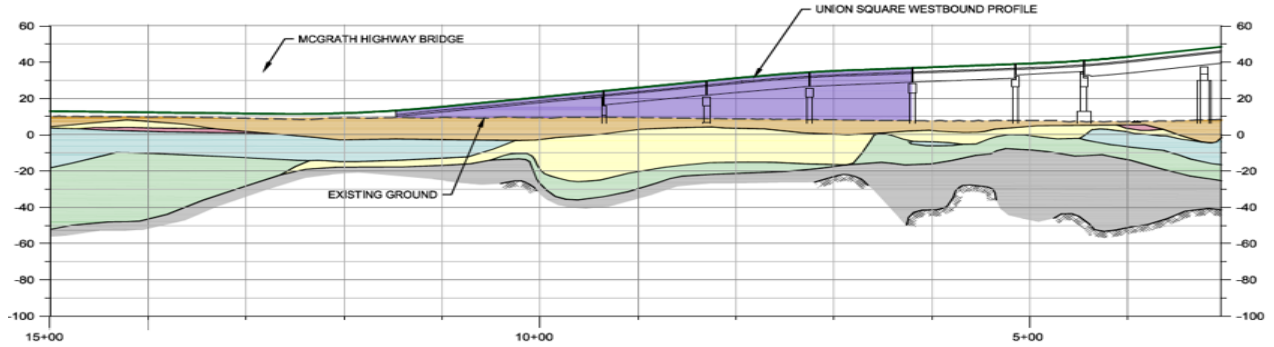


UNION STATION - WESTBOUND

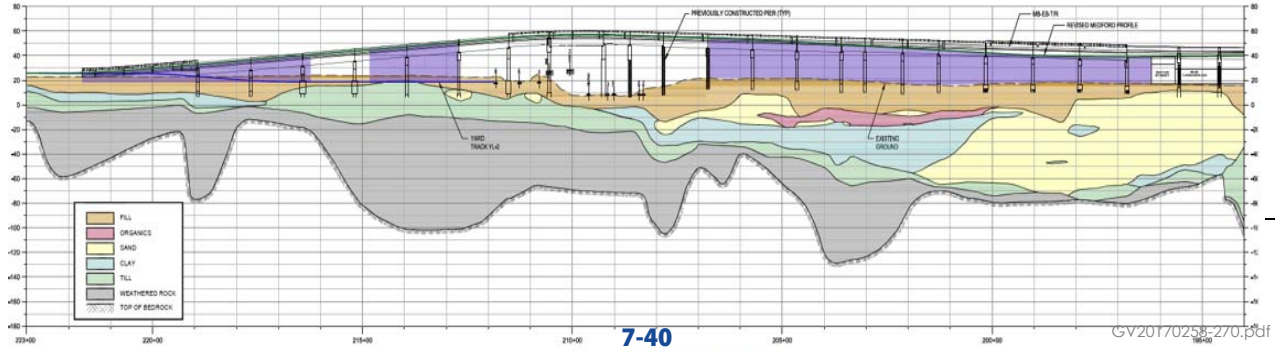

MEDFORD BRANCH - EASTBOUND

GV20170258-270.pdf

Figure ATC-35-3: MSE Wall at Viaduct

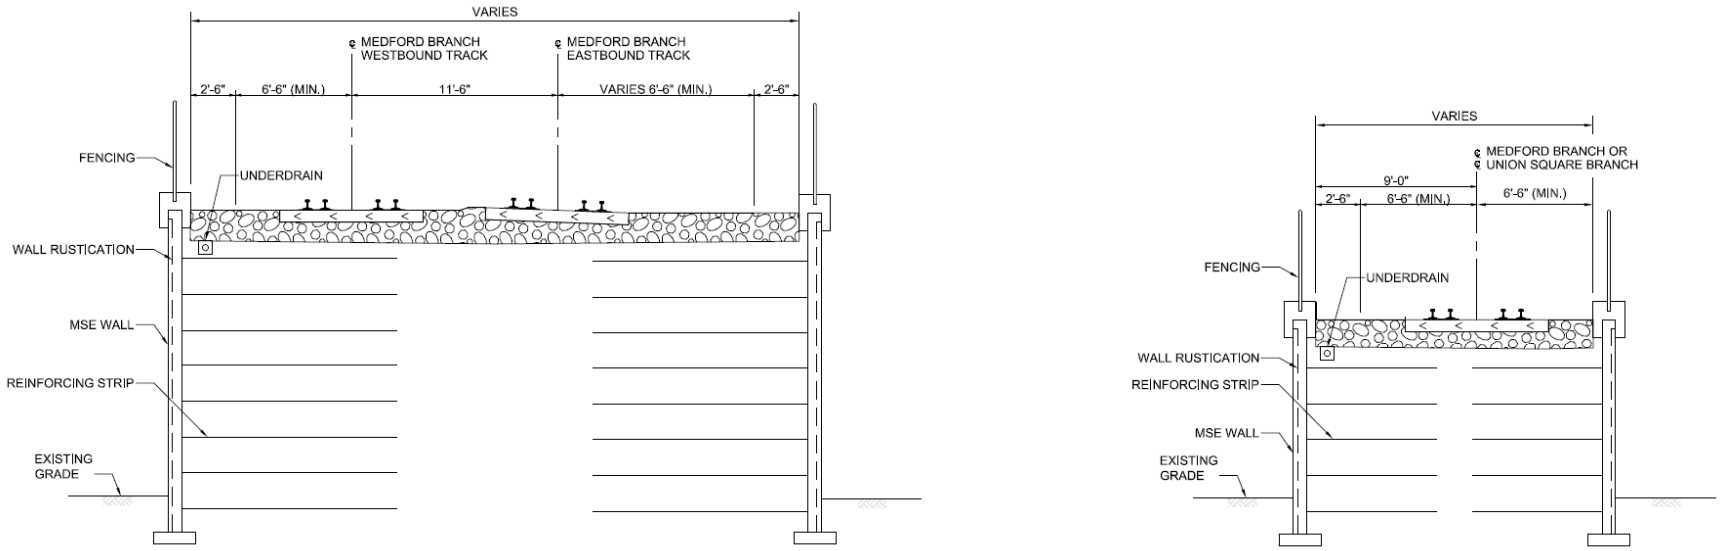

MSE WALL AT VIADUCT

ATC No. 35

MBTA Request for Clarification

ATC Information:

Type of ATC: Formal
Title: GLX Constructors ATC 06 - Viaduct Optimization
Proposer Company: GLX Constructors

Clarification Needed:

The following is MBTA's written request for additional information regarding the ATC Submittal, consistent with Section 3.4 of the Instructions to Proposers. MBTA requests Proposer's prompt response.

Please provide:

- further information regarding how the proposed solution will affect daylight/shadow conditions with respect to the Brick Bottom Condominiums.
- further information regarding routing of Eversource power supply if this proposed solution were accepted and implemented. Please note Eversource's access requirements with respect to in-ground Eversource cables.
- further information (by way of a plan or otherwise) on proposed driving and walking routes to access the signal bungalow, were this proposed solution accepted and implemented.
- information regarding the frequency, methods for ballast tamping and other preventative maintenance due to settlement, with examples of other comparable projects' use and settlement/mitigation/corrective measures taken and procedures in place.

Sent on behalf of Yvelisse Duvergé.

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

FORMAL

ALTERNATIVE TECHNICAL CONCEPTS ("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

JULY 11, 2017 (Final Round)

GLX CONSTRUCTORS FORMAL ATC FORM

VIADUCT OPTIMIZATION

Sections A though P below shall be completed to submit a Formal ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Formal ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. ATC Number

A sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.);

ATC 35

MBTA Preliminary ATC File Number: ATC-000013 – GLX Constructors ATC 07

B. Description and Conceptual Drawings

A description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information;

This ATC replaces three sections of elevated track with MSE walls as follows:

1.) Replace a section of elevated track from approximate Sta. MB-EB 196+00 to Sta. MB-EB 202+00 required on viaduct with an elevated section of track on MSE wall
2.) Replace a section of elevated track from approximate Sta. US-WB 7+75 to Sta. US-WB 11+50 required on viaduct with an elevated section of track on MSE wall
3.) Replace a section of elevated track from approximate Sta. MB-EB 214+00 to Sta. MB-EB 220+00 required on viaduct with an elevated section of track on MSE wall

Please reference Figures ATC-35-1 "Plan View of Proposed MSE Wall Sections" , ATC-35-2 "Profile Views of Proposed MSE Wall Sections" and ATC-35-3 "MSE Wall At Viaduct"

C. Locations and How Used

The locations where, and an explanation of how, the ATC will be used on the Project;

This ATC will be used at approximate Sta. MB-EB 196+00 to Sta. MB-EB 202+00, US-WB 7+75 to Sta. US-WB 11+50, and Sta. MB-EB 214+00 to Sta. MB-EB 220+00 to replace sections of elevated track with MSE walls.

D. Changes in Rail or Transit Operations

Any changes in rail or transit operations requirements associated with the ATC, including ease of operations;

No changes in operations are anticipated as a result of this ATC.

E. Changes in Routine or Capital Maintenance

Any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance;

This ATC will include MSE walls that require less maintenance than an elevated structure and associated bridge deck area.

F. Changes in Anticipated Service Life

Any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC;

MSE wall sections will have a longer service life than the specified bridge sections. This is mainly due to alleviated corrosion or stray current issues associated with elevated bridge structures.

G. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations;

Volume 2, Technical Provisions, Section 1.2.1 General (a) and (b). Volume 2, Exhibit 2B, Project Definition plan sheets: UEV-S-2001, and UWV-S-2000. This ATC replaces sections of elevated concrete structure shown on the Project Definition plans with an MSE wall structure.

H. Justification of Use

An analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed;

This ATC will reduce contaminated excavation and export off site while eliminating contaminated deep foundation spoils. The deep foundations required for an elevated structures are eliminated, thus reducing the deep foundation risk associated with unforeseen conditions. MSE wall construction has lower noise and vibration than elevated structure construction. The reduction in bridge deck provides a significant cost savings to the project.

I. Preliminary Analysis and Quantitative Discussion

A preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation;

No impacts on rail or transit operations are anticipated as a result of this ATC.

J. Impacts on Third Parties

A description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC. Proposers are advised that they may (i) be solely responsible for the cost and schedule impacts of the acquisition of any such Additional Properties, including the cost thereof and obtaining any necessary environmental approvals; (ii) not be entitled to any change order for time or money as a result of site conditions (i.e., hazardous materials, differing site conditions, geotechnical issues, or utilities) on such Additional Properties; and (iii) not be entitled to any change order for time or money as a result of any delay, inability, or cost associated with the acquisition of such Additional Properties;

No impacts to third parties are anticipated as a result of this ATC.

K. History of Use and References

A description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements;

MSE Walls have been used successfully as a part of the Charlotte Area Transit System in Charlotte, North Carolina.

John Mrzygod, City of Charlotte Engineering and Property Management – Charlotte Area Transit System, 704.336.2245, jmrzygod@ci.charlotte.nc.us

L. Additional Risks

A description of added risks to the MBTA or third parties associated with implementing the ATC;

No additional risks to the MBTA or to third parties are anticipated as a result of this ATC.

M. Additional Costs

An estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC;

Additional costs to the MBTA, DB Entity and third parties will not result from this ATC. One of the primary purposes of this ATC is cost reduction.

N. Estimated Price Adjustment

An estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented;

This ATC will result in an estimated savings of $10,000,000. The ATC pricing as shown in this proposal is an all inclusive price. All price deducts and/or adds have been considered, and the resulting price adjustment is offered as shown.

O. Schedule Adjustment

An estimate of the schedule adjustment, should the ATC be approved and implemented; and

This ATC does not require any schedule adjustment.

P. Analysis of Quality, Performance, and Reliability

An analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents.

This ATC will provide an equal quality, performance, and reliability than the specified elevated track section. This ATC would increase the service life while reducing maintenance costs associated with

maintaining corrosion resistance.

Figure ATC-35-1: Plan View of Proposed MSE Wall Sections



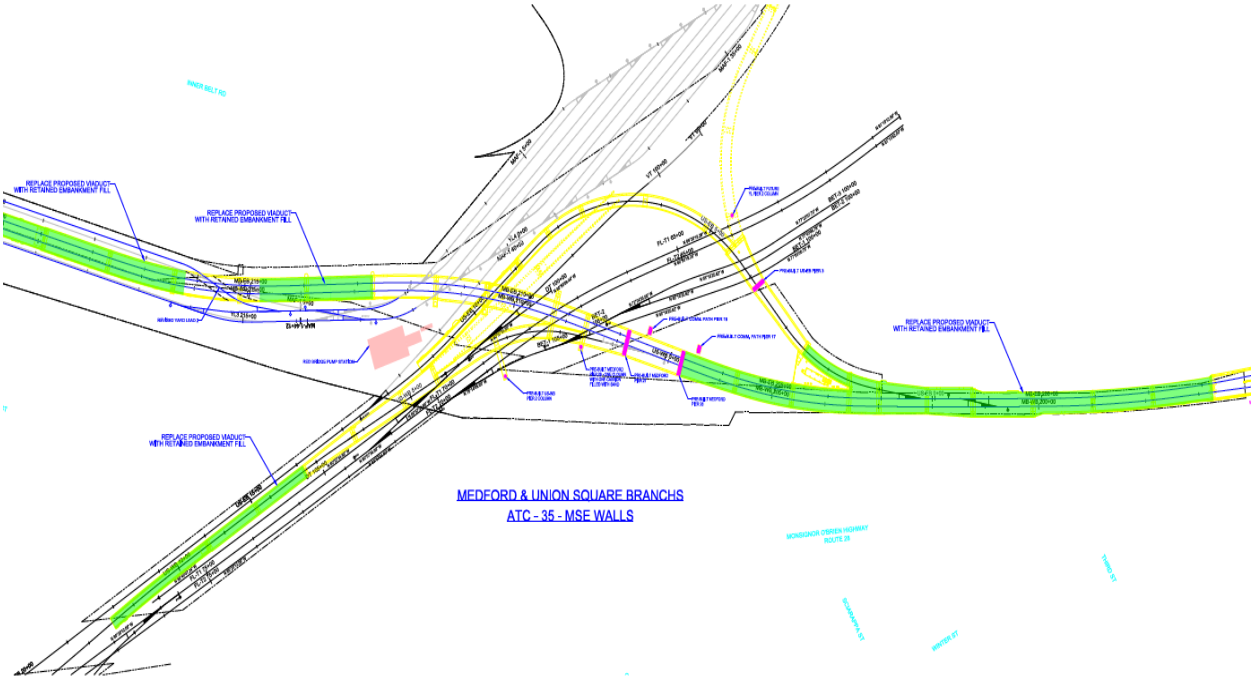


Figure ATC-35-2: Profile Views of Proposed MSE Wall Sections

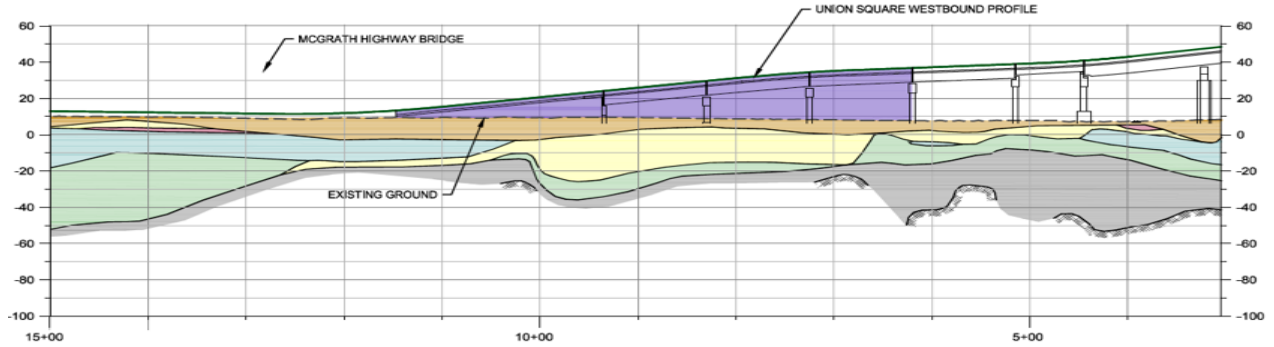


UNION STATION - WESTBOUND

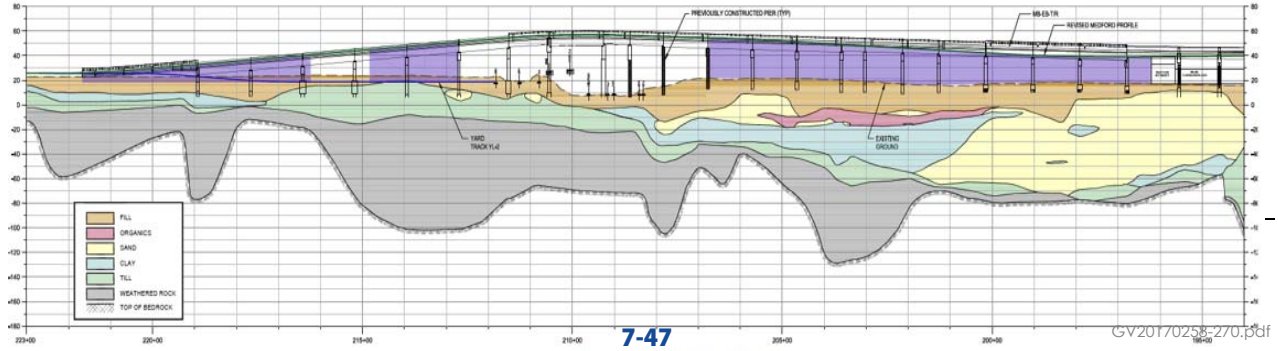

MEDFORD BRANCH - EASTBOUND

GV20170258-270.pdf

Figure ATC-35-3: MSE Wall at Viaduct

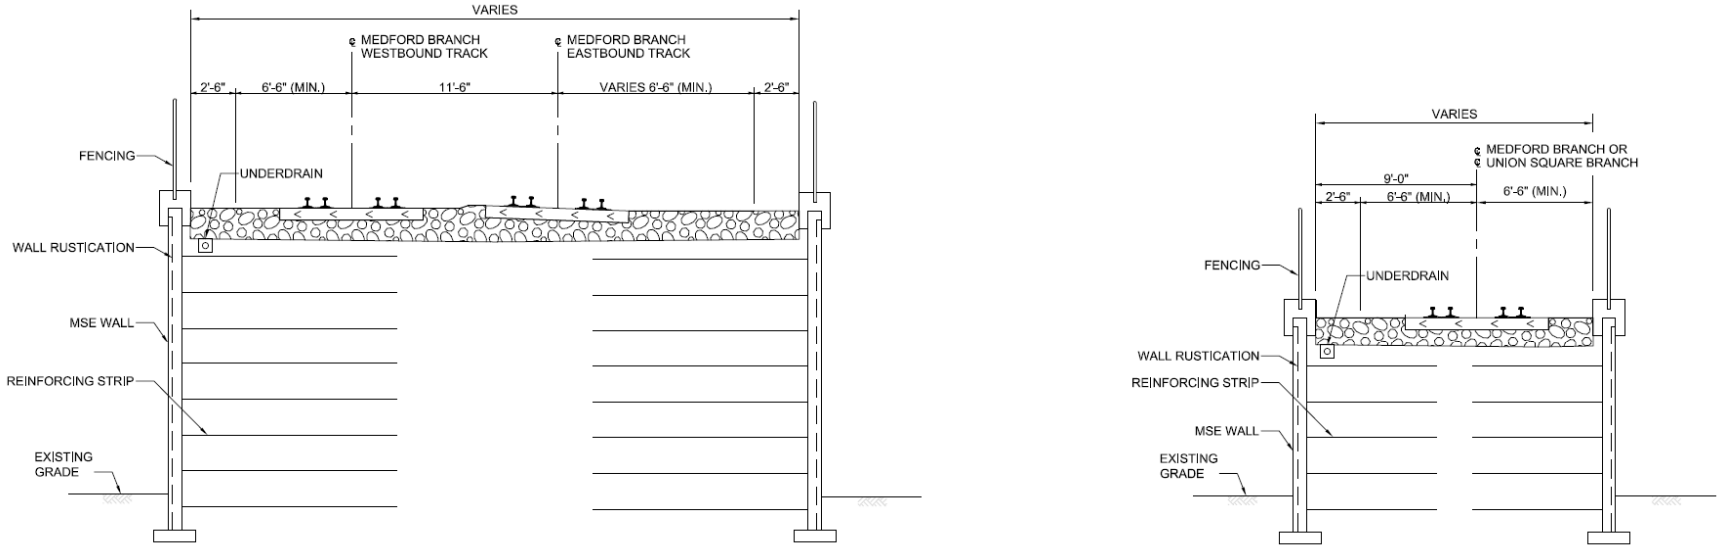

MSE WALL AT VIADUCT

Massachusetts Bay Transportation Authority

GLX

Green Line Extension
Formal Alternative Technical Concept (ATC) Eligibility Checklist

Date: 07-13-2013

Reviewer: Hemal Patel

Proposal Team: GLX Constructors

ATC Number: GLXC ATC 06-GLX Constructors_ATC 35_Formal_17071

Eligibility Determination

		Yes	No
A.	**Identification:** Includes a sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.)	✔	
B.	**General Description:** Includes a description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information	✔	
C.	**Information:** Identifies the locations where, and an explanation of how, the ATC will be used on the Project	✔	
D.	**Changes to Operations Requirements:** Identifies any changes in rail or transit operations requirements associated with the ATC, including ease of operations	✔	
E.	**Changes to Maintenance Requirements:** Identifies any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance	✔	
F.	**Service Life** 1. Identifies any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC	✔	
G.	**Requirements References:** Identifies references to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations	✔	
H.	**Justifications:** Includes an analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed	✔	

		Yes	No
I.	**Internal Impacts:** Includes a preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation	✔	
J.	**External Impacts:** Includes a description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC	✔	
K.	**Previous Use of ATC:** Includes a description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements	✔	
L.	**Additional Risks:** Includes a description of added risks to the MBTA or third parties associated with implementing the ATC	✔	
M.	**Additional Cost:** Includes an estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC	✔	
N.	**Cost Savings:** Includes an estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented	✔	
O.	**Schedule:** Includes an estimate of the schedule adjustment, should the ATC be approved and implemented	✔	
P.	**Equal or Better:** Includes an analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents	✔	

Name: Hemal Patel

Signature: _____

ATC No. 35

Response to RFI 1

MBTA Clarification Needed – Item 1:

Please provide further information regarding how the proposed solution will affect daylight/shadow conditions with respect to the Brick Bottom Condominiums.

GLX Clarification - Item 1:

The proposed ATC 35, to use MSE walls as a substitute for certain elevated spans along the Viaduct, has no impact on the proposed track elevation, nor does the ATC impact track alignment. Furthermore, the Viaduct parapet walls and maintenance walkways shown on the MBTA Project Definition Plans in Exhibit 2B will remain with incorporation of this ATC. Consequently the extents of the shadow lines generated by this ATC will be consistent with the shadow lines generated by the Viaduct that is defined on the Project Definition Plans.

With the elevated spans of the Viaduct, there is a potential for sunlight to extend under the spans. But given the ratios of structure width to the height from grade to underside of structure, there will be minimal opportunity for sun light to extend from one side of the viaduct to the other side, beneath any span in the vicinity of the Brick Bottom Condominiums. Consequently the solid barrier generated by the MSE wall, as proposed by ATC 35, will not produce a noticeable change the levels of lighting extending from one side of the structure to the other.

Attached are figures to further show the relationship between the Brick Bottom Condominiums and the proposed Viaduct/MSE wall structure:

Figure ATC 35-RFI-1-1: Ariel view of existing conditions at Brick Bottom Condominiums.
Figure ATC 35-RFI-1-2: Plan view showing Brick Bottom Condominiums relative to the proposed track alignment and proposed Viaduct/MSE Wall structure.
Figure ATC 35-RFI-1-3: Profile of proposed Viaduct/MSE Wall structure on Medford Branch with Brick Bottom Condominiums outline highlighted.
Figure ATC 35-RFI-1-4: Profile of proposed Viaduct/MSE Wall structure on Union Square Branch with Brick Bottom Condominiums outline highlighted.

MBTA Clarification Needed – Item 2:

Please provide further information regarding routing of Eversource power supply if this proposed solution were accepted and implemented. Please note Eversource's access requirements with respect to in-ground Eversource cables.

GLX Clarification - Item 2:

STV understands the Eversource access requirements for their power lines. The approval of this ATC will require reconfiguring the power feed to the Red Bridge Sub Station. The GLX Constructors team will develop a power feed configuration that will meet Eversource access requirements.

MBTA Clarification Needed – Item 3:

Please provide further information (by way of a plan or otherwise) on proposed driving and walking routes to access the signal bungalow, were this proposed solution accepted and implemented.

GLX Clarification - Item 3:

Please reference attached **Figure ATC 35-RFI-1-5**: Concept Site Plan Demonstrating Options to Access Signal Bungalow. Please note that this site plan shows the most complex of potential conditions which includes the Additive Option of continuing the Community Path beyond Eat Somerville Station. This sketch is representative of only one such options but we are confident that an acceptable means of access the bungalow could be provided.

MBTA Clarification Needed – Item 4:

Please provide information regarding the frequency, methods for ballast tamping and other preventative maintenance due to settlement, with examples of other comparable projects' use and settlement/mitigation/corrective measures taken and procedures in place.

GLX Clarification - Item 4:

Portions of the proposed MSE embankment fill will be constructed in areas where there are compressible soil underlying the surficial fill layer. In these areas, ground improvement will be performed using deep mixing technology to transfer the weight of the embankment fill to the top of the relatively dense glacial till that underlies these compressible soils. The unconfined compressive strength of the soil mix columns will be approximately 250 psi, which is much greater than that of the glacial till. Cluster of deep mixing columns will be installed so that the spacing between them does not exceed 11 feet. Multiple layers of geogrid reinforcement will be used to transfer the weight of the embankment fill to the deep mixing columns. Therefore, there will not be any settlement associated with compression of the existing fill or underlying compressible soils.

The deep mixing methods has been adopted by the Federal Highway Administration and is described in their Publication No. FHWA-HRT-13-046 dated October 2013. Deep mixing was also used successfully in the Fort Point Channel area of the Central Artery Tunnel project with similar ground conditions.

On other portions of the alignment, the embankment fill will be placed over existing fill material that is underlain be relatively incompressible soils. Therefore, settlement should not be an issue.

GLX Constructors will install settlement monitoring points on the MSE embankment fill to confirm any ongoing ground movements prior to placement of the track ballast. Also, any possible settlement of the ballasted track after track installation can be corrected during routine maintenance surfacing.

As stated in the Formal ATC Submission, MSE Walls have been used successfully as a part of the Charlotte Area Transit System CATS) in Charlotte, North Carolina, among other location across the country. Phase 1 of CATS, known as the Blue Line Corridor, has now been in operation for about 7 years. As part of CATS, a back-to-back MSE Wall system, similar to what we are proposing and sometimes up to 50 feet high, supports light rail tracks. The light rail then transitions on to a bridge structure, again

similar to our ATC proposal. This wall/viaduct system has been performing well, and is being replicated as part of Phase 2 (the Blue Line Extension) which is now in construction.

A contact reference on the project is John Mrzygod, City of Charlotte Engineering and Property Management – Charlotte Area Transit System,
704.336.2245, jmrzygod@ci.charlotte.nc.us

Figure ATC 35-RFI-1-1: Ariel view of existing conditions at Brick Bottom Condominiums.

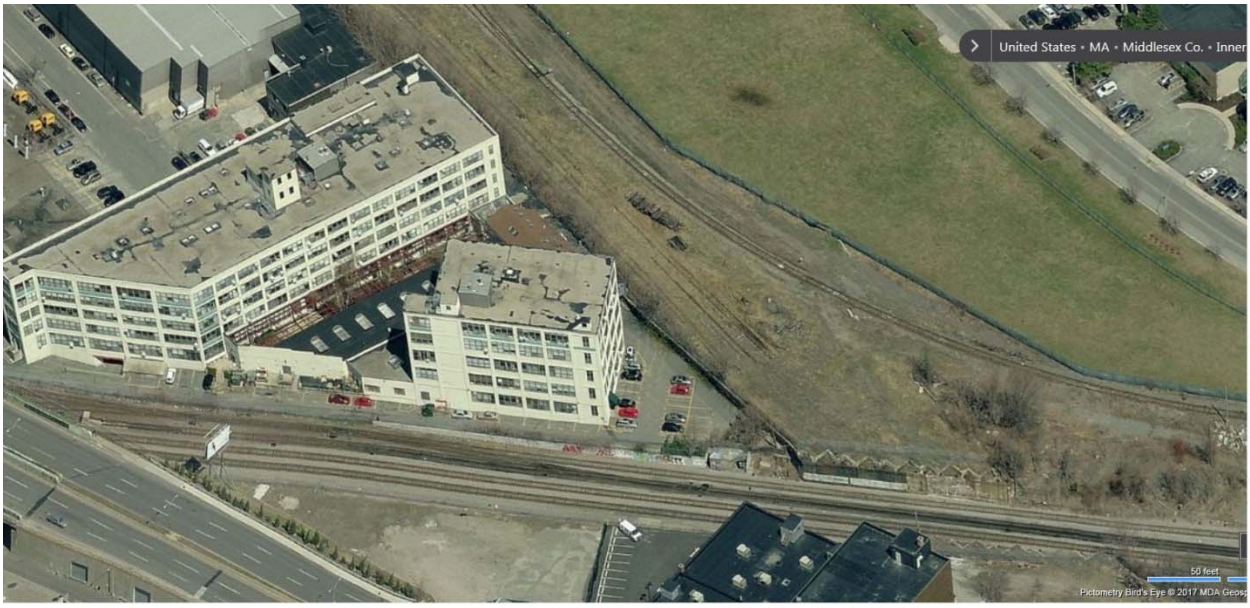


Figure ATC 35-RFI-1-2: Plan view showing Brick Bottom Condominiums relative to the proposed track alignment and proposed Viaduct/MSE Wall structure.

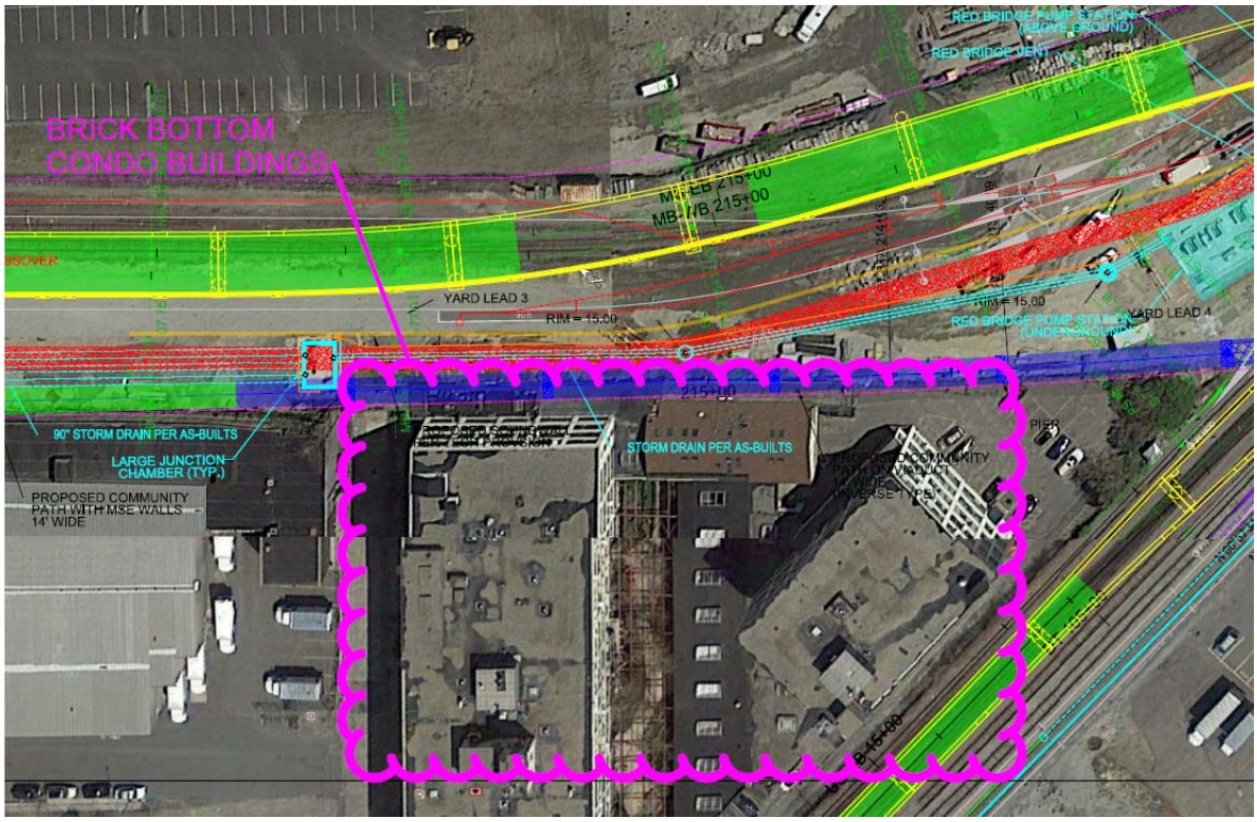


Figure ATC 35-RFI-1-3: Profile of proposed Viaduct/MSE Wall structure on Medford Branch with Brick Bottom Condominiums outline highlighted.

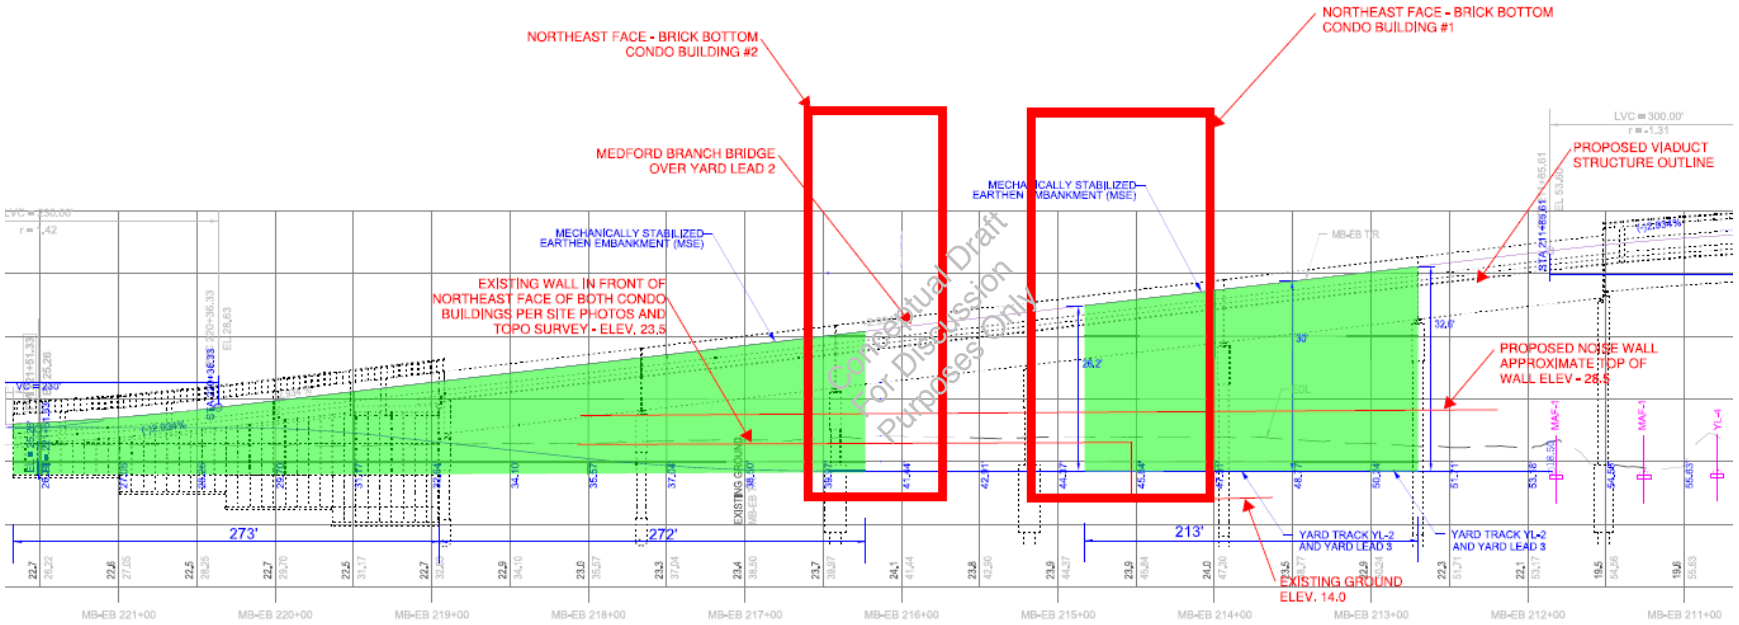


Figure ATC 35-RFI-1-4: Profile of proposed Viaduct/MSE Wall structure on Union Square Branch with Brick Bottom Condominiums outline highlighted.


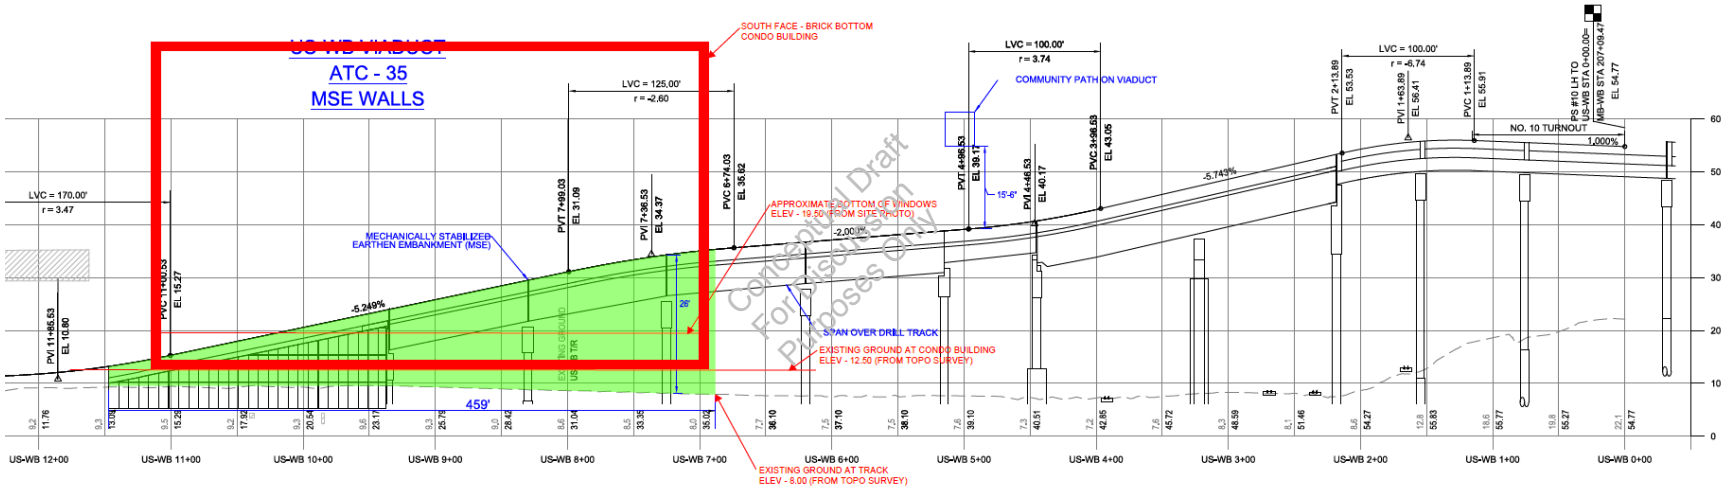


Figure ATC 35-RFI-1-5: Concept Site Plan Demonstrating Options to Access Signal Bungalow

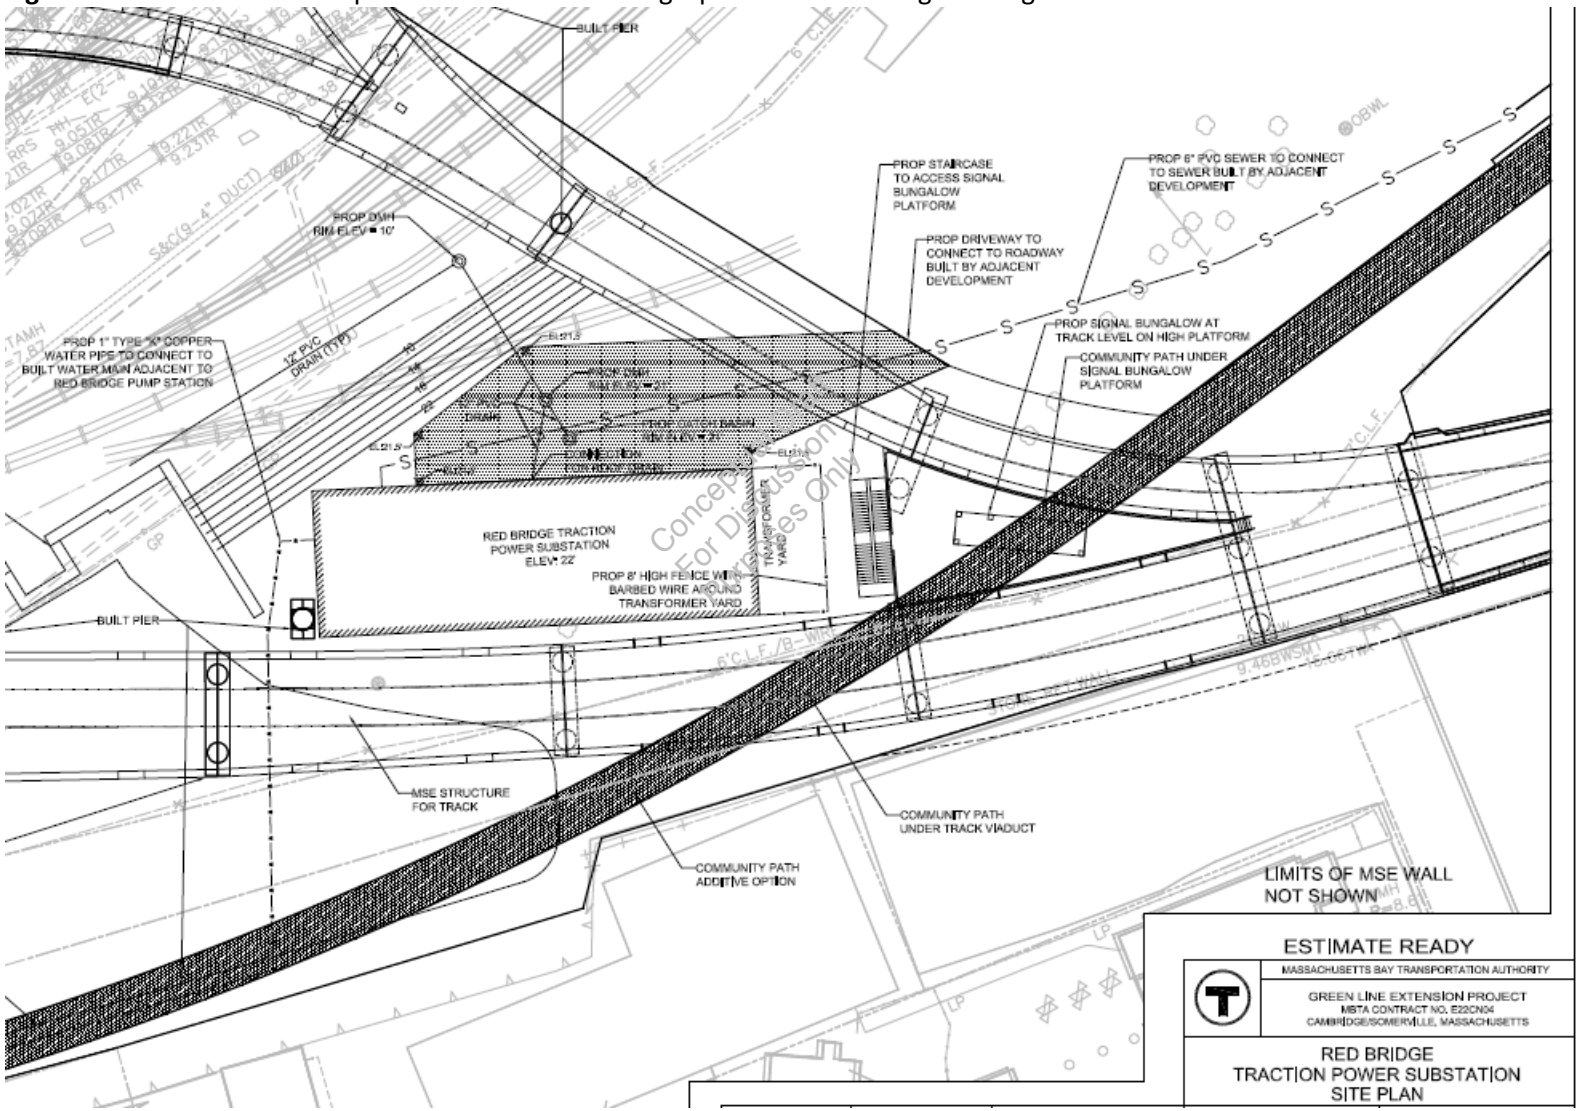

ATC Information:

Type of ATC: Formal
Title: GLX Constructors ATC 06 - Viaduct Optimization
Proposer Company: GLX Constructors

Clarification Needed:

The following is MBTA's written request for additional information regarding the ATC Submittal, consistent with Section 3.4 of the Instructions to Proposers. MBTA requests Proposer's prompt response.

Please provide:

- further information regarding how the proposed solution will affect daylight/shadow conditions with respect to the Brick Bottom Condominiums.
- further information regarding routing of Eversource power supply if this proposed solution were accepted and implemented. Please note Eversource's access requirements with respect to in-ground Eversource cables.
- further information (by way of a plan or otherwise) on proposed driving and walking routes to access the signal bungalow, were this proposed solution accepted and implemented.
- information regarding the frequency, methods for ballast tamping and other preventative maintenance due to settlement, with examples of other comparable projects' use and settlement/mitigation/corrective measures taken and procedures in place.

Sent on behalf of Yvelisse Duvergé.

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

FORMAL

ALTERNATIVE TECHNICAL CONCEPTS ("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

JULY 11, 2017 (Final Round)

VIADUCT OPTIMIZATION

Sections A though P below shall be completed to submit a Formal ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Formal ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. ATC Number

A sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.);

ATC 35

MBTA Preliminary ATC File Number: ATC-000013 – GLX Constructors ATC 07

B. Description and Conceptual Drawings

A description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information;

This ATC replaces three sections of elevated track with MSE walls as follows:

1.) Replace a section of elevated track from approximate Sta. MB-EB 196+00 to Sta. MB-EB 202+00 required on viaduct with an elevated section of track on MSE wall
2.) Replace a section of elevated track from approximate Sta. US-WB 7+75 to Sta. US-WB 11+50 required on viaduct with an elevated section of track on MSE wall
3.) Replace a section of elevated track from approximate Sta. MB-EB 214+00 to Sta. MB-EB 220+00 required on viaduct with an elevated section of track on MSE wall

Please reference Figures ATC-35-1 "Plan View of Proposed MSE Wall Sections" , ATC-35-2 "Profile Views of Proposed MSE Wall Sections" and ATC-35-3 "MSE Wall At Viaduct"

C. Locations and How Used

The locations where, and an explanation of how, the ATC will be used on the Project;

This ATC will be used at approximate Sta. MB-EB 196+00 to Sta. MB-EB 202+00, US-WB 7+75 to Sta. US-WB 11+50, and Sta. MB-EB 214+00 to Sta. MB-EB 220+00 to replace sections of elevated track with MSE walls.

D. Changes in Rail or Transit Operations

Any changes in rail or transit operations requirements associated with the ATC, including ease of operations;

No changes in operations are anticipated as a result of this ATC.

E. Changes in Routine or Capital Maintenance

Any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance;

This ATC will include MSE walls that require less maintenance than an elevated structure and associated bridge deck area.

F. Changes in Anticipated Service Life

Any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC;

MSE wall sections will have a longer service life than the specified bridge sections. This is mainly due to alleviated corrosion or stray current issues associated with elevated bridge structures.

G. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations;

Volume 2, Technical Provisions, Section 1.2.1 General (a) and (b). Volume 2, Exhibit 2B, Project Definition plan sheets: UEV-S-2001, and UWV-S-2000. This ATC replaces sections of elevated concrete structure shown on the Project Definition plans with an MSE wall structure.

H. Justification of Use

An analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed;

This ATC will reduce contaminated excavation and export off site while eliminating contaminated deep foundation spoils. The deep foundations required for an elevated structures are eliminated, thus reducing the deep foundation risk associated with unforeseen conditions. MSE wall construction has lower noise and vibration than elevated structure construction. The reduction in bridge deck provides a significant cost savings to the project.

I. Preliminary Analysis and Quantitative Discussion

A preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation;

No impacts on rail or transit operations are anticipated as a result of this ATC.

J. Impacts on Third Parties

A description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC. Proposers are advised that they may (i) be solely responsible for the cost and schedule impacts of the acquisition of any such Additional Properties, including the cost thereof and obtaining any necessary environmental approvals; (ii) not be entitled to any change order for time or money as a result of site conditions (i.e., hazardous materials, differing site conditions, geotechnical issues, or utilities) on such Additional Properties; and (iii) not be entitled to any change order for time or money as a result of any delay, inability, or cost associated with the acquisition of such Additional Properties;

No impacts to third parties are anticipated as a result of this ATC.

K. History of Use and References

A description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements;

MSE Walls have been used successfully as a part of the Charlotte Area Transit System in Charlotte, North Carolina.

John Mrzygod, City of Charlotte Engineering and Property Management – Charlotte Area Transit System, 704.336.2245, jmrzygod@ci.charlotte.nc.us

L. Additional Risks

A description of added risks to the MBTA or third parties associated with implementing the ATC;

No additional risks to the MBTA or to third parties are anticipated as a result of this ATC.

M. Additional Costs

An estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC;

Additional costs to the MBTA, DB Entity and third parties will not result from this ATC. One of the primary purposes of this ATC is cost reduction.

N. Estimated Price Adjustment

An estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented;

This ATC will result in an estimated savings of $10,000,000. The ATC pricing as shown in this proposal is an all inclusive price. All price deducts and/or adds have been considered, and the resulting price adjustment is offered as shown.

O. Schedule Adjustment

An estimate of the schedule adjustment, should the ATC be approved and implemented; and

This ATC does not require any schedule adjustment.

P. Analysis of Quality, Performance, and Reliability

An analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents.

This ATC will provide an equal quality, performance, and reliability than the specified elevated track section. This ATC would increase the service life while reducing maintenance costs associated with

maintaining corrosion resistance.

Figure ATC-35-1: Plan View of Proposed MSE Wall Sections



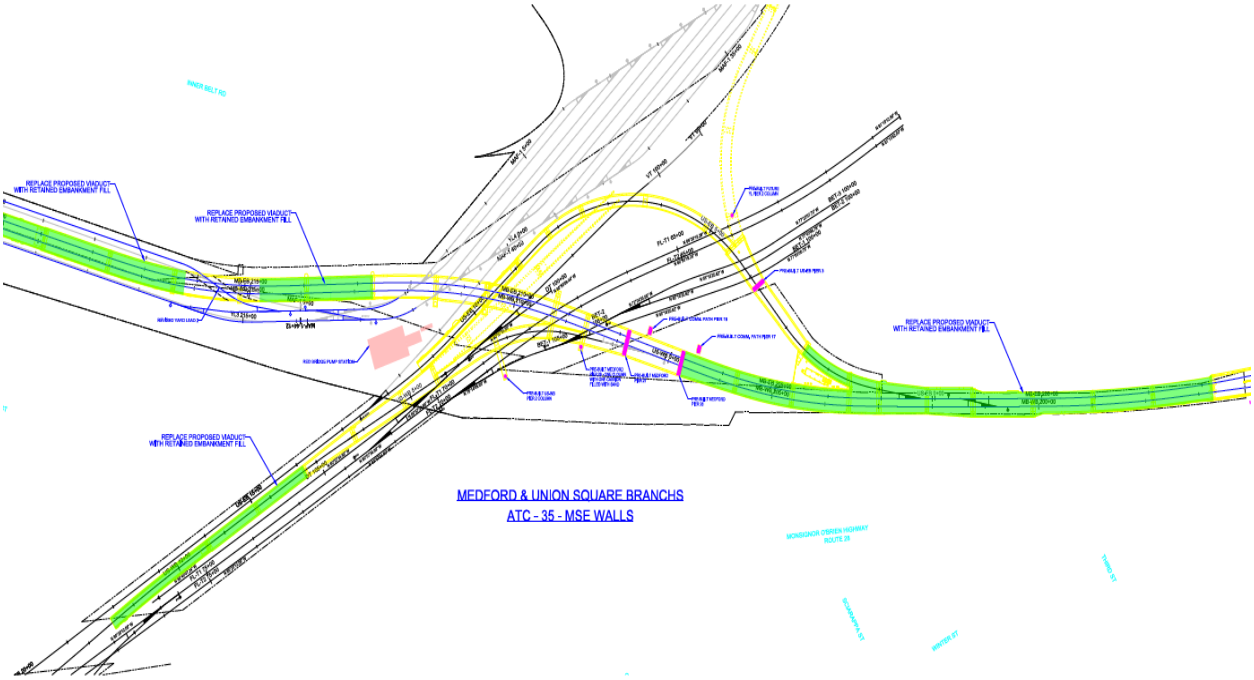


Figure ATC-35-2: Profile Views of Proposed MSE Wall Sections

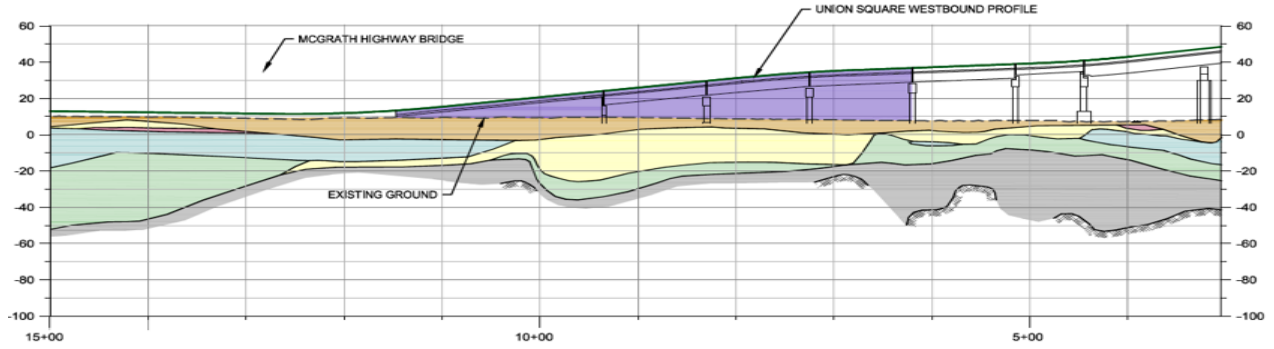


UNION STATION - WESTBOUND

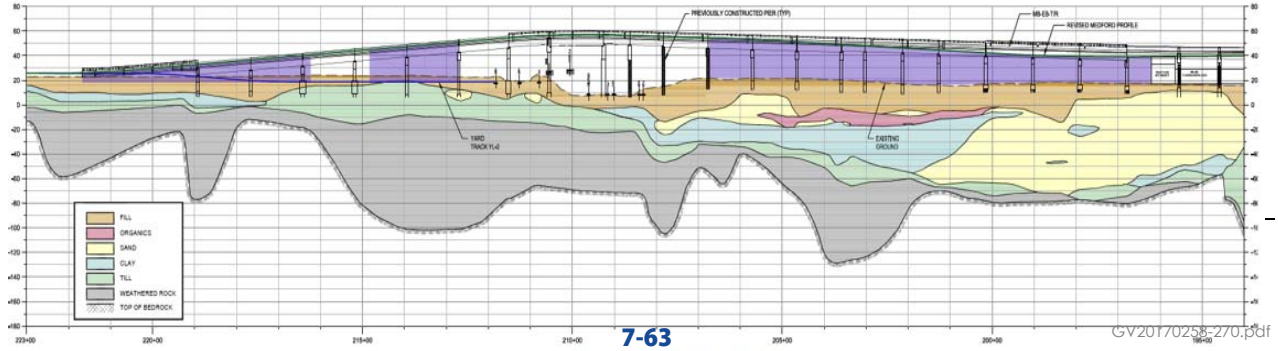

MEDFORD BRANCH - EASTBOUND

GV20170258-270.pdf

Figure ATC-35-3: MSE Wall at Viaduct

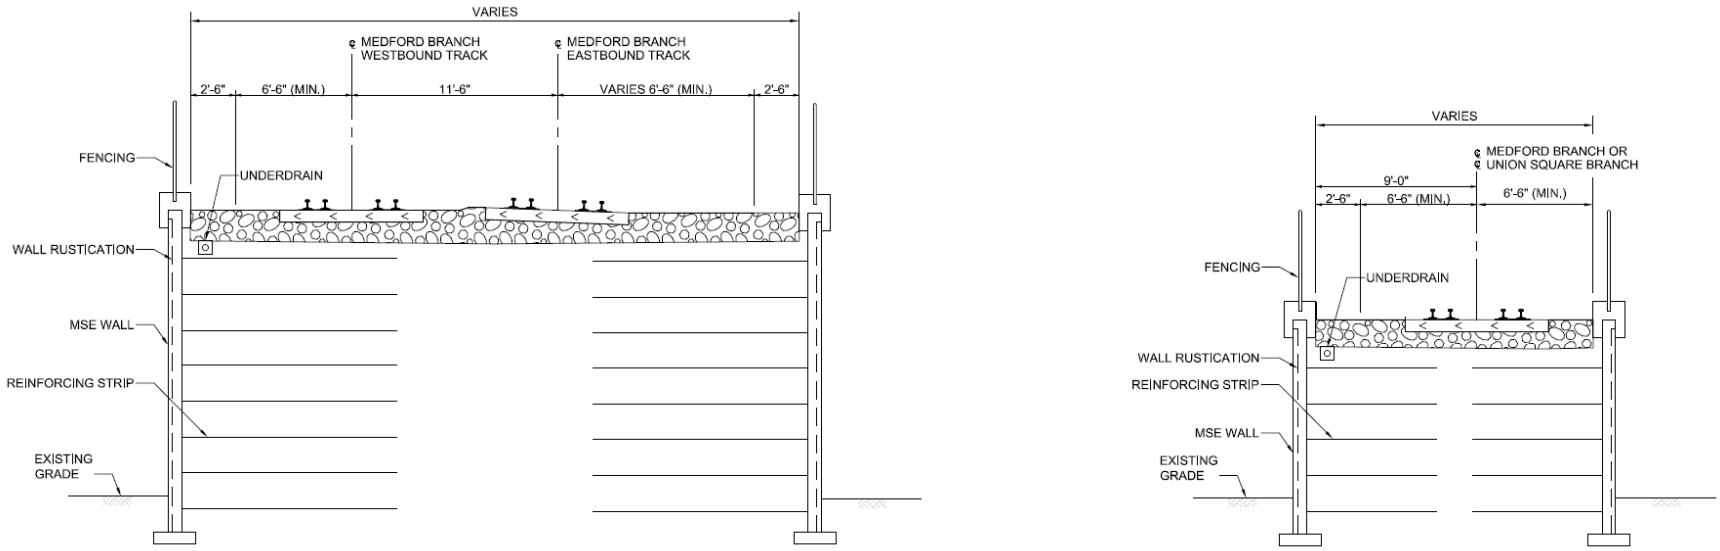

MSE WALL AT VIADUCT

Massachusetts Bay Transportation Authority

GLX

Green Line Extension
Formal Alternative Technical Concept (ATC) Eligibility Checklist

Date: 07-13-2013

Reviewer: Hemal Patel

Proposal Team: GLX Constructors

ATC Number: GLXC ATC 06-GLX Constructors_ATC 35_Formal_17071

Eligibility Determination

		Yes	No
A.	**Identification:** Includes a sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.)	✔	
B.	**General Description:** Includes a description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information	✔	
C.	**Information:** Identifies the locations where, and an explanation of how, the ATC will be used on the Project	✔	
D.	**Changes to Operations Requirements:** Identifies any changes in rail or transit operations requirements associated with the ATC, including ease of operations	✔	
E.	**Changes to Maintenance Requirements:** Identifies any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance	✔	
F.	**Service Life** 1. Identifies any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC	✔	
G.	**Requirements References:** Identifies references to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations	✔	
H.	**Justifications:** Includes an analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed	✔	

		Yes	No
I.	**Internal Impacts:** Includes a preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation	✔	
J.	**External Impacts:** Includes a description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC	✔	
K.	**Previous Use of ATC:** Includes a description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements	✔	
L.	**Additional Risks:** Includes a description of added risks to the MBTA or third parties associated with implementing the ATC	✔	
M.	**Additional Cost:** Includes an estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC	✔	
N.	**Cost Savings:** Includes an estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented	✔	
O.	**Schedule:** Includes an estimate of the schedule adjustment, should the ATC be approved and implemented	✔	
P.	**Equal or Better:** Includes an analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents	✔	

Name: Hemal Patel

Signature: _____

ATC No. 35

MBTA Conditional Acceptance of Formal Submission

ATC Information:

Type of ATC: Formal
Title: GLX Constructors ATC 06 - Viaduct Optimization
Proposer Company: GLX Constructors


Final Disposition:

Sent on behalf of Yvelisse Duvergé. The MBTA accepts this ATC Submittal for inclusion in the Proposal so long as Proposer, as DB Entity, meets the following conditions as part of the performance of the Work under the Contract Documents:

- MSE walls must be designed for adequate bearing capacity and settlement of foundation soils beneath the embankment in accordance with Sections 8 and 15 of the Technical Provisions, as evidenced during the detailed design review submissions per Section 2.7 of the Technical Provisions. If required in design, soil mixed columns are acceptable, but only if the conditions that warrant them apply, and use is in accordance with the Contract Documents.
- MSE wall design shall also comply with other applicable MassDOT/MBTA requirements (e.g., aesthetics) listed in the Contract Documents.
- MSE walls shall be limited to heights not exceeding the width of the structure. Where guideway height and site conditions require height to exceed width, then DB Entity may not use MSE walls but instead viaduct-type structures as required under the unmodified Technical Provisions.
- MSE walls shall not be used in the vicinity of the Brickbottom development (ca. 1 Fitchburg St., Somerville, MA). DB Entity shall design and construct viaduct type structures in such location. The "vicinity" of the Brickbottom development is as depicted in the modified ATC figure 35-1 provided with this response.

Consistent with Section 3 of the ITP, if implementation of this ATC will require approval by a third party (e.g., a governmental entity), Proposer will have full responsibility for, and bear the full risk of, obtaining any such approvals after execution of the DB Contract and submission of data, provided, however, that the MBTA shall retain its role as liaison with any governmental entities as more particularly described in the Contract Documents. If any required third-party approval is not subsequently granted with the result that the Proposer must comply with the requirements of the original Contract Documents, the Proposer will not be entitled to additional compensation or time under the DB Contract.

Figure ATC-35-1: Plan View of Proposed MSE Wall Sections

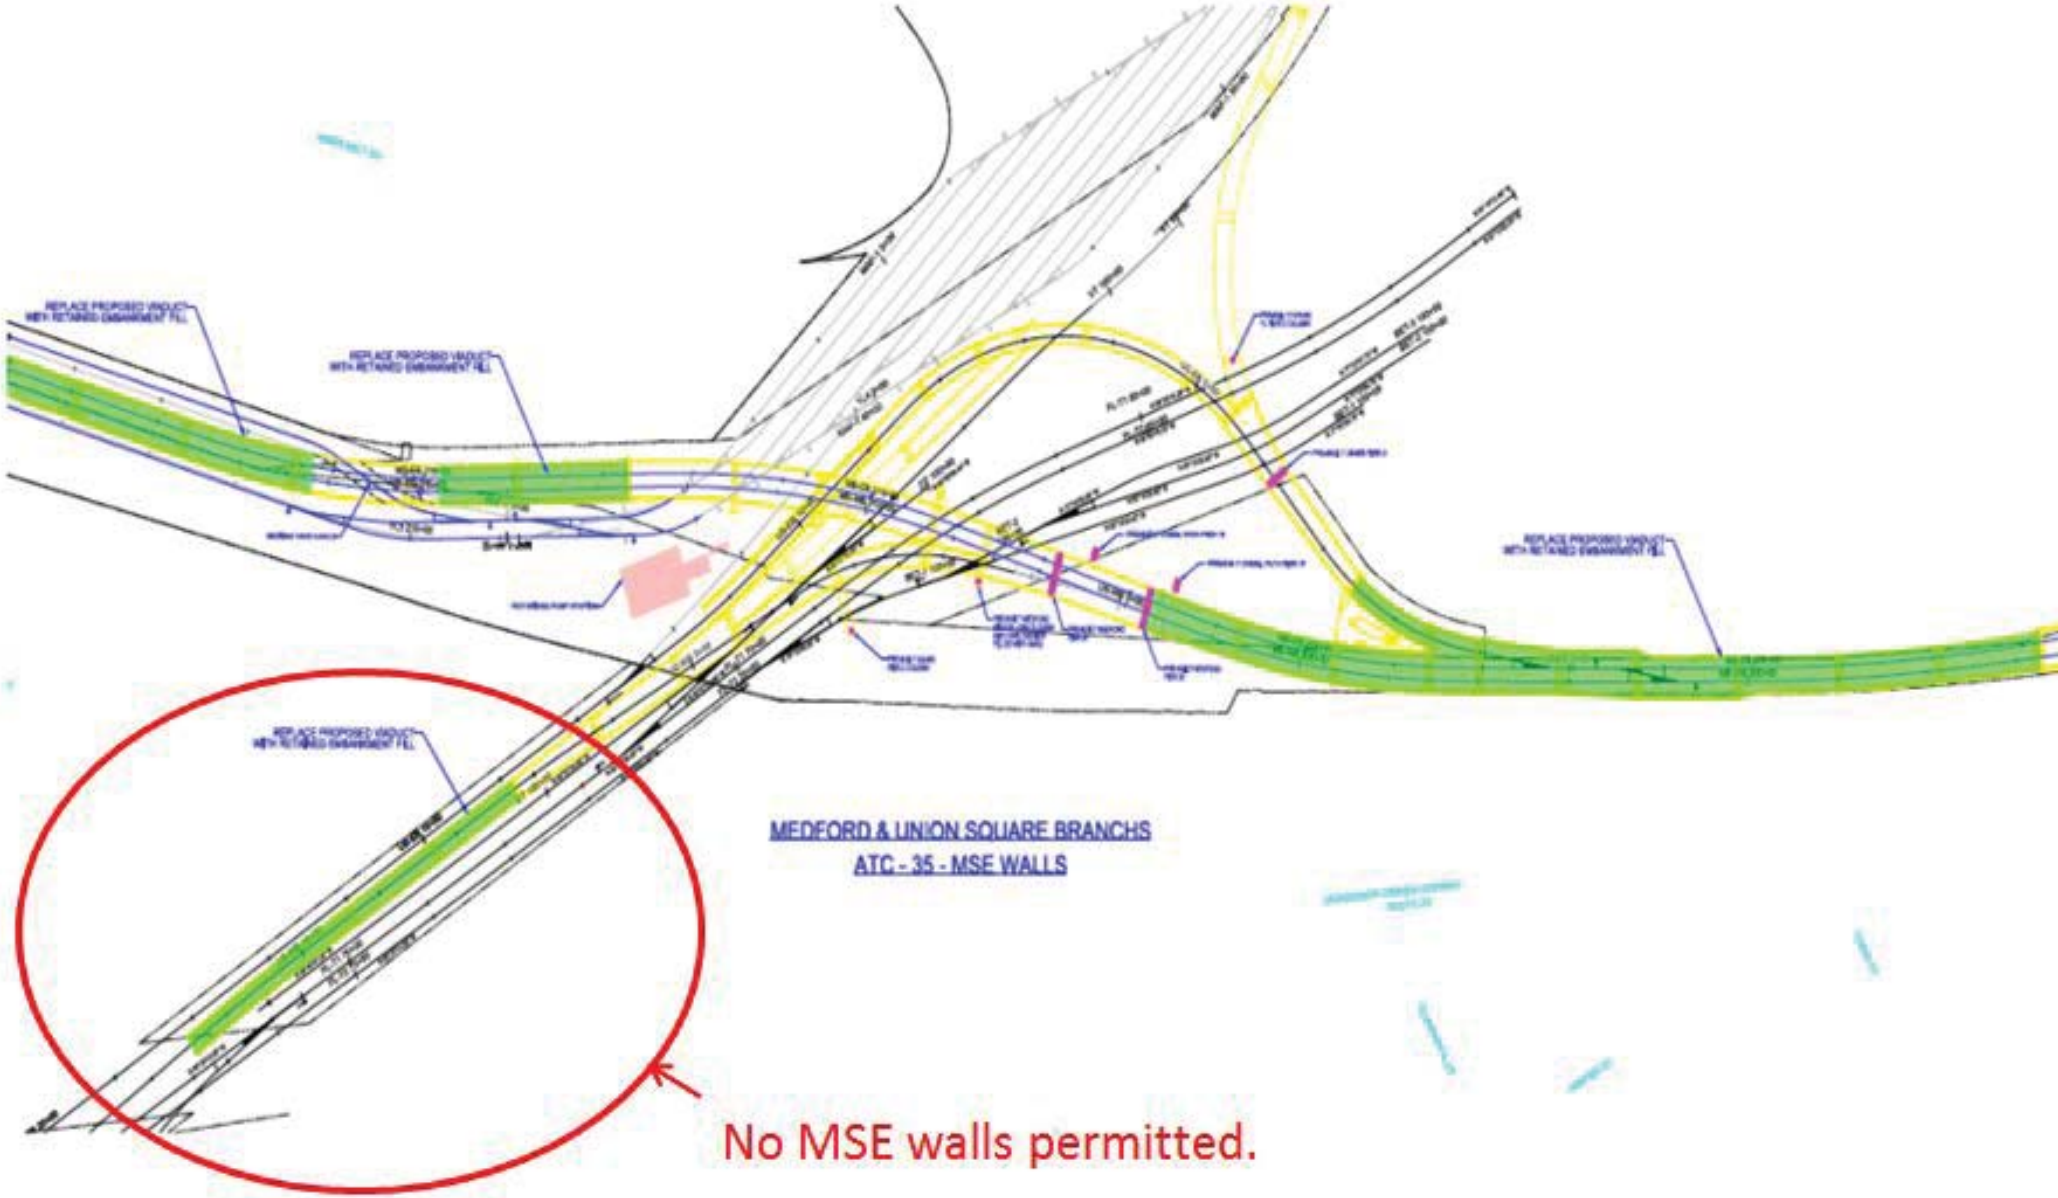

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

FORMAL

ALTERNATIVE TECHNICAL CONCEPTS ("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

JULY 11, 2017 (Final Round)

GLX CONSTRUCTORS FORMAL ATC FORM

VIADUCT OPTIMIZATION

Sections A though P below shall be completed to submit a Formal ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Formal ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. ATC Number

A sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.);

ATC 35

MBTA Preliminary ATC File Number: ATC-000013 – GLX Constructors ATC 07

B. Description and Conceptual Drawings

A description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information;

This ATC replaces three sections of elevated track with MSE walls as follows:

1.) Replace a section of elevated track from approximate Sta. MB-EB 196+00 to Sta. MB-EB 202+00 required on viaduct with an elevated section of track on MSE wall
2.) Replace a section of elevated track from approximate Sta. US-WB 7+75 to Sta. US-WB 11+50 required on viaduct with an elevated section of track on MSE wall
3.) Replace a section of elevated track from approximate Sta. MB-EB 214+00 to Sta. MB-EB 220+00 required on viaduct with an elevated section of track on MSE wall

Please reference Figures ATC-35-1 "Plan View of Proposed MSE Wall Sections" , ATC-35-2 "Profile Views of Proposed MSE Wall Sections" and ATC-35-3 "MSE Wall At Viaduct"

C. Locations and How Used

The locations where, and an explanation of how, the ATC will be used on the Project;

This ATC will be used at approximate Sta. MB-EB 196+00 to Sta. MB-EB 202+00, US-WB 7+75 to Sta. US-WB 11+50, and Sta. MB-EB 214+00 to Sta. MB-EB 220+00 to replace sections of elevated track with MSE walls.

D. Changes in Rail or Transit Operations

Any changes in rail or transit operations requirements associated with the ATC, including ease of operations;

No changes in operations are anticipated as a result of this ATC.

E. Changes in Routine or Capital Maintenance

Any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance;

This ATC will include MSE walls that require less maintenance than an elevated structure and associated bridge deck area.

F. Changes in Anticipated Service Life

Any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC;

MSE wall sections will have a longer service life than the specified bridge sections. This is mainly due to alleviated corrosion or stray current issues associated with elevated bridge structures.

G. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations;

Volume 2, Technical Provisions, Section 1.2.1 General (a) and (b). Volume 2, Exhibit 2B, Project Definition plan sheets: UEV-S-2001, and UWV-S-2000. This ATC replaces sections of elevated concrete structure shown on the Project Definition plans with an MSE wall structure.

H. Justification of Use

An analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed;

This ATC will reduce contaminated excavation and export off site while eliminating contaminated deep foundation spoils. The deep foundations required for an elevated structures are eliminated, thus reducing the deep foundation risk associated with unforeseen conditions. MSE wall construction has lower noise and vibration than elevated structure construction. The reduction in bridge deck provides a significant cost savings to the project.

I. Preliminary Analysis and Quantitative Discussion

A preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation;

No impacts on rail or transit operations are anticipated as a result of this ATC.

J. Impacts on Third Parties

A description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC. Proposers are advised that they may (i) be solely responsible for the cost and schedule impacts of the acquisition of any such Additional Properties, including the cost thereof and obtaining any necessary environmental approvals; (ii) not be entitled to any change order for time or money as a result of site conditions (i.e., hazardous materials, differing site conditions, geotechnical issues, or utilities) on such Additional Properties; and (iii) not be entitled to any change order for time or money as a result of any delay, inability, or cost associated with the acquisition of such Additional Properties;

No impacts to third parties are anticipated as a result of this ATC.

K. History of Use and References

A description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements;

MSE Walls have been used successfully as a part of the Charlotte Area Transit System in Charlotte, North Carolina.

John Mrzygod, City of Charlotte Engineering and Property Management – Charlotte Area Transit System, 704.336.2245, jmrzygod@ci.charlotte.nc.us

L. Additional Risks

A description of added risks to the MBTA or third parties associated with implementing the ATC;

No additional risks to the MBTA or to third parties are anticipated as a result of this ATC.

M. Additional Costs

An estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC;

Additional costs to the MBTA, DB Entity and third parties will not result from this ATC. One of the primary purposes of this ATC is cost reduction.

N. Estimated Price Adjustment

An estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented;

This ATC will result in an estimated savings of $10,000,000. The ATC pricing as shown in this proposal is an all inclusive price. All price deducts and/or adds have been considered, and the resulting price adjustment is offered as shown.

O. Schedule Adjustment

An estimate of the schedule adjustment, should the ATC be approved and implemented; and

This ATC does not require any schedule adjustment.

P. Analysis of Quality, Performance, and Reliability

An analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents.

This ATC will provide an equal quality, performance, and reliability than the specified elevated track section. This ATC would increase the service life while reducing maintenance costs associated with

maintaining corrosion resistance.

Figure ATC-35-1: Plan View of Proposed MSE Wall Sections



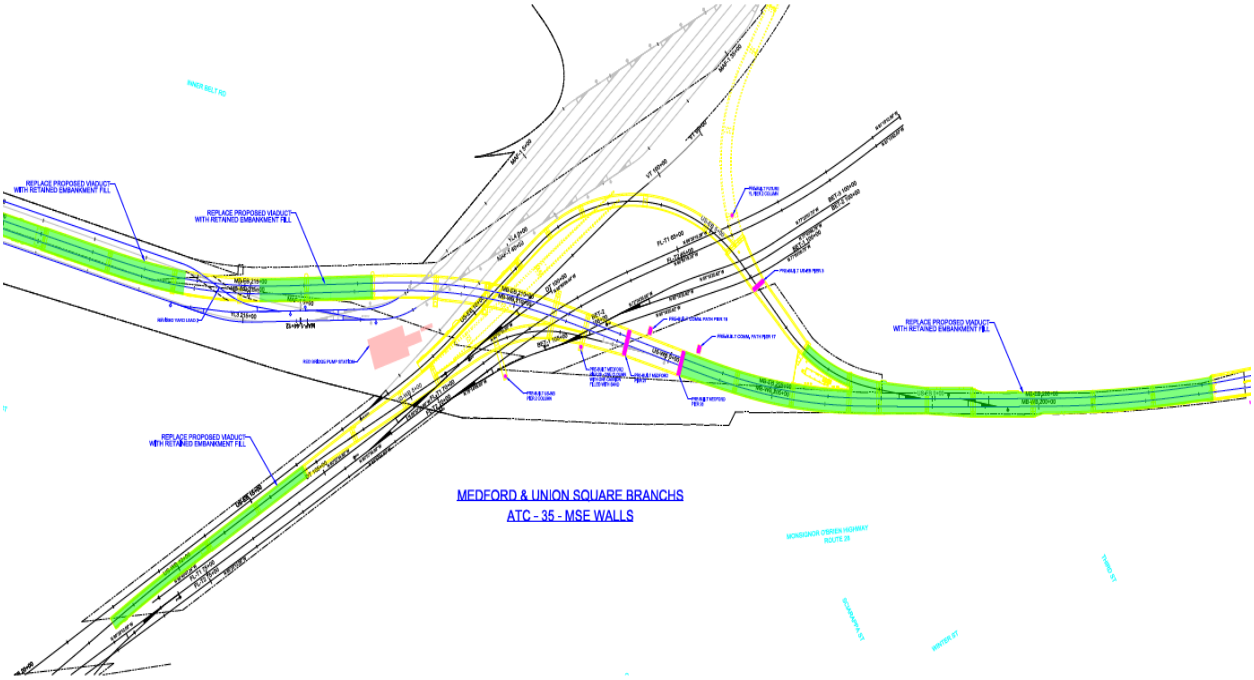


Figure ATC-35-2: Profile Views of Proposed MSE Wall Sections

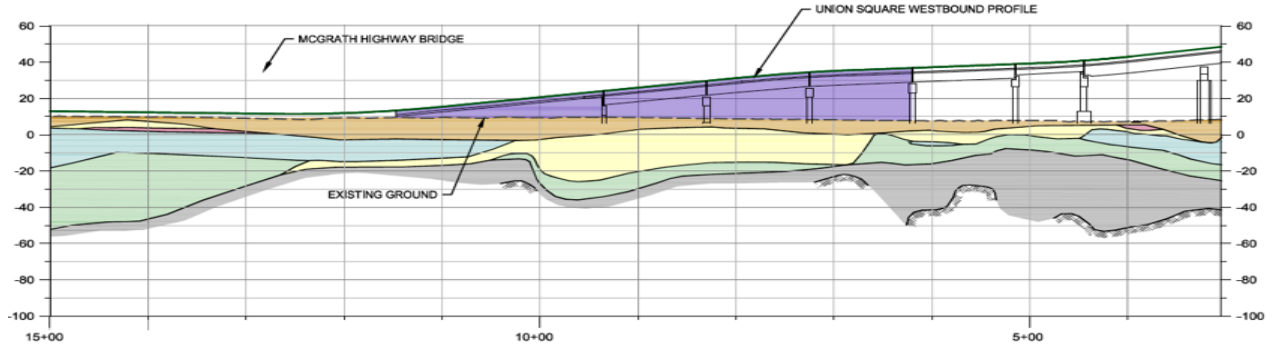


UNION STATION - WESTBOUND

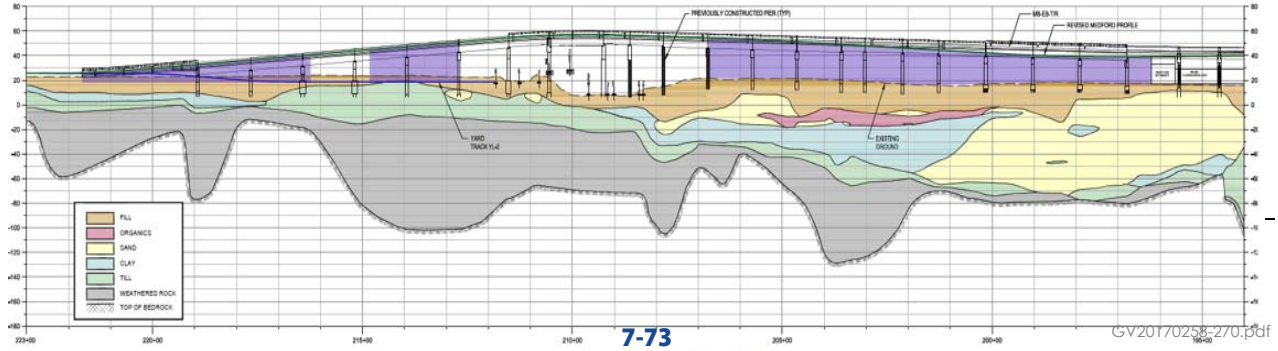

MEDFORD BRANCH - EASTBOUND

GV20170258-270.pdf

Figure ATC-35-3: MSE Wall at Viaduct

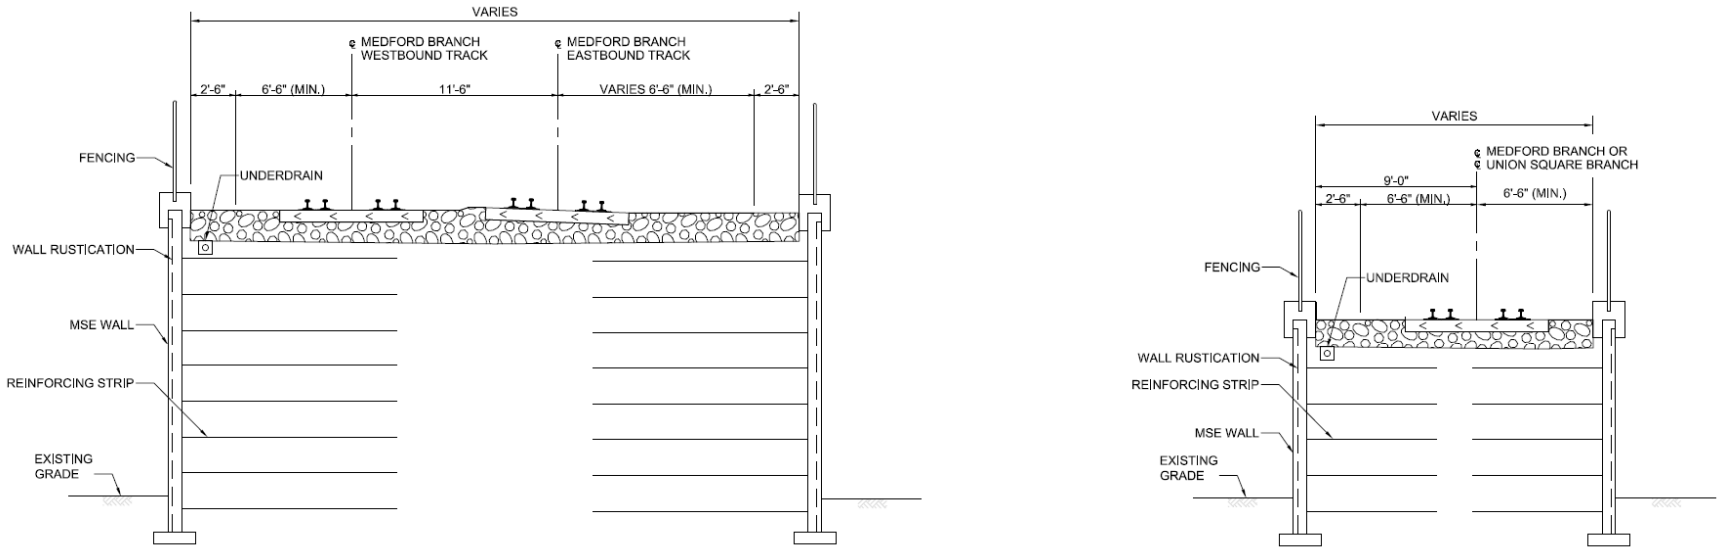

MSE WALL AT VIADUCT

Massachusetts Bay Transportation Authority

GLX

Green Line Extension
Formal Alternative Technical Concept (ATC) Eligibility Checklist

Date: 07-13-2013

Reviewer: Hemal Patel

Proposal Team: GLX Constructors

ATC Number: GLXC ATC 06-GLX Constructors_ATC 35_Formal_17071

Eligibility Determination

		Yes	No
A.	**Identification**: Includes a sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.)	✔	
B.	**General Description**: Includes a description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information	✔	
C.	**Information**: Identifies the locations where, and an explanation of how, the ATC will be used on the Project	✔	
D.	**Changes to Operations Requirements**: Identifies any changes in rail or transit operations requirements associated with the ATC, including ease of operations	✔	
E.	**Changes to Maintenance Requirements**: Identifies any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance	✔	
F.	**Service Life** 1. Identifies any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC	✔	
G.	**Requirements References**: Identifies references to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations	✔	
H.	**Justifications**: Includes an analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed	✔	

		Yes	No
I.	**Internal Impacts:** Includes a preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation	✔	
J.	**External Impacts:** Includes a description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC	✔	
K.	**Previous Use of ATC:** Includes a description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements	✔	
L.	**Additional Risks:** Includes a description of added risks to the MBTA or third parties associated with implementing the ATC	✔	
M.	**Additional Cost:** Includes an estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC	✔	
N.	**Cost Savings:** Includes an estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented	✔	
O.	**Schedule:** Includes an estimate of the schedule adjustment, should the ATC be approved and implemented	✔	
P.	**Equal or Better:** Includes an analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents	✔	

Name: Hemal Patel

Signature: _____

ATC No. 36

ATC No. 36

Preliminary Submission

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

PRELIMINARY

ALTERNATIVE TECHNICAL CONCEPTS

("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

GLX CONSTRUCTORS PRELIMINARY ATC FORM

ATC 36 – ELEVATED COMMUNITY PATH

Sections A though E below must be completed to submit a Preliminary ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Preliminary ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. General Description

A general description (not to exceed two pages) of the Preliminary ATC, how the ATC will be used on the Project, the proposed location of the ATC, and any other pertinent information that would provide a clear understanding of the potential ATC;

This ATC will eliminate the underpass at Walnut Street and reduce the underpass width at Medford Street by elevating the Community Path starting at grade from School Street. The Community Path would continue near cross-street grade along the west side of the ROW to Medford Street. After crossing Medford Street at grade, the Community Path will continue near cross-street grade to Walnut Street. After crossing Walnut Street at grade, the Community Path then progressively declines to track grade south of Walnut Street.

B. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC and an explanation of the nature of the deviations from said requirements;

Volume 2, Exhibit 2B, Project Definition Plan Sheets: WLN-S-2002, MEB-S-2002, 000-K-2012, 000-K-2010, and 000-K-2011. This ATC eliminates underpasses shown on these Project Definition Plans.

C. Benefits

Any potential benefits or implications of incorporating the Preliminary ATC into the Project, including in right-of-way acquisitions, rail operations, and routine or capital maintenance, and other Project risks;

This ATC provides the following benefits:

- Reduces significant impacts to the 48" MWRA waterline at Walnut Street
- Increases safety and security of pedestrians and cyclists through the elimination of pedestrian underpasses at Walnut and Medford Streets.
- Fire and Life Safety features are eliminated for underpasses at Walnut and Medford Streets.
- Provides two additional access points to the community path.
- Provides improved access to community path for maintenance and emergencies.
- Eliminates ventilation requirement for the 200' long Medford Street underpass.
- Potential to eliminate replacement of the Walnut Street bridge west abutment.

D. Conceptual Drawings

Any conceptual drawings (if applicable) of the configuration of the potential ATC or other appropriate descriptive information that provides an understanding of the Preliminary ATC; and

Please reference the attached Figures ATC 36-1 “Elevated Community Path Plan and Cross Section 1” and ATC-36-2 “Elevated Community Path Plan and Cross Section 2”

E. Cost Estimate and Schedule Impacts

An order of magnitude cost estimate and a preliminary analysis of schedule impacts associated with the Preliminary ATC.

This ATC will result in an estimated cost savings of $3 M. Our preliminary analysis indicates no impact to schedule milestones.

Figure ATC 36-1: Elevated Community Path Plan and Cross Section 1



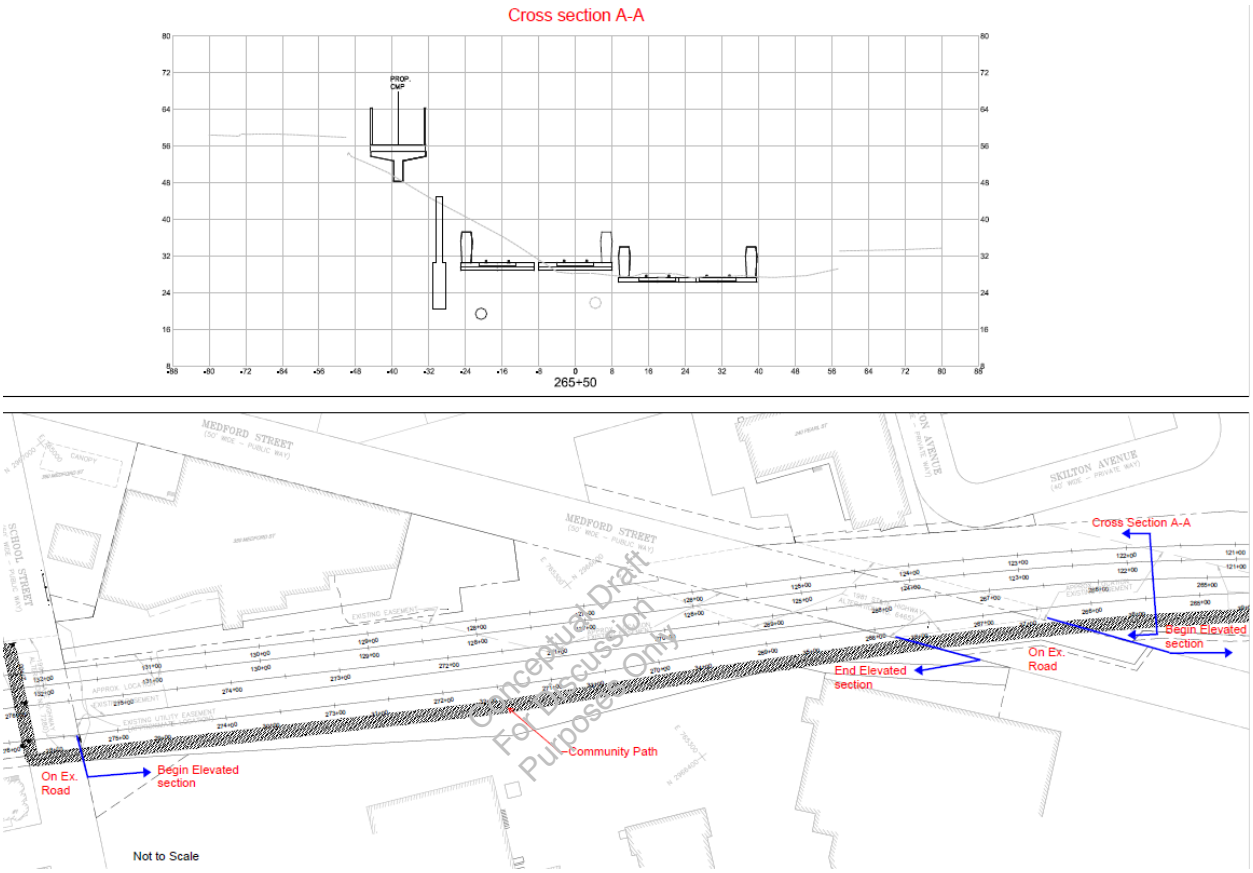


Figure ATC-36-2: Elevated Community Path Plan and Cross Section 2

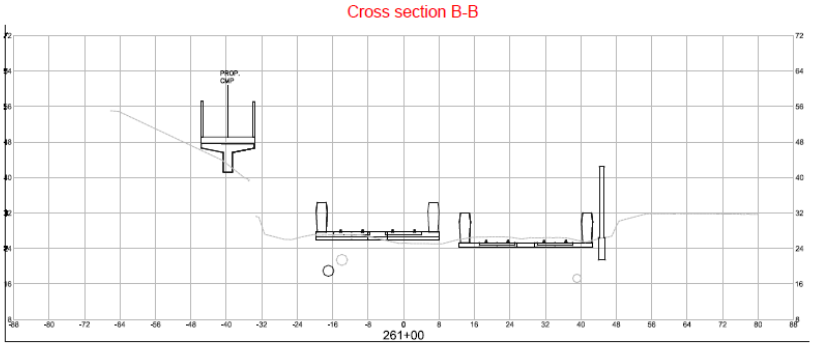

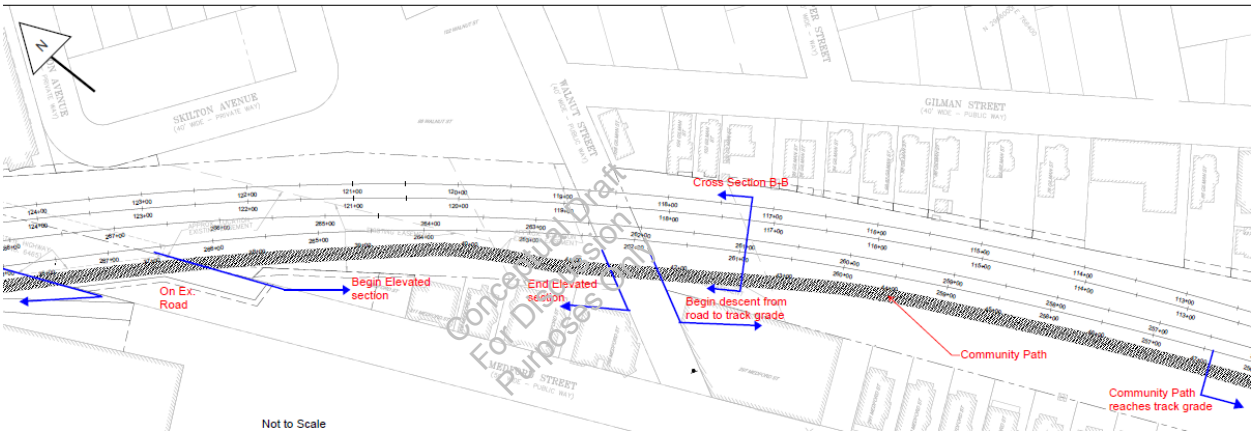

ATC No. 36

MBTA Acceptance of Preliminary Submission

ATC Information:

Type of ATC:	Preliminary
Title:	GLX Constructors ATC 08 - Elevated Community Path
Proposer Company:	GLX Constructors

Final Disposition:

Sent on behalf of Yvelisse Duvergé. The Preliminary ATC can be formally submitted for MBTA review as an ATC Submittal, subject to further refinement and submission of supporting information pursuant to Section 3.3.1 of the Instructions to Proposers.

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

PRELIMINARY

ALTERNATIVE TECHNICAL CONCEPTS

("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

GLX CONSTRUCTORS PRELIMINARY ATC FORM

ATC 36 – ELEVATED COMMUNITY PATH

Sections A though E below must be completed to submit a Preliminary ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Preliminary ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. General Description

A general description (not to exceed two pages) of the Preliminary ATC, how the ATC will be used on the Project, the proposed location of the ATC, and any other pertinent information that would provide a clear understanding of the potential ATC;

This ATC will eliminate the underpass at Walnut Street and reduce the underpass width at Medford Street by elevating the Community Path starting at grade from School Street. The Community Path would continue near cross-street grade along the west side of the ROW to Medford Street. After crossing Medford Street at grade, the Community Path will continue near cross-street grade to Walnut Street. After crossing Walnut Street at grade, the Community Path then progressively declines to track grade south of Walnut Street.

B. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC and an explanation of the nature of the deviations from said requirements;

Volume 2, Exhibit 2B, Project Definition Plan Sheets: WLN-S-2002, MEB-S-2002, 000-K-2012, 000-K-2010, and 000-K-2011. This ATC eliminates underpasses shown on these Project Definition Plans.

C. Benefits

Any potential benefits or implications of incorporating the Preliminary ATC into the Project, including in right-of-way acquisitions, rail operations, and routine or capital maintenance, and other Project risks;

This ATC provides the following benefits:

- Reduces significant impacts to the 48" MWRA waterline at Walnut Street
- Increases safety and security of pedestrians and cyclists through the elimination of pedestrian underpasses at Walnut and Medford Streets.
- Fire and Life Safety features are eliminated for underpasses at Walnut and Medford Streets.
- Provides two additional access points to the community path.
- Provides improved access to community path for maintenance and emergencies.
- Eliminates ventilation requirement for the 200' long Medford Street underpass.
- Potential to eliminate replacement of the Walnut Street bridge west abutment.

D. Conceptual Drawings

Any conceptual drawings (if applicable) of the configuration of the potential ATC or other appropriate descriptive information that provides an understanding of the Preliminary ATC; and

Please reference the attached Figures ATC 36-1 “Elevated Community Path Plan and Cross Section 1” and ATC-36-2 “Elevated Community Path Plan and Cross Section 2”

E. Cost Estimate and Schedule Impacts

An order of magnitude cost estimate and a preliminary analysis of schedule impacts associated with the Preliminary ATC.

This ATC will result in an estimated cost savings of $3 M. Our preliminary analysis indicates no impact to schedule milestones.

Figure ATC 36-1: Elevated Community Path Plan and Cross Section 1



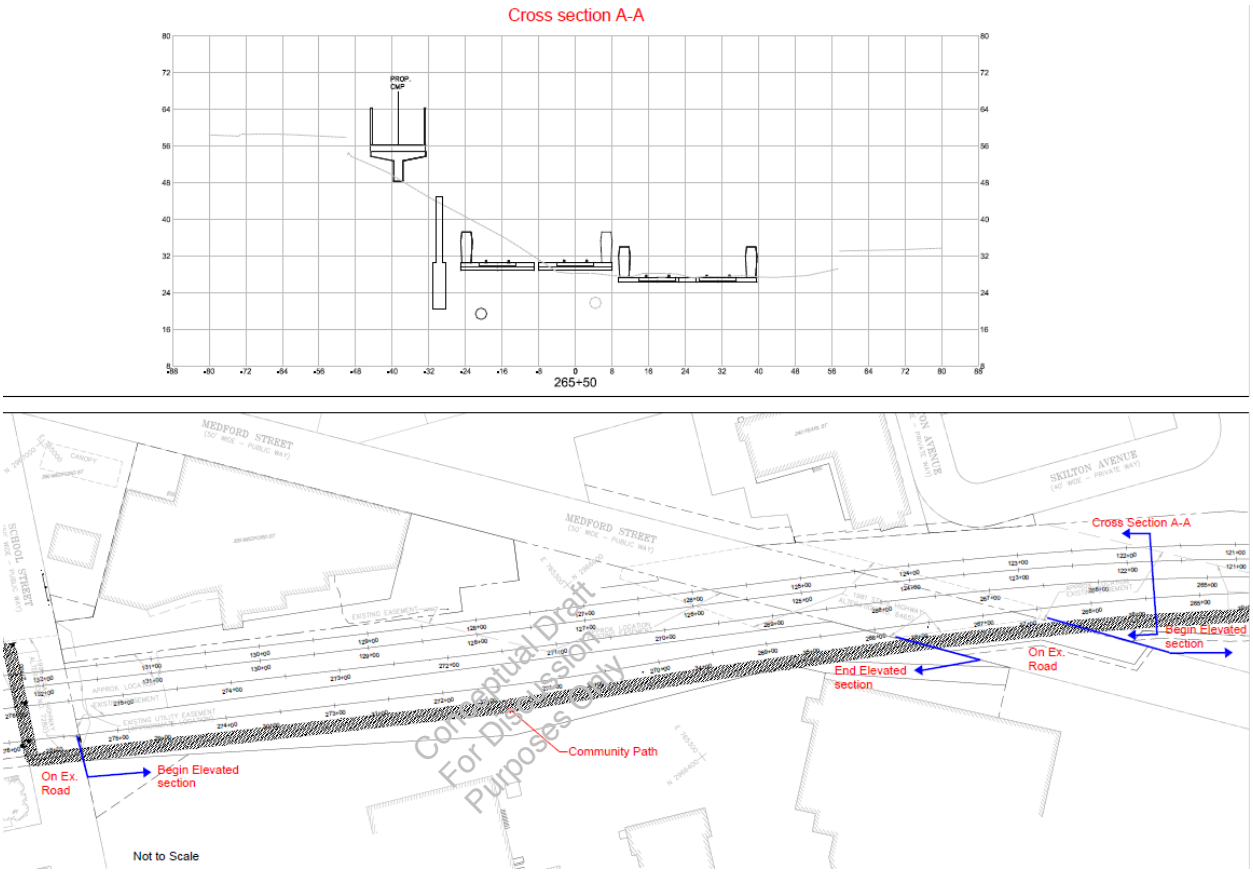


Figure ATC-36-2: Elevated Community Path Plan and Cross Section 2

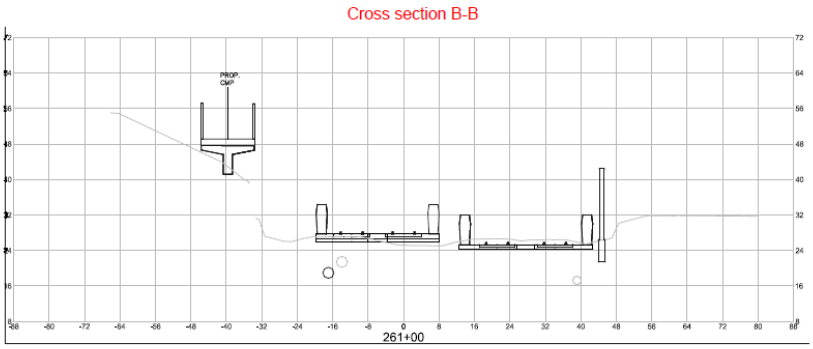

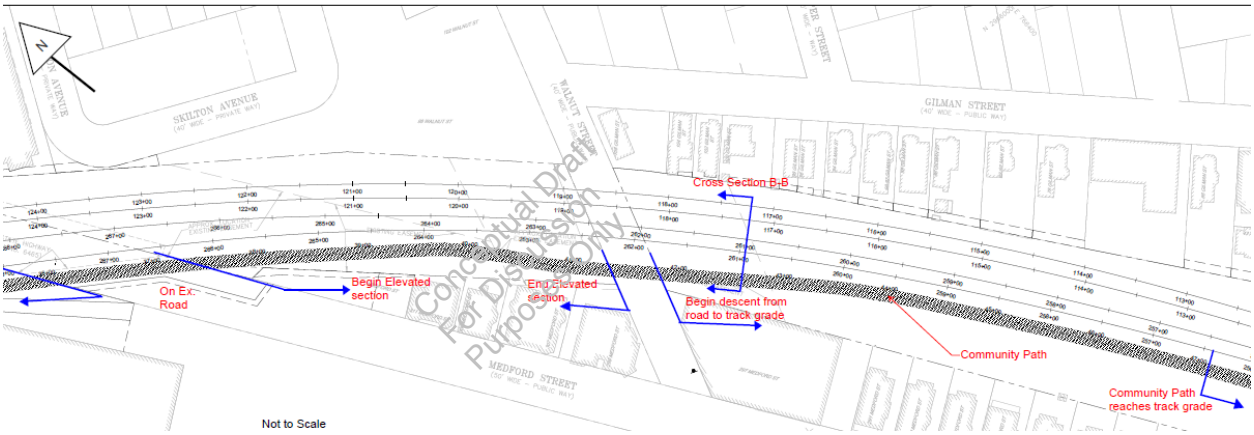

Massachusetts Bay Transportation Authority

GLX

Green Line Extension
Preliminary Alternative Technical Concept (ATC) Eligibility Checklist

Date: 06/12/2017

Reviewer: Hemal Patel

Proposal Team: GLX Constructors

ATC Number: GLXC ATC 08-GLX Constructors_ATC 36_Preliminary_170609

Eligibility Determination

		Yes	No
A.	**General Description**: Includes a general description (not to exceed two pages) of the Preliminary ATC, how the ATC will be used on the Project, the proposed location of the ATC, and any other pertinent information that would provide a clear understanding of the potential ATC	✔	
B.	**Requirements References**: Identifies references to requirements of the Contract Documents that are inconsistent with the proposed ATC and an explanation of the nature of the deviations from said requirements	✔	
C.	**Benefits & Implications**: Identifies Any potential benefits or implications of incorporating the Preliminary ATC into the Project, including in right-of-way acquisitions, rail operations, and routine or capital maintenance	✔	
D.	**Conceptual Drawings** (if applicable): Includes any conceptual drawings (if applicable) of the configuration of the potential ATC or other appropriate descriptive information that provides an understanding of the Preliminary ATC	✔	
E.	**Order of Magnitude**: Includes an order of magnitude cost estimate and a preliminary analysis of schedule impacts associated with the Preliminary ATC	✔	

Name: Hemal Patel

Signature: _____

ATC No. 36

Formal Submission

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

FORMAL

ALTERNATIVE TECHNICAL CONCEPTS ("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

JULY 11, 2017 (Final Round)

GLX CONSTRUCTORS FORMAL ATC FORM

ELEVATED COMMUNITY PATH

Sections A though P below shall be completed to submit a Formal ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Formal ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. ATC Number

A sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.);

ATC 36

MBTA Preliminary ATC File Number: ATC-000014 – GLX Constructors ATC 08

B. Description and Conceptual Drawings

A description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information;

This ATC will eliminate the underpass at Walnut Street and reduce the underpass width at Medford Street by elevating the Community Path starting at grade from School Street. The Community Path would continue near cross-street grade along the west side of the ROW to Medford Street. After crossing Medford Street at grade, the Community Path will continue near cross-street grade to Walnut Street. After crossing Walnut Street at grade, the Community Path then progressively declines to track grade south of Walnut Street. Please reference the attached Figures ATC 36-1 "Elevated Community Path Plan and Profile" and ATC-36-2 "Elevated Community Path Cross Sections"

C. Locations and How Used

The locations where, and an explanation of how, the ATC will be used on the Project;

The ATC will eliminate the Underpasses at Walnut Street and Medford Street by elevating the Community Path starting from approximately 38' left Sta. MB-EB 252+00 at elevation 26.00 crossing Walnut Street at Grade. The Community Path would continue to approximately 38' left Sta. MB-EB 267+00 elevation 56.00. The Community Path would cross Medford Street at Grade. The Community Path would continue to 54' left Sta .MB-EB 275+50 elevation 52.00 where it would tie into School Street. This would be the North End of the Elevated Community Path.

D. Changes in Rail or Transit Operations

Any changes in rail or transit operations requirements associated with the ATC, including ease of operations;

No changes in operations are anticipated as a result of this ATC.

E. Changes in Routine or Capital Maintenance

Any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance;

This ATC eliminates the need for the routine and capital maintenance of lighting for the Walnut Street and Medford Street underpasses, as well as the routing and capital maintenance of the underground ventilation for the Medford Underpass as it would be over 200' long.

F. Changes in Anticipated Service Life

Any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC;

No change in service life is anticipated as a result of this ATC.

G. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations;

Para 9.2.3.3 Geometry (h) Table 9.2-1 Community Path and Roadway Interfaces Medford Street and Walnut Street Underpass of the Technical Provisions.

H. Justification of Use

An analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed;

This ATC eliminates the pedestrian underpass at Walnut Street and Medford Street which increases safety and security of Pedestrians using the Community Path. This ATC also eliminates the need for Fire and Life Safety features and lighting for underpasses at Walnut Street and Medford Street. This ATC improves accessibility for emergency and maintenance vehicles operating on the Community Path

I. Preliminary Analysis and Quantitative Discussion

A preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation;

No impacts on rail or transit operations are anticipated as a result of this ATC.

J. Impacts on Third Parties

A description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC. Proposers are advised that they may (i) be solely responsible for the cost and schedule impacts of the acquisition of any such Additional Properties, including the cost thereof and obtaining any necessary environmental approvals; (ii) not be entitled to any change order for time or money as a result of site conditions (i.e., hazardous materials, differing site conditions, geotechnical issues, or utilities) on such Additional Properties; and (iii) not be entitled to any change order for time or money as a result of any delay, inability, or cost associated with the acquisition of such Additional Properties;

This ATC eliminates the risk of relocating the 48" MWRA Waterline at Walnut Street. This ATC also reduces the footprint of the Community Path which will reduce potential ROW issues.

K. History of Use and References

A description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements;

This ATC uses a similar elevated community path concept that has been successfully used at the NorthPoint park. This concept is also similar to what has been called for on the Project Concept Plans from School Street to Central Street.

L. Additional Risks

A description of added risks to the MBTA or third parties associated with implementing the ATC;

No additional risks to the MBTA or to third parties are anticipated as a result of this ATC.

M. Additional Costs

An estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC;

Additional costs to the MBTA, DB Entity and third parties will not result from this ATC. One of the primary purposes of this ATC is cost reduction.

N. Estimated Price Adjustment

An estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented;

This ATC will result in an estimated savings of $2,000,000. The ATC pricing as shown in this proposal is an all inclusive price. All price deducts and/or adds have been considered, and the resulting price adjustment is offered as shown.

O. Schedule Adjustment

An estimate of the schedule adjustment, should the ATC be approved and implemented; and


This ATC does not require any schedule adjustment.


P. Analysis of Quality, Performance, and Reliability


An analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents.

This ATC will provide equal quality, performance, and reliability to the specified plans. This ATC reduces maintenance cost needed to maintain performance through the elimination or reduction of ventilation and lighting requirements.

Figure ATC 36-1: Elevated Community Path Plan and Profile (2 Pages)

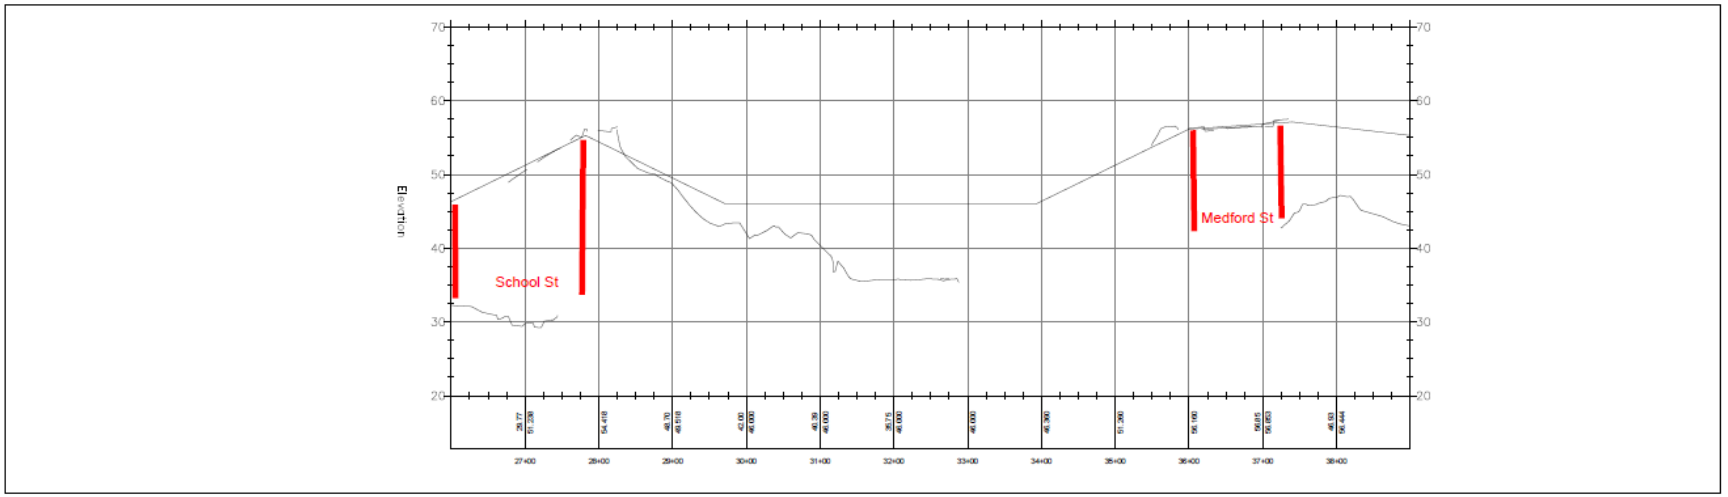

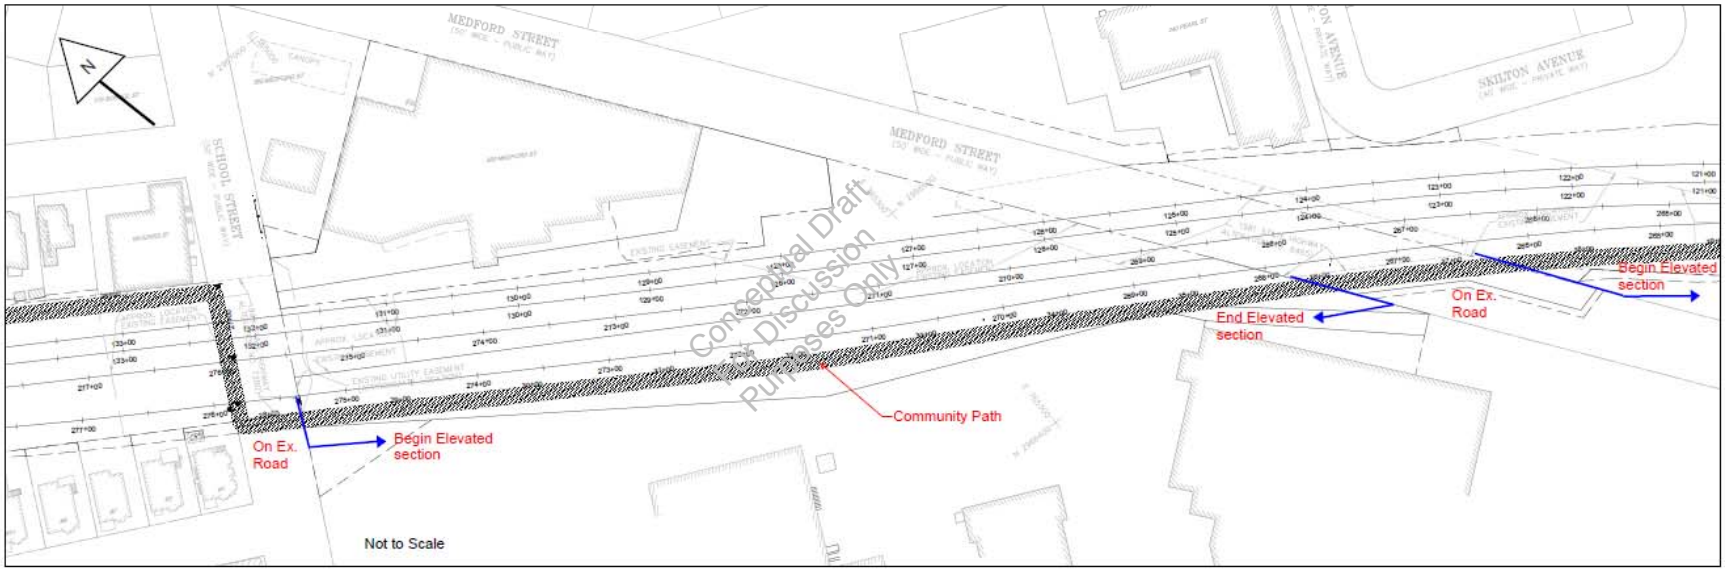

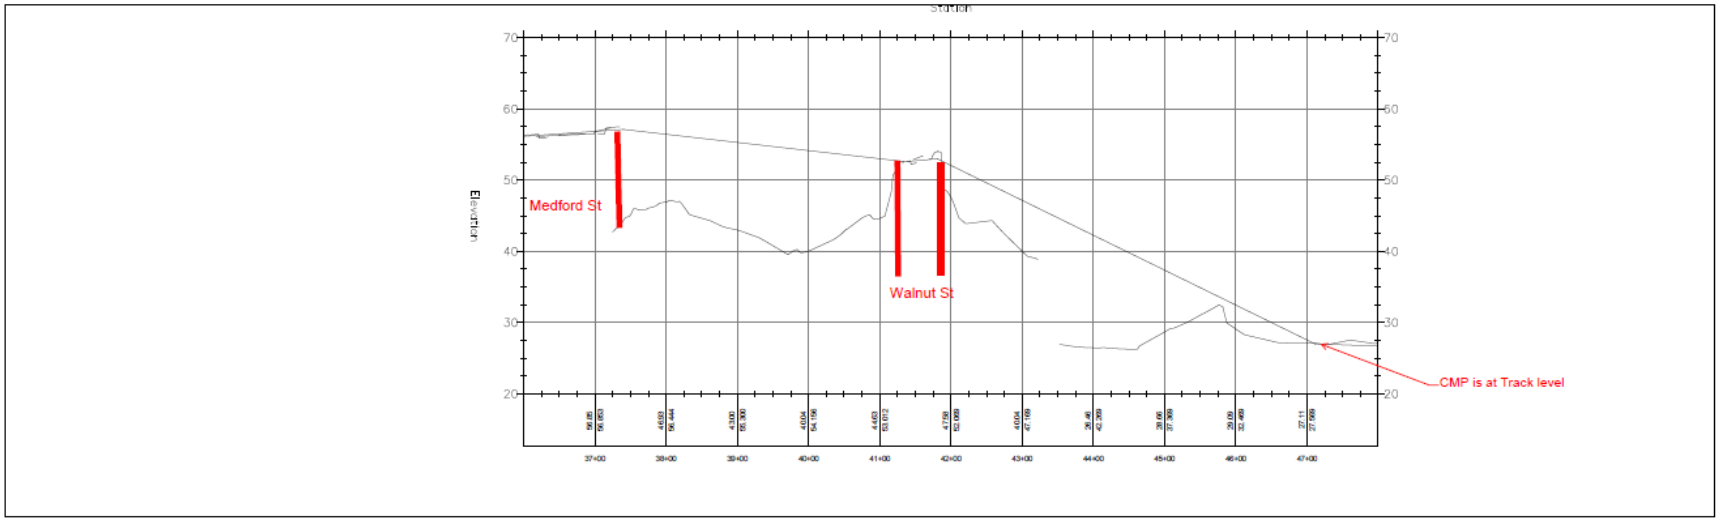
Station
Elevation
70
60
50
40
30
20
Medford St
Walnut St
CMP is at Track level
37+00
38+00
39+00
40+00
41+00
42+00
43+00
44+00
45+00
46+00
47+00





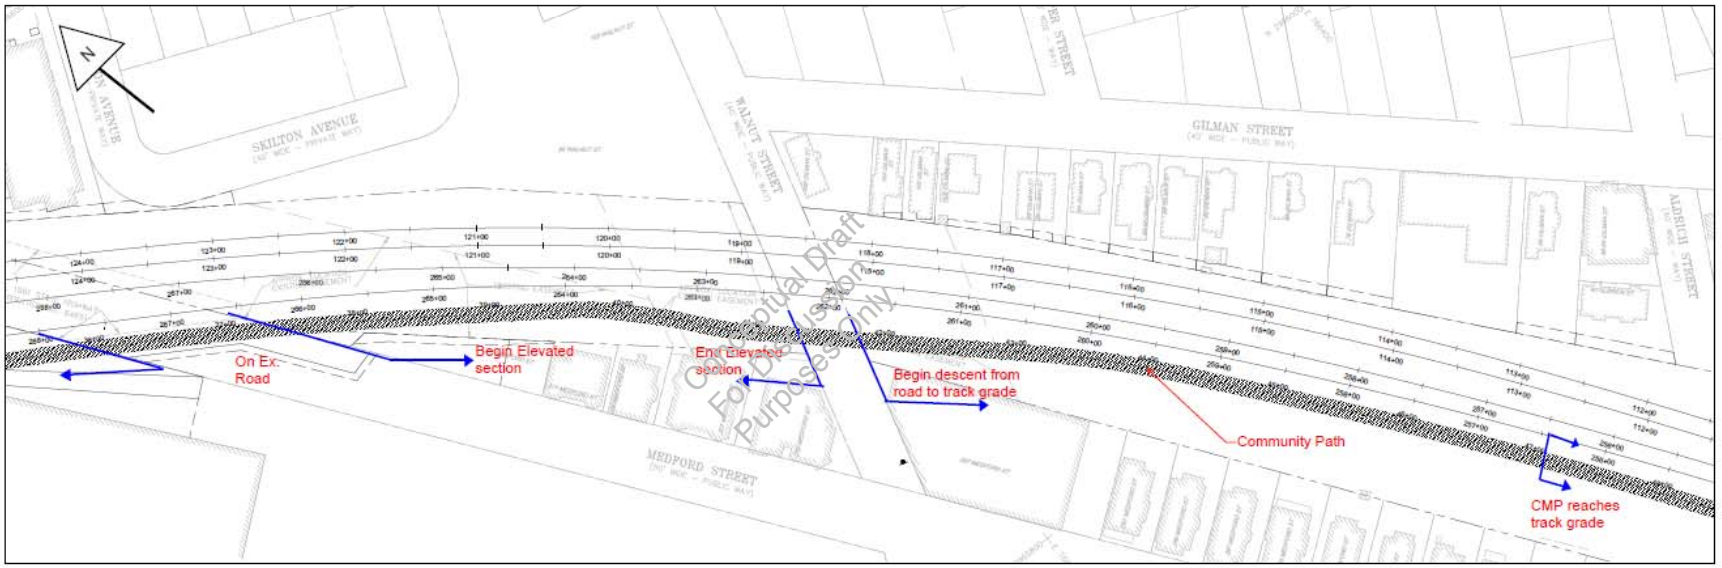

N
SKILTON AVENUE
WALNUT STREET
GILMAN STREET
MEDFORD STREET
On Ex. Road
Begin Elevated section
End Elevated section
Begin descent from road to track grade
Community Path
CMP reaches track grade
Conceptual Draft For Discussion Purposes Only


Figure ATC-36-2: Elevated Community Path Cross Sections (20 Pages)

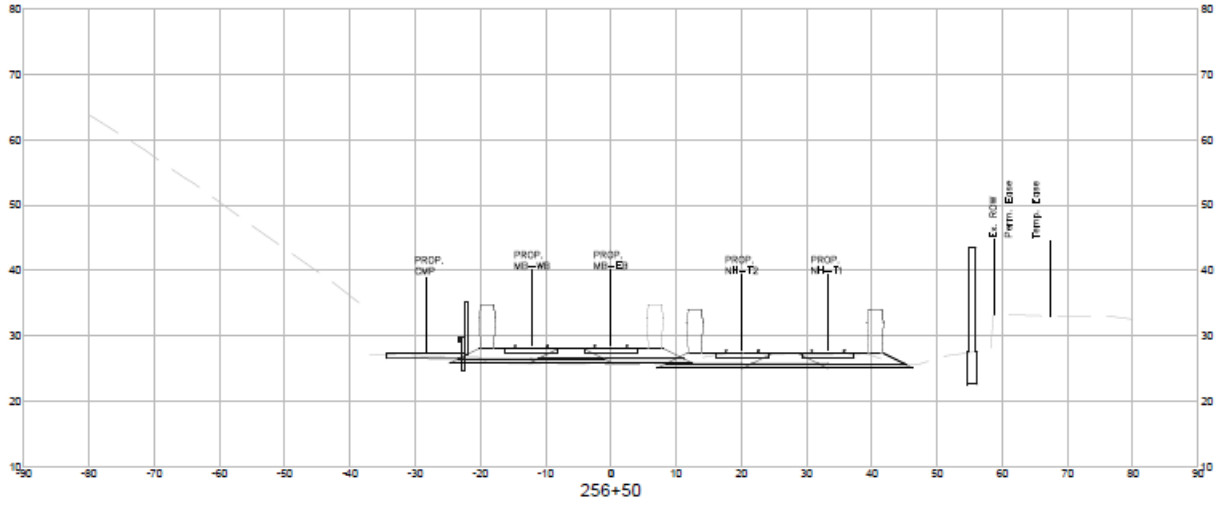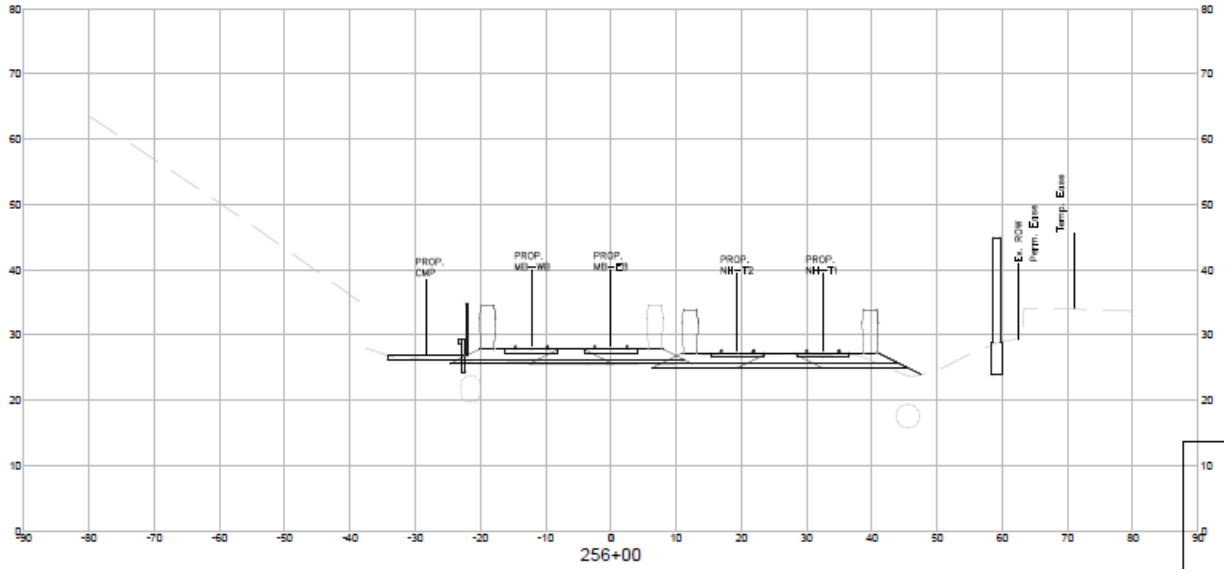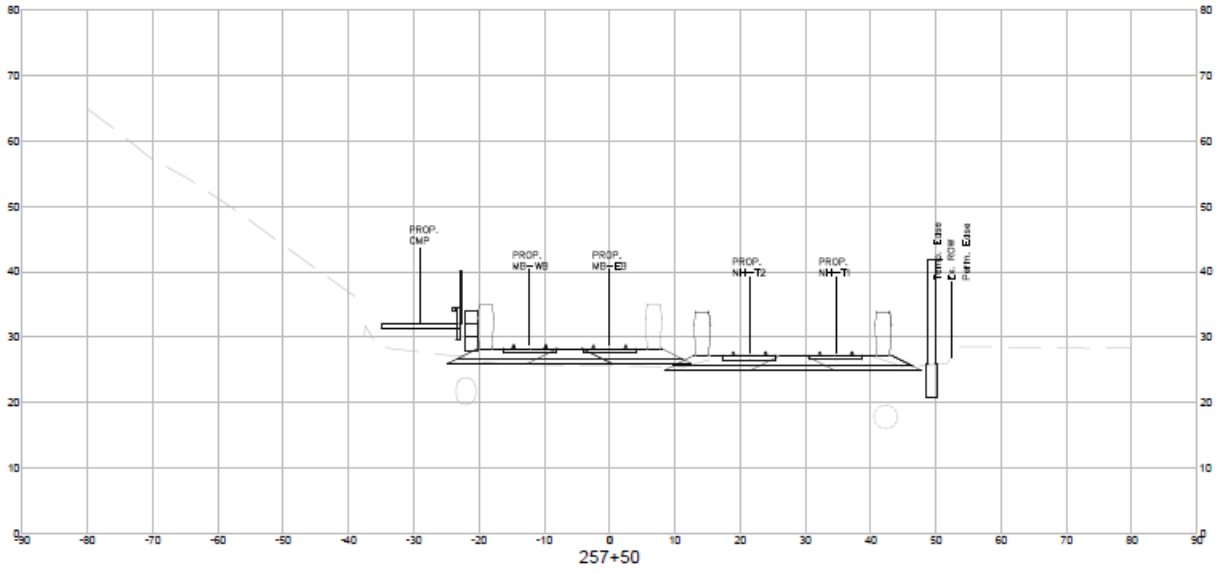


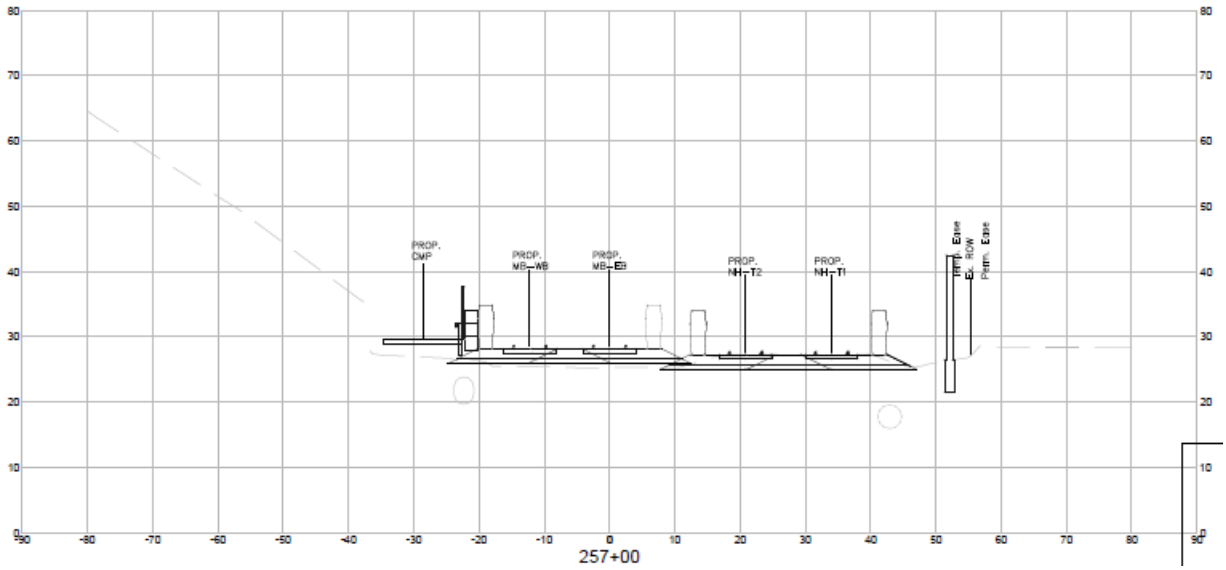




PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Easm
Ex. ROW
Perm. Easm
257+50



PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Easm
Ex. ROW
Perm. Easm
257+00

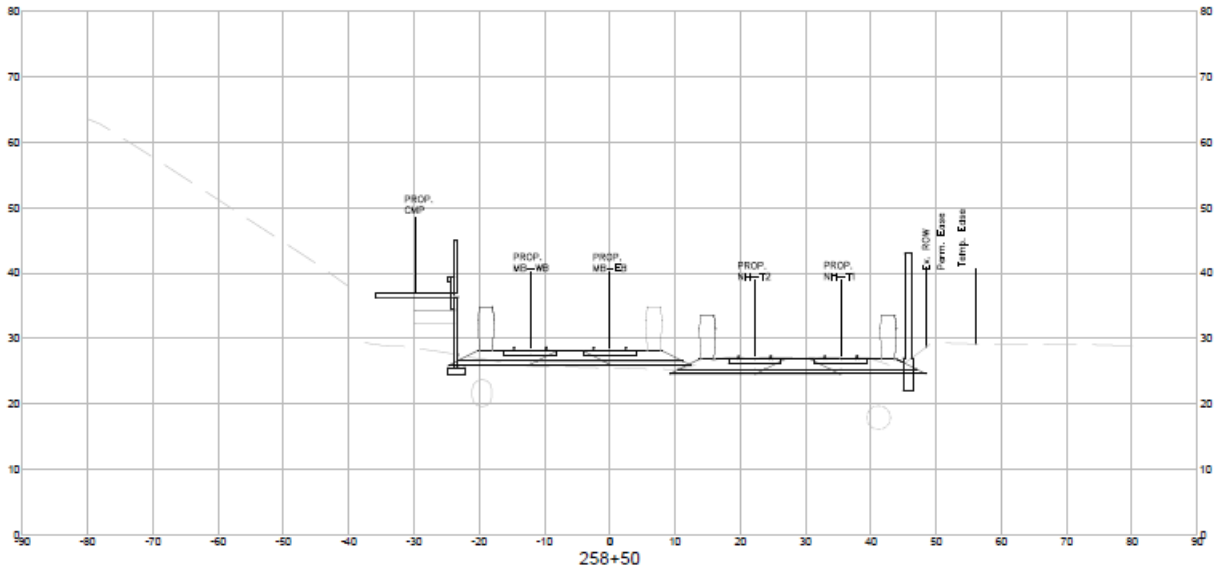

PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–TZ
PROP. NH–TI
Ex. ROW
Perm. Ease
Temp. Ease
258+50

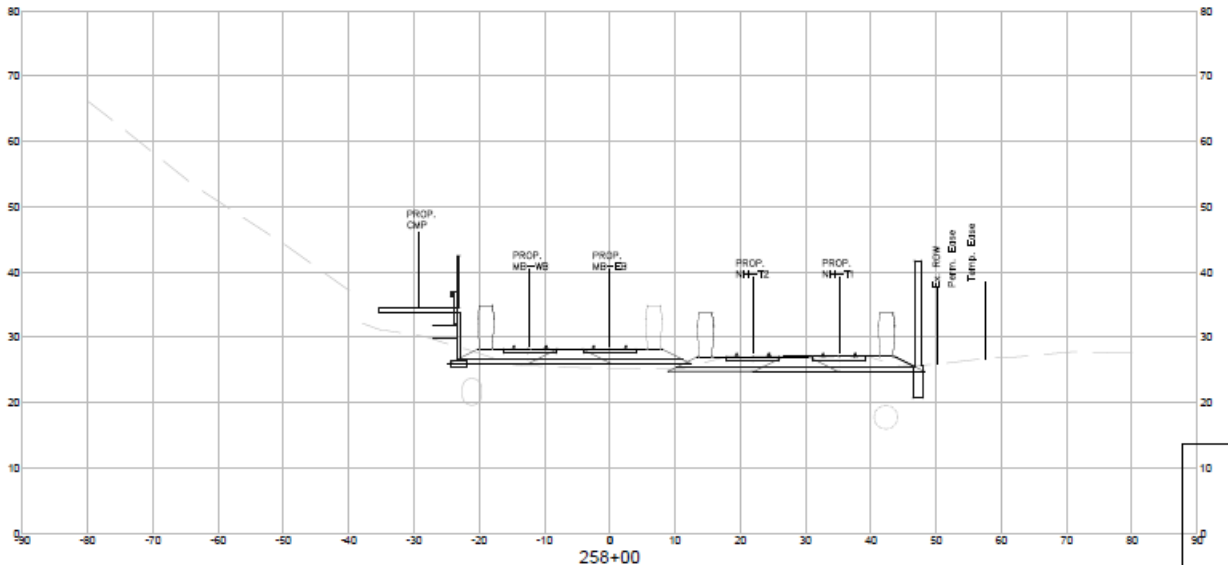

PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–TZ
PROP. NH–TI
Ex. ROW
Perm. Ease
Temp. Ease
258+00

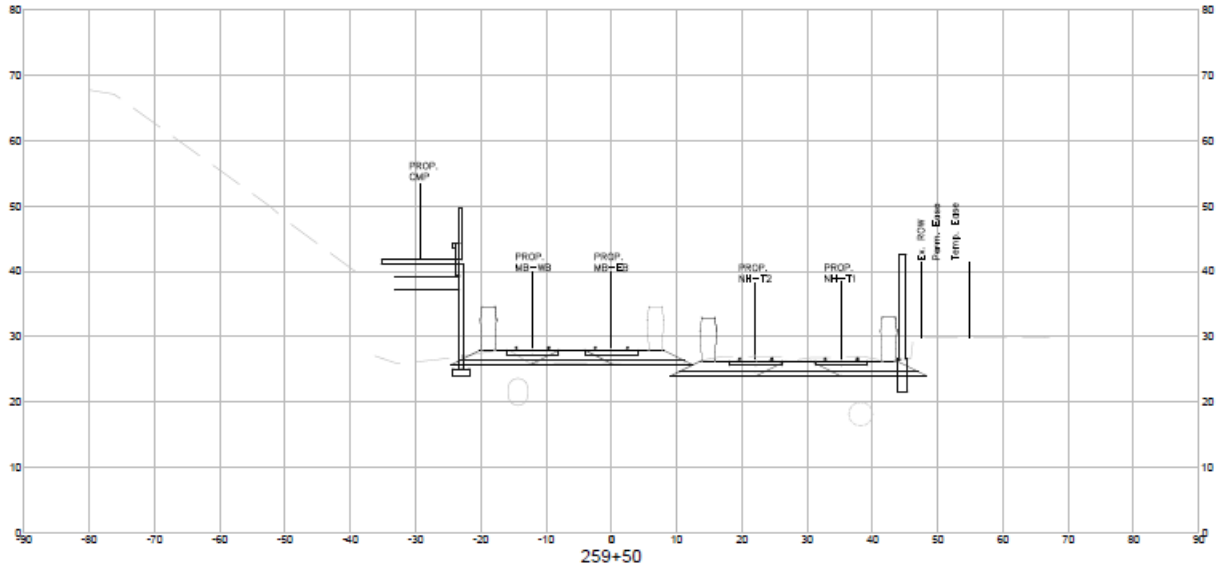

PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
259+50

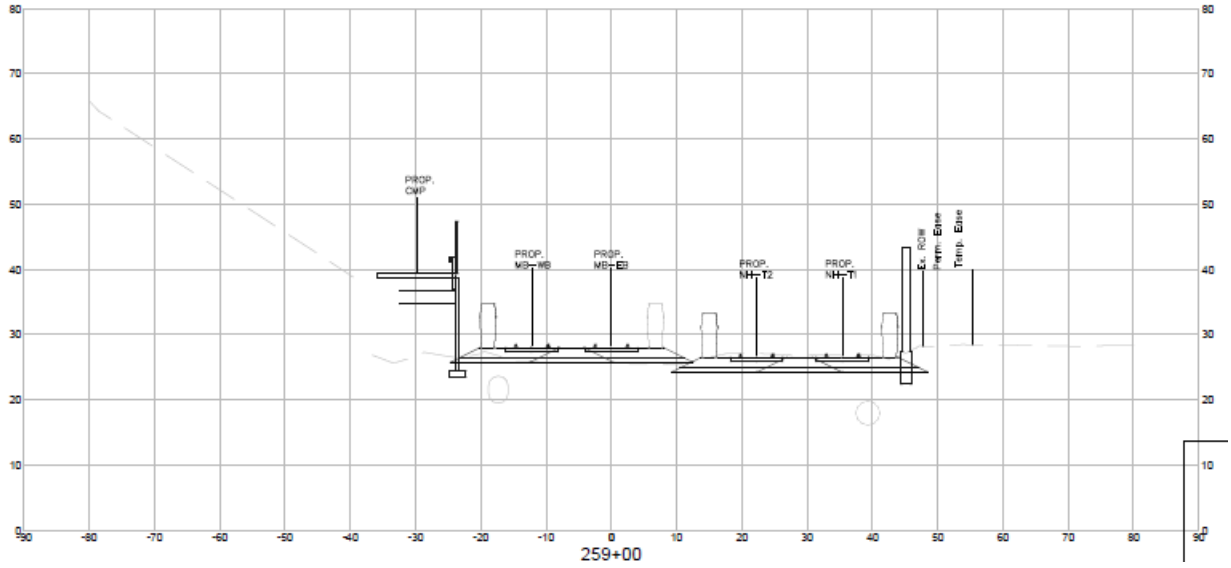

PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
259+00

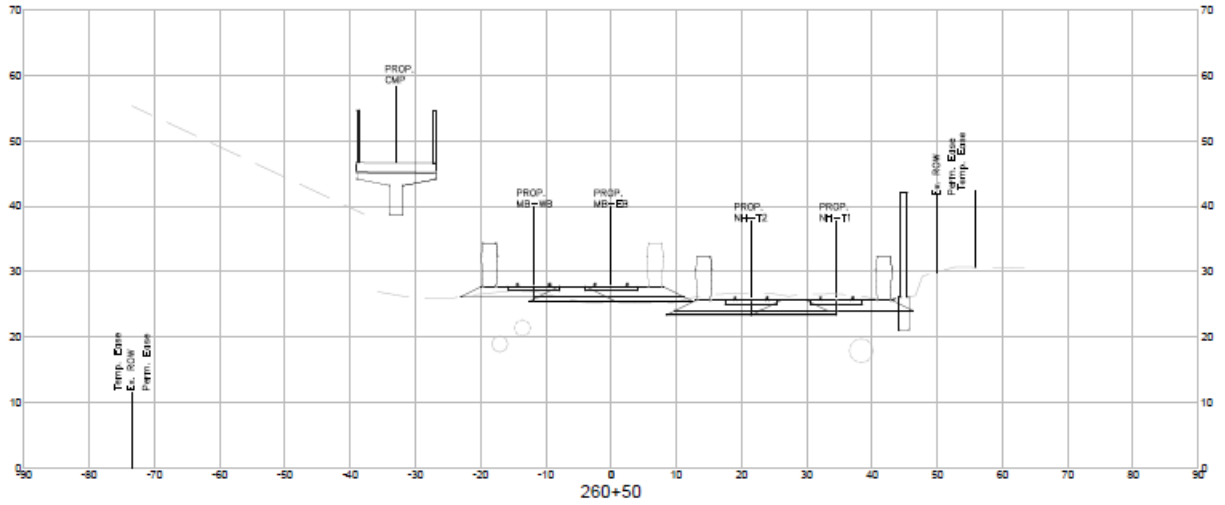

PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
Temp. Ease
Ex. ROW
Perm. Ease
260+50

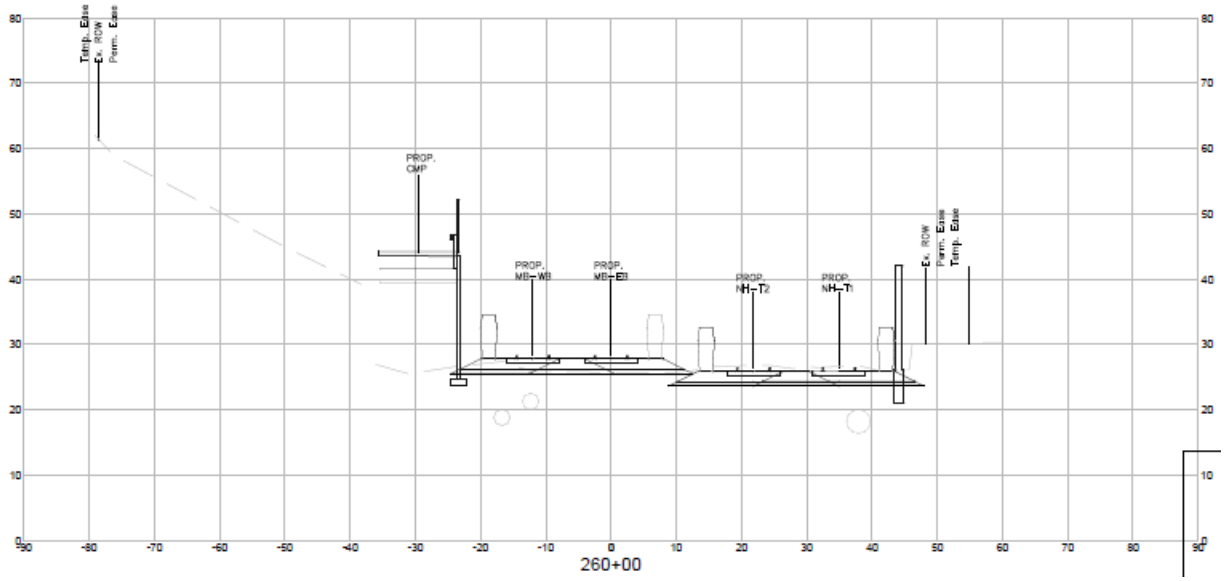

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
260+00

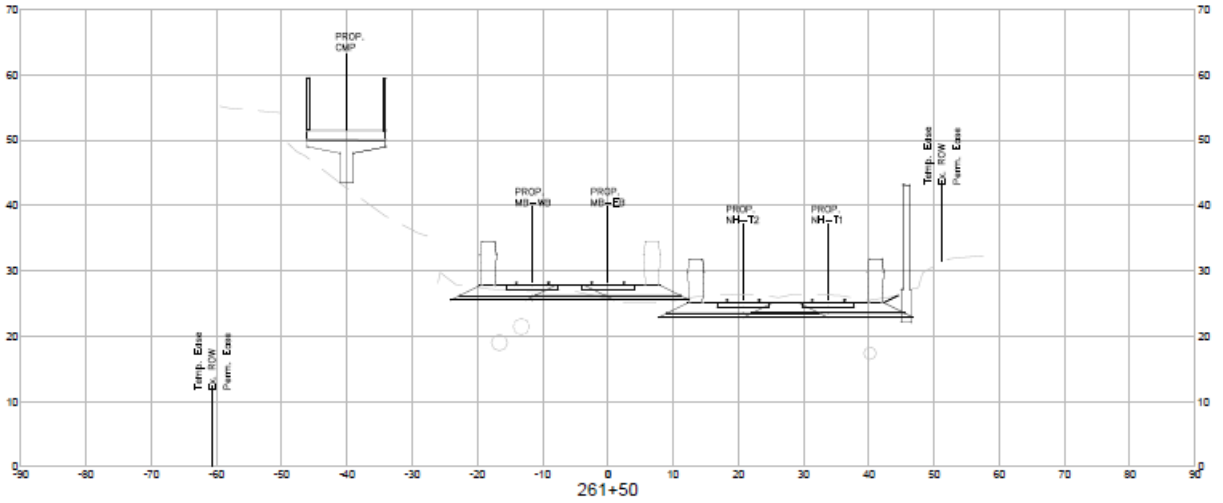

PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
261+50

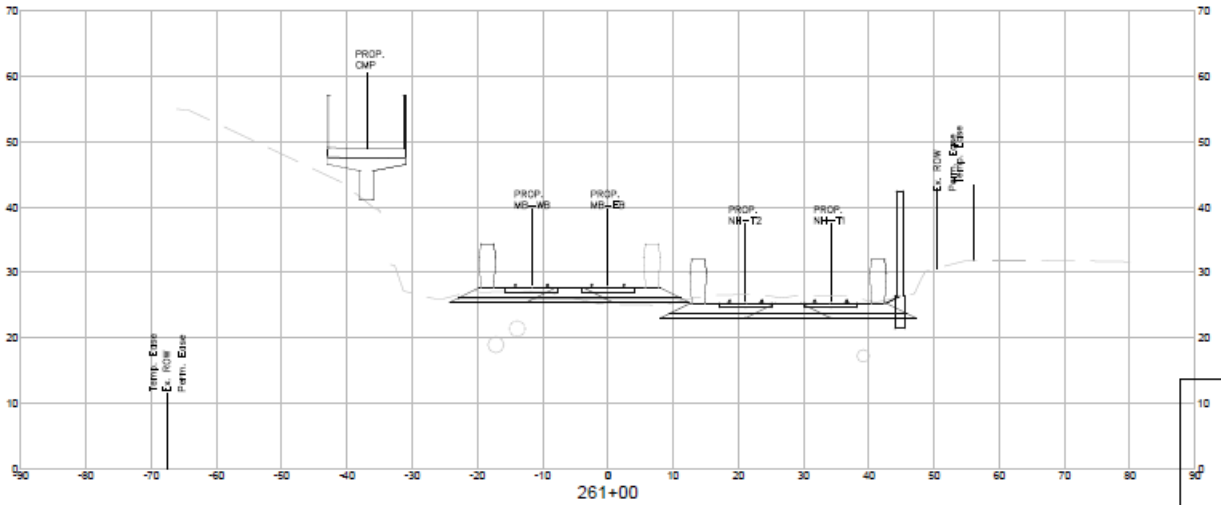

PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
261+00

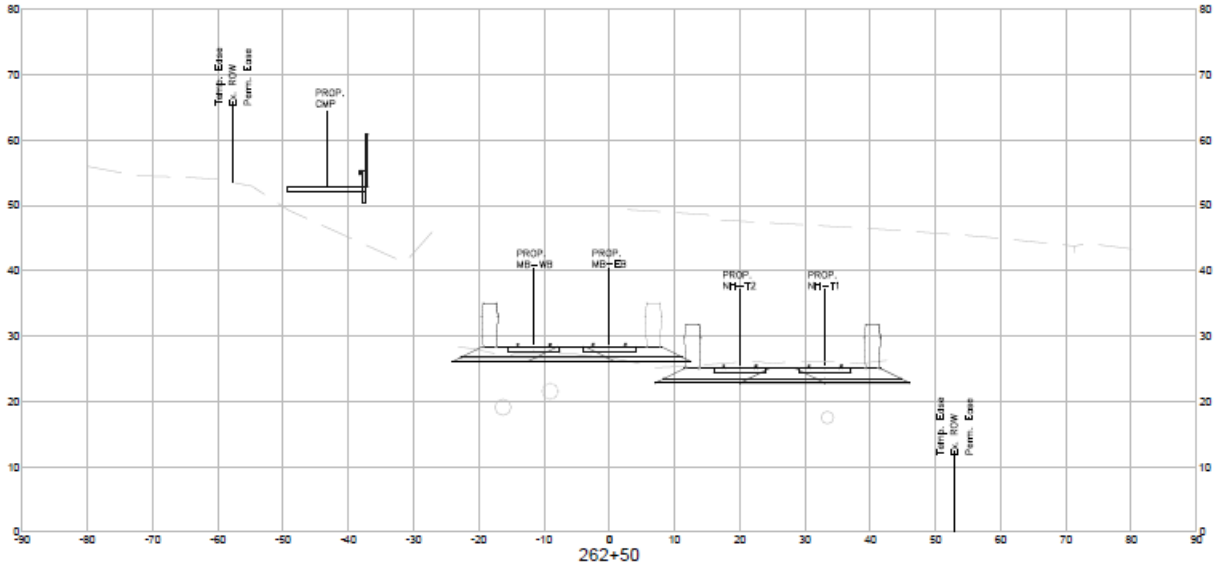

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
262+50

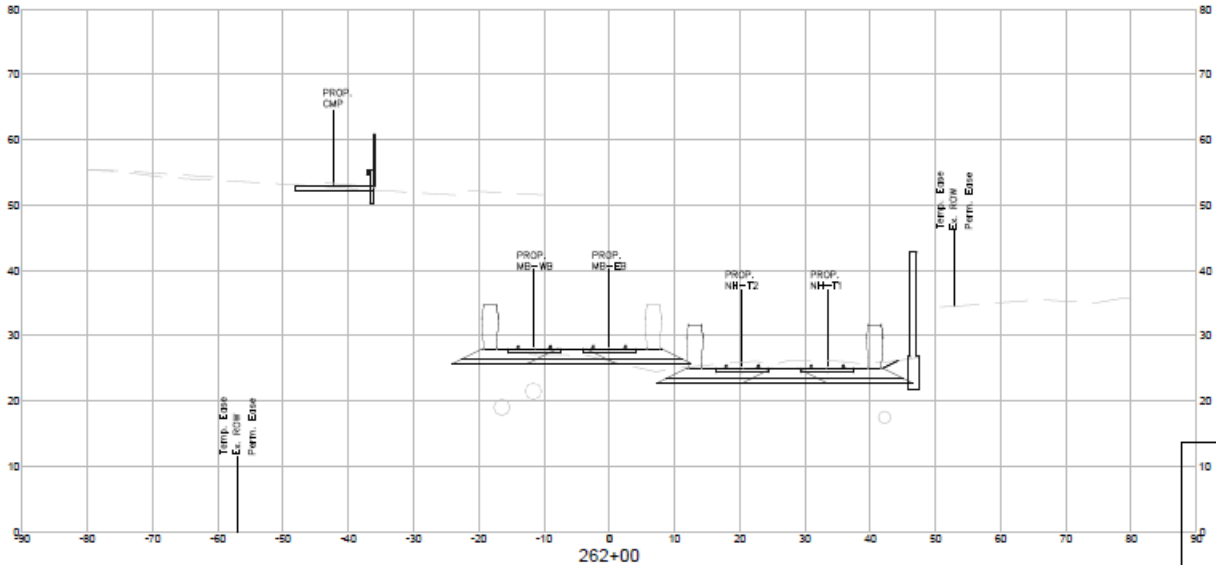

PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
Temp. Ease
Ex. ROW
Perm. Ease
262+00

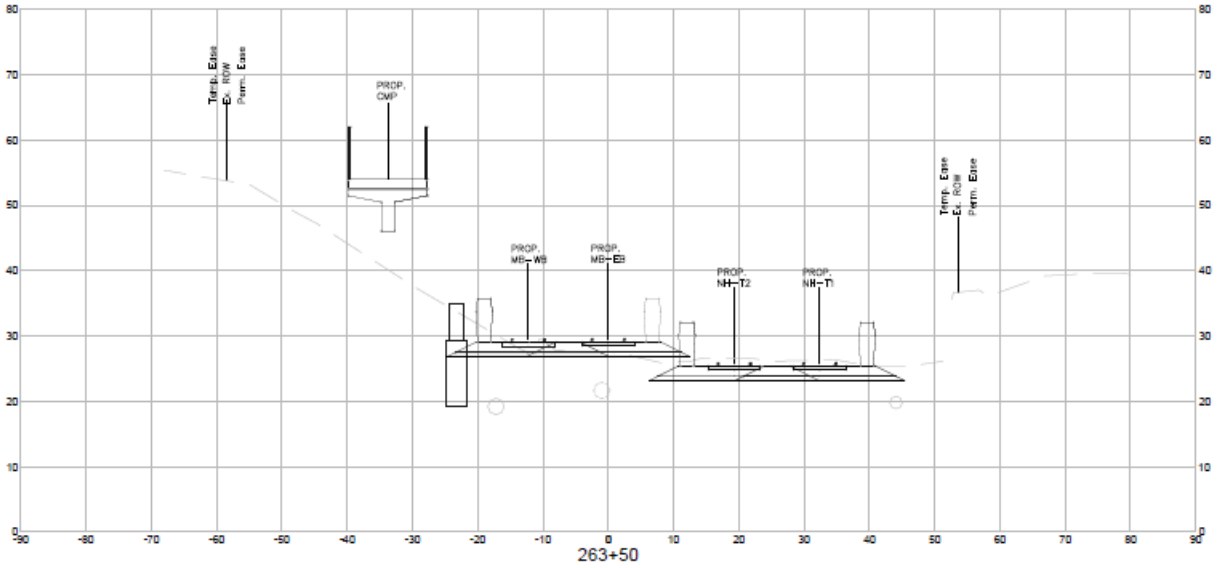

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
263+50

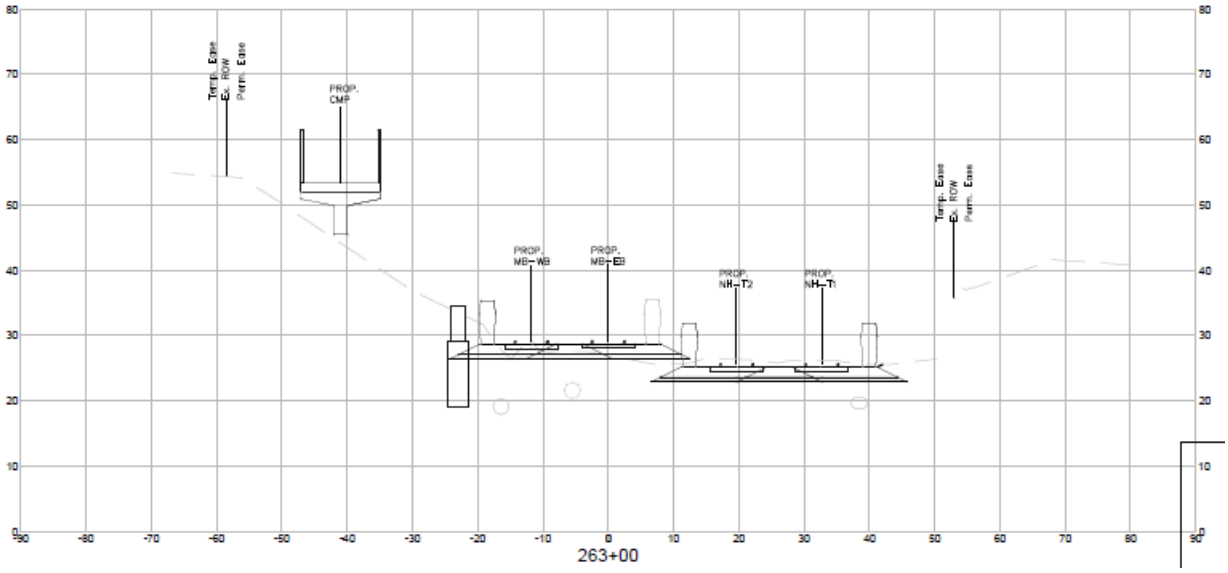

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
263+00

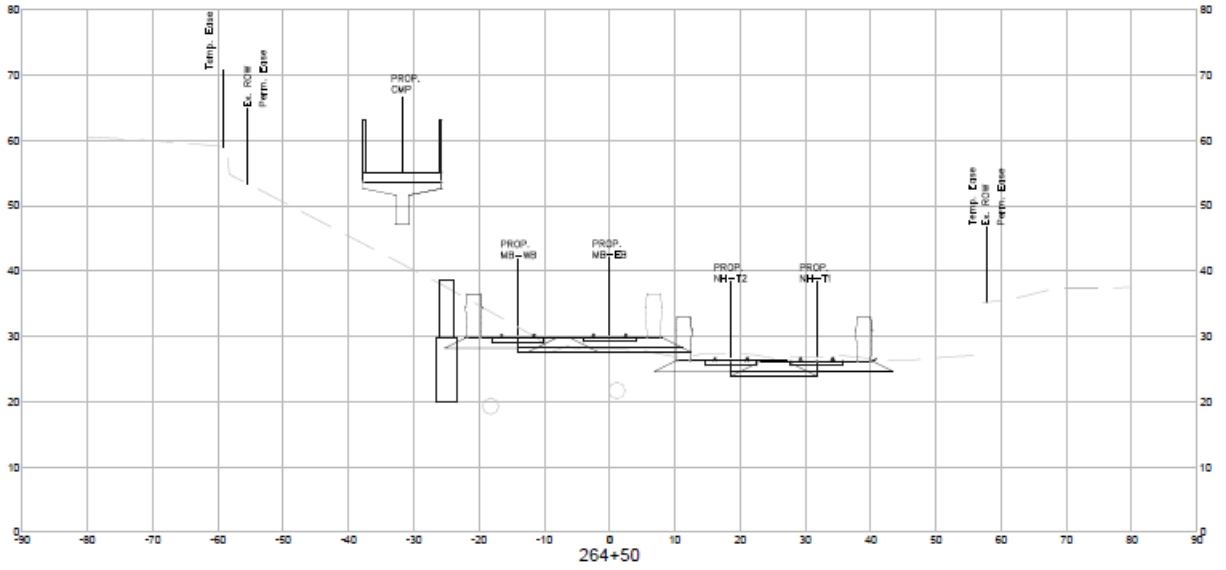

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Temp. Ease
Ex. ROW
Perm. Ease
264+50

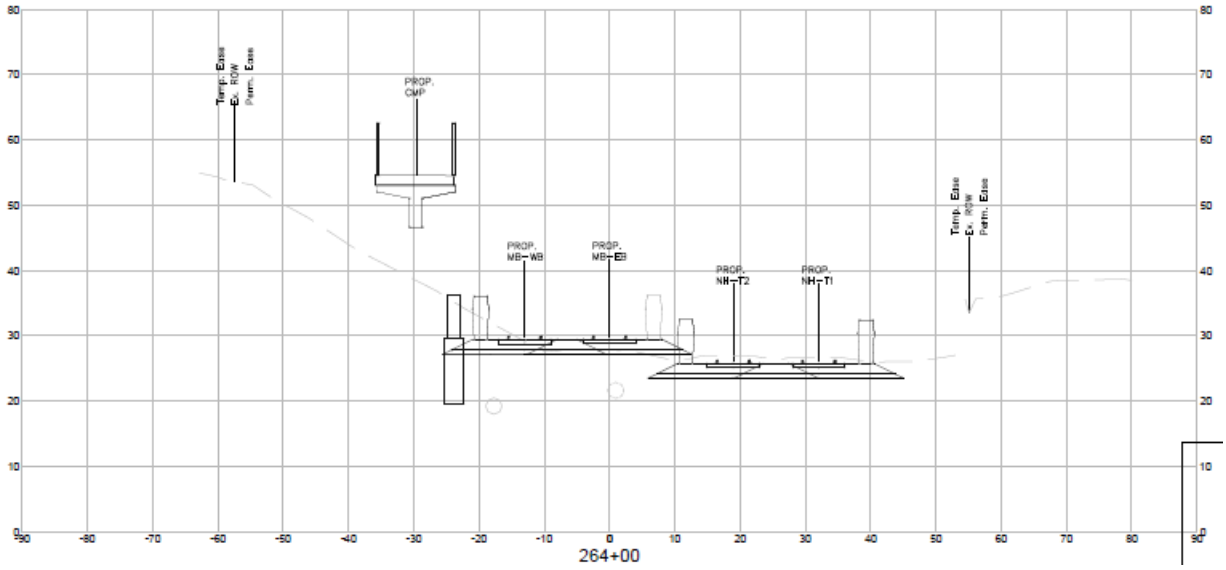

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Temp. Ease
Ex. ROW
Perm. Ease
264+00

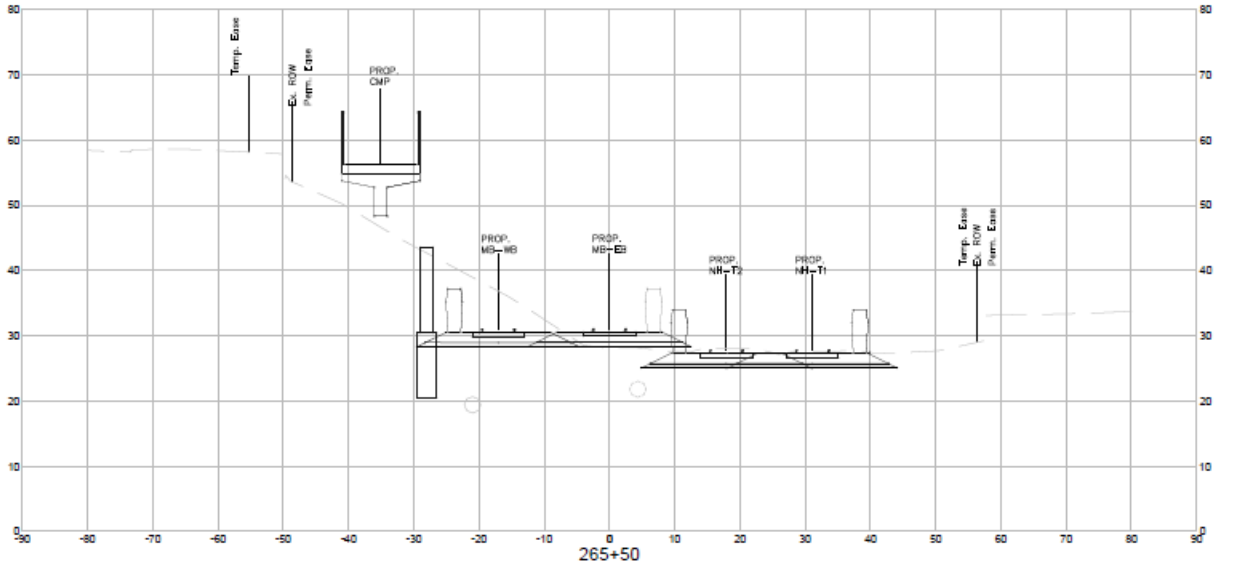

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Temp. Ease
Ex. ROW
Perm. Ease
265+50

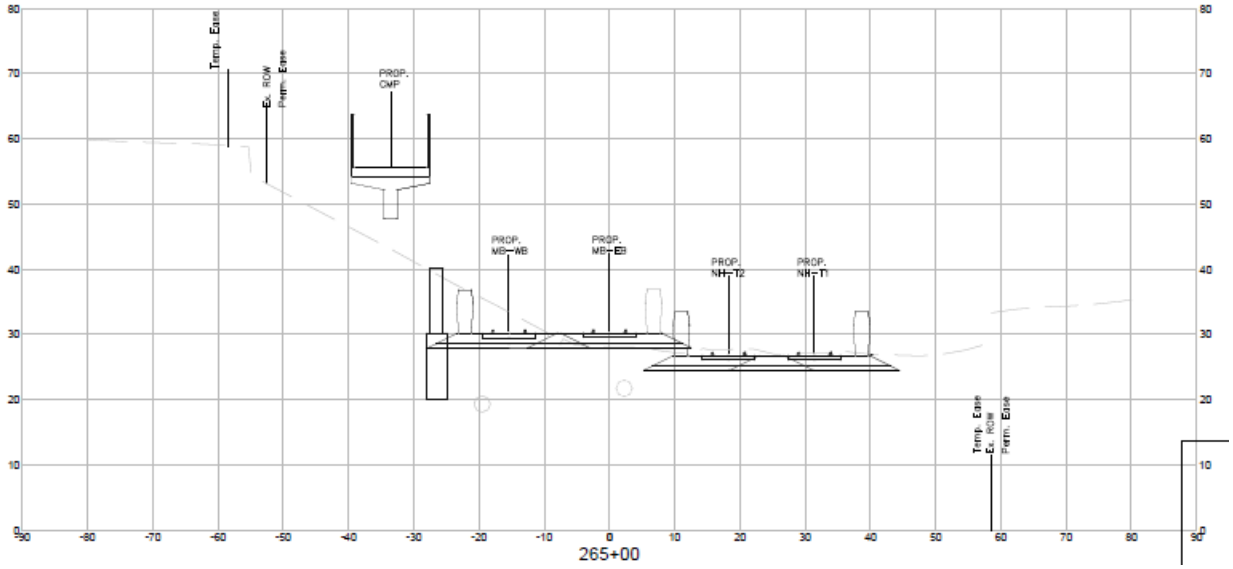

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Temp. Ease
Ex. ROW
Perm. Ease
265+00

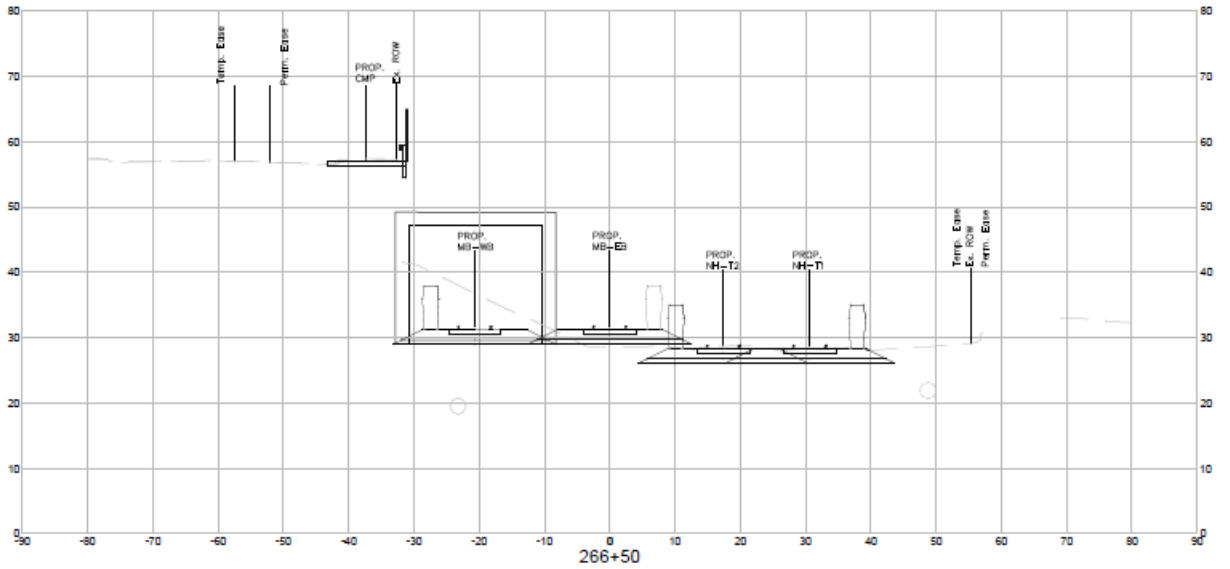

Temp. Ease
Perm. Ease
PROP. CMP
Ex. ROW
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
266+50

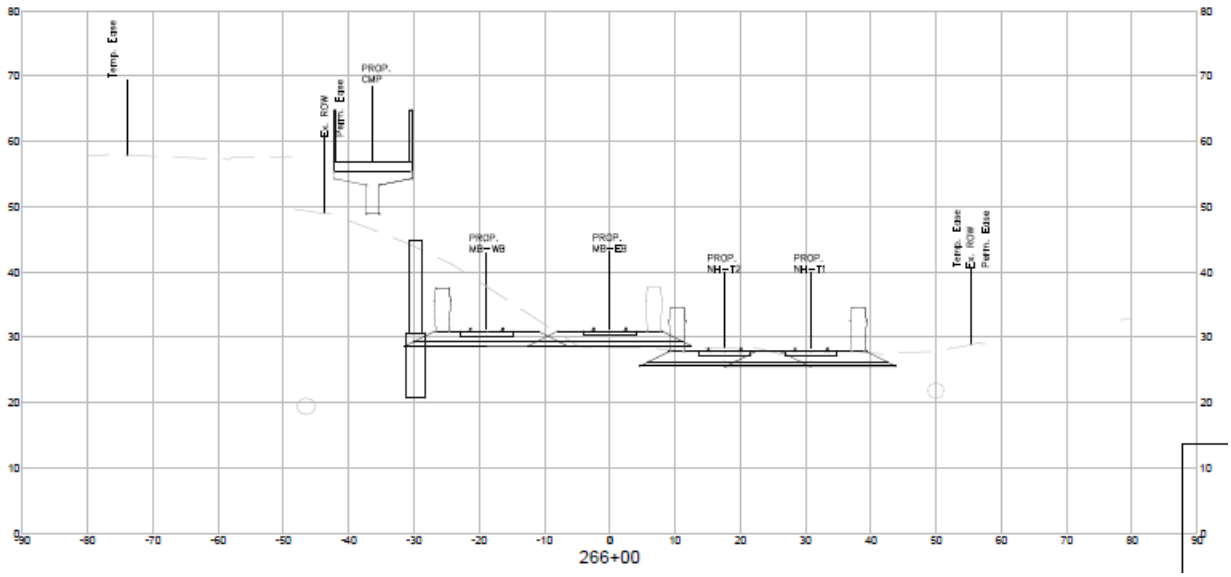

Temp. Ease
PROP. CMP
Ex. ROW
Perm. Ease
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
266+00

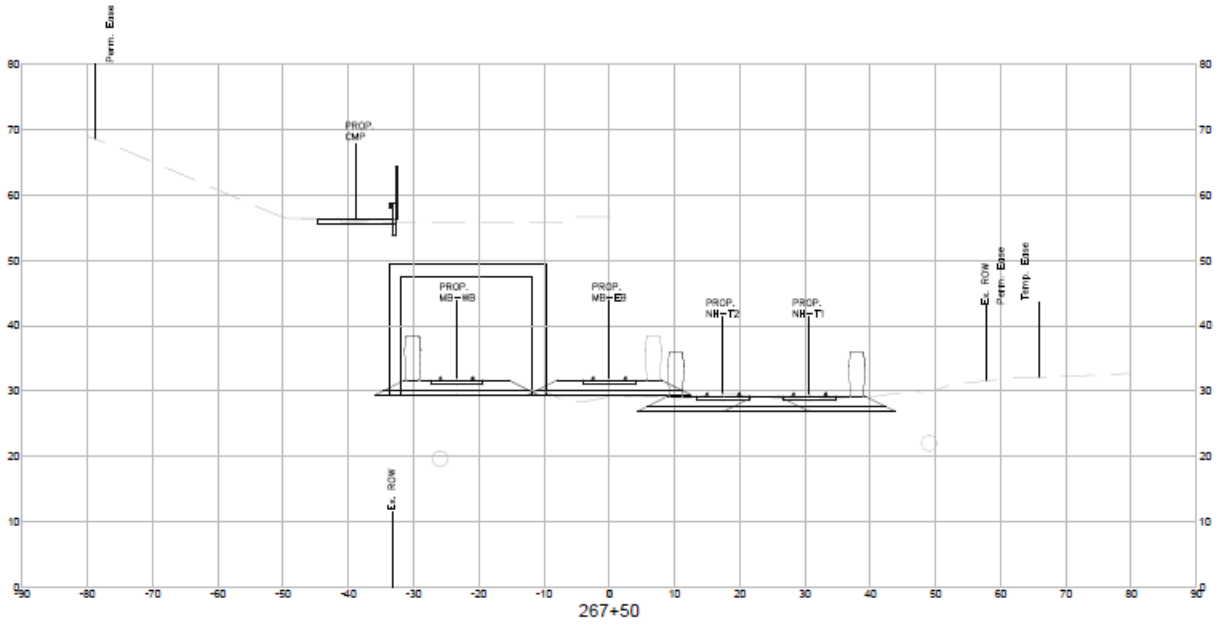

Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Ex. ROW
Perm. Ease
Temp. Ease
Ex. ROW
267+50

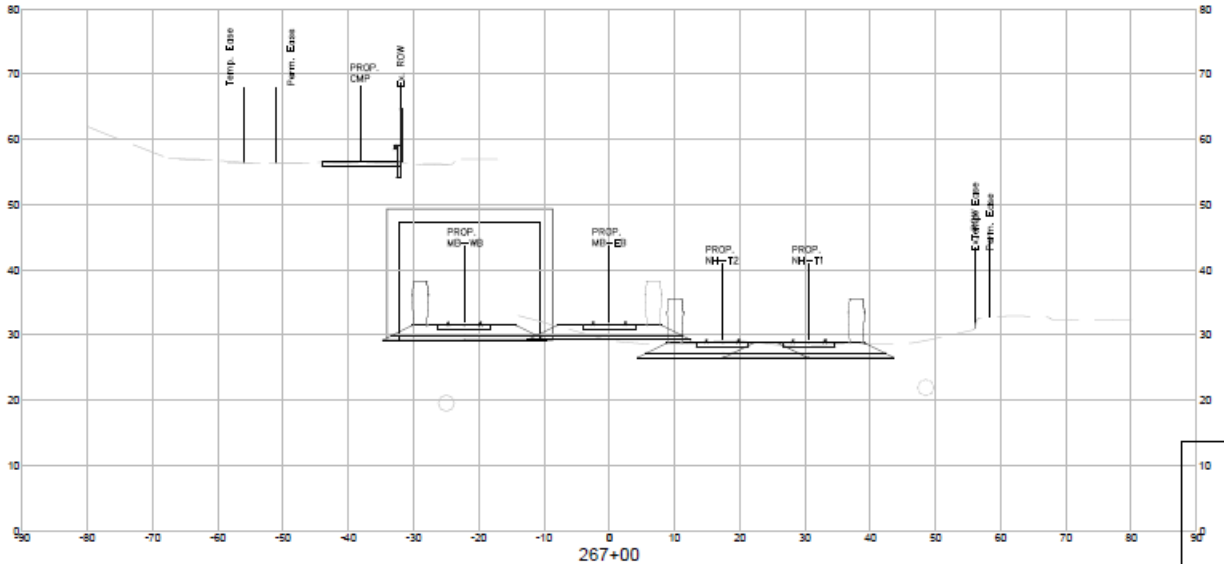

Temp. Ease
Perm. Ease
PROP. CMP
Ex. ROW
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Perm. Ease
267+00

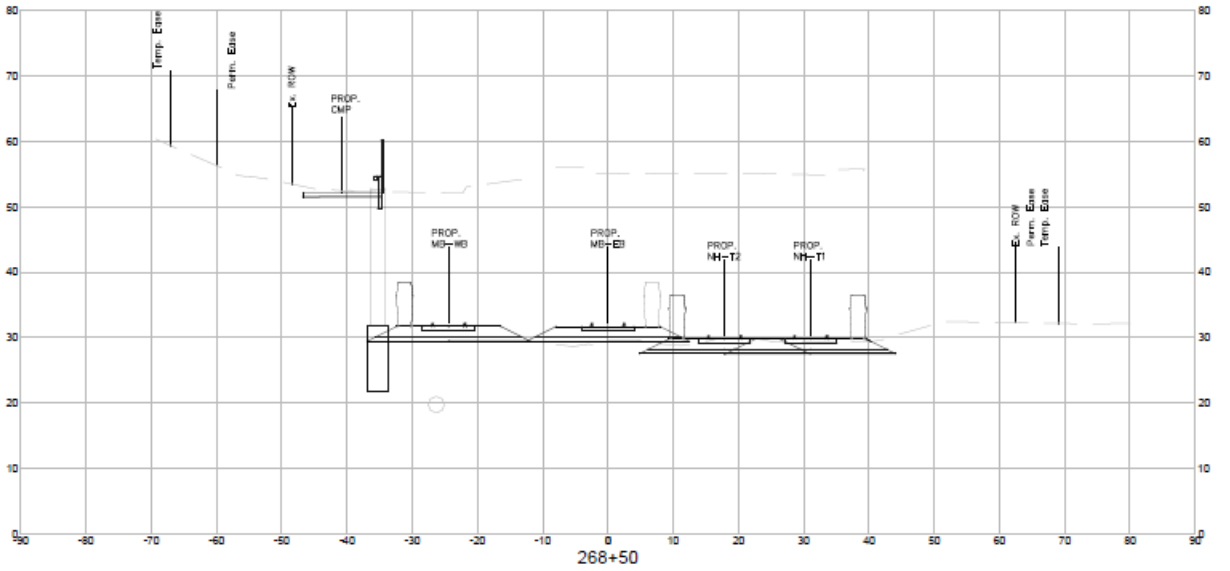

Temp. Ease
Perm. Ease
Ex. ROW
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
268+50

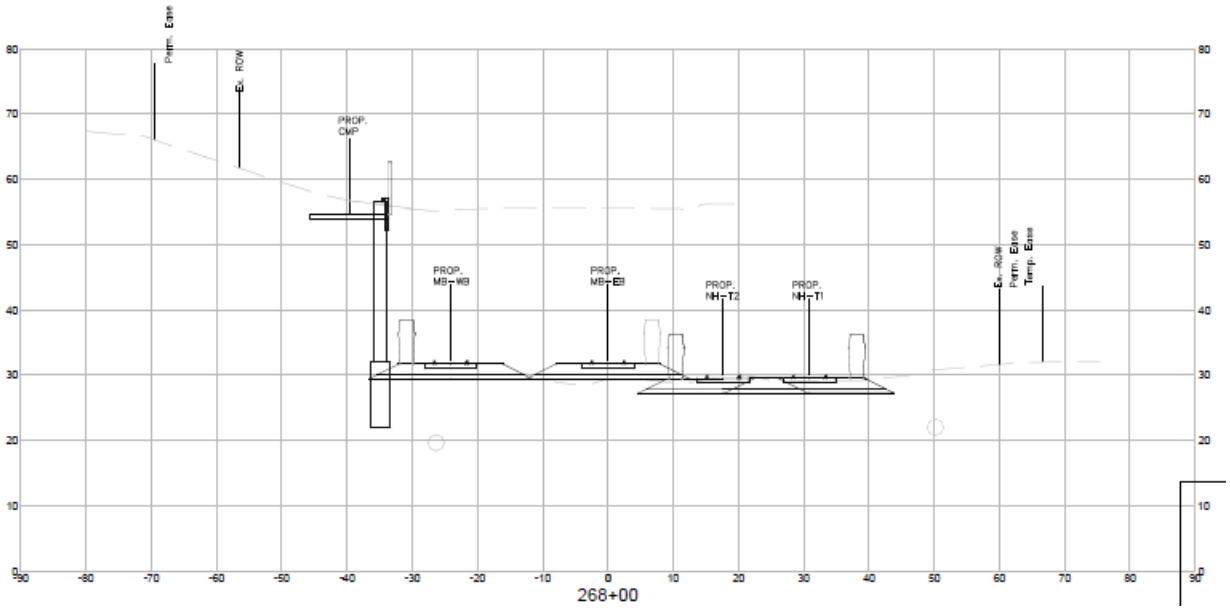

Perm. Ease
Ex. ROW
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
268+00

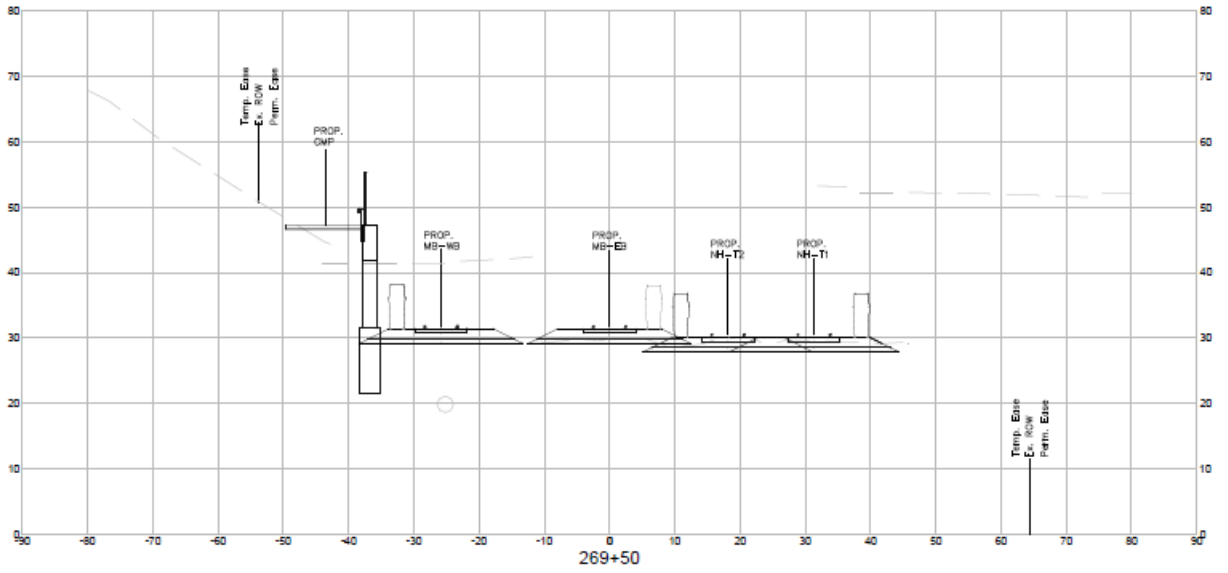

Temp. Ease
Ex. ROW
Perm. Ease
PROP.
CMP
PROP.
MB–WB
PROP.
MB–EB
PROP.
NH–T2
PROP.
NH–T1
Temp. Ease
Ex. ROW
Perm. Ease
269+50

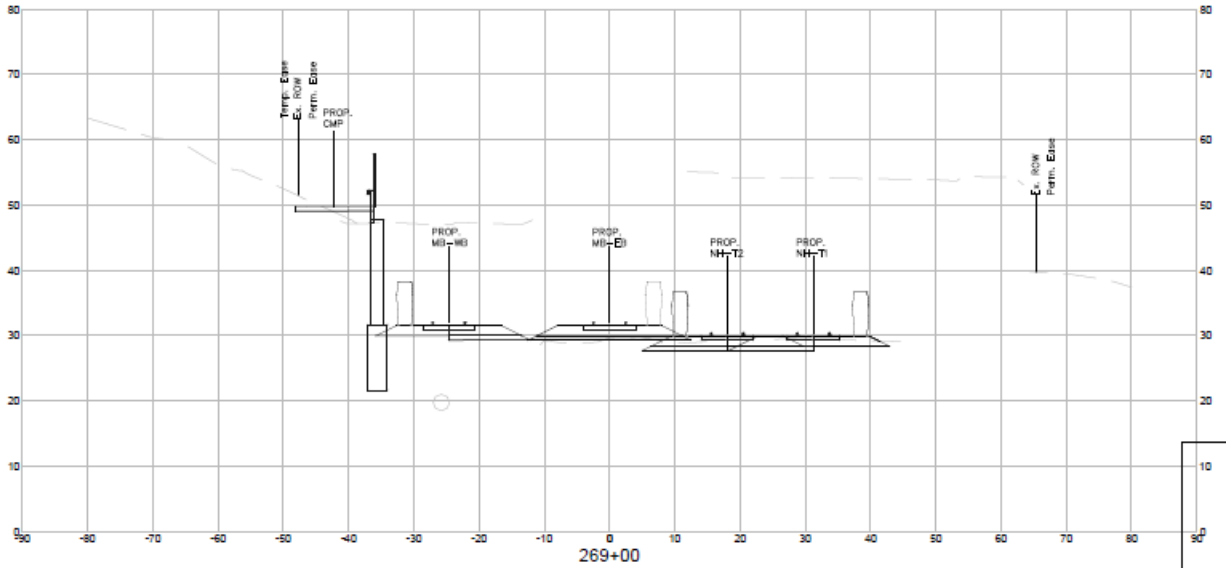

Temp. Ease
Ex. ROW
Perm. Ease
PROP.
CMP
PROP.
MB–WB
PROP.
MB–EB
PROP.
NH–T2
PROP.
NH–T1
Ex. ROW
Perm. Ease
269+00

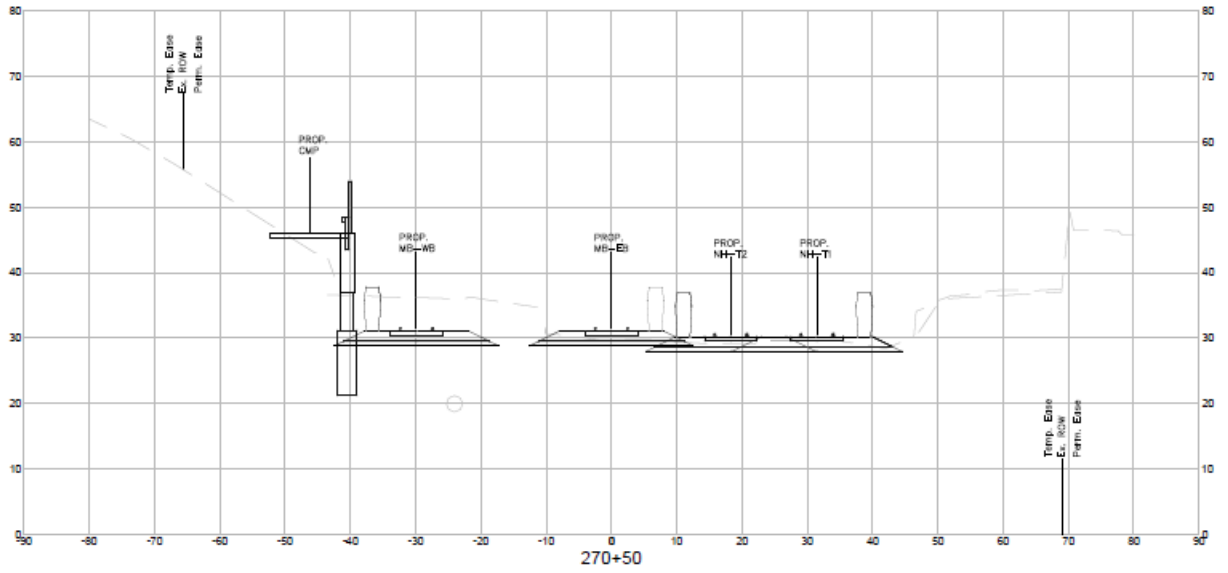

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
270+50

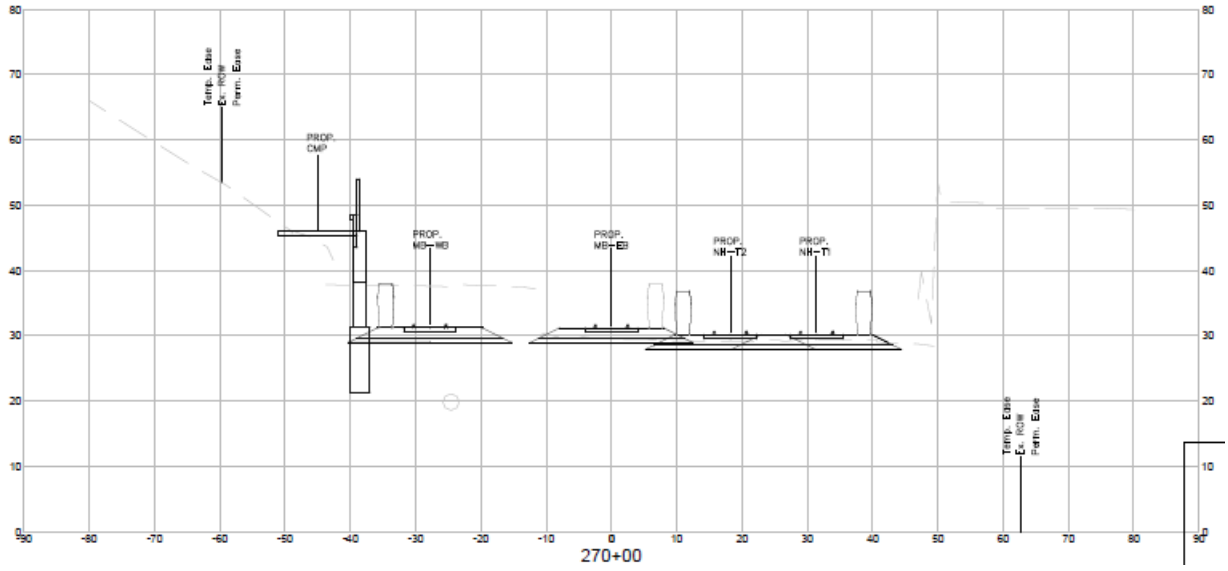

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
270+00

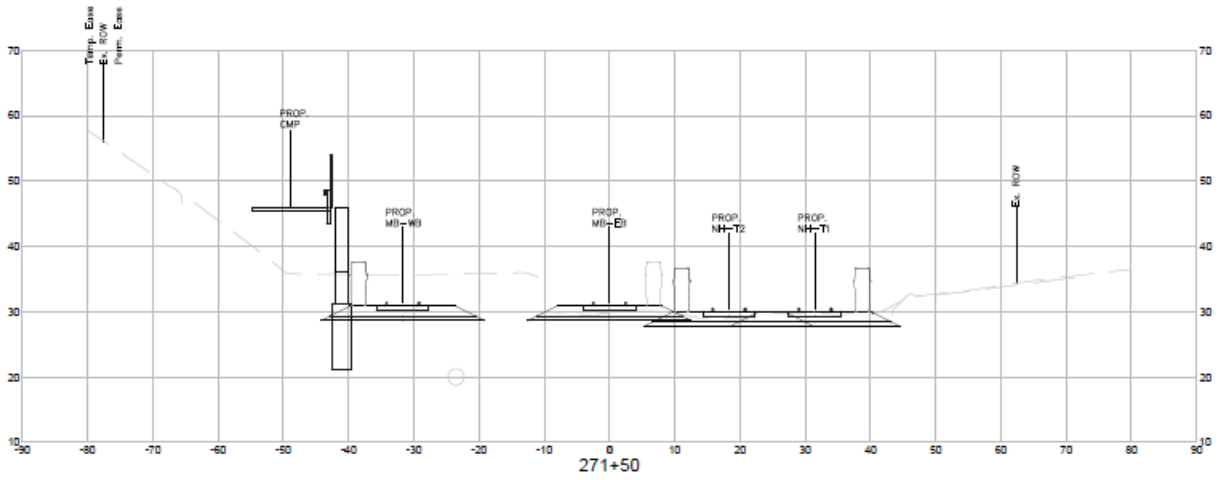

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
271+50

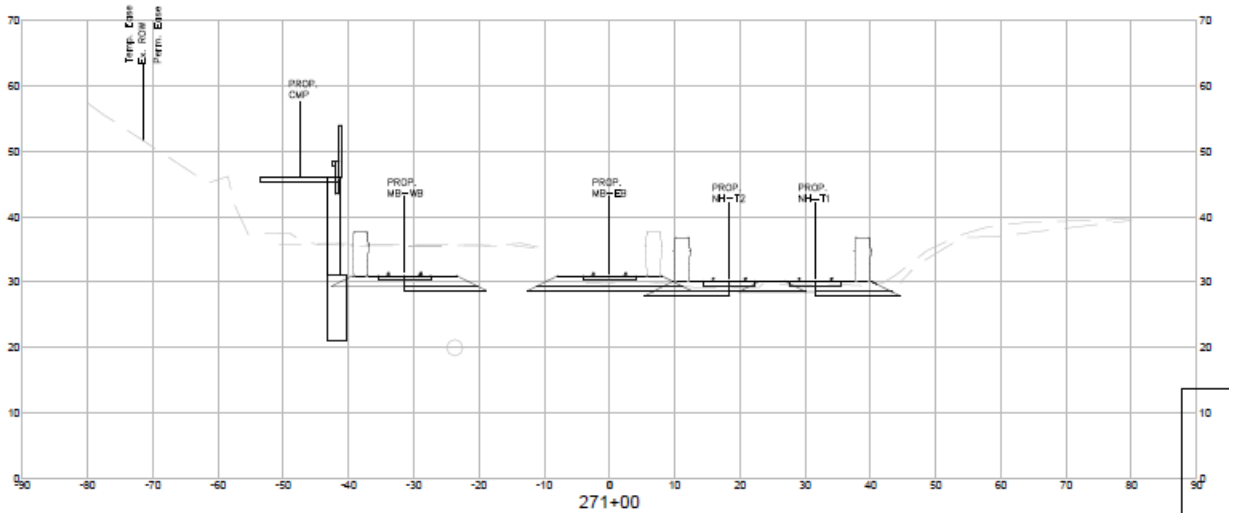

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
271+00

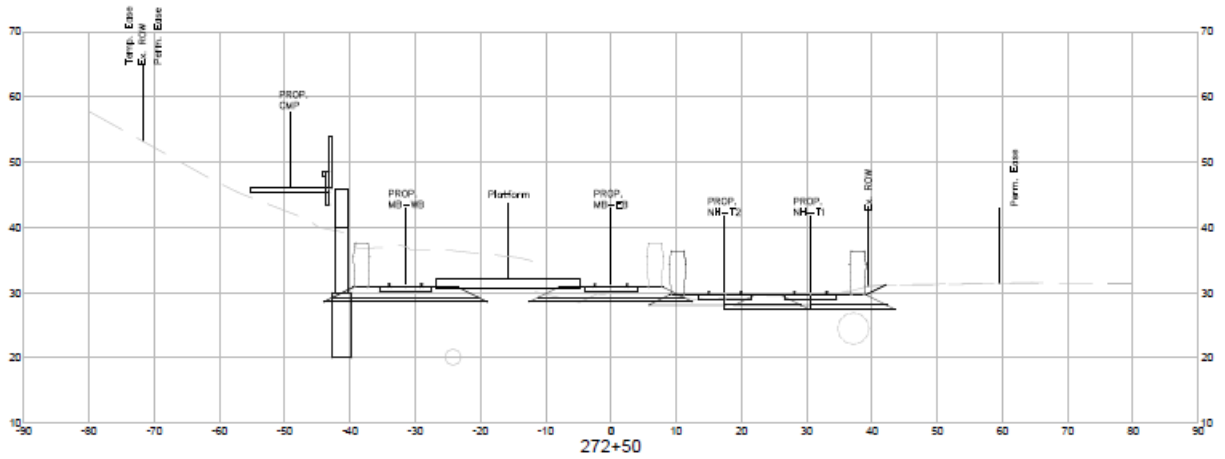

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-MB
Platform
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
272+50

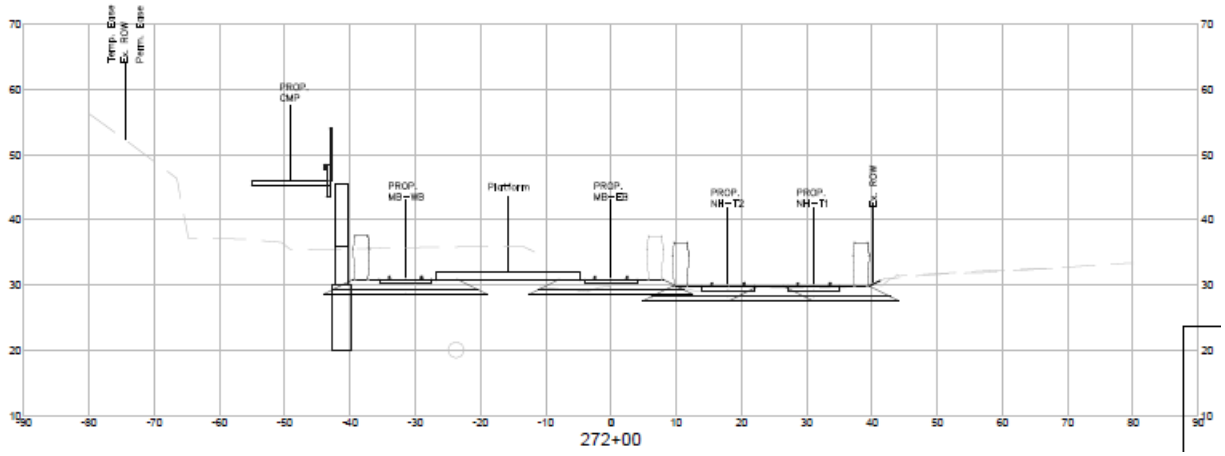

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-MB
Platform
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
272+00

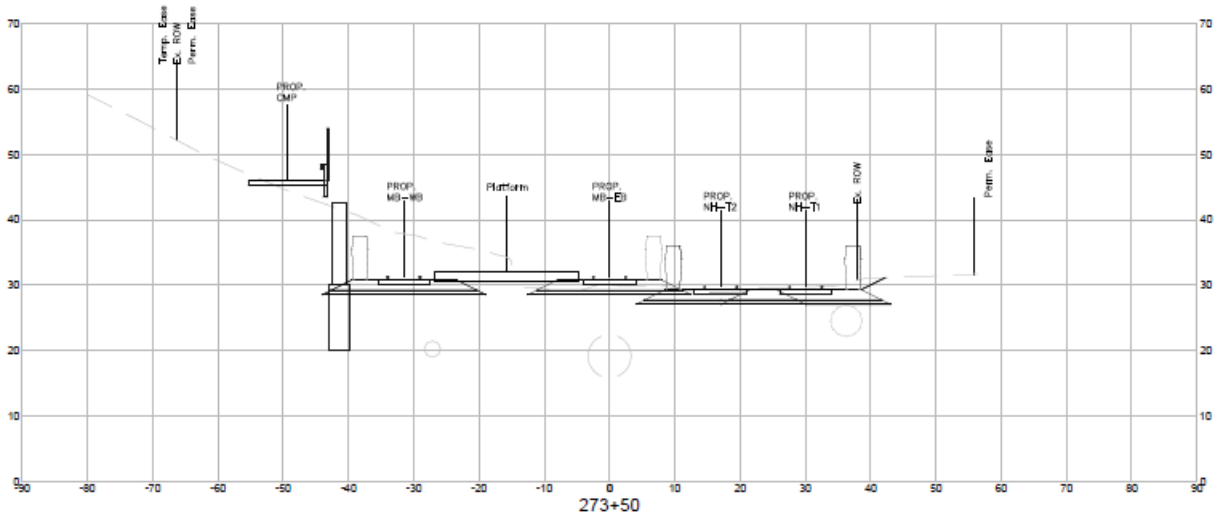

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-MB
Platform
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
273+50

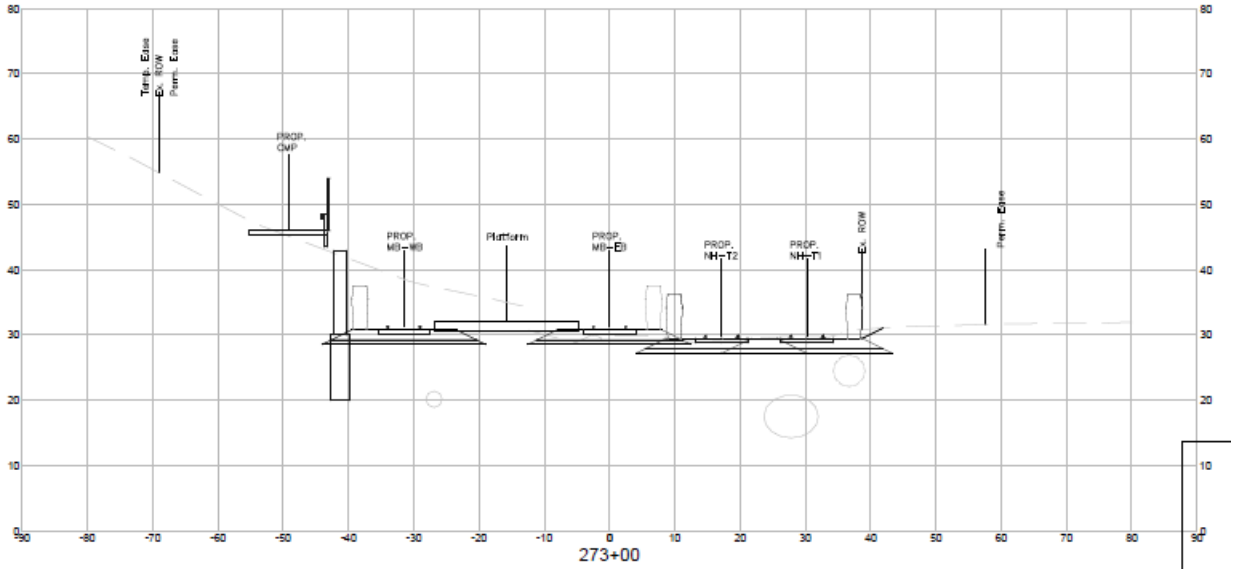
Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-MB
Platform
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
273+00

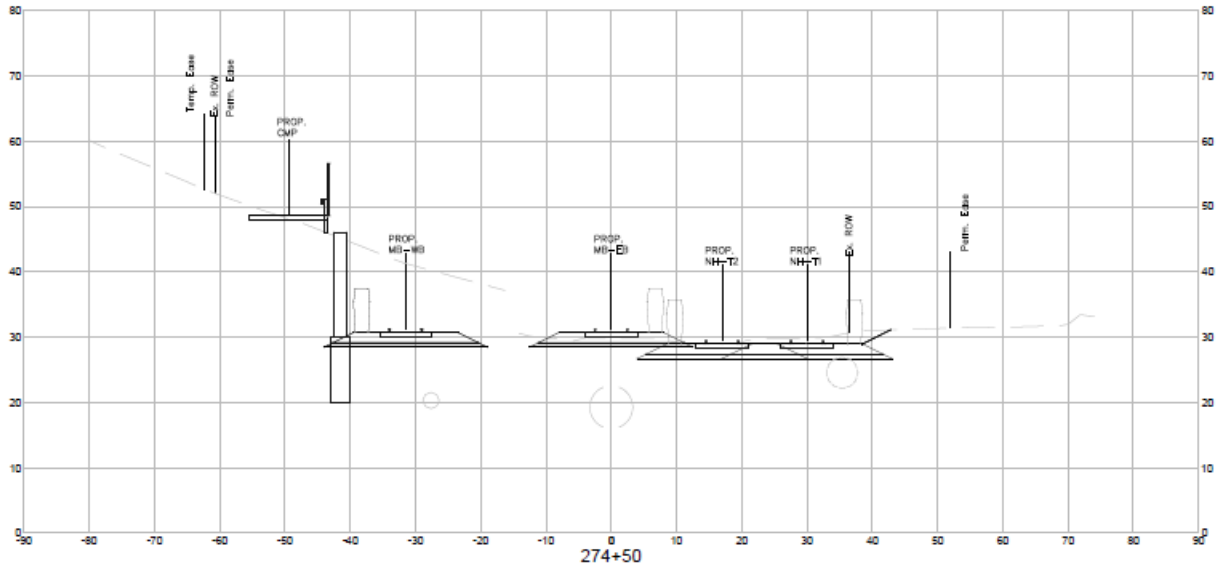
Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
274+50

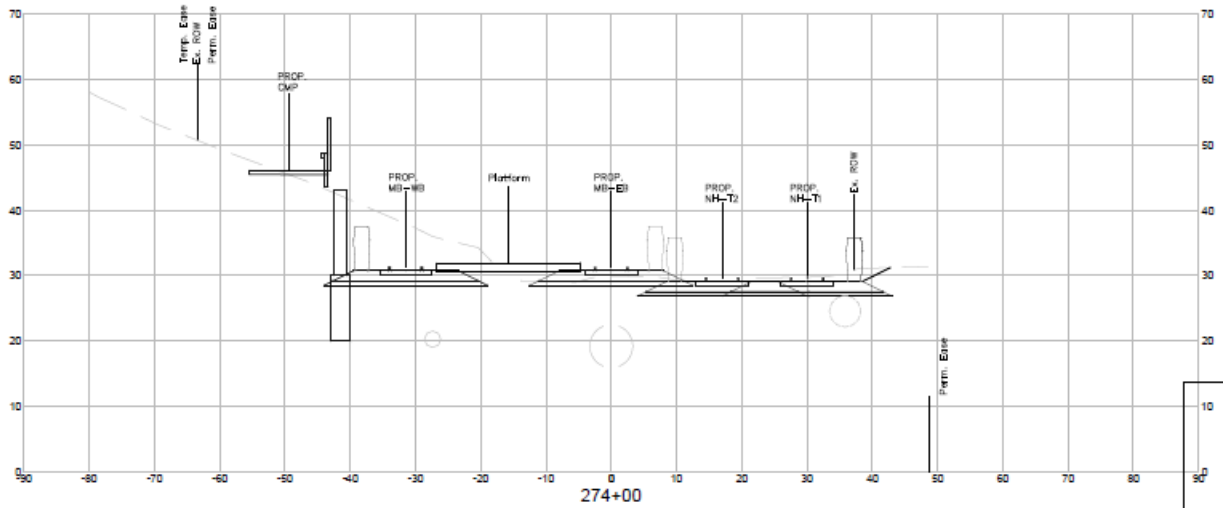
Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
Platform
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
274+00

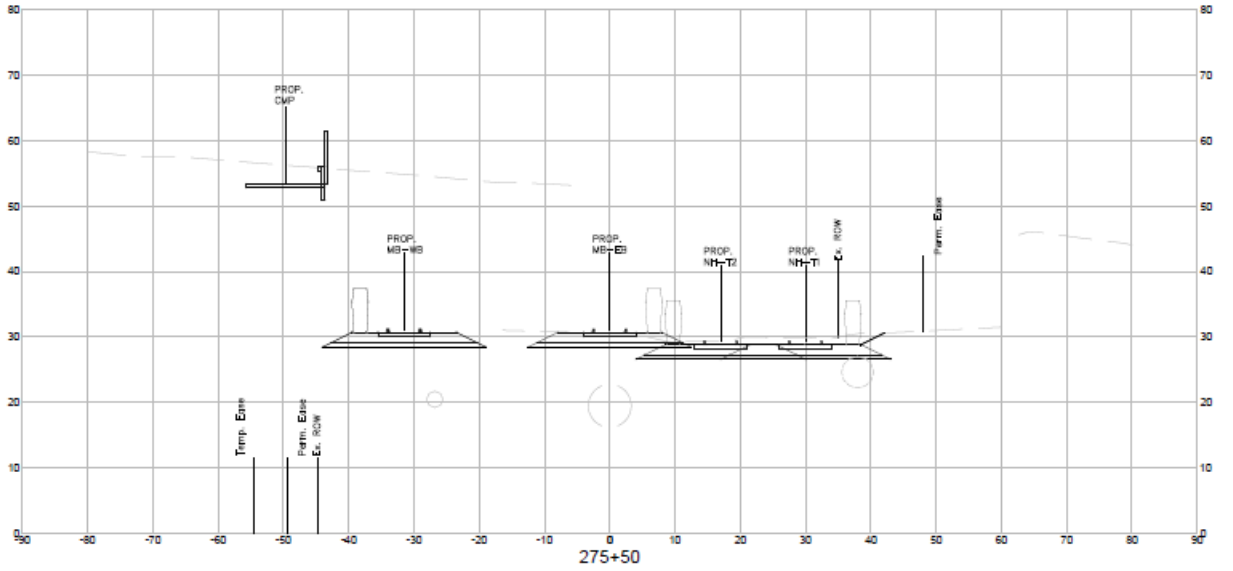
PROP. CMP
PROP. MB-MB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
Perm. Ease
Ex. ROW
275+50

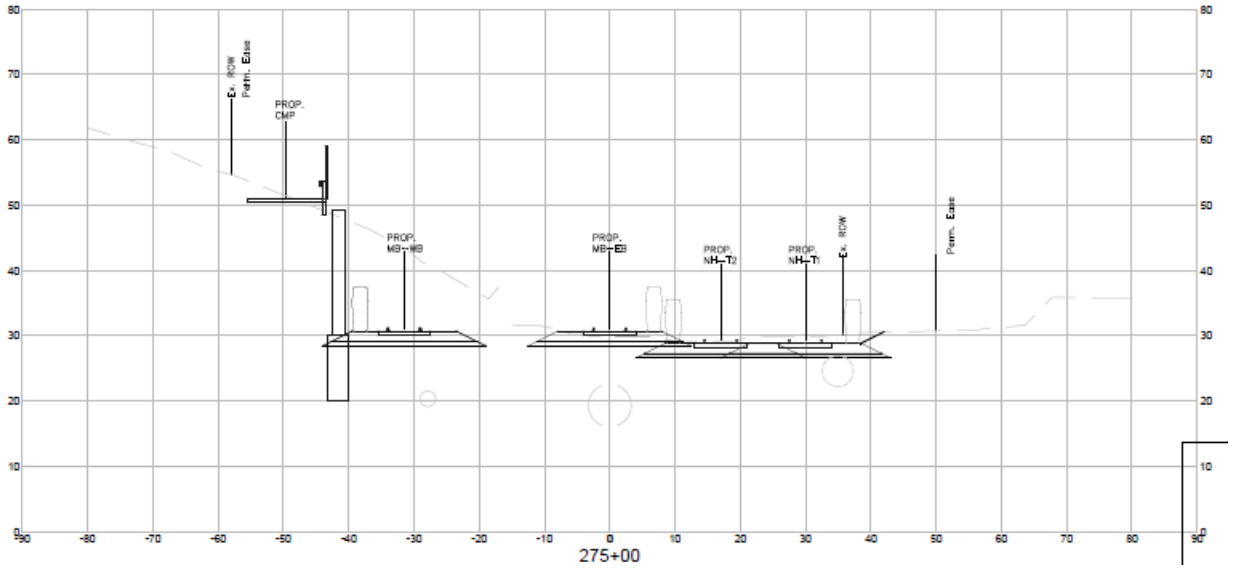
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-MB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
275+00

ATC No. 36

Acceptance of Formal Submission

Massachusetts Bay Transportation Authority

GLX - Procurement

ATC Review

ATC Information:

Type of ATC:	Formal
Title:	GLX Constructors ATC 07 - Elevated Community Path
Proposer Company:	GLX Constructors

Final Disposition:

Sent on behalf of Yvelisse Duvergé. The ATC Submittal is acceptable for inclusion in the Proposal.

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

FORMAL

ALTERNATIVE TECHNICAL CONCEPTS ("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

JULY 11, 2017 (Final Round)

GLX CONSTRUCTORS FORMAL ATC FORM

ELEVATED COMMUNITY PATH

Sections A though P below shall be completed to submit a Formal ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Formal ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. ATC Number

A sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.);

ATC 36

MBTA Preliminary ATC File Number: ATC-000014 – GLX Constructors ATC 08

B. Description and Conceptual Drawings

A description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information;

This ATC will eliminate the underpass at Walnut Street and reduce the underpass width at Medford Street by elevating the Community Path starting at grade from School Street. The Community Path would continue near cross-street grade along the west side of the ROW to Medford Street. After crossing Medford Street at grade, the Community Path will continue near cross-street grade to Walnut Street. After crossing Walnut Street at grade, the Community Path then progressively declines to track grade south of Walnut Street. Please reference the attached Figures ATC 36-1 "Elevated Community Path Plan and Profile" and ATC-36-2 "Elevated Community Path Cross Sections"

C. Locations and How Used

The locations where, and an explanation of how, the ATC will be used on the Project;

The ATC will eliminate the Underpasses at Walnut Street and Medford Street by elevating the Community Path starting from approximately 38' left Sta. MB-EB 252+00 at elevation 26.00 crossing Walnut Street at Grade. The Community Path would continue to approximately 38' left Sta. MB-EB 267+00 elevation 56.00. The Community Path would cross Medford Street at Grade. The Community Path would continue to 54' left Sta .MB-EB 275+50 elevation 52.00 where it would tie into School Street. This would be the North End of the Elevated Community Path.

D. Changes in Rail or Transit Operations

Any changes in rail or transit operations requirements associated with the ATC, including ease of operations;

No changes in operations are anticipated as a result of this ATC.

E. Changes in Routine or Capital Maintenance

Any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance;

This ATC eliminates the need for the routine and capital maintenance of lighting for the Walnut Street and Medford Street underpasses, as well as the routing and capital maintenance of the underground ventilation for the Medford Underpass as it would be over 200' long.

F. Changes in Anticipated Service Life

Any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC;

No change in service life is anticipated as a result of this ATC.

G. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations;

Para 9.2.3.3 Geometry (h) Table 9.2-1 Community Path and Roadway Interfaces Medford Street and Walnut Street Underpass of the Technical Provisions.

H. Justification of Use

An analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed;

This ATC eliminates the pedestrian underpass at Walnut Street and Medford Street which increases safety and security of Pedestrians using the Community Path. This ATC also eliminates the need for Fire and Life Safety features and lighting for underpasses at Walnut Street and Medford Street. This ATC improves accessibility for emergency and maintenance vehicles operating on the Community Path

I. Preliminary Analysis and Quantitative Discussion

A preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation;

No impacts on rail or transit operations are anticipated as a result of this ATC.

J. Impacts on Third Parties

A description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC. Proposers are advised that they may (i) be solely responsible for the cost and schedule impacts of the acquisition of any such Additional Properties, including the cost thereof and obtaining any necessary environmental approvals; (ii) not be entitled to any change order for time or money as a result of site conditions (i.e., hazardous materials, differing site conditions, geotechnical issues, or utilities) on such Additional Properties; and (iii) not be entitled to any change order for time or money as a result of any delay, inability, or cost associated with the acquisition of such Additional Properties;

This ATC eliminates the risk of relocating the 48" MWRA Waterline at Walnut Street. This ATC also reduces the footprint of the Community Path which will reduce potential ROW issues.

K. History of Use and References

A description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements;

This ATC uses a similar elevated community path concept that has been successfully used at the NorthPoint park. This concept is also similar to what has been called for on the Project Concept Plans from School Street to Central Street.

L. Additional Risks

A description of added risks to the MBTA or third parties associated with implementing the ATC;

No additional risks to the MBTA or to third parties are anticipated as a result of this ATC.

M. Additional Costs

An estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC;

Additional costs to the MBTA, DB Entity and third parties will not result from this ATC. One of the primary purposes of this ATC is cost reduction.

N. Estimated Price Adjustment

An estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented;

This ATC will result in an estimated savings of $2,000,000. The ATC pricing as shown in this proposal is an all inclusive price. All price deducts and/or adds have been considered, and the resulting price adjustment is offered as shown.

O. Schedule Adjustment

An estimate of the schedule adjustment, should the ATC be approved and implemented; and


This ATC does not require any schedule adjustment.


P. Analysis of Quality, Performance, and Reliability


An analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents.

This ATC will provide equal quality, performance, and reliability to the specified plans. This ATC reduces maintenance cost needed to maintain performance through the elimination or reduction of ventilation and lighting requirements.

Figure ATC 36-1: Elevated Community Path Plan and Profile (2 Pages)

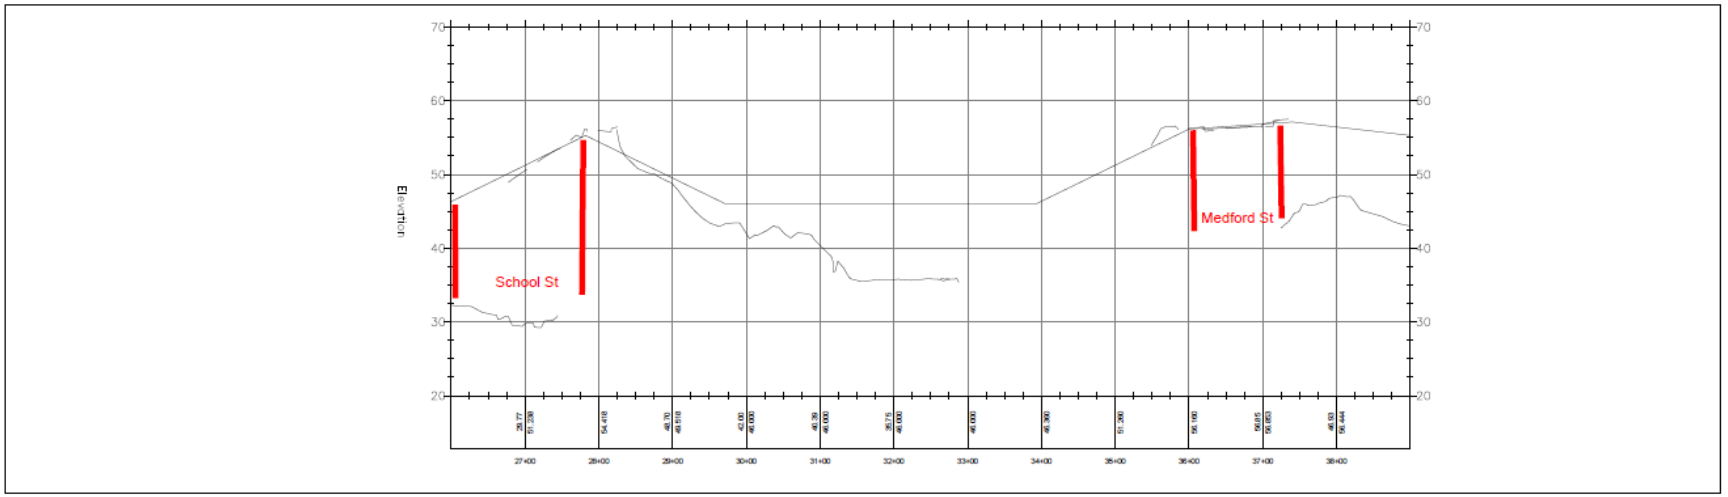

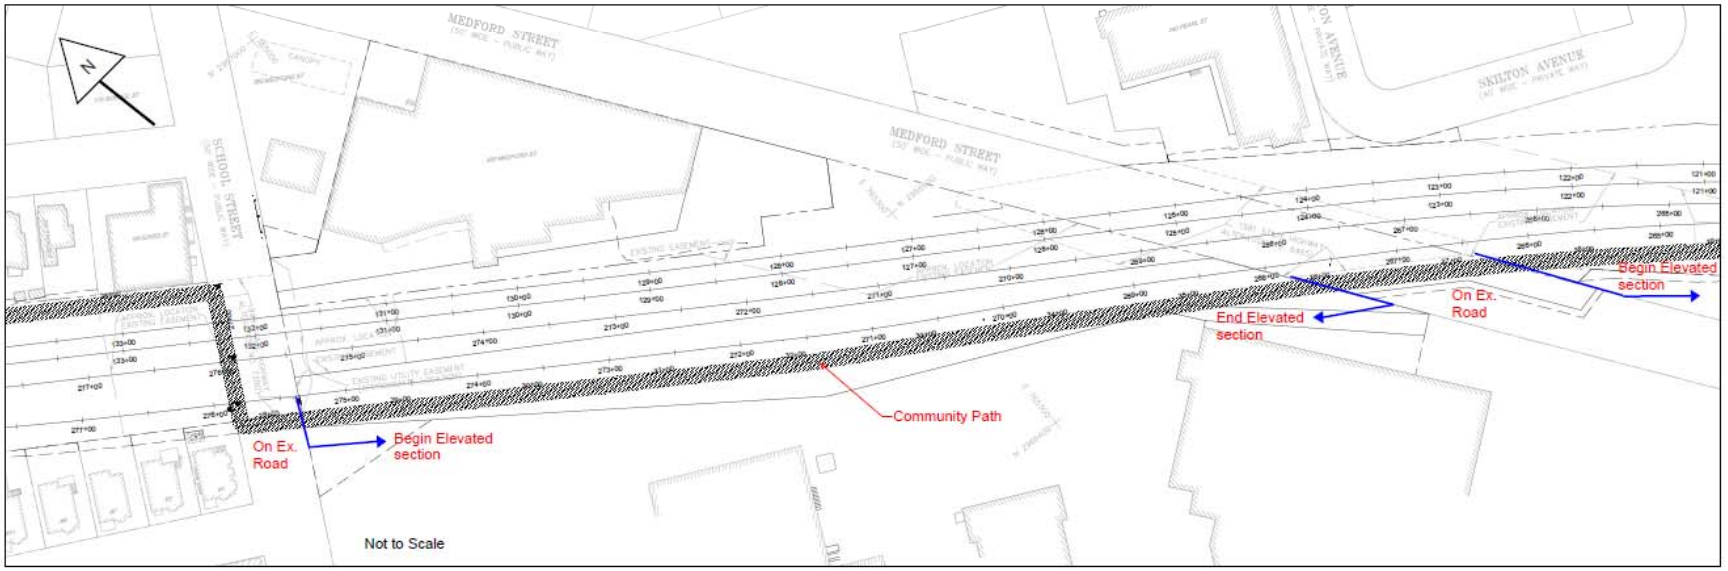

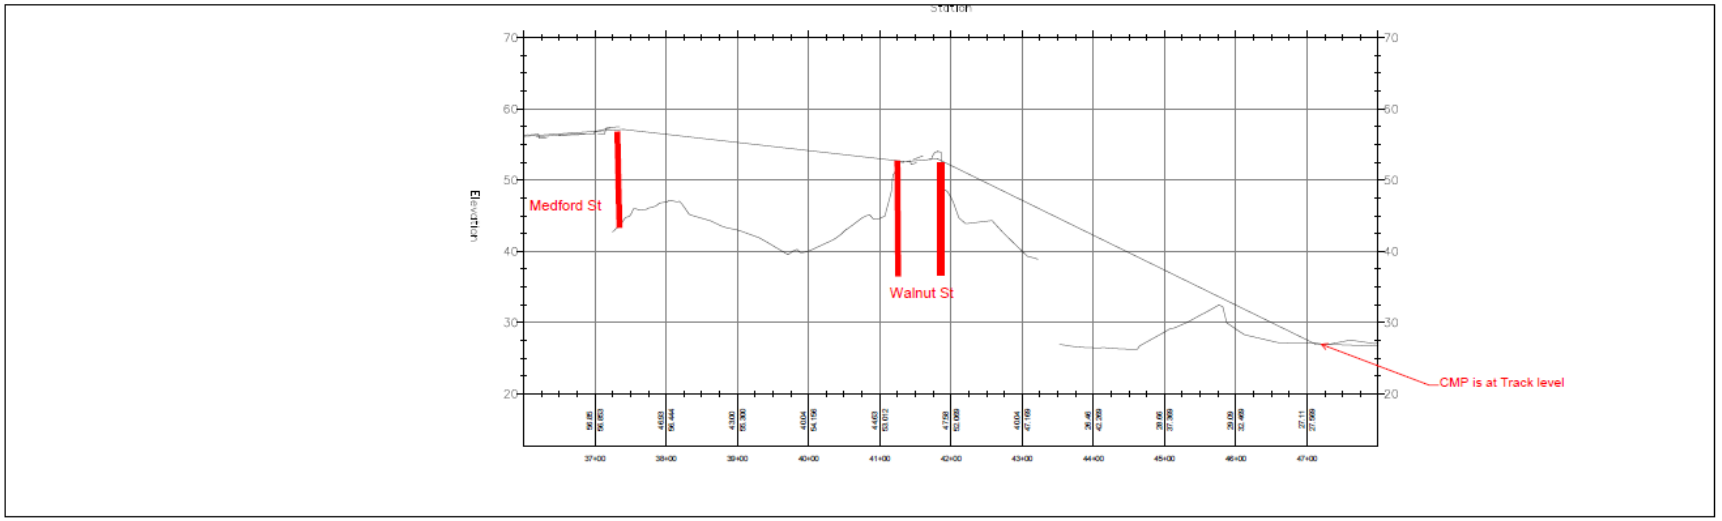
Station
Elevation
70
60
50
40
30
20
Medford St
Walnut St
CMP is at Track level
37+00
38+00
39+00
40+00
41+00
42+00
43+00
44+00
45+00
46+00
47+00





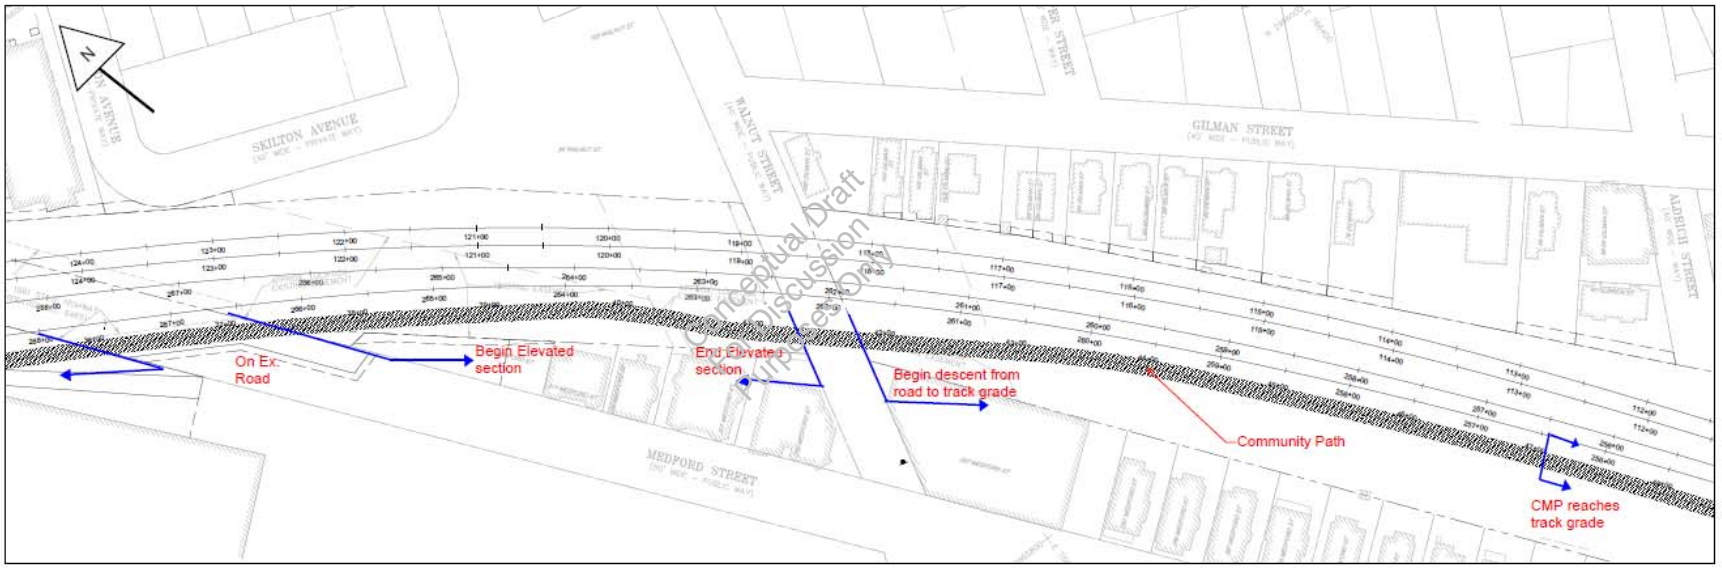

N
SKILTON AVENUE
WALNUT STREET
GILMAN STREET
MEDFORD STREET
Conceptual Draft
For Discussion
Purposes Only
On Ex. Road
Begin Elevated section
End Elevated section
Begin descent from road to track grade
Community Path
CMP reaches track grade


Figure ATC-36-2: Elevated Community Path Cross Sections (20 Pages)

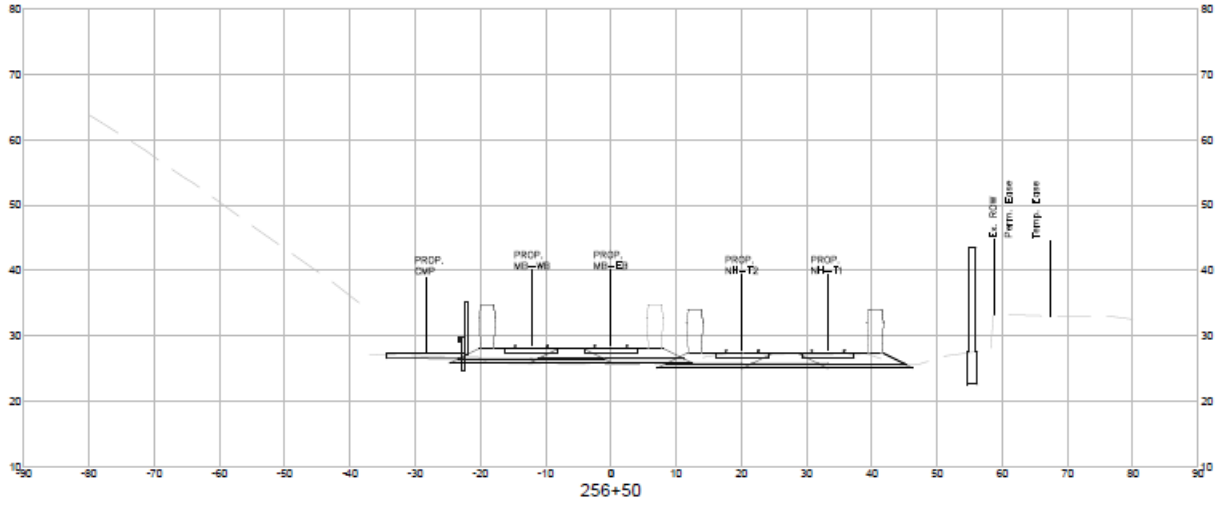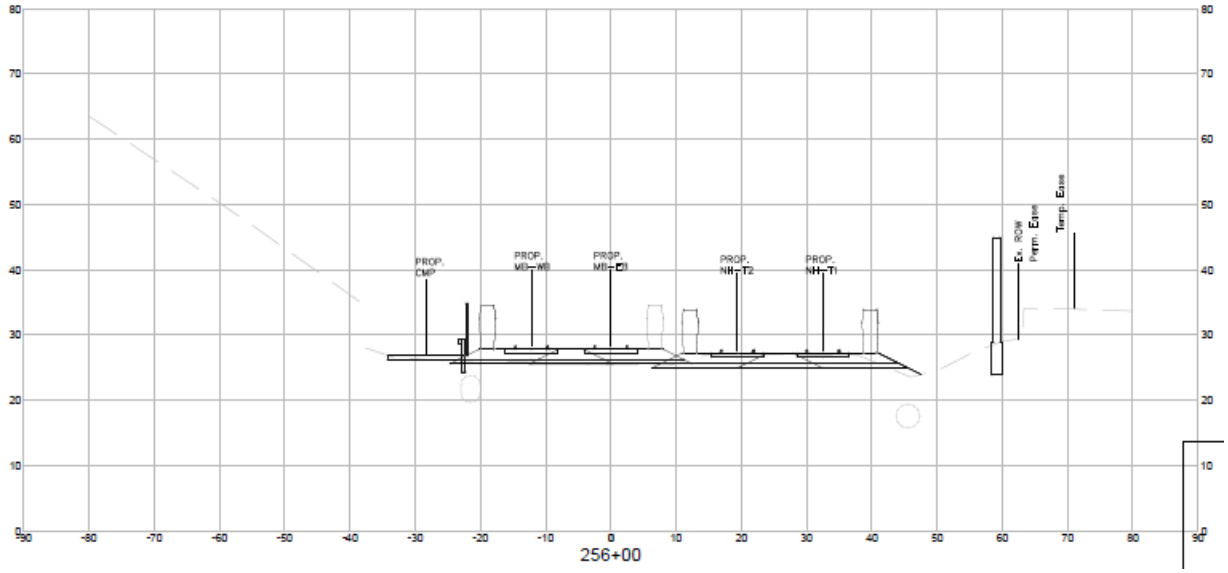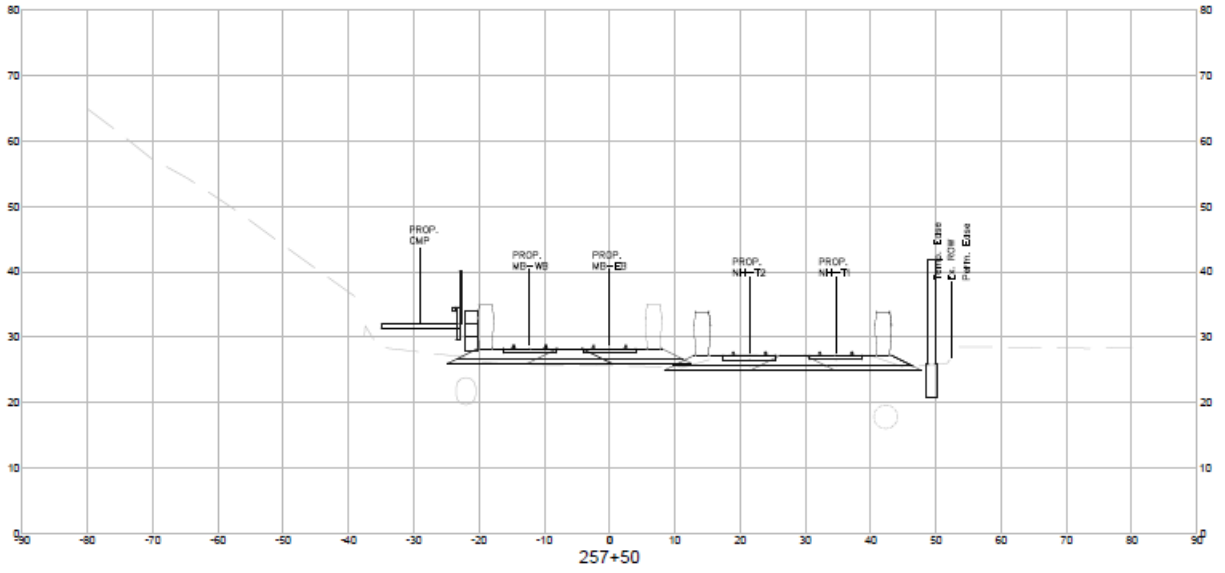


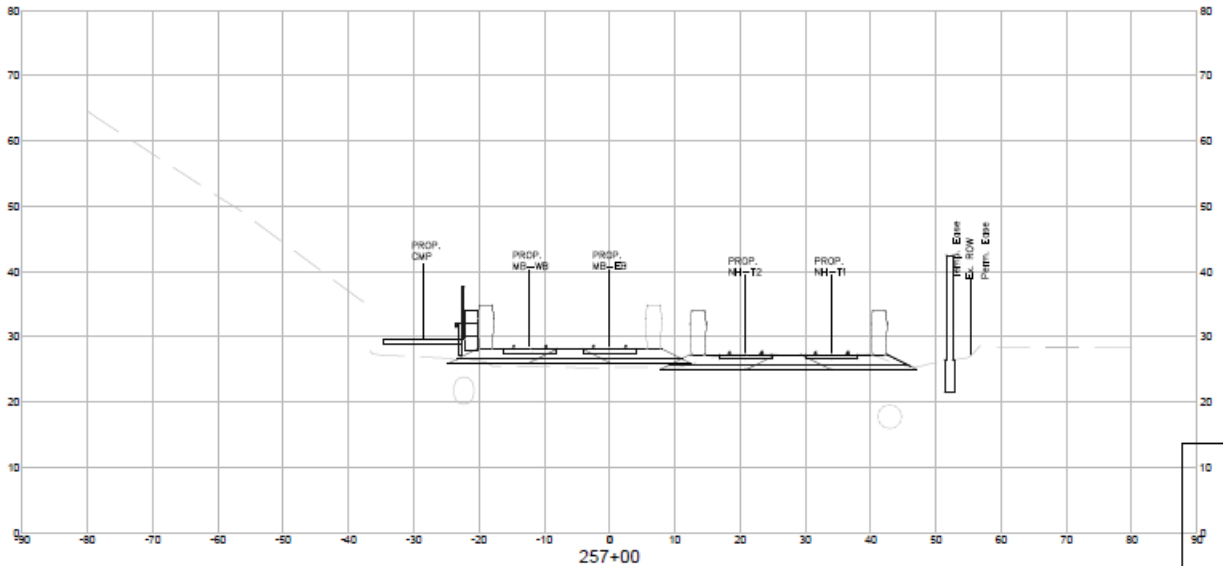




PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
257+50



PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
257+00

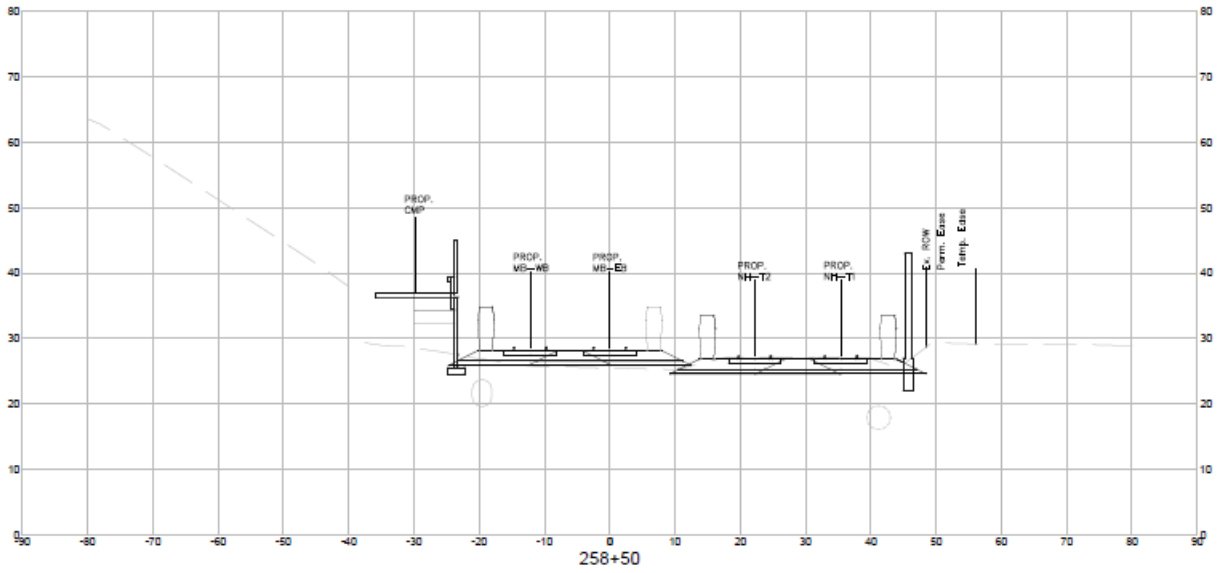

PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–TZ
PROP. NH–TI
Ex. ROW
Perm. Ease
Temp. Ease
258+50

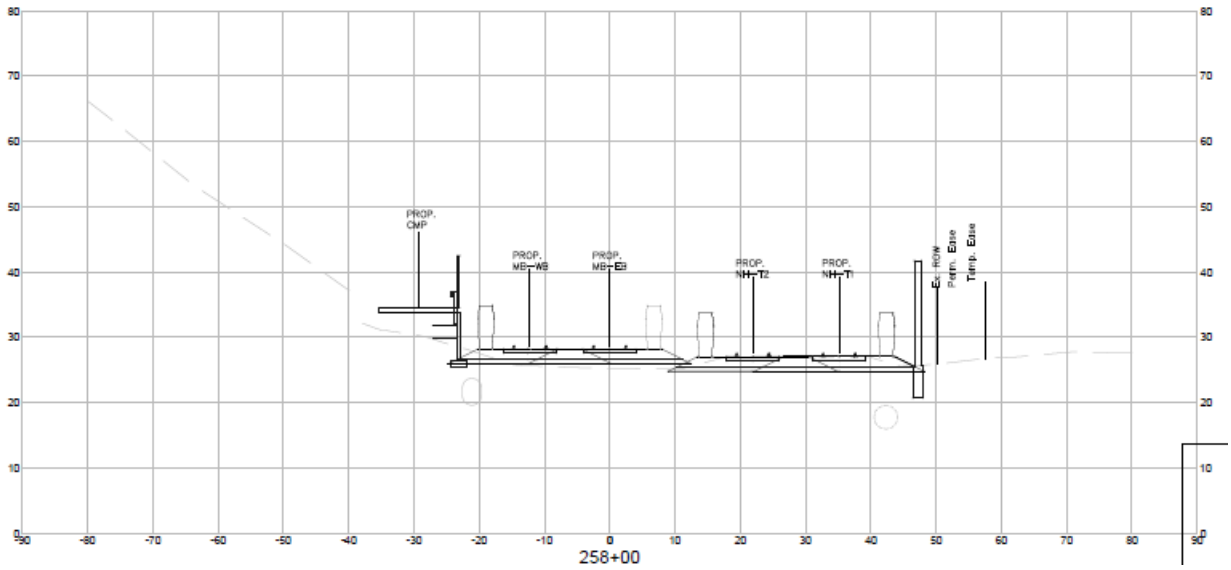

PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–TZ
PROP. NH–TI
Ex. ROW
Perm. Ease
Temp. Ease
258+00

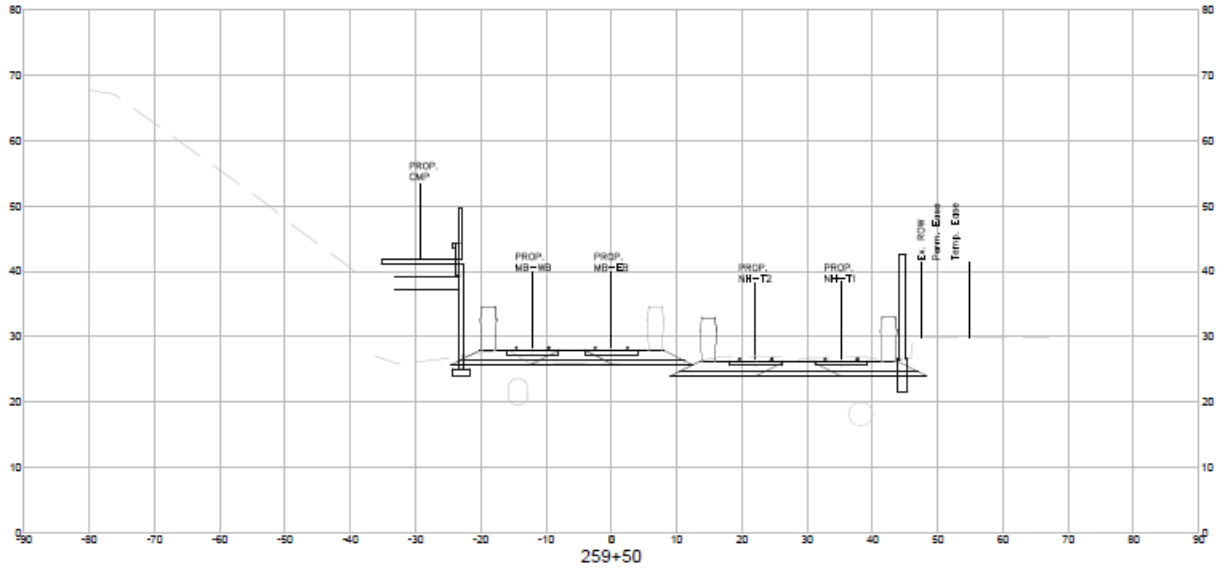

PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
259+50

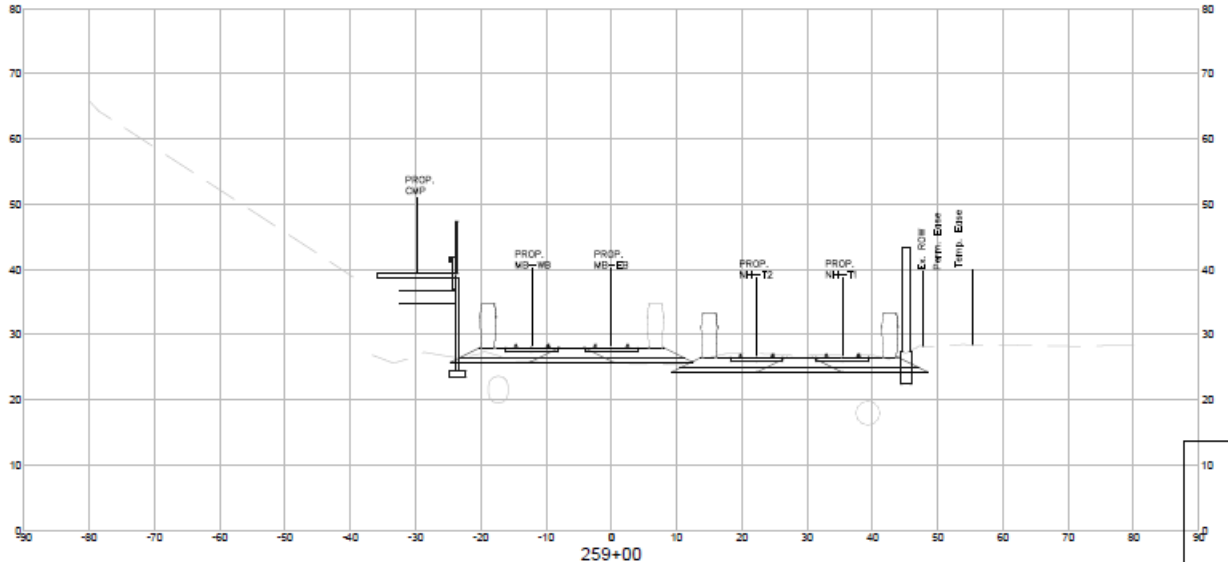

PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
259+00

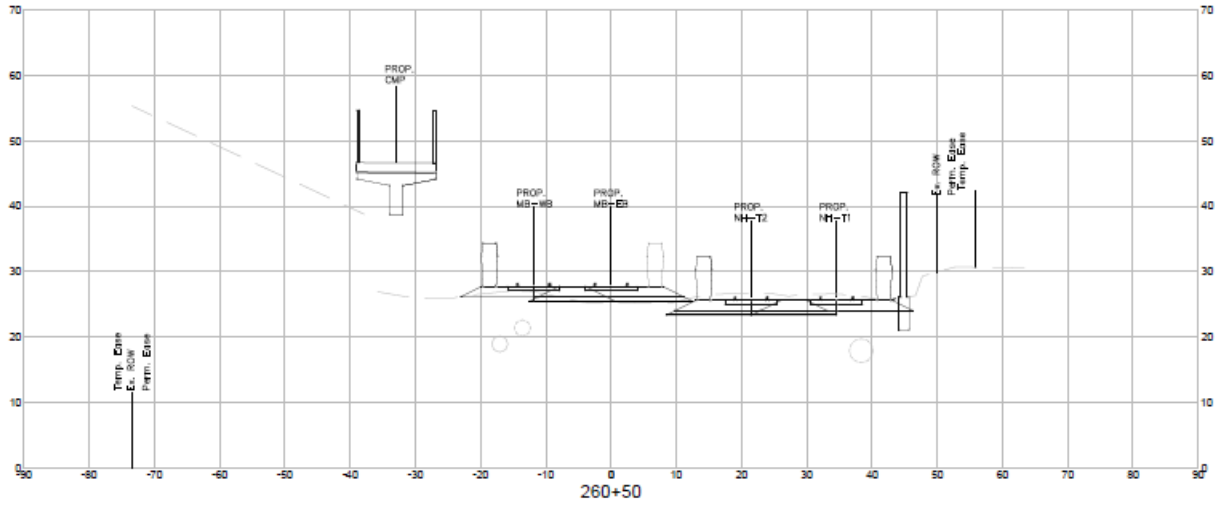

PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
Temp. Ease
Ex. ROW
Perm. Ease
260+50

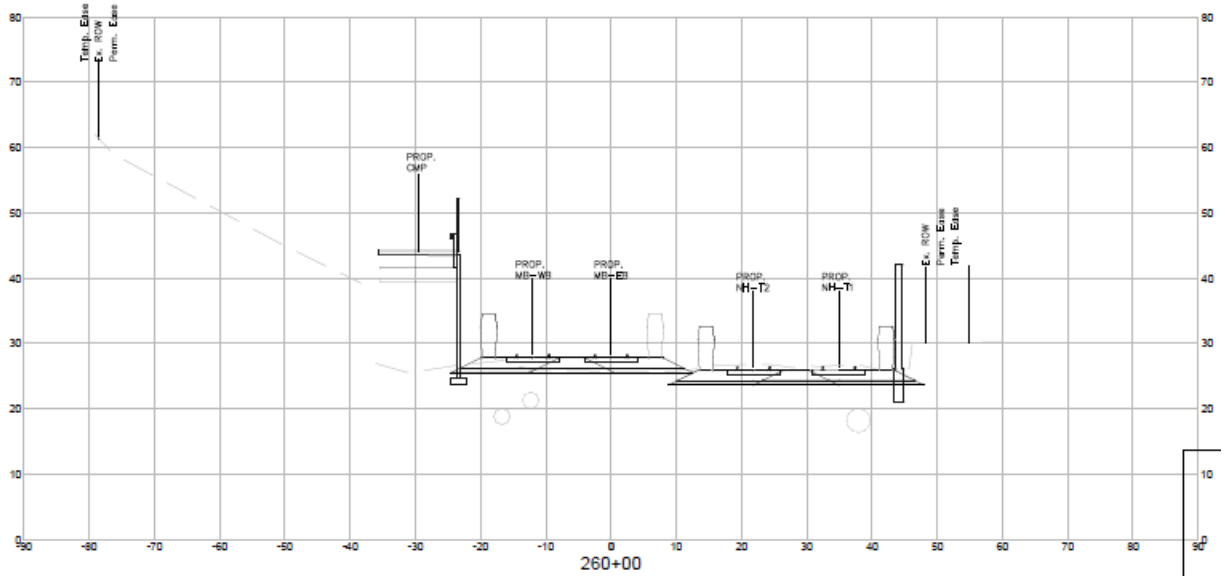

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
260+00

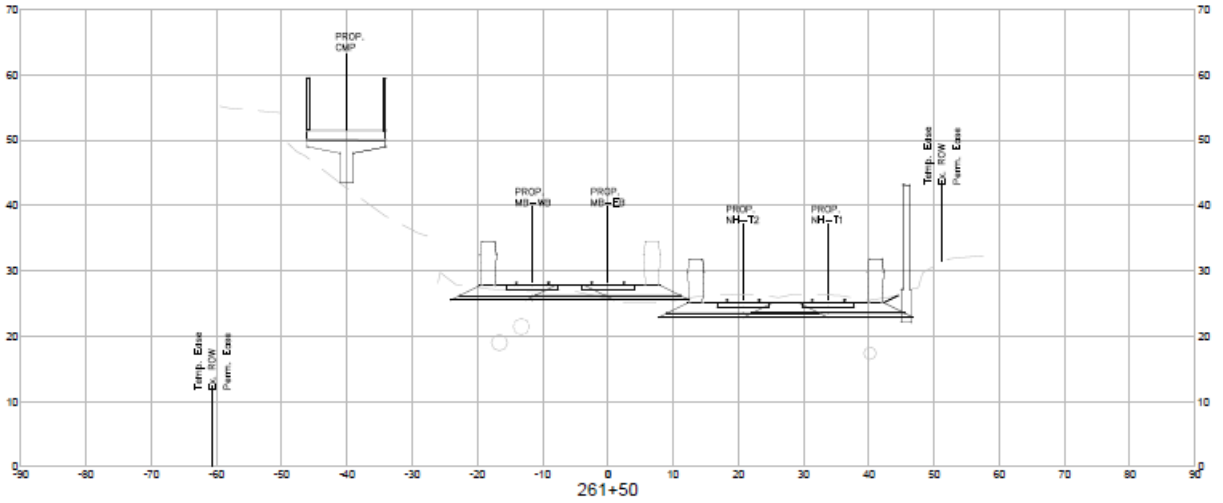

PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
261+50

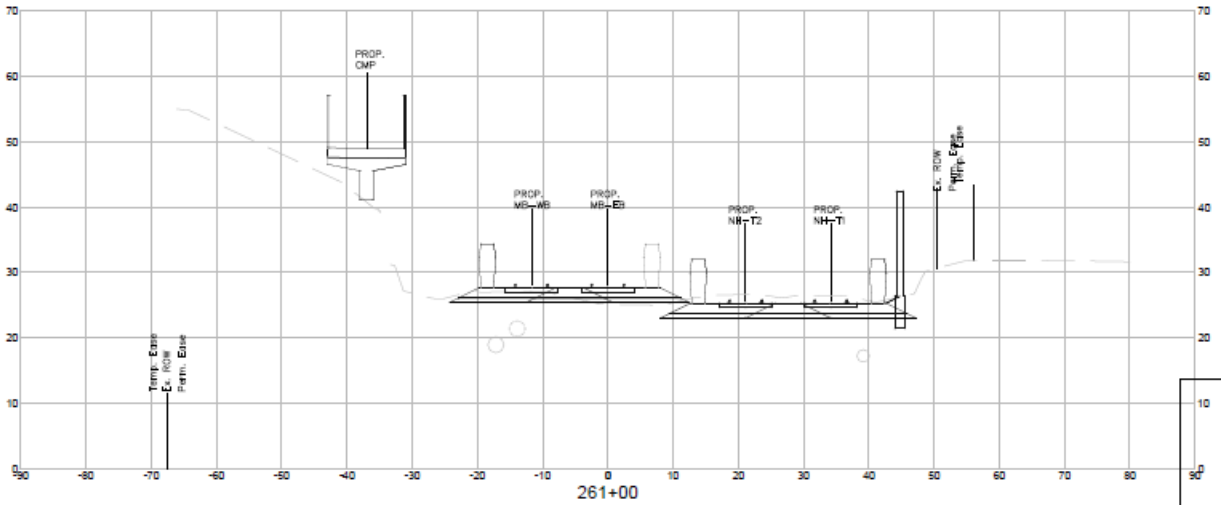

PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
261+00

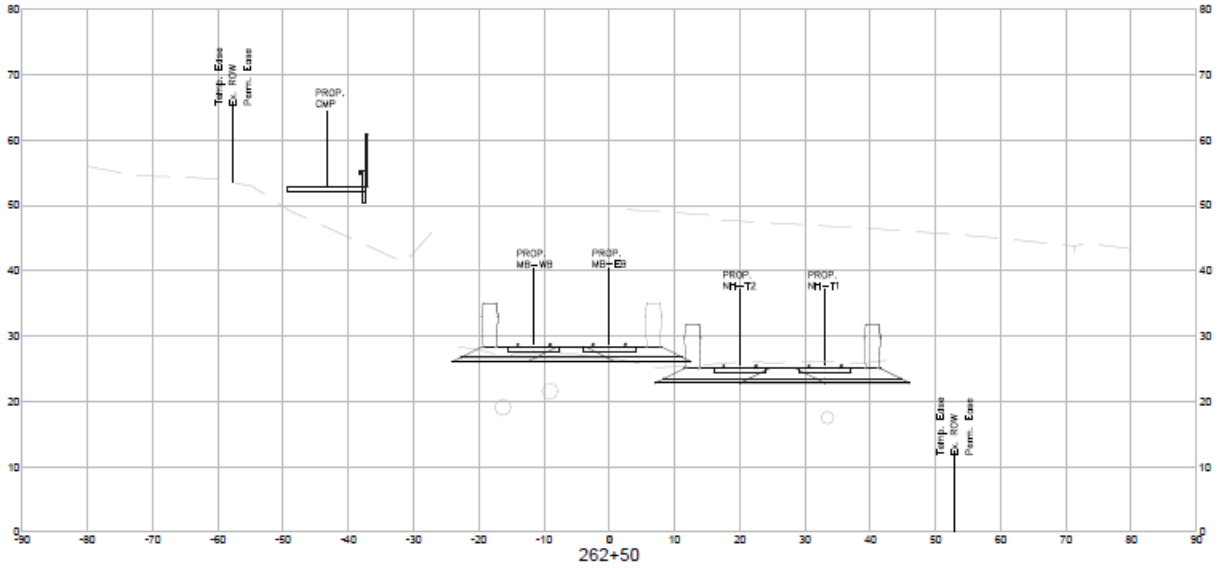

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
262+50

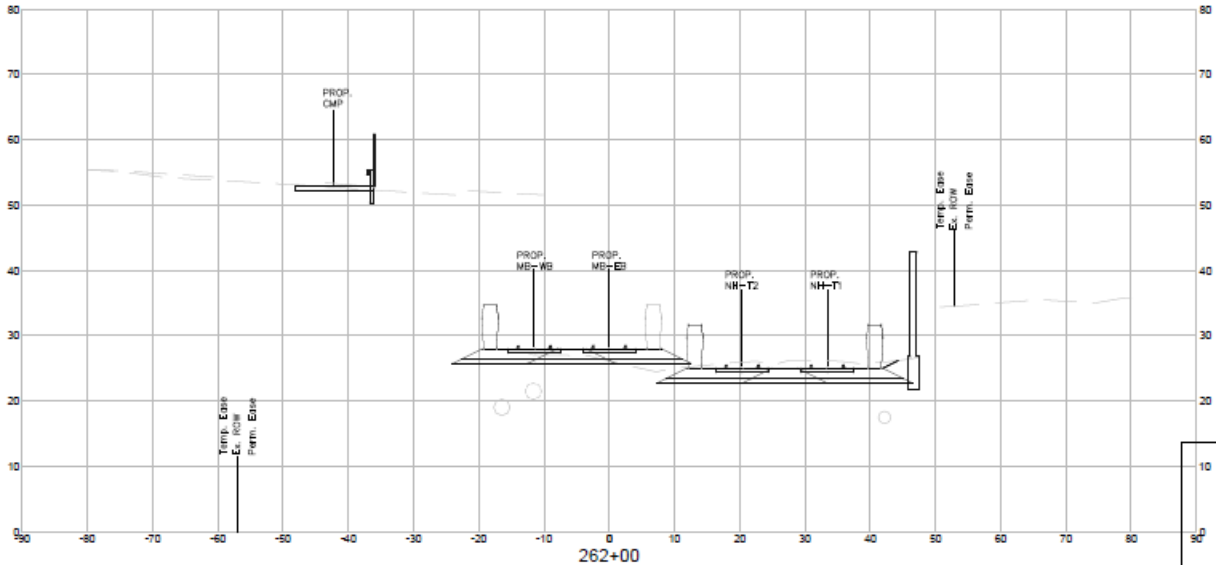

PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
Temp. Ease
Ex. ROW
Perm. Ease
262+00

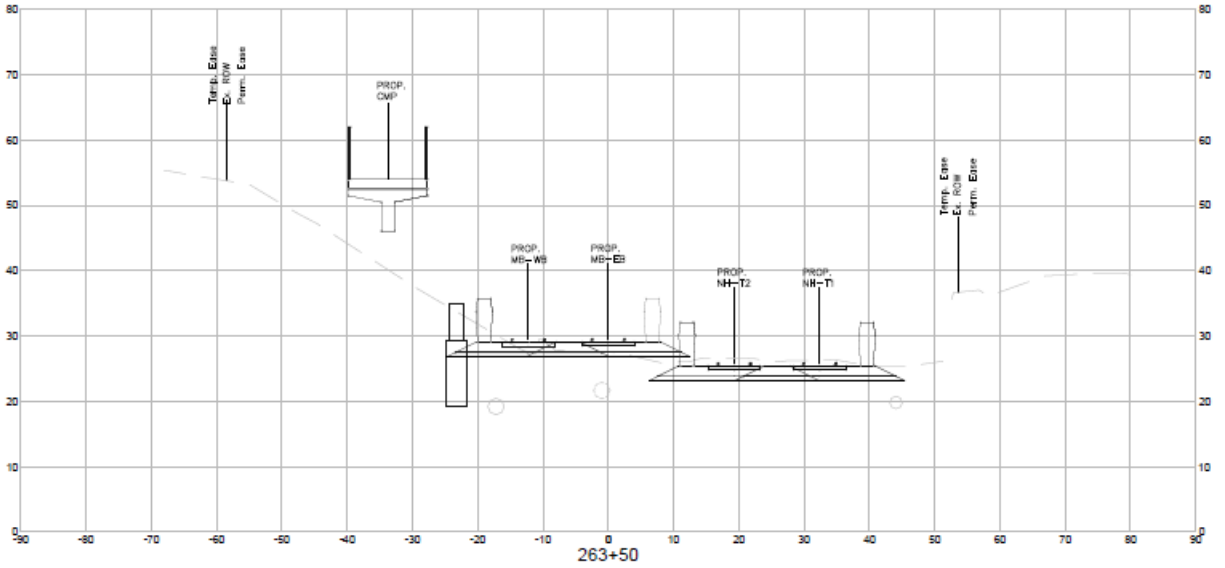

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
263+50

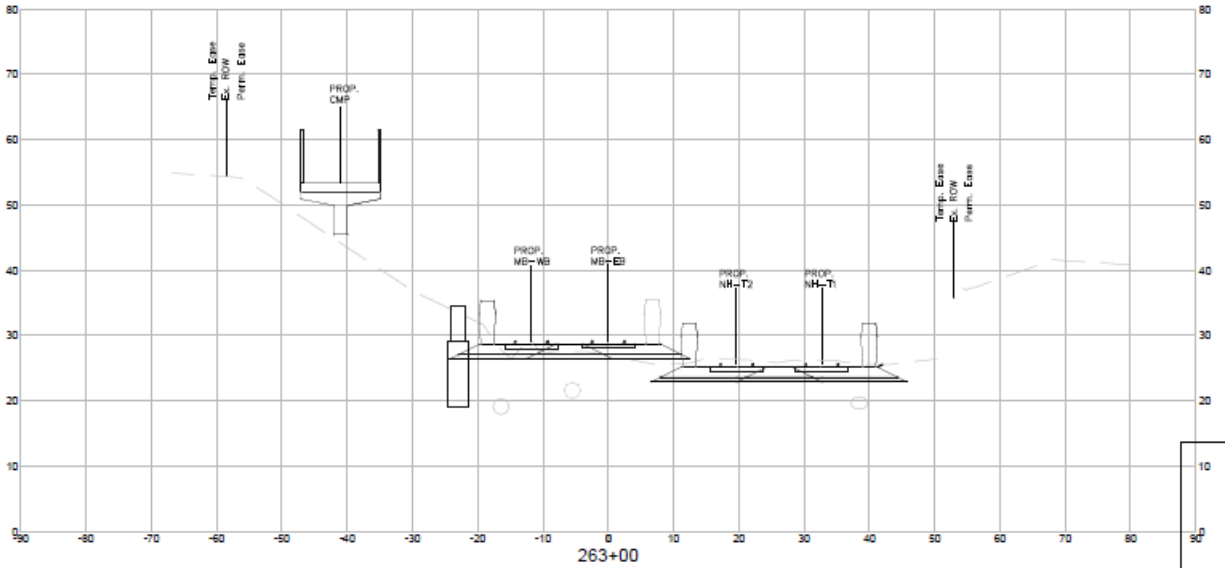

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
263+00

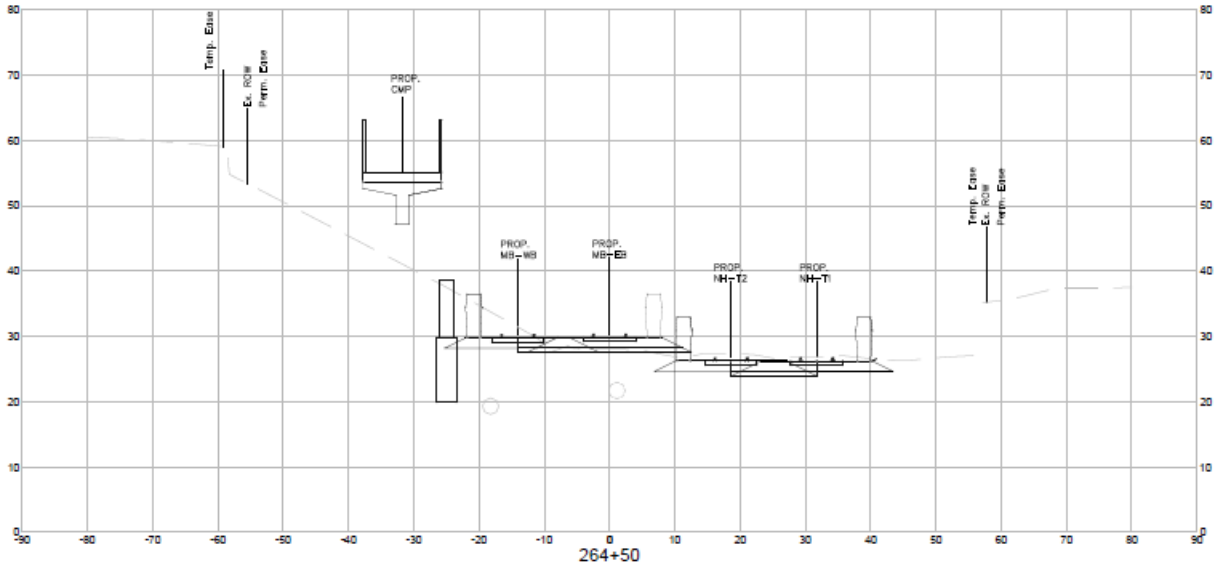

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Temp. Ease
Ex. ROW
Perm. Ease
264+50

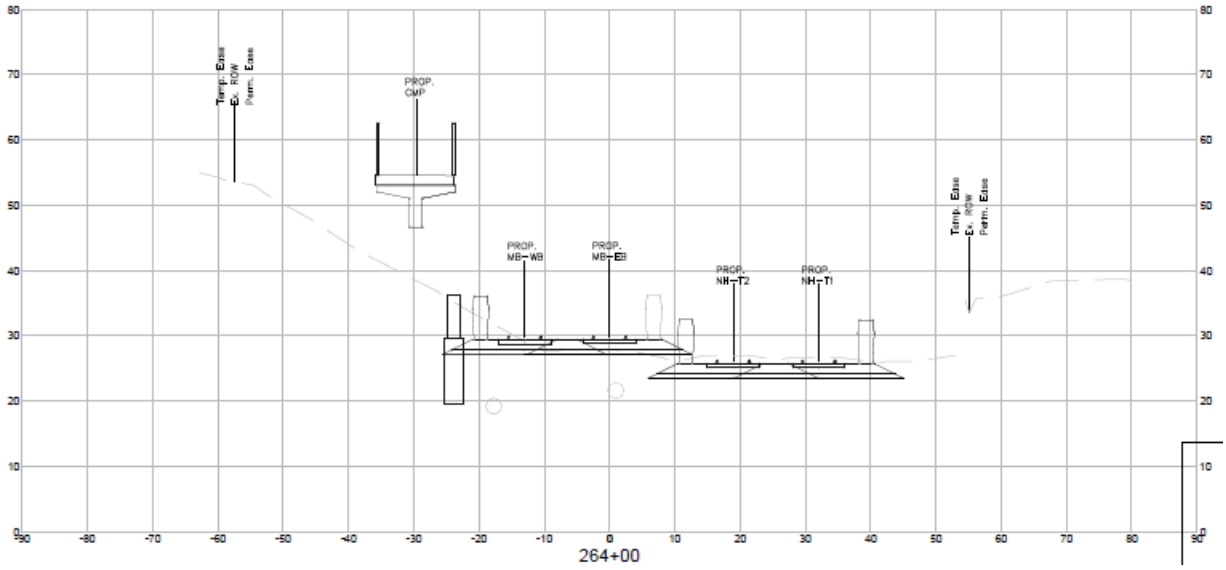

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Temp. Ease
Ex. ROW
Perm. Ease
264+00

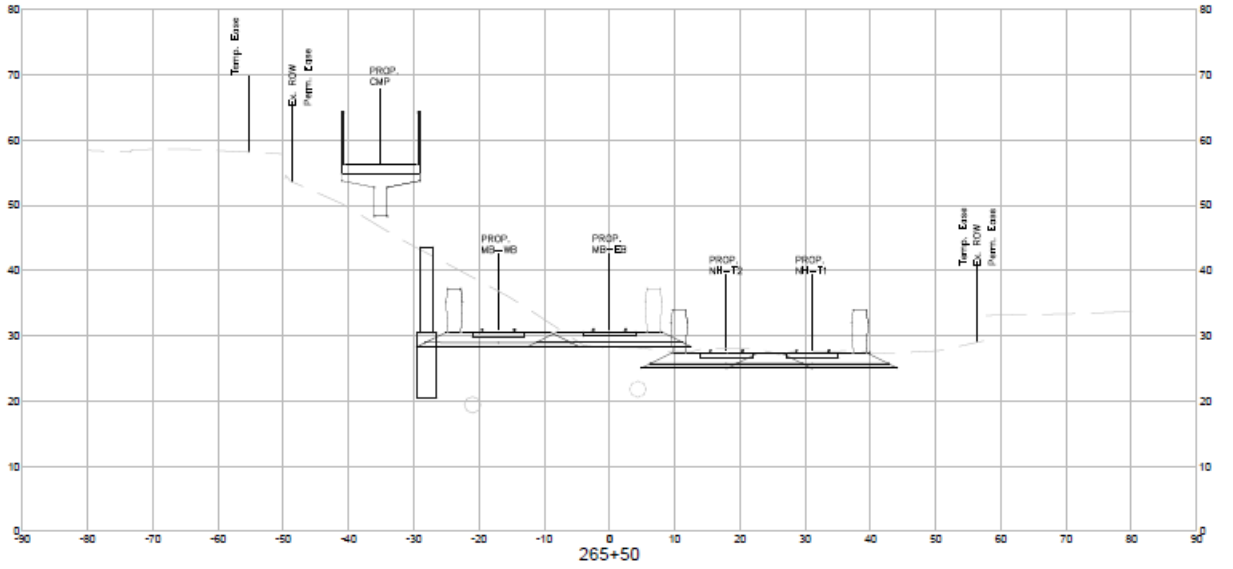

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Temp. Ease
Ex. ROW
Perm. Ease
265+50

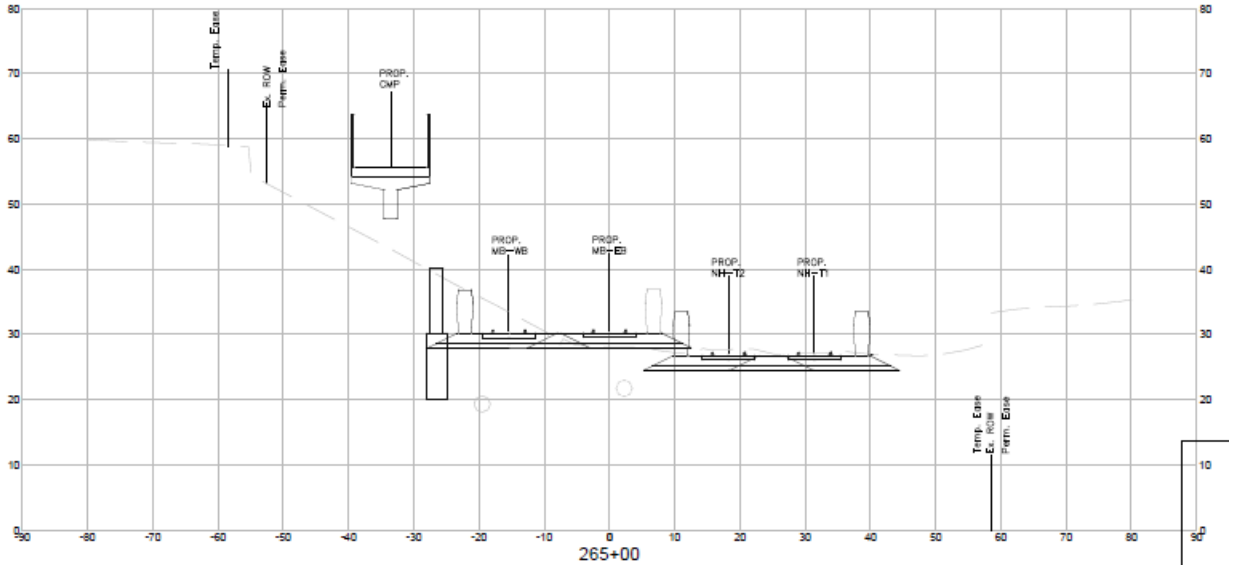

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Temp. Ease
Ex. ROW
Perm. Ease
265+00

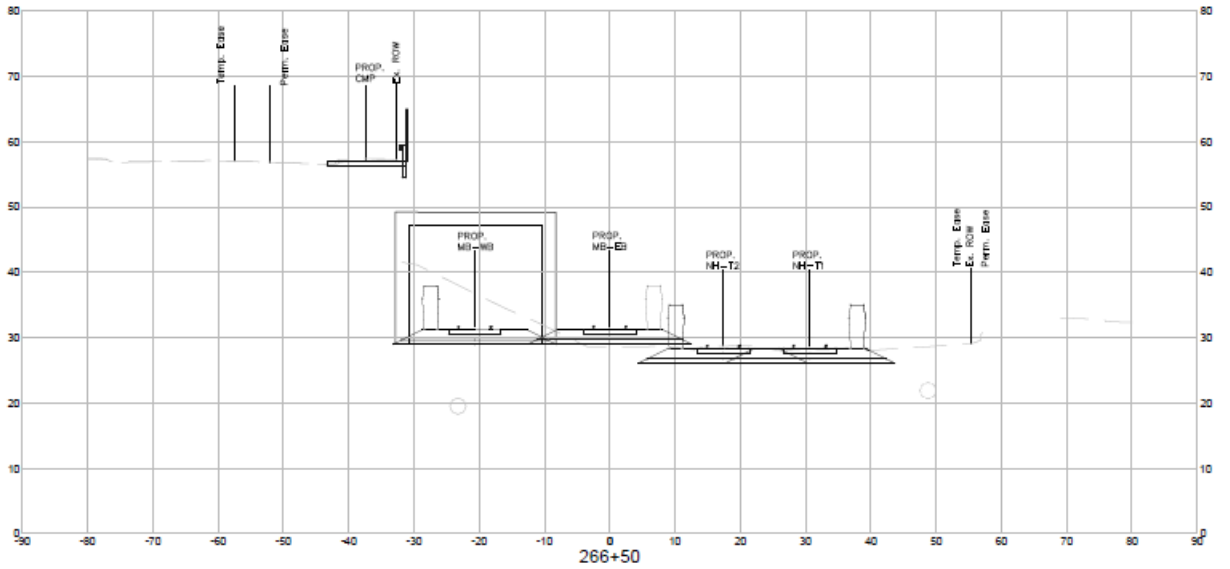

Temp. Ease
Perm. Ease
PROP. CMP
Ex. ROW
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
266+50

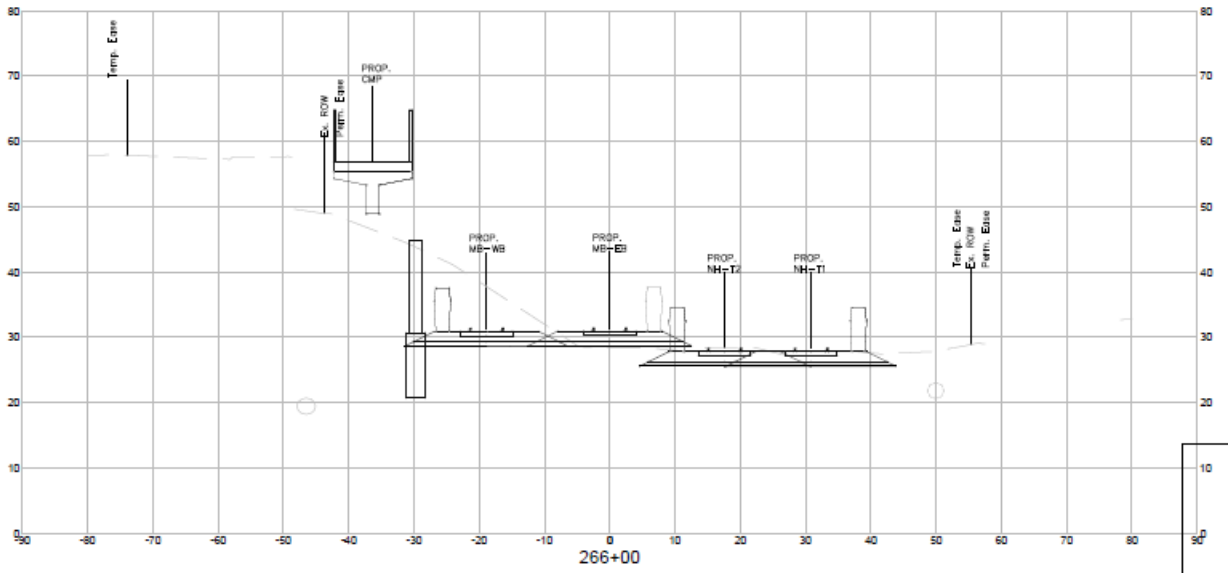

Temp. Ease
PROP. CMP
Ex. ROW
Perm. Ease
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Temp. Ease
Ex. ROW
Perm. Ease
266+00

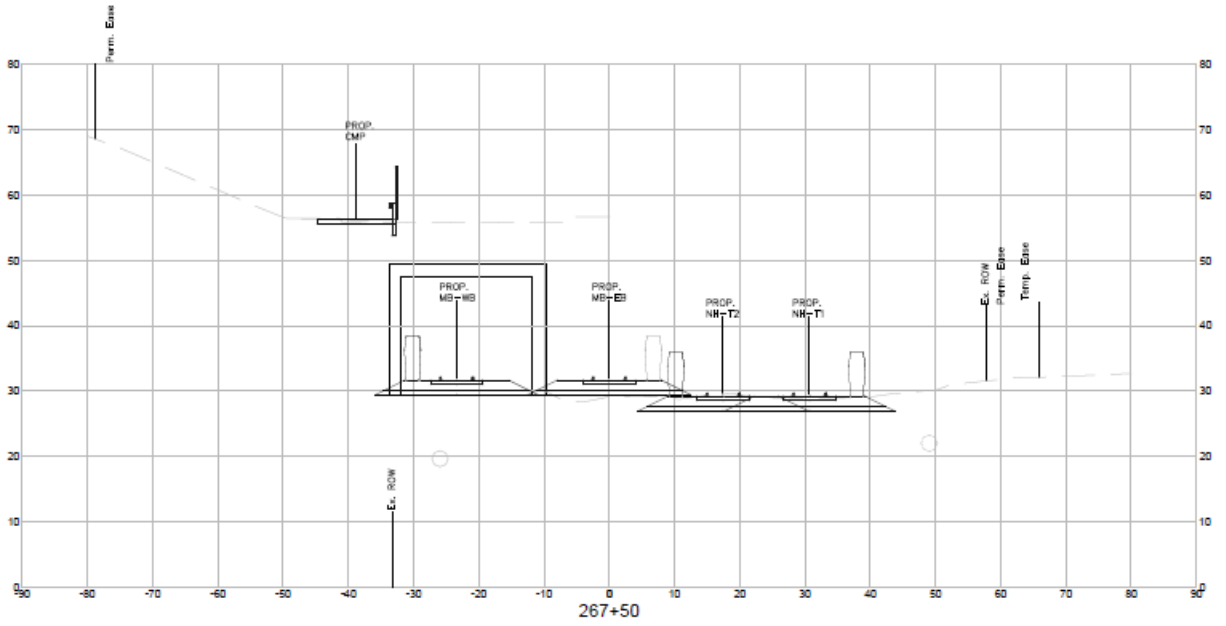

Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Ex. ROW
Perm. Ease
Temp. Ease
Ex. ROW
267+50

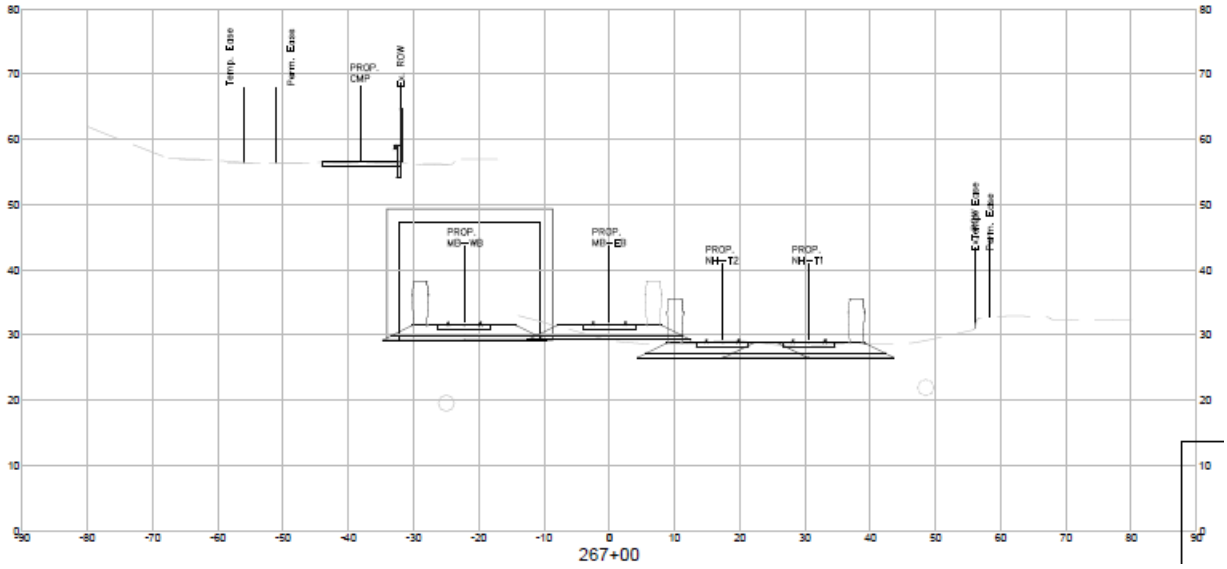

Temp. Ease
Perm. Ease
PROP. CMP
Ex. ROW
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Perm. Ease
267+00

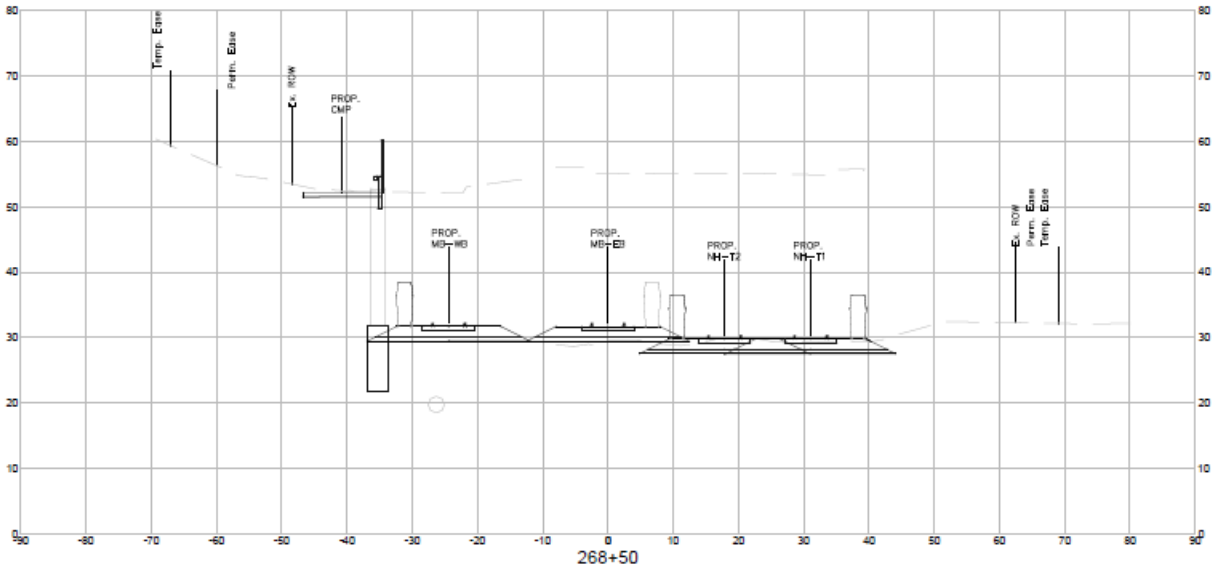

Temp. Ease
Perm. Ease
Ex. ROW
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
268+50

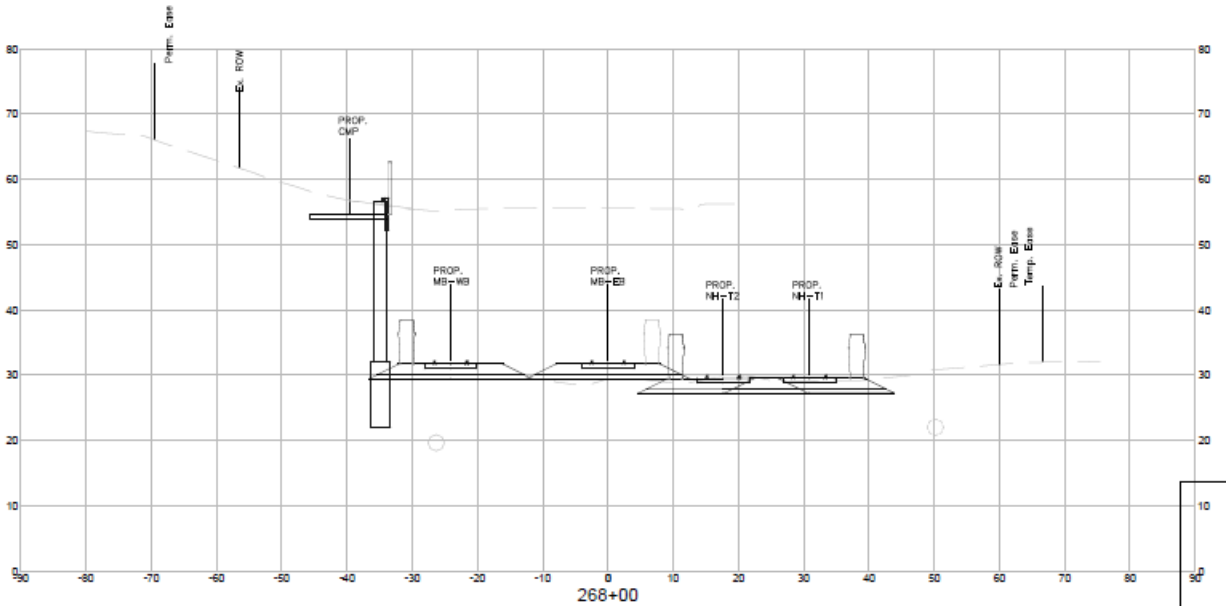

Perm. Ease
Ex. ROW
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
268+00

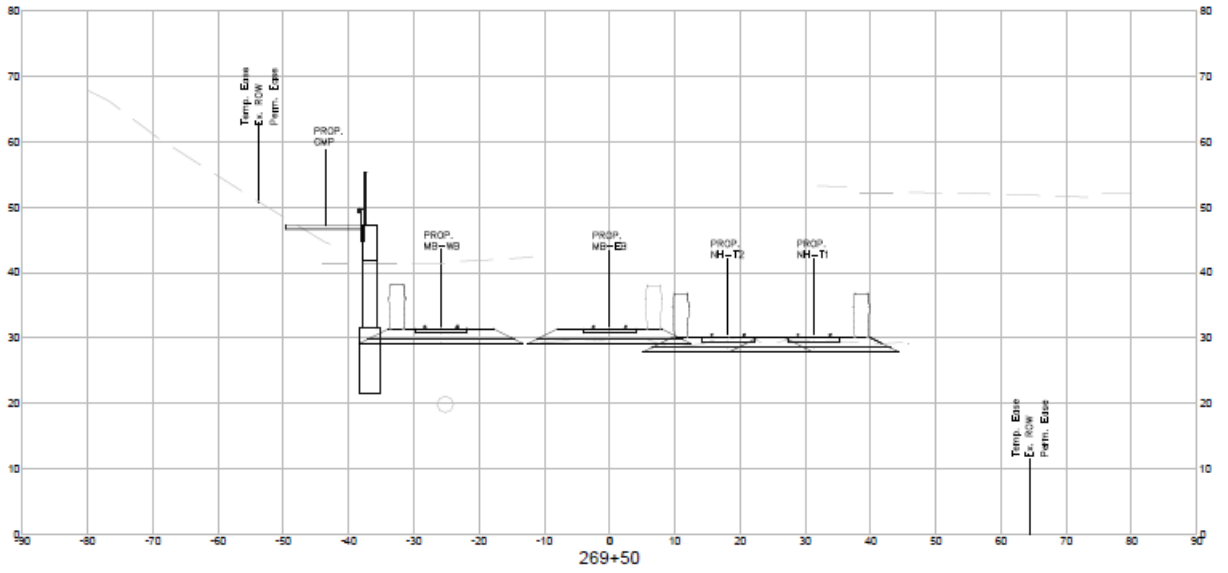

Temp. Ease
Ex. ROW
Perm. Ease
PROP.
CMP
PROP.
MB–WB
PROP.
MB–EB
PROP.
NH–T2
PROP.
NH–T1
Temp. Ease
Ex. ROW
Perm. Ease
269+50

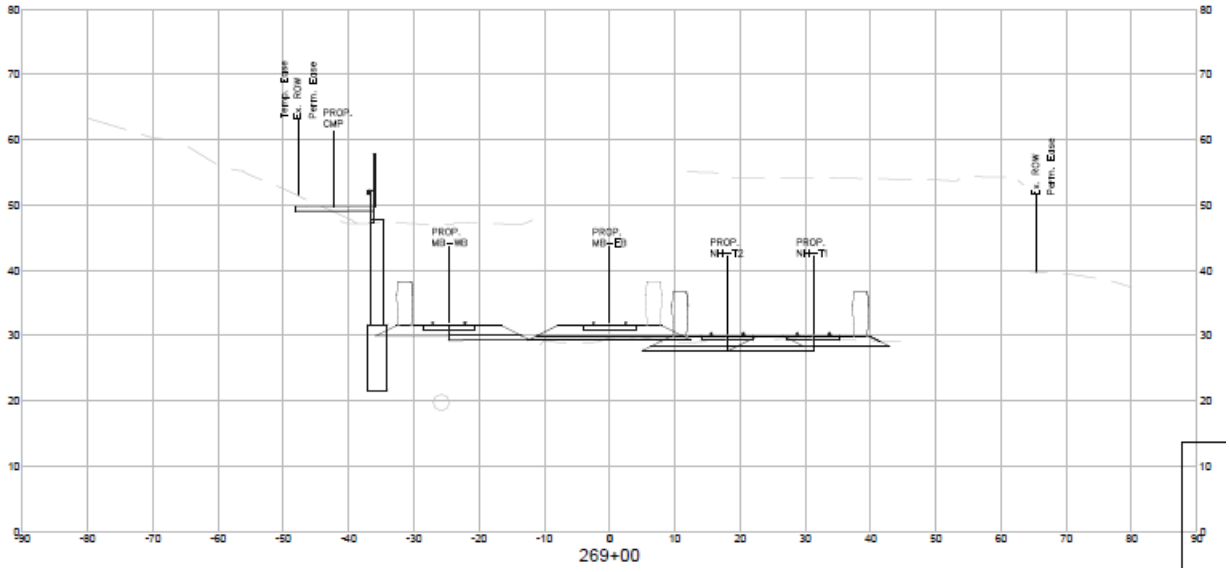

Temp. Ease
Ex. ROW
Perm. Ease
PROP.
CMP
PROP.
MB–WB
PROP.
MB–EB
PROP.
NH–T2
PROP.
NH–T1
Ex. ROW
Perm. Ease
269+00

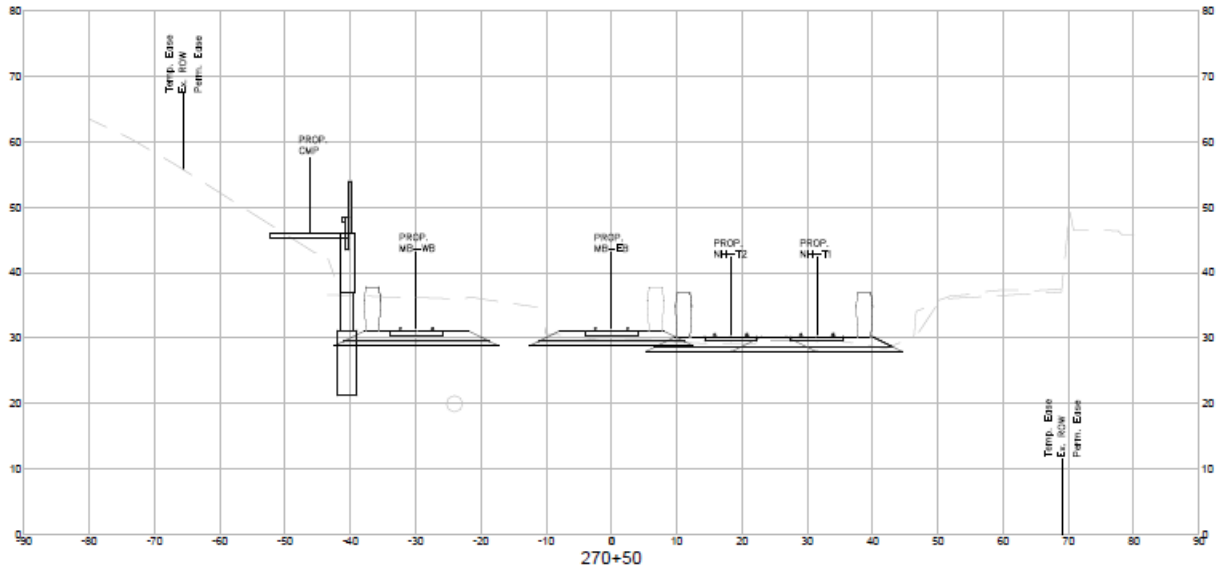

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Temp. Ease
Ex. ROW
Perm. Ease
270+50

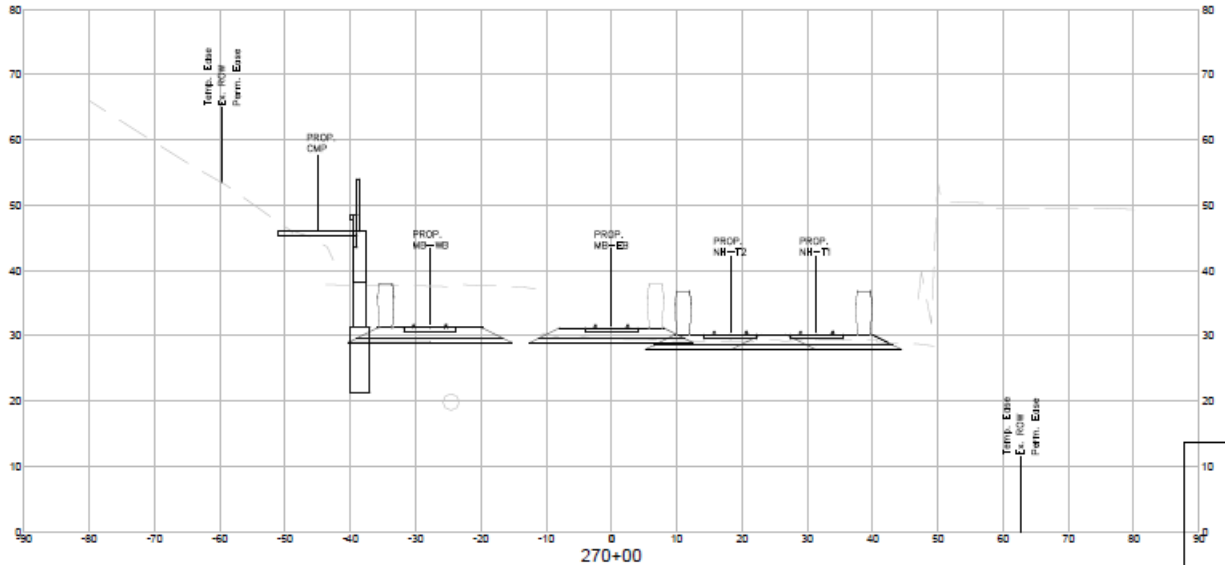

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Temp. Ease
Ex. ROW
Perm. Ease
270+00

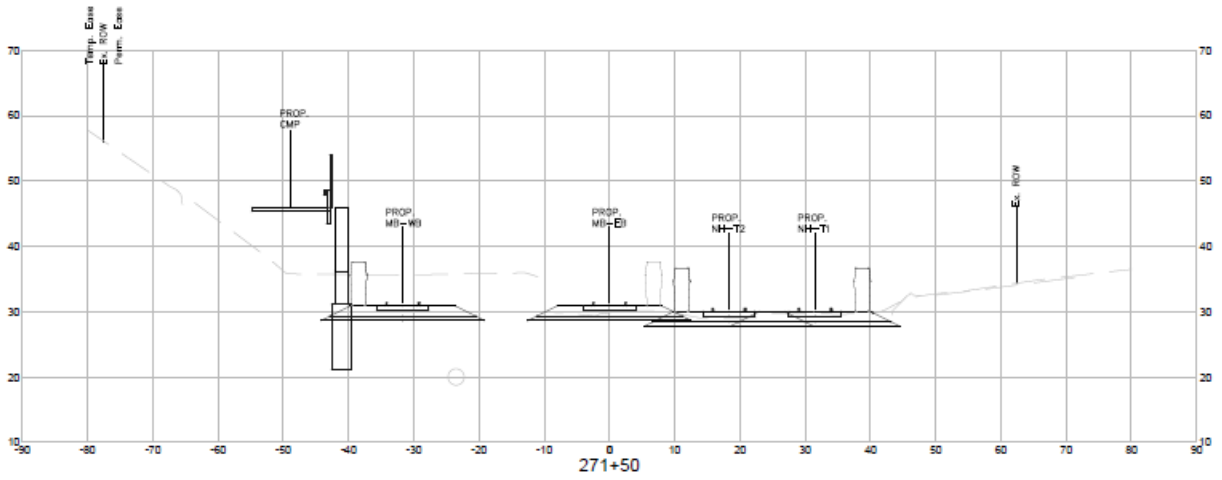

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
Ex. ROW
271+50

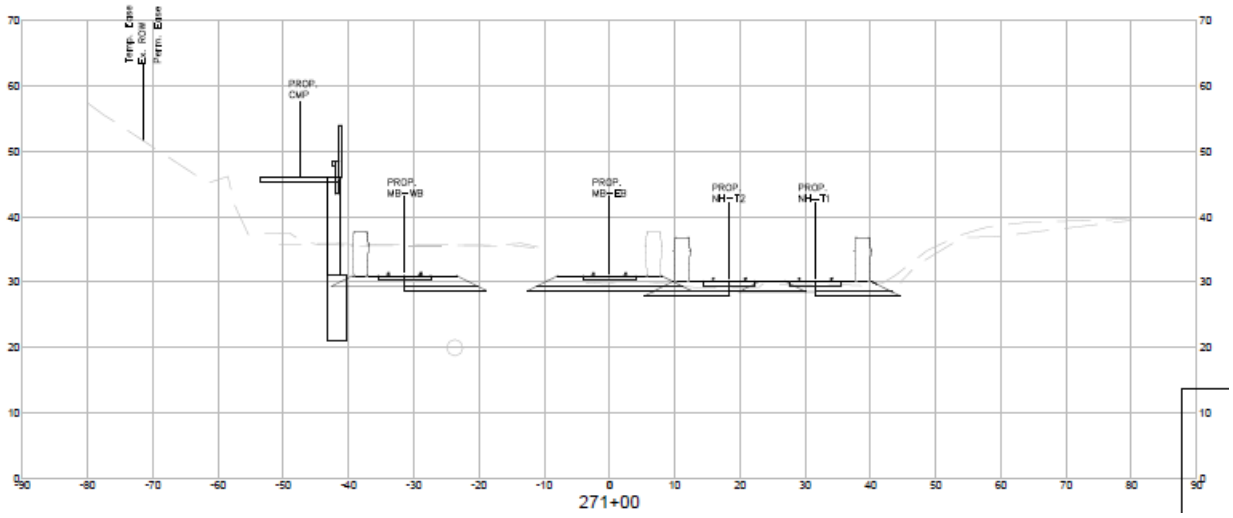

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB–WB
PROP. MB–EB
PROP. NH–T2
PROP. NH–T1
271+00

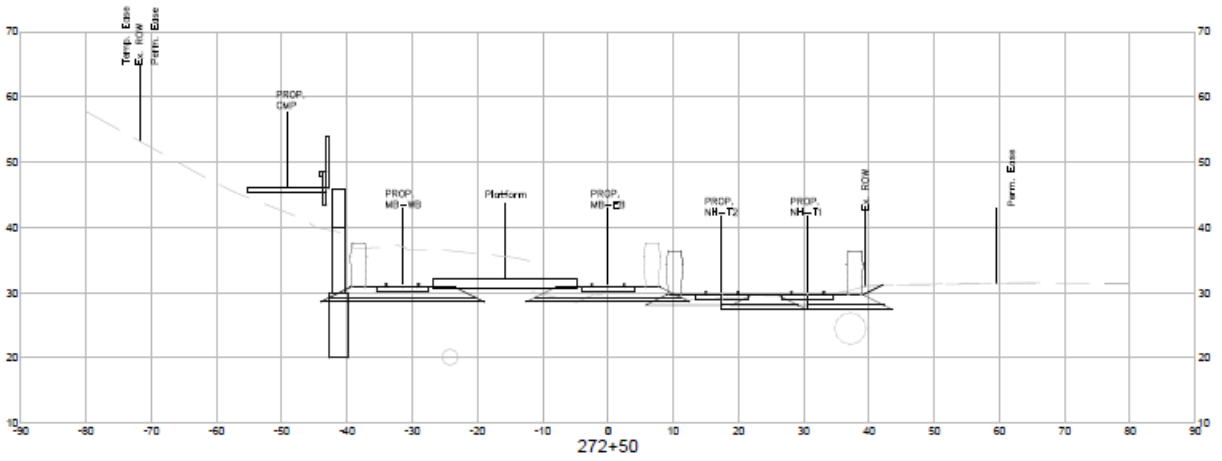

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-MB
Platform
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
272+50

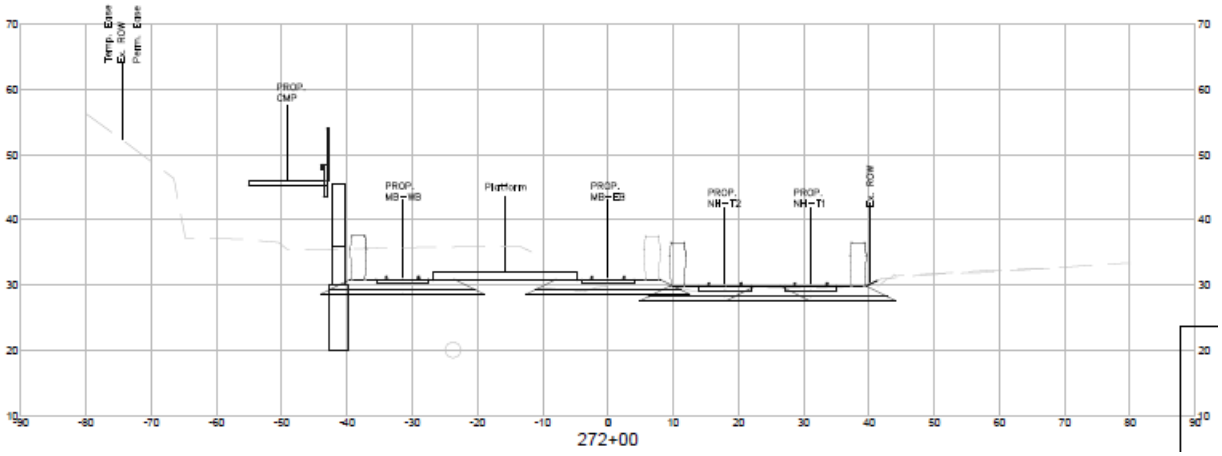

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-MB
Platform
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
272+00

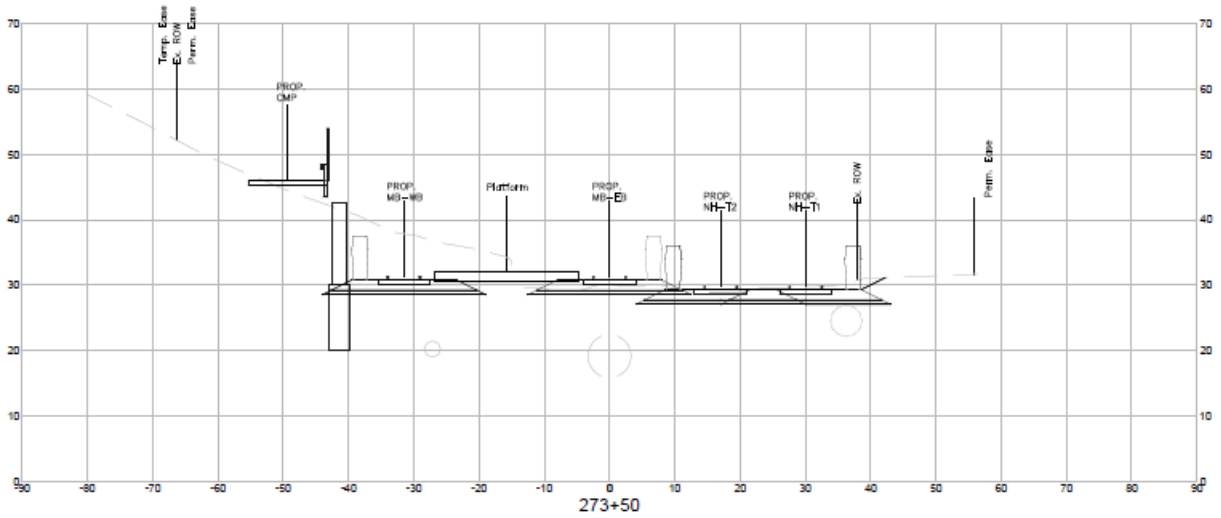

Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-MB
Platform
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
273+50

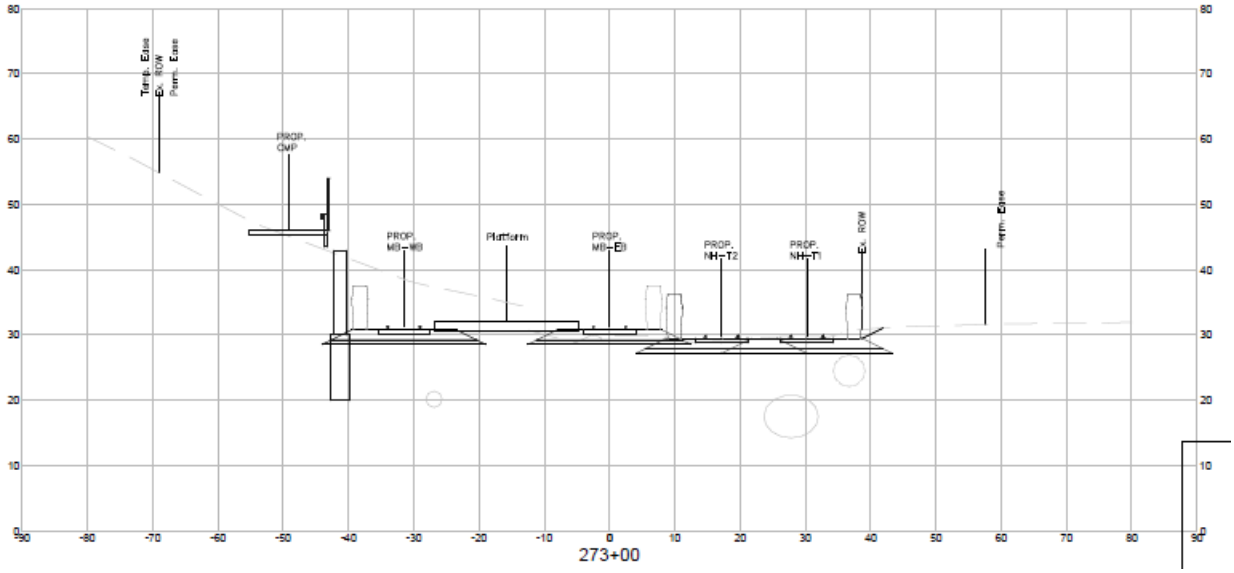
Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-MB
Platform
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
273+00

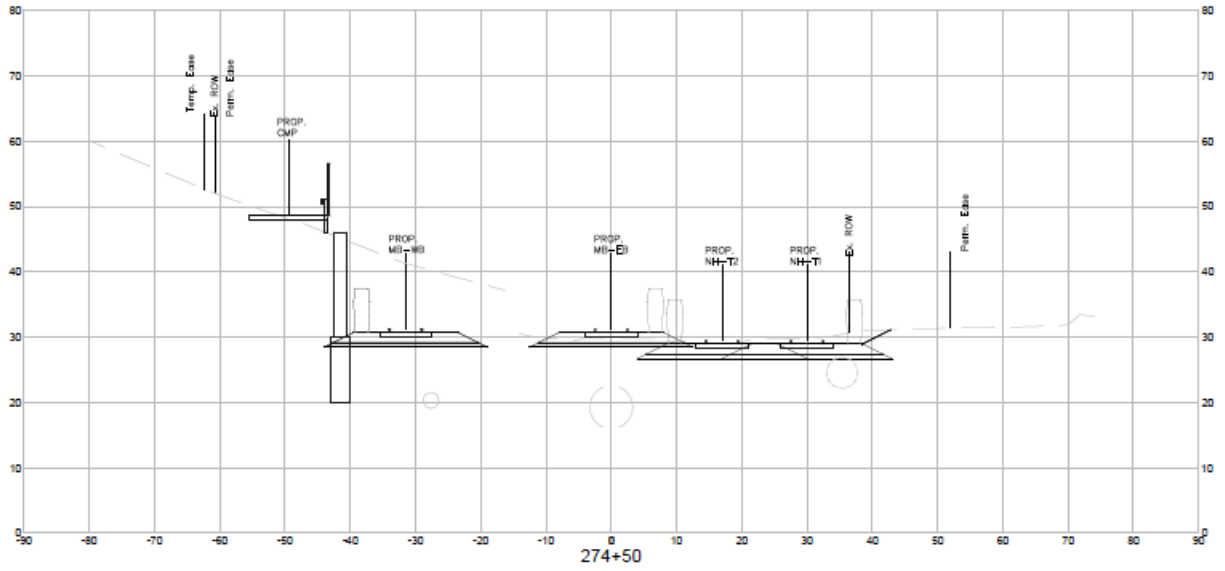
Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
274+50

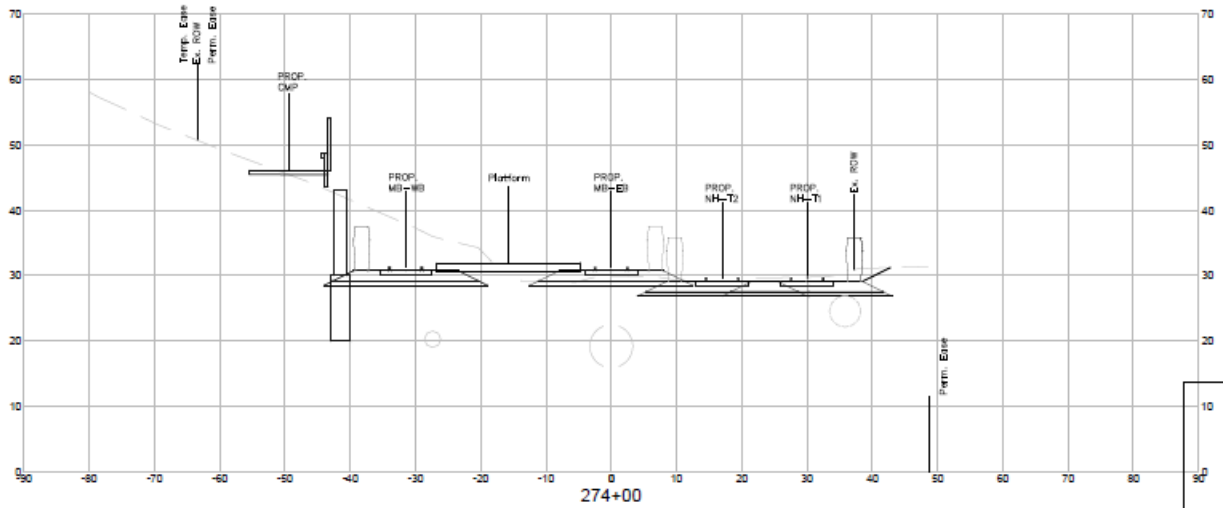
Temp. Ease
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-WB
Platform
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
274+00

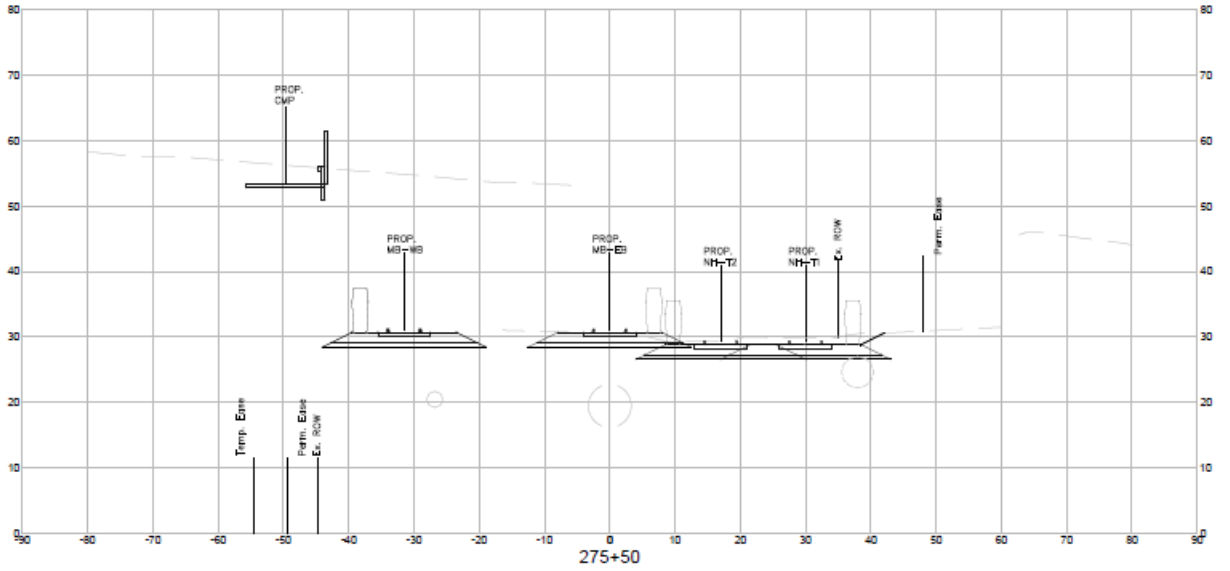
PROP. CMP
PROP. MB-MB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
Temp. Ease
Perm. Ease
Ex. ROW
275+50

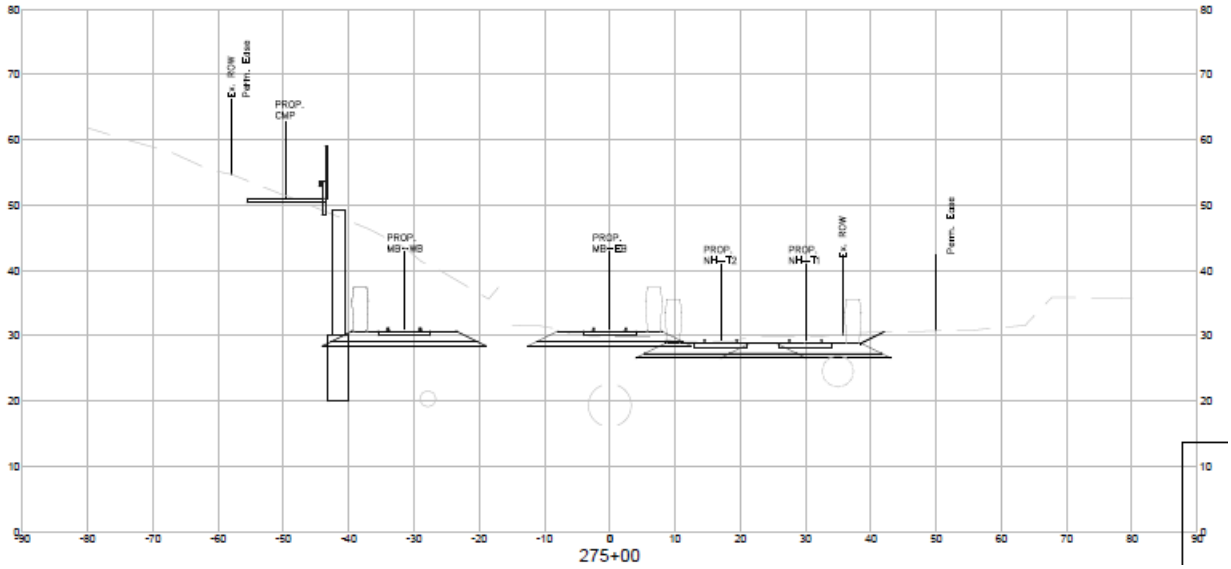
Ex. ROW
Perm. Ease
PROP. CMP
PROP. MB-MB
PROP. MB-EB
PROP. NH-T2
PROP. NH-T1
Ex. ROW
Perm. Ease
275+00

ATC No. 43

ATC No. 43

Preliminary Submission

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

PRELIMINARY

ALTERNATIVE TECHNICAL CONCEPTS

("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

GLX CONSTRUCTORS PRELIMINARY ATC FORM

ATC 43 – REPLACE SUBBALLAST WITH GEOTEXTILE AND GEOGRID REINFORCEMENT – COMMUTER RAIL

Sections A through E below must be completed to submit a Preliminary ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Preliminary ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. General Description

A general description (not to exceed two pages) of the Preliminary ATC, how the ATC will be used on the Project, the proposed location of the ATC, and any other pertinent information that would provide a clear understanding of the potential ATC;

This ATC provides a filter fabric and geogrid reinforcement, and eliminates the subballast along sections of the alignment where subgrade conditions are favorable. The ballast will be 12" thick minimum below tie under rail.

B. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC and an explanation of the nature of the deviations from said requirements;

Volume 2, Exhibit 2B, Project Definition Plans indicate that the track bed shall consist of 12" of ballast over 8" of subballast. This ATC replaces the 8" of subballast with geotextile and geogrid.

C. Benefits

Any potential benefits or implications of incorporating the Preliminary ATC into the Project, including in right-of-way acquisitions, rail operations, and routine or capital maintenance, and other Project risks;

This ATC will provide the following benefits:

- Limit ballast settlement and lateral creep
- Reduce excavation and export of potentially contaminated soils
- Reduce trucking impacts to local streets
- Expedite Installation
- Increase service life
- Reduce ballast maintenance

D. Conceptual Drawings

Any conceptual drawings (if applicable) of the configuration of the potential ATC or other appropriate descriptive information that provides an understanding of the Preliminary ATC; and


Please refer to Figure ATC-43-1, "Proposed Track Bed Section" for proposed track bed section details. Please refer to Figure ATC-43-1, "MBTA Greenbush Line Construction", which shows the track bed during MBTA Greenbush Line construction.

E. Cost Estimate and Schedule Impacts

An order of magnitude cost estimate and a preliminary analysis of schedule impacts associated with the Preliminary ATC.

This ATC will result in an estimated cost saving of $600,000. Our preliminary analysis indicates no impact to schedule milestones.

Figure ATC-43-1: Proposed Track Bed Section

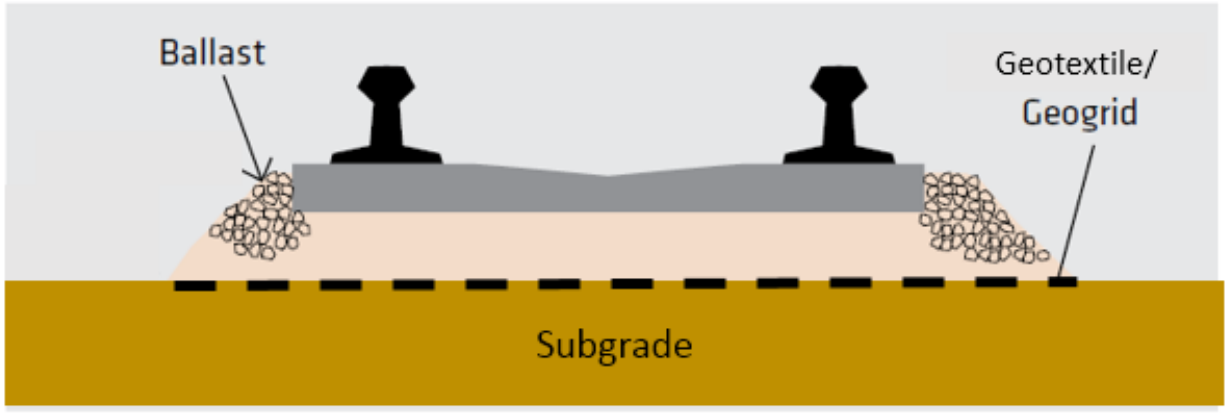

(Ballast min. 12")

Figure ATC-43-2: MBTA Greenbush Line Construction



ATC No. 43

MBTA Acceptance of Preliminary Submission

Massachusetts Bay Transportation Authority

GLX Procurement

ATC Review

ATC Information:

Type of ATC: Preliminary
Title: GLX Constructors ATC 11 - Replace Subballast with Geotextile and Geogrid Reinforcement - Commuter Rail
Proposer Company: GLX Constructors

Final Disposition:

Sent on behalf of Yvelisse Duvergé. The Preliminary ATC can be formally submitted for MBTA review as an ATC Submittal, subject to further refinement and submission of supporting information pursuant to Section 3.3.1 of the Instructions to Proposers.

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

PRELIMINARY

ALTERNATIVE TECHNICAL CONCEPTS

("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

GLX CONSTRUCTORS PRELIMINARY ATC FORM

ATC 43 – REPLACE SUBBALLAST WITH GEOTEXTILE AND GEOGRID REINFORCEMENT – COMMUTER RAIL

Sections A through E below must be completed to submit a Preliminary ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Preliminary ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. General Description

A general description (not to exceed two pages) of the Preliminary ATC, how the ATC will be used on the Project, the proposed location of the ATC, and any other pertinent information that would provide a clear understanding of the potential ATC;

This ATC provides a filter fabric and geogrid reinforcement, and eliminates the subballast along sections of the alignment where subgrade conditions are favorable. The ballast will be 12" thick minimum below tie under rail.

B. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC and an explanation of the nature of the deviations from said requirements;

Volume 2, Exhibit 2B, Project Definition Plans indicate that the track bed shall consist of 12" of ballast over 8" of subballast. This ATC replaces the 8" of subballast with geotextile and geogrid.

C. Benefits

Any potential benefits or implications of incorporating the Preliminary ATC into the Project, including in right-of-way acquisitions, rail operations, and routine or capital maintenance, and other Project risks;

This ATC will provide the following benefits:

- Limit ballast settlement and lateral creep
- Reduce excavation and export of potentially contaminated soils
- Reduce trucking impacts to local streets
- Expedite Installation
- Increase service life
- Reduce ballast maintenance

D. Conceptual Drawings

Any conceptual drawings (if applicable) of the configuration of the potential ATC or other appropriate descriptive information that provides an understanding of the Preliminary ATC; and


Please refer to Figure ATC-43-1, "Proposed Track Bed Section" for proposed track bed section details. Please refer to Figure ATC-43-1, "MBTA Greenbush Line Construction", which shows the track bed during MBTA Greenbush Line construction.

E. Cost Estimate and Schedule Impacts

An order of magnitude cost estimate and a preliminary analysis of schedule impacts associated with the Preliminary ATC.

This ATC will result in an estimated cost saving of $600,000. Our preliminary analysis indicates no impact to schedule milestones.

Figure ATC-43-1: Proposed Track Bed Section

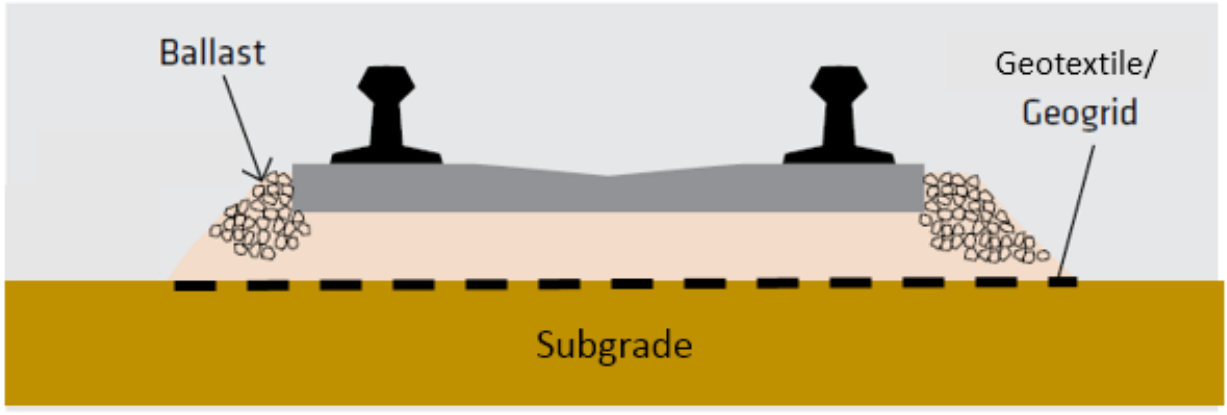

(Ballast min. 12")

Figure ATC-43-2: MBTA Greenbush Line Construction



ATC No. 43

Formal Submission

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

FORMAL

ALTERNATIVE TECHNICAL CONCEPTS ("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

JULY 11, 2017 (Final Round)

GLX CONSTRUCTORS FORMAL ATC FORM

REPLACE SUBBALLAST WITH GEOTEXTILE AND GEOGRID REINFORCEMENT – COMMUTER RAIL

Sections A though P below shall be completed to submit a Formal ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Formal ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. ATC Number

A sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.);

ATC 43

MBTA Preliminary ATC File Number: ATC-000017 – GLX Constructors ATC 11

B. Description and Conceptual Drawings

A description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information;

This ATC provides a filter fabric and geogrid reinforcement, and eliminates the subballast along sections of the alignment where subgrade conditions are favorable. The ballast will be 12" thick minimum below tie under rail. Please refer to Figure ATC-43-1, "Proposed Track Bed Section" for proposed track bed section details. Please refer to Figure ATC-43-1, "MBTA Greenbush Line Construction", which shows the track bed during MBTA Greenbush Line construction.

C. Locations and How Used

The locations where, and an explanation of how, the ATC will be used on the Project;

This ATC will be used where subgrade conditions are favorable when commuter rail track is installed as part of the project.

D. Changes in Rail or Transit Operations

Any changes in rail or transit operations requirements associated with the ATC, including ease of operations;

No changes in operations are anticipated as a result of this ATC.

E. Changes in Routine or Capital Maintenance

Any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance;

This ATC will result in reduced ballast maintenance.

F. Changes in Anticipated Service Life

Any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC;

The separation of fines in the subgrade from the ballast and structural support of the geogrid should permit longer service life than the track bed shown by the Project Definition Plans.

G. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations;

Volume 2, Exhibit 2B, Project Definition Plans indicate that the track bed shall consist of 12" of ballast over 8" of subballast. This ATC replaces the 8" of subballast with geotextile and geogrid.

H. Justification of Use

An analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed;

This ATC will increase the service life of the track bed section by limiting ballast settlement and lateral creep. This will reduce ballast maintenance. During construction, this ATC reduces the excavation and export of potentially contaminated soils. This results in less trucking on local streets. The time required to install this track bed section is shorter than the specified section.

I. Preliminary Analysis and Quantitative Discussion

A preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation;

MBTA Contract No. E22CN0 Formal ATC 37A GLX DB Project Page 4 June 30, 2017 No impacts on rail or transit operations are anticipated as a result of this ATC.

J. Impacts on Third Parties

A description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC. Proposers are advised that they may (i) be solely responsible for the cost and schedule impacts of the acquisition of any such Additional Properties, including the cost thereof and obtaining any necessary environmental approvals; (ii) not be entitled to any change order for time or money as a result of site conditions (i.e., hazardous materials, differing site conditions, geotechnical issues, or utilities) on such Additional Properties; and (iii) not be entitled to any change order for time or money as a result of any delay, inability, or cost associated with the acquisition of such Additional Properties;

No impacts to third parties are anticipated as a result of this ATC.

K. History of Use and References

A description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements;

This ATC concept was successfully used as an equal replacement for the specified track bed section on MBTA's Greenbush Line.

Paul Hadley, MBTA, 617.512.5999, phadley@MBTA.com

L. Additional Risks

A description of added risks to the MBTA or third parties associated with implementing the ATC;

No additional risks to the MBTA or to third parties are anticipated as a result of this ATC.

M. Additional Costs

An estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC;

Additional costs to the MBTA, DB Entity and third parties will not result from this ATC. One of the primary purposes of this ATC is cost reduction.

N. Estimated Price Adjustment

An estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented;

This ATC will result in an estimated savings of $600,000. The ATC pricing as shown in this proposal is an all inclusive price. All price deducts and/or adds have been considered, and the resulting price adjustment is offered as shown.

O. Schedule Adjustment

An estimate of the schedule adjustment, should the ATC be approved and implemented; and


This ATC does not require any schedule adjustment.

P. Analysis of Quality, Performance, and Reliability

An analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents.

This ATC will provide a better quality, performance and reliability than the specified track bed section because the separation of fines in the subgrade from the ballast and structural support of the geogrid should permit longer service life. The longer service life will allow for less maintenance and higher reliability.

Figure ATC-43-1: Proposed Track Bed Section

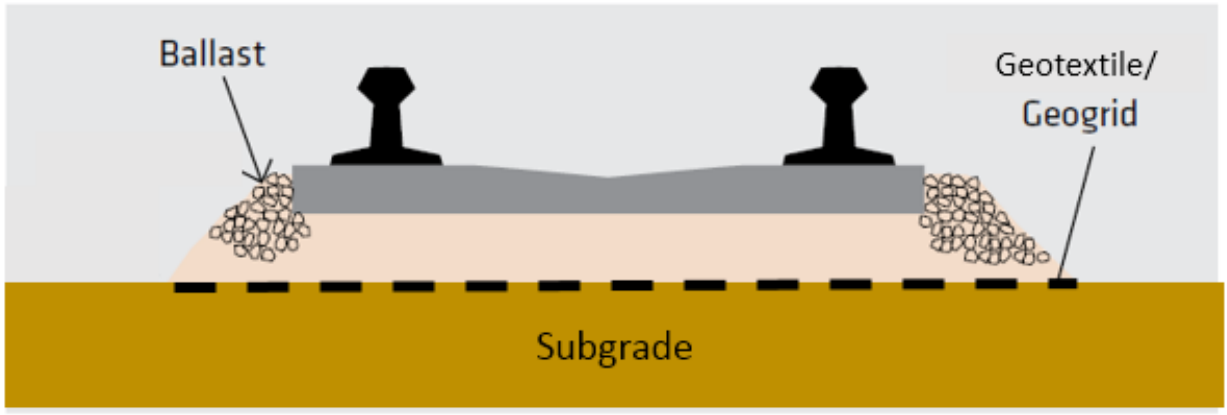

(Ballast min. 12")

Figure ATC-43-2: MBTA Greenbush Line Construction



ATC No. 43

MBTA Acceptance of Formal Submission

ATC Information:

Type of ATC: Formal
Title: GLX Constructors ATC 09 - Replace Subballast with Geotextile & Geogrid Reinforcement - Commuter Rail
Proposer Company: GLX Constructors

Final Disposition:

Sent on behalf of Yvelisse Duvergé. The ATC Submittal is acceptable for inclusion in the Proposal.

COVER SHEET

GLX CONSTRUCTORS

MBTA CONTRACT NO. E22CN07

GREEN LINE EXTENSION DESIGN BUILD PROJECT

CONFIDENTIAL ATCs

FORMAL

ALTERNATIVE TECHNICAL CONCEPTS ("ATCs")

JUNE 9, 2017 (First Round)

JUNE 22, 2017 (Second Round)

JULY 11, 2017 (Final Round)

GLX CONSTRUCTORS FORMAL ATC FORM

REPLACE SUBBALLAST WITH GEOTEXTILE AND GEOGRID REINFORCEMENT – COMMUTER RAIL

Sections A though P below shall be completed to submit a Formal ATC for the Green Line Extension Design Build Project as specified in Section 3.2.1 of the Instructions to Proposers. This Formal ATC must be submitted to the MBTA's Designated Representative as specified in Section 2.4.1 of the Instructions to Proposers via the Project Management Information System.

A. ATC Number

A sequential ATC number identifying the Proposer and the ATC number. (Multi-part or multi-option ATCs shall be submitted as separate individual ATCs with unique sequential numbers.);

ATC 43

MBTA Preliminary ATC File Number: ATC-000017 – GLX Constructors ATC 11

B. Description and Conceptual Drawings

A description and conceptual drawings of the configuration of the ATC or other appropriate descriptive information;

This ATC provides a filter fabric and geogrid reinforcement, and eliminates the subballast along sections of the alignment where subgrade conditions are favorable. The ballast will be 12" thick minimum below tie under rail. Please refer to Figure ATC-43-1, "Proposed Track Bed Section" for proposed track bed section details. Please refer to Figure ATC-43-1, "MBTA Greenbush Line Construction", which shows the track bed during MBTA Greenbush Line construction.

C. Locations and How Used

The locations where, and an explanation of how, the ATC will be used on the Project;

This ATC will be used where subgrade conditions are favorable when commuter rail track is installed as part of the project.

D. Changes in Rail or Transit Operations

Any changes in rail or transit operations requirements associated with the ATC, including ease of operations;

No changes in operations are anticipated as a result of this ATC.

E. Changes in Routine or Capital Maintenance

Any changes in routine or capital maintenance requirements associated with the ATC, including ease of maintenance;

This ATC will result in reduced ballast maintenance.

F. Changes in Anticipated Service Life

Any changes in the anticipated service life of the item(s) comprising the ATC or affected by the ATC;

The separation of fines in the subgrade from the ballast and structural support of the geogrid should permit longer service life than the track bed shown by the Project Definition Plans.

G. References to Contract Documents

References to requirements of the Contract Documents that are inconsistent with the proposed ATC, an explanation of the nature of the deviations from said requirements, and a request for approval of such deviations;

Volume 2, Exhibit 2B, Project Definition Plans indicate that the track bed shall consist of 12" of ballast over 8" of subballast. This ATC replaces the 8" of subballast with geotextile and geogrid.

H. Justification of Use

An analysis justifying use of the ATC and why the deviation, if any, from the requirements of the Contract Documents should be allowed;

This ATC will increase the service life of the track bed section by limiting ballast settlement and lateral creep. This will reduce ballast maintenance. During construction, this ATC reduces the excavation and export of potentially contaminated soils. This results in less trucking on local streets. The time required to install this track bed section is shorter than the specified section.

I. Preliminary Analysis and Quantitative Discussion

A preliminary analysis and quantitative discussion of potential impacts on rail or transit operations (both during and after construction), environmental permitting, community impact, safety, and life-cycle Project and infrastructure costs, including impacts on the cost of repair, replacement, maintenance, and operation;

MBTA Contract No. E22CN0 Formal ATC 37A GLX DB Project Page 4 June 30, 2017 No impacts on rail or transit operations are anticipated as a result of this ATC.

J. Impacts on Third Parties

A description of any impacts on the land or facilities of third parties, including private owners, governmental entities, utility owners, and railroads, and identification of specific additional right of way required to implement the ATC. Proposers are advised that they may (i) be solely responsible for the cost and schedule impacts of the acquisition of any such Additional Properties, including the cost thereof and obtaining any necessary environmental approvals; (ii) not be entitled to any change order for time or money as a result of site conditions (i.e., hazardous materials, differing site conditions, geotechnical issues, or utilities) on such Additional Properties; and (iii) not be entitled to any change order for time or money as a result of any delay, inability, or cost associated with the acquisition of such Additional Properties;

No impacts to third parties are anticipated as a result of this ATC.

K. History of Use and References

A description of any other projects where the ATC has been used, the degree of success or failure of such usage, and names and contact information, including phone numbers and E-mail addresses, for project owner representatives that can confirm such statements;

This ATC concept was successfully used as an equal replacement for the specified track bed section on MBTA's Greenbush Line.

Paul Hadley, MBTA, 617.512.5999, phadley@MBTA.com

L. Additional Risks

A description of added risks to the MBTA or third parties associated with implementing the ATC;

No additional risks to the MBTA or to third parties are anticipated as a result of this ATC.

M. Additional Costs

An estimate of any additional MBTA, DB Entity, and third-party costs associated with implementation of the ATC;

Additional costs to the MBTA, DB Entity and third parties will not result from this ATC. One of the primary purposes of this ATC is cost reduction.

N. Estimated Price Adjustment

An estimate of the price adjustment (i.e., cost savings), should the ATC be approved and implemented;

This ATC will result in an estimated savings of $600,000. The ATC pricing as shown in this proposal is an all inclusive price. All price deducts and/or adds have been considered, and the resulting price adjustment is offered as shown.

O. Schedule Adjustment

An estimate of the schedule adjustment, should the ATC be approved and implemented; and


This ATC does not require any schedule adjustment.

P. Analysis of Quality, Performance, and Reliability

An analysis of how the ATC is equal to or better in quality, performance, and reliability than the requirements of the Contract Documents.

This ATC will provide a better quality, performance and reliability than the specified track bed section because the separation of fines in the subgrade from the ballast and structural support of the geogrid should permit longer service life. The longer service life will allow for less maintenance and higher reliability.

Figure ATC-43-1: Proposed Track Bed Section

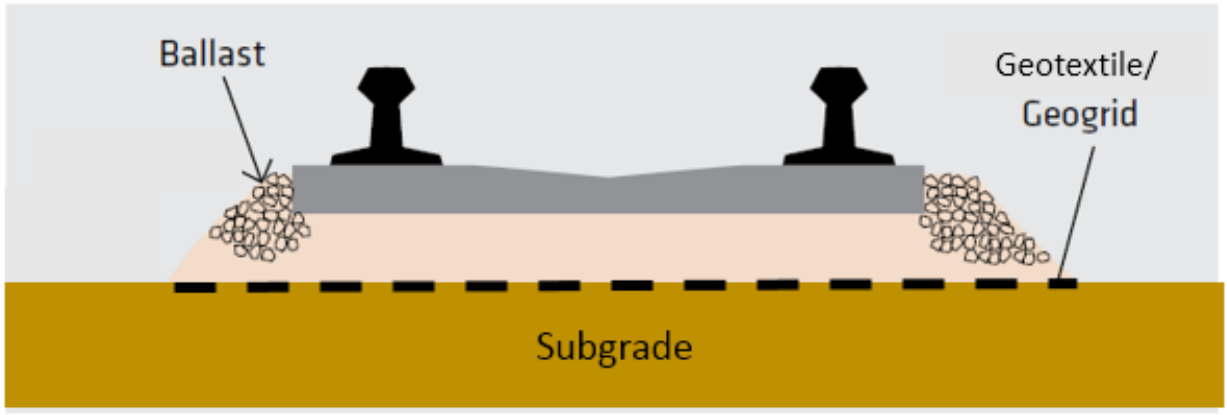


(Ballast min. 12")

Figure ATC-43-2: MBTA Greenbush Line Construction



Technical Proposal • Original • October 2017

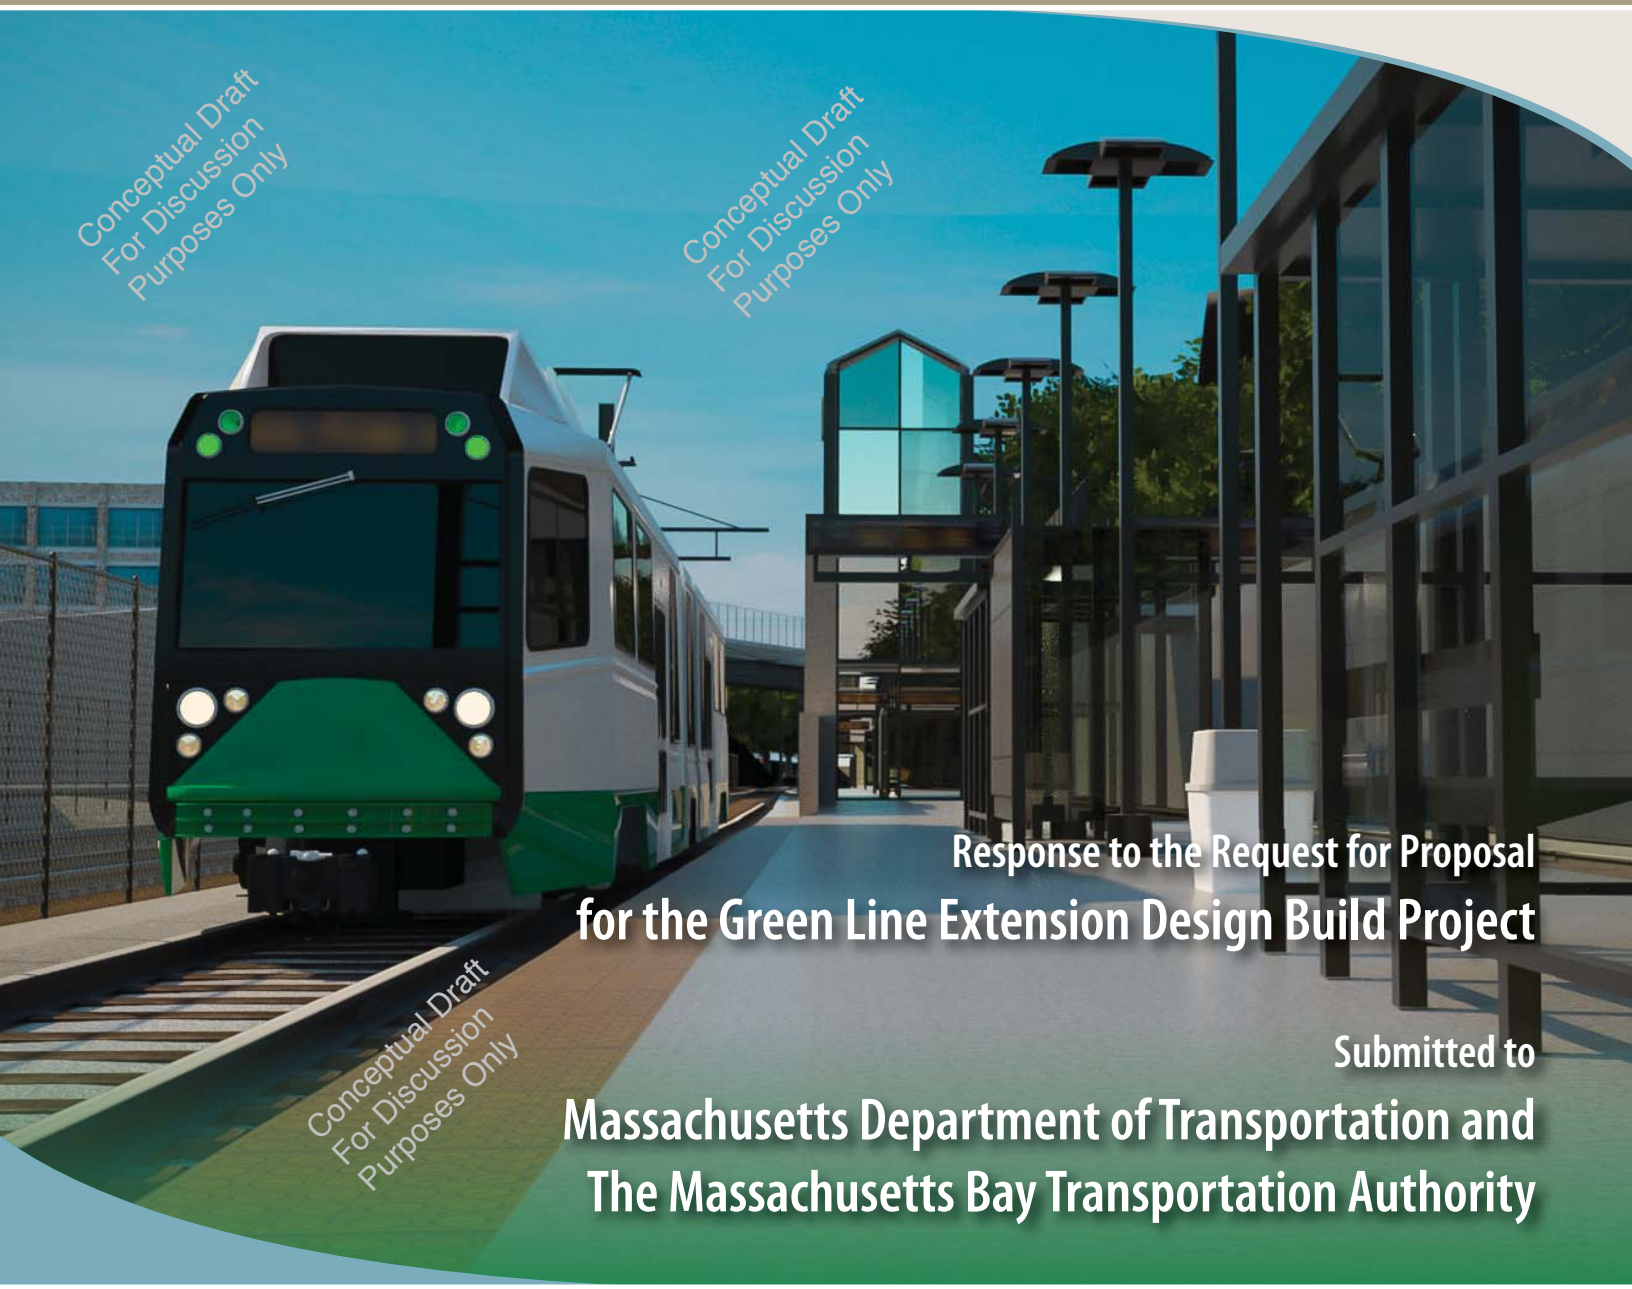

Response to the Request for Proposal for the Green Line Extension Design Build Project

Submitted to

Massachusetts Department of Transportation and The Massachusetts Bay Transportation Authority

Response to Request for Clarification No. 4

Where possible recycled paper was used.

GLX CONSTRUCTORS

GLX Constructors
100 Fluor Daniel Drive, C602D
Greenville, SC 29607
USA

864.320.4489 tel
max.jordan@fluor.com

October 16, 2017

Massachusetts Bay Transportation Authority
GLX Project Office
200 Innerbelt Road, Third Floor
Somerville, MA 02143-4456

Subject: Response to the Request for Clarifications No. 4

Dear Mr. Petersen:

GLX Constructors is pleased to provide you with our response to your Proposal Clarifications dated October 12, 2017.

1. In response to Question No. 1, based on the ITP, Attachment A, Section A3.2.2 (3)(c), the requested Guarantor Letter of Support from Fluor Corporation should not be required pursuant to items (x), (y), or (z) described therein. Notwithstanding the foregoing, attached is an executed Form AA, Guarantor Commitment Letter, stating that Fluor Enterprises, Inc., as a Major Participant, will receive, if required by the MBTA and the Instructions to Proposers, a parent company guarantee on its behalf from its parent, Fluor Corporation.

2. In accordance with Section A3.2.2(C) of Attachment A to the ITP, please see attached letter from Balfour Beatty Infrastructure, Inc. regarding the request to confirm no unaudited interim 2017 financials are available for Balfour Beatty Infrastructure, Inc.

3. In accordance with Section A3.2.2(3)(e) of Attachment A to the ITP, see attached most recent credit reports available for Fluor Corporation, Inc. from Standard & Poor's and Moody's.

4. GLX Constructors confirms receipt of Questions and Responses 7 issued on September 14, 2017.

5. Please see attached certified Articles of Incorporation and Bylaws for the following:

    a. The Middlesex Corporation

    b. Herzog Contracting Corp.

    c. Balfour Beatty Infrastructure, Inc.

6. Regarding the joint venture agreement of GLX Constructors, all members confirm and agree to be held jointly and severally liable to the MBTA for any and all duties and obligations of the joint venture.


7. In response to Question No. 7, please see evidence that the following individuals signing Form C are authorized to execute Form C on behalf of the applicable team member:

    a. Po-Shang Chen, C&C Consulting Engineers, LLC

    b. Deborah A. Jue, Wilson Ihrig

We continue to look forward to working with the MBTA to make this project a success and are happy to answer and additional questions or clarifications that may arise.

Sincerely,



Max Jordan
Authorized Representative

Financial information contained in the GLX Constructors Technical Proposal is located at the GLX Project Office, 200 Innerbelt Road, Third Floor, Somerville, MA 02143-4456.

WILSON IHRIG

Secretary Certificate

CERTIFICATE OF VOTE

I, James E. Phillips, hereby certify that I am the Secretary of Wilson Ihrig (the "Company"), and I further certify that the Directors of the Company have confirmed by unanimous written consent that Derek L. Watry is the Chief Executive Officer of the Company, that Deborah A. Jue is the Treasurer, and both have been since March 13, 2014 or earlier.

I additionally certify that the Company's Articles and By-Laws state, "The board of directors ... may authorize any officer or officers, agent or agents, to enter into any contract or execute any instrument in the name of and on behalf of the corporation," and I certify that the Directors of the Company confirmed by unanimous vote, on August 14, 2012, that "officers of the firm be allowed to sign contracts", including the execution of Form C, and any similar documents certifying information for Wilson Ihrig for the MBTA Green Line Extension, Contract No. E22CN07.

By: _____
Secretary

A True Copy:


Attest: _____
Notary Public

DENISE A. WHITE
COMM. #2178919
Notary Public - California
Alameda County
My Comm. Expires Jan. 8, 2021

My Commission Expires: 1/8/2021

Date: 10/13/2017

Technical Proposal • Original • October 2017

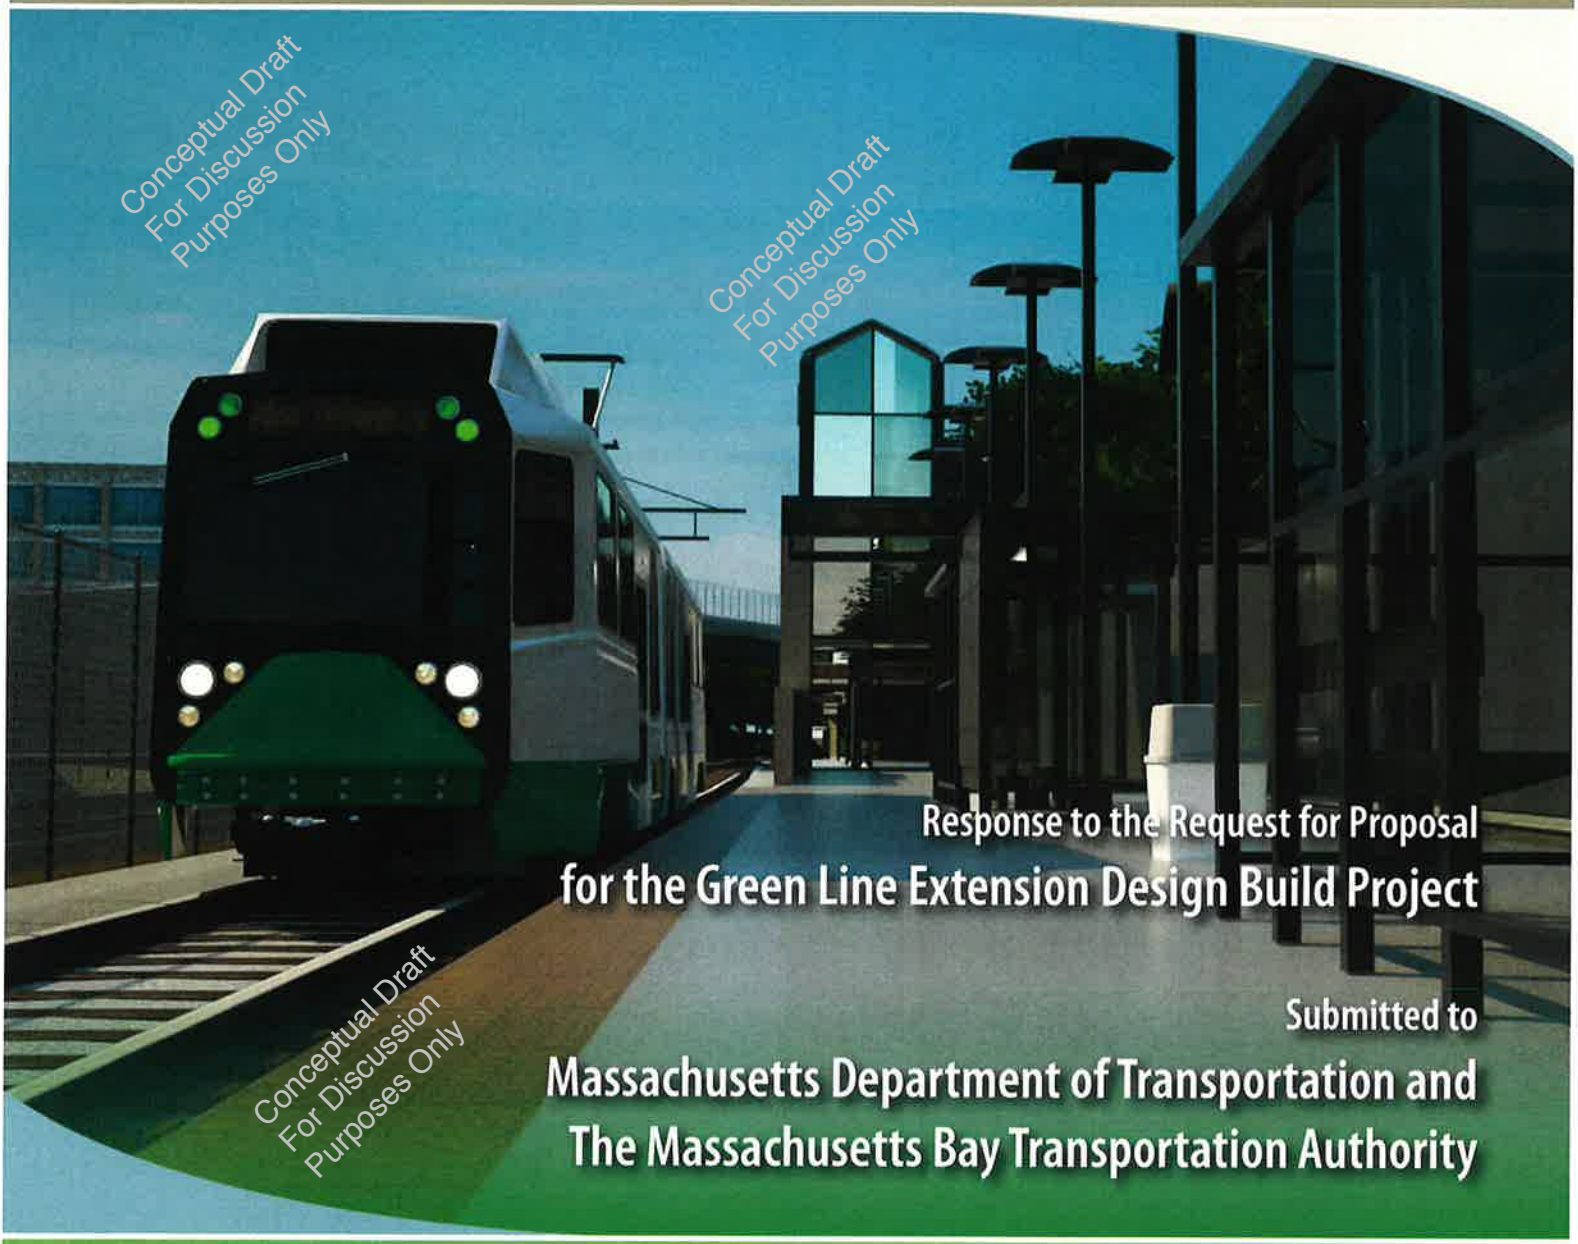

Conceptual Draft For Discussion Purposes Only

Conceptual Draft For Discussion Purposes Only

Conceptual Draft For Discussion Purposes Only

Response to the Request for Proposal for the Green Line Extension Design Build Project

Submitted to

Massachusetts Department of Transportation and The Massachusetts Bay Transportation Authority

Response to Request for Clarification No. 6

Where possible recycled paper was used.

GLX CONSTRUCTORS

GLX Constructors
100 Fluor Daniel Drive, C602D
Greenville, SC 29607
USA

864.320.4489 tel
max.jordan@fluor.com

October 20, 2017

Massachusetts Bay Transportation Authority
Mr. Donald Petersen
GLX Project Office
200 Innerbelt Road, Third Floor
Somerville, MA 02143-4456

Subject: Response to the Request for Clarifications No. 6

Dear Mr. Petersen:

We have carefully reviewed the request for Clarification No. 6 and offer the following response. We regret the difference in interpretation on the support letter. We have truly tried to be responsive within the terms of the RFP and are not trying to be difficult.

Fluor Corporation only recently started doing separate audited financials for its wholly owned subsidiary Fluor Enterprises, Inc. Prior to that, the financials of Fluor Enterprises, Inc. were consolidated within the audited financials of Fluor Corporation. As a result, we provided all of the most recent audited financials that we had at the time of submittal for Fluor Enterprises and Fluor Corporation, along with the unaudited financials for Fluor Enterprises for the previous 3 years.

We are providing in this response, as you have requested, an unaltered Guarantor Commitment to Provide Parent Guaranty for the Green Line Extension Design Build Project per the RFP.

We apologize for any confusion this may have caused and for any misinterpretation of your previous request. If you have any questions or concerns about whether this meets your Request for Clarification No. 6 or your ability to determine the TNW of Fluor or GLX Constructors, please contact me immediately and we will immediately rectify any further problems or shortcomings."

If there are any issues or concerns whatsoever please pick up the phone and call me directly at 864 320 4489 and I will get it resolved.

Sincerely,

Max Jordan
Authorized Representative

FLUOR®

Fluor Corporation
6700 Las Colinas Boulevard
Irving, Texas 75039
USA

469.398.7060 tel
469.398.7715 fax
jim.lucas@fluor.com

James M. Lucas
Senior Vice President, Tax & Treasury, and Treasurer

FORM AA

GUARANTOR COMMITMENT LETTER

October 20, 2017

Yvelisse Duvergé
Manager of Construction Procurement
Massachusetts Bay Transportation Authority
GLX Project Office
200 Innerbelt Road, Second Floor
Somerville, MA 02143-4456

RE: Guarantor Commitment to Provide Parent Guaranty for the Green Line Extension Design Build Project

Dear Ms. Duvergé:

Fluor Corporation, hereinafter "Guarantor," is the parent company of Fluor Enterprises, Inc., a Major Participant of GLX Constructors. This commitment letter is provided on behalf of GLX Constructors, an unincorporated joint venture ("GLX Constructors"), in connection with its Proposal for the Design Build Contract ("DB Contract") for the Green Line Extension Design Build Project ("Project"). Guarantor hereby irrevocably agrees to provide a guaranty, guaranteeing all the obligations of GLX Constructors with respect to the DB Contract in the form of Exhibit 11 of the DB Contract. This commitment is subject only to award of the DB Contract to GLX Constructors, execution of the DB Contract by the MBTA, and GLX Constructors and the issuance of NTP.

Sincerely,

James M. Lucas
Senior Vice President, Tax & Treasury, and Treasurer

EXHIBIT 1R

ADDITIVE OPTION PROPOSAL

(See attached.)



Response to the Request for Proposal

for the Green Line Extension Design Build Project

Submitted to

Massachusetts Department of Transportation and The Massachusetts Bay Transportation Authority

Additive Option Submission

GLX CONSTRUCTORS

TABLE OF CONTENTS

ADDITIVE OPTIONS SUBMISSION →

1. **Design and Construction of Station Canopies to All Stations**
2. **Design and Construction of Elevators to Stations Proposed for New/Additional Elevators**
3. **Inclusion of an Art Program**
4. **Design and Construction of the Community Path Connection to Chester Street**
5. **Design and Construction of the Community Path Connection from East Somerville to Lechmere**
6. **Design and Construction of an Enhanced Vehicle Maintenance Facility**
7. **Appendix A – Alternative Technical Concepts –** *No Alternative Technical Concepts Submitted*

ADDITIVE OPTIONS

“This additive option will enhance the overall commuter experience for the MBTA riders, expand protection for all commuters during inclement weather conditions while simultaneously all but eliminate, the need for snow removal along the entire length and width of the station platform area.

1. DESIGN AND CONSTRUCTION OF STATION CANOPIES TO ALL STATIONS

1.A GENERAL APPROACH AND LOCATION-SPECIFIC DESIGNS

This additive option will enhance the overall commuter experience for the MBTA riders, expand protection for all commuters during inclement weather conditions, while simultaneously all but eliminate the need for snow removal along the entire length and width of the station platform area. In covering the entire length and width of the station platform area with a continuous canopy it insures the MBTA's physically challenged riders will have a smooth, clear, and totally protected path-of–travel from the elements from the point where they enter the station to when they embark on the train and vice versa on their return trip to the station.

GLX Constructors' Lead Designer, STV, is very familiar with gull wing canopy concept portrayed in Figures 1 and 2 under the Volume No. 3 – Additive Options. As shown in Figure 1-1, this base concept was used by STV in designing the canopy structure system for the recently completed MBTA Boston Landing Commuter Rail (Purple Line) Station in Brighton, Massachusetts. Because of that design, similarity to what is shown as an additive concept for this Project, we have adapted it for our proposal herein by extending the wings of the canopy 5-1/4 feet beyond the edge of the platform.

With the exception of Lechmere Station, the platforms at all of the other six stations are identical. They are all 225-feet long, and their widths vary by only by 1 to 3 feet. Under our base proposal, we have been able to tweak the track geometry whereas both tracks through all six stations in question are parallel to another. The edge of platform is set at 4 to 9 feet from center line of track and therefore also runs parallel to the tracks. Since both the tracks and platform edges are straight this means the edge of the canopies are also straight making its framing, structural support, and canopy roof assembly almost identical at all six stations. This simplifies the fabrication process which in turn helps control costs and more importantly maintains symmetry at all stations along the entire length of the Green Line extension.

The platform at Lechmere Station is unique since it is driven by the track geometry throughout the station. Both tracks are curved differently and the profile, albeit the same for both tracks varies between the two headhouses serving the station platform. This results in a much wider and varying platform width and curved height throughout, requiring two rows of canopies which Additive Option Item 1 acknowledges. Although different than the other stations, our proposed design concept plans provided herein shows that the base design can be easily tweaked by reducing the span of the inner wings of both rows of columns and adding additional framing members (purlins) at the outer wings framing at the wider sections of platforms while still maintaining the 5-1/4 foot overhang along the continuous curved edge of the platform as required per the RFP. Once again, symmetry with the other stations canopy design remains intact.



Figure 1-1. MBTA Boston Landing Commuter Rail Line Canopy. *The wing-style canopy used will be adapted for this Project to extend the wings of the canopy 5-1/4 feet beyond the edge of the platforms.*

GLX CONSTRUCTORS

Our proposed canopy design presented takes into account the possibility and requirements for the station platform and canopy structure to be extended in the future to accommodate a four-LRV car platform. As shown in the framing plans at the end of this section, the last end-roof section of the canopy structure is cantilevered 7'-6" off the last canopy support column shown. When and if the platform canopy is extended, the next column can be placed 7'-6" from the edge of the end of the existing platform. This creates the 15'-0" spacing to match the other existing canopy support columns in place thus providing the same rhythm and symmetry between the existing and new, making the canopy to appear to be as one.

Changes from the Technical Proposal

To support this enhancement, some of the enclosed, standalone shelters and light poles will be replaced by the canopies. The canopy support columns will be more robust with heavier reinforcement than the replaced light poles. The overall size and shape of the foundation to accommodate the canopy loading will be minimal. The canopy roof framing will support light fixtures as well as other system components and devices required on the station platform, such as VMS, PA speakers, CCTV cameras, etc. Conduits and wiring will be changed to run aboveground and at the underside of the canopy structure to feed all of the aforementioned systems.

The canopy roof will require a stormwater collection system, with a minimal number of downspouts and lateral drainage piping running under the platform to connect with the closed storm water system in the track bed.

1.B SCHEDULE IMPACT ASSESSMENT

GLX Constructors' efforts to support this Additive Option will not impact the proposed schedule.

1.C STATION CANOPIES DRAWINGS


We adjusted the spacing of the canopy support columns to match the spacing of the light poles along the entire length of platform. We are basically dropping it in and substituting the canopy columns for the light poles. This in turn means minimal or no impacts will be experienced because of the effort we put forth in meticulously laying out the platform furnishings, such as emergency kiosks, benches, wayfinding signage, spider maps, and information plaque per the MBTA Standards and Guidelines and the required code and MBTA driven accessibility path-of–travel at the platform level under our base proposal drawing. Although the canopy structure would displace the light poles under the base proposal it indirectly provides a more flexible means for providing the required illumination levels throughout the station. The lighting plan layout and lighting fixture schedule provided demonstrates this flexibility. By supporting the light fixtures off the underside of the canopy framing allows lighting to be placed continuously along the edge of the canopy to illuminate the platform edge in accordance with the specific MBTA standards for foot candle requirements. The canopy also allows the other interior lighting to be spaced accordingly to provide a more even coverage of illumination. The proposal canopy herein also offers alternative support for the other systems along the station platform such as VMS signage that under the base proposal requires its own support pole and foundation assembly, PA speakers, passive wayfinding signage, FA devices, CCTV security cameras, etc. all while providing the minimum 9'-0" clearance requirement as shown in the cross sections on the drawings.

The gull wing shape of the canopy roof structure also provides the most efficient means for collecting and discharging of storm water runoff. The aforementioned cross sections contained under this section as well as the framing plans show a center gutter system which are sloped to a series of closed down spouts which occur at the low point at every other canopy structure support column (approximately 30 feet o.c.) which in turn are connected to lateral drainage piping underneath the platform which then lead out to a closed track system storm water infrastructure collection system in the track bed. In the case of Lechmere Station the drainage piping will be brought over to the nearest viaduct pier(s) then down to connect to the storm water infrastructure below the street level as depicted and noted in the cross sections provided.

As with the base proposal the cross sections show a crowned platform center to promote positive drainage to either track bed.


At Lechmere station, the entire platform slab is supported by its own steel girder framing system as shown on the cross sections. The girder framing system, although separate and independent of the Viaduct structure, is supported by the viaduct piers. The design of the platform slab and its steel girder framing system take into account the loading conditions that will be imposed by the canopy structure if this additive option is incorporated into the work.

RFP	
Drawing Number	**Drawing Title**
OPT1-01	Typical Single Wing Station Platform Canopy Elevation and Section – Additive Option 1
OPT1-02	Typical Single Wing Station Platform Canopy Section – Additive Option 1
OPT1-03	Typical Canopy Details – Additive Option 1
OPT1-04	Typical Station Canopy Lighting Plan – Additive Option 1
OPT1-05	Lechmere Part 1 Canopy Plan, Elevation and Sections – Additive Option 1
OPT1-06	Lechmere Part 2 Canopy Plan, Elevation and Sections – Additive Option 1
OPT1-07	Lechmere Canopy Section At Column Line 1 – Additive Option 1
OPT1-08	Lechmere Canopy Section At Column Line 23 – Additive Option 1
OPT1-09	Lechmere Canopy Lighting Plan Sheet 1 Of 2 – Additive Option 1
OPT1-10	Lechmere Canopy Lighting Plan Sheet 2 Of 2 – Additive Option 1

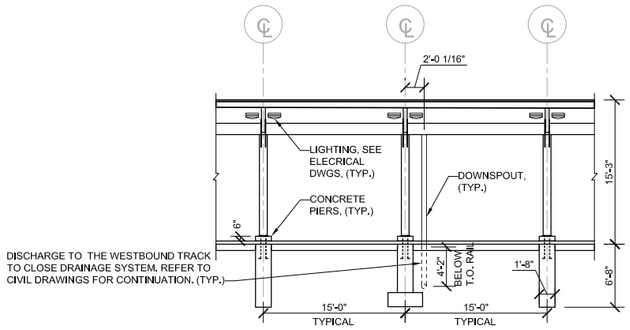


TYPICAL PIER SPACING

SCALE: 1/8"= 1'-0"

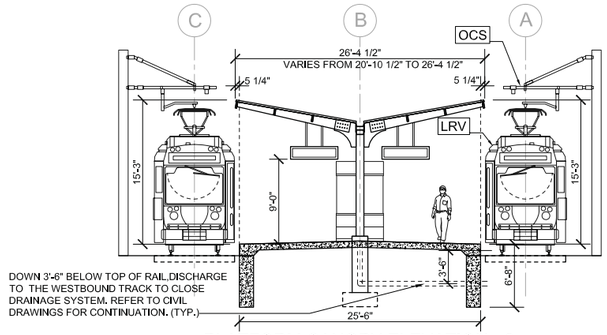


PLATFORM CANOPY ELEVATION - 2

SCALE: 1/8"= 1'-0" TYPE 3

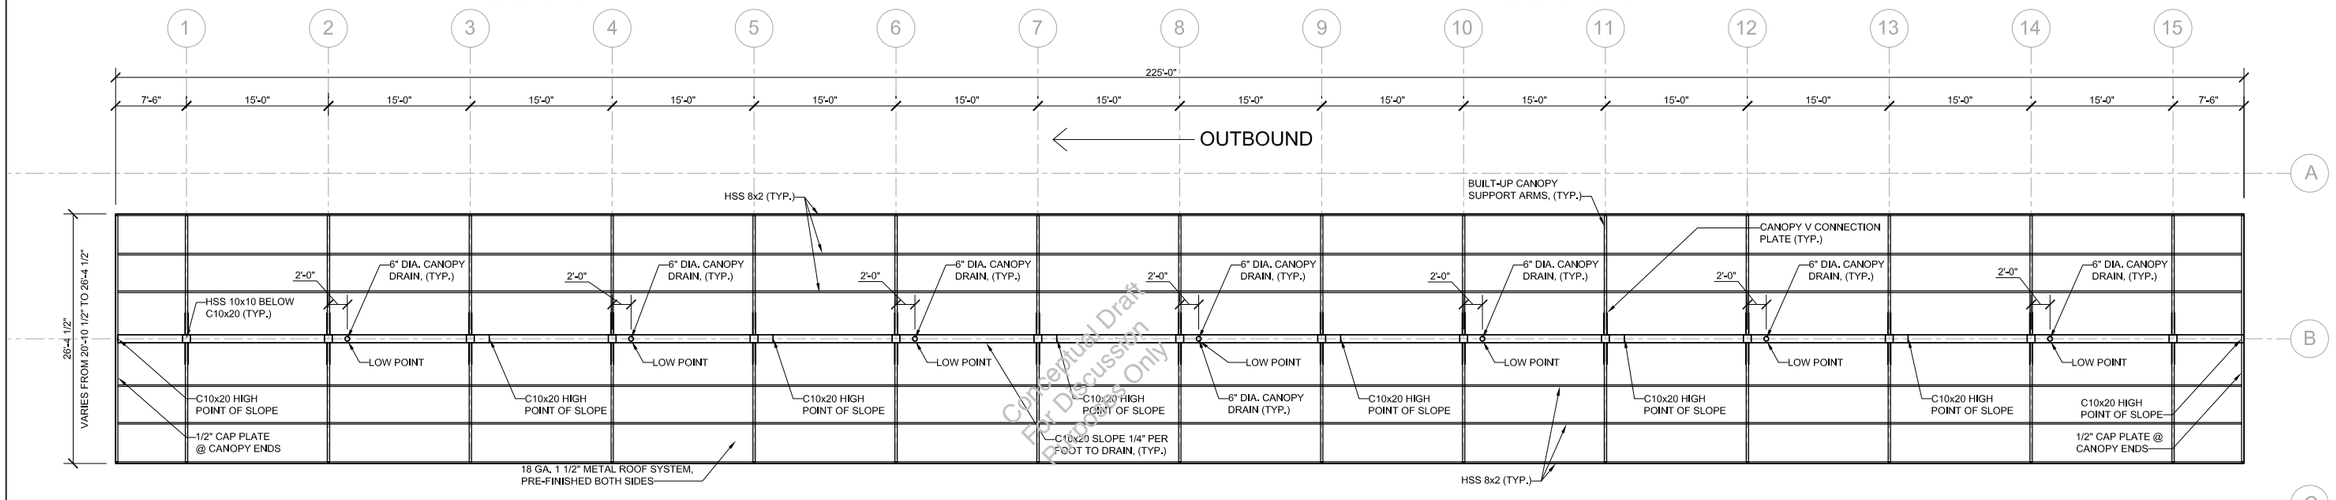

PLATFORM CANOPY PLAN

SCALE: 1/8"= 1'-0" TYPE 3 DATE: 7-24-17

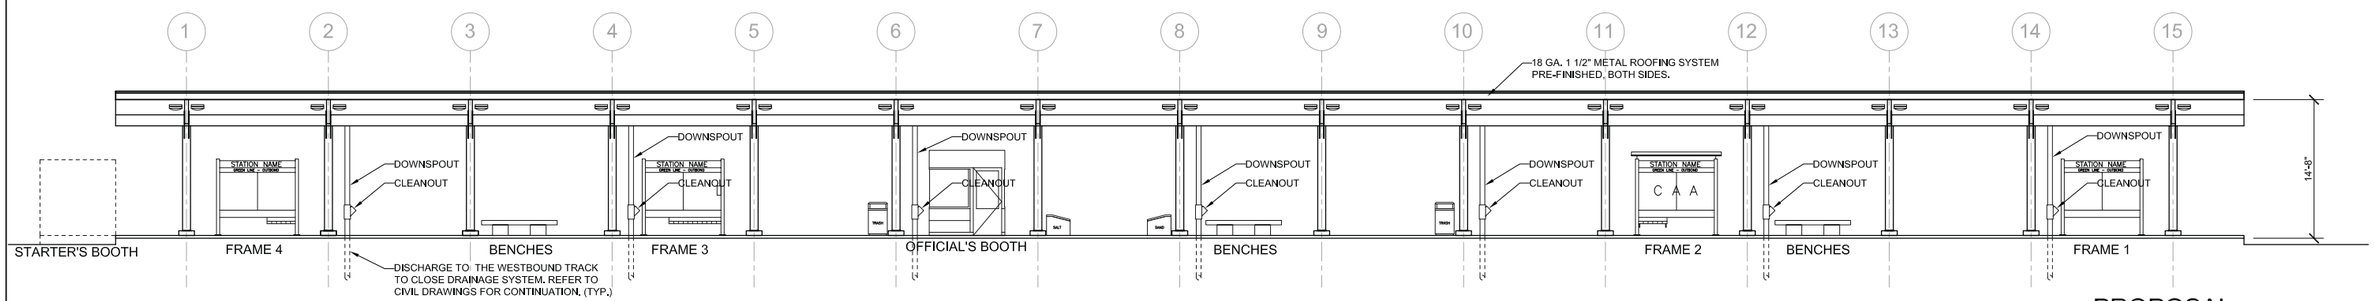

PLATFORM CANOPY ELEVATION - 1

SCALE: 1/8"= 1'-0" TYPE 3 DATE: 7-14-17

GRAPHIC_SCALE

0 4' 8' 12' 16' 20'

1/8"=1'-0"

NOTES:

1. THIS PLAN AND ELEVATION APPLIES TO ALL STATIONS EXCEPT LECHMERE STATION
2. PLATFORM CANOPY WIDTH VARIES FROM 20'-10 1/2" TO 26'-4 1/2"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY


GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

TYPICAL SINGLE WING STATION PLATFORM CANOPY, ELEVATION AND SECTION - ADDITIVE OPTION 1

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-278.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	ND	SHEET: OPT1-01	.

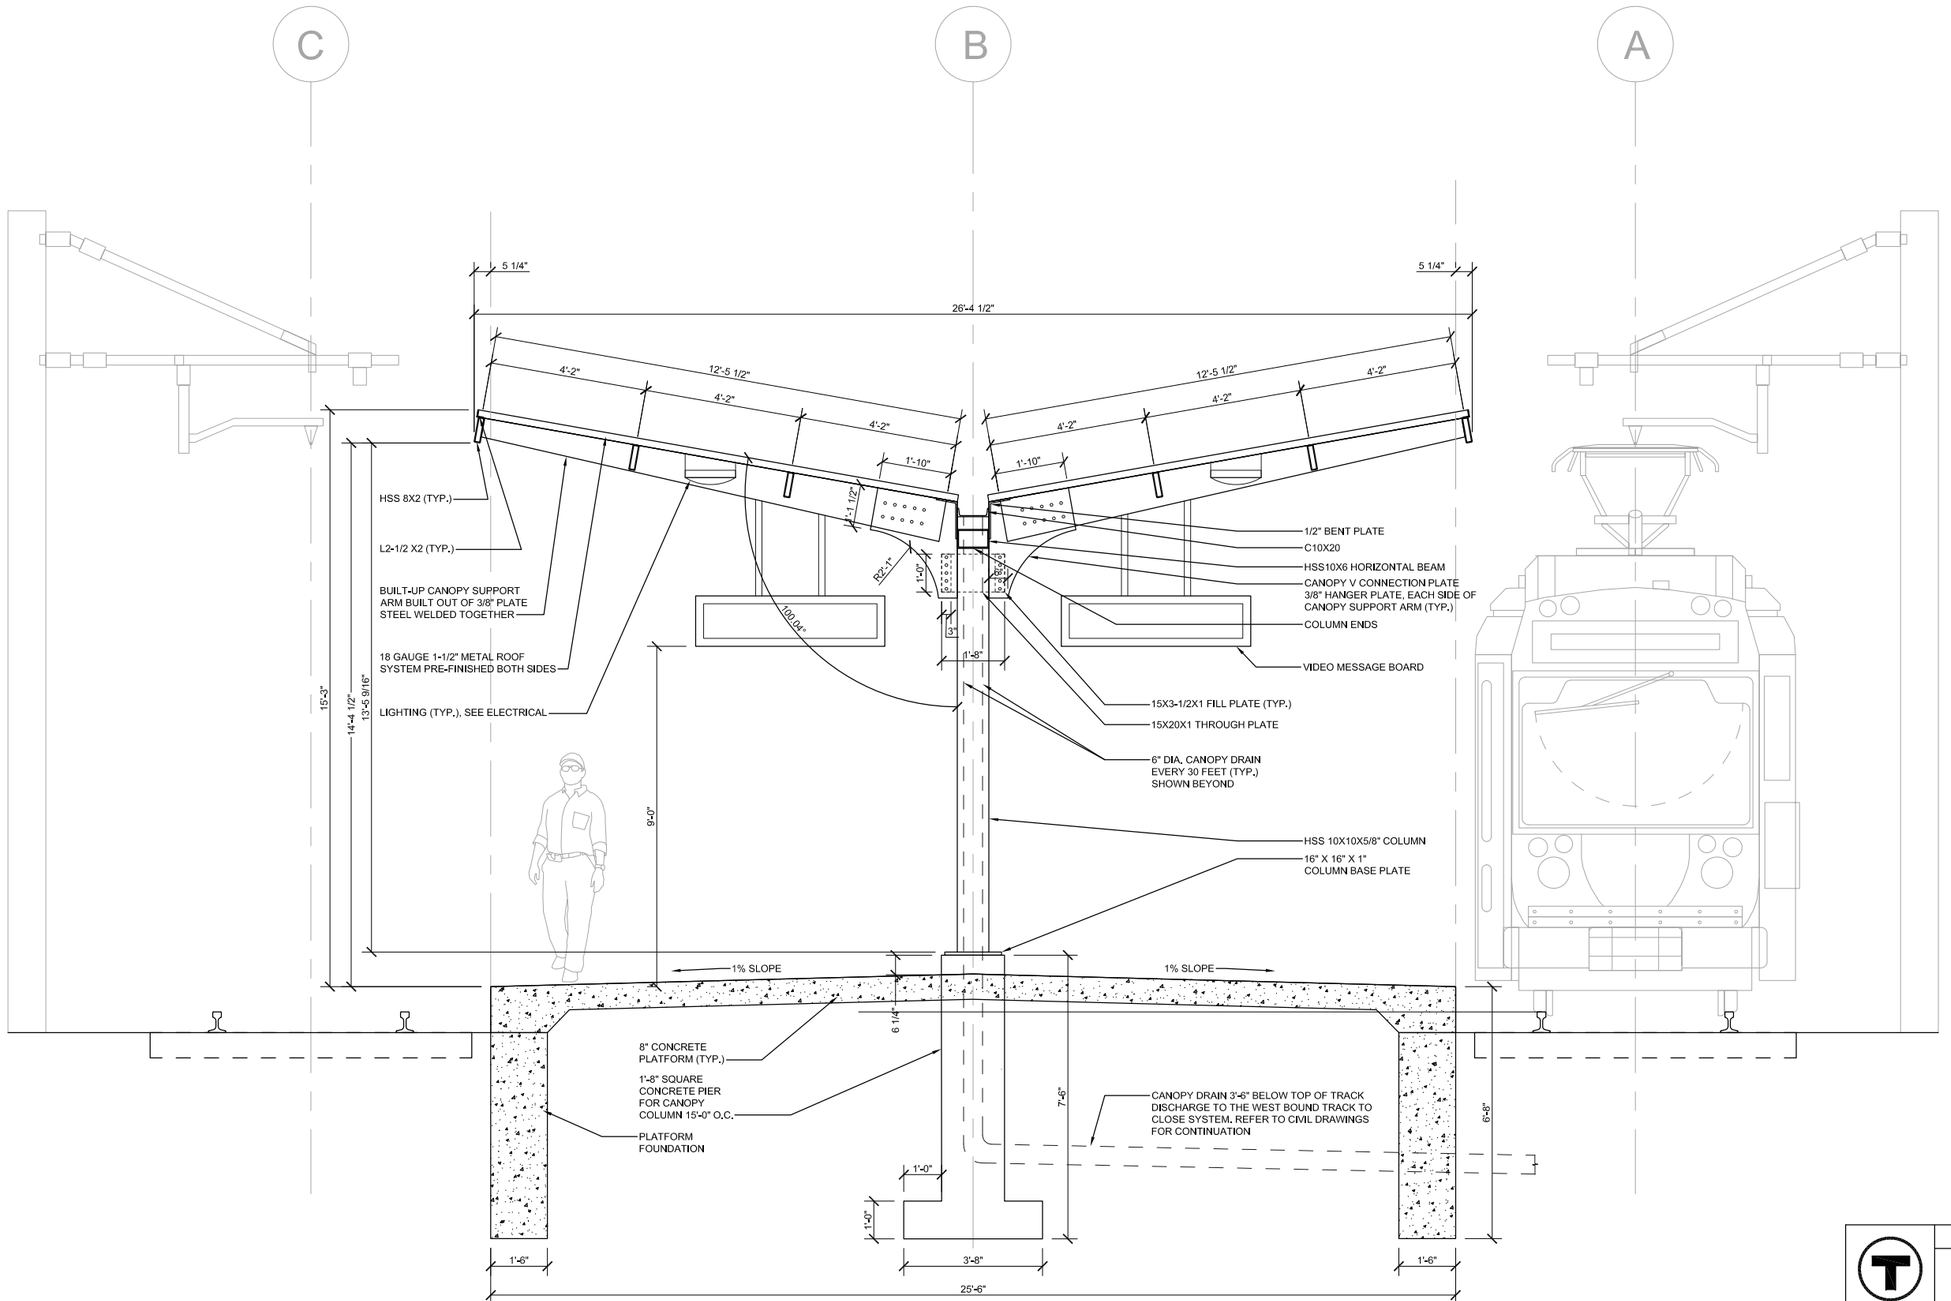

TYPICAL SECTION - 1

SCALE: 1/2"= 1'-0" TYPE 3 DATE: 7-14-17

PLATFORM TYPE 3-COLLEGE SQUARE STATION. - (25'-6") WIDE PLATFORM

ALL STEEL SHALL BE GRADE Fy = 50 KSI

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY


GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

TYPICAL SINGLE WING PLATFORM CANOPY SECTION - ADDITIVE OPTION 1

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-278.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	ND	SHEET: OPT1-02	.

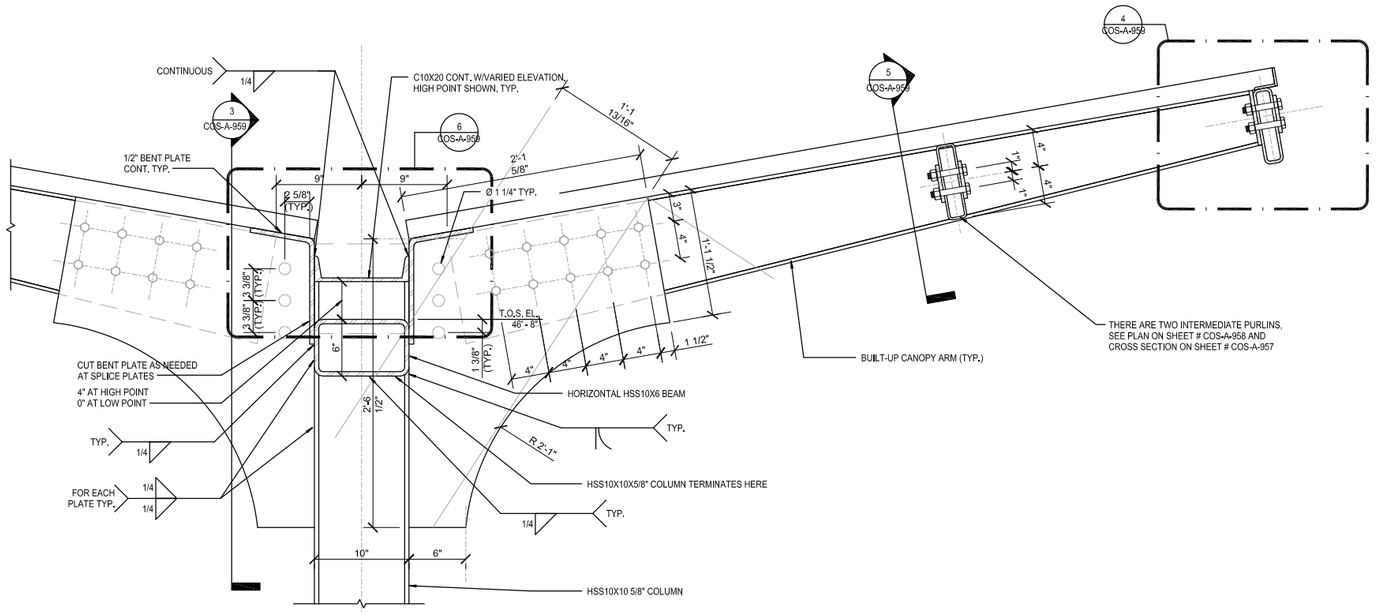


PLATFORM CANOPY ARM DETAIL

1 1/2" = 1'-0"

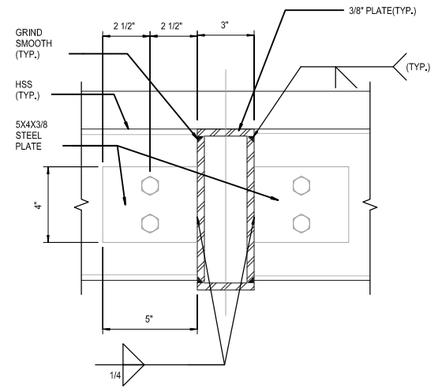


5 DETAIL

COS-A-959 3" = 1'-0"

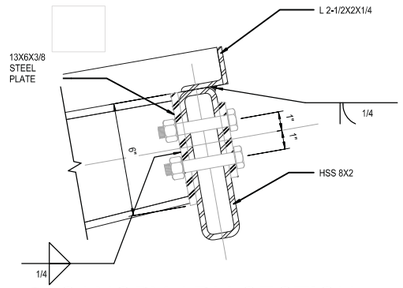


4 CANOPY ARM SECTION

COS-A-959 3" = 1'-0"

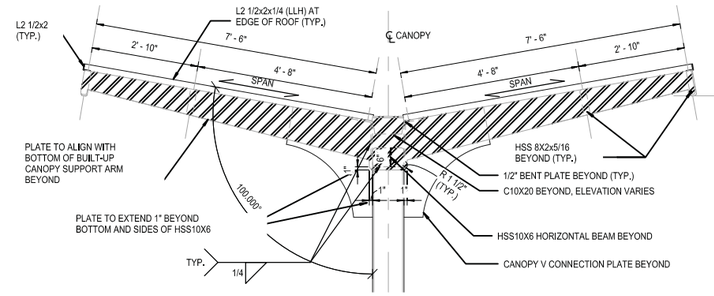


PLATFORM CANOPY END PLATE

1/2" = 1'-0"

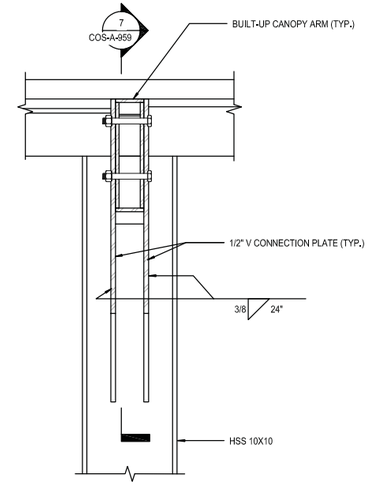


3 SECTION

COS-A-959 1 1/2" = 1'-0"

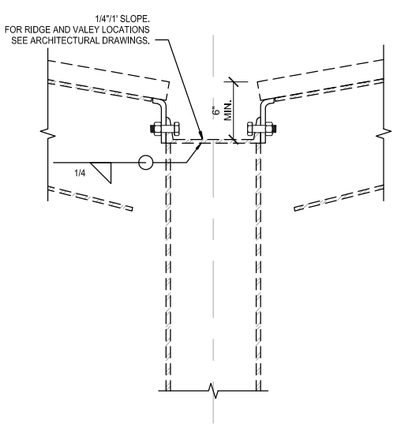


7 SECTION

COS-A-959 1 1/2" = 1'-0"

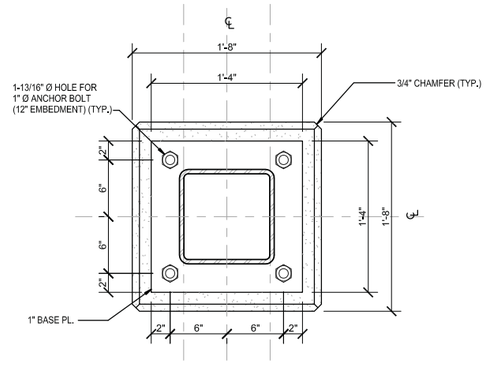

PLATFORM CANOPY BASE PLATE DETAIL

COS-A-959 1 1/2" = 1'-0"

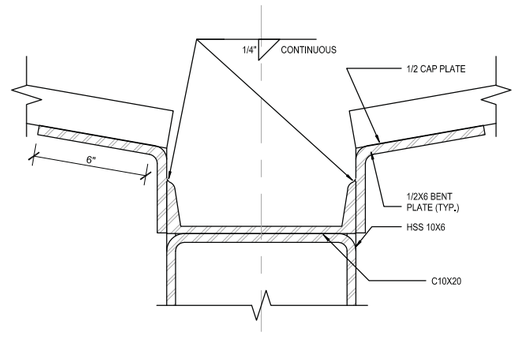

6 DETAIL

COS-A-959 3" = 1'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


TYPICAL CANOPY DETAILS
- ADDITIVE OPTION 1

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


GV20170258-278.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	ND	SHEET: OPT1-03	.

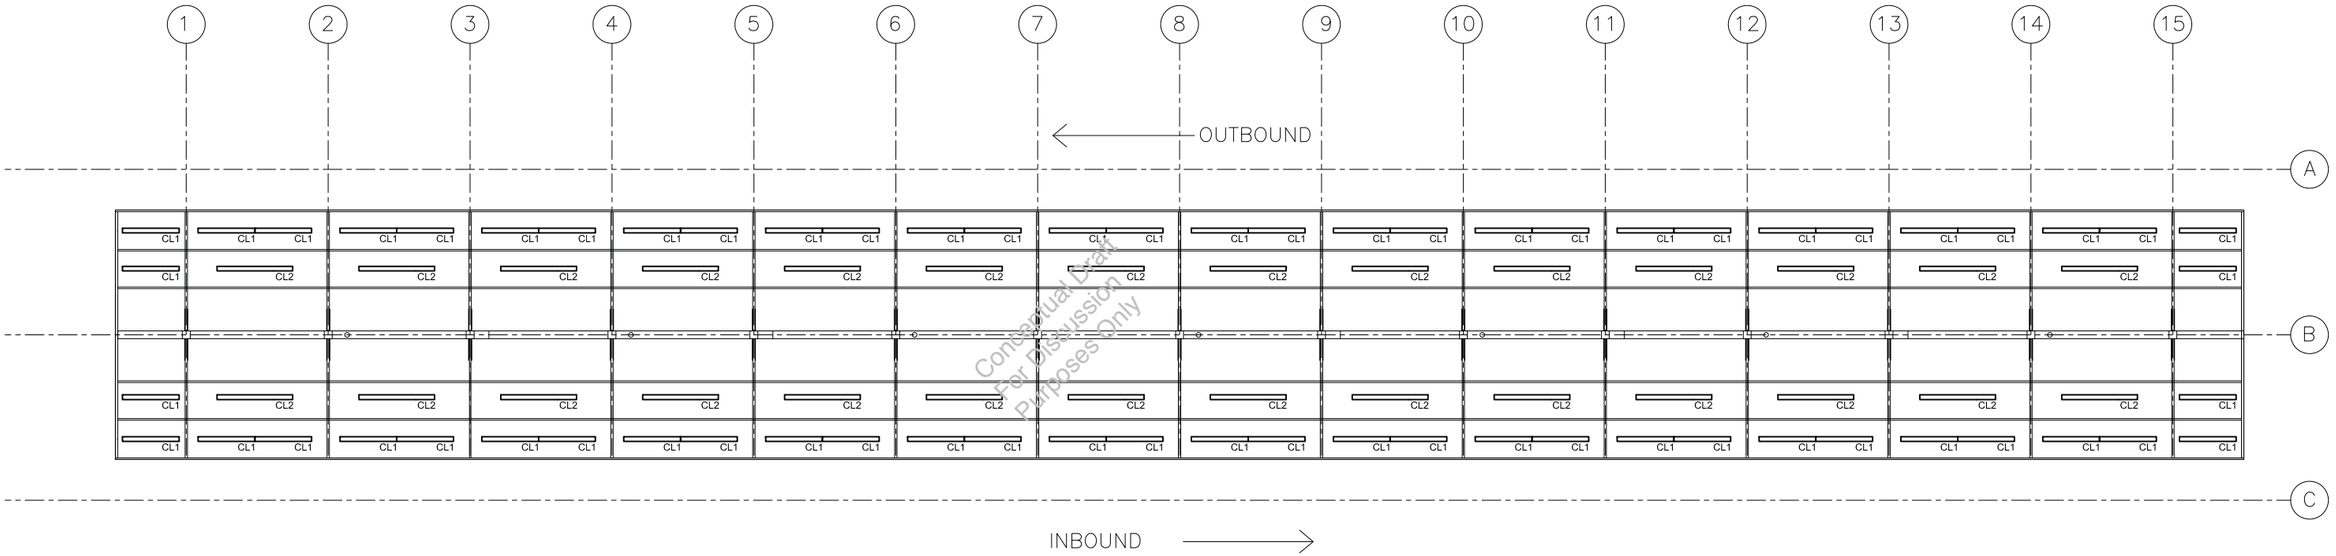

TYPICAL STATION PLATFORM CANOPY LIGHTING PLAN

1/8"=1'-0" 0 4' 8' 16'

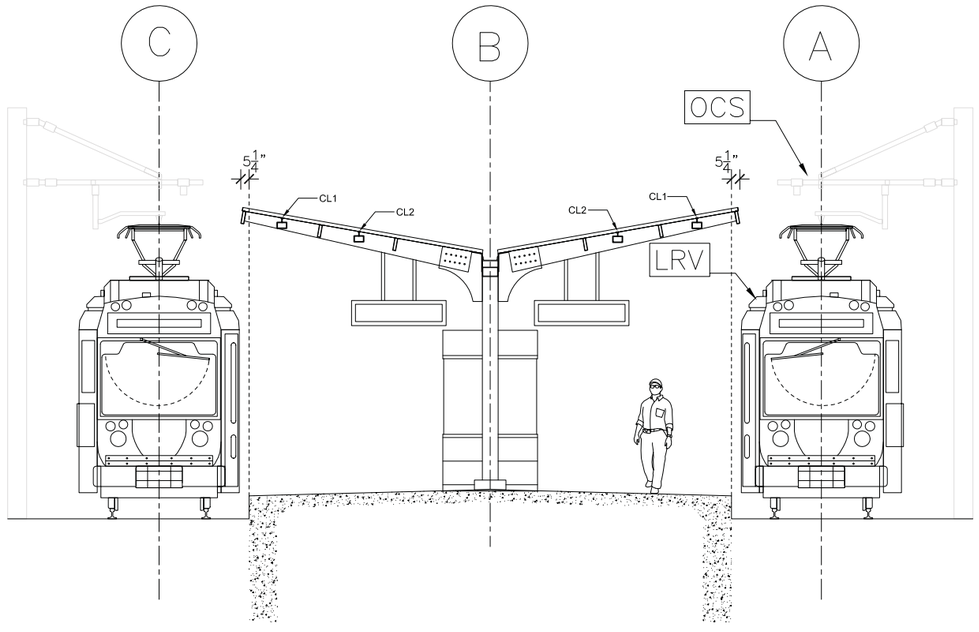

TYPICAL STATION PLATFORM CANOPY LIGHTING SECTION

1/4"=1'-0" 0 2' 4' 8'

LIGHTING FIXTURE SCHEDULE								
FIXTURE TYPE	MANUFACTURER	CATALOG NUMBER	DESCRIPTION	MOUNTING	LAMP TYPE	VOLTAGE	LAMP WATTS	NOTES
CL1	FORUM	AQD-36-125LED30-SAT-H2.5"X6-UNV-SV	WET LOCATION RECTANGULAR LUMINAIRE	PENDANT	LED	120-277	75	MOUNT APPROX. 14'-0" FROM BOTTOM OF LIGHT FIXTURE
CL2	FORUM	AQD-36-125LED30-SAT-H2.5"X8-UNV-SV	WET LOCATION RECTANGULAR LUMINAIRE	PENDANT	LED	120-277	100	MOUNT APPROX. 13'-2" FROM BOTTOM OF LIGHT FIXTURE

NOTES:
1. LIGHTING ON THIS DRAWING APPLIES TO ALL STATIONS EXCEPT LECHMERE STATION

Conceptual Draft For Discussion Purposes Only

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


TYPICAL STATION PLATFORM CANOPY LIGHTING PLAN - ADDITIVE OPTION 1

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-278.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	AR	AR	ND	SHEET: OPT1-04	.

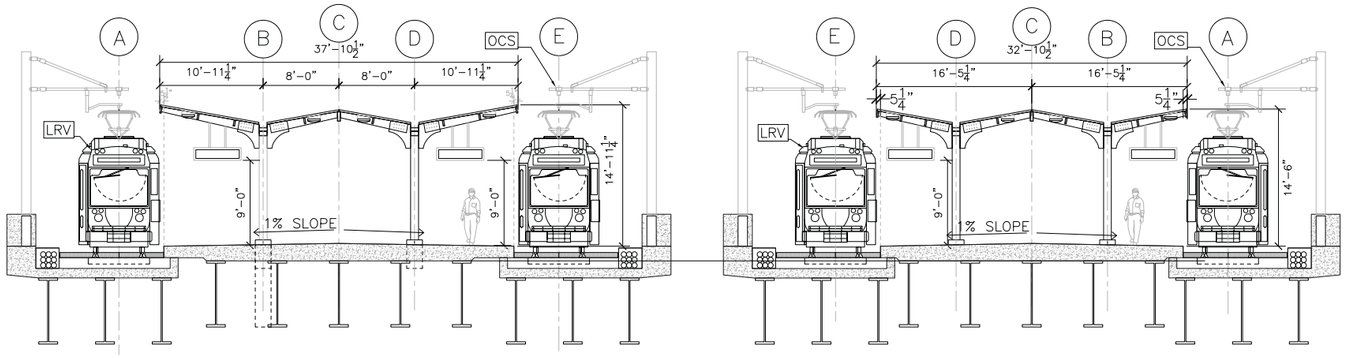


PLATFORM CANOPY SECTION @ CL1

SCALE: 1/8"= 1'-0"

PLATFORM CANOPY SECTION @ CL 23

SCALE: 1/8"= 1'-0"

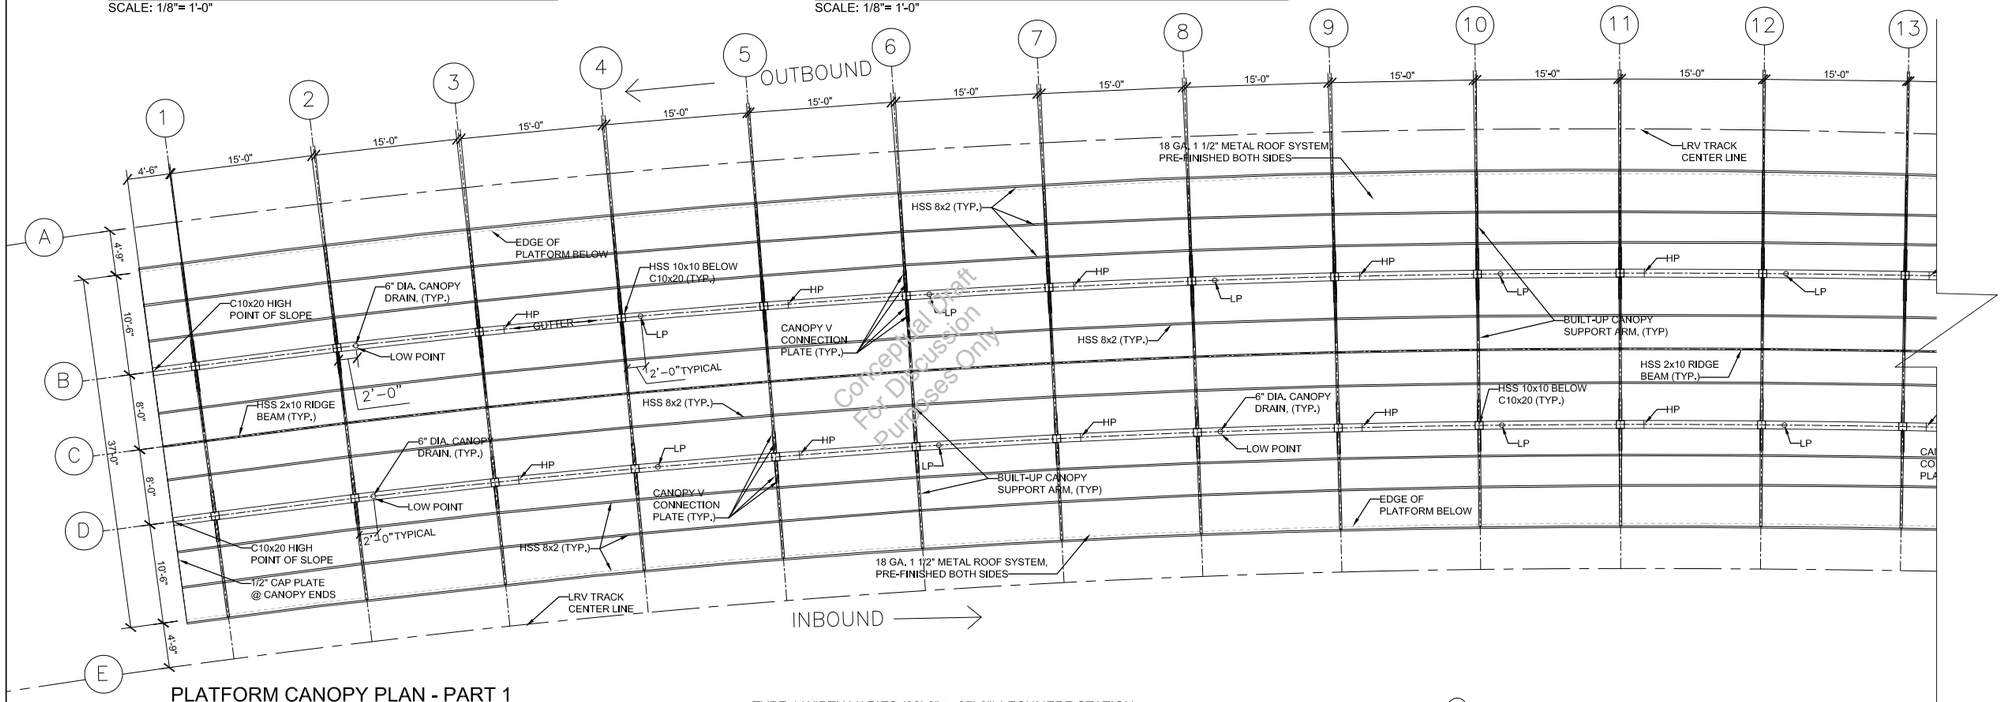


Conceptual Design For Discussion Purposes Only

PLATFORM CANOPY PLAN - PART 1

SCALE: 1/8"= 1'-0" TYPE 4, DATE: 7-31-17

TYPE 4-WIDTH VARIES (32'-0" to 37'-0") LECHMERE STATION

TOTAL LENGTH @ CENTER LINE Ⓒ OF PLATFORM=339'-4" +/-

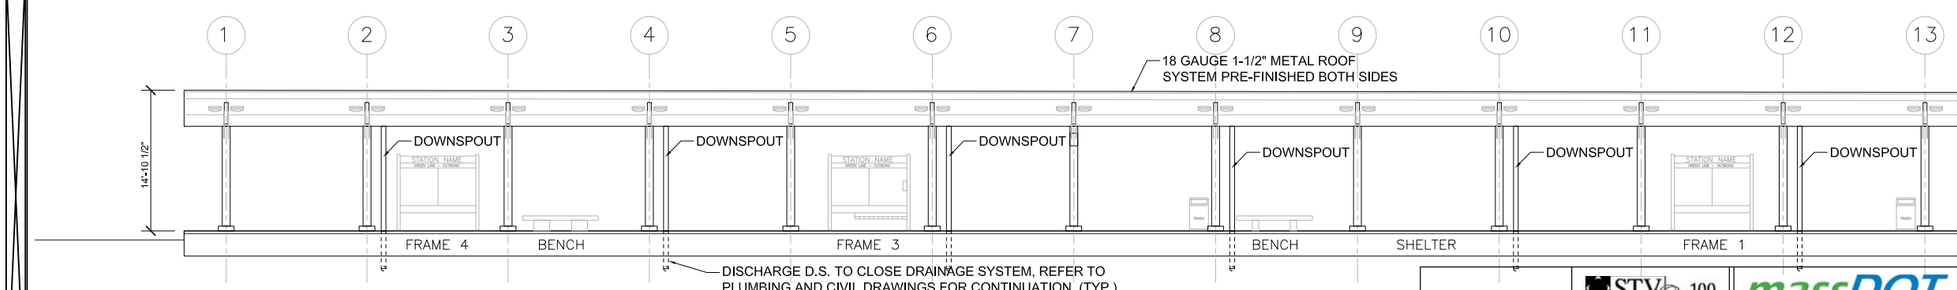

PLATFORM CANOPY ELEVATION - PART 1

SCALE: 1/8"= 1'-0" TYPE 4 DATE: 7-31-17

PLATFORM TYPE 4 = LECHMERE- 32'-0" to 37'-0" WIDE PLATFORM

ALL PLATFORM CANOPY STEEL SHALL BE GRADE Fy = 50 KSI

0 1' 2' 3' 4' 5' 1/8" = 1'-0"

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY


GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

LECHMERE STATION PART 1
CANOPY PLAN, ELEVATION AND SECTIONS
- ADDITIVE OPTION 1

GLX CONSTRUCTORS


GV20170258-278.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	ND	SHEET: OPT1-05	.

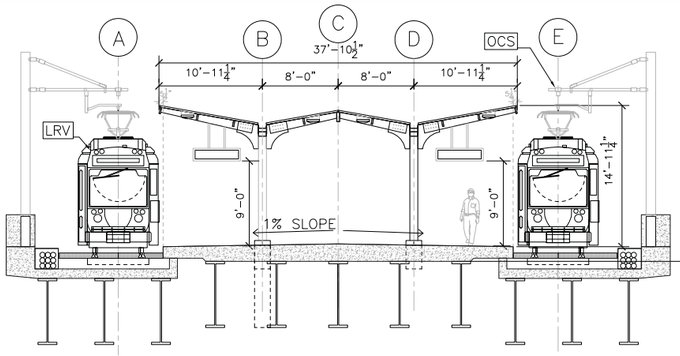


PLATFORM CANOPY SECTION @ CL 1

SCALE: 1/8"= 1'-0"

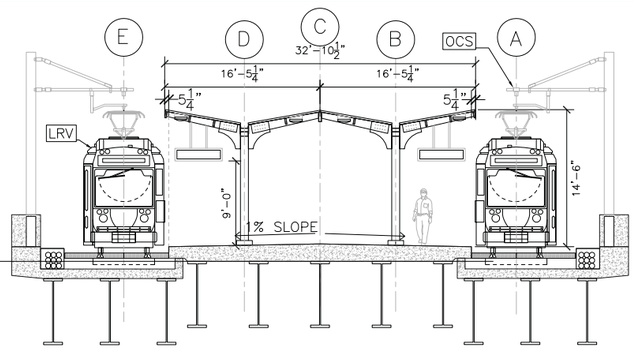


PLATFORM CANOPY SECTION @ CL 23

SCALE: 1/8"= 1'-0"

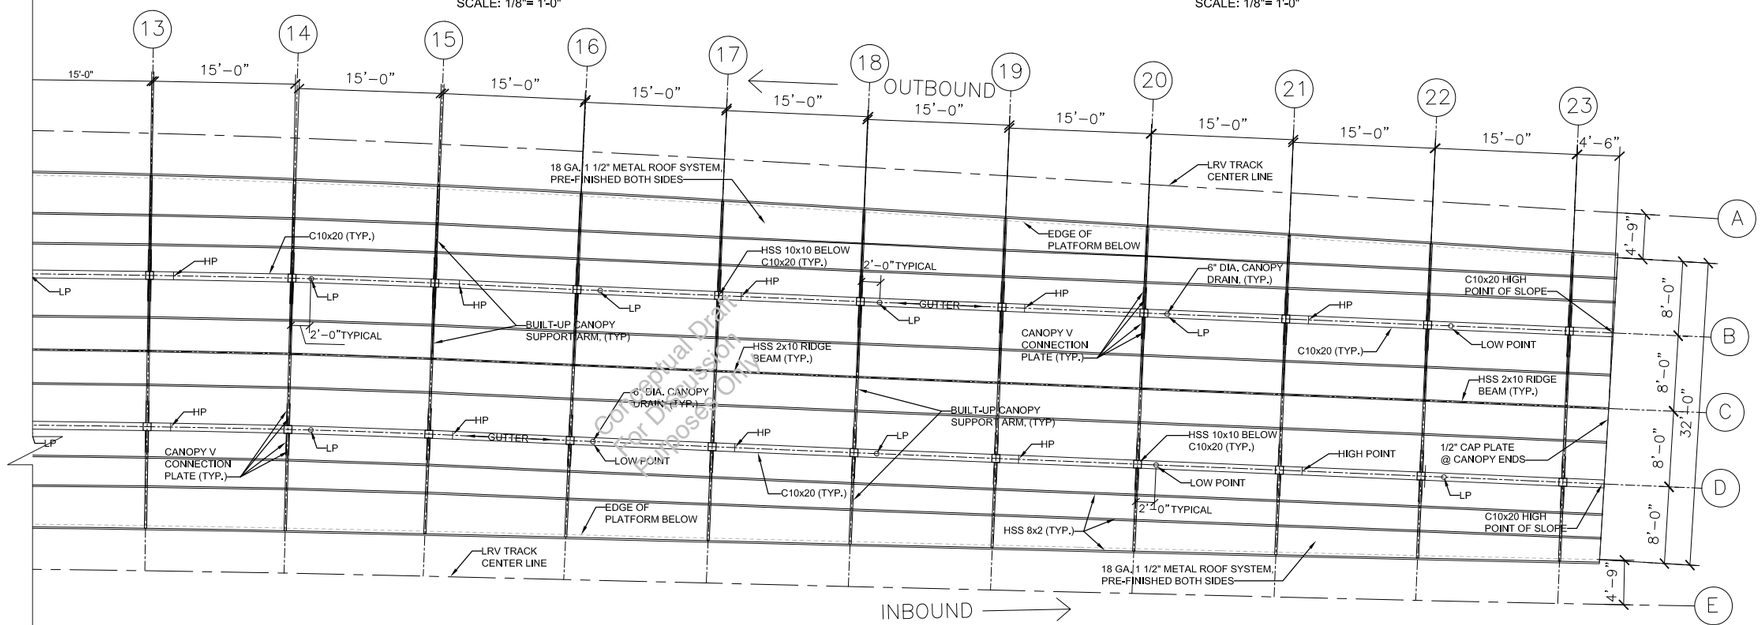

PLATFORM CANOPY PLAN - PART 2

SCALE: 1/8"= 1'-0" TYPE 4 DATE: 7-31-17

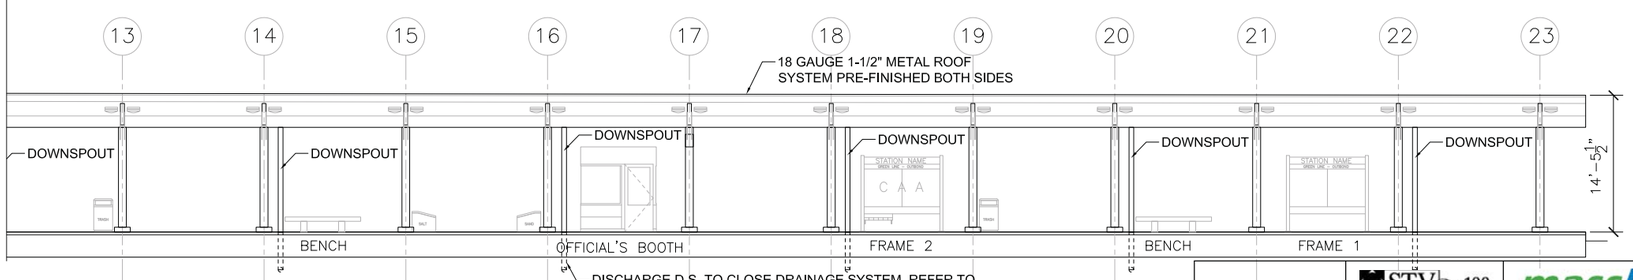

PLATFORM CANOPY ELEVATION - PART 2

SCALE: 1/8"= 1'-0" TYPE 4 DATE: 7-31-17

PLATFORM TYPE 4 = LECHMERE- 32'-0" to 37'-0" WIDE PLATFORM

ALL PLATFORM CANOPY STEEL SHALL BE GRADE Fy = 50 KSI

0 1' 2' 3' 4' 5'

1/8" = 1'-0"

8

Conceptual Drawing
Not for Design or Construction
Purposes Only

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


LECHMERE STATION PART 2
CANOPY PLAN, ELEVATION AND SECTIONS
- ADDITIVE OPTION 1

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-278.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	ND	SHEET: OPT1-06	·

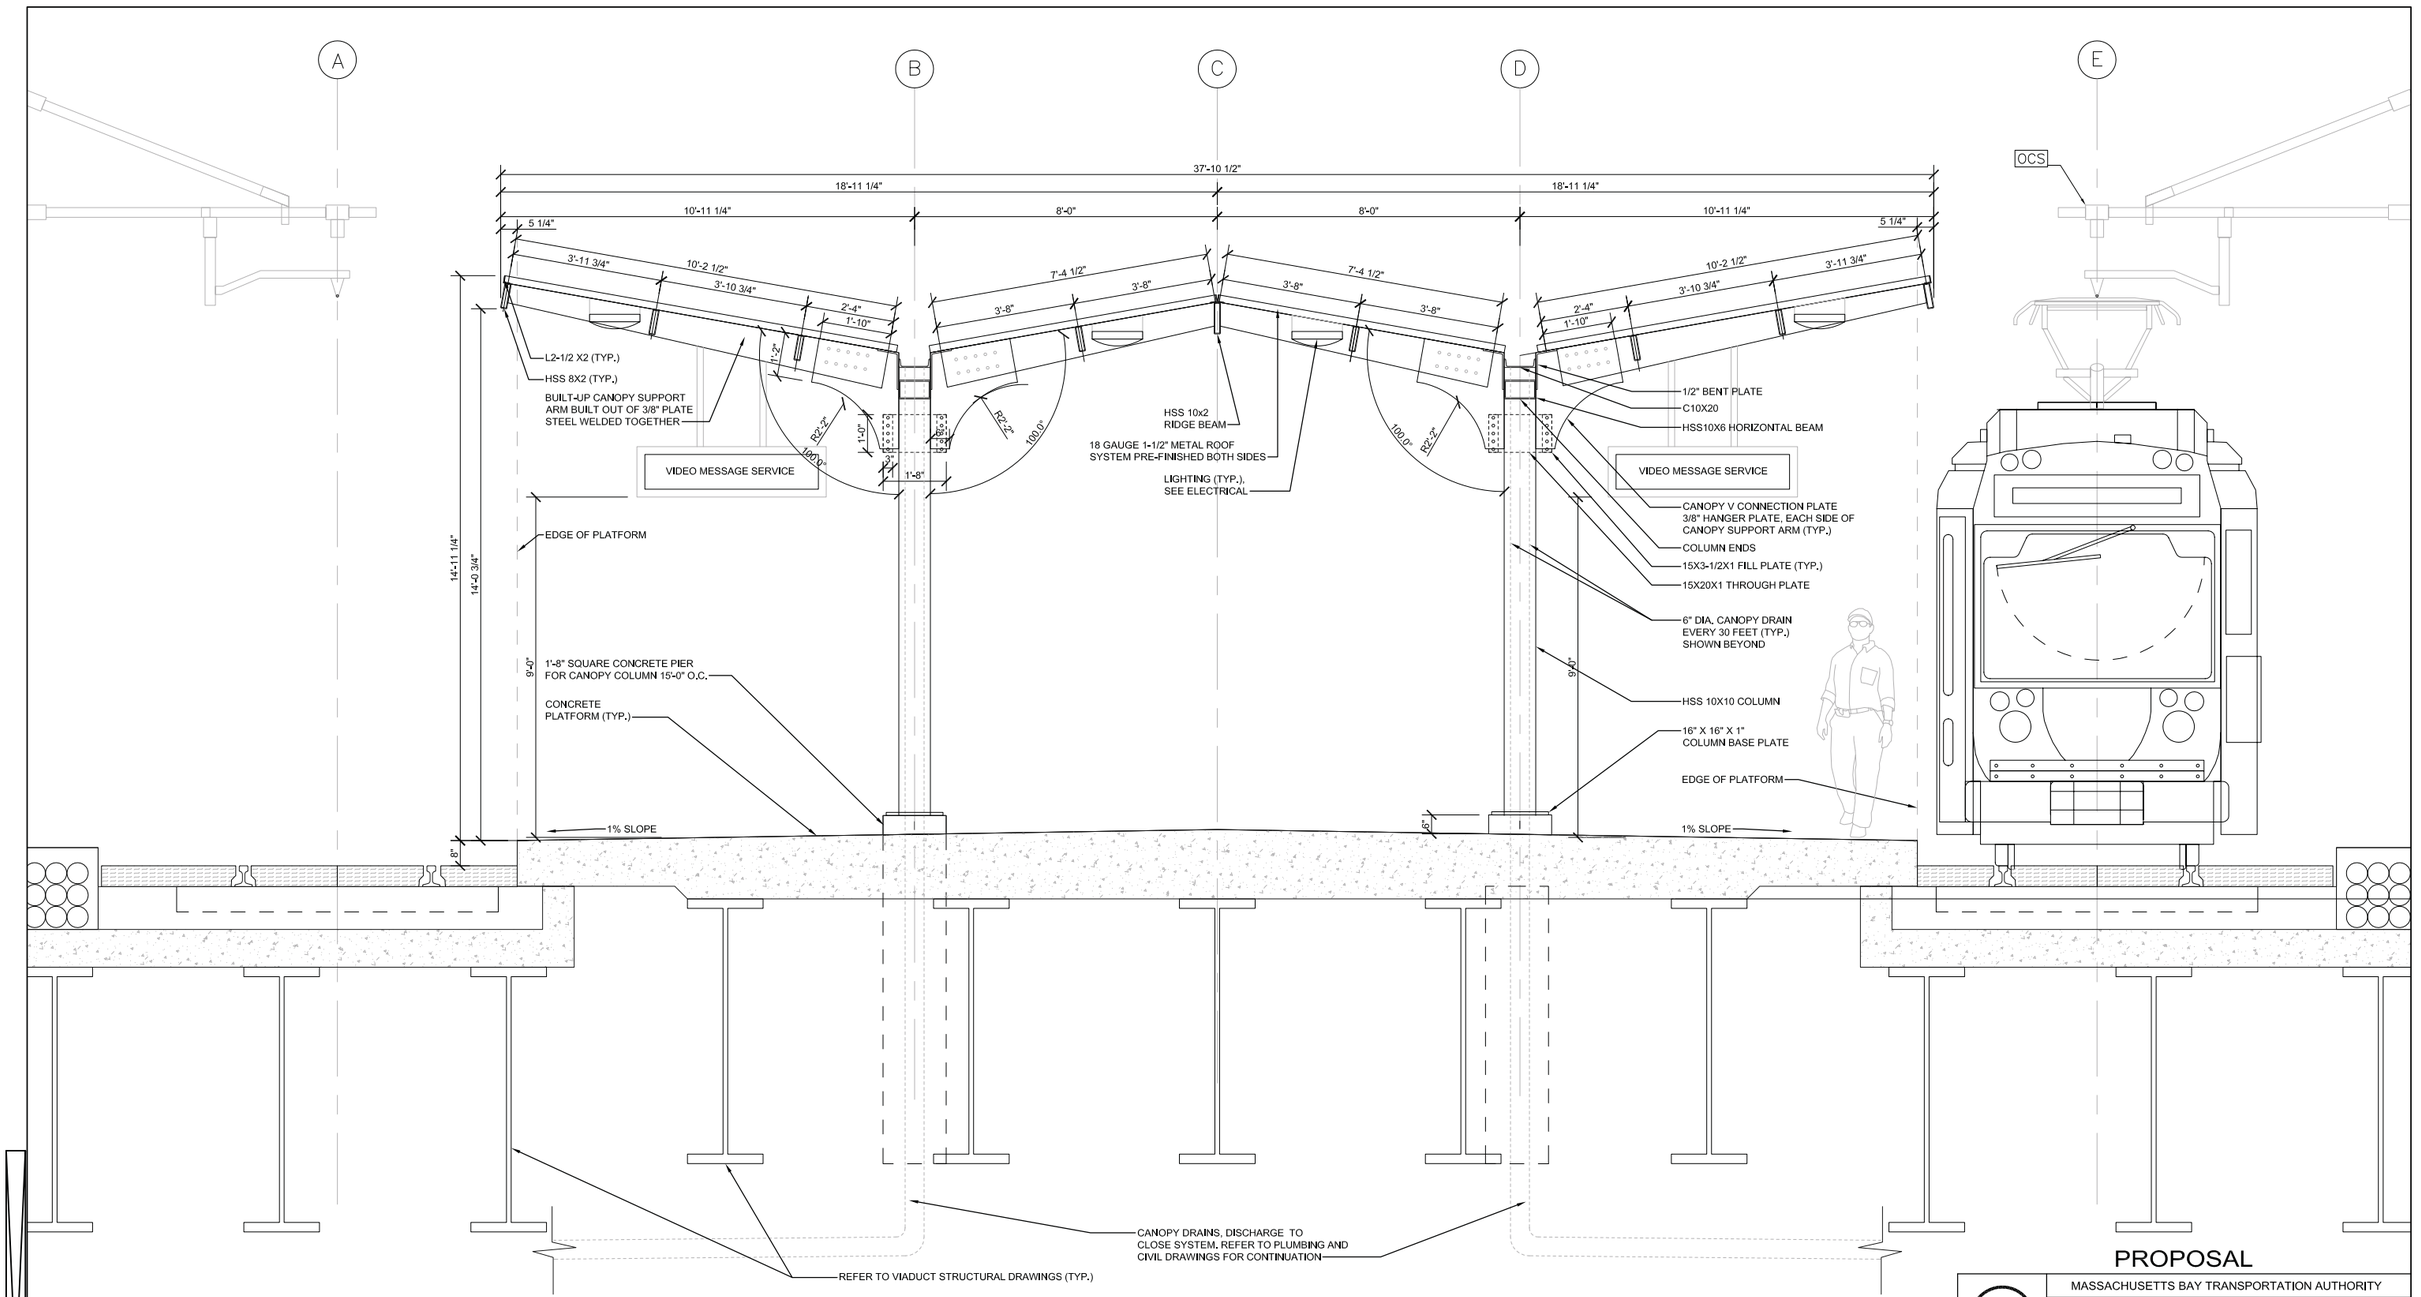

PLATFORM CANOPY SECTION @ CL 1

SCALE: 1/2"= 1'-0" TYPE 4, DATE: 7-31-17

PLATFORM TYPE 4 = LECHMERE- 32'-0" to 37'-0" WIDE PLATFORM

ALL PLATFORM CANOPY STEEL SHALL BE GRADE Fy = 50 KSI

0 1' 2' 3' 4' 5'

1/2" = 1'-0"

9

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


LECHMERE STATION
CANOPY SECTION @ COLUMN LINE 1
- ADDITIVE OPTION 1

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-278.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	ND	SHEET: OPT1-07	·

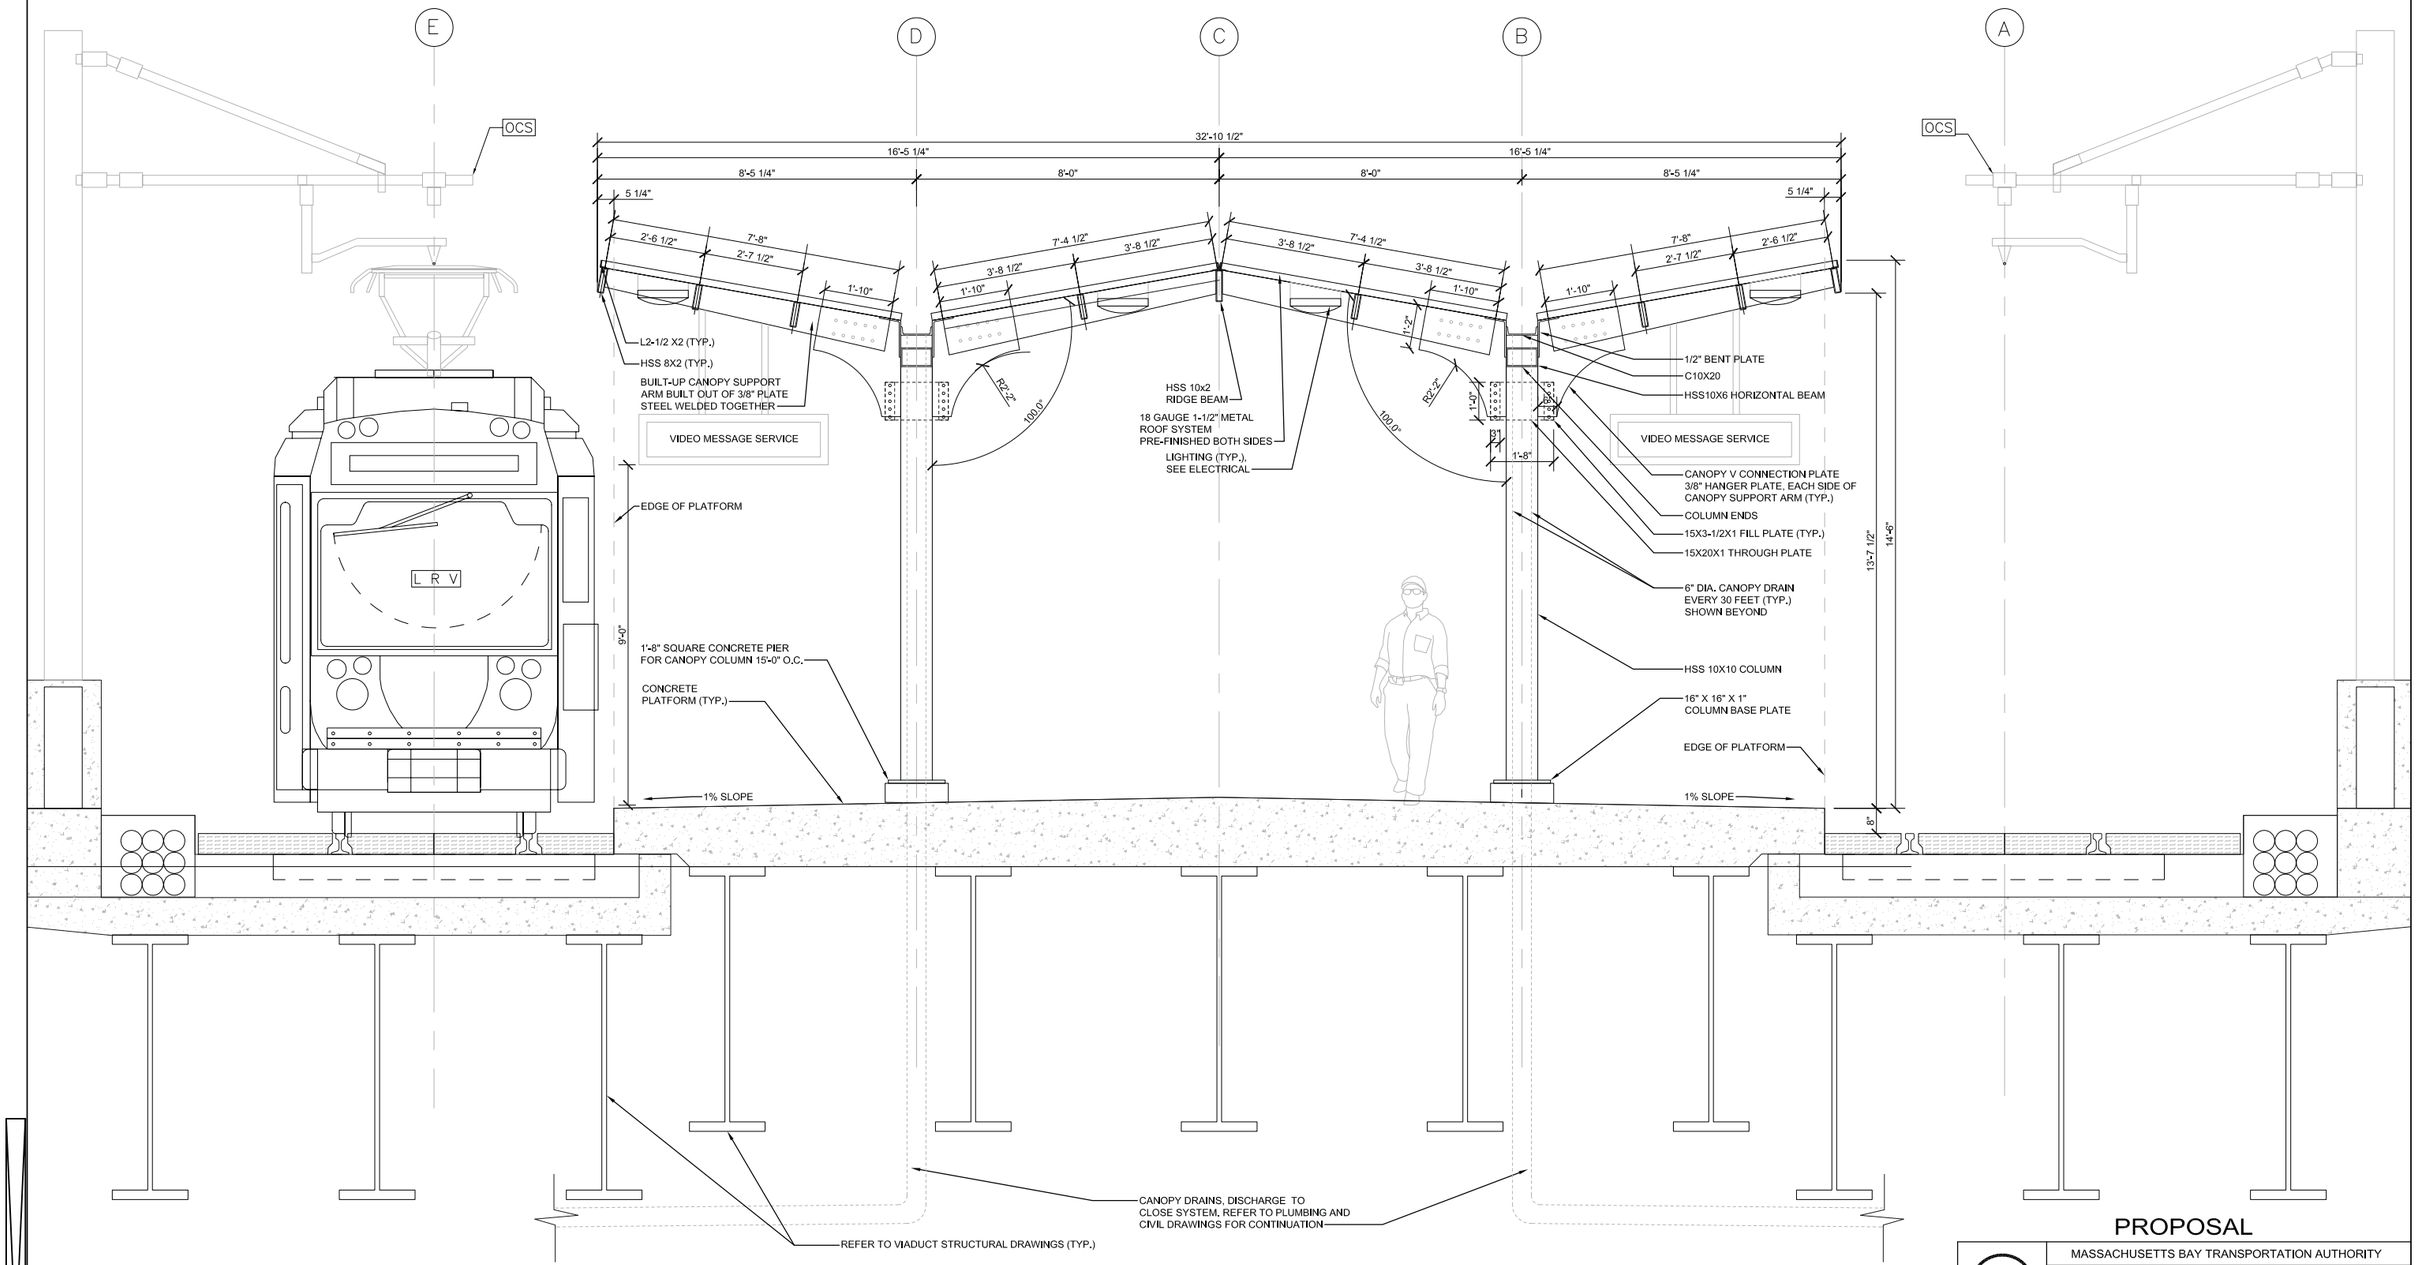

PLATFORM CANOPY SECTION @ CL 23

SCALE: 1/2"= 1'-0" TYPE 4, DATE: 7-31-17

PLATFORM TYPE 4 = LECHMERE- 32'-0" to 37'-0" WIDE PLATFORM

ALL PLATFORM CANOPY STEEL SHALL BE GRADE Fy = 50 KSI

0 1' 2' 3' 4' 5' 1/2" = 1'-0"

10

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

PROPOSAL


MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

LECHMERE STATION
CANOPY SECTION @ COLUMN LINE 23
- ADDITIVE OPTION 1


GV20170258-278.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	PDS	PDS	ND	SHEET: OPT1-08	·

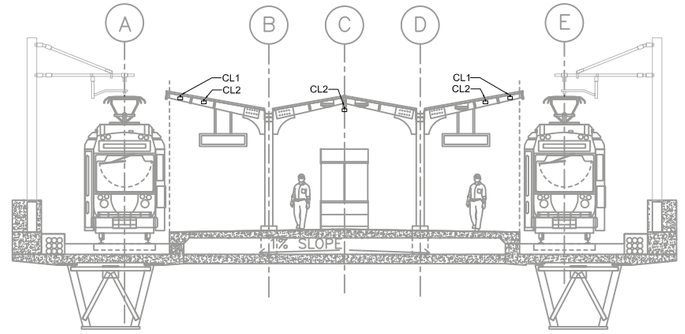

LECHMERE STATION CANOPY LIGHTING SECTION

1/8"=1'-0" 0 4' 8' 16'

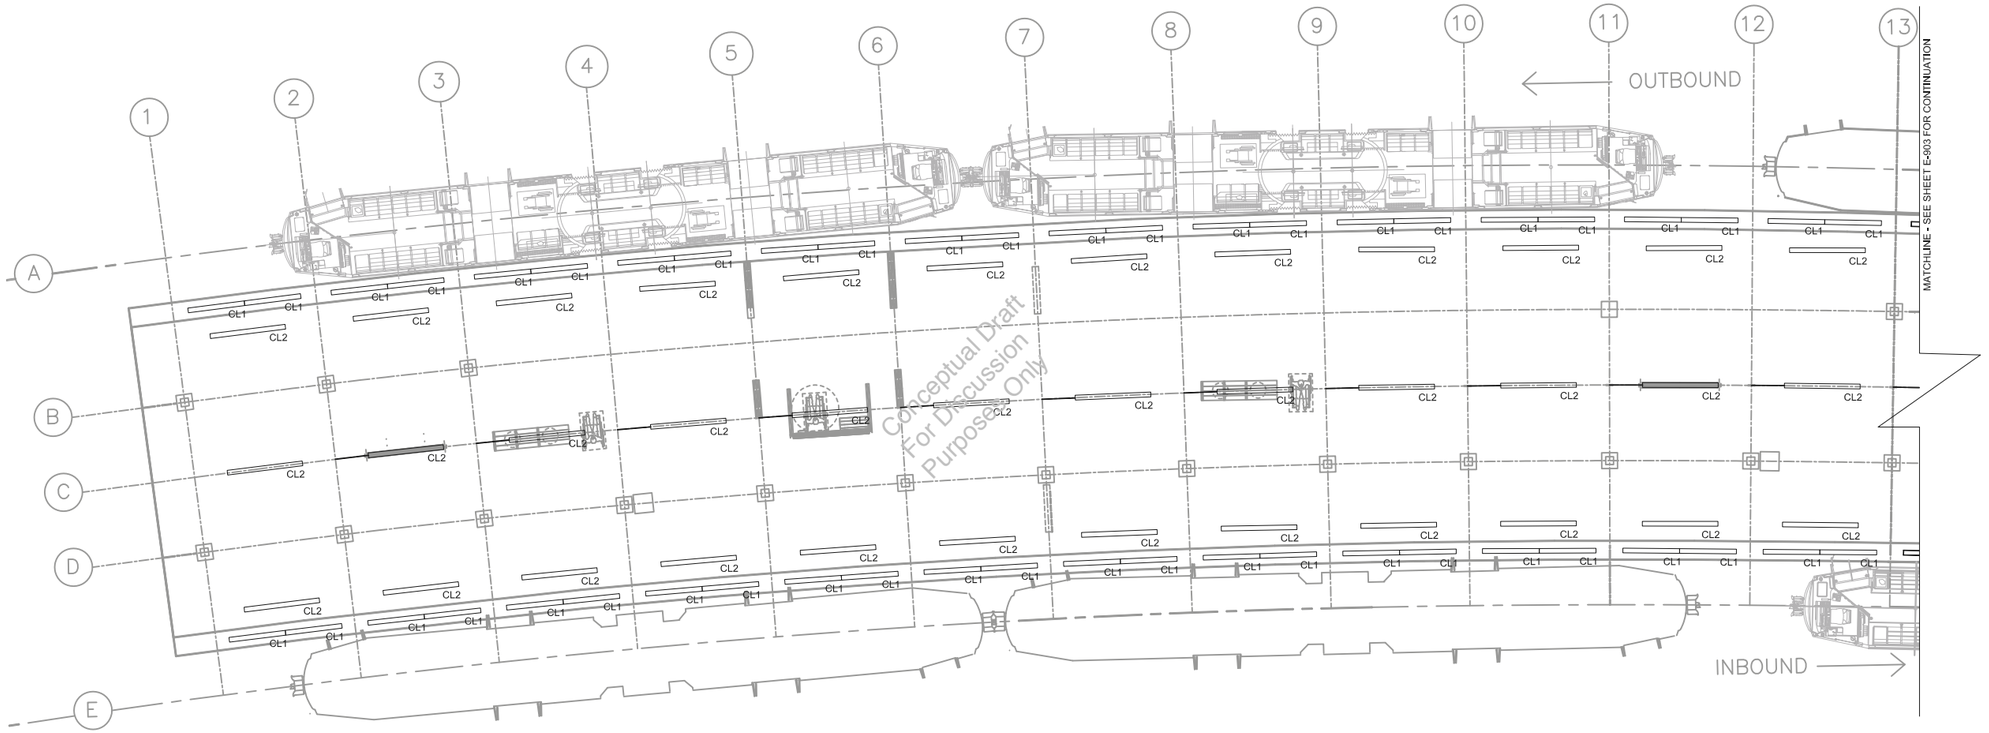

LECHMERE STATION

LECHMERE STATION CANOPY LIGHTING PLAN

1/8"=1'-0" 0 4' 8' 16'

LIGHTING FIXTURE SCHEDULE

FIXTURE TYPE	MANUFACTURER	CATALOG NUMBER	DESCRIPTION	MOUNTING	LAMP TYPE	VOLTAGE	LAMP WATTS	NOTES
CL1	FORUM	AQD-36-125LED30-SAT-H2.5"X6-UNV-SV	WET LOCATION RECTANGULAR LUMINAIRE	PENDANT	LED	120-277	75	MOUNT APPROX. 14'-0" FROM BOTTOM OF LIGHT FIXTURE
CL2	FORUM	AQD-36-125LED30-SAT-H2.5"X8-UNV-SV	WET LOCATION RECTANGULAR LUMINAIRE	PENDANT	LED	120-277	100	MOUNT APPROX. 13'-2" FROM BOTTOM OF LIGHT FIXTURE

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


LECHMERE STATION
CANOPY LIGHTING PLAN SHEET 1 OF 2
- ADDITIVE OPTION 1

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-278.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	AR	AR	ND	SHEET: OPT1-09	.

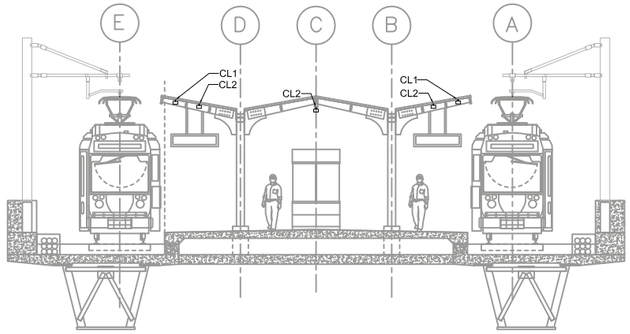

LECHMERE STATION CANOPY LIGHTING SECTION

1/8"=1'-0" 0 4' 8' 16'

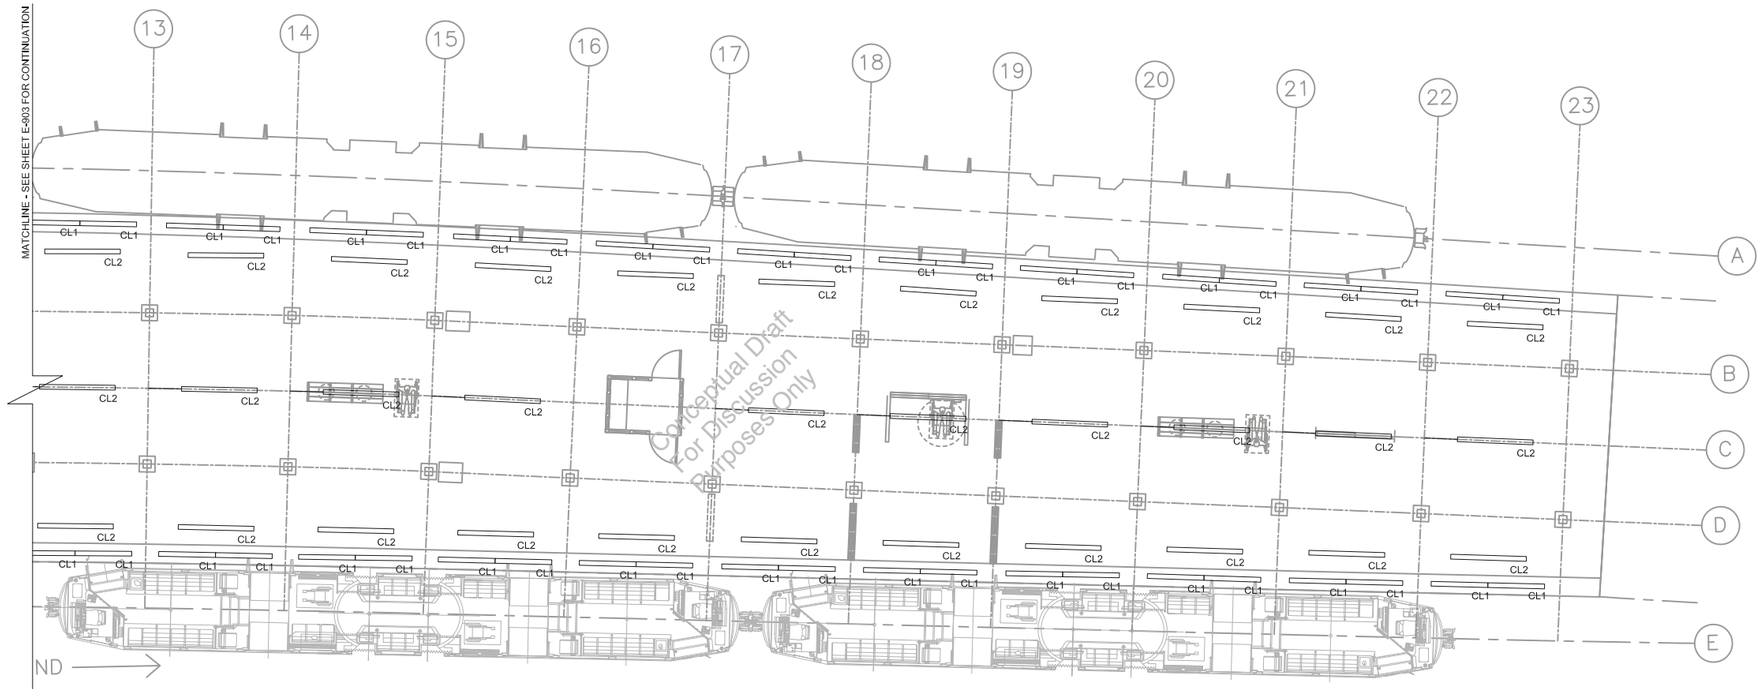

LECHMERE STATION CANOPY LIGHTING PLAN

1/8"=1'-0" 0 4' 8' 16'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

LECHMERE STATION
CANOPY LIGHTING PLAN SHEET 2 OF 2
- ADDITIVE OPTION 1

ISSUE	DATE	DESCRIPTION	BY	CHKD	APP.

GV20170258-278.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	AR	AR	ND	SHEET: OPT1-10	.

2. DESIGN AND CONSTRUCTION OF ELEVATORS TO STATIONS PROPOSED FOR NEW/ADDITIONAL ELEVATORS

2.A GENERAL APPROACH AND LOCATION-SPECIFIC DESIGNS

This additive option provides commuters with a different type of means of egress from the RFP base requirements, including:

- Alternatives for accessing and exiting particular stations in the way of additional means of egress to and from the station.
- A second means of egress from a different direction or level.

All of the additive options draw from our base design proposal drawings. This allows us to match and maintain the aesthetic style and materials that are being proposed under our proposed design approach while minimizing the impact to the base design if the additive option means of egresses are incorporated into one or all of the stations in question, reducing cost. For example, we utilized the same layout and concept for the additional elevator at Magoun Station that is reflected in our base proposal plans for College Station. This approach addresses all criteria under Sections 12 and 14 of Volume 2, Technical Provisions, because we have taken into consideration the space, dimensions, structural, architectural, and projected MEP requirements, and therefore, we are not reinventing the wheel. We applied this approach to all the additive options means of egress being considered.

“All of the additive options draw from our base design proposal drawings. This allows us to match and maintain the aesthetic style and materials that are being proposed under our proposed design approach while minimizing the impact to the base design if the additive option means of egresses are incorporated into one or all of the stations in question, reducing cost.

The following subsections correspond with the additive options listed under Volume 3 – Addendum Number. 9; 3.2.2. Additive Option Item 2: Elevators.

Lechmere Station North Headhouse. Under the base proposal, the entire elevator shaft construction, including foundations, structural steel framing, CMU walls and glass curtain walls, roof assembly, penthouse ventilation (in wall fixed louvers), and entrance canopies top and bottom are provided in the design. The elevator control room, located in the supporting headhouse facility, is sized for the additional elevator already. Circulation leading to and from the elevator doors at the street and station levels are already taken into account in the base design floor plans.

Incorporating the additional elevator at the Lechmere Station North Headhouse has little or no impact on the Technical Provisions. Other than specifying the actual elevator cab and hoisting equipment, which would be exact to the other two elevators programmed for this station as part of the base proposal, all of the infrastructure and shaft is accounted for under the base design proposal drawings.

Additional HVAC will need to be provided in the elevator control room, but this is minimal. Even though an additional elevator is being proposed, the electrical service for the station does not need to be upgraded from a 600 amp service. There is no additional lighting required. A minimal amount of additional wayfinding signage will be required.

Gilman Square Station. This additive option substitutes a second stairway and elevator in lieu of the emergency covered exit switchback ramp system under the base RFP. However, the second stairway and elevator would be located on the east side of the School Street Bridge as opposed to the ramp system on the west side of the School Street Bridge. Our interpretation of the additive option description indicates the MBTA intends to use the second stairway and elevator as a second means of egress to enter and exit the station as opposed to the ramp being used only as an emergency exit.

The layout and arrangement of support spaces, including crash walls, has essentially been rotated 180 degrees and mirrors the Main Station Headhouse floorplate and arrangement. The layout, as shown on the proposal drawings, also takes into account the possible extension of the station platform in the future to 300 feet. The stairs are covered over its entire run and extends 5 feet beyond the last riser at the top and bottom per the RFP criteria. Canopy extensions have also been provided over the elevator door opening top and bottom per the RFP.

Incorporating the second set of stairs, elevator, and support spaces (essentially second Station Headhouse) has little or no impact on the Technical Provisions, since it is replacing a structure that encompasses a much larger footprint. Additional HVAC will need to be provided since a second elevator control room is required.

Since an additional elevator is being proposed the electrical service for the station will need to be upgraded from 400 amps under the base RFP to a 600 amp service. There is additional lighting required but is less than provided for the emergency ramp system so it may be considered awash.

A minimal amount of additional wayfinding signage will be required since it will be used as a second station entrance/exit. An additional fare collection machine (ticket vending) was not called for as part of the additive options, but can be discussed and addressed with the MBTA if this additive option is exercised.

Note: ATC 36 – Raised Community Path has been approved by the MBTA. The ATC has a direct impact on the main station entrance/exit to and from Gilman Square under the based RFP proposal. However, it does not impact in any way the substitute elevator and stair headhouse additive option presented.

Magoun Square Station. This additive option calls for an additional elevator to be provided adjacent to the base proposal elevator location. To comply with the adjacency criteria, and as previously mentioned above, we utilized the same layout and concept that is reflected in our base proposal plans for College Station. Both elevator doors will be facing one another and will share a common covered enter/exit landing area (top and bottom) in accordance with the RFP criteria. The additional elevator will have its own elevator control room. The

structural foundation, framing, and elevator shaft construction mirrors what we are proposing under our base proposal for College Station.

Incorporating the second elevator and support spaces will have a minimal impact on the Technical Provisions. The base floorplate of the Station Headhouse will have to be elongated in order to fit a second elevator and elevator control room at the station platform level. However, additional foundations, structural framing for the shaft construction, as well as glass curtain walls, CMU, and crash walls will be required along with additional roof assembly.

Additional HVAC will need to be provided since a second elevator control room is required. Since an additional elevator is being proposed, the electrical service for the station will need to be upgraded from 400 amps under the base RFP to a 600 amp service. There is additional lighting required but it is minimal. Additional wayfinding signage will be required, but again it's envisioned to be minimal.

Ball Square Station. Ball Square Station is an at-grade station. This additive option is to provide a stairway and elevator off of the Broadway Street Bridge leading down to the Station platform level. It will provide commuters with a second means of egress to enter and exit the station. We interpret the additive option criteria to mean that the stairs and elevator are not to replace or substitute the main at-grade (track crossing) station entrance under the base RFP. Again, keeping with the same aesthetics and style architecture, we will use the same concept and layout as shown for the Gillman Square Station substitute 2nd stair and elevator headhouse Additive option for Ball Square Station is only rotating it 180 degrees. However, unlike the School Street Bridge, where the span is in parallel with the entrance to the elevator and stairs at Gilman Square Station, the Broadway Bridge span is skewed. This will require a short triangular elevated walkway plaza to be provided between the bridge and the stairs/elevator headhouse at Ball Square Station, which our proposal drawings show.

Incorporating a second means of egress in the way of a set of stairs, elevator, and support spaces will have a minimal impact on the Technical Provisions, mainly since the headhouse, which encompasses all of these elements, will be located southeast and away from the at-grade station platform area and as close to the Broadway Street Bridge as possible to keep the length and size of the aforementioned triangular elevated walkway plaza to a minimum. However, in doing so, its impact is felt once reaching the station platform level. An open roof corridor is now being created between the stairs/elevator and the actual station platform requiring crash walls to be provided on either side where they were not required before, since the station was considered an at-grade station. Additionally, the stand alone building services building cluster, which is comprised of the electrical, communications and EFM rooms, fall within the footprint of the aforementioned corridor. This will require the structural roof framing of these spaces to be more robust to handle the crash wall loads imposed on them.

In addition to the above, foundations and structural framing for the elevator shaft construction, as well as glass curtain and CMU walls, will be required along with additional roof framing and assemblies for both stairs and elevator. Structural steel framing and concrete deck will be required for the elevated walkway plaza. HVAC will need to be provided, since an elevator does not exist. Additional lighting and wayfinding signage will be required, but they both will be localized. Since there is only one elevator being proposed, the electrical service for the station does not need to be upgraded from 400 amp service.

Changes from the Technical Proposal

The proposed Addition of Elevators to Stations Proposed for New/Additional Elevators does not require any deviation from the requirements of the Technical Proposal.

2.B SCHEDULE IMPACT ASSESSMENT


GLX Constructors' efforts to support this additive option, as described, are minimal and will not impact the proposed schedule.

2.C ELEVATORS DRAWINGS

The drawings provided show graphically, and in more detail, what is described above for all of the additive options under this section.


As with our base proposal, the design of any and all additive options under this section will include and address all criteria and requirements set forth under Sections 12 and 14 in Volume 2 – Technical Provisions of the RFP.

ITP Request	RFP	
	Drawing Number	Drawing Title
C2.0	OPT2-01	Overall Plans And Headhouse Sections – Additive Option 2
C2.0	OPT2-03	Platform, Headhouse Plans and Section – Additive Option 2
C2.0	OPT2-05	Overall And Walkway Plans – Additive Option 2

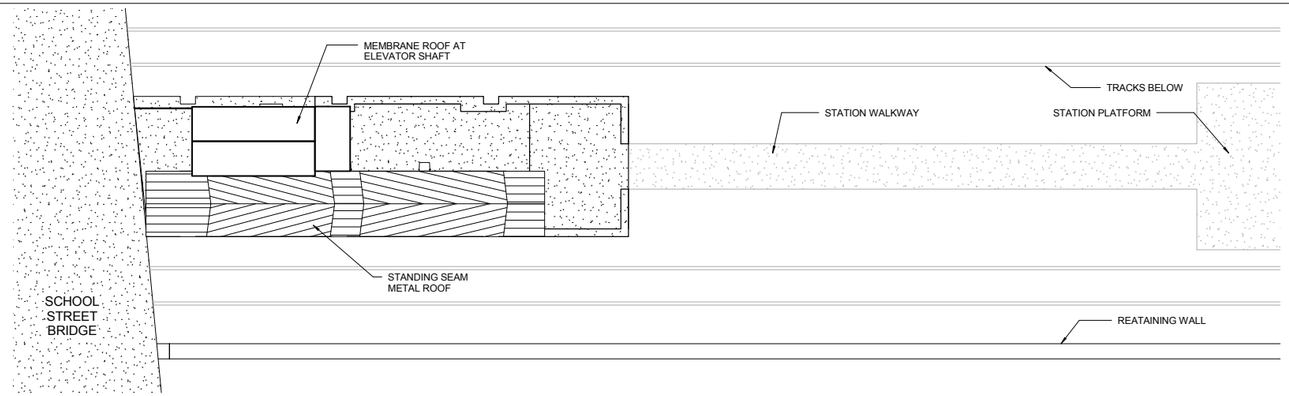


SCHOOL STREET HEAD HOUSE - ENTRY LEVEL

1" = 10'-0"

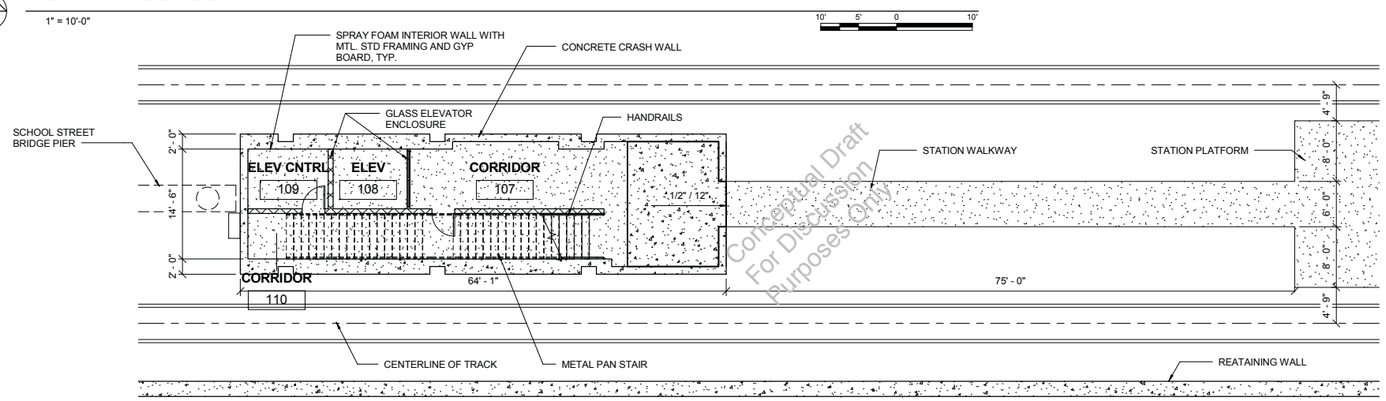


SCHOOL STREET HEAD HOUSE - PLATFORM LEVEL

1" = 10'-0"

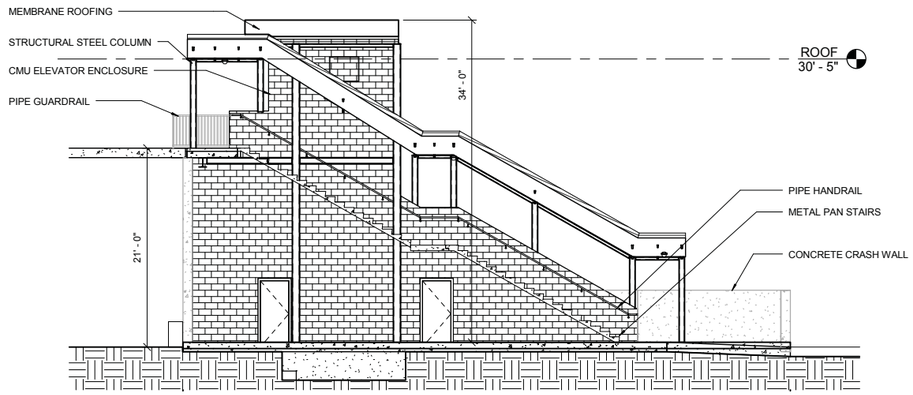

SCHOOL STREET HEAD HOUSE - SECTION

1/8" = 1'-0"

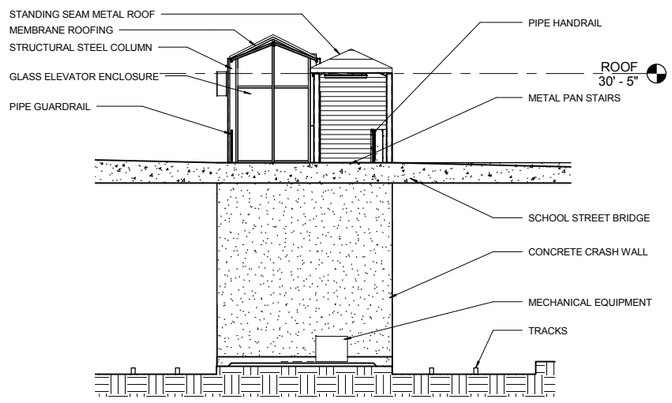

SCHOOL STREET HEAD HOUSE - TRANSVERSE SECTION

1/8" = 1'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


GILMAN STATION
OVERALL PLANS & HEADHOUSE SECTIONS - ADDITIVE OPTION 2

GLX CONSTRUCTORS

GV20170258-279.pdf


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: OPT2-01	.

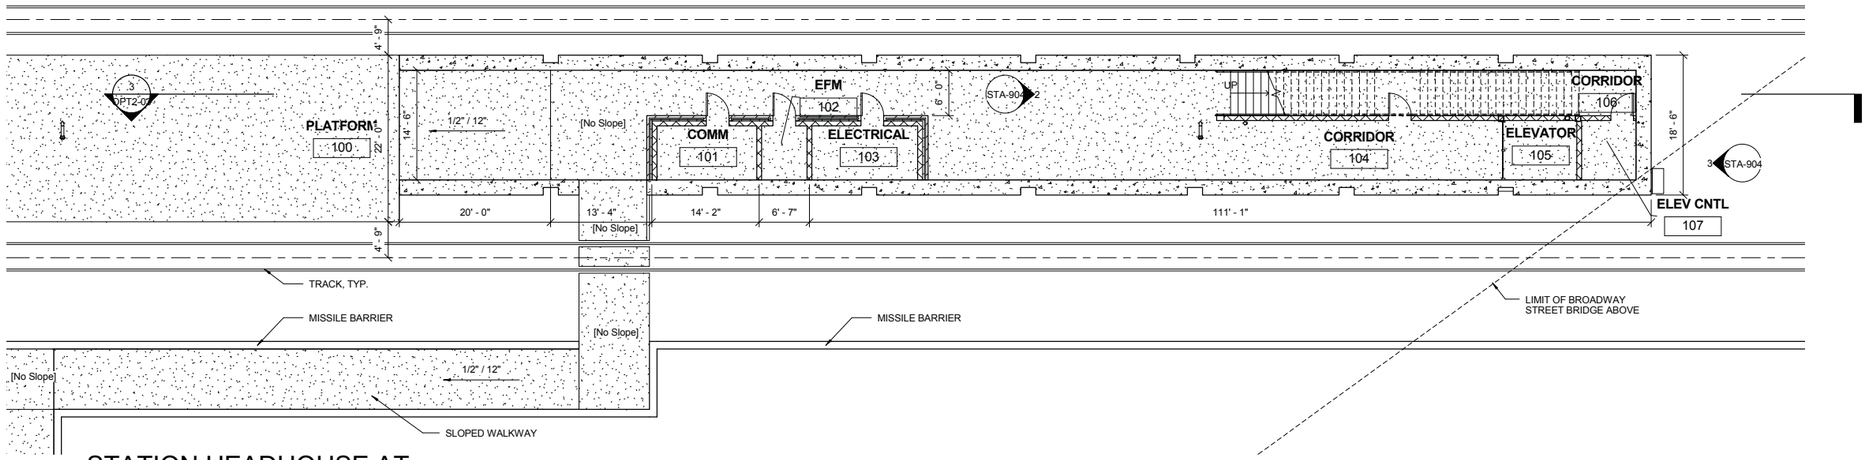

STATION HEADHOUSE AT PLATFORM LEVEL


1" = 10'-0"

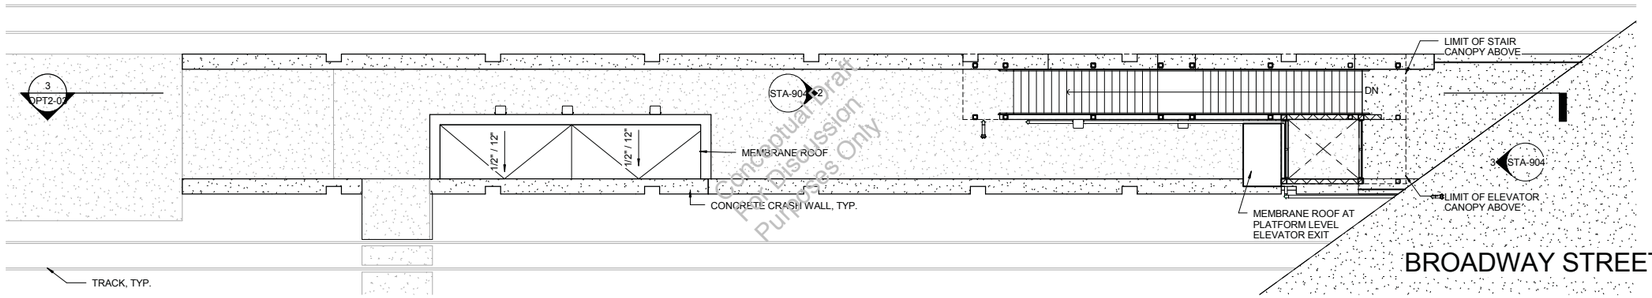

Conceptual Draft
For Discussion
Purposes Only

STATION HEADHOUSE AT STREET LEVEL

1" = 10'-0"

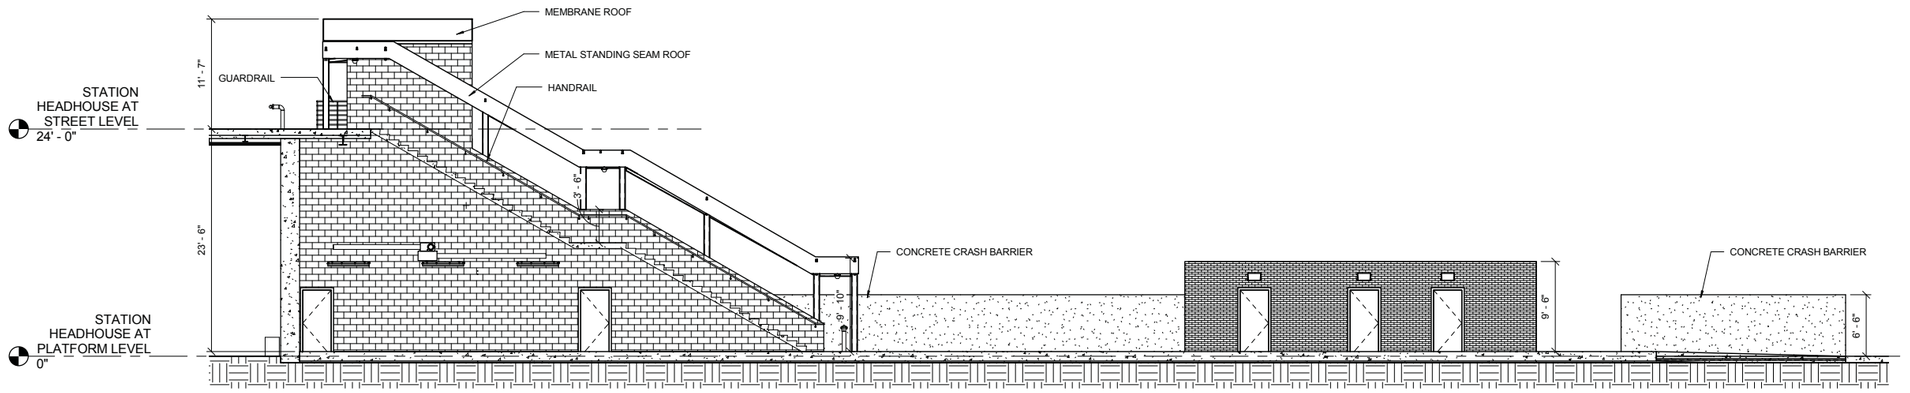

LONGITUDINAL SECTION

3 OPT2-03

1/8" = 1'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY


GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

BALL STATION
PLATFORM, HEADHOUSE PLANS & SECTION
- ADDITIVE OPTION 2

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-279.pdf


SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: OPT2-03	.



OVERALL PLAN AT PLATFORM LEVEL

1" = 30'-0"


30' 15' 0 30'



OVERALL PLAN AT STREET LEVEL

1" = 30'-0"

30' 15' 0 30'

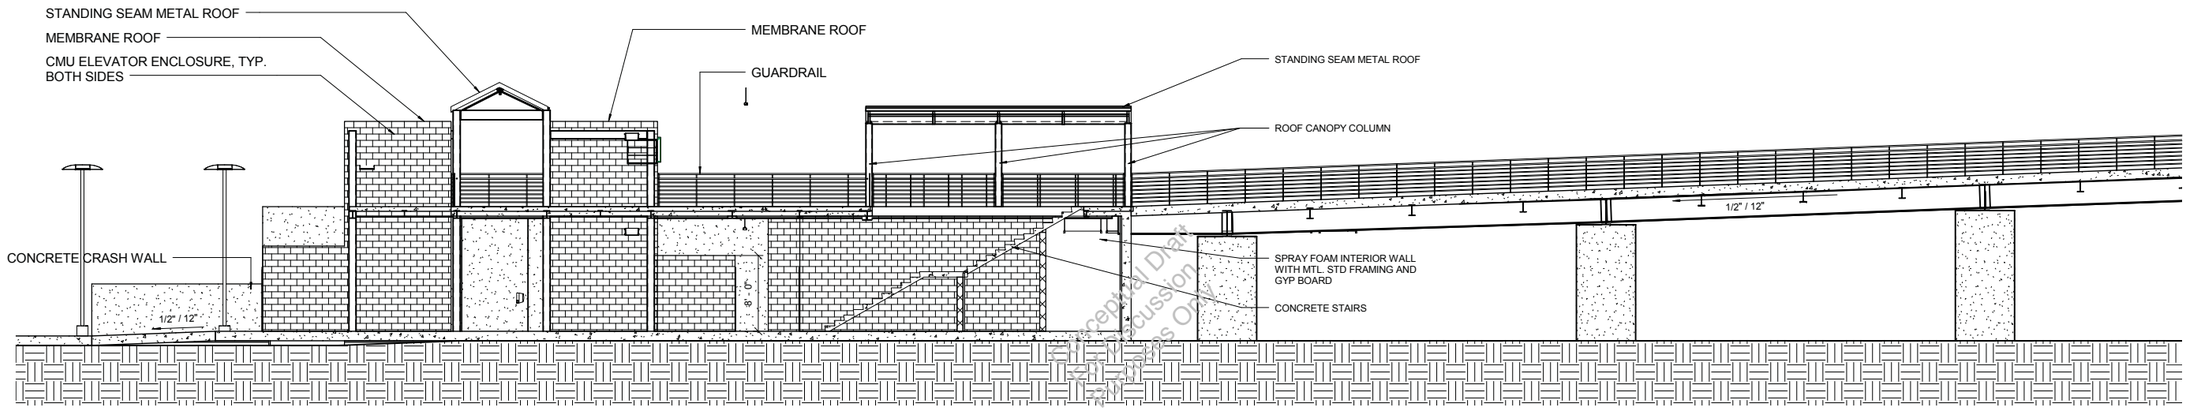

Not Accepted / Draft
Not for Construction
For Discussion Only

LONGITUDINAL SECTION

3 / STA-906

1/8" = 1'-0"

0 4' 8' 16'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

MAGOUN STATION OVERALL, WALKWAY PLANS AND SECTION - ADDITIVE OPTION 2

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-279.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: OPT2-05	.

3. INCLUSION OF AN ART PROGRAM

3.A GENERAL APPROACH AND LOCATION-SPECIFIC DESIGNS

The inclusion of an art program on the Green line Extension provides the following benefits to the Project:

- Enhance visual interest
- Improve the user experience
- Integrate with the community
- Offer enjoyment to the neighborhood
- Unify the system
- Differentiate the station

For many years, the MBTA has promoted the inclusion of meaningful artwork into station and system-wide design to foster an approachable and pleasant environment for the commuting public. Many people spend more than a short time commuting to and from work during the week, passing through, or spending time in these facilities. The MBTA recognizes the importance of the experience and the enhancement of travel for this population. In addition, they recognize that for those who live in the communities where these stations are, there should be a commitment to improving and enriching the environs and creating a relationship between the station, artwork, and community.

Artwork Integration

It is understood that the art should be integrated into the stations. In order for it to be integrated, it cannot be an afterthought, and the process of working with an artist should begin as soon as possible. Investigating the opportunities for incorporation should be made throughout the elements of the station and also explored throughout the areas of the passenger experience leading up to the station. Each of the various stations have opportunities for integration of artwork, and while this can be an opportunity to unify the entire system, it also needs to differentiate each place, each station.

Working with the Artist, the MBTA and the Contractor

The MBTA's arts budget is for enhancement of essential station elements such as fences, wall surfaces, and screening panels and includes only the cost differential between the underlying element and the artist-enhancement. The budget allowance is for the designer, artist and builder to design the incorporation of the artwork, coordination, and fabrication of the artwork and the installation. It also includes any necessary lighting, power, drainage, or infrastructure associated with the piece.

Because of the integral nature of the artwork, the artist and the concept need to be selected as early in the process as possible in order to work directly with our team to guide and influence the overall incorporation of artwork into the station design. Because there are seven stations, decisions will need to be made early on as to what might be incorporated as station-unifying features and what might be incorporated as station-specific.

The artwork will need to comply with the safety, accessibility, durability, and maintenance requirements of other elements of the stations. The artwork must be durable, vandal-resistant, and require no additional maintenance as well as conform to the MBTA standards of resilience, indestructibility, and preservation.

There are three phases indicated to be included in the project schedule and described in Figure 3-1.

PHASE 1 ARTWORK FEASIBILITY CONFIRMATION	PHASE 2 FINAL DESIGN AND FABRICATION	PHASE 3 ARTWORK INSTALLATION
▸ Confirm feasibility of artwork ▸ Approval of concepts ▸ Review for technical compliance ▸ Review for budgetary compliance ▸ Submittal of comments to MBTA regarding technical issues and solutions ▸ Submittal of budget confirmation and indications of cost savings measures ▸ Work with artist if needed to reduce costs	▸ Design and fabrication of artwork ▸ Technical submittal of 2-D drawings ▸ Technical submittal of engineering drawings ▸ Calculations for structural elements ▸ Specifications for artwork over and above station structures ▸ Response to technical reviews at preliminary, intermediate, release for construction submittals, and log of comments and responses	▸ Coordinate the installation of work with the artist ▸ Fabricate and install the artwork ▸ Coordinate with artist for inspection of work ▸ Punch List of artwork

Figure 3-1. Project Schedule Phases. *These phases allow time for concept approvals, technical reviews, budget adherence, design, fabrication, and installation.*

Stations

As noted above, possibilities and opportunities present themselves at each station. The RFP lists possible and anticipated elements that may lend themselves to integral or added artwork. All stations in the RFP have listed the possible treatment of fences, screens, porcelain enamel panels, site elements, retaining walls, glazing, lighting, ceilings, tile wall surfaces, or other features. Because many of these features are similar among stations, they might become a way of unifying the stations using artwork. For example, all stations include bike cages, and most of them are of a very large scale. A similar way of treating the elements of the bike cage (color, material, caging) creatively would be one way to include interest, artwork, and a pleasant experience.

Although there are many features that are similar at each station, they each also have character, elements, and layouts that provide diverse opportunities for artwork. The plans and elevations of the stations suggest unique possibilities for each station:

College Station. The pedestrian bridge from College Avenue to Boston Avenue and College Station is an excellent opportunity for integrated artwork. Not only are people passing along the bridge, but the bridge can be viewed from both College Avenue and Boston Avenue. Enhancement of the essential elements of railings, barriers, and landings could include the incorporation of artwork. The bridge's entrance and arrival points could feature interesting elements, as well such as elements cast into paving.

The long expanse of missile barrier type fencing could be rethought of as integrated artwork element. Its entire length is not only viewed by automobiles and pedestrians along Boston Avenue, but also by people waiting on the platform and by passengers within the trains.

Other opportunities exist within or on the outside of the headhouse containing the vertical transportation elements. The stretch of masonry or concrete walls housing the utility rooms, as well as the fencing (missile barrier) on the second level provide occasions for artwork integration. Areas that open up through two levels could experience art from two levels.

Ball Square. Potential at this station exists along the long processional to the platform that could celebrate arrival to and departure from the station. Either or both sides of the sloped pathway to the platform would allow introduction of artwork along the way or along the right of way fence. Artwork in this area would not only enhance the user experience but should be developed to be seen from Broadway, as well as the entry point on Boston Avenue, thus enlivening what would otherwise remain a graveled expanse.

The back wall of the traction power substation prominently presents itself to the station platform as the right-of-way fence. This wall would be a fine canvas for many different types of art, which could be directly incorporated into the building material, not just applied to the building.

This is similar to the Wellington Carhouse Project that GLX Constructors' Lead Designer, STV, recently completed design on. The Carhouse, another utilitarian building, is immediately adjacent to the Wellington subway platform. The use of colorful metal panels and textured precast concrete panels gives a nod to the local river in their design, and presents an interesting face to the users of the station.

Magoun Square. Magoun Square presents opportunities for both the exterior and interior of the station. Because there is a stairway and an elevator headhouse that passes pedestrians from the upper level to the platform level below, there are interior opportunities to include artwork on the platform level wall and ceiling surfaces. The exterior of these walls, which house utility rooms, can be seen from the train and from nearby developments and the surfaces could be treated with interest to acknowledge this.



This is similar to the Wellington Carhouse Project that GLX Constructors' Lead Designer, STV, recently completed design on. The Carhouse, another utilitarian building, is immediately adjacent to the Wellington subway platform. The use of colorful metal panels and textured precast concrete panels gives a nod to the local river in their design, and presents an interesting face to the users of the station.



Gilman Station Bike Storage Facility. The large cage area on the storage facility would be an appropriate area to incorporate the proposed artwork.

The open stairway is roofed but screening materials on these open sides can be both functional (wind screens or fall barriers), beautiful, or interesting, lending themselves to art that can be transparent or open.

Gilman Square. The entry points from both School Street and Medford Street to the headhouse area of Gilman Square is both large and unobstructed enough to allow incorporation of artwork along the community path. Similar to some of the other stations the very large bike cage will also invite concepts incorporating interesting features.

The masonry walls of the lower level of the headhouse also lend themselves to treatments that would provide interest and enrichment, similarly to the Magoun Square Station.

East Somerville. The leg of the Community Path that someone will traverse on the way to this station will provide an excellent opportunity for artwork incorporation. This artwork might lend itself to integration with wayfinding, benches, fencing, plantings, or lighting to be experienced on the way to and from the platform.

Union Square Station. Union Square Station has two points of entry/departure for pedestrians and those arriving by vehicle. At-grade fencing and walls separating track areas from arriving pedestrians are opportunities for incorporation of artwork. The street connection from Union Square, while currently outside the limit of work, would also be an opportunity for incorporating artwork while offering enjoyment to the neighborhood.

Lechmere Station's two opposing headhouses will be seen from new neighboring condominium developments as well as the existing neighborhood of East Cambridge. The design should incorporate features of visual interest to both these neighboring uses. The retaining wall at the Glass Factory parking area is also viewable from both sides (condos and East Cambridge/station) and presents an excellent opportunity for artwork. Similar to the other stations with headhouses, any necessary walls and ceilings naturally lend themselves to decoration; as well the guardrails and handrails which provide opportunities to incorporate artwork that may be designed to be experienced from both levels. Uniquely, at Lechmere Station the opportunity exists to treat the soffit of the viaduct, starting perhaps with color and lighting.

Changes from the Technical Proposal

The proposed Art Program does not require any deviation from the requirements of the Technical Proposal.

3.B SCHEDULE IMPACT ASSESSMENT

GLX Constructors' efforts to support this additive option will not impact the proposed schedule.

4. DESIGN AND CONSTRUCTION OF THE COMMUNITY PATH CONNECTION TO CHESTER STREET

4.A GENERAL APPROACH AND LOCATION-SPECIFIC DESIGNS

The Chester Street Path will provide an important addition point of entry and departure for the users of the Community Path, cementing it as more than just a connection between MBTA Green Line stations, and truly as a multiuse path. From careful review of the grades, GLX Constructors prepared an ADA compliant slope from the Community Path alignment (included in the RFP) adjacent to the GLX Eastbound light rail track to the Northern corner of Chester Avenue and Cross Street. The total ramp length is approximately 330'. The ramp will be supported by a combination of solider pile and lagging walls and modular pre-cast block walls, both of which are being employed widely throughout the project. From our site visits, we noted that the Cross Street Truss Bridge has recently been reconstructed. The recent bridge work creates a number of challenges, including the need to avoid the corrugated metal bridge joint plate and concrete truss barrier. Our design will include an extended sidewalk along Chester Avenue providing additional space for passengers entering or exiting the path. This extended landing area may require relocation of the existing street light at the north corner.

This additive option compliments GLX Constructors approved ATC 36 to elevate the Community Path between School Street and Walnut Street. These combined efforts create an additional three locations for the surrounding community to access the Community Path, significantly increasing its use. These locations include access to Medford Street, Walnut Street, and Chester Avenue. This additive option also increases connections opportunities to the Somerville High School and the Somerville Public Library.

Changes from the Technical Proposal


The proposed Chester Avenue Path does not require any deviation from the requirements of the Technical Proposal.

4.B SCHEDULE IMPACT ASSESSMENT


GLX Constructors' efforts to support this additive option will not impact the proposed schedule.

4.C COMMUNITY PATH CONNECTION TO CHESTER STREET DRAWINGS

ITP Request	RFP	
	Drawing Number	Drawing Title
C2.0	OPT 4-01	Chester Avenue Connection Community Path Plan and Profile – Additive Option 4
C2.0	OPT 4-02	Chester Avenue Connection Typical Sections – Additive Option 4
C2.0	OPT 4-03	Chester Avenue Connection Retaining Wall Table – Additive Option 4

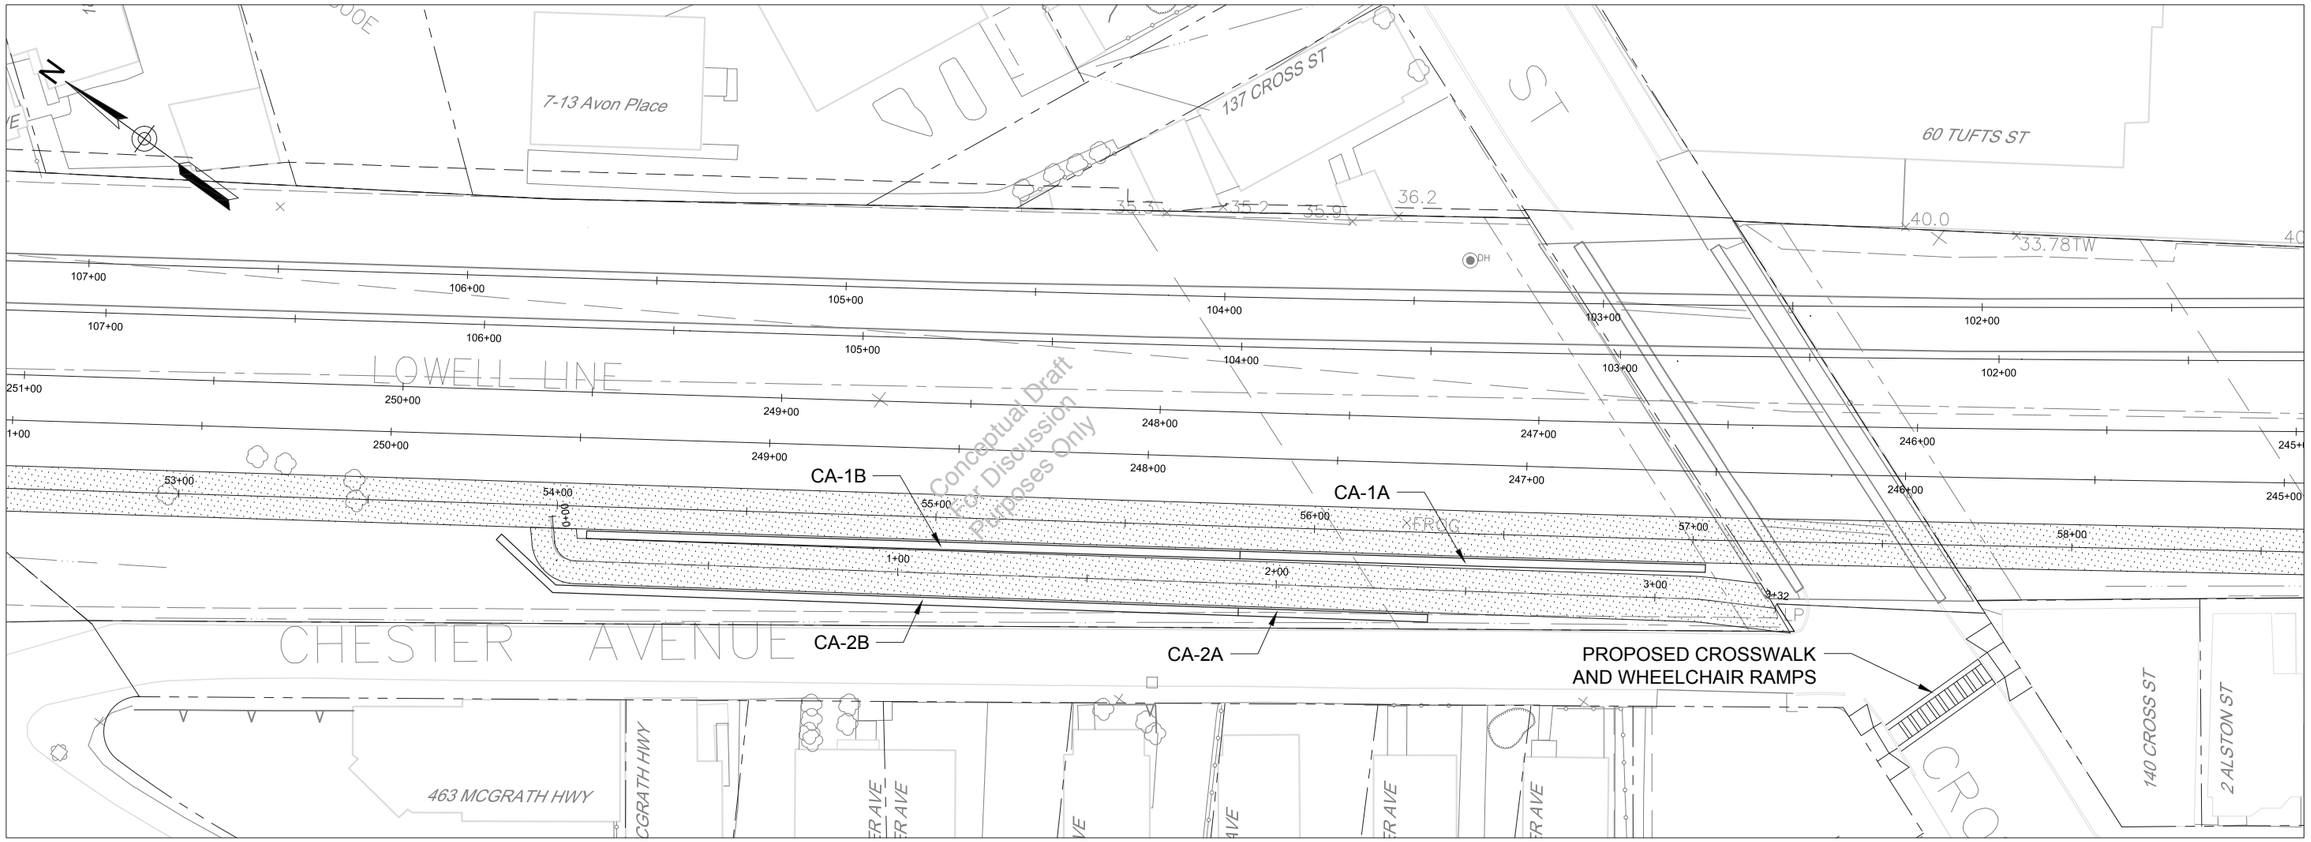

Chester Ave Community Path Profile

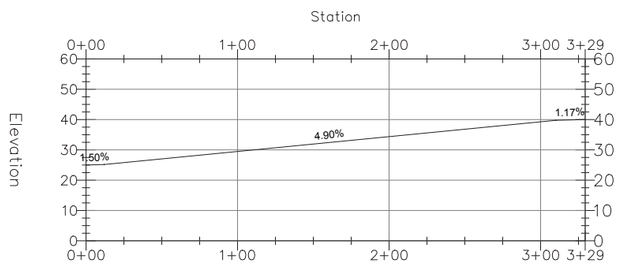

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


CHESTER AVENUE CONNECTION
COMMUNITY PATH PLAN AND PROFILE
ADDITIVE OPTION # 4

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-280.pdf

SCALE: 1"= 20'	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	BD	BD	SB	SHEET: OPT 4-01	.

PLOTTED: 09/20/17 12:46PM BY:DECKERB
DRAWING: I:\PROPOSALS\GLX\STV CAD WORKING\GLX MASTER FILES\COMMUNITY PATH\CMP-C-AP - CHESTER AVE ALTERNATE.DWG [LAYOUT2] 09/19/17 3:45PM

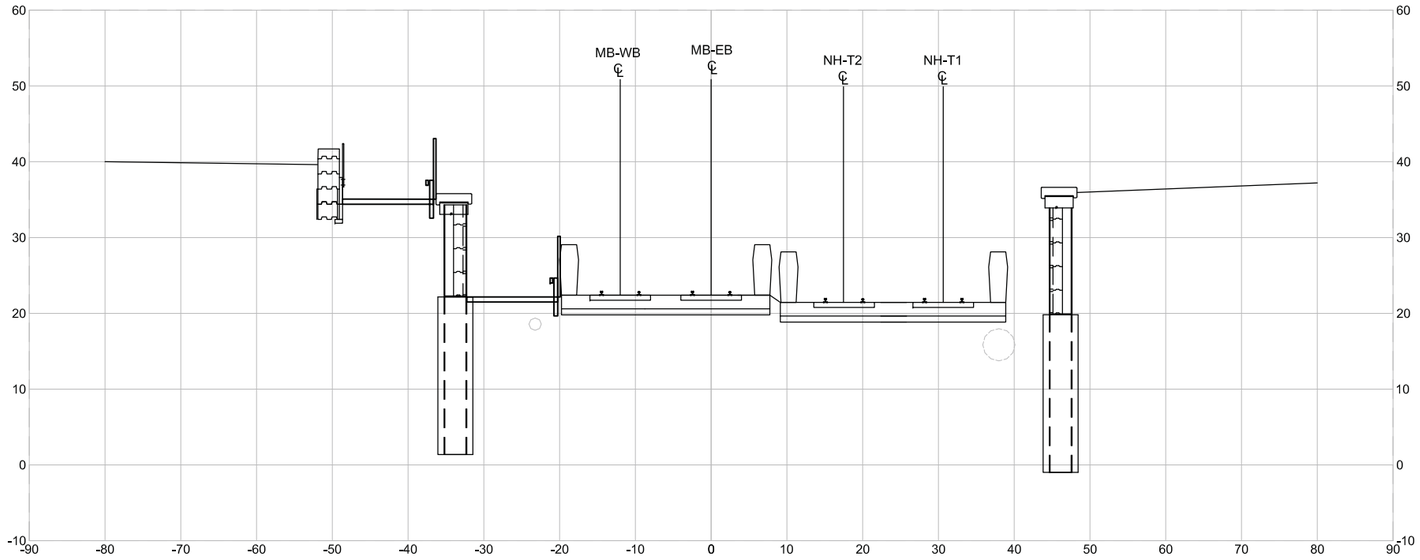

Typical Section 1

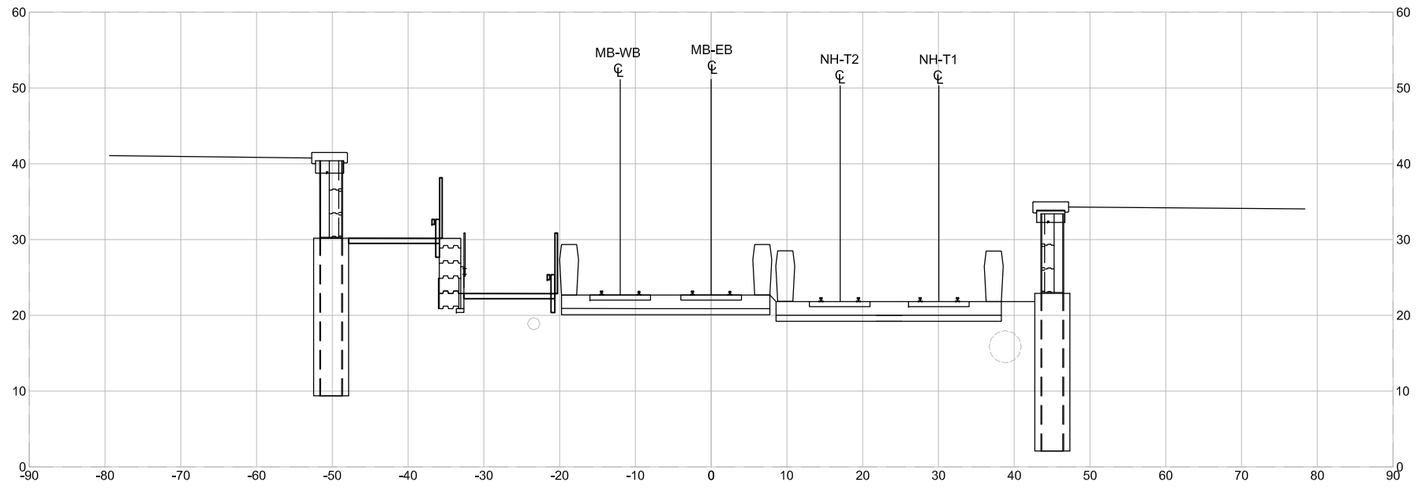

Typical Section 2

1"=10'

10' 5' 0 10'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


CHESTER AVENUE CONNECTION
TYPICAL SECTIONS
ADDITIVE OPTION # 4

GV20170258-280.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: 1"= 10'	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	BD	BD	PT	SHEET: OPT 4-02	·

PLOTTED: 09/20/17 2:47PM BY:CHAHARA
DRAWING: I:\PROJECTS\GLX\STV CAD WORKING\CIVIL 3D MODELS\GLX-CORRIDOR - CHESTER.DWG [PROPOSAL SECTIONS] 09/20/17 2:45PM

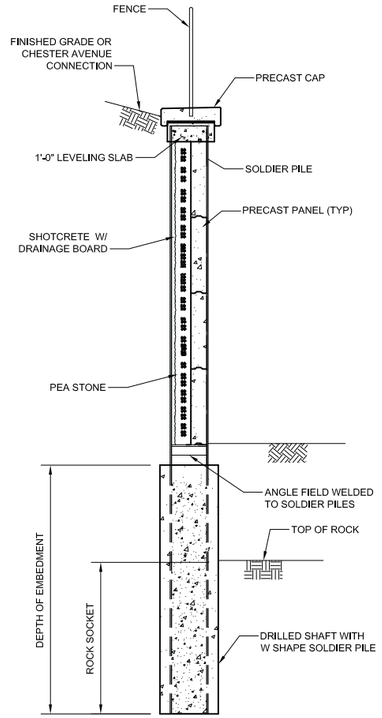


TYPICAL SOLDIER PILE AND LAGGING (SPL) WALL

1/4"=1'-0" 0 2' 4' 8'

SOLDIER PILE AND LAGGING WALL												
WALL	STATION		OFFSET (FT) FROM ME-EB	OFFSET (FT) WALL FACE-TEMP EASE	OFFSET (FT) WALL FACE-PERM EASE	PILE SIZE	PILE SPACING (FT)	SHAFT DIAMETER (FT)	EXPOSED FACE (FT)	PILE LENGTH (FT)	SOIL EMBEDMENT (FT)	ROCK SOCKET (FT)
	START	END										
CA-1A	246+50	247+50	35-37	17-20	17-20	W24x229	8	3	19	46	20	7
	247+50	247+75	35	21	21	W24x117	8	3	14	37	20	3
CA-2B	247+75	249+50	48-50	9-12	9-12	W24x229	8	3	16	45	22	7

SEE SHEET S-001 FOR SOLDIER PILE AND LAGGING WALL DETAILS.

NOTE:
CRIB WALL REPLACEMENT LIMIT FOR MCW-1 IS FROM STA. 249+50 TO STA. 251+36.
REFERENCE CRIB WALL REPLACEMENT WITH MPB SHEET S-003 FOR DETAILS.

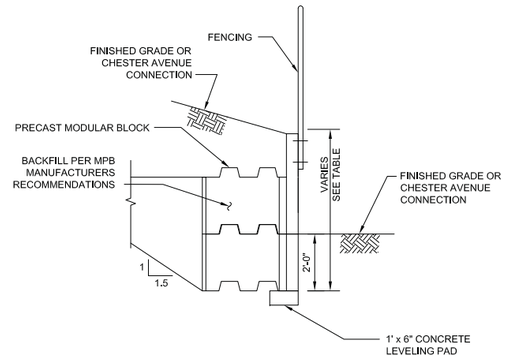

MODULAR PRECAST BLOCK WALL SECTION

3/8"=1'-0" 0 2' 4' 6'

MODULAR PRECAST BLOCK WALL				
WALL	STATION		OFFSET (FT) FROM ME-EB	TOTAL HEIGHT (FT)
	START	END		
CA-1B	247+75	248+25	32	12
	248+25	249+25	32	10
CA-2A	247+25	247+75	48	8

SEE SHEET S-003 FOR MODULAR PRECAST WALL DETAILS.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

CHESTER AVENUE CONNECTION
RETAINING WALL TABLE
ADDITIVE OPTION 4

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-280.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	DMM	DMM	JMP	SHEET: OPT 4 - 03	.

PLOTTED: 09/22/17 2:14PM BY:HARTD
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\RETAINING WALLS-NOISE WALLS_PROPOSAL DRAWINGS\OPT 4 - 03 CHESTER AVE CONN RET WALL TABLE ADDITIVE OPT

5 DESIGN AND CONSTRUCTION OF THE COMMUNITY PATH CONNECTION FROM EAST SOMERVILLE TO LECHMERE

5.A GENERAL APPROACH AND LOCATION-SPECIFIC DESIGNS

Design

Horizontal and vertical alignments of the Community Path from East Somerville Station to the existing Lechmere path segment are already constructed.

The original Community Path in this area was on a 2,200-foot-long viaduct structure that ran along the east side of the Medford Branch viaduct. Both viaducts were approximately at the same elevation and profile grade, and even shared some of the piers. It appears the Community Path was deleted from the Definition Plans due to the expense of this very long viaduct with shared piers.

Additive Option 5 requested an alternative alignment for the path from East Somerville Station to the existing Lechmere Path. GLX Constructors reviewed many concepts, and was able to develop an alignment that is a more cost efficient one than the original, while still being able to thread through the constricted corridor. The proposed path is entirely contained within the Project ROW, except for the South end that is within the Project's permanent easement. The path is partly on a viaduct structure, but is only 1,175 feet in length, approximately 1,000 feet shorter in length than the original path.

GLX Constructors' alignment starts at ground level at the existing Lechmere Path on the narrow permanent easement granted by the developer of this area. This narrow easement is the main driver of the horizontal alignment. The height of the elevated Union Square West Bound track is the main driver of the vertical alignment.

The horizontal alignment goes under the elevated US-EB; avoids the Red Bridge Traction Power Station; goes under the elevated Medford Branch; goes over the pond and retaining wall built in an advanced contract; goes over the Fitchburg line, the elevated US-WB, and the at-grade US-EB; avoids the Brick Bottom pump station; then goes north to meet the project's community path at the East Somerville Station.

The vertical alignment starts at-grade at the existing Lechmere Community Path, then goes up at an almost 5 percent grade to crest over the elevated Union Square Eastbound track. The path's profile then goes down to grade as the path travels to the path at the East Somerville Station.

The proposed path's horizontal and vertical alignments meet the requirements of the project Technical Provisions, including clearances, maximum grade, minimum curve radius, and minimum width.

Sections of the Community Path that cross the various project elements will be constructed on an elevated viaduct. The viaduct will be a ten span structure with spans varying from approximately 65 to 145 feet. The longest span, also the tallest span crosses the Fitchburg Line Tracks. For this span, we have chosen to utilize a prefabricated truss structure supported by drilled shafts and concrete pier caps. This structure type was selected to minimize disruptions to the active tracks below. The completed span can be constructed offsite and will then be lifted onto the piers, requiring only a single short duration track outage.

The deck will then be cast. Bridge rail and anti-missile fence erection will follow. As much of this work is outside of any foul areas, this work will require minimal impact to train operations and the addition of this option will have no impact on the overall project schedule.

Chester Street Paths Connection Drawings

As the approach spans descend from the main span highpoint, the path will transition and be supported between two MSE walls. The walls will begin when the path is approximately 12 feet above grade and end when it transitions to the at-grade paths connecting to the new East Somerville Station and existing Lechmere Path. MSE supported portions of the community path are shown on Figure 5-1.

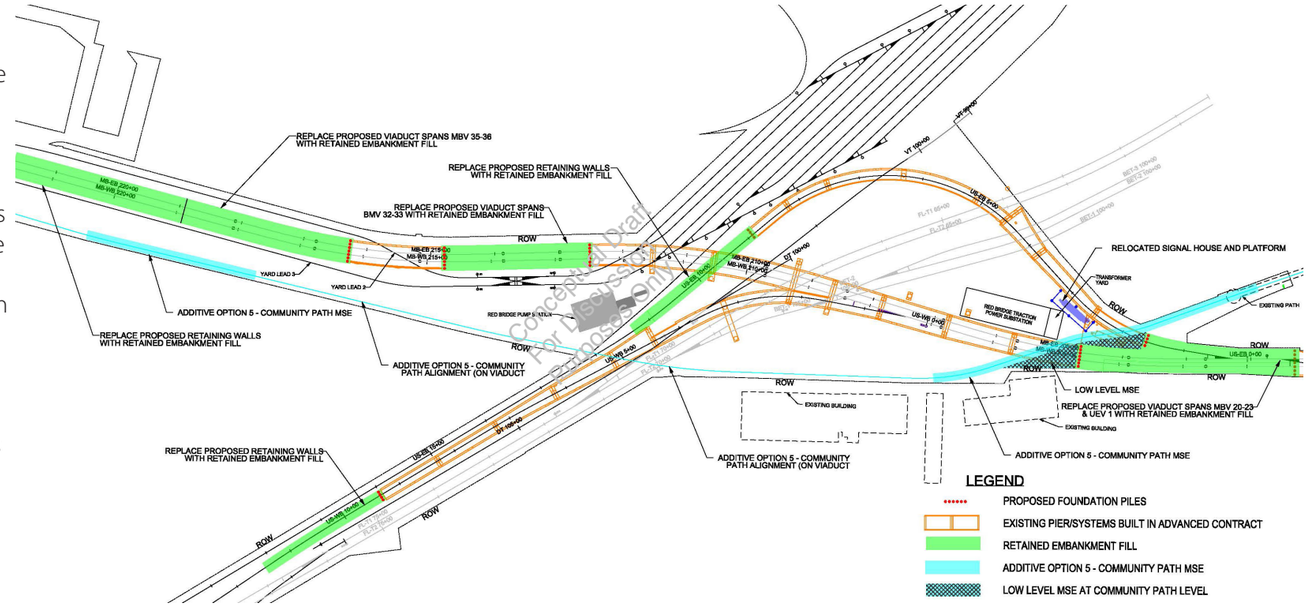


Figure 5-1. Location of MSE supported Community Path. *MSE supported Community Path guideway approved as part of ATC 35 reduces risk associated with construction of deep foundation elements and reduces long-term maintenance costs.*

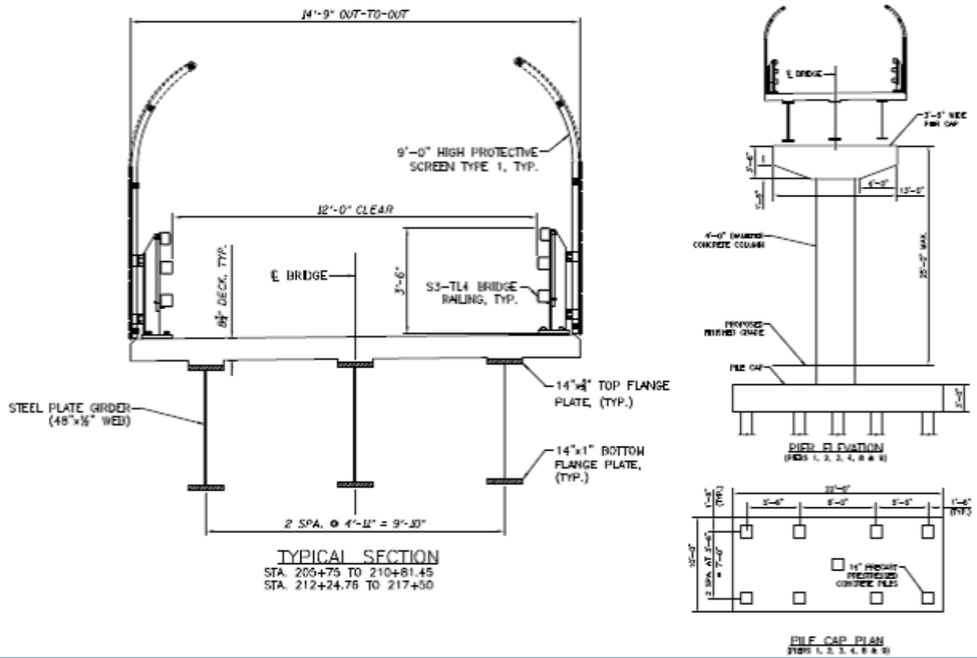


Figure 5-2. Community Path, Approach Span Superstructure Details. *The drawing above is a typical cross section of the prefabricated approach span for the community path, and a section and plan of the pier foundation that will support the approach span.*

The path will then transition from MSE walls to an at-grade segment constructed of bituminous concrete. As with all sections raised and at-grade, the Community path will be graded to provide positive drainage and will include a closed drainage system. The path will be designed to meet ADA requirements and include lighting to meet the required design criteria.

This mixed-use Community Path connection from East Somerville to Lechmere will serve walkers, bikers, and small maintenance vehicles. It will be an elevated structure less than a half-mile in length, with 1,370 feet on a MSE wall and the remaining 1,050 feet on a viaduct structure. This particular Community Path will cross over the Fitchburg Commuter Line, the Valley Line, the US-EB, the US-WB, and YL-4 between MB-EB Sta 210+00 and MB-EB Sta 212+25.

Specifically, the Community Path will cross beneath the Medford Viaduct between MB-EB Sta 203+50 and MB-EB Sta 205+50. It will be elevated on the MSE wall and will continue to MB-EB Sta 206+43.17, at which point it will transition to viaduct. The Community Path will continue on viaduct to MB-EB Sta 216+92.85. From here, it will return to MSE Wall to its touchdown point at MB-EB Sta 223+62.85. Because of the complexity of the Community Path's location, our constructability reviews hold an elevated importance to minimize any potential down time to rail services.

Construction

We understand the far-reaching impact to the MBTA and the surrounding community of closing an active railroad – even if only briefly during the non-peak hours of 10:30 am and 3:30 pm. In response, we will prefabricate the truss which will minimize the amount of time we must close the track.

On the Community Path Connection from East Somerville to Lechmere, we will begin construction at the North Point Path terminus and proceed northward. The MSE wall will be built from MB-EB Sta 200+00 to MB-EB Sta 206+43. Concurrently, we will proceed with construction on Piers 1-4.

After completing the MSE wall from MB-EB Sta 200+00 to MB-EB Sta 206+43, we will construct an MSE wall from MB-EB Sta 223+63 to MB-EB Sta 217+00. We will complete Piers 5-8 concurrently with the MSE wall construction.

After Abutment 1 and Piers 1-4 are complete, steel girder erection can proceed for Span 1-4, and we will begin to construct Piers 5-8. Likewise, when we complete Abutment 2 and Piers 5-8, we will proceed with the steel girder erection for Span 6-9.

In the case of Span 5, we will design, fabricate, assemble, and erect the span as a truss in lieu of bridge girder spans. By taking this approach, we can set Span 5 in one pick instead of many picks, resulting in significantly less interference with railroad operations. We have determined that the ideal time to erect the Span 5 truss would be between 7:30 p.m. and 5:30 a.m., during which commuter operations are at their least for the day.



Our construction team is well-versed in accelerating construction to avoid rail closures. On the Utah I-15 CORE Highway Design Build Project, GLX Constructors' Team Members used Accelerated Bridge Construction (ABC) to expedite the schedule. Under this ABC method, four bridges were constructed on the side of I-15. With the use of a remote-controlled, self-propelled modular transporter, the bridges were swiftly moved into place overnight, allowing for only a single-night full freeway closure—without affecting the safety or travel times of motorists using the interstate.

Changes from the Technical Proposal


The proposed Community Path Connection does not require any deviation from the requirements of the Technical Proposal.

5.B SCHEDULE IMPACT ASSESSMENT

The GLX Constructors' planned effort to support this additive option will not impact the proposed schedule.

5.C COMMUNITY PATH CONNECTION FROM EAST SOMERVILLE TO LECHMERE DRAWINGS


ITP Request	RFP	
	Drawing Number	Drawing Title
C2.0	OPT 5 – 01	Community Path Viaduct General Plan – Additive Option 5
C2.0	OPT 5 – 02	Community Path Viaduct Typical Sections – Additive Option 5
C2.0	OPT 5 – 03	Community Path Viaduct Pier Details – Additive Option 5
C2.0	OPT 5 – 04	ATC 35-MSE Plan View – Additive Option 5
C2.0	OPT 5 – 05	Community Path Plan and Profile – Additive Option 5
C2.0	OPT 5 – 06	Community Path Plan and Profile – Additive Option 5
C2.0	OPT 5 – 07	Community Path Plan and Profile – Additive Option 5

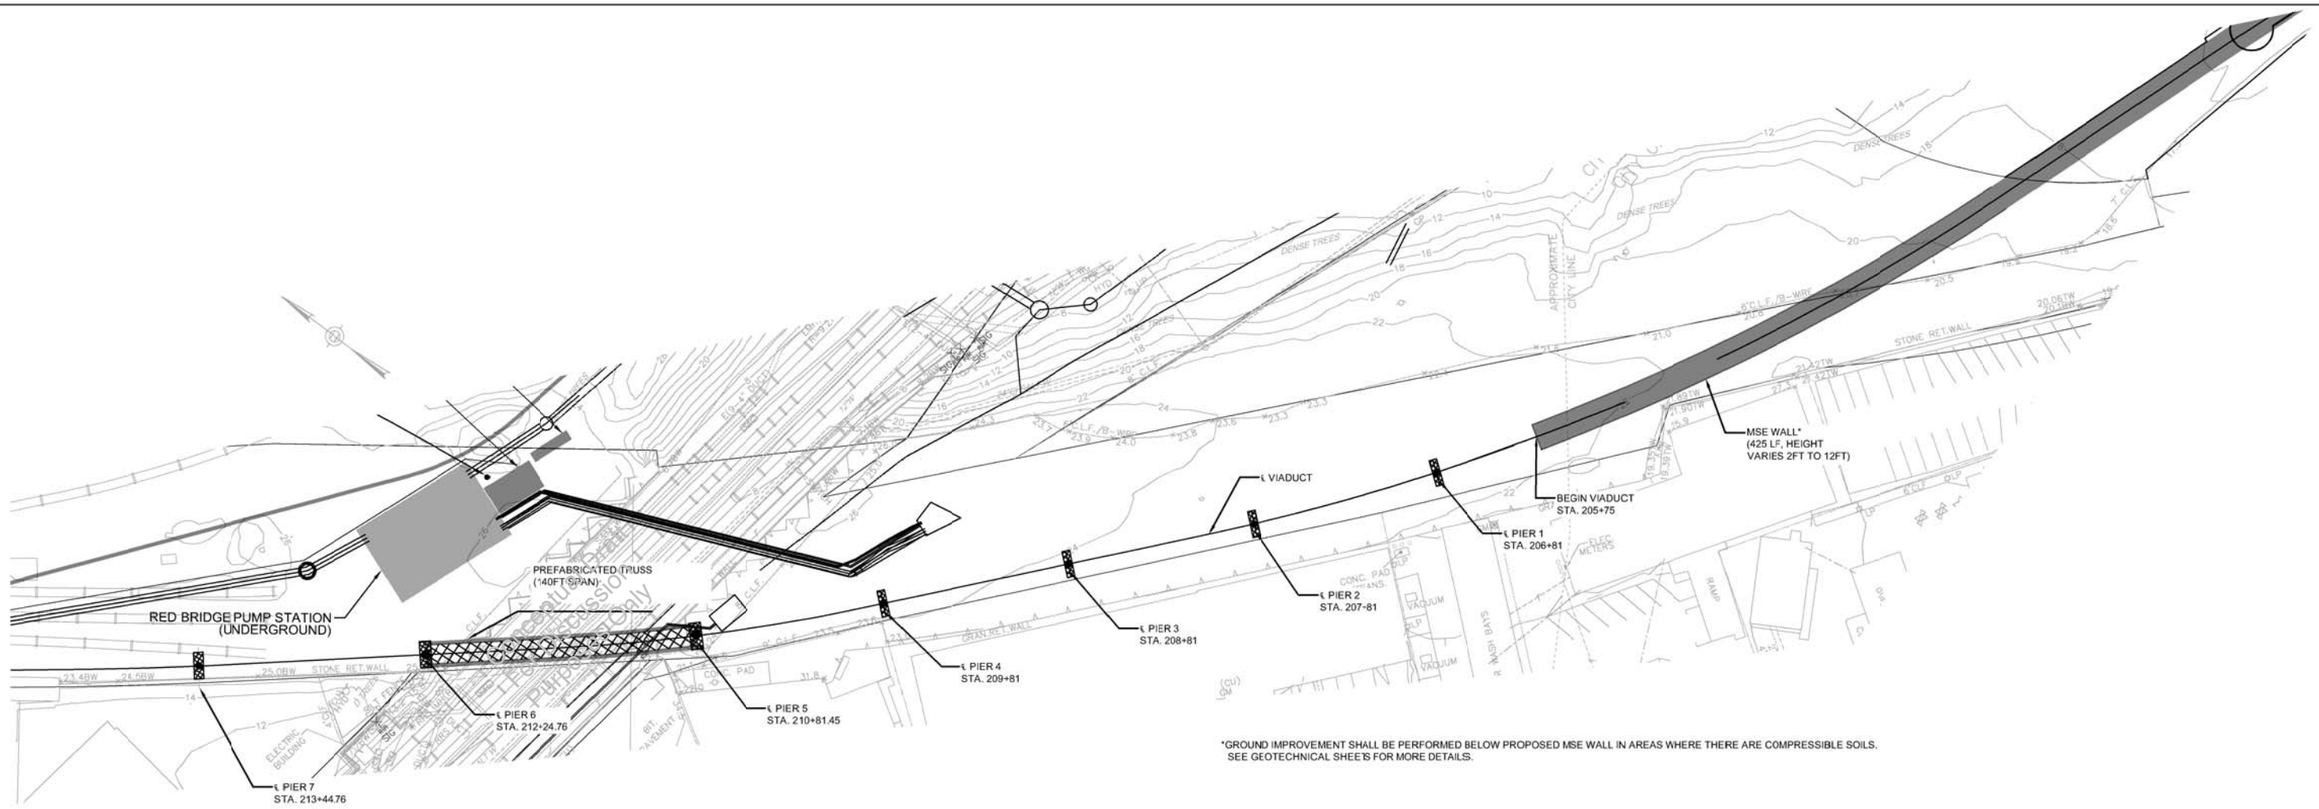

*GROUND IMPROVEMENT SHALL BE PERFORMED BELOW PROPOSED MSE WALL IN AREAS WHERE THERE ARE COMPRESSIBLE SOILS.
SEE GEOTECHNICAL SHEETS FOR MORE DETAILS.

PLAN

NOT TO SCALE

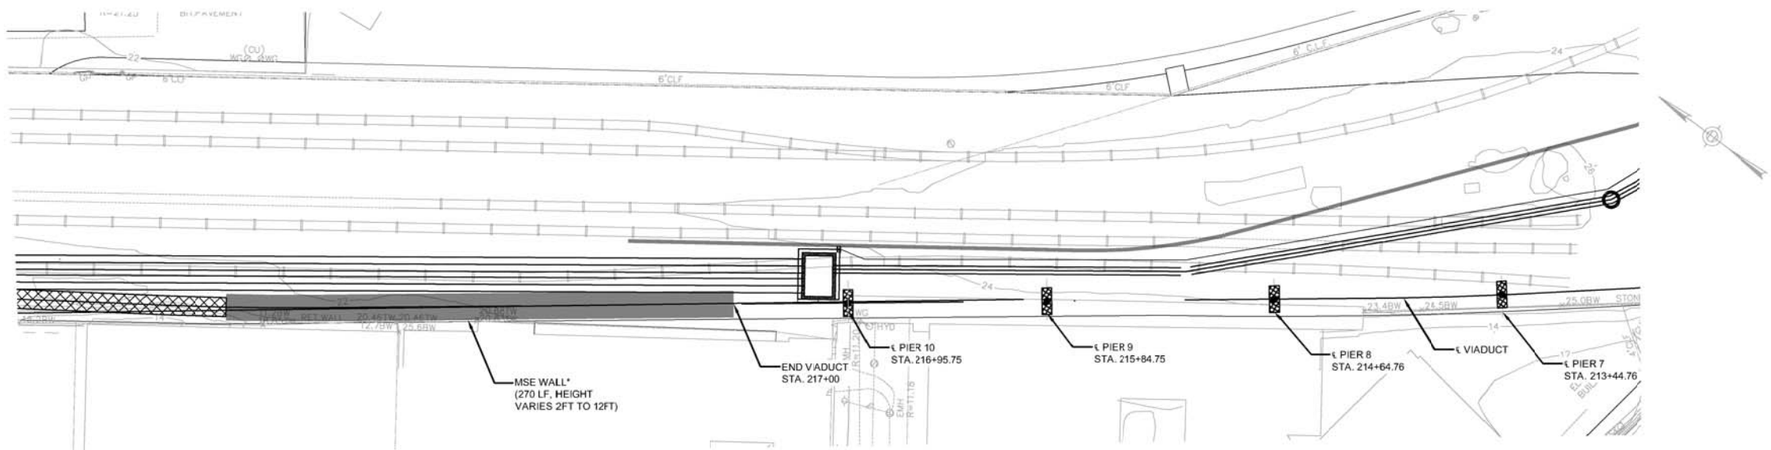

PLAN

NOT TO SCALE

*GROUND IMPROVEMENT SHALL BE PERFORMED BELOW PROPOSED MSE WALL IN AREAS WHERE THERE ARE COMPRESSIBLE SOILS.
SEE GEOTECHNICAL SHEETS FOR MORE DETAILS.

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

COMMUNITY PATH VIADUCT
GENERAL PLAN
ADDITIVE OPTION 5


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-281.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


SCALE: N.T.S.	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. -	ISSUE
DATE: SEPT. 28, 2017	JMP	STB	JM	SHEET: OPT 5 - 01	-

PLOTTED: 09/19/17 3:34PM BY:PATTIS&M
DRAWING: L:\PROPOSALS\2017\0052220 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CULBRIDGE\UNION SQUARE VIADUCT\FINAL\S-040.DWG [000-V-1047] 09/19/17 3:30PM

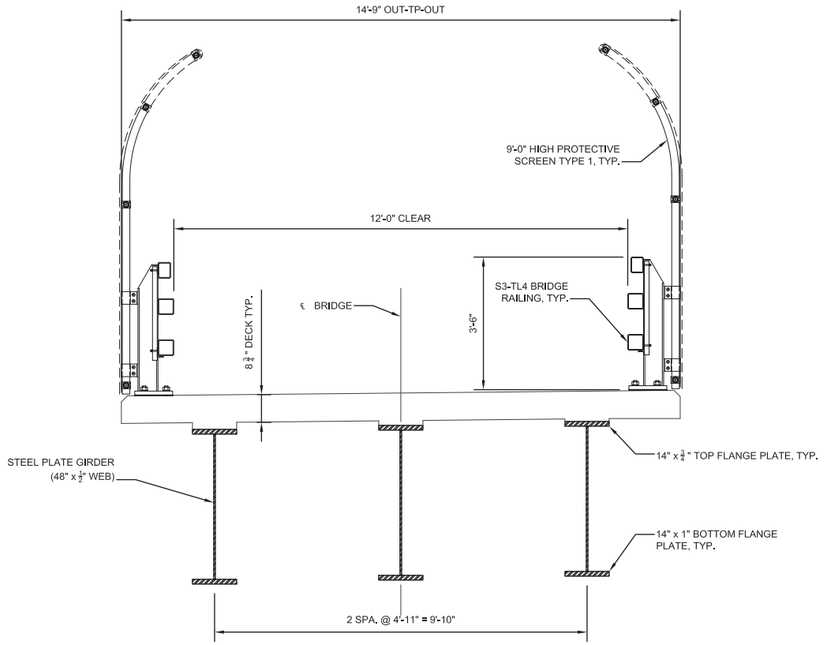


TYPICAL SECTION (STA. 205+75 TO 210+81.45) (STA. 212+24.76 TO 217+50)

NOT TO SCALE

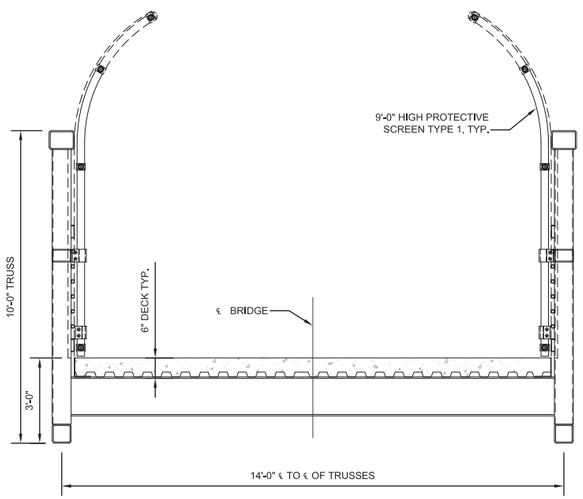

TYPICAL SECTION (STA. 210+81.45 TO 212+24.76)

NOT TO SCALE

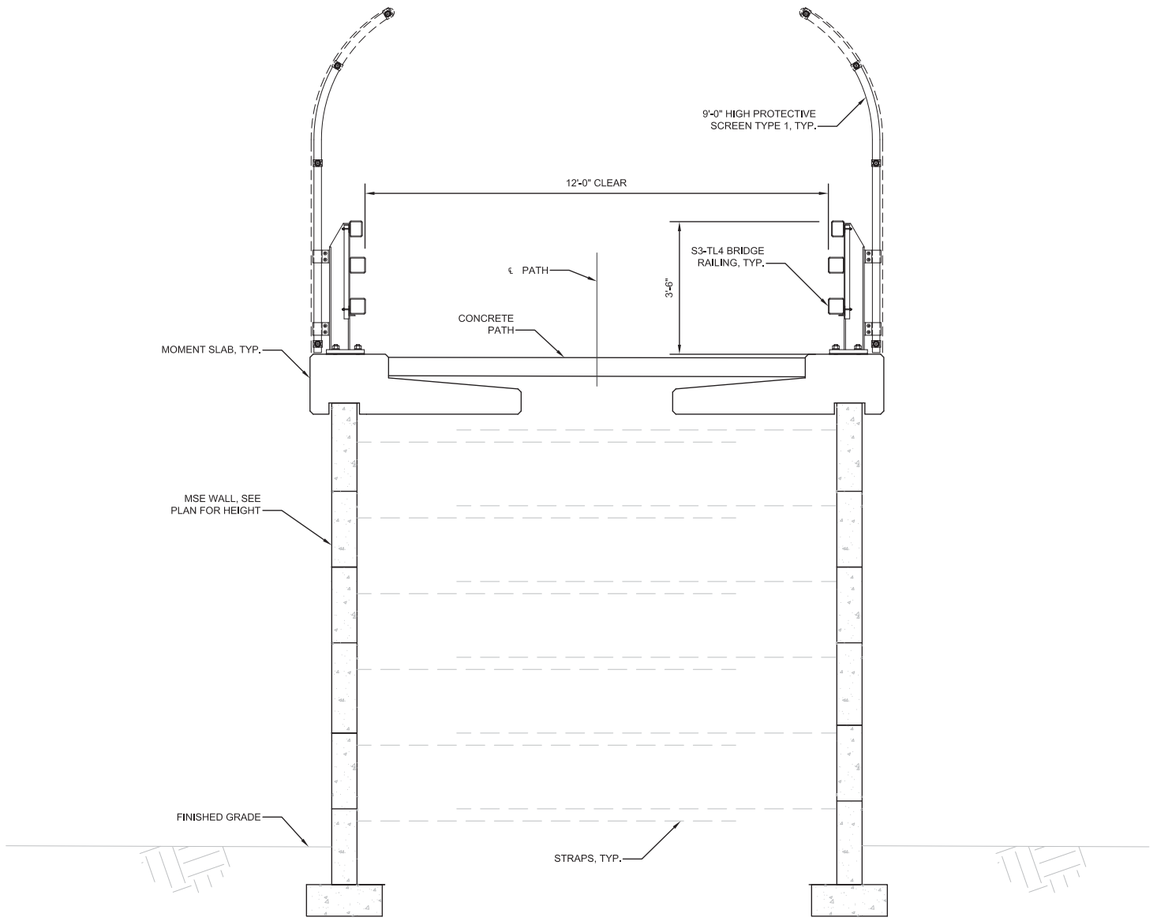

TYPICAL SECTION (STA. 201+50 TO 205+75) (STA. 217+00 TO 219+70)

NOT TO SCALE

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

COMMUNITY PATH VIADUCT
TYPICAL SECTION
ADDITIVE OPTION 5


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-281.pdf


SCALE: N.T.S.	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	STB	SB	JM	SHEET: OPT 5 - 02	·

PLOTTED: 09/19/17 3:39PM BY:PATTIS,M
DRAWING: L:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CJ_BRIDGE\UNION SQUARE VIADUCT\FINAL\S-041.DWG [LAYOUT1] 09/19/17 3:39PM

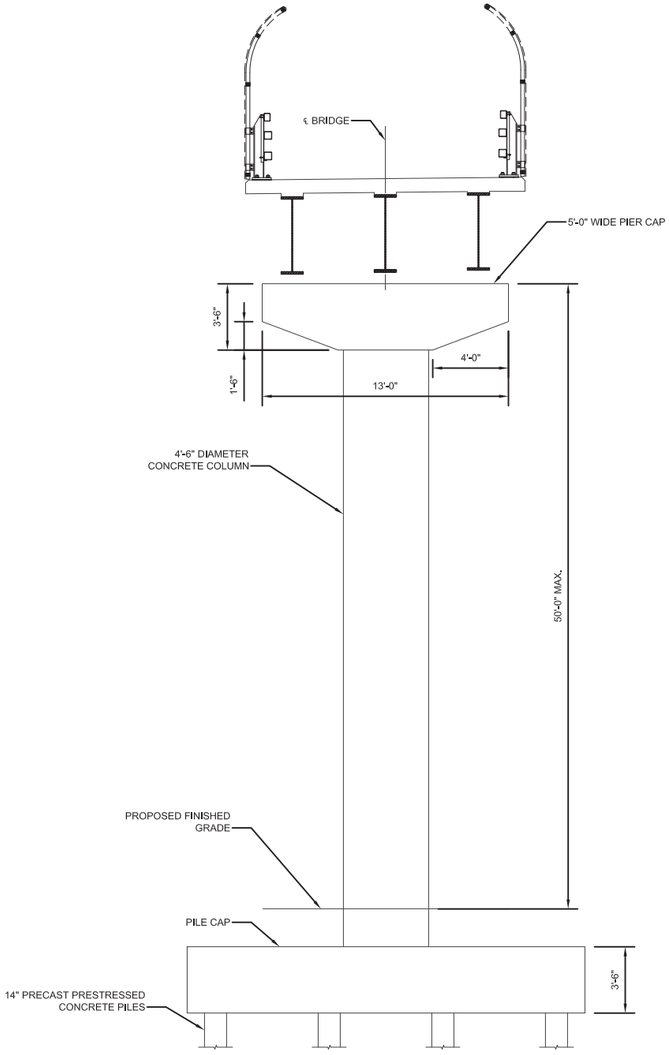


PIER TYPE 1 ELEVATION

NOT TO SCALE (PIER 7)

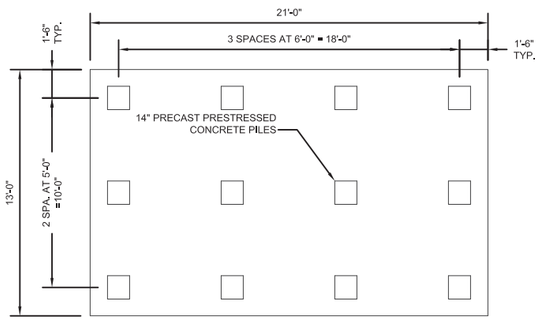


PILE CAP PLAN

NOT TO SCALE (PIER 7)

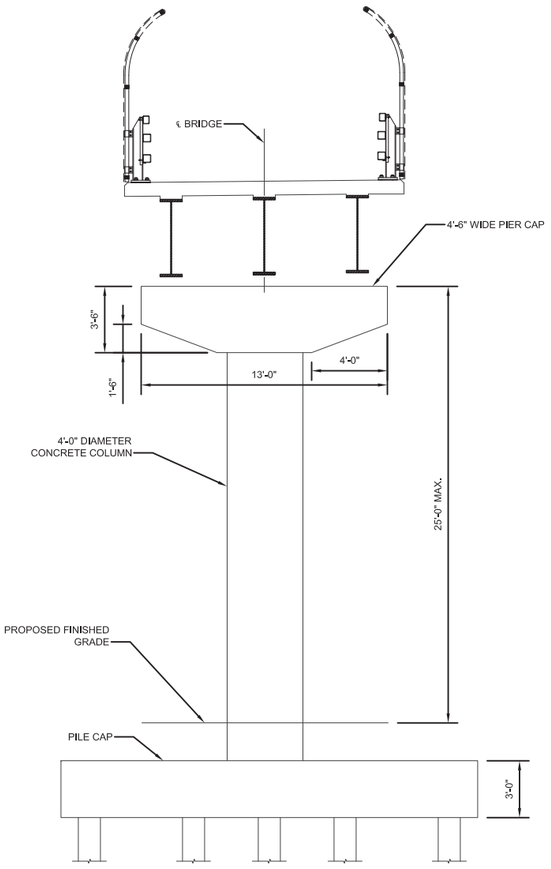


PIER TYPE 2 ELEVATION

NOT TO SCALE (PIERS 1, 2, 3, 4, 8, & 9)

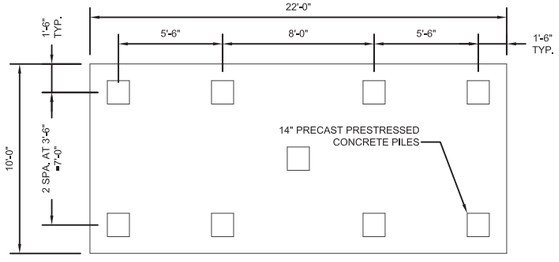

PILE CAP PLAN

NOT TO SCALE (PIERS 1, 2, 3, 4, 8, & 9)

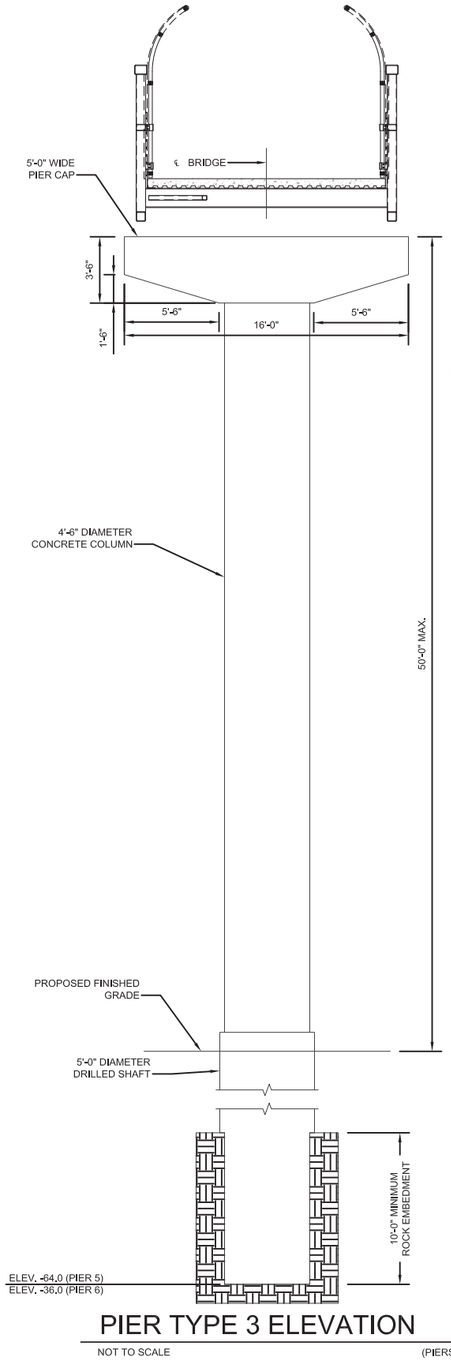


PIER TYPE 3 ELEVATION

NOT TO SCALE (PIERS 5 & 6)


FOUNDATION	GROUND ELEVATION	PILE TIP ELEVATION	PILE LENGTH
EAST ABUTMENT*	28	-40	66
PIER 1	23	-40	60
PIER 2	23	-40	60
PIER 3	24	-40	61
PIER 4	24	-40	61
PIER 7	16	-40	53
PIER 8	16	-40	53
PIER 9	19	-40	56
PIER 10	23	-40	60
WEST ABUTMENT*	29	-40	67

* ASSUME 5 PILES ARE REQUIRED AT EACH ABUTMENT




TYPICAL COLUMN SECTION PIER TYPE 1 AND 3

NOT TO SCALE



TYPICAL COLUMN SECTION PIER TYPE 2

NOT TO SCALE



DRILLED SHAFT SECTION PIER TYPE 3

NOT TO SCALE

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


COMMUNITY PATH VIADUCT
PIER DETAILS
ADDITIVE OPTION 5

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-281.pdf

SCALE: N.T.S.	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	STB	SB	JM	SHEET: OPT 5 - 03	·

PLOTTED: 09/19/17 3:39PM BY:PATTISM
DRAWING: L:\PROPOSALS\2017\0062820 GLX D-B\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CJ_BRIDGE\UNION SQUARE VIADUCT\FINAL\S-042.DWG [LAYOUT1] 09/19/17 3:29PM

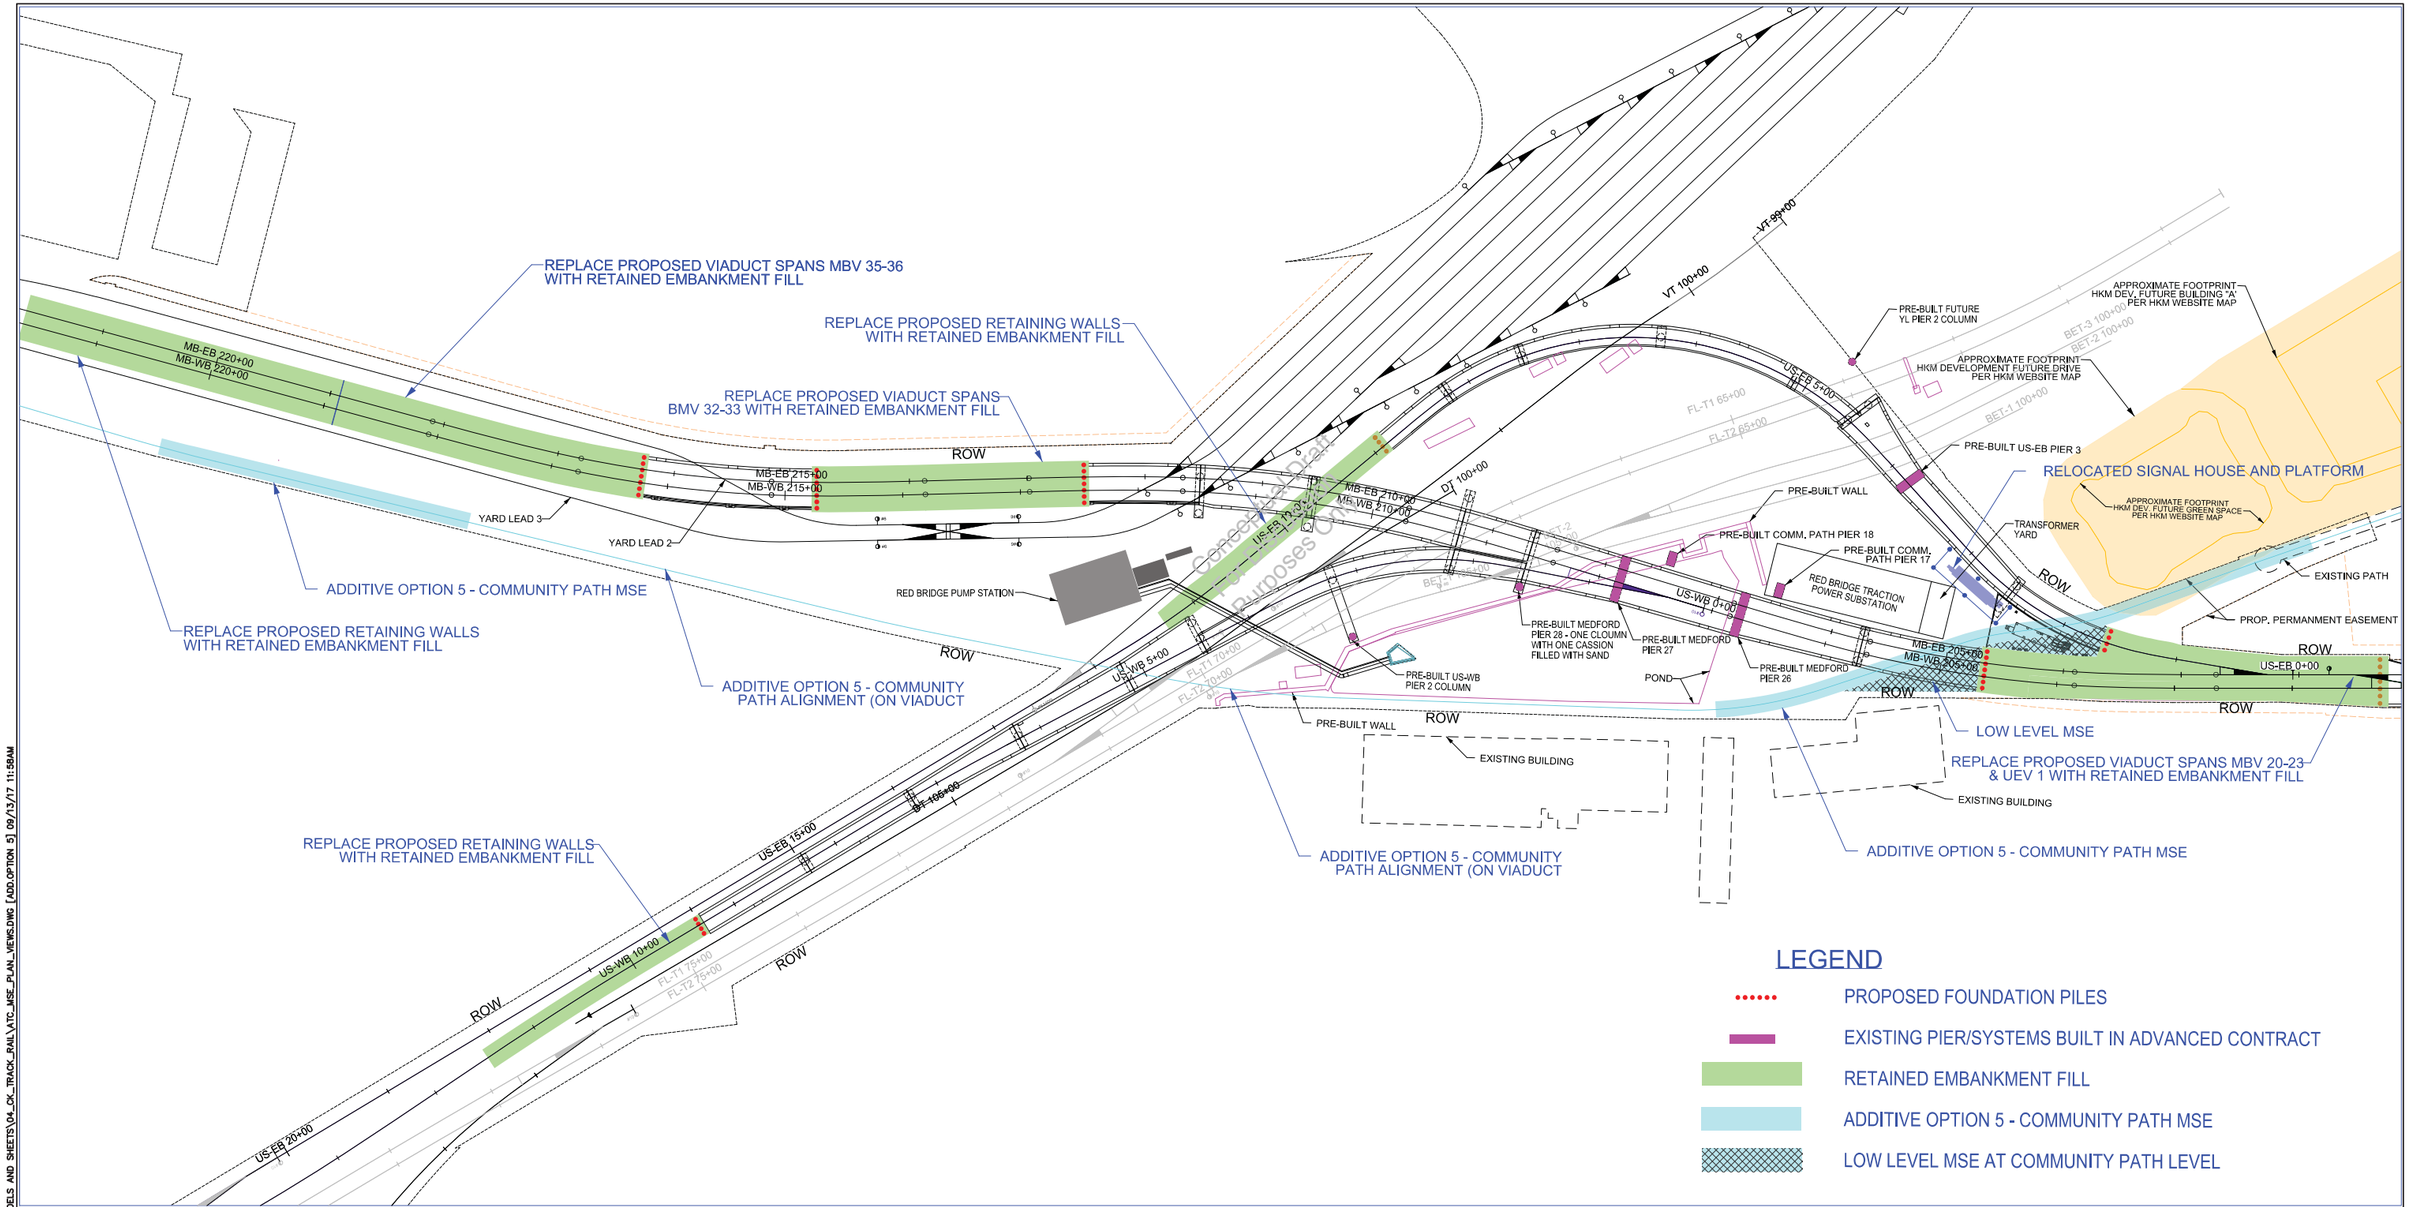

LEGEND

- PROPOSED FOUNDATION PILES
- EXISTING PIER/SYSTEMS BUILT IN ADVANCED CONTRACT
- RETAINED EMBANKMENT FILL
- ADDITIVE OPTION 5 - COMMUNITY PATH MSE
- LOW LEVEL MSE AT COMMUNITY PATH LEVEL

PLAN

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

ATC 35 - MSE
PLAN VIEW
ADDITIVE OPTION 5

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: NTS	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO.	ISSUE
DATE: SEPT. 28, 2017	PJB	PJB	JM	SHEET: OPT 5 - 04	

GV20170258-281.pdf


PLOTTED: 09/13/17 12:02PM BY:BRYANTPJ
DRAWING: I:\PROPOSALS\2017\0062820 GLX D-BY\STV 2017 RFP DESIGN\90_CAD MODELS AND SHEETS\04_CK_TRACK_RAIL\ATC_MSE_PLAN_VIEWS.DWG [ADD.OPTION 5] 09/13/17 11:59AM

PROPOSED EAST SOMERVILLE STATION

PROPOSED MEDFORD BRANCH ON GRADE

PROPOSED COMMUNITY PATH ON GRADE

Conceptual Draft For Discussion Purposes Only

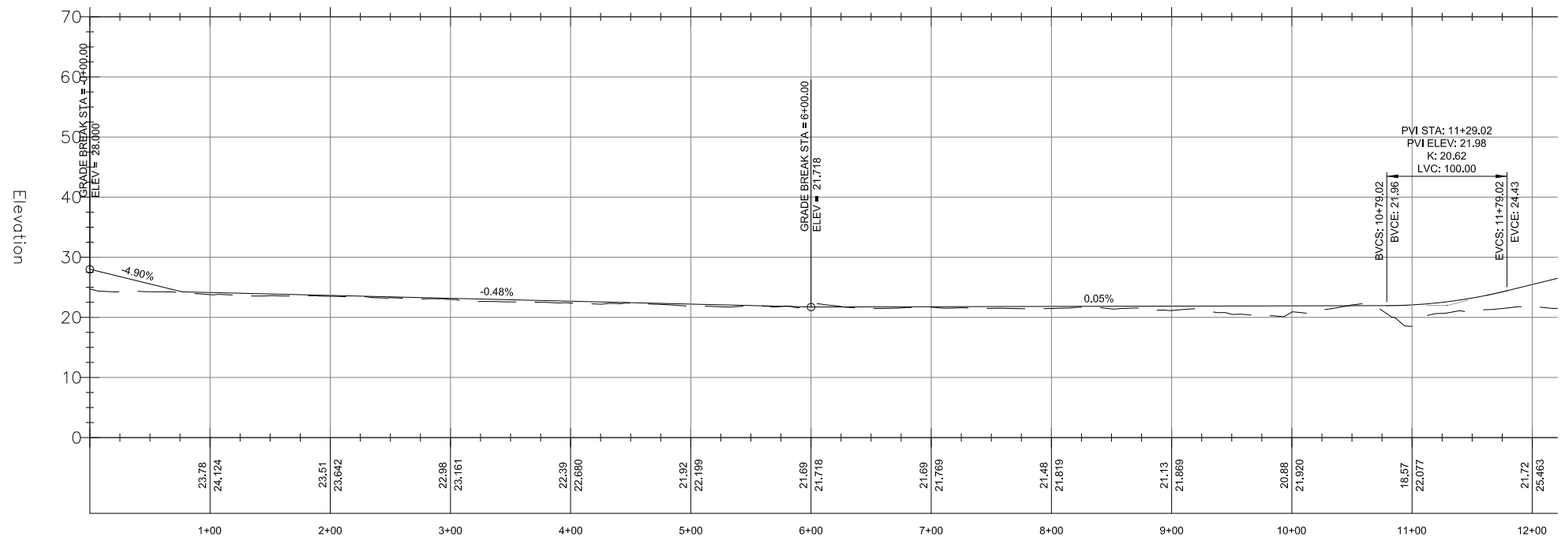

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


COMMUNITY PATH PLAN AND PROFILE ADDITIVE OPTION # 5


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-281.pdf

SCALE: 1"= 40'	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	BD	BD	PT	SHEET: OPT 5-05	

PLOTTED: 09/20/17 4:38PM BY: DECKERB
DRAWING: I:\PROPOSALS\06X\TECH DESIGN\PEDESTRIAN PATH\CMP-C-AP.DWG [LAYOUT (2)] 09/20/17 4:37PM

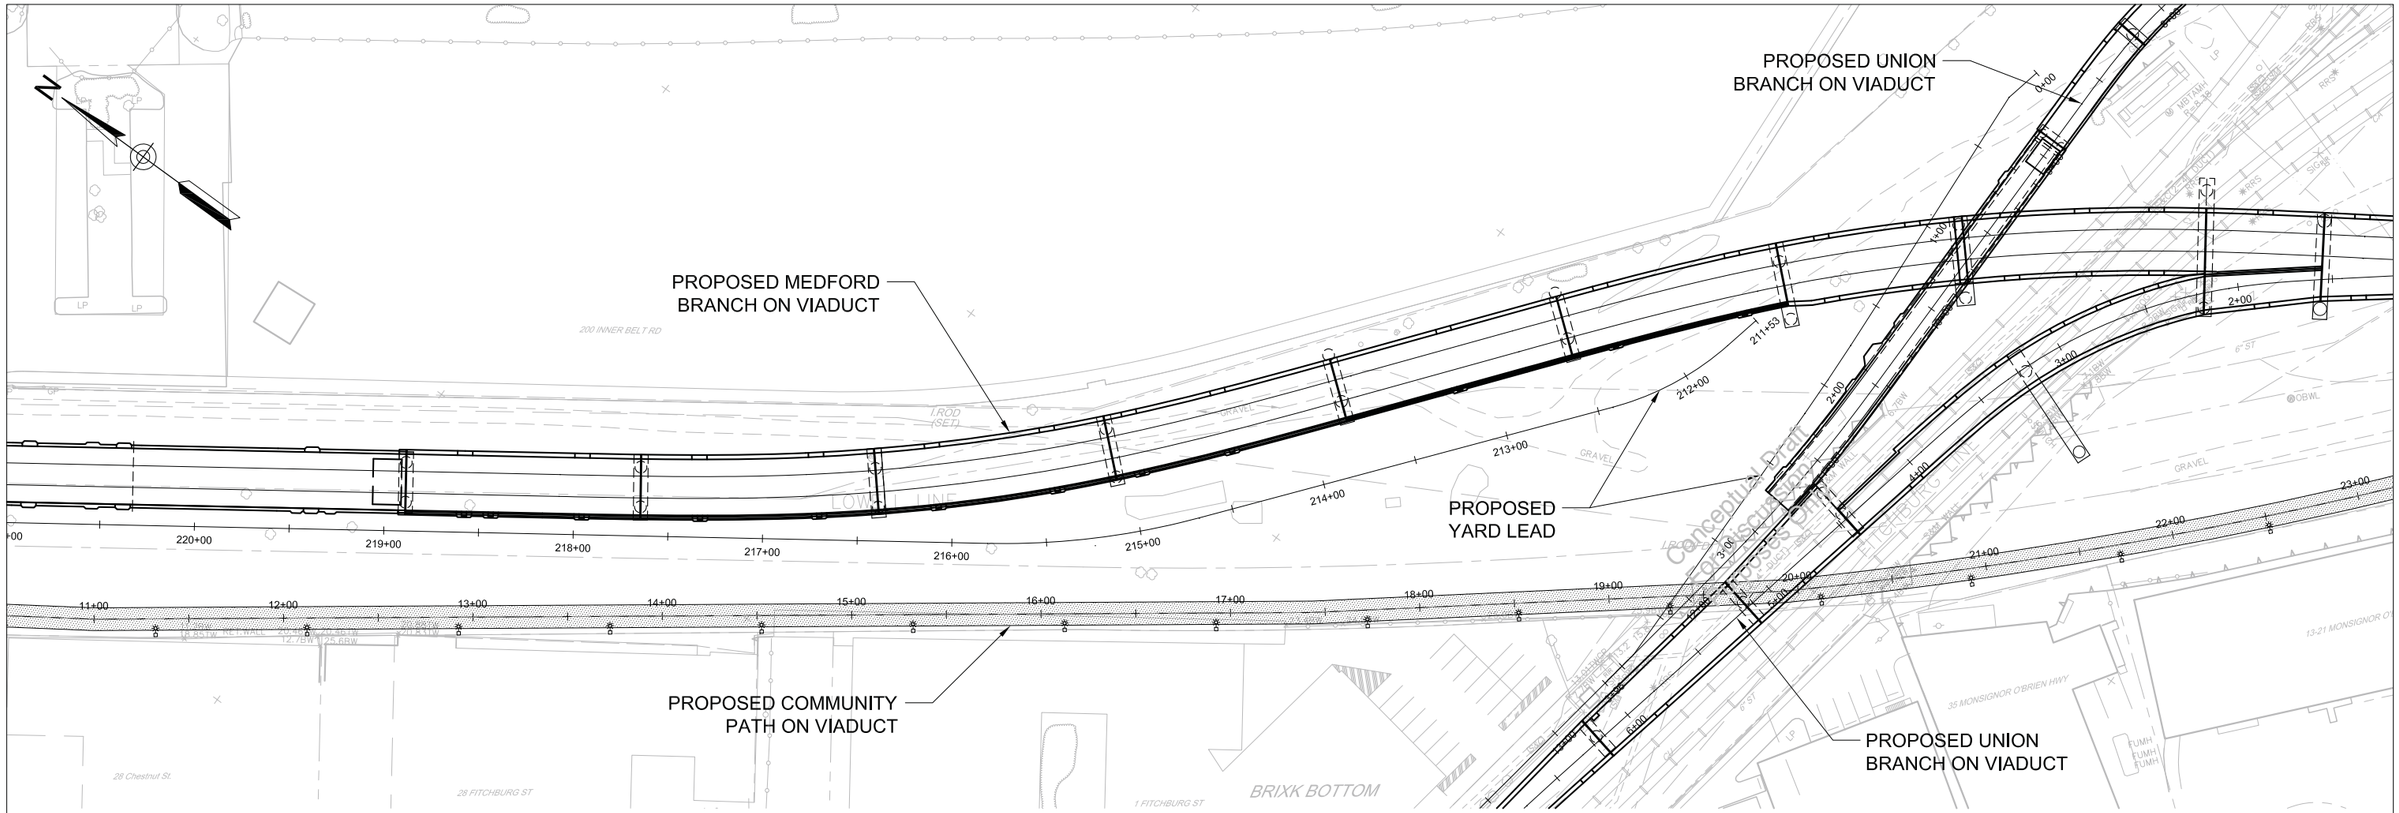

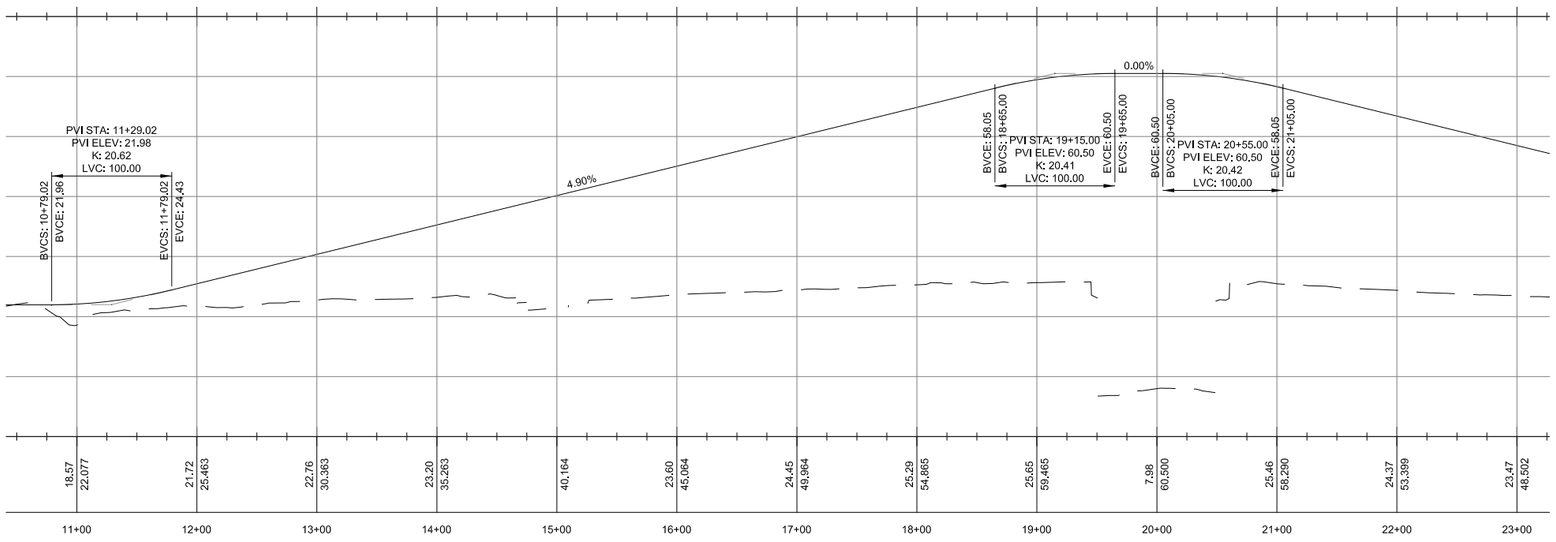

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

COMMUNITY PATH PLAN AND PROFILE ADDITIVE OPTION # 5


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS


GV20170258-281.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: 1"= 40'	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	BD	BD	PT	SHEET: OPT 5-06	·

PLOTTED: 09/22/17 8:55AM BY: DECKERB
DRAWING: I:\PROPOSALS\08A\TECH DESIGN\PEDESTRIAN PATH\OMP-C-AP.DWG [LAYOUT: (2)] 09/22/17 8:55AM

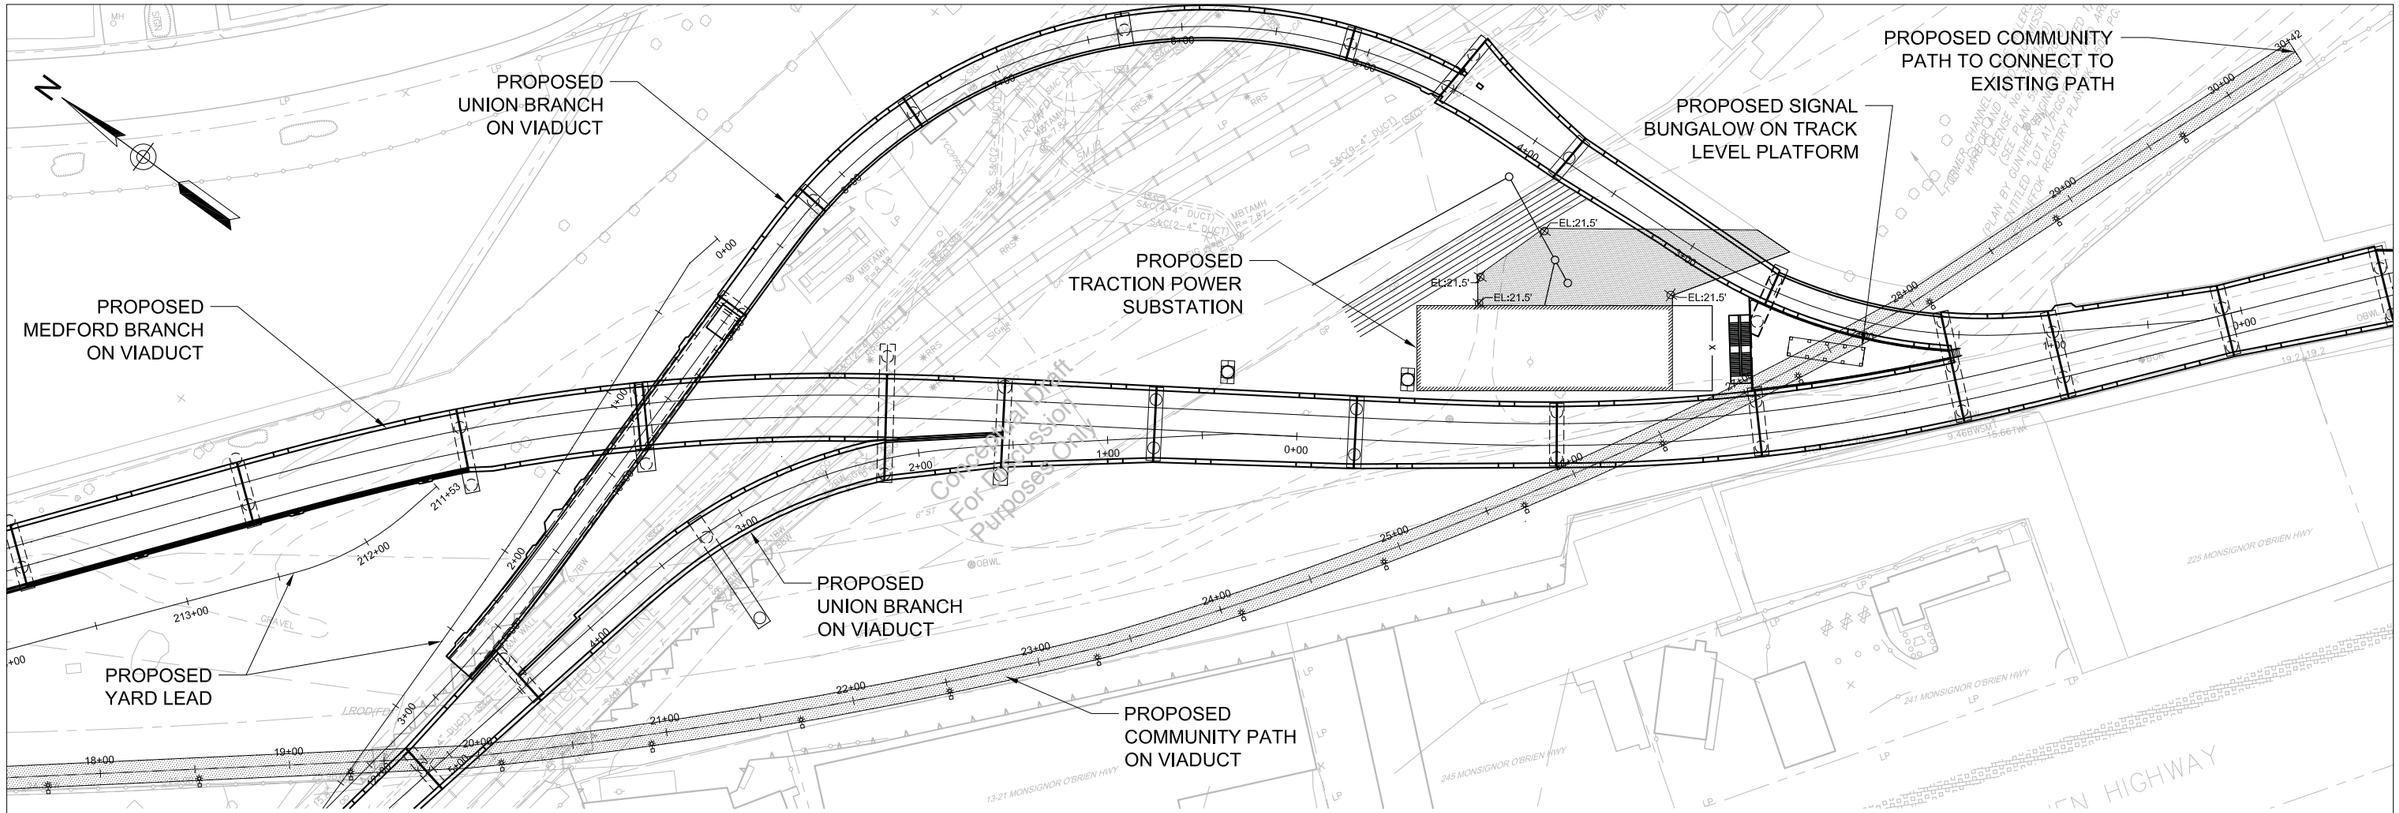

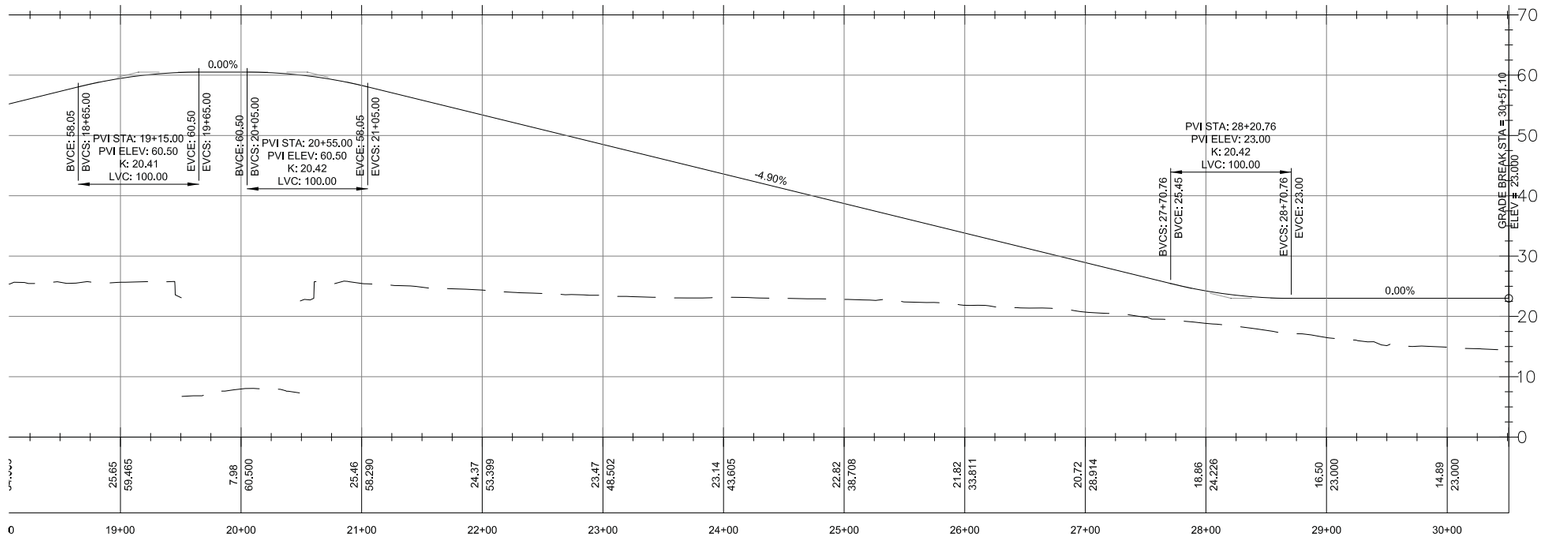

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

COMMUNITY PATH PLAN AND PROFILE ADDITIVE OPTION # 5

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: 1"= 40'
DATE: SEPT. 28, 2017

DRAWN BY	DESIGN BY	CHECK BY
BD	BD	PT

PLAN NO. .
SHEET: OPT 5-07
ISSUE .

GV20170258-281.pdf

PLOTTED: 09/22/17 8:47AM BY: DECKERB
DRAWING: I:\PROPOSALS\GLX\TECH DESIGN\PEDESTRIAN PATH\CMP-C-AP.DWG [LAYOUT: (3)] 09/22/17 8:46AM

6. DESIGN AND CONSTRUCTION OF AN ENHANCED VMF

6.A GENERAL APPROACH AND LOCATION-SPECIFIC DESIGNS

The main focus of this additive option is to provide:

- The means and equipment to increase productivity and facilitate multiple/simultaneous vehicle inspections and repair work at the VMF
- A more expansive and flexible transportation building space to execute and schedule operators shifts and communicate activities between the VMF, storage yard tracks, and revenue service along the ROW
- Increased storage yard track capacity, which allows more options for train movements throughout the yard.

All of the additive options outlined in the RFP for the VMF fall within the programmed floor plate. Architectural, structural, and building support systems (MEP), the infrastructure, for the additional set of vehicle lifts along Track 4, South and the inclusion of the wheel truing machine (Track 4 North) are part of the base RFP Technical Provision requirements. The site location of the VMF, and its floor plate size, remain as is. Conversely the floor plate size of the transportation building has increased, but its location on site has not. However, its related site work (i.e., relocated parking lot, roadway circulation, landscaping treatment, and lighting) and track (i.e., additional storage yard tracks, related drainage, and pedestrian access between the building and yard) surroundings and adjacencies have.

We believe all of the additive options being considered under this section bring added value across the board to the overall project. In the case of the wheel truing machine and additional vehicle lift in the VMF, not only will the equipment increase and expand productivity, it will eliminate the need for regularly scheduled maintenance having to be performed at another facility. Incorporating these essential maintenance equipment items into the project will not only reduce or eliminate deadhead costs, but save time, in general, and keep feeding vehicles into the revenue stream more efficiently and timely. The enhanced and expanded transportation building provides a more robust and durable complex that, along with the planned additive landscaping and site furnishings options, creates a more pleasant work environment for MBTA personnel. Last, but not least, anytime there is an opportunity to expand track storage upfront and not add after the fact will eliminate potential impacts and costs.

The following narrative bullets correspond with the additive options as listed under Volume 3 – Addendum No. 8; 3.2.6. Additive Option Item – Enhanced VMF, dated August 17, 2017.

Wheel Truing Machine. Volume 2 – Exhibit 2A.1 Specification Section No. 11550 – Wheel Truing Machine calls for a wheel truing and reprofiling milling machine to be furnished. The most comparable machine that can be used on wheelsets, with or without stub axles, would be the MBTA's No. 7, 8, and 9 Green Line LRVs and meet the requirements and criteria set forth in the aforementioned specification is the underfloor Stanray M2 machine manufactured by Simmons, which is a centerless milling style wheel truing machine. Alternatively, the wheel truing function can also be accomplished on the Green Line fleet with a lathe-style wheel truing machine. Should this option be exercised, an underfloor Stanray M2 wheel truing machine, also manufactured by Simmons, or a lathe-style wheel truing machine, manufactured by either Hegenscheidt or Delta Manufacturing, is recommended. However, the underfloor lathe-style machine usually requires a deeper pit.

Incorporating this type machine into the work has little or no impact on the Technical Proposal. The exact size, depth, and location of the wheel truing pit along Track 3, together with stairs, access points, and working envelope will have to be tweaked under subsequent design phases, but it is anticipated to be minimal. Adjustments to structural pits, support walls, and slabs will also be minimal, in fact the pit depth might be even shallower. There is no impact or change anticipated for the electrical power currently sized. Pit light revisions will be minimal.

Additional Set of Jacking Equipment (Vehicle (car hoist) Lift) and set of Bogie out tracks. This option calls for a hoist, LRV, with body stands, rotating hoist, manufactured by the Ray-Jurgen Company or approved equal, to be furnished and installed along Track 4 – North along with 3 sets of embedded Bogie-out tracks, one set per pit, approximately ten-feet long and running west, perpendicular to Track 4, as part of the based RFP. Based on our interpretation of the aforementioned specification a Model No. PKRL-40-4 with an overall lifting capacity of 129,000 pounds, as manufactured by the Ray-Jurgen Company, meets the intent of the MBTA specifications. We are proposing to furnish and install the same for the additional set of jacking equipment in the vehicle lift pits furnished and installed in Track 4 – South as part of the base RFP. We will also mirror the Bogie-out track layout from the base RFP.

Incorporating this type machine into the work has little or no impact on the Technical proposal. All pits, infrastructure, track rails, and building support systems will essentially be replicated. There is no impact or change anticipated for the electrical power currently sized. Whether or not this additional set of lifts is incorporated into the work, we recommend the three sets of Bogie-out tracks be made part of the based RFP since their rails need to be embedded in the concrete floor slab.

Full Height Storage. This option applies to Storage Room Nos. 120 and 124 (125) as shown on Project Definition Plan MAF-A-1100. The specifications and plan calls for all these rack pallets, which measure 10-feet in height (and are the highest in both of these rooms) to be manufactured by Lyon Workspace products or approved equal. Under this section, the minimum clear ceiling height in Storage rooms 120 and 124 is 14-feet minimum. Therefore, our interpretation, that there is already a 4-foot clearance from the top of the highest specified shelving to the underside of the building assembly in the criteria under the base RFP. The VMF plans, sections, and elevations we generated for our proposal have included and addressed this clearance requirement.

Enhanced Transportation Building. Under this additive option, the size of the transportation building is increasing in size from 1,425 square feet to over 5,000 square feet. Project Definition Plan TSP-A-1000 shows ramps and stairs on the north and south sides of the building, which we interpreted along with the required grades in the area, that the floor of the building needs to be raised. This is confirmed by avoiding to have to provide a gas vapor barrier membrane and venting system beneath the floor slab because of the environmental Activities Use Limitation (AUL) in place for this area of the site. Our base proposal design was based on a prefabricated, modular-code compliant structure supported on raised CIP concrete pedestals. However, the enhanced transportation building will be stick built construction to meet the requirements for a 50-year life span and will be supported on a conventional spread footing foundation.

Incorporating the expanded transportation building will have an impact on the Technical Proposal, as it is a much larger building with different construction materials being incorporated to extend its longevity and it has more activities and functions taking place within in its space. Because it requires a more conventional foundation system, the entire footprint will be in contact with the ground. Based on the current environmental AUL in place for this area of the site, the building will require a gas vapor barrier membrane and venting be placed underneath the entire floor slab. However, the same utility services tie-in points, routing and sizes for gas, domestic and fire protection water, sanitary and storm will essentially remain as is. Per the base RFP, the transportation building electrical service is to be fed from the switchgear in the VMF; that still applies. We have provided a 400 amp service for the transportation building. This size is adequate for the enhanced Transportation building.

Changes from the Technical Proposal

The proposed addition of an enhanced VMF does not require any deviation from the requirements of the Technical Proposal.

6.B SCHEDULE IMPACT ASSESSMENT

GLX Constructors' efforts to support this additive option as described are minimal and will not impact the proposed schedule.

6.C ENHANCED VMF (TRANSPORTATION) DRAWINGS

Drawings OPT6-01 through OPT6-11 provide the site plan showing the revised parking lot layout and roadway circulation along with the related site lighting. Floor plans, exterior building elevations, and sections along with finish room and door schedules have been provided. We have also provided a typical exterior wall section to show the construction materials are durable and in line with criteria set forth in the Technical Provisions and that the its assembly will pass NFPA 285 requirements. The drawings also show spread footing foundations, as well as the building superstructure steel framing. MEP buildings support systems will be advanced in subsequent design phases if the enhanced transportation building is incorporated into the work.

RFP	
Drawing Number	**Drawing Title**
OPT6-01	Vehicle Maintenance Facility Site Plan – Additive Option 6
OPT6-02	Enhanced Transportation Building Site Plan – Additive Option 6
OPT6-03	Enhanced Transportation Building First Floor Plan – Additive Option 6
OPT6-04	Enhanced Transportation Building Exterior Elevations – Additive Option 6
OPT6-05	Enhanced Transportation Building Sections – Additive Option 6
OPT6-06	Enhanced Transportation Building Door and Finish Schedule – Additive Option 6
OPT6-07	Enhanced Transportation Building Foundation Plan – Additive Option 6
OPT6-08	Enhanced Transportation Building Column Framing Plan – Additive Option 6
OPT6-09	Enhanced Transportation Building Roof Framing Plan and Building Section – Additive Option 6
OPT6-10	Vehicle Maintenance Facility Yard Lead and Maintenance Facility – Additive Option 6
OPT6-11	Vehicle Maintenance Facility Pole and Foundation Schedule – Additive Option 6

SUBSURFACE DETENTION CHAMBER

VMF EMPLOYEE PARKING (65 SPACES)

GAS METER

GAS FIRED EMERGENCY GENERATOR

1500 KVA TRANSFORMER

ELECTRIC METER

TRASH COMPACTOR & BALER

9-3" C POWER DUCT BANK

4-4" C TEL, FA, AND SECURITY DUCT BANK

10" FIRE PROTECTION

4" DOMESTIC WATER

LIFT GATES AND CARD READER

PERIMETER SECURITY FENCE

RETAINING WALL

LIFT GATES WITH CARD READER

8" GAS

6" SANITARY

PERIMETER SECURITY FENCE

TRANSPORTATION BUILDING PARKING AREA (89 SPACES)

MAX. FLINE SEE DRAWING No. C-031 (ADD 0)

VEHICLE MAINTENANCE FACILITY (FF EL = 18.50)

DC NEGATIVE MANHOLE (5 BETWEEN VMF AND RED BRIDGE TPSS)

DC POSITIVE MANHOLE (6 BETWEEN VMF AND RED BRIDGE TPSS)

6-4" C POWER AND SYSTEMS DUCT BANK TO TRANSPORTATION BUILDING

2-5" C POSITIVE TRACTION POWER DUCT BANK & 2-5" C NEGATIVE TRACTION POWER DUCT BANK

MAF-1 20+00

MAF-1 25+00

MAF-1 15+00

Conceptual Draft For Discussion Purposes Only

1"=40' 40' 0 40'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICAL MAINTENANCE FACILITY SITE PLAN - ADDITIVE OPTION 6


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-282.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	DK	DK	ND	SHEET: OPT6-01	.

PLOTTED: 09/08/17 2:08PM BY:KERKSDJ
DRAWING: \\STVGROUP.STVNC.COM\V3\BOMA\VOL3\PROPOSALS\GLX\TECH DESIGN\VMF-901 ETB-902 SITE PLANS.DWG [VMF-901] 09/08/17 10:54AM

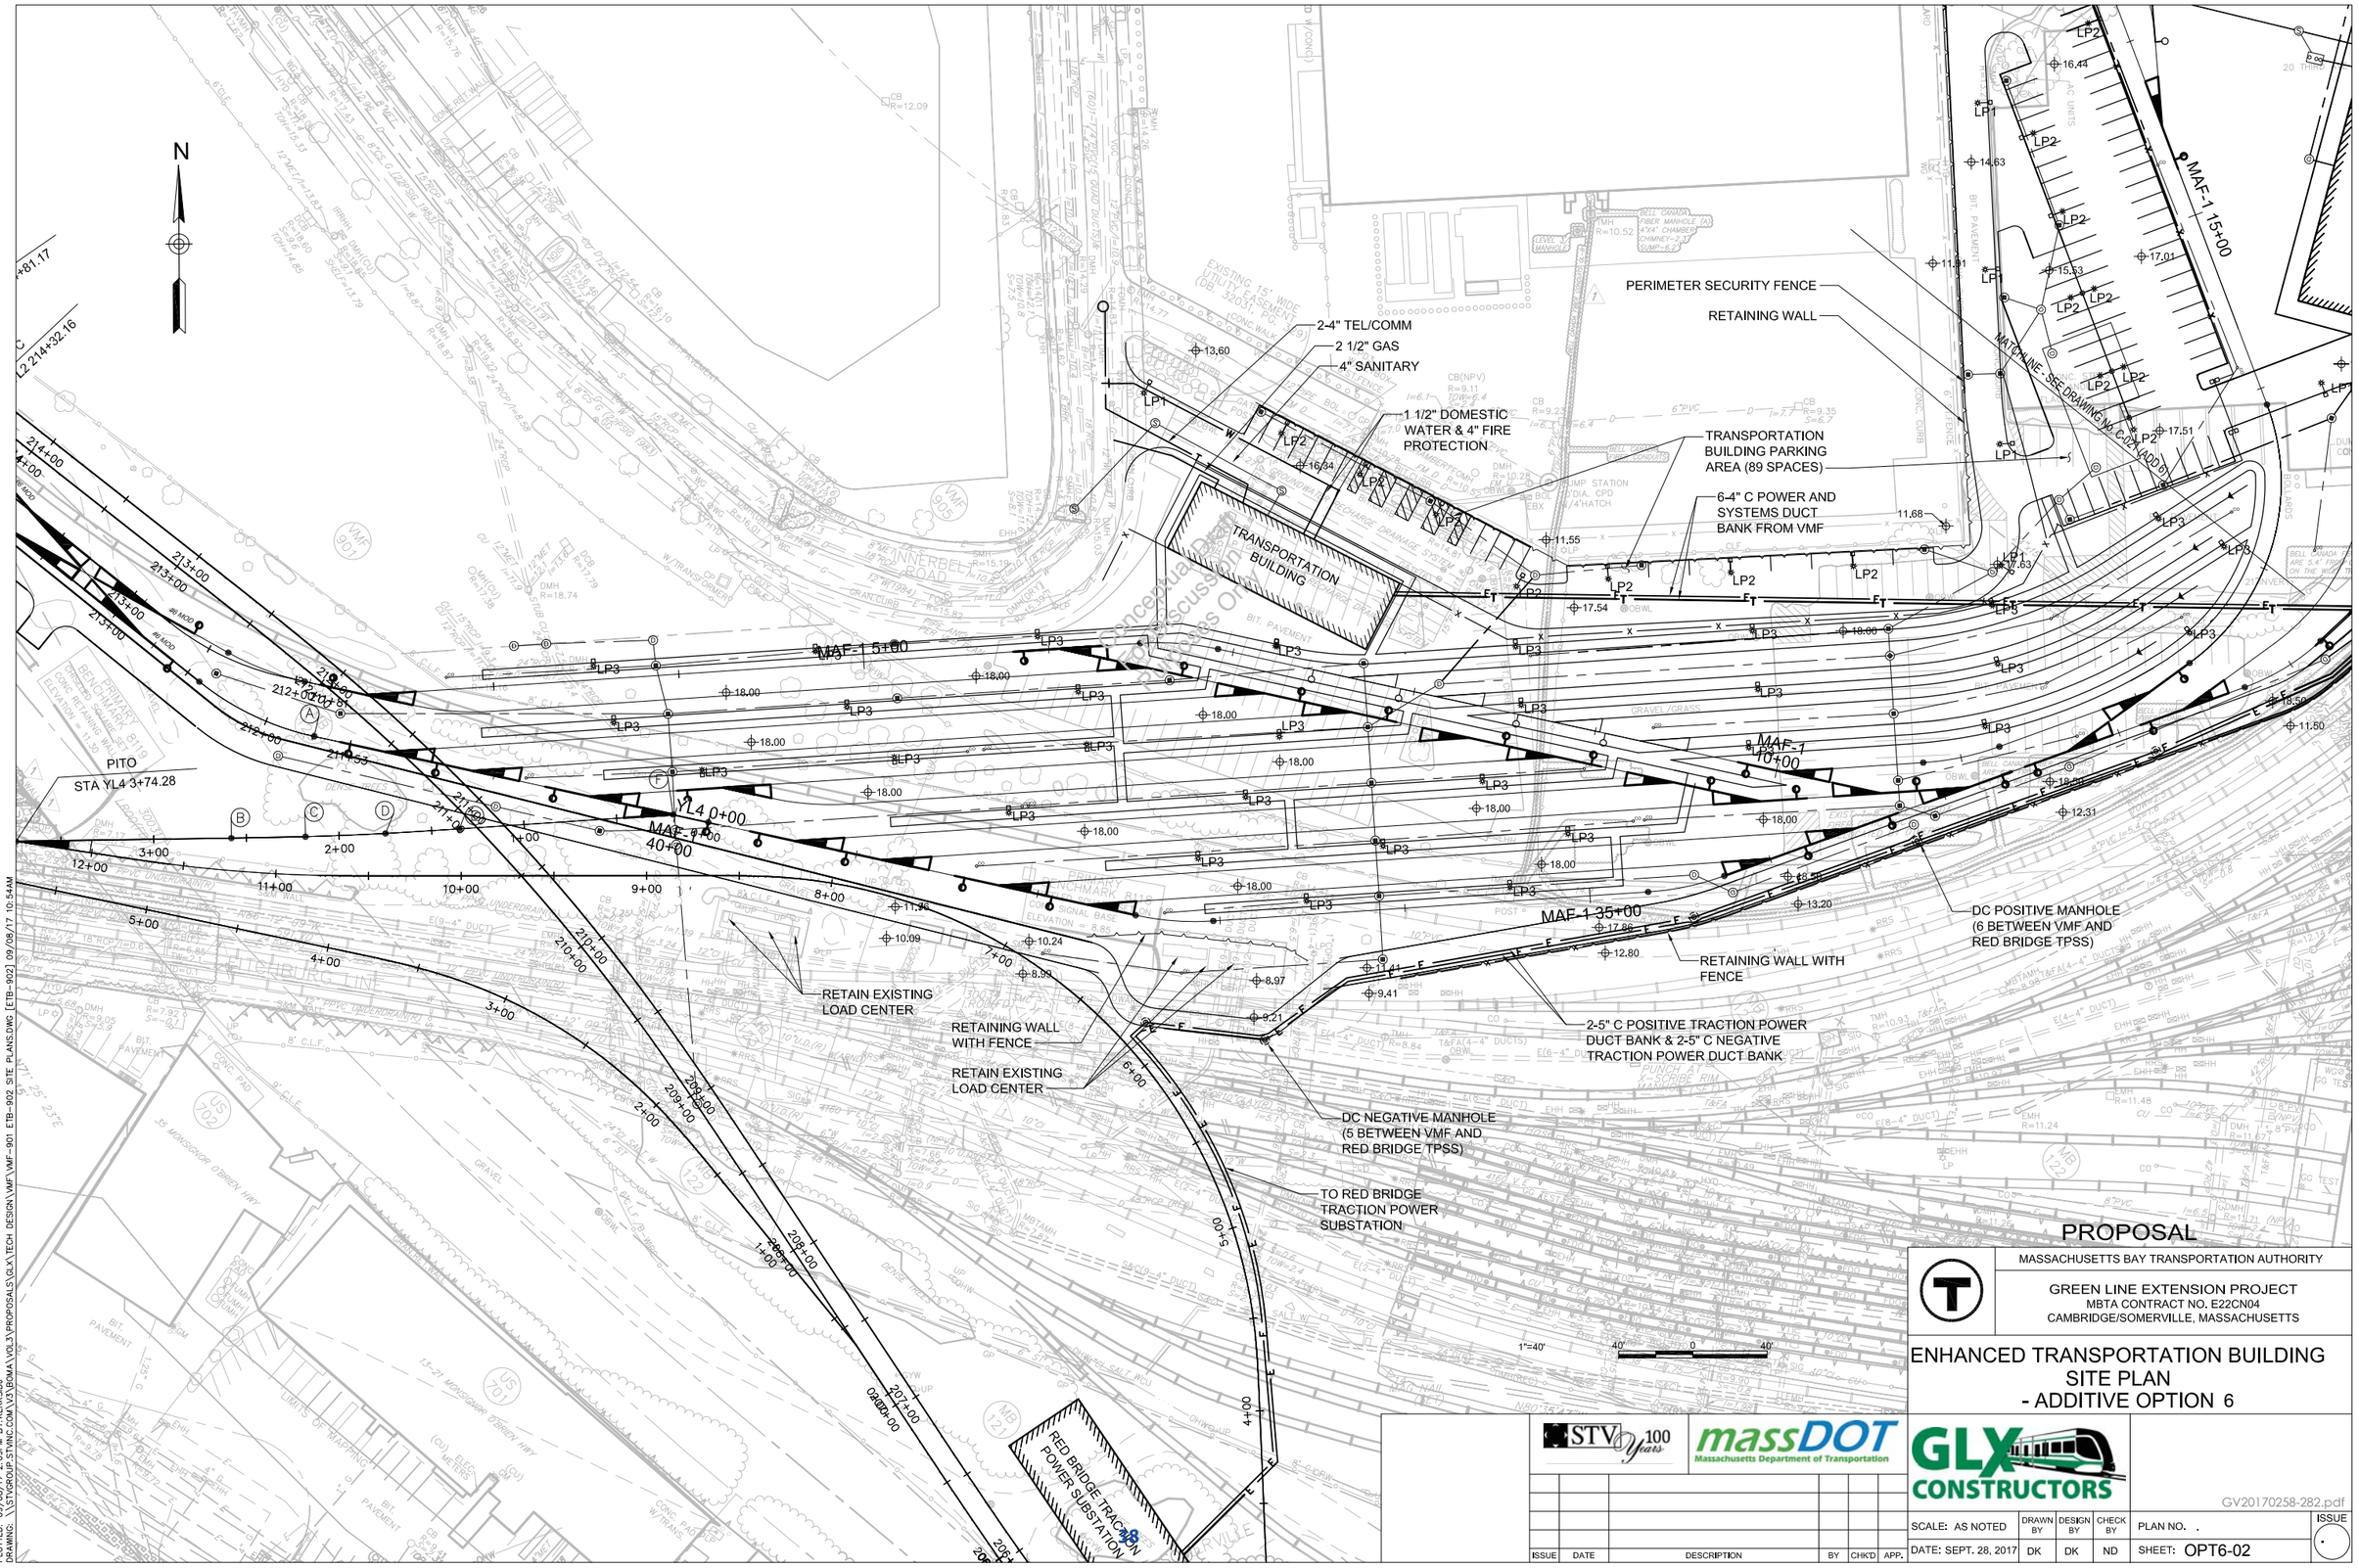

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

ENHANCED TRANSPORTATION BUILDING SITE PLAN - ADDITIVE OPTION 6


STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-282.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	DK	DK	ND	SHEET: OPT6-02	.

PLOTTED: 09/08/17 2:09PM BY:KERKSIDJ
DRAWING: \\STVGROUP.STVINC.COM\V3\BOMA\VOL3\PROPOSALS\GLX\TECH DESIGN\VMF\VMF-901 ETB-902 SITE PLANS.DWG [ETB-902] 09/08/17 10:54AM

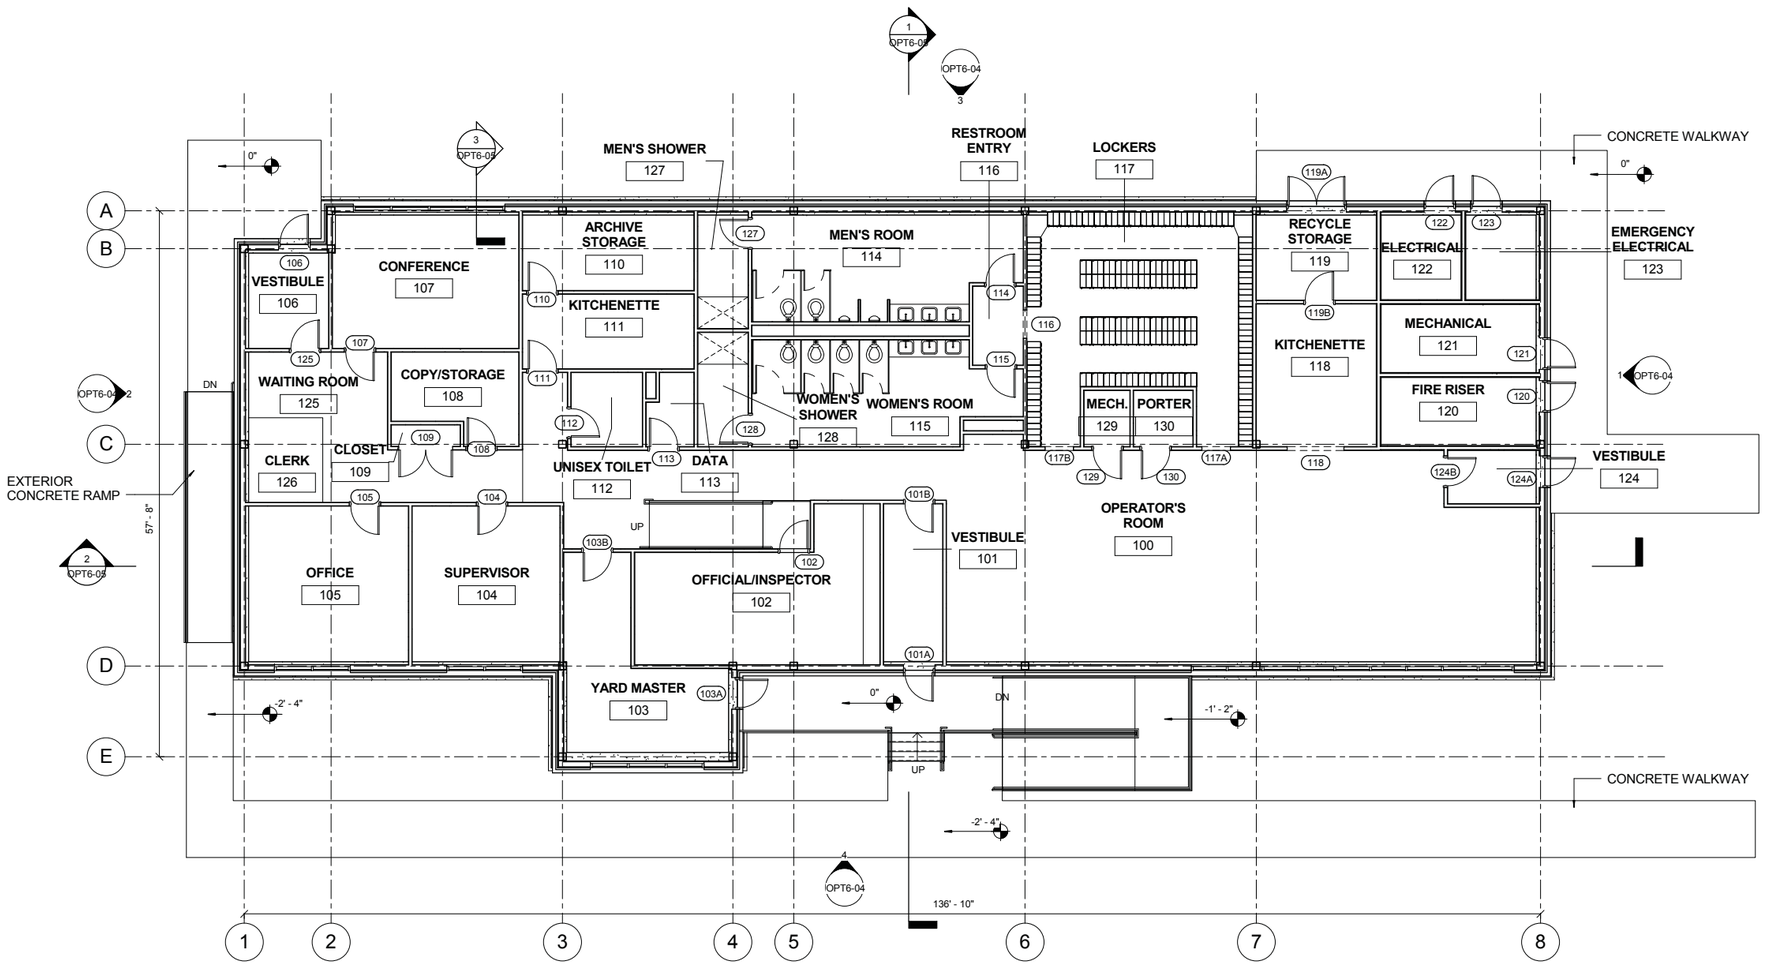

FIRST FLOOR PLAN

1/8" = 1'-0"

0 4' 8' 16'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY


GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

ENHANCED TRANSPORTATION BUILDING
FIRST FLOOR PLAN
- ADDITIVE OPTION 6

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.


GV20170258-282.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: OPT6-03	.

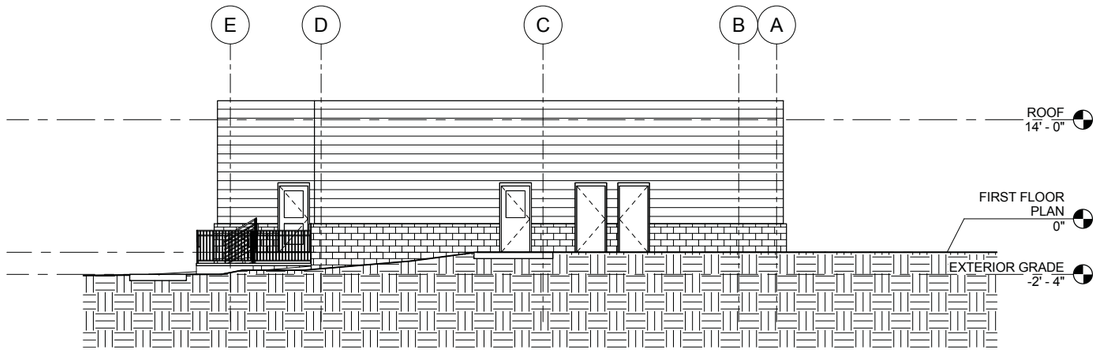


1 A-102 EAST ELEVATION

1/8" = 1'-0"

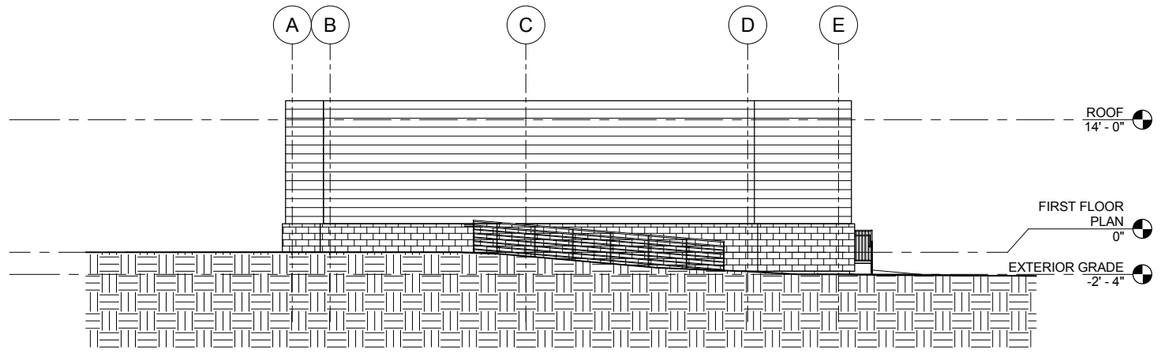


2 A-102 WEST ELEVATION

1/8" = 1'-0"

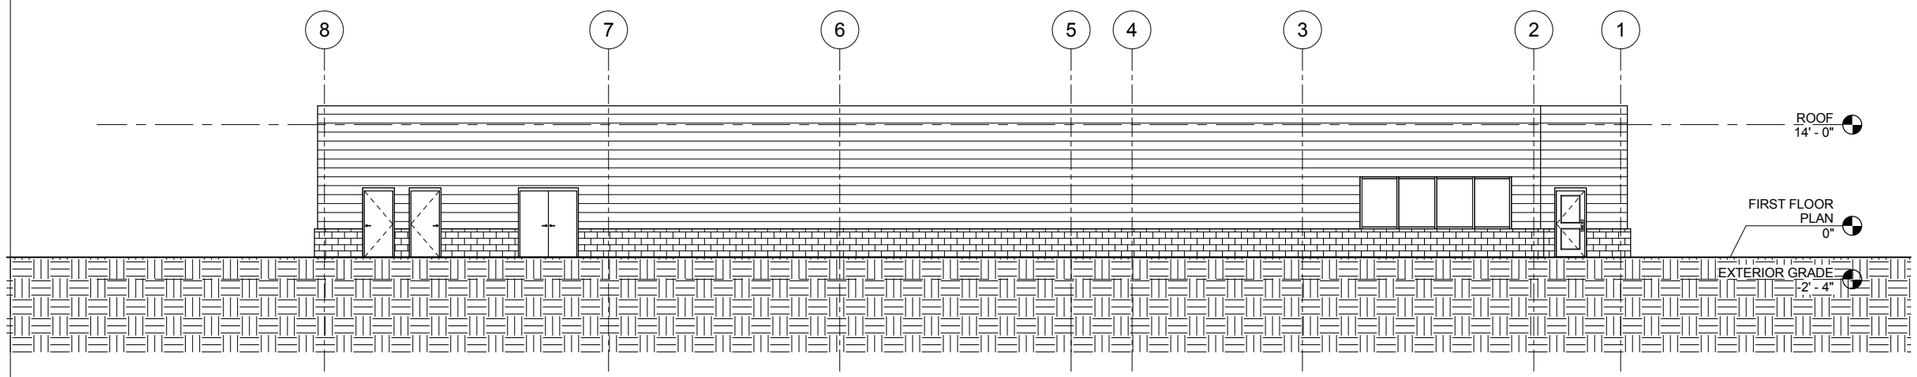

3 A-102 NORTH ELEVATION

1/8" = 1'-0"

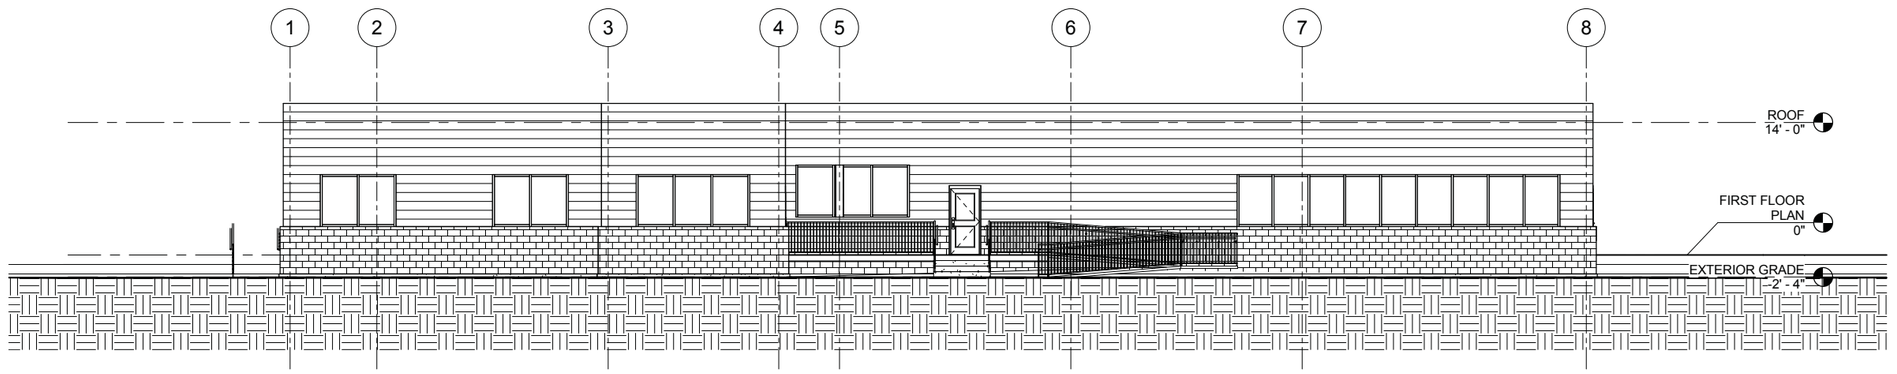

4 A-102 SOUTH ELEVATION

1/8" = 1'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


ENHANCED TRANSPORTATION BUILDING
EXTERIOR ELEVATIONS
- ADDITIVE OPTION 6

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-282.pdf


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: OPT6-04	.

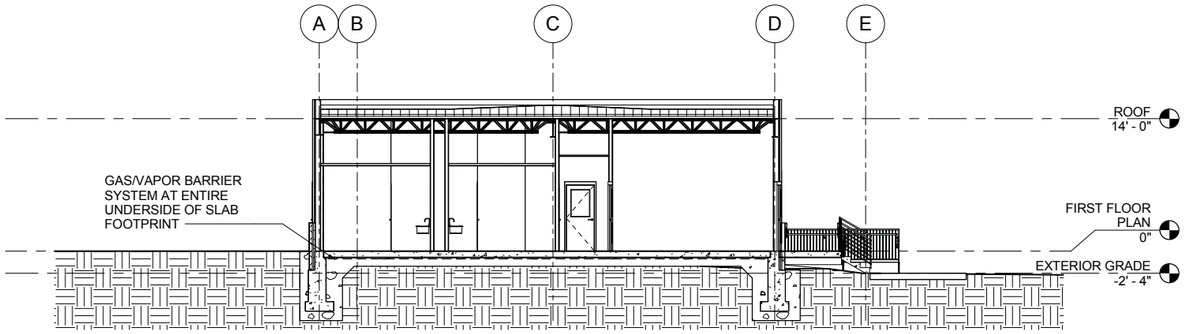


1 / A-102 TRANSVERSE SECTION

1/8" = 1'-0"

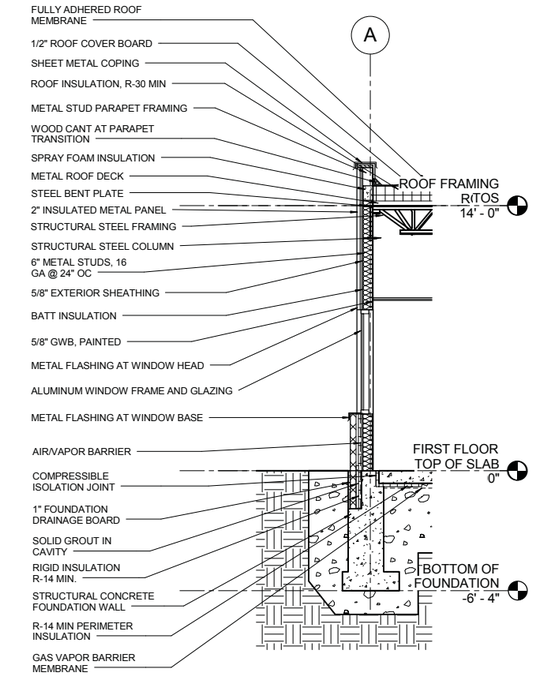

3 / A-102 TYPICAL WALL SECTION

1/4" = 1'-0"

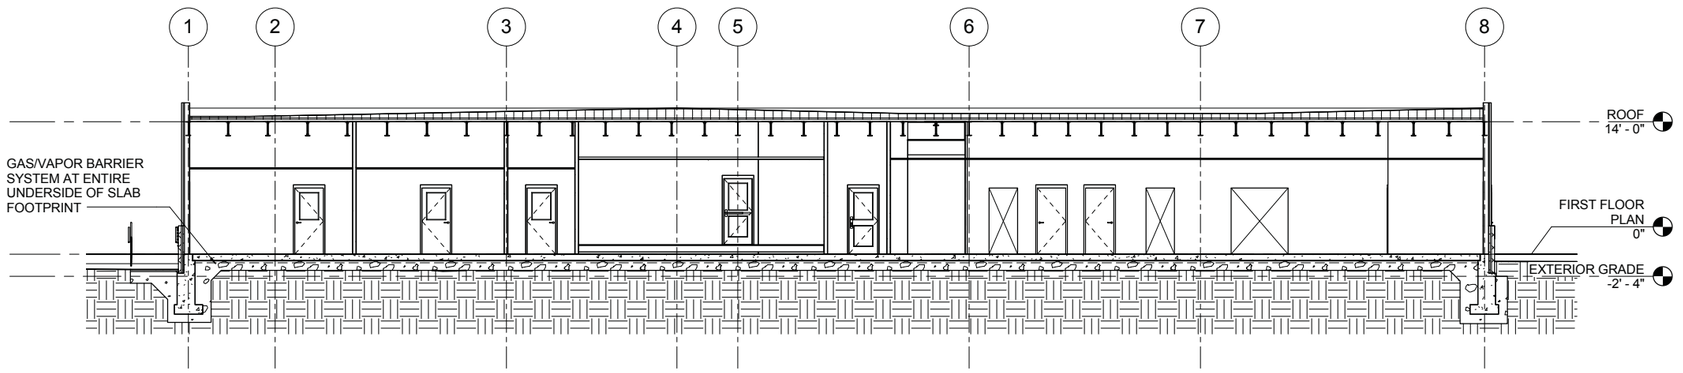

2 / A-102 LONGITUDINAL SECTION

1/8" = 1'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

ENHANCED TRANSPORTATION BUILDING SECTIONS
- ADDITIVE OPTION 6

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-282.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: OPT6-05	.

- DOOR SCHEDULE 1 -

DOOR NUMBER	LOCATION	DOOR					FRAME					FIRE RATING	HARDWARE SET	REMARKS
		TYPE	MAT.	NOMINAL SIZE			TYPE	MAT.	DETAIL					
				WIDTH	HEIGHT	THICKNESS			JAMB	HEAD	SILL			
101A	VESTIBULE	B	HM	3' - 0"	7' - 0"	1 3/4"					0"			
101B	OPERATOR'S ROOM	B	HM	3' - 0"	7' - 0"	1 3/4"					0"			
102	OFFICIAL/INSPECTOR	B	HM	3' - 0"	7' - 0"	1 3/4"					1' - 0"			
103A	YARD MASTER	B	HM	3' - 0"	7' - 0"	1 3/4"					0"			
103B	OPERATOR'S ROOM	A	HM	3' - 0"	7' - 0"	1 3/4"					0"			
104	WAITING ROOM	A	HM	3' - 0"	7' - 0"	1 3/4"					0"			
105	WAITING ROOM	A	HM	3' - 0"	7' - 0"	1 3/4"					0"			
106	VESTIBULE	B	HM	3' - 0"	7' - 0"	1 3/4"					0"			
107	CONFERENCE	A	HM	3' - 0"	7' - 0"	1 3/4"					0"			
108	WAITING ROOM	A	HM	3' - 0"	7' - 0"	1 3/4"					0"			
109	CLOSET	F	HM	5' - 8"	6' - 8"	2"					0"			
110	KITCHENETTE	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
111	OPERATOR'S ROOM	A	HM	3' - 0"	7' - 0"	1 3/4"					0"			
112	OPERATOR'S ROOM	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
113	OPERATOR'S ROOM	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
114	RESTROOM ENTRY	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
115	RESTROOM ENTRY	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
116	LOCKERS	E	-	0"	0"						0"			
117A	LOCKERS	E	-	0"	0"						0"			
117B	LOCKERS	E	-	0"	0"						0"			
118	KITCHENETTE	G	-	0"	0"						0"			
119A	RECYCLE STORAGE	D	HM	6' - 0"	7' - 0"	1 3/4"					0"			
119B	KITCHENETTE	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
120	FIRE RISER	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
121	MECHANICAL	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
122	ELECTRICAL	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
123	EMERGENCY ELECTRICAL	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
124A	VESTIBULE	A	HM	3' - 0"	7' - 0"	1 3/4"					0"			
124B	OPERATOR'S ROOM	A	HM	3' - 0"	7' - 0"	1 3/4"					0"			
125	WAITING ROOM	B	HM	3' - 0"	7' - 0"	1 3/4"					0"			
127	MEN'S ROOM	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
128	WOMEN'S ROOM	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
129	MECH.	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			
130	PORTER	C	HM	3' - 0"	7' - 0"	1 3/4"					0"			

- ROOM SCHEDULE -

Room Number	Room Name	Area	Floor Finish	Base Finish	Wall Finish	Ceiling Finish	Ceiling Height	Comments
100	OPERATOR'S ROOM	1773 SF	RS-1	RB-1	PT-1	ACT-1	10' - 0"	
101	VESTIBULE	106 SF	RS-1	RB-1	PT-1	ACT-1	9' - 0"	
102	OFFICIAL/INSPECTOR	342 SF	RS-1	RB-1	PT-1	ACT-1	9' - 0"	
103	YARD MASTER	261 SF	CPT-1	RB-1	PT-1	ACT-1	9' - 0"	
104	SUPERVISOR	261 SF	CPT-1	RB-1	PT-1	ACT-1	9' - 0"	
105	OFFICE	288 SF	CPT-1	RB-1	PT-1	ACT-1	9' - 0"	
106	VESTIBULE	91 SF	RS-1	RB-1	PT-1	ACT-1	9' - 0"	
107	CONFERENCE	283 SF	CPT-1	RB-1	PT-1	ACT-1	9' - 0"	
108	COPY/STORAGE	113 SF	CFT-1	RB-1	PT-1	ACT-1	9' - 0"	
109	CLOSET	16 SF	RS-1	RB-1	PT-1	ACT-1	9' - 0"	
110	ARCHIVE STORAGE	149 SF	CPT-1	RB-1	PT-1	ACT-1	9' - 0"	
111	KITCHENETTE	142 SF	RS-1	RB-1	PT-1	ACT-1	9' - 0"	
112	UNISEX TOILET	59 SF	CFT-1	CWT-1	CWT-1	EP-1	9' - 0"	
113	DATA	35 SF	RS-1	RB-1	PT-1	ES	9' - 0"	EXPOSED CEILING STRUCTURE
114	MEN'S ROOM	306 SF	CFT-1	CWT-1	CWT-1	EP-1	9' - 0"	
115	WOMEN'S ROOM	283 SF	CFT-1	CWT-1	CWT-1	EP-1	9' - 0"	
116	RESTROOM ENTRY	44 SF	CFT-1	CWT-1	CWT-1	EP-1	9' - 0"	
117	LOCKERS	511 SF	RS-1	RB-1	PT-1	ACT-1	9' - 0"	
118	KITCHENETTE	191 SF	RS-1	RB-1	PT-1	ACT-1	9' - 0"	
119	RECYCLE STORAGE	118 SF	SC-1	RB-1	EP-1	ES	9' - 0"	EXPOSED CEILING STRUCTURE
120	FIRE RISER	120 SF	SC-1	RB-1	PT-1	ES	9' - 0"	EXPOSED CEILING STRUCTURE
121	MECHANICAL	120 SF	SC-1	RB-1	PT-1	ES	9' - 0"	EXPOSED CEILING STRUCTURE
122	ELECTRICAL	78 SF	SC-1	RB-1	PT-1	ES	9' - 0"	EXPOSED CEILING STRUCTURE
123	EMERGENCY ELECTRICAL	71 SF	SC-1	RB-1	PT-1	ES	9' - 0"	EXPOSED CEILING STRUCTURE
124	VESTIBULE	54 SF	RS-1	RB-1	PT-1	ACT-1	9' - 0"	
125	WAITING ROOM	243 SF	CFT-1	RB-1	PT-1	ACT-1	9' - 0"	
126	CLERK	73 SF	CFT-1	RB-1	PT-1	ACT-1	9' - 0"	
127	MEN'S SHOWER	65 SF	CFT-1	CWT-1	CWT-1	EP-1	9' - 0"	
128	WOMEN'S SHOWER	64 SF	CFT-1	CWT-1	CWT-1	EP-1	9' - 0"	
129	MECH.	29 SF	SC-1	RB-1	EP-1	ES	9' - 0"	EXPOSED CEILING STRUCTURE
130	PORTER	37 SF	SC-1	RB-1	EP-1	ES	9' - 0"	EXPOSED CEILING STRUCTURE

Grand total: 31

FINISH LEGEND

SEALED CONCRETE

SC-1 — MANUFACTURER: STYLE: COLOR:

FLOOR TILE

CERMAIC TILE

CFT-1 — MANUFACTURER: STYLE: COLOR: SIZE:

RESILIANT SHEET

RS-1 — MANUFACTURER: STYLE: COLOR: SIZE:

WALL BASE

CERAMIC TILE

CWT-1 — MANUFACTURER: STYLE: COLOR: SIZE:

RUBBER

RB-1 — MANUFACTURER: STYLE: COLOR: SIZE:

WALL FINISHES

CERAMIC TILE

CWT-1 — MANUFACTURER: STYLE: COLOR: SIZE:

PAINT

PT-1 — MANUFACTURER: COLOR: CEILING FINISH: WALL FINISH: (PAINTED CMU)

EP-1 — MANUFACTURER: STYLE: EPOXY COATING ON GWB COLOR:

CEILING

PAINTED GWB

EP-1 — TYPE: SUSPENDED OR FRAMED GYPSUM BOARD PAINTED EP-1

ACOUTIC CEILING TILE

ACT-1 — TYPE: SUSPENDED ACT

ABBREVIATIONS

CWT:	CERAMIC WALL TILE
CFT:	CERAMIC FLOOR TILE
EP:	EPOXY COATING
SC:	SEALED CONCRETE
ES:	EXPOSED STRUCTURE
PT:	PAINT
RB:	RUBBER BASE
GWB	GYPSUM WALL BOARD

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY


GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

ENHANCED TRANSPORTATION BUILDING
DOOR AND FINISH SCHEDULE
- ADDITIVE OPTION 6

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-282.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: OPT6-06	.

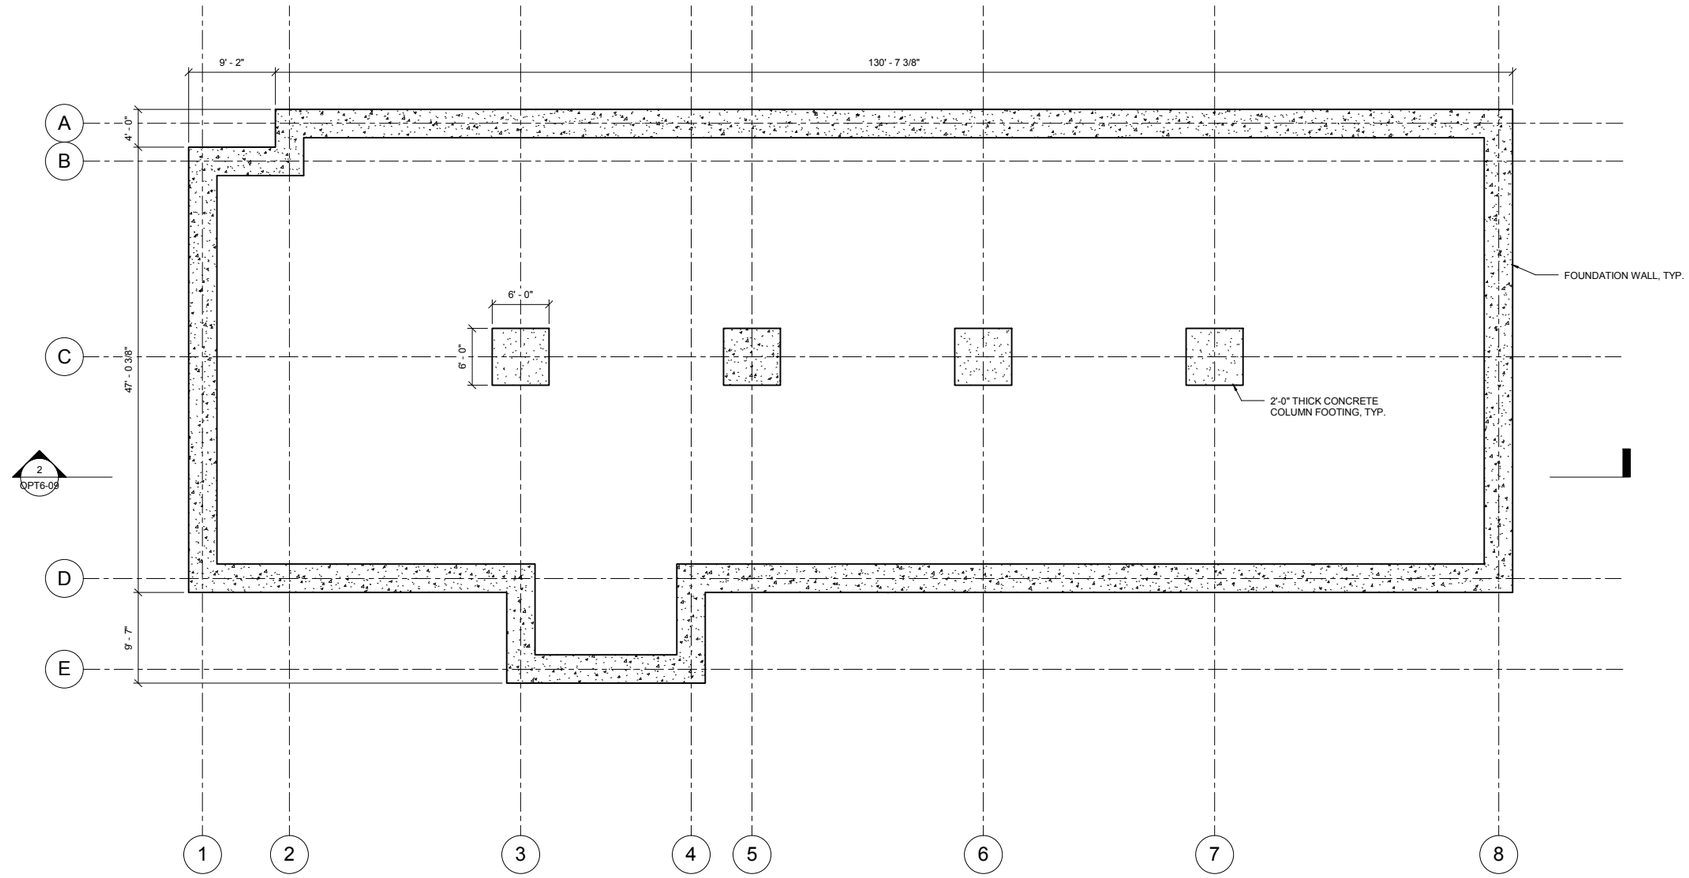

FOUNDATION PLAN

1/8" = 1'-0" 0 4' 8' 16'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY


GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

ENHANCED TRANSPORTATION BUILDING
FOUNDATION PLAN
- ADDITIVE OPTION 6

GV20170258-282.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: OPT6-07	.

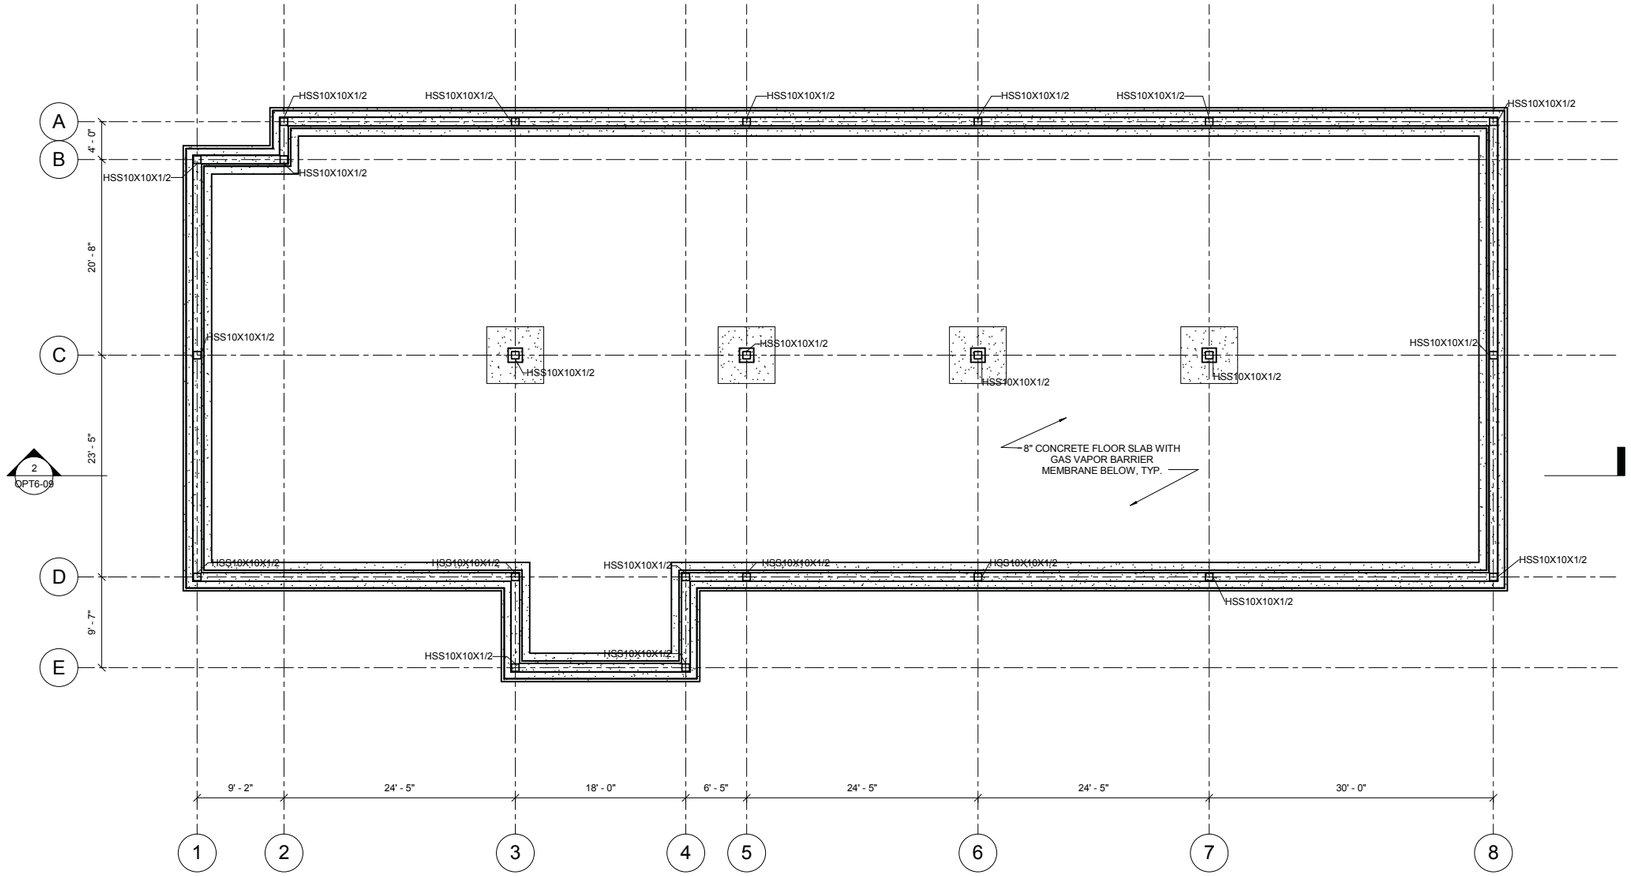

COLUMN FRAMING PLAN

1/8" = 1'-0"

0 4' 8' 16'

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


ENHANCED TRANSPORTATION BUILDING
COLUMN FRAMING PLAN
- ADDITIVE OPTION 6

GLX CONSTRUCTORS

GV20170258-282.pdf


ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: OPT6-08	.

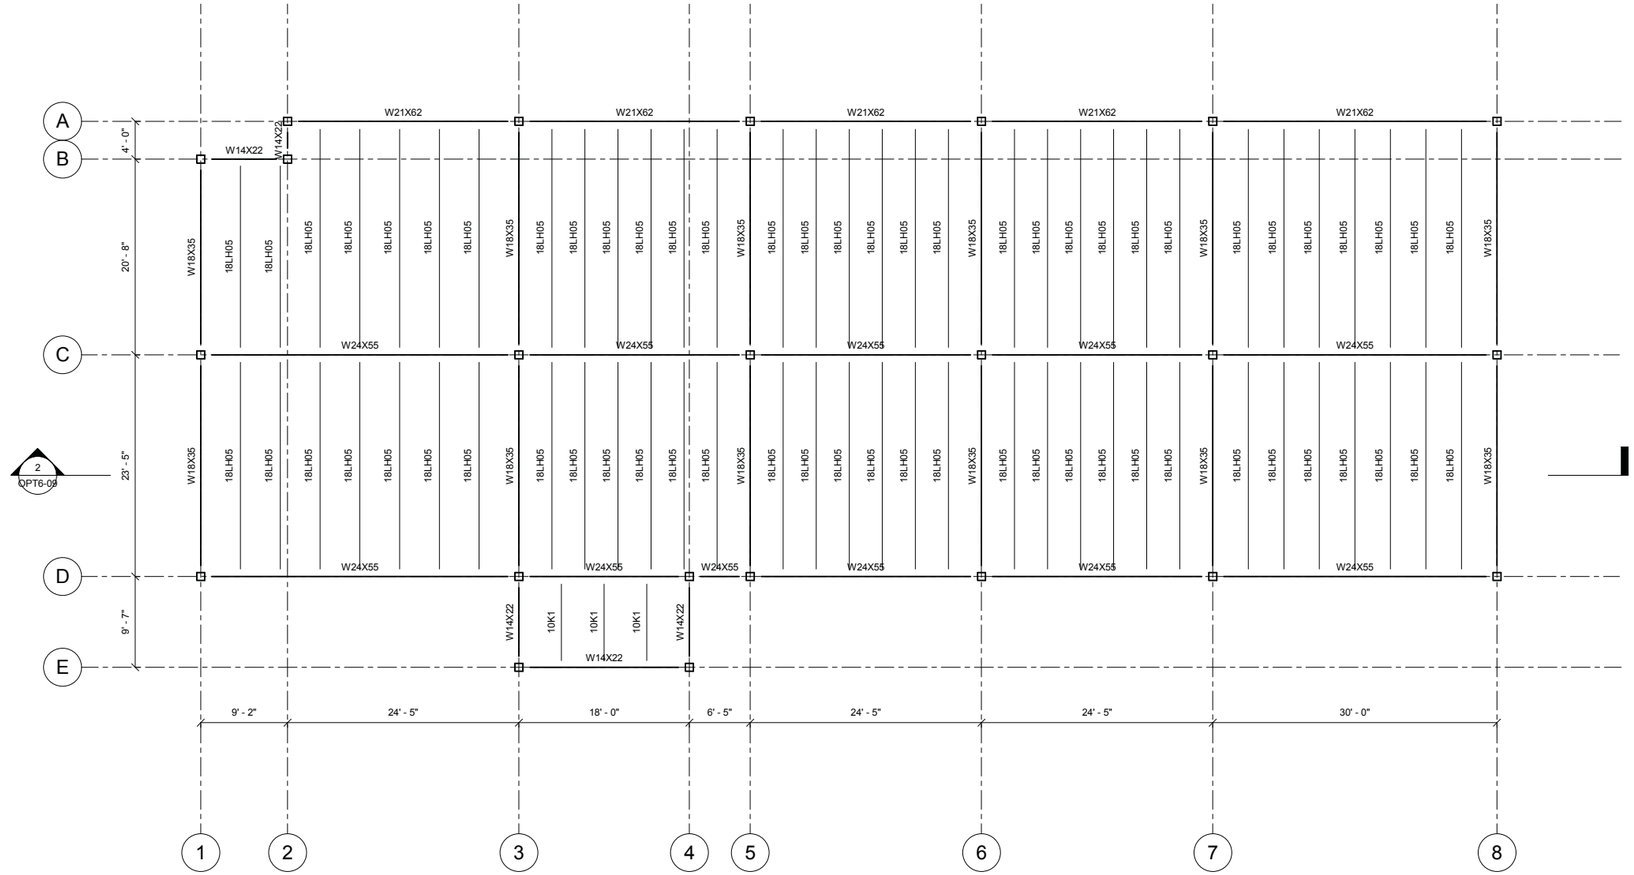

ROOF FRAMING PLAN

1/8" = 1'-0"

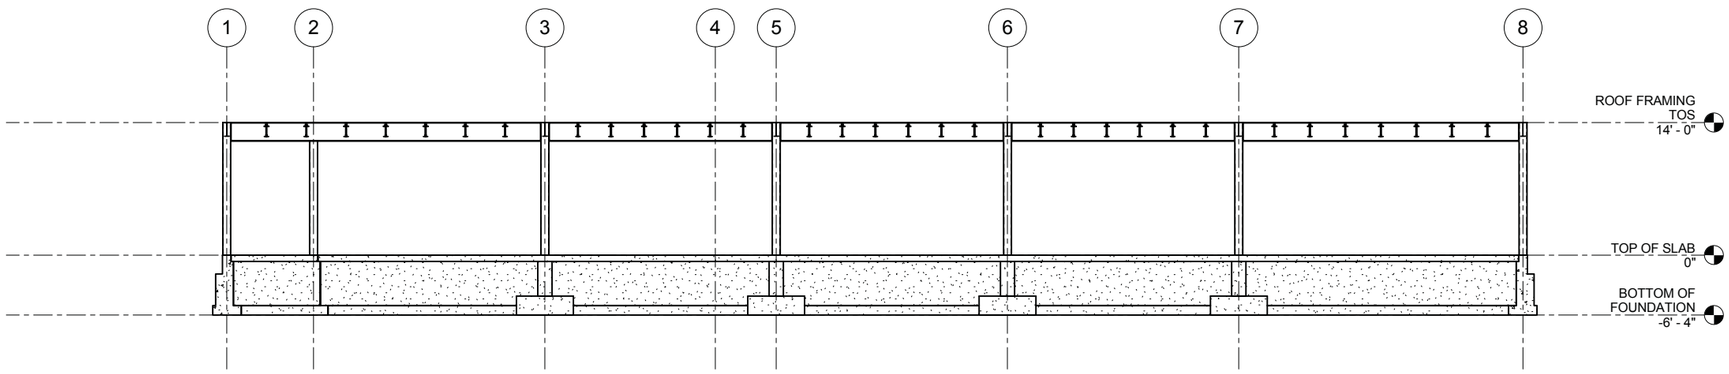

2 LONGITUDINAL SECTION

OPT6-07

1/8" = 1'-0"

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS


ENHANCED TRANSPORTATION BUILDING ROOF FRAMING PLAN & BUILDING SECTION - ADDITIVE OPTION 6

GV20170258-282.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	SP	SP		SHEET: OPT6-09	.

PLOTTED: 09/08/17 9:22AM BY: THARPBM
DRAWING: C:\USERS\THARPBM\ONEDRIVE - STV INCORPORATED\PROJECTS\MBTA\GREEN LINE - GLX EXTENSION\WORKING SET\CAD\YARD_20170825.DWG [S-3353] 09/08/17 9:22AM

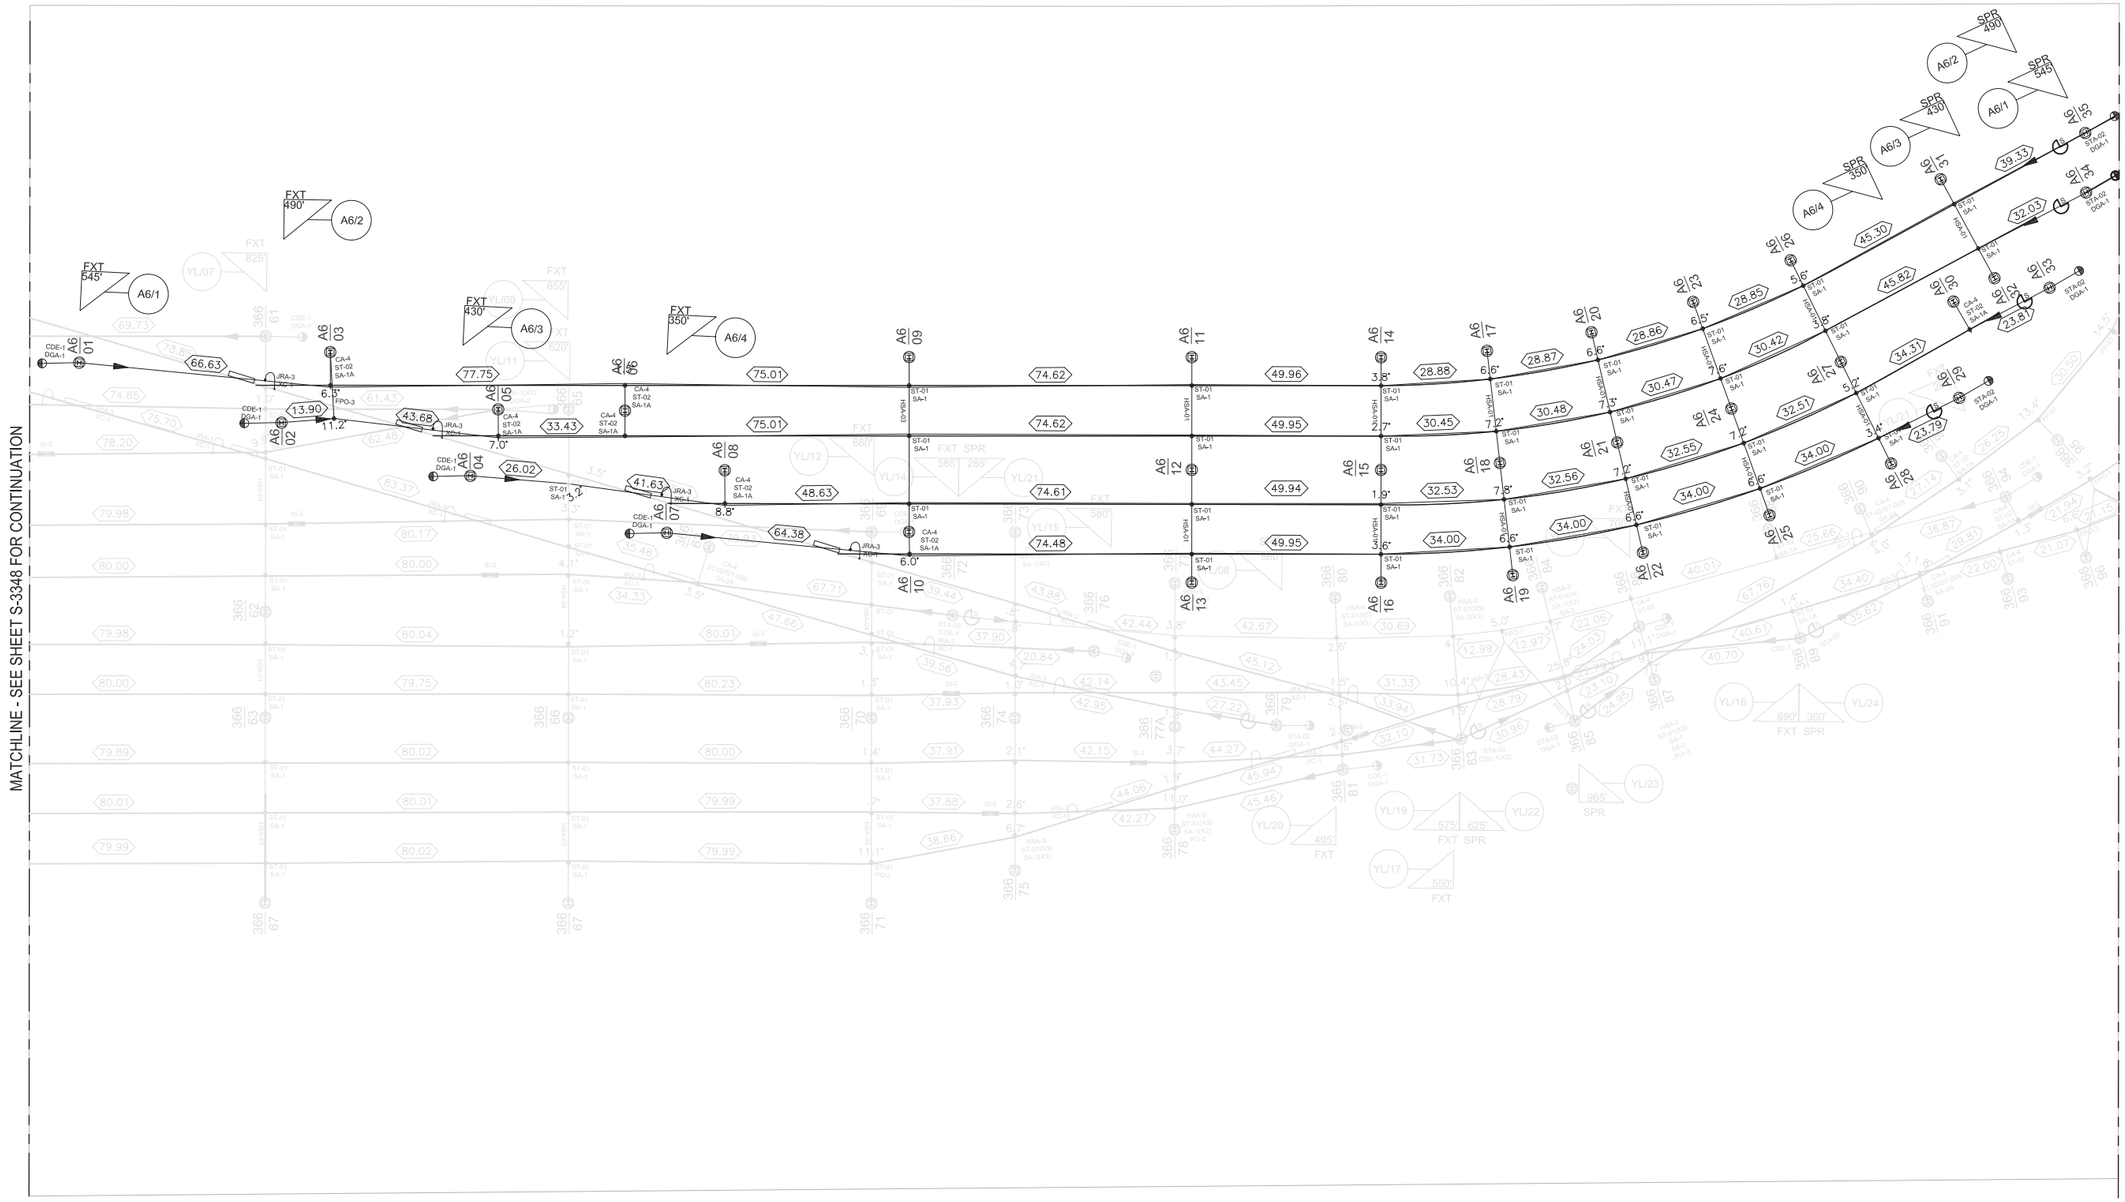

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY
YARD LEAD & MAINTENANCE FACILITY
- ADDITIVE OPTION 6

10 0 10 20
SCALE IN FEET

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

GV20170258-282.pdf

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	BT	BT	ND	SHEET: OPT6-10	.

ITEM NO.	ALIGNMENT	POLE NUMBER	OFFSET (FT)	POLE TYPE	SOIL PROFILE	FDN TYPE	FDN DEPTH (FT)	BASE PLATE TYPE
781	ADD6	A6/01	-	W12x79	F	FDN-1	18	ABTP-1
782	ADD6	A6/02	-	W12x79	F	FDN-1	18	ABTP-1
783	ADD6	A6/03	-	W12x79	F	FDN-1	18	ABTP-1
784	ADD6	A6/04	-	W12x79	F	FDN-1	18	ABTP-1
785	ADD6	A6/05	-	W12x106	F	FDN-1	26	ABTP-1
786	ADD6	A6/06	-	W12x53	F	FDN-1	16	ABTP-1
787	ADD6	A6/07	-	W12x79	F	FDN-1	18	ABTP-1
788	ADD6	A6/08	-	W12x79	F	FDN-1	18	ABTP-1
789	ADD6	A6/09	-	W12x79	F	FDN-1	18	ABTP-1
790	ADD6	A6/10	-	W12x53	F	FDN-1	16	ABTP-1
791	ADD6	A6/11	-	W12x53	F	FDN-1	16	ABTP-1
792	ADD6	A6/12	-	W12x53	F	FDN-1	16	ABTP-1
793	ADD6	A6/13	-	W12x53	F	FDN-1	16	ABTP-1
794	ADD6	A6/14	-	W12x53	F	FDN-1	16	ABTP-1
795	ADD6	A6/15	-	W12x53	F	FDN-1	16	ABTP-1
796	ADD6	A6/16	-	W12x53	F	FDN-1	16	ABTP-1
797	ADD6	A6/17	-	W12x53	F	FDN-1	16	ABTP-1
798	ADD6	A6/18	-	W12x53	F	FDN-1	16	ABTP-1
799	ADD6	A6/19	-	W12x53	F	FDN-1	16	ABTP-1
800	ADD6	A6/20	-	W12x53	F	FDN-1	16	ABTP-1
801	ADD6	A6/21	-	W12x53	F	FDN-1	16	ABTP-1
802	ADD6	A6/22	-	W12x53	F	FDN-1	16	ABTP-1
803	ADD6	A6/23	-	W12x53	F	FDN-1	16	ABTP-1
804	ADD6	A6/24	-	W12x53	F	FDN-1	16	ABTP-1
805	ADD6	A6/25	-	W12x53	F	FDN-1	16	ABTP-1
806	ADD6	A6/26	-	W12x53	F	FDN-1	16	ABTP-1
807	ADD6	A6/27	-	W12x53	F	FDN-1	16	ABTP-1
808	ADD6	A6/28	-	W12x53	F	FDN-1	16	ABTP-1
809	ADD6	A6/29	-	W12x79	F	FDN-1	18	ABTP-1
810	ADD6	A6/30	-	W12x53	F	FDN-1	16	ABTP-1
811	ADD6	A6/31	-	W12x53	F	FDN-1	16	ABTP-1
812	ADD6	A6/32	-	W12x53	F	FDN-1	16	ABTP-1
813	ADD6	A6/33	-	W12x79	F	FDN-1	18	ABTP-1
814	ADD6	A6/34	-	W12x79	F	FDN-1	18	ABTP-1
815	ADD6	A6/35	-	W12x79	F	FDN-1	18	ABTP-1

ITEM NO.	ALIGNMENT	POLE NUMBER	BASE PLATE TYPE	SOIL PROFILE	FDN TYPE	FDN DEPTH (FT)
187	ADD6	A6/01	ABDG-1	F	FDN-1	12
188	ADD6	A6/02	ABDG-1	F	FDN-1	12
189	ADD6	A6/04	ABDG-1	F	FDN-1	12
190	ADD6	A6/07	ABDG-1	F	FDN-1	12
191	ADD6	A6/29	ABDG-1	F	FDN-1	12
192	ADD6	A6/33	ABDG-1	F	FDN-1	12
193	ADD6	A6/34	ABDG-1	F	FDN-1	12
194	ADD6	A6/35	ABDG-1	F	FDN-1	12

NOTES:

1. POLE LOCATIONS, TYPE, FOUNDATION TYPE, AND DEPTH ARE PRELIMINARY AND WILL BE FURTHER VALIDATED AND COORDINATED WITH ALL DISCIPLINES DURING FINAL DESIGN.
2. POLES SHALL BE SUFFICIENT LENGTH SUCH THAT TOP OF POLE IS A MINIMUM OF 30'-0" ABOVE TOP OF RAIL ON ALL LOCATIONS WHERE PARALLEL FEEDERS ARE CARRIED. POLE CAN BE REDUCED SUCH THAT TOP OF POLE IS A MINIMUM OF 24'-0" ABOVE TOP OF RAIL IF NO ADDITIONAL WIRES ARE CARRIED ABOVE THE MESSENGER.

POLE ROUTE NUMBERS	
285	LECHMERE VIADUCT
364	MEDFORD BRANCH
365	UNION SQUARE BRANCH
366	RED BRIDGE/ COBBLE HILL YARD
ADD6	ADDITIVE OPTION

10 0 10 20
SCALE IN FEET

PROPOSAL

MASSACHUSETTS BAY TRANSPORTATION AUTHORITY

GREEN LINE EXTENSION PROJECT
MBTA CONTRACT NO. E22CN04
CAMBRIDGE/SOMERVILLE, MASSACHUSETTS

VEHICLE MAINTENANCE FACILITY POLE AND FOUNDATION SCHEDULE - ADDITIVE OPTION 6

STV 100 Years | massDOT Massachusetts Department of Transportation | GLX CONSTRUCTORS

GV20170258-282.pdf

ISSUE	DATE	DESCRIPTION	BY	CHK'D	APP.

SCALE: AS NOTED	DRAWN BY	DESIGN BY	CHECK BY	PLAN NO. .	ISSUE
DATE: SEPT. 28, 2017	BT	BT	ND	SHEET: OPT6-11	.

PLOTTED: 09/08/17 9:25AM BY: THARPBM
DRAWING: C:\USERS\THARPBM\ONEDRIVE - STV INCORPORATED\PROJECTS\MBTA\GREEN LINE - GLX EXTENSION\WORKING SET\CAD\YARD_20170825.DWG [VMF-113] 09/08/17 9:22AM

EXHIBIT 1S

SUBCONTRACTOR APPROVAL REQUEST

SUBCONTRACTOR APPROVAL REQUEST

Date: _____
Contract No. _____
Contract Title: _____

Subcontractor Name: _____
Address: _____
_____
Phone No.: _____
Project Superintendent: _____
Project Superintendent E-Mail Address: _____
Sub-Contractor's Company Tax ID Number: _____

Specification Section and Scope of Work :
_____
_____

Estimated Contract Value: $ _____

Form A – Work History Attached _____

MBTA Authorized Representative

MBTA Review:

_____ Approved **_____ Not Approved**

---------- **----------**
MBTA Director QA/QC **Date**

Reason for Disapproval: _____

032014

FORM A

SUBCONTRACTOR WORK HISTORY

Date Project Completed (Month/Year)	Project Title/Location (City, State)	Contract Value ($)	Description of Work	Client Name/Phone Number

Sub-Contractor Approval Request Instructions

1. The DB Entity shall submit to the MBTA the required Subcontractor information including general company information, and a completed Form A Work History. All blanks on page 1 of the request need to be completed.

2. The Form A Work History should include a minimum of five (5) completed projects finished within the last ten (10) years. The completed projects listed in Form A should be relevant to the proposed work, and the project information should be complete and accurate. Both MBTA projects and non-MBTA projects can be submitted for review. A Subcontractor prepared work history list that includes all the required information is an acceptable alternative to completing the Form A – Work History attachment if all the required Form A information is included in the sub-contractor work history list.

3. The MBTA completes the top section of the Subcontractor Approval Request based on information provided by DB Entity. First tier Subcontractors must be submitted for approval. The following second tier Subcontractors must also be submitted for approval:

   A. Structural Steel Fabricators and Erectors
   B. Miscellaneous Metal Fabricators and Erectors

4. The MBTA should be contacted if there are any questions on which Subcontractors should be submitted for approval.

5. All Subcontractor approval requests should be submitted to the MBTA a minimum of one week prior to the Subcontractor starting work.

6. The MBTA Authorized Representative shall review the Subcontractor approval request prior to submission, verify the Form A is attached and filled out correctly, and sign the request, and forward to MBTA QA/QC.

7. The MBTA QA/QC will review the request and forward a decision to the MBTA Authorized Representative. If the request is not approved, DB Entity shall make the necessary corrections and re-submit for approval.

8. Once approved, the MBTA QA/QC will forward all Subcontractor approvals to the MBTA Authorized Representative.

9. If the MBTA observes an unapproved Subcontractor starting work, the Subcontractor must stop work, and a Subcontractor Request must be submitted.
